

RECOVERY & RESILIENCE

APRIL 2024 CONEY ISLAND UPDATE

NYCHA'S SUPERSTORM SANDY RECOVERY PROGRAM







Progress
Community
Engagement
Q&A



Visit the <u>Capital Projects & Needs</u> <u>Tracker</u> for information on NYCHA's capital investments



Sandy website: tinyurl.com/SandyRecovery



Disaster.Recovery@nycha.nyc.gov















Ground and playgrounds

Superstorm Sandy Impact





Superstorm Sandy Investment


4 boroughs

35 sites

200+ buildings


60,000 residents

+\$3 billion of investment

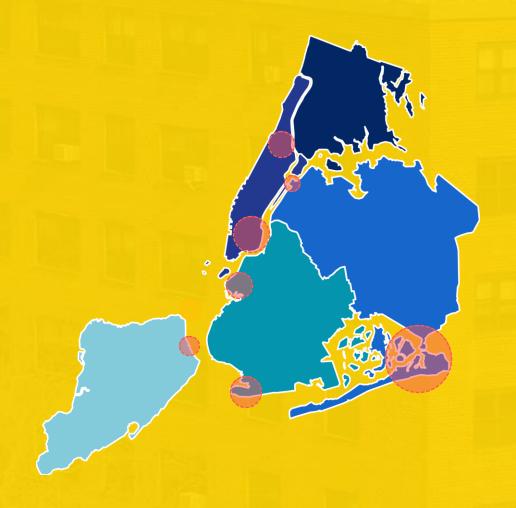





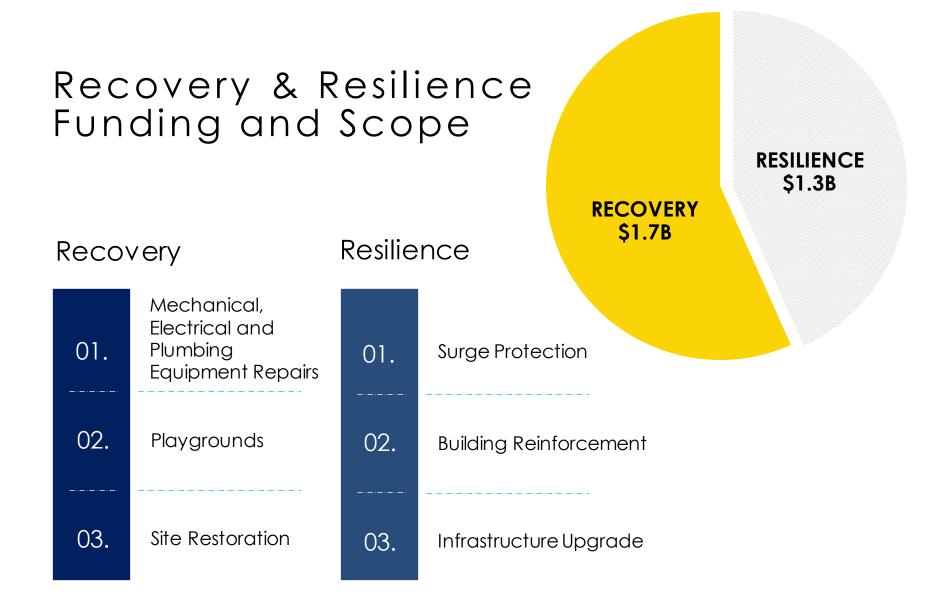





R&R Scope of Work



Standby generators



New boiler equipment



Flood proofing



Mechanical, electrical, and plumbing annexes



Site lighting upgrades



CCTV cameras



Ground restoration





History

Progress

Community Engagement Q&A



Visit the <u>Capital Projects & Needs</u> <u>Tracker</u> for information on NYCHA's capital investments



Sandy website: tinyurl.com/SandyRecovery



Disaster.Recovery@nycha.nyc.gov





Coney Island Milestones



sites substantially complete



\$821 M total estimated expenditure



generators installed;

generators operational



new structures constructed



boilers installed;

boilers operational



37 roofs replaced



playgrounds renovated



cameras operational



floodproofing components installed



hot water heaters installed





Gravesend

Status Substantially complete **Est. Total Expenditure** \$159 M













Coney Island I (Sites 4&5)

Status Substantially complete **Est. Total Expenditure** \$69 M













Haber

Status Substantially complete **Est. Total Expenditure** \$55 M













Coney Island Houses

Status Substantially complete **Est. Total Expenditure** \$95 M














Coney Island 1B (Unity Towers)

Status Substantially complete **Est. Total Expenditure** \$30 M













Carey Gardens


Status In construction **Anticipated completion** 2025

Est. Total Expenditure $$138\,M$













Coney Island Sites (Site 8)

Status In construction **Anticipated completion** Q4 2024





Est. Total Expenditure \$275 M










Coney Island Sites (Surfside)

Status In construction **Anticipated completion** Q4 2024



Est. Total Expenditure \$275 M











Coney Island Sites (O'Dwyer)

Status In construction **Anticipated completion** Q4 2024















History Progress

Community Engagement

Q&A



Visit the <u>Capital Projects & Needs</u> <u>Tracker</u> for information on NYCHA's capital investments



Sandy website: tinyurl.com/SandyRecovery



Disaster.Recovery@nycha.nyc.gov





Community Engagement

Metrics since 2014

Total calls: 105,950

Flyers distributed: 40,000Meetings attended: 682

Engagement strategy

- Dedicated community liaisons
- Monthly construction progress emails
- Monthly walkthroughs at active sites with tenant association presidents
- Informational graphics posted sitewide
- Attendance at all tenant association meetings
- R&R-organized community meetings, as needed
- Flyer distribution
- Phonebanking









History
Progress
Community
Engagement

Q&A



Visit the <u>Capital Projects & Needs</u> <u>Tracker</u> for information on NYCHA's capital investments



Sandy website: tinyurl.com/SandyRecovery



Disaster.Recovery@nycha.nyc.gov







Thank You

NYCHA Recovery and Resilience Department Disaster.Recovery@nycha.nyc.gov - 212-306-8532 tinyurl.com/SandyRecovery

> Sign up for email updates at **bit.ly/3WM3B6Q** Visit the <u>Capital Projects & Needs Tracker</u> for information on NYCHA's capital investments



RECOVERY —— &—
