260 West 26th Street

NEW YORK, NEW YORK

BLOCK: 775; LOTS 4, 69, 77, 78, 79 and 80

Remedial Action Report

BCP Site Number: 11CBCP011M

Prepared for:

Chelsea W26 LLC

37 West 65th Street

New York, NY 10023-6610

Prepared by:

Stephen J. Osmundsen, P.E.

514 Pantigo Road

East Hampton, NY 11937-2628

JUNE 2012

REMEDIAL ACTION REPORT

TABLE OF CONTENTS

TABLE OF CONTENTS ii

FIGURES AND TABLES iv

APPENDICES v

LIST OF ACRONYMS vi

CERTIFICATION vii

EXECUTIVE SUMMARY 1

REMEDIAL ACTION REPORT 8

1.0 SITE BACKGROUND 8

1.1 Site Location and Prior Usage 8

1.2 Proposed Redevelopment Plan 9

1.3 Description of Surrounding Property 10

1.4 Remedial Investigation 10

2.0 DESCRIPTION OF REMEDIAL ACTIONS. 10

3.0 COMPLIANCE WITH REMEDIAL ACTION WORK PLANNALYSIS . 12

3.1 Health and Safety Plan 12

3.2 Community Air Monitoring Plan 12

3.3 Soil/Materials Management Plan 13

3.4 Strom-Water Pollution Prevention 13

3.5 Deviations From the Remedial Action Work Plan 13

TABLE OF CONTENTS

(continued)

4.0 REMEDIAL PROGRAM 16

4.1 Project Organization 16

4.2 Site Controls 16

4.3 Waste Classification Testing 22

4.4 Materials Excavation and Removal 23

4.4.1 Lead-Hazardous Soil 23

4.4.2 Non-Hazardous Material 25

4.5 Materials Disposal 26

4.6 Backfill Import 28

4.7 Demarcation 28

5.0 ENGINEERING CONTROLS 28

6.0 INSTITUTIONAL CONTROLS 29

7.0 SITE MANAGEMENT 29

8.0 REFERENCES 30

FIGURES

1. Property Location Map
2. Site Plan with Adjoining Properties
3. Location of Soil Samples Obtained Prior to Completing Excavation
4. Waste Classification Test Pit Locations
5. Project Organization Chart
6. Site Plan with Hazardous-Lead Remedial Excavation and Sampling Locations
7. Map Illustrating the Extent of Site-wide Soil Excavation

TABLES

1. Analytical Results for Volatile Organic Compounds in Soil Samples
2. Analytical Results for Semi-Volatile Organic Compounds in Soil Samples
3. Analytical Results for Pesticides in Soil Samples
4. Analytical Results for Metals in Soil Samples
5. Summary of Hazardous Waste Disposal Activities
6. Summary of Non-Hazardous Waste Disposal Activities
7. Summary of Waste Characterization Sampling for Test Pits

APPENDICES

A Sustainability Report

B Property Redevelopment Plans (electronic copies only)

C Community Air Monitoring Field Records

D Project Photographs

E Laboratory Results for Soil Samples Prior to Completing Excavation

F Daily Reports (electronic copies)

G Soil Profile and Report with Waste Classification Data

H Disposal Approval Letters and Operating Permits

I Disposal Manifests for Hazardous Waste Disposal Activities

J Soil Test Results for Post-Excavation Samples from Test Pits TP-5 and TP-7

K Disposal Manifests for Non-Hazardous Waste Disposal Activities

L Water-proofing Membrane Specifications

LIST OF ACRONYMS

Acronym	Definition
CAMP	Community Air Monitoring Plan
DER-10	NYS DEC Division of Environmental Remediation Technical Guidance Manual 10
EC	Engineering Control
HASP	Health and Safety Plan
IC	Institutional Control
NYC BCP	New York City Brownfield Cleanup Program
NYC DEP	New York City Department of Environmental Protection
NYC DOHMH	New York City Department of Health and Mental Hygiene
NYC OER	New York City Office of Environmental Remediation
ORC	Oxygen Release Compound
PID	Photoionization Detector
QA/QC	Quality Assurance/Quality Control
QEP	Qualified Environmental Professional
RAR	Remedial Action Report
RAWP	Remedial Action Work Plan
SCG	Standards, Criteria and Guidance
SCO	Soil Cleanup Objective
SMMP	Soil/Materials Management Plan
SMP	Site Management Plan
SVOCs	Semi-Volatile Organic Compounds
UST	Underground Storage Tank
VOCs	Volatile Organic Compounds

CERTIFICATION

I, Stephen J. Osmundsen, am currently a registered professional engineer licensed by the State of New York. I had primary direct responsibility for implementation of the remedial program for the 260 West 26th Street, New York, NY Site. NYC BCP Site Number is 11CBCP011M.

I certify that the OER-approved Remedial Action Work Plan dated April 2011 and Stipulations in a letter dated May 17, 2011 were implemented and that all requirements in those documents have been substantively complied with. I certify that contaminated soil, fill, liquids or other material from the property were taken to facilities licensed to accept this material in full compliance with applicable laws and regulations.

Stephen J. Osmundsen
Name

056136
PE License Number

Signature

JUN 22 2012
Date

Date

EXECUTIVE SUMMARY

Site Location and Prior Usage

The Site is located at 260 West 26th Street in the Chelsea section of Manhattan, New York and is identified as Block: 775; Lots: 4, 69, 77, 78, 79, and 80 on the New York City Tax Map. Figure 1 shows the Site location. The Site area is 26,000 square feet and is bounded by West 26th Street to the north, residential and commercial buildings to the south, a four-story veterinary practice to the east, and Eighth Avenue to the west. A map depicting the Site boundaries is shown in Figure 2. Until the recent construction began, the Site contained a two-story building and an automotive parking lot with aboveground hydraulic car lifts. A video store and art gallery was located on the first floor of the building. The tenant space located on the second floor of the structure was vacant. The two-story building was demolished in preparation for Site redevelopment.

Summary of Proposed Redevelopment Plan

The proposed future use of the Site includes 204 residential units with a mix of studios as well as one and two bedroom apartments. Forty-one of the 204 units will be rented by lottery to residents earning 40% and 60% of the area median income. The remaining units will be rented at market rate. There will also be approximately 17,000 square feet of retail as well as 600 square feet of community facility. The proposed Site development plans are presented as Appendix B. The current zoning designation is C6-2A. The proposed use is consistent with existing zoning for the property.

The two-story building along the southern boundary of the Site was demolished in preparation for the proposed new building. The new building will cover the entire Site. Excavation for the building's foundation will extend site-wide from grade down to and partially into bedrock. As part of redevelopment activities, approximately 14,500 tons of soil and 10,000 cubic yards of bedrock were excavated. The new structure will be 12 stories tall with setbacks allowing for penthouses and roof terraces in addition to balconies for indoor/outdoor living. The building will be a LEED-certified building and will include many green features including a monitored boiler, low-flow fixtures, energy saving appliances, as well as energy-efficient and LED lighting. The building residents will have access to a landscaped roof terrace with panoramic views equipped with lounge furniture and a party space with a gas grill. The basement will consist of mechanical and storage rooms, a parking garage, and commercial storage rooms. The second floor of the building will host an array of amenities including a possible play room, gym, media or recreation room. Laundry facilities and an outdoor play area for children will also be located on the second floor.

Summary of Past Uses of Site and Environmental Findings

Review of the Sanborn Maps show that the Site was first developed with five 3-story structures and a theater in 1890. By 1976 the Site contained five 3-story stores and dwellings, a two-story store, and a parking area. In 1988, the Site contained two 3-story commercial and residential structures, one 3-story store, one 2-story store and a parking area. By 2003, the Site contained three 3-story commercial and residential buildings, a two-story store, and a parking area.

A search of the New York City Department of Finance (NYCDOF) ACRIS database was also conducted for the Site. Copies of records are included in the Phase I Environmental Site Assessment (ESA) that was conducted in March 2011 (Ref. 1).

Based on the results of the Phase I and Remedial Investigation, the AOCs identified for this Site include:

1. **Urban Fill**

In all areas of the Site that were tested during the Remedial Investigation, the soil displayed characteristics of historic fill. Elevated levels of several Semi-Volatile Organic Compounds (SVOCs) commonly referred to as Poly Aromatic Hydrocarbons (PAHs) and metals were detected throughout the Site at varying depths.

2. **Suspect USTs**

A fuel oil fill port and vent pipe were observed in the northeastern portion of the parking lot during the Phase I ESA. An additional fill port was identified near the aboveground hydraulic lifts on the western portion of the Site during the RI Site inspection. In addition, the September 2005 Phase I identified two 275-gallon abandoned ASTs at the Site and the NYCDOB database identified the presence of an oil boiler on Lot 78. Although no records indicating the proper removal of these tanks were provided as the buildings have since been demolished, the geophysical survey did not confirm the presence or absence of any anomalies indicative of suspect USTs, ASTs, or leaching structures beneath the surface of the Site.

3. **Unrecorded Historic Spills**

During the Phase I inspection, small amounts of hydraulic oil and grease were observed to be leaking from several of the hydraulic lifts onto the asphalt-surface of the parking lot. As elevated levels of several SVOCs were detected throughout the Site in soils at shallow depths, it is possible that some of the detections in the area of the lifts may be related to these minor spills in addition to urban fill. An electronic copy of the Phase 1 ESA was included in the Remedial Investigation Report (Ref. 2).

Summary of Environmental Findings

1. Elevation of the property ranges from 23 to 25 feet (Manhattan Highway Datum).

2. Groundwater was encountered at 21 feet below grade during the Remedial Investigation. Regional groundwater flows in a westerly direction.

3. Depth to bedrock ranges from eight to 20 feet below grade at the Site.

4. The stratigraphy of the Site, from the surface down, consists of urban fill underlain by unconsolidated Cretaceous age deposits composed of interbedded layers of silt, sand, and gravel.

5. Soil/fill samples collected during the RI contained the metals arsenic, copper, lead, mercury, and zinc at levels above NYSDEC Part 375 Unrestricted Use Soil Cleanup Objectives (Track 1 SCOs). Most exceedences of Track 1 occur in the shallow fill samples. Relatively few samples that exceed Track 1 also exceed NYSDEC Part 375 Track 2 Restricted Residential SCOs. VOCs are not identified above Track 1 or Track 2 Restricted Residential SCOs. Low levels of one PCB Aroclor and various pesticides were also identified at levels above NYSDEC Part 375 Unrestricted Use Soil Cleanup Objectives. No soil/fill samples exceeded the Track 2 Restricted Residential SCOs for PCBs. Several SVOCs exceeded Track 1 SCOs. These include benzo(a)anthracene, benzo(a)pyrene, benzo(b)flouranthene, benzo(k)flouranthene, chrysene, dibenzo(a,h)anthracene, and indeno(1,2,3-cd)pyrene. The SVOC compounds identified and the concentrations observed are typical for historical fill found commonly in urban areas elsewhere in NYC. These metals and SVOC findings are attributed to historic fill material disposed on the property and are not considered indicative of any disposal, release or spill.

6. Groundwater samples collected during the RI showed a slight exceedence of NYSDEC Technical and Operational Guidance Series (TOGS) groundwater standards or guidance values (Ref. 3) for the VOC toluene and the SVOC chrysene. No PCBs or pesticides exceeded TOGS. The dissolved metals magnesium, selenium, and sodium were detected slightly above TOGS.

7. Soil vapor samples collected during the RI contained low level VOCs. Most of the soil vapor detections are below 2 ug/m^3 and there were no valid findings above 5 ug/m^3. The compounds detected in soil vapor are mostly derivatives of BTEX. Some of the VOCs identified in the soil vapor are also found in onsite soils but at very low concentrations, generally estimated values below one ug/kg. These compounds are also predominantly BTEX derivatives that are most commonly derived from automotive fuel sources. The soil vapor detections are attributed, to on-site automotive parking operations and off-site sources. The area is predominantly paved and encapsulated and vapors from offsite sources will have a tendency to migrate laterally prior to discharge to the atmosphere.

8. A fuel oil fill port and vent pipe were observed in the northeastern portion of the parking lot and an additional fill port was identified near the hydraulic lifts on the western portion of the Site.

9. The geophysical investigation did not confirm the absence or presence of USTs associated with the fill ports and vent pipes or any anomalies indicative of suspect USTs or leaching structures beneath the surface of the Site.

Summary of the Remedy

1. Prepared a Community Protection Statement and implemented a Citizen Participation Plan.
2. Performed a Community Air Monitoring Program for particulates and volatile organic compounds.
3. Developed a Remedial Action Work Plan with a Track 1 cleanup as the project's primary goal and established Track 4 Soil Cleanup Objectives (SCOs) in the event Track 1 could not be attained.
4. Conducted in-situ soil waste classification testing to profile the soil to obtain disposal approval at suitable facilities.
5. Mobilized site security, equipment, utility mark outs and marking & staking excavation areas.
6. Screened excavated soil/fill during intrusive work for indications of contamination by visual means, odor, and monitoring with a PID.
7. Conducted a site-wide excavation and removed all on-site soil/fill to bedrock to achieve Track 1 SCOs.
8. Transported and disposed all soil/fill material at permitted facilities in accordance with all applicable laws and regulations for handling, transport, and disposal, and the RAWP. Sampled and analyzed excavated media as required by disposal facilities. Appropriately segregated excavated media on-site.
9. Cleaned up a minor surface petroleum spill in compliance with applicable laws and regulations.
10. Installed a water-proofing membrane beneath the building slab and up the basement walls.
11. Implemented storm-water pollution prevention measures in compliance with applicable laws and regulations.

12. Performed limited dewatering after storm events as-needed in accordance with a NYCDEP discharge permit.
13. Performed all activities required for the remedial action in compliance with applicable laws and regulations.
14. Submitted a RAR that: certifies that the remedial requirements have achieved the Track 1 cleanup requirements; defines the Site boundaries; and describes the remedial activities including any changes from the RAWP.

REMEDIAL ACTION REPORT

1.0 SITE BACKGROUND

Chelsea W26 LLC has enrolled in the New York City Brownfield Cleanup Program (NYC BCP) as a Volunteer to investigate and remediate a property located at 260 West 26th Street in the Chelsea section of Manhattan, New York (the Site). A Remedial Investigation (RI) was performed to compile and evaluate data and information necessary to develop a Remedial Action Work Plan (RAWP) (Ref. 4). A remedial action was performed pursuant to an OER-approved RAWP in a manner that has rendered the Site protective of public health and the environment consistent with the proposed use of the property. This RAR describes the remedial action performed under the RAWP. The remedial action described in this document provides for the protection of public health and the environment, complies with applicable environmental standards, criteria and guidance and applicable laws and regulations. A Sustainability Report is included as Appendix A.

1.1 SITE LOCATION AND PRIOR USAGE

The Site is located at 260 West 26th Street in the Chelsea section of Manhattan, New York and is identified as Block: 775; Lots: 4, 69, 77, 78, 79, and 80 on the New York City Tax Map. A Site Location Map is included as Figure 1. The Site area is 26,000 square feet and is bounded by West 26th Street to the north, residential and commercial buildings to the south, a four-story veterinary practice to the east, and Eighth Avenue to the west. A Site Plan illustrating the Site boundaries is included as Figure 2. Currently, the Site contains a two-story building and an automotive parking lot with aboveground hydraulic car lifts. A video store and art gallery is located on the first floor of the building. The tenant space located on the second floor of the structure is currently

vacant. The two-story building is slated for demolition in preparation for Site redevelopment.

1.2 PROPOSED REDEVELOPMENT PLAN

The proposed future use of the Site includes 204 residential units with a mix of studios as well as one and two bedroom apartments. Forty-one of the 204 units will be rented by lottery to residents earning 40% and 60% of the area median income. The remaining units will be rented at market rate. There will also be approximately 17,000 square feet of retail as well as 600 square feet of community facility. The proposed Site development plans are presented as Appendix B. The current zoning designation is C6-2A. The proposed use is consistent with existing zoning for the property.

The two-story building along the southern boundary of the Site was demolished in preparation for the proposed new building. The new building will cover the entire Site. Excavation for the building's foundation will extend Site wide from grade down to and partially into bedrock. As part of redevelopment activities, approximately 14,500 tons of soil and 10,000 cubic yards of rock were excavated. The new structure will be 12 stories tall with setbacks allowing for penthouses and roof terraces in addition to balconies for indoor/outdoor living. The building will be a LEED-certified building and will include many green features including a monitored boiler, low-flow fixtures, energy saving appliances, as well as energy-efficient and LED lighting. The building residents will have access to a landscaped roof terrace with panoramic views equipped with lounge furniture and a party space with a gas grill. The basement will consist of mechanical and storage rooms, a parking garage, and commercial storage rooms. The second floor of the building will host an array of amenities including a possible play room, gym, media or recreation room. Laundry facilities and an outdoor play area for children will also be located on the second floor.

1.3 DESCRIPTION OF SURROUNDING PROPERTY

The Site is located in a developed area consisting of a mixed-use of residential and commercial buildings. West 26th Street is located to the north of the Site. Residential and commercial buildings are located to the south of the Site. Eighth Avenue is located to the west of the Site. A four-story commercial building is located to the east of the Site.

There are no surface bodies of water on-site or within approximately ½-mile from the Site. There are no Federal Wetlands mapped within ½ -mile of the Site. The Site is not located within a FEMA 100 or 500 Year Flood Zone. Public water is supplied to the Site and there is no on-site use of the shallow water beneath the Site. Figure 2 shows the surrounding land usage.

1.4 REMEDIAL INVESTIGATION

A Remedial Investigation was performed and the results are documented in a companion document called "*Remedial Investigation Report*", dated April 2011 (RIR). The RIR is included as Appendix G of the approved-Remedial Action Work Plan dated April 2011.

2.0 DESCRIPTION OF REMEDIAL ACTIONS

The factors considered during the selection of the remedial action included protection of human health, protection of the environment, compliance with standards, criteria, and guidelines (SCGs), short-term effectiveness and impacts, long-term effectiveness and permanence, reduction of toxicity, mobility, or volume of contaminated material, implementability, cost effectiveness, community acceptance, land use, and sustainability of the remedial action. The Site was remediated in accordance with the scope of work

presented in an OER-approved Remedial Action Work Plan (RAWP) dated April 2011 and the Stipulation List dated May 17, 2011 (Ref. 5). All deviations from the RAWP are noted below.

The following remedial actions were completed in this program:

1. Prepared a Community Protection Statement and implemented a Citizen Participation Plan.
2. Performed a Community Air Monitoring Program for particulates and volatile organic compounds.
3. Developed a Remedial Action Work Plan with a Track 1 cleanup as the project's primary goal and established Track 4 Soil Cleanup Objectives (SCOs) in the event Track 1 could not be attained.
4. Mobilized site security, equipment, utility mark outs and marking & staking excavation areas.
5. Performed waste classification testing to profile the soil for disposal purposes at properly licensed facilities.
6. Screened excavated soil/fill during intrusive work for indications of contamination by visual means, odor, and monitoring with a PID.
7. Conducted a site-wide excavation and removed all on-site soil/fill to bedrock to achieve Track 1 SCOs.
8. Transported and disposed all soil/fill material at permitted facilities in accordance with all applicable laws and regulations for handling, transport, and disposal, and the RAWP. Sampled and analyzed excavated media as required by disposal facilities. Appropriately segregated excavated media on-site.
9. Cleaned up a minor surface petroleum spill in compliance with applicable laws and regulations.

10. Installed a water-proofing membrane beneath the building slab and up the basement walls.
11. Implemented storm-water pollution prevention measures in compliance with applicable laws and regulations.
12. Performed limited dewatering after storm events as-needed in accordance with a NYCDEP discharge permit.
13. Performed all activities required for the remedial action in compliance with applicable laws and regulations.
14. Submitted a RAR that: certifies that the remedial requirements have achieved the Track 1 cleanup requirements; defines the Site boundaries; and describes the remedial activities including any changes from the RAWP.

3.0 COMPLIANCE WITH REMEDIAL ACTION WORK PLAN

3.1 HEALTH & SAFETY PLAN (HASP)

The remedial construction activities performed under this program were in compliance with the Health and Safety Plan and applicable laws and regulations. The Site Safety Coordinator was Jessica Proscia of CA RICH Consultants, Inc.

3.2 COMMUNITY AIR MONITORING PLAN

The Community Air Monitoring Plan provided for the collection and analysis of air samples during remedial construction activities to ensure proper protections were

employed to protect workers and the neighboring community. Monitoring was performed in compliance with the Community Air Monitoring Plan in the approved RAWP. The results of Community Air monitoring are shown in Appendix C.

3.3 SOIL/MATERIALS MANAGEMENT PLAN

The Soil/Materials Management Plan in the RAWP provided detailed plans for managing all soils/materials that were disturbed at the Site, including excavation, handling, storage, transport and disposal. It also included a series of controls to assure effective, nuisance-free remedial activity in compliance with applicable laws and regulations. Remedial construction activities performed under this program were in full compliance with the SMMP in the approved RAWP.

3.4 STORMWATER POLLUTION PREVENTION

Storm water pollution prevention included physical methods and processes to control and/or divert surface water flows and to limit the potential for erosion and migration of Site soils, via wind or water. Remedial construction activities performed under this program were in full compliance with methods and processes defined in the RAWP for storm water prevention and applicable laws and regulations

3.5 DEVIATIONS FROM THE REMEDIAL ACTION WORK PLAN

There were two deviations from the RAWP that took place during the property redevelopment and remediation. The first deviation pertained to a minor spill incident and the second involved the collection of soil samples from the excavation for decision making purposes prior to reaching the terminal depth in the northwest corner of the Site. The details for both of these deviations are presented in the following paragraphs.

The spill incident occurred during preliminary Site preparatory activities. The initial stage of redevelopment was to discontinue the use of the property as an aboveground automotive parking lot. The on-site equipment related to the parking business was limited to an attendant booth and aboveground hydraulic lifts. On July 18, 2011, after the removal of the lifts a small amount of hydraulic oil was observed on the asphalt parking lot surface. Although the hydraulic oil appeared to be limited to the asphalt surface and no underground hydraulic tanks were removed during the lift decommissioning the spill was discussed with NYC OER representatives and out of an abundance of caution reported to the NYSDEC Spill Hotline. NYSDEC assigned Spill # 1104255 to the Site.

At the time of the incident absorbent material was utilized to absorb the liquids on the asphalt surface. During the performance of waste classification test pit excavations on August 30, 2011 the asphalt surface of the affected area was peeled back to allow the underlying soil to be examined for evidence of contamination. Upon removal of the asphalt, the soil was inspected by an Environmental Scientist from CA RICH Consultants, Inc. of Plainview, New York. CA RICH's inspector utilized both a Photo-Ionization Detector (PID) and olfactory senses to examine the soil and no evidence of soil contamination was found. These findings were discussed with NYC OER representatives and no soil sampling was required since the Site soils were being tested for waste classification purposes and were schedule for off-site disposal. The asphalt removed from the surface was placed in a stockpile, covered with plastic in preparation for its disposal along with the remaining surface asphalt at the Bay Shore Recycling facility in Woodbridge, New Jersey. A photograph of the soil beneath the stain on the asphalt is included in Appendix D.

The planned work activities in the RAWP included an approximate 15-foot deep site-wide excavation into bedrock to facilitate the construction of the new buildings' foundation with a provision for the collection of endpoint soil samples if the bottom of

the excavation contained soil as opposed to bedrock. While the elevation of bedrock beneath the majority of the Site was relatively shallow it sloped downward in grids A1, A2, A3, B1, B2 and B3 in the northwest corner of the Site. To evaluate the soil quality at 14-15 feet below grade in these grids, three sets of soil samples were collected from grids A1, A3 and B2 for comparison to Track 1 SCOs (Ref. 6) on January 13, 2012. Upon receipt of the results, it was revealed that three pesticides as well as the metals lead, mercury and zinc were found above Track 1 SCOs and below Track 2 restricted residential standards.

The results were discussed with NYC OER and the Site Owner and it was decided to remove an additional 2 feet of soil from grid A1 on January 23, 2012 to see if the levels of pesticides dropped below Track 1 SCOs. Although the concentration of the pesticide 4,4 DDT was reduced to 57 ppb it was still above Track 1 SCOs and plans were made to further the excavation to bedrock in grids A1, A2, A3, B1, B2 and B3 to achieve the Track 1 cleanup requirements. All of the material was removed from the Site as part of the remediation. A summary of the results is presented on Tables 1-4. A copy of the laboratory reports is included in Appendix E. The sample locations are depicted on Figure 3.

It is noted that soil samples B2 and B2G were obtained beneath the area of the former surface spill at the request of NYC OER. The test results for these samples did not contain any VOCs or SVOCs above the NYSDEC CP-51 soil guidance criteria (Ref. 7). In addition, all soil from this area was removed as the excavation was advanced further until bedrock. The actions taken pertaining to the minor surface spill incident and the soil sampling are protective of public health and the environment and no further action is necessary. Based on the remedial work performed, NYSDEC closed Spill # 1104255 on June 4, 2012.

4.0 REMEDIAL PROGRAM

4.1 PROJECT ORGANIZATION

The Professional Engineer (PE) for this project is Stephen J. Osmundsen. The Qualified Environmental Professional and Project Geologist is Richard J. Izzo of CA Rich Consultants, Inc. The Principal personnel who participated in the remedial action and assisted the Remedial Engineer with the coordination and implementation of all environmental components of the RAWP were Stephen Malinowski, Jessica Proscia and Jason Cooper of CA RICH Consultants, Inc. A project organization chart is included as Figure 5.

4.2 SITE CONTROLS

Site Preparation

- During July of 2011 a construction fence was erected around the building located on the southwestern portion of the Site. The building was demolished and removed from the Site in July and August 2011.
- The hydraulic automotive lifts associated with the former parking business were removed from the Site in July 2011.
- A pre-construction meeting was held with OER, the General Contractor and the excavation contractors on August 25, 2011. An OER Project Notice was posted at the project entrance and remained in place during all phases of the Remedial Action.
- A pedestrian walkway and construction fence were constructed along West 26th Street and 8th Avenue between August 26, 2011 and September 8, 2011.

- The BCP Enrollee identified utilities that might be affected by work under the RAWP as well as Site redevelopment activities. Any utilities that would be affected were turned off by the appropriate utility company prior to the test pit excavation activities which were conducted on August 30, 2011.

- The trees along the south property line were removed on September 8, 2011.

- Artimus Construction, Inc. obtained any local, State or Federal permits or approvals that were required to perform the work under this Plan.

Mobilization

- Excavation equipment was mobilized to the Site on August 30, 2011. Additional excavation equipment was mobilized to the Site in October and November 2011 as the excavation advanced down to and into bedrock.
- The asphalt pavement from the former parking lot and the concrete sidewalk surrounding the Site were removed from September 1, 2011 through September 8, 2011. On September 7, 2011 a gravel pad for the truck inspection and wash station was installed near the construction entrance along 8th Avenue.

Stabilization

- In preparation of the site-wide excavation to bedrock, the installation of soldier piles began on September 12, 2011 and was completed on October 18, 2011. The soldier piles enabled the installation of shoring and lagging around the perimeter of the Site to safely advance the excavation. The appropriate management of the structural stability of off-site structures and installation of sheeting and shoring during on-site activities including the excavation was handled by Artimus

Construction, Inc. and its excavation and foundation contractor Indus General Construction Inc. In addition, underpinning of the certain adjacent structures was conducted during the week of November 14, 2011. Since the Site is surrounded by adjoining buildings or New York City streets that are serviced with storm water catch basins, precipitation to the ground surface adjoining the Site did not result in a soil erosion or sedimentation control issue. However, in anticipation of the need to remove excessive quantities of storm water that could pool up in low portions of the Site during excavation activities a discharge permit was obtained from the NYCDEP by Artimus Construction, Inc. on November 23, 2011.

Soil Screening

- Visual, olfactory and PID soil screening and assessment were performed by a Qualified Environmental Professional (QEP) during all remedial excavations into known or potentially contaminated material. Soil screening was performed regardless of when the invasive work was done and included all excavation and invasive work performed during the remedy and during the development phase, such as excavations for foundations and utility work. There were no elevated PID readings obtained during the excavation activities except on February 22, 2012. On this date it was determined that the PID readings were the result of a minor hydraulic fluid leak from the excavation equipment. The affected soil was properly handled and transported to the Pure Soil Technology Facility which is permitted to accept soil containing hydraulic fluid.

Stockpile Management

- The majority of the excavation activities were conducted by directly loading the material into trucks for off-site disposal. However, during the first stage of the excavation soil stockpiles were generated. Stockpiles of soil were kept covered at all times with appropriately anchored tarps. Stockpiles were inspected each work day and after every storm event, damaged tarp covers were promptly repaired/replaced. Results of inspections were recorded in a logbook maintained at the Site and were available for inspection by NYC OER. A hose connected to a fire hydrant was available on-site for dust control.

Truck Inspection

- A gravel pad was installed near the Site entrance and a truck inspection and wash station was operated on-site. If needed, all outbound trucks were washed at the truck wash before leaving the Site until the remedial construction was complete. Locations where vehicles entered or exited the Site were inspected daily for evidence of off-site sediment tracking. Cleaning of the adjacent streets was performed as needed to maintain a clean condition with respect to Site-derived materials.

Site Security

- A wooden construction fence was erected around the perimeter of the Site. The entrances were secured with chains and locks when the Site was closed. During hours of operation a security guard was stationed at the entrance along 8th Avenue. All personnel entering the Site were required to sign in and out the Site. Security cameras were also in-place at various locations to record on-site activities.

Nuisance Controls

- Dust control was obtained by conducting dust monitoring at the perimeter of the Site during invasive on-site work. Although there were no elevated dust readings observed during the excavation activities, dust suppression was achieved through the use of a dedicated on-site hose connected to a fire hydrant. The hose was equipped with a nozzle capable of spraying water directly onto off-road areas including excavations and stockpiles to prevent a dust situation from on-site excavation and trucking equipment. A gravel apron was provided at the truck entry/exit point of the Site to provide a clean and dust-free road surface. In addition, on-site roads were limited in length to minimize the area required for water sprinkling. There were no dust complaints received during the performance of the remedial activities.

- Odor control was obtained by screening excavated soil and conducting perimeter monitoring with a PID during intrusive on-site work. In addition, Site personnel conducting the excavation used olfactory senses to detect any nuisance odors during excavation. To further prevent any odors all stockpiles were covered with secured tarps and the majority of the soil was directly loaded into trucks for off-site disposal. There were no odor complaints received during the performance of the remedial activities.

- During the excavation of bedrock on November 7, 2011, the NYCDEP arrived at the Site in response to a noise complaint. It was determined that the noise was attributable to the excavation equipment chipping bedrock in the excavation. At the time of the incident three machines were being utilized to excavate the bedrock and DEP personnel equipped with a decibel meter informed construction personnel that the level was ½ to 1 decibel above NYC limits. No violation was

issued and work was continued, with only two excavators. These actions reduced the noise level and the construction team, using their decibel meter on-site during the rock chopping to ensure that noise was properly controlled.

Reporting

Daily reports were submitted to NYCOER via e-mail during the implementation by the end of each day following the reporting period and included:

- An update of progress made during the reporting day;
- Locations of work and quantities of material imported and exported from the Site;
- References to alpha-numeric map for Site activities;
- A summary of any and all complaints with relevant details (names, phone numbers);
- A summary of CAMP findings, including excursions (if any);
- An explanation of notable Site conditions.

Daily reports included a description of daily activities keyed to an alpha-numeric grid map for the Site that identified the work areas. The reports included a summary of air sampling results, odor and dust problems and corrective actions, and all complaints received from the public. All daily reports are included in electronic format in Appendix F. The digital photo log required by the RAWP is included in each daily report as well as Appendix D.

4.3 WASTE CLASSIFICATION TESTING

On August 30, 2011, a track-mounted excavator was utilized to install eight test pits identified as TP-1 through TP-8 in a uniform pattern across the Site. Each test pit was extended from grade to approximately 15 feet deep or bedrock (whichever was shallower). During the excavation activities, CA RICH personnel continuously screened the subsurface soil for VOCs with a PID for evidence of volatile organic contamination. There were no PID readings observed during the sampling event. Soil samples were collected from the test pits in accordance with the frequency criteria required by two prospective recycling facilities and two beneficial reuse facilities.

The sampling included the collection of a discrete grab sample from middle sidewall of each test pit for VOCs using the En Core sampling method. An additional discrete sample for VOCS was collected with an En Core sample from the lower middle sidewall of test pits TP-1, TP-2, TP-3 and TP-4 for a total of 12 VOC samples. A five-point composite sample was collected from the sidewalls and bottom of test pits TP-5, TP-6, TP-7 and TP-8 for an expanded list of chemical parameters in order to meet the acceptance criteria of multiple beneficial reuse facilities. The sampling for test pits TP-1, TP-2, TP-3 and TP-4, included the collection of one five-point composite sample from 0-7 feet and a second from 7-14 feet for the expanded list of chemical parameters. In addition, 12 five-point composite samples were collected for Total Petroleum Hydrocarbons.

Gloves worn for sample handling were discarded between sample collections. All soil samples were placed in lab-supplied containers, stored in an ice-filled cooler and submitted to American Analytical Laboratories (a State-certified laboratory located in Farmingdale, NY) for analysis. A complete copy of the Soil Profile Report further detailing sampling methodologies and a copy of the soil test results are included in

Appendix G. A Site plan depicting test pit locations on an alphanumeric grid is included as Figure 4. A summary of the testing parameters is provided on Table 7.

The results of the waste classification testing indicated that test pits TP-5 and TP-7 must be disposed of as lead-contaminated hazardous soil while the remainder of the soil would qualify for disposal at Soil Safe's facility in Logan, New Jersey or for beneficial reuse at the Bellmawr Redevelopment site. Based on these results, the construction team made plans to begin the Site excavation with the removal of the hazardous soil identified in test pits TP-5 and TP-7 and then proceed with site-wide excavation of non-hazardous material. Copies of the disposal facility approval letters and operating permits for Soil Safe and the Bellmawr Redevelopment Site are included in Appendix H.

4.4 MATERIALS EXCAVATION AND REMOVAL

4.4.1 LEAD-HAZARDOUS SOIL

The results of the soil waste classification testing indicated that the soil from test pits TP-5 and TP-7 contained hazardous levels of lead. Based on the results, a RCRA Subtitle C Site Identification Form was submitted to the United States Environmental Protection Agency (USEPA) notifying them of the generation of hazardous waste. The USEPA assigned EPA ID number NYR000814218 to the Site and arrangements were made to excavate the soil for off-site disposal at the Clean Earth of North Jersey (CENJ) facility. A copy of the approval letter and operating permit from the CENJ facility is included in Appendix H.

Upon receipt of the disposal approval paperwork, excavation equipment was utilized to unearth the soil from former test pits TP-5 and TP-7. On October 5, 2011 three truckloads of soil were removed from the affected areas in accordance with the excavation protocols established in the RAWP. The material was transported by licensed

waste haulers to the CENJ facility under waste manifest control. After the excavation a five point composite samples was collected from each of the sidewalls both excavations and analyzed for total and TCLP lead. The bottom of each excavation was extended to bedrock. The soil samples were submitted to American Analytical Laboratories for expedited chemical analysis and the excavation areas were isolated using temporary construction fences.

The soil test results indicated that the lead levels were reduced below hazardous levels at all locations except the north sidewall of TP-5 and the east sidewall of TP-7. On October 7, 2011 an additional five feet of soil was removed from the respective sidewalls of each excavation and a second set of soil samples of each sidewall were collected for TCLP and total lead analysis. The samples were submitted to American Analytical Laboratories for expedited chemical analysis and the excavation areas were isolated using temporary construction fences. The results for the second set of samples indicated that the soil containing hazardous levels of lead was removed and the remaining soils could be disposed as non-hazardous material. The total lead concentrations at the perimeter of the excavation for TP-5 ranged from 4.03 ppm to 267 ppm and the TCLP lead concentrations ranged from non-detect to 1.18 mg/L. The total lead concentrations at the perimeter of the excavation for TP-7 ranged from 6.66 ppm to 310 ppm and the TCLP lead concentrations ranged from 0.014 mg/L to 2.52 mg/L.

Copies of the hazardous waste manifests documenting the proper off-site transportation of 148.20 tons of hazardous soil to the CENJ facility are included in Appendix I. A summary of the waste disposal activities is provided on Table 5. The locations of the former hazardous soil lead areas and sampling locations are depicted on Figure 6. A copy of the laboratory results for the total and TCLP lead samples is included in Appendix J.

4.4.2 NON-HAZARDOUS MATERIAL

The non-hazardous soil excavation was conducted between October 7, 2011 and February 23, 2012. The excavation included the removal of all on-site soils to the shallow bedrock interface. The elevation of bedrock for the entire Site with the exception of the northwest corner was less than the required excavation depth necessary to facilitate installation of the new buildings foundation (15-feet). The presence of shallow bedrock required the excavation and removal of approximately 10,000 cubic yards of bedrock to achieve the required depth for construction. The broken up pieces of bedrock, brick and concrete were segregated and transported off-site to Red Roc Materials in Lyndhurst, NJ, Bay Shore Recycling in Woodbridge, NJ.

As previously detailed in Section 3.5, the elevation of bedrock sloped down below the required excavation depth of 15 feet in the northwest corner of the Site. Prior to over-excavating the soil remaining between the required depth of excavation and the bedrock interface soil samples were collected to determine the levels of any residual contaminants. Based on the results of soil samples collected between 14 and 16 feet below it was determined that levels of pesticides and select metals were above Track 1 Unrestricted Soil Cleanup Objectives (SCOs). The residual contaminant levels were discussed with both NYCOER and the Site Owner and a decision was made to advance the excavation in the northwest corner of the Site and removal all soil until the bedrock interface was encountered to achieve the projects primary cleanup objective of Track 1 Unrestricted SCO.

As the excavation neared completion additional waste classification samples were collected on January 10, 2012 and February 3, 2012 to meet the frequency criteria of the Soil Safe facility. Due to the presence of excess amount of debris beneath the construction ramp in grids C1, C2 and C3 the new results along with the previous results

from test pit TP-3 were forwarded to the Pure Soil Technologies facility in Jackson Township, NJ for disposal approval. A copy of the additional waste classification data is included in Appendix G. A copy of Pure Soil Technologies approval letter and operating permit are included in Appendix H. There were no underground storage tanks encountered during the excavation and no material was reused on-site.

4.5 MATERIALS DISPOSAL

The soil disposal activities were conducted between October 7, 2011 and February 23, 2012. The site-wide excavation included the off-site disposal of a total of 14,568.70 tons of non-hazardous soil, 148.20 of lead hazardous soil, and approximately 10,750 cubic yards of bedrock, brick and concrete. All transport of materials was performed by licensed haulers in accordance with appropriate local, State, and Federal regulations, including 6 NYCRR Part 364. Haulers were appropriately licensed and trucks properly placarded. Loaded vehicles leaving the Site were appropriately tarped, securely covered, and manifested in accordance with appropriate local, State, Federal and New York State Department of Transportation requirements (and all other applicable transportation requirements).

Prior to shipping any waste off-site the selected disposal facilities were provided with information indicating that the material was being generated as part of a cleanup at a NYC Brownfield Site. The facilities were also provided with complete copies of waste characterization test results, a summary of the soil profiling methodologies and historical environmental reports. A copy of the letters to the facilities and waste classification results are included in Appendix G.

Upon review of the soil profile and analytical data approval letters were received from Soil Safe, Inc., Pure Soil Technologies and the Bellmawr Redevelopment Site acknowledging their acceptance of the material. Copies of acceptance letters from each disposal facility stating it is approved to accept the material and the corresponding operating permits are included in Appendix H.

The tonnage and destination of the soil removed and disposed off-site is presented below:

Destination	Type of Material	Quantity	No of Trucks
Clean Earth of NJ	Lead-Hazardous Soil	148.20 tons	5
Bellmawr Site	Non-Hazardous Soil	572.84 tons	18
Soil Safe, Inc.	Non-Hazardous Soil	11,583.61 tons	343
Pure Soil Technologies	Non-Hazardous Soil	2,412.25 tons	75
	Totals	**14716.90 tons**	**441**

A summary of the hazardous and non-hazardous waste disposal shipment is presented on Tables 5 and 6. Copies of the final shipping manifest for each shipment are included in Appendix I and K. Tables 5 and 6 summarize the dates, destination and total quantities of each class truckload of material removed from the Site.

4.6 BACKFILL IMPORT

Prior to installing the building foundation approximately 1,500 cubic yards of recycled crushed concrete aggregate meeting NYC DOT specifications was imported to the Site from NYC Concrete Materials in Maspeth, NY. The material was utilized to bring over excavated areas up to the required construction grade.

4.7 DEMARACTION

All on-site soils were excavated until bedrock and no residual contaminated soil remained on-site. As such demarcation was not necessary.

5.0 ENGINEERING CONTROLS

The remediation of the Site included site-wide excavation to bedrock to achieve a Track 1 cleanup. As such no engineering controls are required under this Remedial Action. As an additional measure and a building structural requirement, a water-proofing membrane known as Grace 300LT and 160LT was installed beneath the entire Site. The water-proofing membrane was installed by building contractors with its installation periodically inspected by the Remedial Engineer or his designee. The water/vapor barrier was installed according to the manufacturer's product specifications over the entire bottom of the Site including the elevator shafts and sump ejector pits. A technical product specification sheet for the Grace 160LT and 300LT barriers is included as Appendix L. Photographs documenting the installation are included in Appendix D. The Grace water-proofing membrane will also serve as an additional layer of protection against potential soil vapor intrusion from an unknown off-site source in the future. As part of the building design, the sub-grade parking garage will be ventilated in accordance with the City of New York building code.

6.0 INSTITUTIONAL CONTROLS

The remediation of the Site included site-wide excavation to bedrock to achieve a Track 1 cleanup, As such no Institutional Controls are required under this Remedial Action.

7.0 SITE MANAGEMENT PLAN

The remediation of the Site included site-wide excavation to bedrock to achieve a Track 1 cleanup. As such a Site Management Plan is not required under this Remedial Action.

8.0 REFERENCES

1) CA RICH Consultants, Inc. March 2011. Phase I Environmental Site Assessment, 260 West 26th Street, New York, New York.

2) CA RICH Consultants, Inc. April 2011. Remedial Investigation Report, 260 West 26th Street, New York, New York.

3) NYSDEC. October 22, 1993. Technical and Operational Guidance Series (1.1.1) Ambient Water Quality Standards and Guidance Values.

4) Osmundsen, Stephen J., April 2011. Remedial Action Work Plan, 260 West 26th Street, New York, New York.

5) CA RICH Consultants, Inc., May 17, 2011. Stipulation List for Remedial Action Work Plan, 260 West 26th Street, New York, New York.

6) New York State Department of Environmental Conservation. Dec. 14, 2006. 6 NYCRR Part 375 Environmental Remediation Programs, Soil Cleanup Objectives & Cleanup Levels.

7) New York State Department of Environmental Conservation, CP-51 Soil Cleanup Guidance; October 21, 2010.

FIGURES

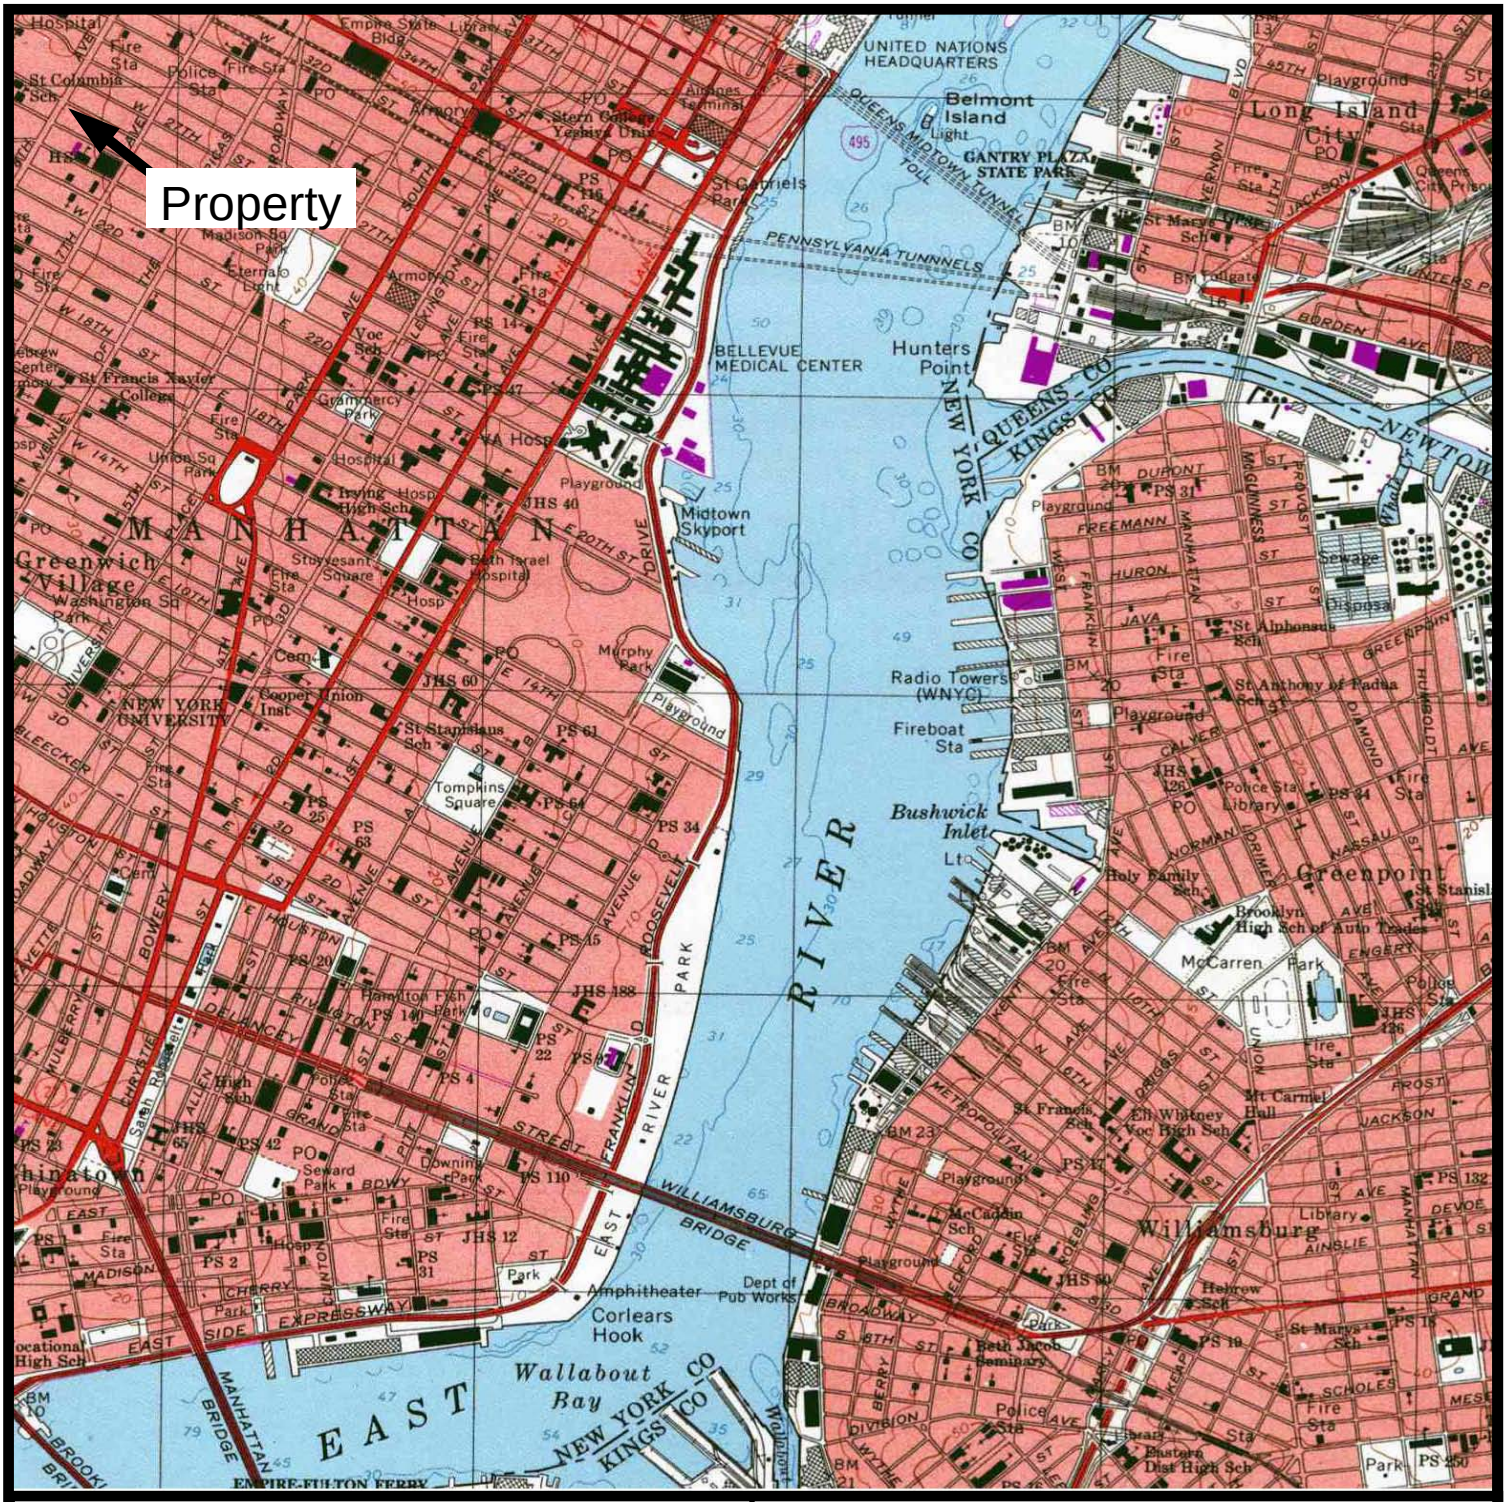

APPROX. SCALE (ft.)

0 1,200 2,400 N

Adapted from USGS 1995 Brooklyn Quadrangle Map.

CA RICH CONSULTANTS, INC.

Certified Ground Water and Environmental Specialists
17 Dupont Street, Plainview, NY 11803

TITLE: PROPERTY LOCATION MAP	DATE: 2/25/11
	SCALE: AS SHOWN
FIGURE: 1	DRAWN BY: JEP
DRAWING:	260 West 26th Street Manhattan, New York
	APPR. BY: DS

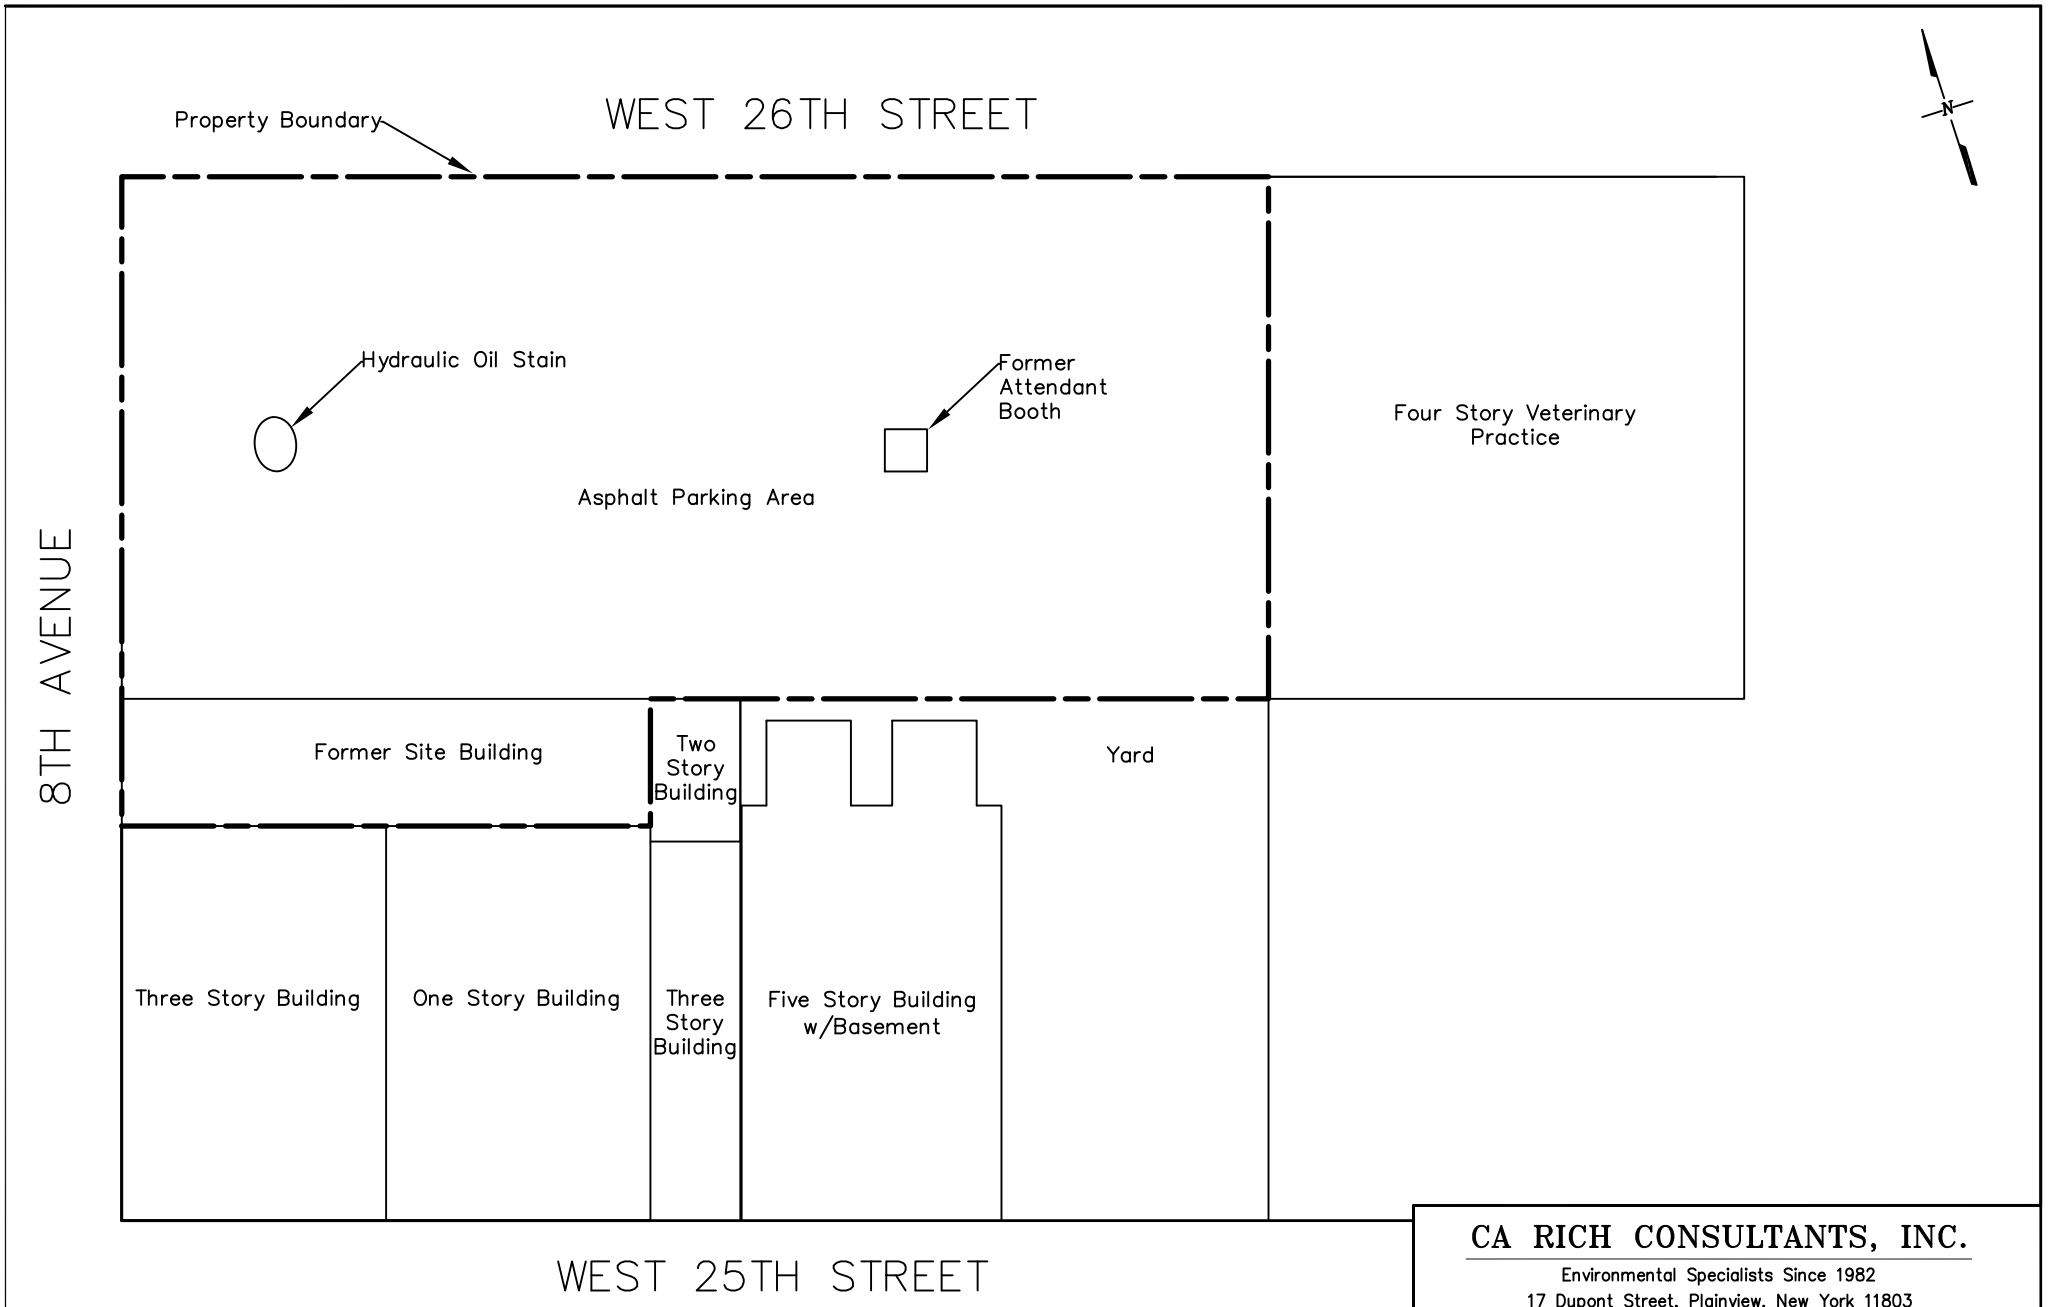

CA RICH CONSULTANTS, INC.

Environmental Specialists Since 1982

17 Dupont Street, Plainview, New York 11803

TITLE: Site Plan and Adjoining Properties		DATE: 4/4/2012
		SCALE: As Shown
FIGURE: 2	260 West 26th Street Manhattan, New York	DRAWN BY: J.T.C.
DRAWING NO: 2011-M7E		APPR. BY: S.T.M.

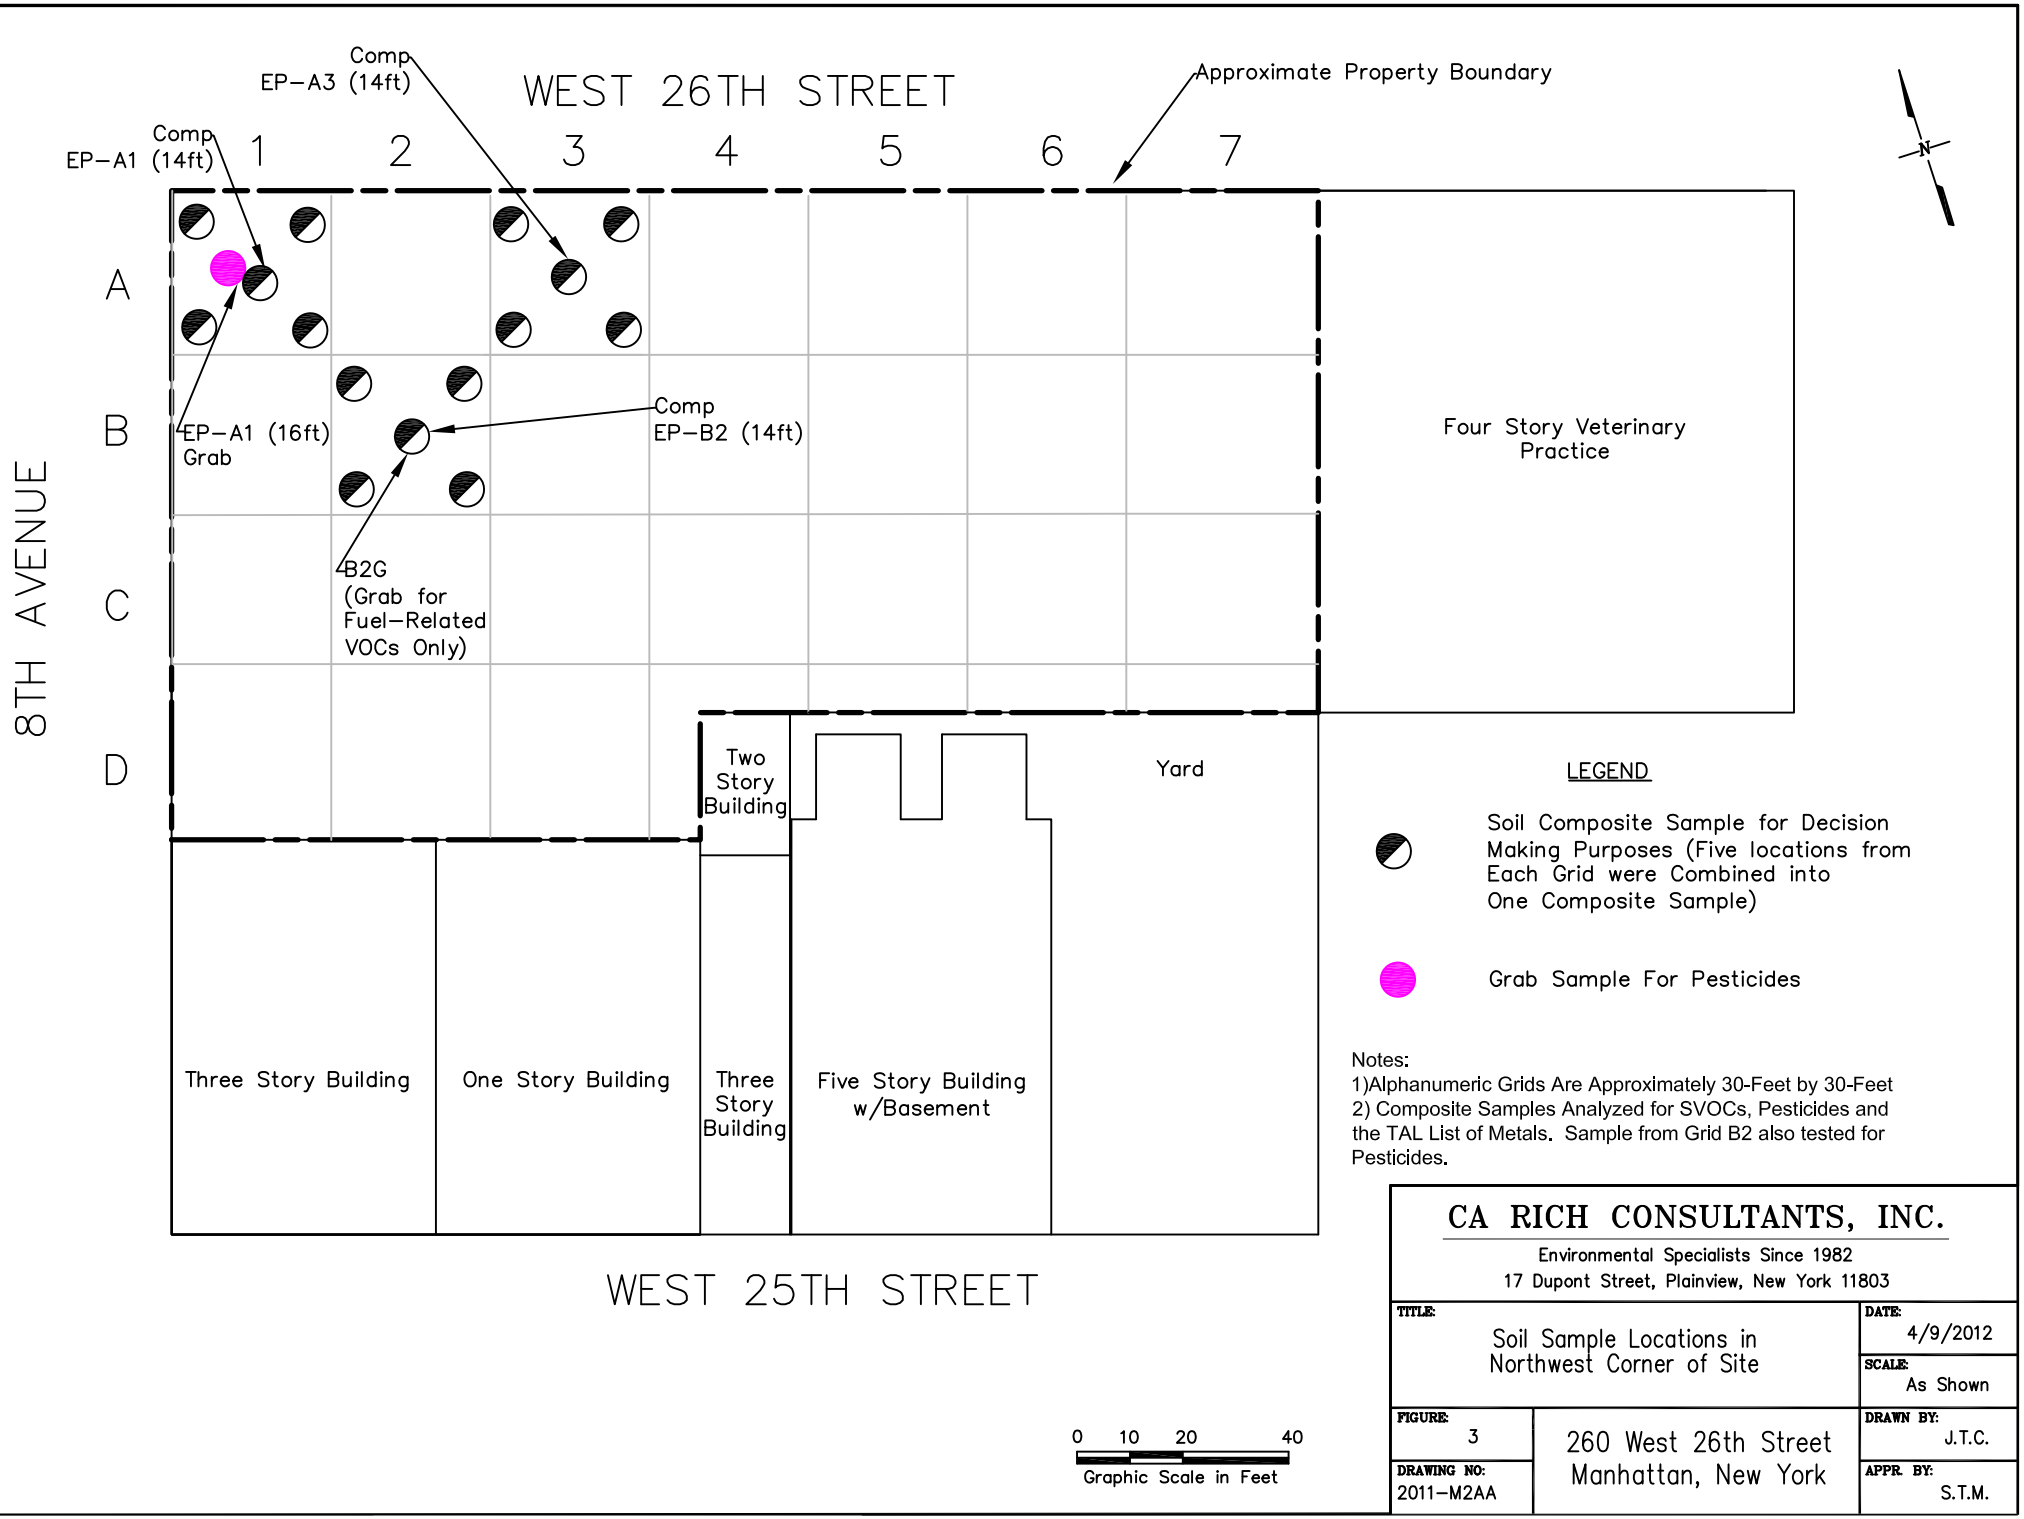
WEST 26TH STREET
WEST 25TH STREET
8TH AVENUE
Approximate Property Boundary
Comp EP-A3 (14ft)
Comp EP-A1 (14ft)
EP-A1 (16ft) Grab
Comp EP-B2 (14ft)
B2G (Grab for Fuel-Related VOCs Only)
Four Story Veterinary Practice
Two Story Building
Yard
Three Story Building
One Story Building
Three Story Building
Five Story Building w/Basement
LEGEND
Soil Composite Sample for Decision Making Purposes (Five locations from Each Grid were Combined into One Composite Sample)
Grab Sample For Pesticides
Notes:
1)Alphanumeric Grids Are Approximately 30-Feet by 30-Feet
2) Composite Samples Analyzed for SVOCs, Pesticides and the TAL List of Metals. Sample from Grid B2 also tested for Pesticides.
0 10 20 40
Graphic Scale in Feet
CA RICH CONSULTANTS, INC.
Environmental Specialists Since 1982
17 Dupont Street, Plainview, New York 11803
TITLE: Soil Sample Locations in Northwest Corner of Site
DATE: 4/9/2012
SCALE: As Shown
FIGURE: 3
DRAWING NO: 2011-M2AA
260 West 26th Street Manhattan, New York
DRAWN BY: J.T.C.
APPR. BY: S.T.M.

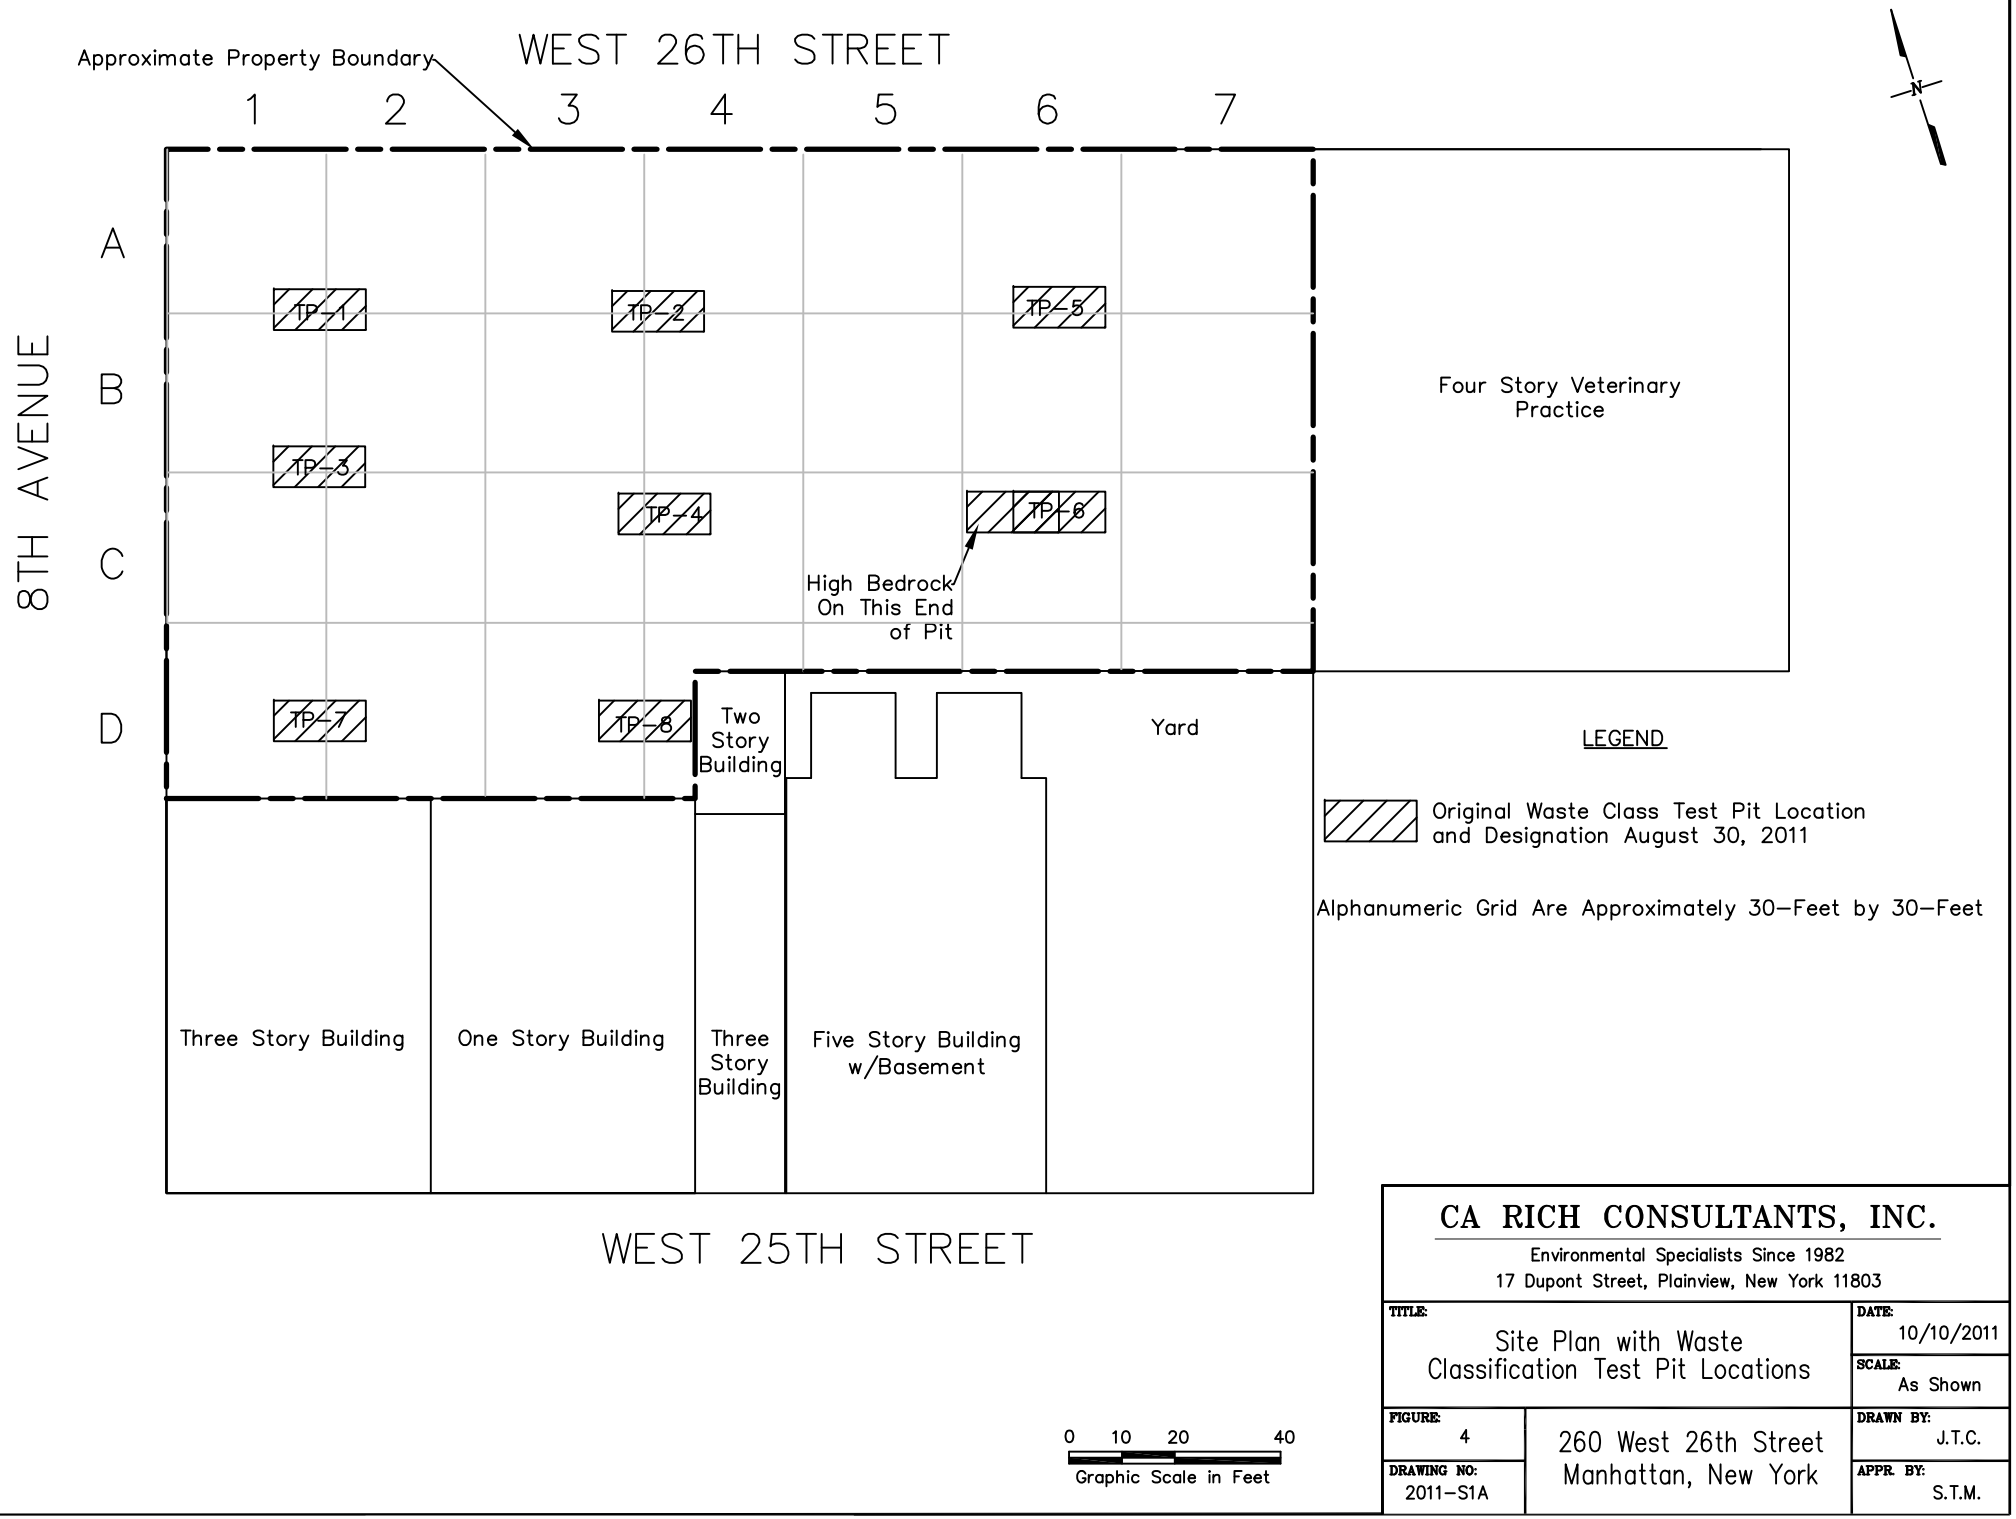

CA RICH CONSULTANTS, INC.

Environmental Specialists Since 1982

17 Dupont Street, Plainview, New York 11803

TITLE: Site Plan with Waste Classification Test Pit Locations	DATE: 10/10/2011
	SCALE: As Shown
FIGURE: 4	DRAWN BY: J.T.C.
DRAWING NO: 2011-S1A	APPR. BY: S.T.M.

260 West 26th Street
Manhattan, New York

ORGANIZATIONAL CHART FOR
260 WEST 26TH STREET
NEW YORK, NEW YORK

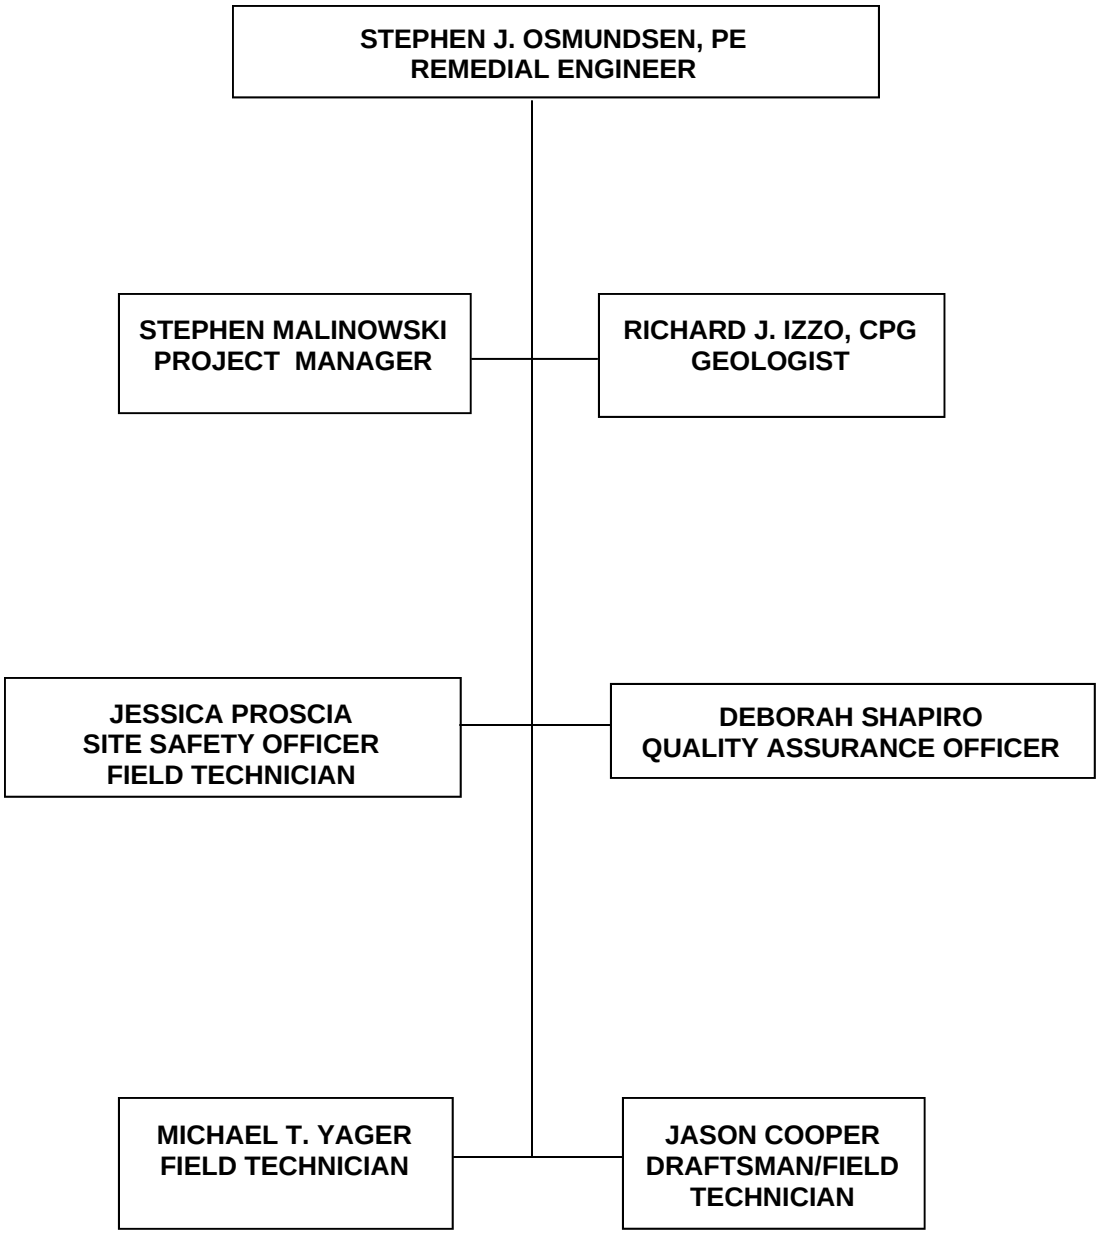

Figure 5

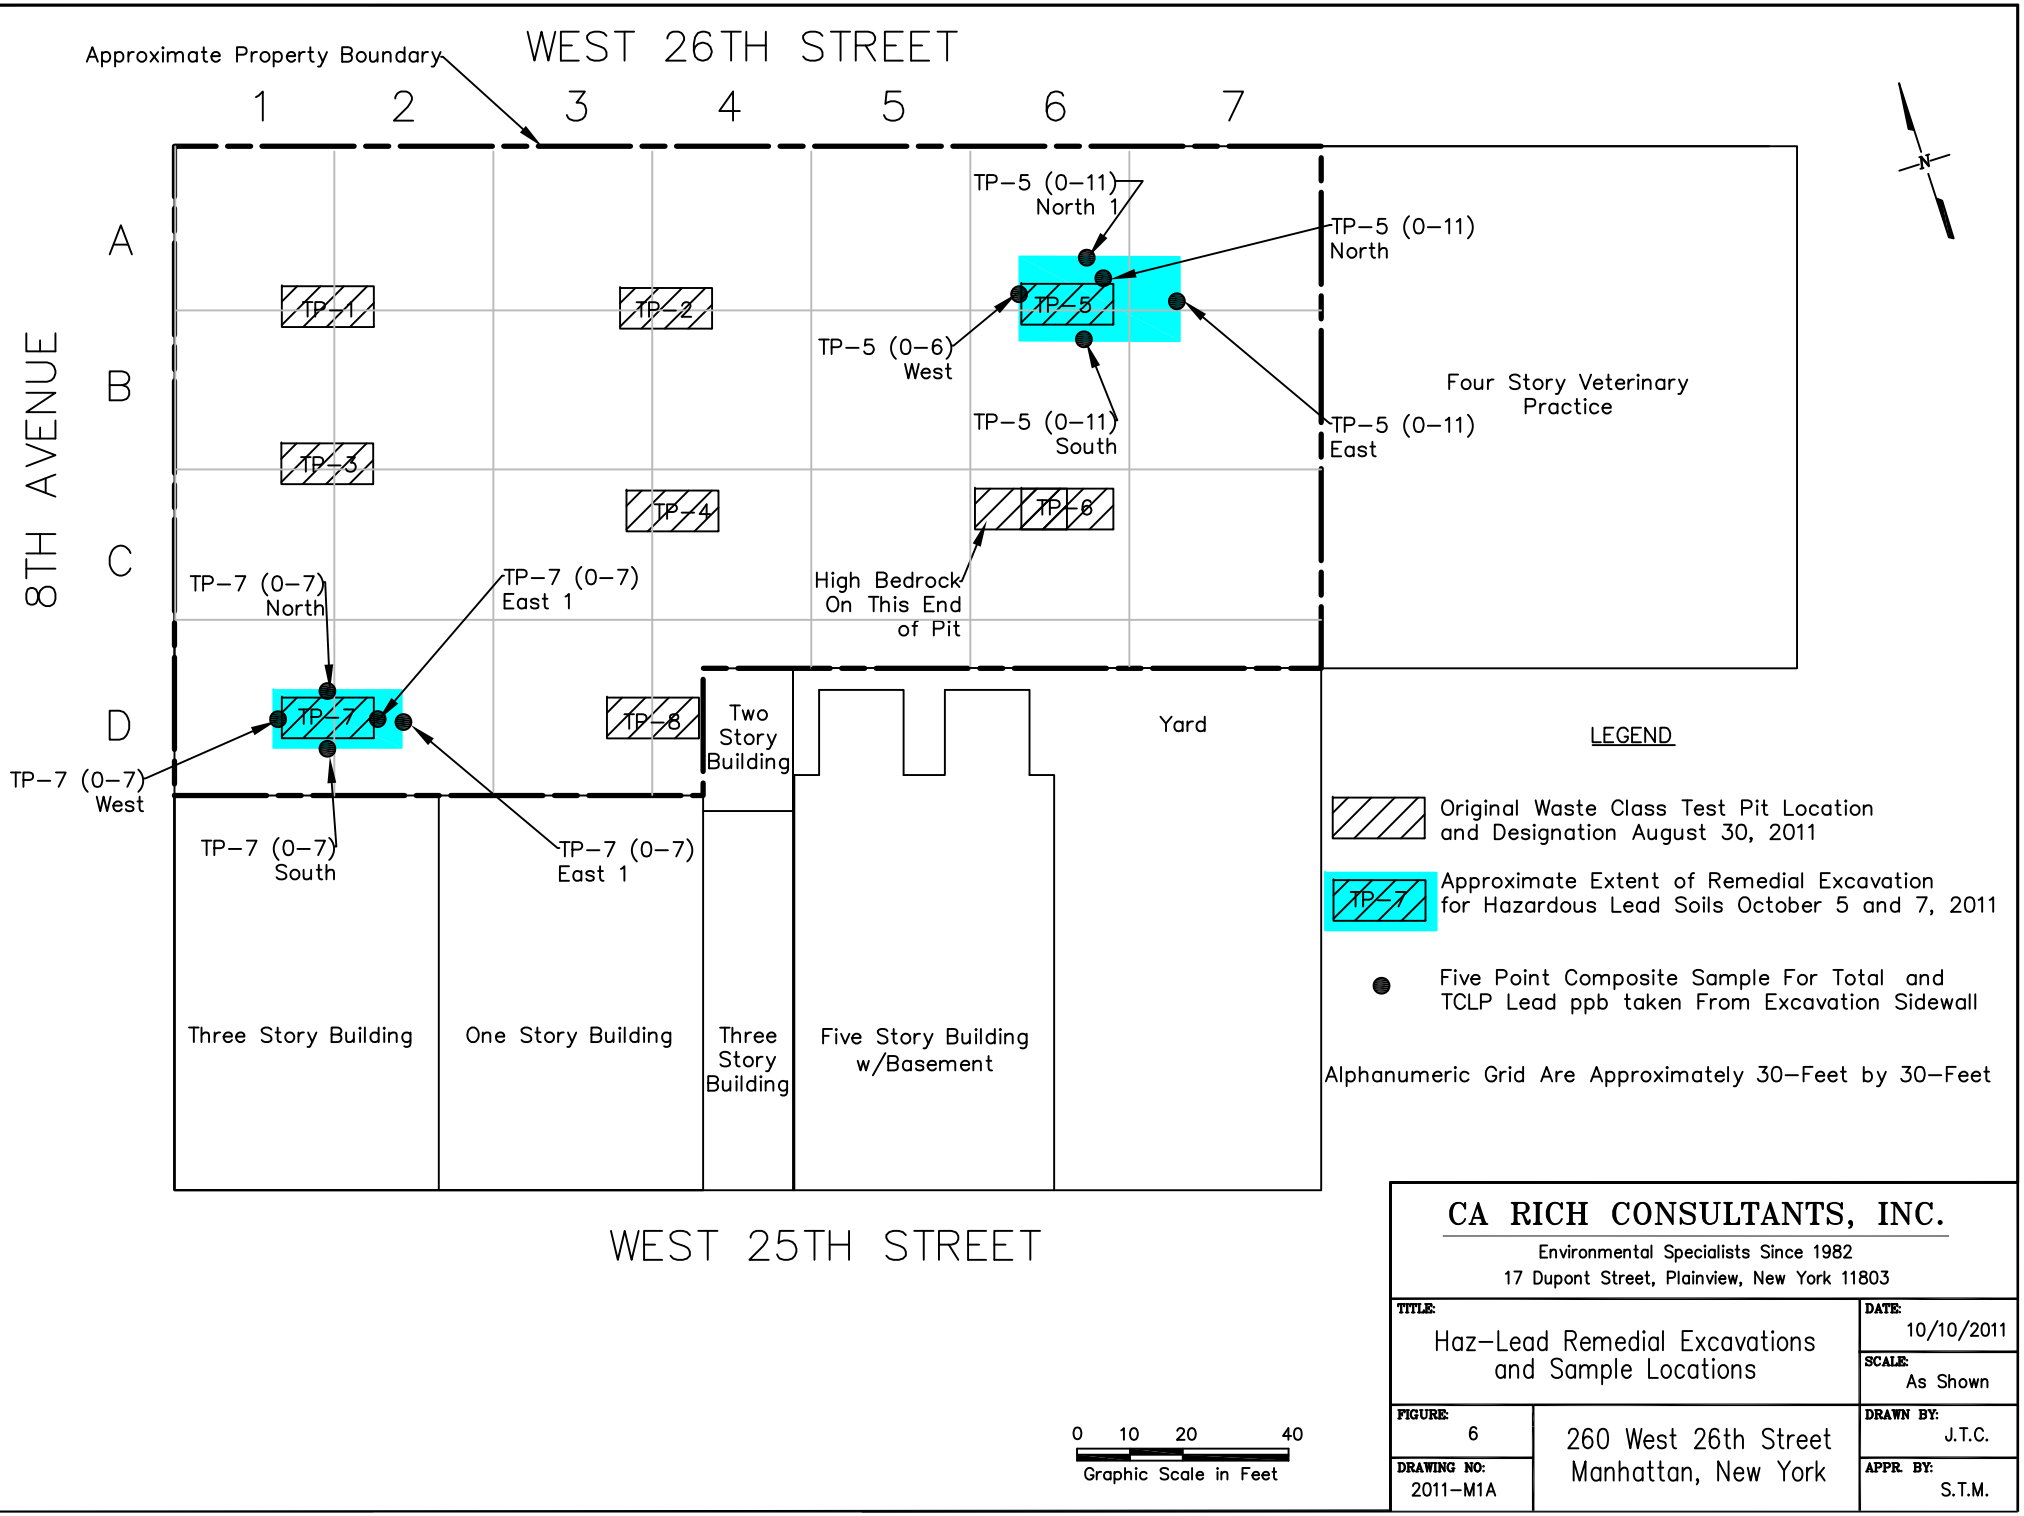

CA RICH CONSULTANTS, INC.

Environmental Specialists Since 1982

17 Dupont Street, Plainview, New York 11803

TITLE: Haz-Lead Remedial Excavations and Sample Locations	DATE: 10/10/2011
	SCALE: As Shown
FIGURE: 6	DRAWN BY: J.T.C.
DRAWING NO: 2011-M1A	260 West 26th Street Manhattan, New York
	APPR. BY: S.T.M.

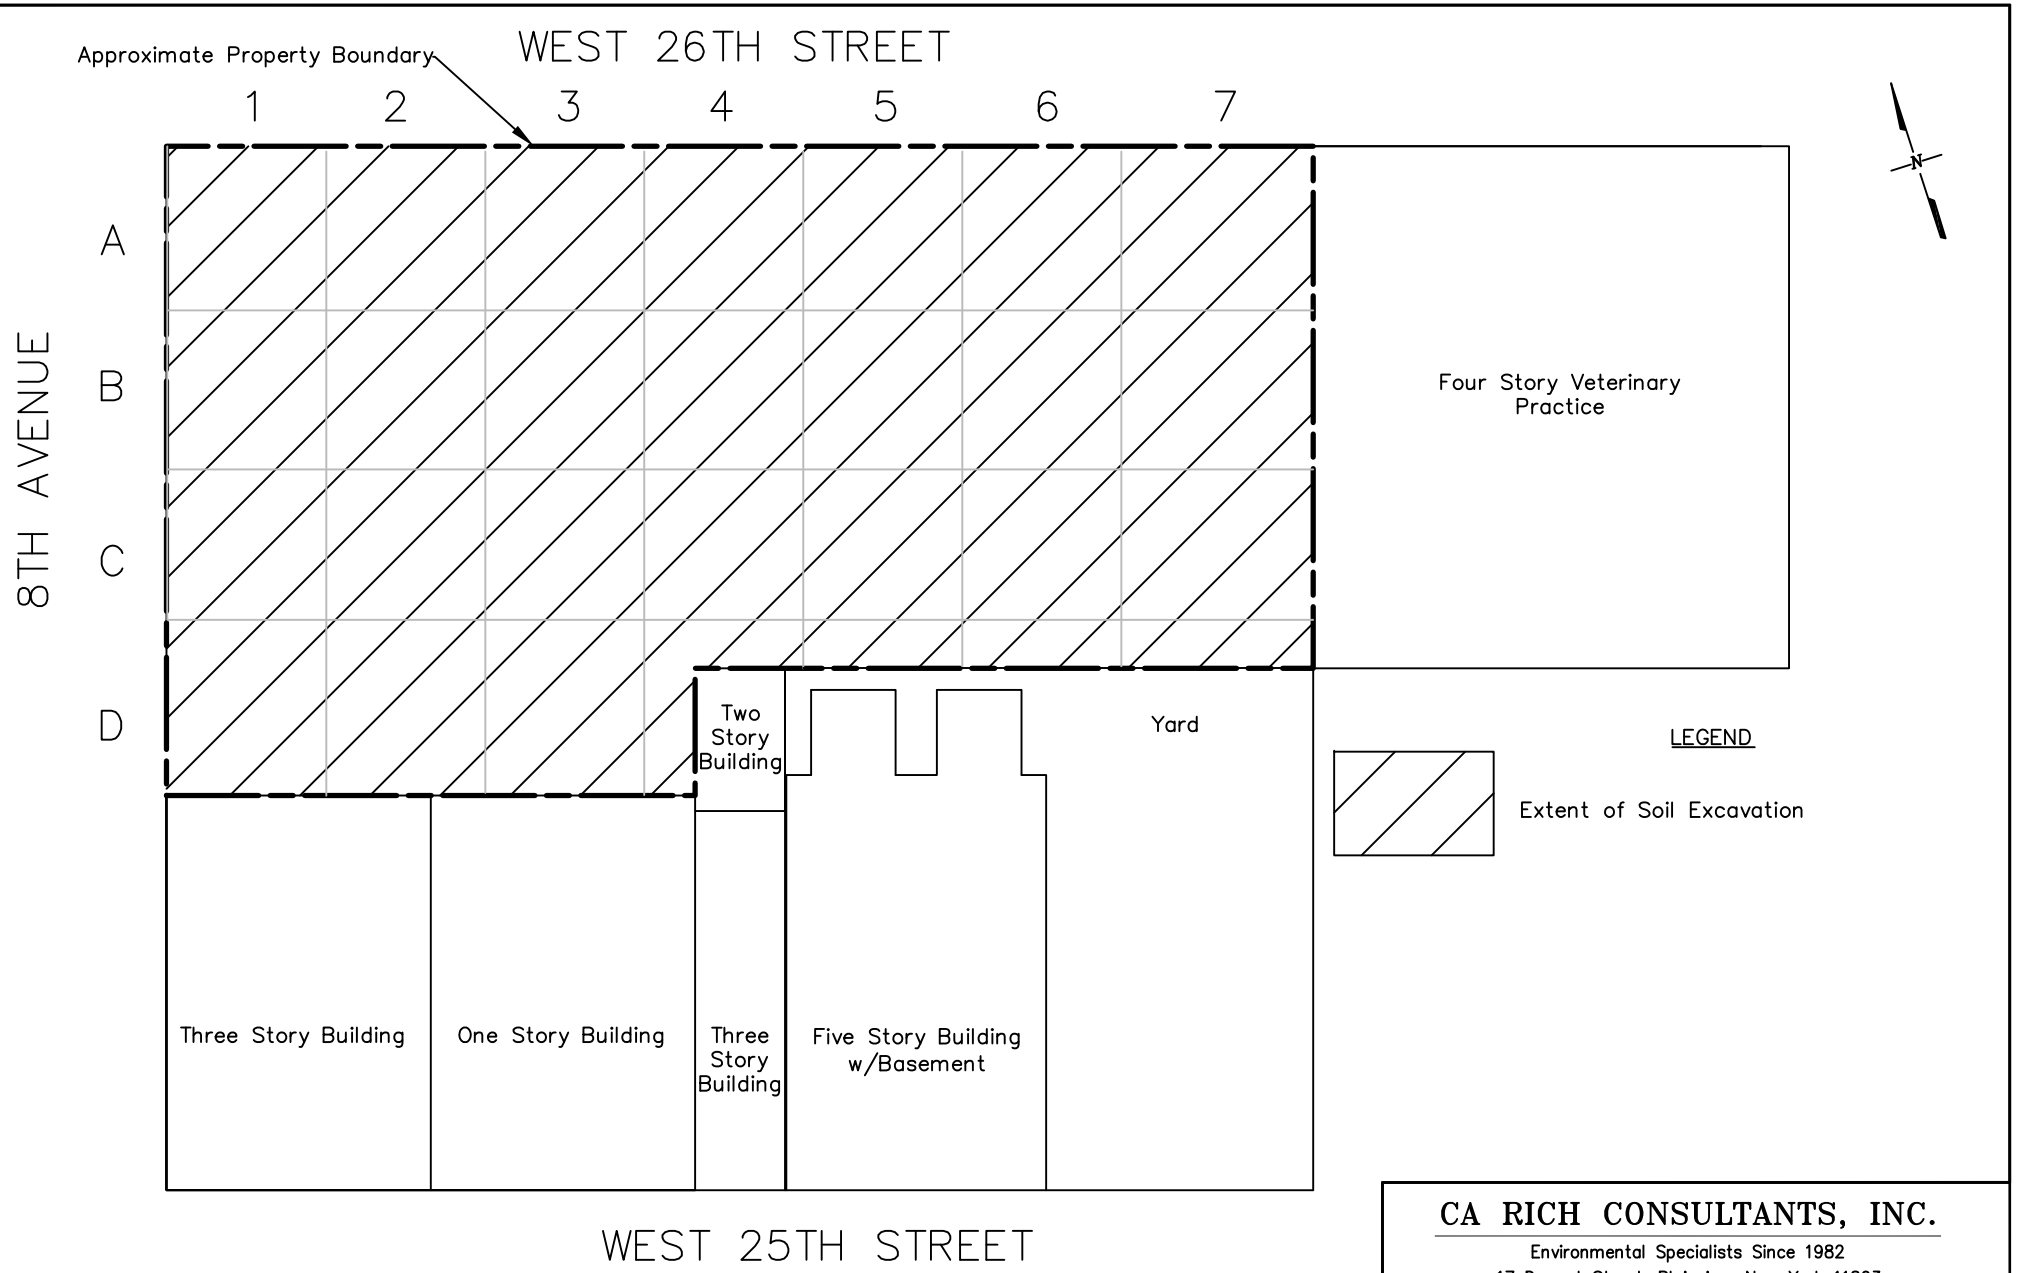

CA RICH CONSULTANTS, INC.

Environmental Specialists Since 1982

17 Dupont Street, Plainview, New York 11803

TITLE: Map Illustrating the of Extent Site–wide Soil Excavation	DATE: 4/5/2012
	SCALE: As Shown
FIGURE: 7	DRAWN BY: J.T.C.
DRAWING NO: 2011–N1A	260 West 26th Street Manhattan, New York
	APPR. BY: S.T.M.

TABLES

TABLE 1

Analytical Results for Volatile Organic Compounds in Soil Samples

260 West 26th Street, New York, NY

Sample ID	EP-B2G	EP-XX	*Part 375
Sample Depth	14'	14'	SCOs
Matrix	Soil	Soil	Unrestricted
Date Sampled	1/13/2012	1/13/2012	Use
Units	ug/Kg	ug/Kg	ug/Kg
Volatile Organics			
Benzene	ND	ND	60
n-Butylbenzene	ND	ND	12,000
sec-Butylbenzene	ND	ND	11,000
tert-Butylbenzene	ND	ND	5,900
Ethylbenzene	0.35 J	0.25 J	1,000
Isopropylbenzene	ND	ND	2,300 **
p-Isopropyltoluene	3.8 J	1.2 J	10,000 **
Methyl Tert Butyl Ether	ND	ND	930
Naphthalene	2.0 J	1.8 J	1,2000 **
n-Propylbenzene	ND	ND	3,900
Toluene	ND	ND	700
1,2,4-Trimethylbenzene	ND	ND	3,600
1,3,5-Trimethylbenzene	ND	0.27 J	8,400
m,p-Xylene	0.80 J	0.53 J	260
o-Xylene	0.34 J	0.26 J	260
Xylene (total)	1.1 J	0.79 J	260

Notes:

All concentrations are reported in micrograms per kilogram (μg/kg) or parts per billion.

ND=Indicates the compound was analyzed for but not detected.

Sample EP-XX is a duplicate of Sample EP-B2G

J=Analyte detected below quantitation limits

** 6 NYCRR Part 375 Unrestricted Use Soil Cleanup Objectives.*

*** Guidnace value for these compounds were obatined from the NYSDEC CP-51 Guidance document.*

TABLE 2
Analytical Results for Semi-Volatile Organic Compounds in Soil Samples
260 West 26th Street, New York, NY

Sample ID	EP-A1	EP-A3	EP-B2	EP-X	*Part 375
Sample Depth	14'	14'	14'	14'	SCOs
Matrix	Soil	Soil	Soil	Soil	Unrestricted
Date Sampled	1/13/2012	1/13/2012	1/13/2012	1/13/2012	Use
Units	ug/Kg	ug/Kg	ug/Kg	ug/Kg	ug/Kg
Semi Volatile Organics					
2-Chlorophenol	ND	ND	ND	ND	NVG
4-Chloro-3-methyl phenol	ND	ND	ND	ND	NVG
2,4-Dichlorophenol	ND	ND	ND	ND	NVG
2,4-Dimethylphenol	ND	ND	ND	ND	NVG
2,4-Dinitrophenol	ND	ND	ND	ND	NVG
4,6-Dinitro-o-cresol	ND	ND	ND	ND	NVG
2-Methylphenol	ND	ND	ND	ND	330
3&4-Methylphenol	ND	ND	ND	ND	NVG
2-Nitrophenol	ND	ND	ND	ND	NVG
4-Nitrophenol	ND	ND	ND	ND	NVG
Pentachlorophenol	ND	ND	ND	ND	800
Phenol	ND	ND	ND	ND	330
2,3,4,6-Tetrachlorophenol	ND	ND	ND	ND	NVG
2,4,5-Trichlorophenol	ND	ND	ND	ND	NVG
2,4,6-Trichlorophenol	ND	ND	ND	ND	NVG
Acenaphthene	30.9 J	58.7	52.5	ND	20,000
Acenaphthylene	ND	26.3 J	28.4 J	ND	100,000
Acetophenone	ND	ND	ND	ND	NVG
Anthracene	59.9	146	146	15.9 J	100,000
Atrazine	ND	ND	ND	ND	NVG
Benzo(a)anthracene	135	304	348	71.8	1,000
Benzo(a)pyrene	122	271	314	67.4	1,000
Benzo(b)fluoranthene	109	256	315	60.4	1,000
Benzo(g,h,i)perylene	69.6	168	199	43.1	100,000
Benzo(k)fluoranthene	83.9	154	180	44.4	800
4-Bromophenyl phenyl ether	ND	ND	ND	ND	NVG
Butyl benzyl phthalate	ND	ND	ND	ND	NVG
1,1'-Biphenyl	ND	ND	ND	ND	NVG
Benzaldehyde	ND	ND	ND	ND	NVG
2-Chloronaphthalene	ND	ND	ND	ND	NVG
4-Chloroaniline	ND	ND	ND	ND	NVG
Carbazole	23.7 J	72	70	ND	NVG
Caprolactam	ND	ND	ND	ND	NVG
Chrysene	126	291	325	64.1	1,000
bis(2-Chloroethoxy)methane	ND	ND	ND	ND	NVG
bis(2-Chloroethyl)ether	ND	ND	ND	ND	NVG
bis(2-Chloroisopropyl)ether	ND	ND	ND	ND	NVG
4-Chlorophenyl phenyl ether	ND	ND	ND	ND	NVG
2,4-Dinitrotoluene	ND	ND	ND	ND	NVG
2,6-Dinitrotoluene	ND	ND	ND	ND	NVG
3,3'-Dichlorobenzidine	ND	ND	ND	ND	NVG
Dibenzo(a,h)anthracene	15.6 J	40.2	48.5	ND	330
Dibenzofuran	19.5 J	51.6 J	49.9 J	ND	7,000
Di-n-butyl phthalate	ND	ND	ND	ND	NVG
Di-n-octyl phthalate	ND	ND	ND	ND	NVG
Diethyl phthalate	ND	ND	ND	ND	NVG
Dimethyl phthalate	ND	ND	ND	ND	NVG
bis(2-Ethylhexyl)phthalate	93.6	133	109	69.4	NVG
Fluoranthene	306	727	813	131	100,000
Fluorene	32.1	73.9	67.7	ND	30,000
Hexachlorobenzene	ND	ND	ND	ND	330
Hexachlorobutadiene	ND	ND	ND	ND	NVG
Hexachlorocyclopentadiene	ND	ND	ND	ND	NVG
Hexachloroethane	ND	ND	ND	ND	NVG
Indeno(1,2,3-cd)pyrene	62.5	144	178	37.8	500
Isophorone	ND	ND	ND	ND	NVG
2-Methylnaphthalene	ND	31.1 J	19.7 J	ND	NVG
2-Nitroaniline	ND	ND	ND	ND	NVG
3-Nitroaniline	ND	ND	ND	ND	NVG
4-Nitroaniline	ND	ND	ND	ND	NVG
Naphthalene	24.9 J	49.3	30.7 J	ND	12,000
Nitrobenzene	ND	ND	ND	ND	NVG
N-Nitroso-di-n-propylamine	ND	ND	ND	ND	NVG
N-Nitrosodiphenylamine	ND	ND	ND	ND	NVG
Phenanthrene	237	692	683	72.6	100,000
Pyrene	253	640	687	131	100,000
1,2,4,5-Tetrachlorobenzene	ND	ND	ND	ND	NVG

Notes:
All concentrations are reported in micrograms per kilogram (μg/kg) or parts per billion.
NVG=No Value Given
J=Analyte detected below quantitation limits
EP-X is a field duplicate of sample EP-A1
**** 6 NYCRR Part 375 Unrestricted Use Soil Cleanup Objectives.***

TABLE 3

Analytical Results for Pesticides in Soil Samples
260 West 26th Street, New York, NY

Sample ID	EP-A1	EP-A3	EP-B2	EP-X	GP-A1	*Part 375 SCOs Unrestricted Use
Sample Depth	14'	14'	14'	14'	16'	
Matrix	Soil	Soil	Soil	Soil	Soil	
Date Sampled	1/13/2012	1/13/2012	1/13/2012	1/13/2012	1/23/2012	
Units	ug/Kg	ug/Kg	ug/Kg	ug/Kg	ug/Kg	ug/Kg
Pesticides						
Aldrin	ND	ND	ND	ND	ND	5
alpha-BHC	ND	ND	ND	ND	ND	20
beta-BHC	ND	ND	ND	ND	ND	36
delta-BHC	ND	ND	ND	ND	ND	40
gamma-BHC (Lindane)	ND	ND	ND	ND	ND	100
alpha-Chlordane	2.6	ND	2.4	3.3	2.8	94
gamma-Chlordane	2.6	ND	3.0	3.9	2.6	NVG
Dieldrin	ND	ND	ND	ND	ND	5
4,4'-DDD	**6.3**	3.1	**3.4**	1.6	2.2	3.3
4,4'-DDE	**10.6**	**4.5**	**7.3**	**3.8**	**5.6**	3.3
4,4'-DDT	**82.7 c**	**16.8**	**29.1**	**18.2**	**57.4 b**	3.3
Endrin	ND	ND	ND	ND	ND	14
Endosulfan sulfate	ND	ND	ND	ND	ND	2400
Endrin aldehyde	ND	ND	ND	ND	ND	NVG
Endosulfan-I	ND	ND	ND	ND	ND	2400
Endosulfan-II	ND	ND	ND	ND	ND	2400
Heptachlor	ND	ND	ND	ND	ND	42
Heptachlor epoxide	ND	ND	ND	ND	ND	NVG
Methoxychlor	ND	ND	ND	ND	ND	NVG
Endrin ketone	ND	ND	ND	ND	ND	NVG
Toxaphene	ND	ND	ND	ND	ND	NVG

Notes:

All concentrations are reported in micrograms per kilogram (μg/kg) or parts per billion.

b - result is from run#2

c - calibration %RSD/%D exceeded for non-CCC analytes

EP-X is a field duplicate of sample EP-A1

E - compound was reported above the instruments calibration range

NVG - No Given Value

Bold and boxed indicates that value is above 6 NYCRR Part 375 Unrestricted Use Soil Cleanup Objectives.

TABLE 4
Analytical Results for Metals in Soil Samples
260 West 26th Street, New York, NY

Sample ID	EP-A1	EP-A3	EP-B2	EP-X	*Part 375
Sample Depth	14'	14'	14'	14'	SCOs
Matrix	Soil	Soil	Soil	Soil	Unrestricted
Date Sampled	1/13/2012	1/13/2012	1/13/2012	1/13/2012	Use
Units	mg/Kg	mg/Kg	mg/Kg	mg/Kg	mg/Kg
Metals					
Aluminum	6,770	11,300	7,510	6,180	NVG
Antimony	ND	ND	ND	ND	NVG
Arsenic	ND	2.4	ND	ND	13
Barium	96.1	211	136	81.8	350
Beryllium	0.35	0.41	0.39	0.32	7.2
Cadmium	ND	ND	ND	ND	2.5
Calcium	7,290	9,900	6,730	6,020	NVG
Chromium	17.6	22.4	18.6	17.7	NVG
Cobalt	5.7	9.3	6.6	ND	NVG
Copper	14.1	35	17.4	10	50
Iron	11,500	20,600	13,700	10,900	NVG
Lead	40.4	**104**	55.4	21.4	63
Magnesium	4,110	6,490	4,170	3,630	NVG
Manganese	269	321	322	299	1,600
Mercury	0.14	0.17	**0.2**	0.048	0.18
Nickel	24.4	22.4	21.7	23.4	30
Potassium	2,750	6,440	3,610	2,890	NVG
Selenium	ND	ND	ND	ND	3.9
Silver	ND	ND	ND	ND	2
Sodium	ND	ND	ND	ND	NVG
Thallium	ND	ND	ND	ND	NVG
Vanadium	21.2	42.7	26.7	20.6	NVG
Zinc	42.2	**127**	58.2	36.1	109

Notes:

All concentrations are reported in milligrams per kilogram (mg/kg) or parts per million.

ND=Indicates the compound was analyzed for but not detected.

NVG - No Given Value

EP-X is a field duplicate of sample EP-A1

Bold and boxed indicates that value is above 6 NYCRR Part 375 Unrestricted Use Soil Cleanup Objectives.

Table 5

Summary of Hazardous Waste Disposal Activities

260 West 26th Street, New York, NY
BCP Project #11CBCP011M

Truck #	Date	Manifest #	Classification	Facility Destination	Weight In Tons	Cumm Qty Tons
1	10/05/11	008930754	Haz-Solid (Lead)	Clean Earth of North Jersey	28.98	28.98
2	10/05/11	008930754	Haz-Solid (Lead)	Clean Earth of North Jersey	30.53	59.51
3	10/05/11	008930754	Haz-Solid (Lead)	Clean Earth of North Jersey	31.93	91.44
4	10/07/11	008930770	Haz-Solid (Lead)	Clean Earth of North Jersey	29.84	121.28
5	10/07/11	008930771	Haz-Solid (Lead)	Clean Earth of North Jersey	26.92	148.20
				Total Tons	**148.20**	

Table 6

Summary of Non-Hazardous Waste Disposal Activities

260 West 26th Street, New York, NY
BCP Project #11CBCP011M

Truck #	Date	Manifest #	Classification	Facility Destination	Weight In Tons	Cumm Qty Tons
1	10/07/11	001	Non-Haz Soil	Soil Safe, Inc.	29.57	29.57
2	10/07/11	002	Non-Haz Soil	Soil Safe, Inc.	29.34	58.91
3	10/07/11	003	Non-Haz Soil	Soil Safe, Inc.	33.89	92.80
4	10/07/11	004	Non-Haz Soil	Soil Safe, Inc.	24.73	117.53
5	10/07/11	005	Non-Haz Soil	Soil Safe, Inc.	33.59	151.12
6	10/07/11	006	Non-Haz Soil	Soil Safe, Inc.	36.75	187.87
7	10/07/11	007	Non-Haz Soil	Soil Safe, Inc.	36.59	224.46
8	10/10/11	001	Non-Haz Soil	Soil Safe, Inc.	33.75	258.21
9	10/10/11	002	Non-Haz Soil	Soil Safe, Inc.	33.88	292.09
10	10/10/11	003	Non-Haz Soil	Soil Safe, Inc.	36.37	328.46
11	10/10/11	004	Non-Haz Soil	Soil Safe, Inc.	34.33	362.79
12	10/10/11	005	Non-Haz Soil	Soil Safe, Inc.	31.79	394.58
13	10/10/11	006	Non-Haz Soil	Soil Safe, Inc.	33.35	427.93
14	10/10/11	007	Non-Haz Soil	Soil Safe, Inc.	37.10	465.03
15	10/10/11	008	Non-Haz Soil	Soil Safe, Inc.	40.74	505.77
16	10/10/11	009	Non-Haz Soil	Soil Safe, Inc.	35.93	541.70
17	10/10/11	010	Non-Haz Soil	Soil Safe, Inc.	36.11	577.81
18	10/10/11	011	Non-Haz Soil	Soil Safe, Inc.	38.86	616.67
19	10/10/11	012	Non-Haz Soil	Soil Safe, Inc.	38.52	655.19
20	10/10/11	013	Non-Haz Soil	Soil Safe, Inc.	42.93	698.12
21	10/10/11	014	Non-Haz Soil	Soil Safe, Inc.	31.78	729.90
22	10/10/11	015	Non-Haz Soil	Soil Safe, Inc.	33.99	763.89
23	10/10/11	547897	Non-Haz Soil	Soil Safe, Inc.	39.99	803.88
24	10/10/11	547900	Non-Haz Soil	Soil Safe, Inc.	36.26	840.14
25	10/19/11	001	Non-Haz Soil	Bellmawr Waterfront Redev. Site	28.18	868.32
26	10/19/11	002	Non-Haz Soil	Bellmawr Waterfront Redev. Site	30.61	898.93
27	10/19/11	003	Non-Haz Soil	Bellmawr Waterfront Redev. Site	29.93	928.86
28	10/19/11	004	Non-Haz Soil	Bellmawr Waterfront Redev. Site	30.36	959.22
29	10/19/11	005	Non-Haz Soil	Bellmawr Waterfront Redev. Site	32.70	991.92
30	10/19/11	006	Non-Haz Soil	Bellmawr Waterfront Redev. Site	36.94	1,028.86
31	10/19/11	007	Non-Haz Soil	Bellmawr Waterfront Redev. Site	28.92	1,057.78
32	10/19/11	008	Non-Haz Soil	Bellmawr Waterfront Redev. Site	32.99	1,090.77
33	10/19/11	009	Non-Haz Soil	Bellmawr Waterfront Redev. Site	33.13	1,123.90
34	10/19/11	010	Non-Haz Soil	Bellmawr Waterfront Redev. Site	29.15	1,153.05
35	10/20/11	001	Non-Haz Soil	Soil Safe, Inc.	35.36	1,188.41
36	10/20/11	002	Non-Haz Soil	Soil Safe, Inc.	29.24	1,217.65
37	10/20/11	003	Non-Haz Soil	Soil Safe, Inc.	24.08	1,241.73
38	10/20/11	004	Non-Haz Soil	Soil Safe, Inc.	28.95	1,270.68
39	10/20/11	005	Non-Haz Soil	Soil Safe, Inc.	31.78	1,302.46

Table 6

Summary of Non-Hazardous Waste Disposal Activities

260 West 26th Street, New York, NY
BCP Project #11CBCP011M

Truck #	Date	Manifest #	Classification	Facility Destination	Weight In Tons	Cumm Qty Tons
40	10/20/11	006	Non-Haz Soil	Soil Safe, Inc.	31.68	1,334.14
41	10/20/11	007	Non-Haz Soil	Soil Safe, Inc.	28.16	1,362.30
42	10/20/11	008	Non-Haz Soil	Soil Safe, Inc.	31.46	1,393.76
43	10/20/11	009	Non-Haz Soil	Soil Safe, Inc.	28.81	1,422.57
44	10/20/11	010	Non-Haz Soil	Soil Safe, Inc.	25.57	1,448.14
45	10/20/11	011	Non-Haz Soil	Soil Safe, Inc.	34.51	1,482.65
46	10/20/11	012	Non-Haz Soil	Soil Safe, Inc.	36.11	1,518.76
47	10/20/11	013	Non-Haz Soil	Soil Safe, Inc.	34.24	1,553.00
48	10/20/11	014	Non-Haz Soil	Soil Safe, Inc.	35.17	1,588.17
49	10/20/11	015	Non-Haz Soil	Soil Safe, Inc.	34.23	1,622.40
50	10/20/11	016	Non-Haz Soil	Soil Safe, Inc.	34.79	1,657.19
51	10/20/11	017	Non-Haz Soil	Soil Safe, Inc.	34.50	1,691.69
52	10/20/11	018	Non-Haz Soil	Soil Safe, Inc.	29.45	1,721.14
53	10/20/11	019	Non-Haz Soil	Soil Safe, Inc.	36.66	1,757.80
54	10/20/11	020	Non-Haz Soil	Soil Safe, Inc.	34.99	1,792.79
55	10/20/11	021	Non-Haz Soil	Soil Safe, Inc.	33.19	1,825.98
56	10/20/11	022	Non-Haz Soil	Soil Safe, Inc.	36.59	1,862.57
57	10/20/11	023	Non-Haz Soil	Soil Safe, Inc.	36.28	1,898.85
58	10/21/11	001	Non-Haz Soil	Soil Safe, Inc.	32.09	1,930.94
59	10/21/11	002	Non-Haz Soil	Soil Safe, Inc.	26.73	1,957.67
60	10/21/11	003	Non-Haz Soil	Soil Safe, Inc.	34.60	1,992.27
61	10/21/11	004	Non-Haz Soil	Soil Safe, Inc.	32.32	2,024.59
62	10/21/11	005	Non-Haz Soil	Soil Safe, Inc.	36.90	2,061.49
63	10/21/11	006	Non-Haz Soil	Soil Safe, Inc.	40.13	2,101.62
64	10/21/11	007	Non-Haz Soil	Soil Safe, Inc.	34.84	2,136.46
65	10/21/11	008	Non-Haz Soil	Soil Safe, Inc.	28.18	2,164.64
66	10/21/11	009	Non-Haz Soil	Soil Safe, Inc.	26.90	2,191.54
67	10/21/11	010	Non-Haz Soil	Soil Safe, Inc.	33.05	2,224.59
68	10/21/11	011	Non-Haz Soil	Soil Safe, Inc.	29.64	2,254.23
69	10/21/11	012	Non-Haz Soil	Soil Safe, Inc.	34.05	2,288.28
70	10/21/11	013	Non-Haz Soil	Soil Safe, Inc.	39.26	2,327.54
71	10/21/11	014	Non-Haz Soil	Soil Safe, Inc.	33.62	2,361.16
72	10/21/11	015	Non-Haz Soil	Soil Safe, Inc.	40.05	2,401.21
73	10/21/11	016	Non-Haz Soil	Soil Safe, Inc.	33.51	2,434.72
74	10/21/11	017	Non-Haz Soil	Soil Safe, Inc.	32.07	2,466.79
75	10/21/11	018	Non-Haz Soil	Soil Safe, Inc.	36.28	2,503.07
76	10/21/11	019	Non-Haz Soil	Soil Safe, Inc.	35.92	2,538.99
77	10/21/11	020	Non-Haz Soil	Soil Safe, Inc.	38.21	2,577.20

Table 6

Summary of Non-Hazardous Waste Disposal Activities

260 West 26th Street, New York, NY
BCP Project #11CBCP011M

Truck #	Date	Manifest #	Classification	Facility Destination	Weight In Tons	Cumm Qty Tons
78	10/21/11	021	Non-Haz Soil	Soil Safe, Inc.	37.66	2,614.86
79	10/21/11	022	Non-Haz Soil	Soil Safe, Inc.	35.80	2,650.66
80	10/21/11	023	Non-Haz Soil	Soil Safe, Inc.	37.67	2,688.33
81	10/21/11	024	Non-Haz Soil	Soil Safe, Inc.	37.16	2,725.49
82	10/21/11	025	Non-Haz Soil	Soil Safe, Inc.	38.14	2,763.63
83	10/21/11	026	Non-Haz Soil	Soil Safe, Inc.	37.20	2,800.83
84	10/21/11	027	Non-Haz Soil	Soil Safe, Inc.	41.31	2,842.14
85	10/21/11	028	Non-Haz Soil	Soil Safe, Inc.	36.71	2,878.85
86	10/21/11	029	Non-Haz Soil	Soil Safe, Inc.	35.08	2,913.93
87	10/21/11	030	Non-Haz Soil	Soil Safe, Inc.	37.89	2,951.82
88	10/21/11	031	Non-Haz Soil	Soil Safe, Inc.	37.22	2,989.04
89	10/21/11	032	Non-Haz Soil	Soil Safe, Inc.	35.08	3,024.12
90	10/21/11	033	Non-Haz Soil	Soil Safe, Inc.	33.40	3,057.52
91	10/24/11	07506	Non-Haz Soil	Bellmawr Waterfront Redev. Site	32.48	3,090.00
92	10/24/11	07507	Non-Haz Soil	Bellmawr Waterfront Redev. Site	33.13	3,123.13
93	10/24/11	07510	Non-Haz Soil	Bellmawr Waterfront Redev. Site	30.92	3,154.05
94	10/24/11	07511	Non-Haz Soil	Bellmawr Waterfront Redev. Site	29.10	3,183.15
95	10/24/11	07512	Non-Haz Soil	Bellmawr Waterfront Redev. Site	35.04	3,218.19
96	10/24/11	07513	Non-Haz Soil	Bellmawr Waterfront Redev. Site	31.85	3,250.04
97	10/24/11	07514	Non-Haz Soil	Bellmawr Waterfront Redev. Site	35.56	3,285.60
98	10/24/11	07507	Non-Haz Soil	Bellmawr Waterfront Redev. Site	31.85	3,317.45
99	10/24/11	001	Non-Haz Soil	Soil Safe, Inc.	27.24	3,344.69
100	10/24/11	002	Non-Haz Soil	Soil Safe, Inc.	28.25	3,372.94
101	10/24/11	003	Non-Haz Soil	Soil Safe, Inc.	31.24	3,404.18
102	10/24/11	004	Non-Haz Soil	Soil Safe, Inc.	31.05	3,435.23
103	10/24/11	005	Non-Haz Soil	Soil Safe, Inc.	30.67	3,465.90
104	10/24/11	006	Non-Haz Soil	Soil Safe, Inc.	31.65	3,497.55
105	10/24/11	007	Non-Haz Soil	Soil Safe, Inc.	34.85	3,532.40
106	10/24/11	008	Non-Haz Soil	Soil Safe, Inc.	31.56	3,563.96
107	10/24/11	009	Non-Haz Soil	Soil Safe, Inc.	31.10	3,595.06
108	10/24/11	010	Non-Haz Soil	Soil Safe, Inc.	33.19	3,628.25
109	10/24/11	011	Non-Haz Soil	Soil Safe, Inc.	32.72	3,660.97
110	10/24/11	012	Non-Haz Soil	Soil Safe, Inc.	35.21	3,696.18
111	10/24/11	013	Non-Haz Soil	Soil Safe, Inc.	31.36	3,727.54
112	10/24/11	014	Non-Haz Soil	Soil Safe, Inc.	34.47	3,762.01
113	10/24/11	015	Non-Haz Soil	Soil Safe, Inc.	28.17	3,790.18
114	10/24/11	016	Non-Haz Soil	Soil Safe, Inc.	30.15	3,820.33
115	10/24/11	017	Non-Haz Soil	Soil Safe, Inc.	35.46	3,855.79

Table 6

Summary of Non-Hazardous Waste Disposal Activities

260 West 26th Street, New York, NY
BCP Project #11CBCP011M

Truck #	Date	Manifest #	Classification	Facility Destination	Weight In Tons	Cumm Qty Tons
116	10/24/11	018	Non-Haz Soil	Soil Safe, Inc.	39.72	3,895.51
117	10/24/11	019	Non-Haz Soil	Soil Safe, Inc.	34.94	3,930.45
118	10/24/11	020	Non-Haz Soil	Soil Safe, Inc.	33.51	3,963.96
119	10/24/11	021	Non-Haz Soil	Soil Safe, Inc.	31.99	3,995.95
120	10/24/11	022	Non-Haz Soil	Soil Safe, Inc.	31.00	4,026.95
121	10/24/11	023	Non-Haz Soil	Soil Safe, Inc.	29.10	4,056.05
122	10/24/11	024	Non-Haz Soil	Soil Safe, Inc.	30.73	4,086.78
123	10/24/11	025	Non-Haz Soil	Soil Safe, Inc.	31.37	4,118.15
124	10/24/11	026	Non-Haz Soil	Soil Safe, Inc.	29.91	4,148.06
125	10/24/11	027	Non-Haz Soil	Soil Safe, Inc.	33.58	4,181.64
126	10/24/11	028	Non-Haz Soil	Soil Safe, Inc.	33.50	4,215.14
127	10/24/11	029	Non-Haz Soil	Soil Safe, Inc.	32.52	4,247.66
128	10/24/11	030	Non-Haz Soil	Soil Safe, Inc.	28.10	4,275.76
129	10/24/11	031	Non-Haz Soil	Soil Safe, Inc.	35.74	4,311.50
130	10/24/11	032	Non-Haz Soil	Soil Safe, Inc.	29.58	4,341.08
131	10/25/11	001	Non-Haz Soil	Soil Safe, Inc.	31.47	4,372.55
132	10/25/11	002	Non-Haz Soil	Soil Safe, Inc.	34.27	4,406.82
133	10/25/11	003	Non-Haz Soil	Soil Safe, Inc.	33.29	4,440.11
134	10/25/11	004	Non-Haz Soil	Soil Safe, Inc.	30.28	4,470.39
135	10/25/11	005	Non-Haz Soil	Soil Safe, Inc.	30.63	4,501.02
136	10/25/11	006	Non-Haz Soil	Soil Safe, Inc.	30.07	4,531.09
137	10/25/11	007	Non-Haz Soil	Soil Safe, Inc.	33.37	4,564.46
138	10/25/11	008	Non-Haz Soil	Soil Safe, Inc.	33.74	4,598.20
139	10/25/11	009	Non-Haz Soil	Soil Safe, Inc.	36.59	4,634.79
140	10/25/11	010	Non-Haz Soil	Soil Safe, Inc.	29.53	4,664.32
141	10/25/11	011	Non-Haz Soil	Soil Safe, Inc.	37.25	4,701.57
142	10/25/11	012	Non-Haz Soil	Soil Safe, Inc.	29.62	4,731.19
143	10/25/11	013	Non-Haz Soil	Soil Safe, Inc.	35.54	4,766.73
144	10/25/11	014	Non-Haz Soil	Soil Safe, Inc.	29.15	4,795.88
145	10/25/11	015	Non-Haz Soil	Soil Safe, Inc.	37.87	4,833.75
146	10/25/11	016	Non-Haz Soil	Soil Safe, Inc.	33.33	4,867.08
147	10/25/11	017	Non-Haz Soil	Soil Safe, Inc.	33.93	4,901.01
148	10/25/11	018	Non-Haz Soil	Soil Safe, Inc.	32.84	4,933.85
149	10/25/11	019	Non-Haz Soil	Soil Safe, Inc.	29.80	4,963.65
150	10/25/11	020	Non-Haz Soil	Soil Safe, Inc.	34.75	4,998.40
151	10/25/11	021	Non-Haz Soil	Soil Safe, Inc.	29.49	5,027.89
152	10/25/11	022	Non-Haz Soil	Soil Safe, Inc.	29.49	5,057.38
153	10/25/11	023	Non-Haz Soil	Soil Safe, Inc.	38.35	5,095.73

Table 6

Summary of Non-Hazardous Waste Disposal Activities

260 West 26th Street, New York, NY
BCP Project #11CBCP011M

Truck #	Date	Manifest #	Classification	Facility Destination	Weight In Tons	Cumm Qty Tons
154	10/25/11	024	Non-Haz Soil	Soil Safe, Inc.	31.86	5,127.59
155	10/25/11	025	Non-Haz Soil	Soil Safe, Inc.	30.04	5,157.63
156	10/25/11	026	Non-Haz Soil	Soil Safe, Inc.	31.61	5,189.24
157	10/25/11	027	Non-Haz Soil	Soil Safe, Inc.	36.52	5,225.76
158	10/25/11	028	Non-Haz Soil	Soil Safe, Inc.	33.48	5,259.24
159	10/25/11	029	Non-Haz Soil	Soil Safe, Inc.	34.66	5,293.90
160	10/25/11	030	Non-Haz Soil	Soil Safe, Inc.	32.75	5,326.65
161	10/25/11	031	Non-Haz Soil	Soil Safe, Inc.	32.85	5,359.50
162	10/25/11	032	Non-Haz Soil	Soil Safe, Inc.	32.67	5,392.17
163	10/25/11	033	Non-Haz Soil	Soil Safe, Inc.	33.61	5,425.78
164	10/25/11	034	Non-Haz Soil	Soil Safe, Inc.	35.04	5,460.82
165	10/25/11	035	Non-Haz Soil	Soil Safe, Inc.	32.98	5,493.80
166	10/26/11	001	Non-Haz Soil	Soil Safe, Inc.	30.16	5,523.96
167	10/26/11	002	Non-Haz Soil	Soil Safe, Inc.	30.77	5,554.73
168	10/26/11	003	Non-Haz Soil	Soil Safe, Inc.	29.57	5,584.30
169	10/26/11	004	Non-Haz Soil	Soil Safe, Inc.	34.68	5,618.98
170	10/26/11	005	Non-Haz Soil	Soil Safe, Inc.	33.07	5,652.05
171	10/26/11	006	Non-Haz Soil	Soil Safe, Inc.	32.21	5,684.26
172	10/26/11	007	Non-Haz Soil	Soil Safe, Inc.	31.39	5,715.65
173	10/26/11	008	Non-Haz Soil	Soil Safe, Inc.	31.56	5,747.21
174	10/26/11	009	Non-Haz Soil	Soil Safe, Inc.	33.60	5,780.81
175	10/26/11	010	Non-Haz Soil	Soil Safe, Inc.	33.62	5,814.43
176	10/26/11	011	Non-Haz Soil	Soil Safe, Inc.	37.65	5,852.08
177	10/26/11	012	Non-Haz Soil	Soil Safe, Inc.	32.62	5,884.70
178	10/26/11	013	Non-Haz Soil	Soil Safe, Inc.	29.62	5,914.32
179	10/26/11	014	Non-Haz Soil	Soil Safe, Inc.	30.96	5,945.28
180	11/01/11	001	Non-Haz Soil	Soil Safe, Inc.	42.71	5,987.99
181	11/01/11	002	Non-Haz Soil	Soil Safe, Inc.	34.69	6,022.68
182	11/01/11	003	Non-Haz Soil	Soil Safe, Inc.	35.95	6,058.63
183	11/01/11	004	Non-Haz Soil	Soil Safe, Inc.	34.12	6,092.75
184	11/01/11	005	Non-Haz Soil	Soil Safe, Inc.	35.14	6,127.89
185	11/01/11	006	Non-Haz Soil	Soil Safe, Inc.	37.20	6,165.09
186	11/02/11	001	Non-Haz Soil	Soil Safe, Inc.	36.59	6,201.68
187	11/02/11	002	Non-Haz Soil	Soil Safe, Inc.	38.61	6,240.29
188	11/02/11	003	Non-Haz Soil	Soil Safe, Inc.	40.14	6,280.43
189	11/02/11	004	Non-Haz Soil	Soil Safe, Inc.	38.24	6,318.67
190	11/02/11	005	Non-Haz Soil	Soil Safe, Inc.	37.31	6,355.98
191	11/02/11	006	Non-Haz Soil	Soil Safe, Inc.	41.61	6,397.59

Table 6

Summary of Non-Hazardous Waste Disposal Activities

260 West 26th Street, New York, NY
BCP Project #11CBCP011M

Truck #	Date	Manifest #	Classification	Facility Destination	Weight In Tons	Cumm Qty Tons
192	11/02/11	007	Non-Haz Soil	Soil Safe, Inc.	41.52	6,439.11
193	11/02/11	008	Non-Haz Soil	Soil Safe, Inc.	36.92	6,476.03
194	11/02/11	009	Non-Haz Soil	Soil Safe, Inc.	36.89	6,512.92
195	11/02/11	010	Non-Haz Soil	Soil Safe, Inc.	33.62	6,546.54
196	11/02/11	011	Non-Haz Soil	Soil Safe, Inc.	37.79	6,584.33
197	11/02/11	012	Non-Haz Soil	Soil Safe, Inc.	41.81	6,626.14
198	11/03/11	001	Non-Haz Soil	Soil Safe, Inc.	39.13	6,665.27
199	11/03/11	002	Non-Haz Soil	Soil Safe, Inc.	38.67	6,703.94
200	11/03/11	003	Non-Haz Soil	Soil Safe, Inc.	41.61	6,745.55
201	11/03/11	004	Non-Haz Soil	Soil Safe, Inc.	36.00	6,781.55
202	11/03/11	005	Non-Haz Soil	Soil Safe, Inc.	37.54	6,819.09
203	11/03/11	006	Non-Haz Soil	Soil Safe, Inc.	36.64	6,855.73
204	11/03/11	007	Non-Haz Soil	Soil Safe, Inc.	36.38	6,892.11
205	11/03/11	008	Non-Haz Soil	Soil Safe, Inc.	36.37	6,928.48
206	11/03/11	009	Non-Haz Soil	Soil Safe, Inc.	35.45	6,963.93
207	11/03/11	010	Non-Haz Soil	Soil Safe, Inc.	35.02	6,998.95
208	11/03/11	011	Non-Haz Soil	Soil Safe, Inc.	35.47	7,034.42
209	11/04/11	001	Non-Haz Soil	Soil Safe, Inc.	30.58	7,065.00
210	11/04/11	002	Non-Haz Soil	Soil Safe, Inc.	36.08	7,101.08
211	11/04/11	003	Non-Haz Soil	Soil Safe, Inc.	34.62	7,135.70
212	11/07/11	001	Non-Haz Soil	Soil Safe, Inc.	27.00	7,162.70
213	11/07/11	002	Non-Haz Soil	Soil Safe, Inc.	31.95	7,194.65
214	11/15/11	001	Non-Haz Soil	Soil Safe, Inc.	33.89	7,228.54
215	11/15/11	002	Non-Haz Soil	Soil Safe, Inc.	30.20	7,258.74
216	11/15/11	003	Non-Haz Soil	Soil Safe, Inc.	34.94	7,293.68
217	11/15/11	004	Non-Haz Soil	Soil Safe, Inc.	30.22	7,323.90
218	11/15/11	005	Non-Haz Soil	Soil Safe, Inc.	27.45	7,351.35
219	11/15/11	006	Non-Haz Soil	Soil Safe, Inc.	36.22	7,387.57
220	11/15/11	007	Non-Haz Soil	Soil Safe, Inc.	37.55	7,425.12
221	11/17/11	001	Non-Haz Soil	Soil Safe, Inc.	36.70	7,461.82
222	11/17/11	002	Non-Haz Soil	Soil Safe, Inc.	28.47	7,490.29
223	11/17/11	003	Non-Haz Soil	Soil Safe, Inc.	41.37	7,531.66
224	11/17/11	004	Non-Haz Soil	Soil Safe, Inc.	34.23	7,565.89
225	11/17/11	005	Non-Haz Soil	Soil Safe, Inc.	40.80	7,606.69
226	11/17/11	006	Non-Haz Soil	Soil Safe, Inc.	31.84	7,638.53
227	11/18/11	001	Non-Haz Soil	Soil Safe, Inc.	27.50	7,666.03
228	11/18/11	002	Non-Haz Soil	Soil Safe, Inc.	28.86	7,694.89
229	11/18/11	003	Non-Haz Soil	Soil Safe, Inc.	33.63	7,728.52

Table 6

Summary of Non-Hazardous Waste Disposal Activities

260 West 26th Street, New York, NY
BCP Project #11CBCP011M

Truck #	Date	Manifest #	Classification	Facility Destination	Weight In Tons	Cumm Qty Tons
230	11/18/11	004	Non-Haz Soil	Soil Safe, Inc.	36.81	7,765.33
231	11/18/11	005	Non-Haz Soil	Soil Safe, Inc.	28.88	7,794.21
232	11/18/11	006	Non-Haz Soil	Soil Safe, Inc.	34.03	7,828.24
233	11/21/11	001	Non-Haz Soil	Soil Safe, Inc.	31.35	7,859.59
234	11/21/11	002	Non-Haz Soil	Soil Safe, Inc.	32.45	7,892.04
235	11/21/11	003	Non-Haz Soil	Soil Safe, Inc.	35.77	7,927.81
236	11/21/11	004	Non-Haz Soil	Soil Safe, Inc.	33.47	7,961.28
237	11/21/11	005	Non-Haz Soil	Soil Safe, Inc.	35.85	7,997.13
238	11/21/11	006	Non-Haz Soil	Soil Safe, Inc.	29.85	8,026.98
239	12/06/11	120601	Non-Haz Soil	Soil Safe, Inc.	27.13	9,297.48
240	12/06/11	120602	Non-Haz Soil	Soil Safe, Inc.	31.68	9,329.16
241	12/06/11	120603	Non-Haz Soil	Soil Safe, Inc.	33.76	9,362.92
242	12/06/11	120604	Non-Haz Soil	Soil Safe, Inc.	33.03	9,395.95
243	12/06/11	120605	Non-Haz Soil	Soil Safe, Inc.	35.19	9,431.14
244	12/06/11	120606	Non-Haz Soil	Soil Safe, Inc.	35.28	9,466.42
245	12/06/11	120607	Non-Haz Soil	Soil Safe, Inc.	36.77	9,503.19
246	12/06/11	120608	Non-Haz Soil	Soil Safe, Inc.	35.92	9,539.11
247	12/06/11	120609	Non-Haz Soil	Soil Safe, Inc.	38.50	9,577.61
248	12/06/11	120610	Non-Haz Soil	Soil Safe, Inc.	36.64	9,614.25
249	12/06/11	120611	Non-Haz Soil	Soil Safe, Inc.	32.80	9,647.05
250	12/06/11	120612	Non-Haz Soil	Soil Safe, Inc.	36.96	9,684.01
251	12/06/11	120613	Non-Haz Soil	Soil Safe, Inc.	37.40	9,721.41
252	12/13/11	001	Non-Haz Soil	Soil Safe, Inc.	32.22	8,059.20
253	12/13/11	002	Non-Haz Soil	Soil Safe, Inc.	35.49	8,094.69
254	12/13/11	003	Non-Haz Soil	Soil Safe, Inc.	36.26	8,130.95
255	12/13/11	004	Non-Haz Soil	Soil Safe, Inc.	35.16	8,166.11
256	12/13/11	005	Non-Haz Soil	Soil Safe, Inc.	37.59	8,203.70
257	12/13/11	006	Non-Haz Soil	Soil Safe, Inc.	36.54	8,240.24
258	12/13/11	007	Non-Haz Soil	Soil Safe, Inc.	33.65	8,273.89
259	12/13/11	008	Non-Haz Soil	Soil Safe, Inc.	34.34	8,308.23
260	12/13/11	009	Non-Haz Soil	Soil Safe, Inc.	36.56	8,344.79
261	12/13/11	010	Non-Haz Soil	Soil Safe, Inc.	44.70	8,389.49
262	12/13/11	011	Non-Haz Soil	Soil Safe, Inc.	35.56	8,425.05
263	12/13/11	012	Non-Haz Soil	Soil Safe, Inc.	31.65	8,456.70
264	12/14/11	001	Non-Haz Soil	Soil Safe, Inc.	24.99	8,481.69
265	12/14/11	002	Non-Haz Soil	Soil Safe, Inc.	31.56	8,513.25
266	12/14/11	003	Non-Haz Soil	Soil Safe, Inc.	31.66	8,544.91
267	12/14/11	004	Non-Haz Soil	Soil Safe, Inc.	35.57	8,580.48

Table 6

Summary of Non-Hazardous Waste Disposal Activities

260 West 26th Street, New York, NY
BCP Project #11CBCP011M

Truck #	Date	Manifest #	Classification	Facility Destination	Weight In Tons	Cumm Qty Tons
268	12/14/11	005	Non-Haz Soil	Soil Safe, Inc.	36.96	8,617.44
269	12/14/11	006	Non-Haz Soil	Soil Safe, Inc.	32.17	8,649.61
270	12/14/11	007	Non-Haz Soil	Soil Safe, Inc.	31.11	8,680.72
271	12/14/11	008	Non-Haz Soil	Soil Safe, Inc.	36.55	8,717.27
272	12/15/11	001	Non-Haz Soil	Soil Safe, Inc.	35.13	8,752.40
273	12/15/11	002	Non-Haz Soil	Soil Safe, Inc.	33.78	8,786.18
274	12/15/11	003	Non-Haz Soil	Soil Safe, Inc.	37.67	8,823.85
275	12/15/11	004	Non-Haz Soil	Soil Safe, Inc.	30.80	8,854.65
276	12/15/11	005	Non-Haz Soil	Soil Safe, Inc.	30.76	8,885.41
277	12/15/11	006	Non-Haz Soil	Soil Safe, Inc.	32.27	8,917.68
278	12/15/11	007	Non-Haz Soil	Soil Safe, Inc.	26.75	8,944.43
279	12/15/11	008	Non-Haz Soil	Soil Safe, Inc.	37.36	8,981.79
280	12/15/11	009	Non-Haz Soil	Soil Safe, Inc.	30.16	9,011.95
281	12/15/11	010	Non-Haz Soil	Soil Safe, Inc.	29.76	9,041.71
282	12/15/11	011	Non-Haz Soil	Soil Safe, Inc.	29.58	9,071.29
283	12/15/11	012	Non-Haz Soil	Soil Safe, Inc.	31.57	9,102.86
284	12/15/11	013	Non-Haz Soil	Soil Safe, Inc.	34.56	9,137.42
285	12/15/11	014	Non-Haz Soil	Soil Safe, Inc.	36.58	9,174.00
286	12/15/11	015	Non-Haz Soil	Soil Safe, Inc.	29.60	9,203.60
287	12/15/11	016	Non-Haz Soil	Soil Safe, Inc.	34.28	9,237.88
288	12/15/11	017	Non-Haz Soil	Soil Safe, Inc.	32.47	9,270.35
289	12/27/11	001	Non-Haz Soil	Soil Safe, Inc.	33.76	9,755.17
290	12/27/11	002	Non-Haz Soil	Soil Safe, Inc.	32.52	9,787.69
291	12/27/11	003	Non-Haz Soil	Soil Safe, Inc.	35.12	9,822.81
292	12/27/11	004	Non-Haz Soil	Soil Safe, Inc.	32.56	9,855.37
293	12/27/11	005	Non-Haz Soil	Soil Safe, Inc.	36.54	9,891.91
294	12/27/11	006	Non-Haz Soil	Soil Safe, Inc.	35.13	9,927.04
295	12/27/11	007	Non-Haz Soil	Soil Safe, Inc.	31.99	9,959.03
296	12/27/11	008	Non-Haz Soil	Soil Safe, Inc.	34.12	9,993.15
297	12/27/11	009	Non-Haz Soil	Soil Safe, Inc.	33.86	10,027.01
298	12/27/11	010	Non-Haz Soil	Soil Safe, Inc.	32.18	10,059.19
299	12/28/11	001	Non-Haz Soil	Soil Safe, Inc.	34.53	10,093.72
300	12/28/11	002	Non-Haz Soil	Soil Safe, Inc.	35.72	10,129.44
301	12/28/11	003	Non-Haz Soil	Soil Safe, Inc.	31.58	10,161.02
302	12/28/11	004	Non-Haz Soil	Soil Safe, Inc.	30.60	10,191.62
303	12/28/11	005	Non-Haz Soil	Soil Safe, Inc.	32.43	10,224.05
304	12/28/11	006	Non-Haz Soil	Soil Safe, Inc.	30.60	10,254.65
305	12/28/11	007	Non-Haz Soil	Soil Safe, Inc.	34.52	10,289.17

Table 6

Summary of Non-Hazardous Waste Disposal Activities

260 West 26th Street, New York, NY
BCP Project #11CBCP011M

Truck #	Date	Manifest #	Classification	Facility Destination	Weight In Tons	Cumm Qty Tons
306	12/28/11	008	Non-Haz Soil	Soil Safe, Inc.	31.55	10,320.72
307	12/28/11	009	Non-Haz Soil	Soil Safe, Inc.	32.73	10,353.45
308	12/28/11	010	Non-Haz Soil	Soil Safe, Inc.	32.99	10,386.44
309	12/28/11	011	Non-Haz Soil	Soil Safe, Inc.	32.12	10,418.56
310	12/28/11	012	Non-Haz Soil	Soil Safe, Inc.	32.53	10,451.09
311	12/28/11	013	Non-Haz Soil	Soil Safe, Inc.	31.18	10,482.27
312	12/29/11	014	Non-Haz Soil	Soil Safe, Inc.	32.29	10,514.56
313	12/29/11	001	Non-Haz Soil	Soil Safe, Inc.	32.40	10,546.96
314	12/29/11	002	Non-Haz Soil	Soil Safe, Inc.	36.66	10,583.62
315	12/29/11	003	Non-Haz Soil	Soil Safe, Inc.	33.11	10,616.73
316	12/29/11	004	Non-Haz Soil	Soil Safe, Inc.	34.62	10,651.35
317	12/29/11	005	Non-Haz Soil	Soil Safe, Inc.	36.48	10,687.83
318	12/29/11	006	Non-Haz Soil	Soil Safe, Inc.	33.70	10,721.53
319	12/29/11	007	Non-Haz Soil	Soil Safe, Inc.	37.80	10,759.33
320	12/29/11	008	Non-Haz Soil	Soil Safe, Inc.	32.21	10,791.54
321	01/09/12	001	Non-Haz Soil	Soil Safe, Inc.	34.77	10,826.31
322	01/09/12	002	Non-Haz Soil	Soil Safe, Inc.	27.09	10,853.40
323	01/09/12	003	Non-Haz Soil	Soil Safe, Inc.	27.60	10,881.00
324	01/09/12	004	Non-Haz Soil	Soil Safe, Inc.	30.19	10,911.19
325	01/09/12	005	Non-Haz Soil	Soil Safe, Inc.	34.79	10,945.98
326	01/09/12	006	Non-Haz Soil	Soil Safe, Inc.	35.24	10,981.22
327	01/09/12	007	Non-Haz Soil	Soil Safe, Inc.	35.52	11,016.74
328	01/09/12	008	Non-Haz Soil	Soil Safe, Inc.	36.15	11,052.89
329	01/09/12	009	Non-Haz Soil	Soil Safe, Inc.	32.67	11,085.56
330	01/10/12	001	Non-Haz Soil	Soil Safe, Inc.	33.50	11,119.06
331	01/10/12	002	Non-Haz Soil	Soil Safe, Inc.	30.02	11,149.08
332	01/10/12	003	Non-Haz Soil	Soil Safe, Inc.	37.93	11,187.01
333	01/10/12	004	Non-Haz Soil	Soil Safe, Inc.	32.04	11,219.05
334	01/10/12	005	Non-Haz Soil	Soil Safe, Inc.	29.91	11,248.96
335	01/10/12	006	Non-Haz Soil	Soil Safe, Inc.	33.90	11,282.86
336	01/10/12	007	Non-Haz Soil	Soil Safe, Inc.	35.79	11,318.65
337	01/10/12	008	Non-Haz Soil	Soil Safe, Inc.	33.84	11,352.49
338	01/10/12	009	Non-Haz Soil	Soil Safe, Inc.	35.04	11,387.53
339	01/10/12	010	Non-Haz Soil	Soil Safe, Inc.	32.96	11,420.49
340	01/10/12	011	Non-Haz Soil	Soil Safe, Inc.	30.32	11,450.81
341	01/10/12	012	Non-Haz Soil	Soil Safe, Inc.	32.73	11,483.54
342	01/11/12	001	Non-Haz Soil	Soil Safe, Inc.	40.58	11,524.12
343	01/11/12	002	Non-Haz Soil	Soil Safe, Inc.	31.06	11,555.18

Table 6

Summary of Non-Hazardous Waste Disposal Activities

260 West 26th Street, New York, NY
BCP Project #11CBCP011M

Truck #	Date	Manifest #	Classification	Facility Destination	Weight In Tons	Cumm Qty Tons
344	01/11/12	003	Non-Haz Soil	Soil Safe, Inc.	31.27	11,586.45
345	01/11/12	004	Non-Haz Soil	Soil Safe, Inc.	33.69	11,620.14
346	01/11/12	005	Non-Haz Soil	Soil Safe, Inc.	33.30	11,653.44
347	01/11/12	006	Non-Haz Soil	Soil Safe, Inc.	31.65	11,685.09
348	01/11/12	007	Non-Haz Soil	Soil Safe, Inc.	30.79	11,715.88
349	01/12/12	001	Non-Haz Soil	Soil Safe, Inc.	36.89	11,752.77
350	01/12/12	002	Non-Haz Soil	Soil Safe, Inc.	34.27	11,787.04
351	01/12/12	003	Non-Haz Soil	Soil Safe, Inc.	30.11	11,817.15
352	01/12/12	004	Non-Haz Soil	Soil Safe, Inc.	31.65	11,848.80
353	01/12/12	005	Non-Haz Soil	Soil Safe, Inc.	26.00	11,874.80
354	01/12/12	006	Non-Haz Soil	Soil Safe, Inc.	37.37	11,912.17
355	01/12/12	007	Non-Haz Soil	Soil Safe, Inc.	34.57	11,946.74
356	01/12/12	008	Non-Haz Soil	Soil Safe, Inc.	29.41	11,976.15
357	01/16/12	001	Non-Haz Soil	Soil Safe, Inc.	33.34	12,009.49
358	01/16/12	002	Non-Haz Soil	Soil Safe, Inc.	36.16	12,045.65
359	01/16/12	003	Non-Haz Soil	Soil Safe, Inc.	39.83	12,085.48
360	01/16/12	004	Non-Haz Soil	Soil Safe, Inc.	36.80	12,122.28
361	01/16/12	005	Non-Haz Soil	Soil Safe, Inc.	34.17	12,156.45
362	01/31/12	001	Non-Haz Soil	Pure Soil Technologies	32.10	12,188.55
363	01/31/12	002	Non-Haz Soil	Pure Soil Technologies	22.44	12,210.99
364	01/31/12	003	Non-Haz Soil	Pure Soil Technologies	35.43	12,246.42
365	01/31/12	004	Non-Haz Soil	Pure Soil Technologies	30.71	12,277.13
366	01/31/12	005	Non-Haz Soil	Pure Soil Technologies	31.53	12,308.66
367	01/31/12	006	Non-Haz Soil	Pure Soil Technologies	32.46	12,341.12
368	02/03/12	001	Non-Haz Soil	Pure Soil Technologies	32.61	12,373.73
369	02/03/12	002	Non-Haz Soil	Pure Soil Technologies	27.53	12,401.26
370	02/03/12	003	Non-Haz Soil	Pure Soil Technologies	37.17	12,438.43
371	02/03/12	004	Non-Haz Soil	Pure Soil Technologies	29.02	12,467.45
372	02/03/12	005	Non-Haz Soil	Pure Soil Technologies	34.09	12,501.54
373	02/03/12	006	Non-Haz Soil	Pure Soil Technologies	29.07	12,530.61
374	02/03/12	007	Non-Haz Soil	Pure Soil Technologies	33.59	12,564.20
375	02/03/12	008	Non-Haz Soil	Pure Soil Technologies	32.14	12,596.34
376	02/13/12	001	Non-Haz Soil	Pure Soil Technologies	36.18	12,632.52
377	02/13/12	002	Non-Haz Soil	Pure Soil Technologies	34.42	12,666.94
378	02/13/12	003	Non-Haz Soil	Pure Soil Technologies	33.52	12,700.46
379	02/13/12	004	Non-Haz Soil	Pure Soil Technologies	32.65	12,733.11
380	02/13/12	005	Non-Haz Soil	Pure Soil Technologies	32.16	12,765.27
381	02/13/12	006	Non-Haz Soil	Pure Soil Technologies	32.92	12,798.19

Table 6

Summary of Non-Hazardous Waste Disposal Activities

260 West 26th Street, New York, NY
BCP Project #11CBCP011M

Truck #	Date	Manifest #	Classification	Facility Destination	Weight In Tons	Cumm Qty Tons
382	02/13/12	007	Non-Haz Soil	Pure Soil Technologies	28.91	12,827.10
383	02/13/12	008	Non-Haz Soil	Pure Soil Technologies	31.65	12,858.75
384	02/13/12	009	Non-Haz Soil	Pure Soil Technologies	33.89	12,892.64
385	02/13/12	010	Non-Haz Soil	Pure Soil Technologies	35.40	12,928.04
386	02/13/12	011	Non-Haz Soil	Pure Soil Technologies	34.65	12,962.69
387	02/13/12	012	Non-Haz Soil	Pure Soil Technologies	32.60	12,995.29
388	02/13/12	013	Non-Haz Soil	Pure Soil Technologies	35.37	13,030.66
389	02/13/12	014	Non-Haz Soil	Pure Soil Technologies	30.93	13,061.59
390	02/13/12	015	Non-Haz Soil	Pure Soil Technologies	29.09	13,090.68
391	02/13/12	016	Non-Haz Soil	Pure Soil Technologies	32.55	13,123.23
392	02/14/12	03108	Non-Haz Soil	Pure Soil Technologies	33.70	13,156.93
393	02/14/12	03107	Non-Haz Soil	Pure Soil Technologies	34.83	13,191.76
394	02/14/12	03101	Non-Haz Soil	Pure Soil Technologies	34.30	13,226.06
395	02/14/12	03106	Non-Haz Soil	Pure Soil Technologies	33.69	13,259.75
396	02/14/12	03105	Non-Haz Soil	Pure Soil Technologies	33.49	13,293.24
397	02/14/12	03245	Non-Haz Soil	Pure Soil Technologies	33.94	13,327.18
398	02/14/12	03248	Non-Haz Soil	Pure Soil Technologies	29.42	13,356.60
399	02/14/12	03249	Non-Haz Soil	Pure Soil Technologies	33.65	13,390.25
400	02/14/12	03251	Non-Haz Soil	Pure Soil Technologies	26.32	13,416.57
401	02/14/12	03252	Non-Haz Soil	Pure Soil Technologies	33.89	13,450.46
402	02/14/12	03104	Non-Haz Soil	Pure Soil Technologies	28.26	13,478.72
403	02/14/12	03246	Non-Haz Soil	Pure Soil Technologies	27.64	13,506.36
404	02/14/12	03247	Non-Haz Soil	Pure Soil Technologies	28.55	13,534.91
405	02/14/12	03250	Non-Haz Soil	Pure Soil Technologies	30.69	13,565.60
406	02/14/12	03253	Non-Haz Soil	Pure Soil Technologies	27.33	13,592.93
407	02/22/12	03241	Non-Haz Soil	Pure Soil Technologies	32.66	13,625.59
408	02/22/12	03116	Non-Haz Soil	Pure Soil Technologies	36.37	13,661.96
409	02/22/12	03136	Non-Haz Soil	Pure Soil Technologies	34.88	13,696.84
410	02/22/12	13120	Non-Haz Soil	Pure Soil Technologies	32.84	13,729.68
411	02/22/12	03138	Non-Haz Soil	Pure Soil Technologies	37.00	13,766.68
412	02/22/12	03146	Non-Haz Soil	Pure Soil Technologies	33.54	13,800.22
413	02/22/12	03145	Non-Haz Soil	Pure Soil Technologies	32.58	13,832.80
414	02/22/12	03142	Non-Haz Soil	Pure Soil Technologies	32.24	13,865.04
415	02/22/12	03126	Non-Haz Soil	Pure Soil Technologies	32.81	13,897.85
416	02/22/12	03134	Non-Haz Soil	Pure Soil Technologies	30.31	13,928.16
417	02/22/12	03124	Non-Haz Soil	Pure Soil Technologies	29.24	13,957.40
418	02/22/12	03123	Non-Haz Soil	Pure Soil Technologies	31.65	13,989.05
419	02/22/12	03128	Non-Haz Soil	Pure Soil Technologies	32.25	14,021.30

Table 6

Summary of Non-Hazardous Waste Disposal Activities

260 West 26th Street, New York, NY
BCP Project #11CBCP011M

Truck #	Date	Manifest #	Classification	Facility Destination	Weight In Tons	Cumm Qty Tons
420	02/22/12	03130	Non-Haz Soil	Pure Soil Technologies	32.44	14,053.74
421	02/22/12	03141	Non-Haz Soil	Pure Soil Technologies	29.04	14,082.78
422	02/22/12	03243	Non-Haz Soil	Pure Soil Technologies	32.25	14,115.03
423	02/22/12	03242	Non-Haz Soil	Pure Soil Technologies	31.43	14,146.46
424	02/22/12	03117	Non-Haz Soil	Pure Soil Technologies	33.26	14,179.72
425	02/22/12	03119	Non-Haz Soil	Pure Soil Technologies	32.21	14,211.93
426	02/22/12	03137	Non-Haz Soil	Pure Soil Technologies	35.10	14,247.03
427	02/22/12	03118	Non-Haz Soil	Pure Soil Technologies	33.62	14,280.65
428	02/22/12	03139	Non-Haz Soil	Pure Soil Technologies	33.91	14,314.56
429	02/22/12	03143	Non-Haz Soil	Pure Soil Technologies	29.59	14,344.15
430	02/22/12	03144	Non-Haz Soil	Pure Soil Technologies	30.27	14,374.42
431	02/22/12	03127	Non-Haz Soil	Pure Soil Technologies	31.91	14,406.33
432	02/23/12	03131	Non-Haz Soil	Pure Soil Technologies	33.66	14,439.99
433	02/23/12	03132	Non-Haz Soil	Pure Soil Technologies	31.67	14,471.66
434	02/23/12	03122	Non-Haz Soil	Pure Soil Technologies	32.89	14,504.55
435	02/23/12	03153	Non-Haz Soil	Pure Soil Technologies	35.49	14,540.04
436	02/23/12	03240	Non-Haz Soil	Pure Soil Technologies	28.66	14,568.70
				Total Tons =	**14,568.70**	

Table 7
Summary of Waste Characterization Sampling for Test Pits
260 West 26th Street, New York, NY

Sample Location	Depth (feet)	Sample Type	Sample Jars	Analysis
TP-1	0-7 varying depth	5-pt. composite	(2) 2 oz.	TPH 8015M - Two (2) five point composite samples from different depths
TP-1	0-7 at Highest PID	grab	(2) encore and (1) 2 oz.	VOCs 8260B (NJDEP Soil Cleanup List + TCL/TAL)
TP-1	0-7	5-pt. composite	(2) 8oz.	SVOCs (NJDEP Soil Cleanup List + TCL/TAL), Total Metals (TAL) + Cyanide and Hexavalant Chromium, PCBs, Herbidies/Pesticides (NJDEP Soil Cleanup List+TCL/TAL), Full TCLP (VOCs, SVOCs, Metals, Herbs/Pest and RCRA Characteristics)
TP-1	0-7	5-pt. composite	(1) 8oz.	PAHs 8270, RCRA Metals 6010, Ign, react, corrivity/pH, PCBs 8082A, TCLP RCRA Metals 1311/6010
TP-1	7-14	5-pt. composite	(2) 2 oz.	TPH 8015M - Two (2) five point composite samples from different depths
TP-1	7-14 at Highest PID	grab	(2) encore and (1) 2 oz.	VOCs 8260B (NJDEP Soil Cleanup List + TCL/TAL)
TP-1	7-14	5-pt. composite	(2) 8oz.	SVOCs (NJDEP Soil Cleanup List + TCL/TAL), Total Metals (TAL) + Cyanide and Hexavalant Chromium, PCBs, Herbidies/Pesticides (NJDEP Soil Cleanup List+TCL/TAL), Full TCLP (VOCs, SVOCs, Metals, Herbs/Pest and RCRA Characteristics)
TP-1	7-14	5-pt. composite	(1) 8oz.	PAHs 8270, RCRA Metals 6010, Ign, react, corrivity/pH, PCBs 8082A, TCLP RCRA Metals 1311/6010
TP-2	0-7 varying depth	5-pt. composite	(2) 2 oz.	TPH 8015M - Two (2) five point composite samples from different depths
TP-2	0-7 at Highest PID	grab	(2) encore and (1) 2 oz.	VOCs 8260B (NJDEP Soil Cleanup List + TCL/TAL)
TP-2	0-7	5-pt. composite	(2) 8oz.	SVOCs (NJDEP Soil Cleanup List + TCL/TAL), Total Metals (TAL) + Cyanide and Hexavalant Chromium, PCBs, Herbidies/Pesticides (NJDEP Soil Cleanup List+TCL/TAL), Full TCLP (VOCs, SVOCs, Metals, Herbs/Pest and RCRA Characteristics)
TP-2	0-7	5-pt. composite	(1) 8oz.	PAHs 8270, RCRA Metals 6010, Ign, react, corrivity/pH, PCBs 8082A, TCLP RCRA Metals 1311/6010
TP-2	7-14	5-pt. composite	(2) 2 oz.	TPH 8015M - Two (2) five point composite samples from different depths
TP-2	7-14 at Highest PID	grab	(2) encore and (1) 2 oz.	VOCs 8260B (NJDEP Soil Cleanup List + TCL/TAL)
TP-2	7-14	5-pt. composite	(2) 8oz.	SVOCs (NJDEP Soil Cleanup List + TCL/TAL), Total Metals (TAL) + Cyanide and Hexavalant Chromium, PCBs, Herbidies/Pesticides (NJDEP Soil Cleanup List+TCL/TAL), Full TCLP (VOCs, SVOCs, Metals, Herbs/Pest and RCRA Characteristics)
TP-2	7-14	5-pt. composite	(1) 8oz.	PAHs 8270, RCRA Metals 6010, Ign, react, corrivity/pH, PCBs 8082A, TCLP RCRA Metals 1311/6010
TP-3	0-7 varying depth	5-pt. composite	(2) 2 oz.	TPH 8015M - Two (2) five point composite samples from different depths
TP-3	0-7 at Highest PID	grab	(2) encore and (1) 2 oz.	VOCs 8260B (NJDEP Soil Cleanup List + TCL/TAL)
TP-3	0-7	5-pt. composite	(2) 8oz.	SVOCs (NJDEP Soil Cleanup List + TCL/TAL), Total Metals (TAL) + Cyanide and Hexavalant Chromium, PCBs, Herbidies/Pesticides (NJDEP Soil Cleanup List+TCL/TAL), Full TCLP (VOCs, SVOCs, Metals, Herbs/Pest and RCRA Characteristics)
TP-3	0-7	5-pt. composite	(1) 8oz.	PAHs 8270, RCRA Metals 6010, Ign, react, corrivity/pH, PCBs 8082A, TCLP RCRA Metals 1311/6010
TP-3	7-14	5-pt. composite	(2) 2 oz.	TPH 8015M - Two (2) five point composite samples from different depths
TP-3	7-14 at Highest PID	grab	(2) encore and (1) 2 oz.	VOCs 8260B (NJDEP Soil Cleanup List + TCL/TAL)
TP-3	7-14	5-pt. composite	(2) 8oz.	SVOCs (NJDEP Soil Cleanup List + TCL/TAL), Total Metals (TAL) + Cyanide and Hexavalant Chromium, PCBs, Herbidies/Pesticides (NJDEP Soil Cleanup List+TCL/TAL), Full TCLP (VOCs, SVOCs, Metals, Herbs/Pest and RCRA Characteristics)
TP-3	7-14	5-pt. composite	(1) 8oz.	PAHs 8270, RCRA Metals 6010, Ign, react, corrivity/pH, PCBs 8082A, TCLP RCRA Metals 1311/6010
TP-4	0-7 varying depth	5-pt. composite	(2) 2 oz.	TPH 8015M - Two (2) five point composite samples from different depths
TP-4	0-7 at Highest PID	grab	(2) encore and (1) 2 oz.	VOCs 8260B (NJDEP Soil Cleanup List + TCL/TAL)
TP-4	0-7	5-pt. composite	(2) 8oz.	SVOCs (NJDEP Soil Cleanup List + TCL/TAL), Total Metals (TAL) + Cyanide and Hexavalant Chromium, PCBs, Herbidies/Pesticides (NJDEP Soil Cleanup List+TCL/TAL), Full TCLP (VOCs, SVOCs, Metals, Herbs/Pest and RCRA Characteristics)
TP-4	0-7	5-pt. composite	(1) 8oz.	PAHs 8270, RCRA Metals 6010, Ign, react, corrivity/pH, PCBs 8082A, TCLP RCRA Metals 1311/6010
TP-4	7-14	5-pt. composite	(2) 2 oz.	TPH 8015M - Two (2) five point composite samples from different depths
TP-4	7-14 at Highest PID	grab	(2) encore and (1) 2 oz.	VOCs 8260B (NJDEP Soil Cleanup List + TCL/TAL)
TP-4	7-14	5-pt. composite	(2) 8oz.	SVOCs (NJDEP Soil Cleanup List + TCL/TAL), Total Metals (TAL) + Cyanide and Hexavalant Chromium, PCBs, Herbidies/Pesticides (NJDEP Soil Cleanup List+TCL/TAL), Full TCLP (VOCs, SVOCs, Metals, Herbs/Pest and RCRA Characteristics)
TP-4	7-14	5-pt. composite	(1) 8oz.	PAHs 8270, RCRA Metals 6010, Ign, react, corrivity/pH, PCBs 8082A, TCLP RCRA Metals 1311/6010
TP-5	0 - bedrock varying depth	5-pt. composite	(4) 2 oz.	TPH 8015M - Four (4) five point composite samples from different depths
TP-5	0 - bedrock at Highest PID	grab	(2) encore and (1) 2 oz.	VOCs 8260B (NJDEP Soil Cleanup List + TCL/TAL)
TP-5	0 - bedrock	5-pt. composite	(2) 8oz.	SVOCs (NJDEP Soil Cleanup List + TCL/TAL), Total Metals (TAL) + Cyanide and Hexavalant Chromium, PCBs, Herbidies/Pesticides (NJDEP Soil Cleanup List+TCL/TAL), Full TCLP (VOCs, SVOCs, Metals, Herbs/Pest and RCRA Characteristics)
TP-5	0 - bedrock	5-pt. composite	(1) 8oz.	PAHs 8270, RCRA Metals 6010, Ign, react, corrivity/pH, PCBs 8082A, TCLP RCRA Metals 1311/6010
TP-6	0 - bedrock varying depth	5-pt. composite	(4) 2 oz.	TPH 8015M - Four (4) five point composite samples from different depths
TP-6	0 - bedrock at Highest PID	grab	(2) encore and (1) 2 oz.	VOCs 8260B (NJDEP Soil Cleanup List + TCL/TAL)
TP-6	0 - bedrock	5-pt. composite	(2) 8oz.	SVOCs (NJDEP Soil Cleanup List + TCL/TAL), Total Metals (TAL) + Cyanide and Hexavalant Chromium, PCBs, Herbidies/Pesticides (NJDEP Soil Cleanup List+TCL/TAL), Full TCLP (VOCs, SVOCs, Metals, Herbs/Pest and RCRA Characteristics)
TP-6	0 - bedrock	5-pt. composite	(1) 8oz.	PAHs 8270, RCRA Metals 6010, Ign, react, corrivity/pH, PCBs 8082A, TCLP RCRA Metals 1311/6010
TP-7	0 - bedrock varying depth	5-pt. composite	(4) 2 oz.	TPH 8015M - Four (4) five point composite samples from different depths
TP-7	0 - bedrock at Highest PID	grab	(2) encore and (1) 2 oz.	VOCs 8260B (NJDEP Soil Cleanup List + TCL/TAL)
TP-7	0 - bedrock	5-pt. composite	(2) 8oz.	SVOCs (NJDEP Soil Cleanup List + TCL/TAL), Total Metals (TAL) + Cyanide and Hexavalant Chromium, PCBs, Herbidies/Pesticides (NJDEP Soil Cleanup List+TCL/TAL), Full TCLP (VOCs, SVOCs, Metals, Herbs/Pest and RCRA Characteristics)
TP-7	0 - bedrock	5-pt. composite	(1) 8oz.	PAHs 8270, RCRA Metals 6010, Ign, react, corrivity/pH, PCBs 8082A, TCLP RCRA Metals 1311/6010
TP-8	0 - bedrock varying depth	5-pt. composite	(4) 2 oz.	TPH 8015M - Four (4) five point composite samples from different depths
TP-8	0 - bedrock at Highest PID	grab	(2) encore and (1) 2 oz.	VOCs 8260B (NJDEP Soil Cleanup List + TCL/TAL)
TP-8	0 - bedrock	5-pt. composite	(2) 8oz.	SVOCs (NJDEP Soil Cleanup List + TCL/TAL), Total Metals (TAL) + Cyanide and Hexavalant Chromium, PCBs, Herbidies/Pesticides (NJDEP Soil Cleanup List+TCL/TAL), Full TCLP (VOCs, SVOCs, Metals, Herbs/Pest and RCRA Characteristics)
TP-8	0 - bedrock	5-pt. composite	(1) 8oz.	PAHs 8270, RCRA Metals 6010, Ign, react, corrivity/pH, PCBs 8082A, TCLP RCRA Metals 1311/6010

One composite sample from the site must also get Paint filter Method 9095

APPENDIX A

Sustainability Report

APPENDIX A

SUSTAINABILITY REPORT

This Remedial Action Work Plan provides for sustainable remediation and redevelopment through a variety of means that are defined in this Sustainability Report.

Reuse of Clean, Recyclable Materials. Reuse of clean, recyclable materials reduces consumption of non-renewable virgin resources and can provide energy savings and greenhouse gas reduction since these materials can be locally-derived. We have used approximately 1,582 cubic yards of recycled crushed concrete aggregate.

Conservation of Non-Renewable Resources. Reduced consumption of non-renewable resources such as soil and top-soil lowers the overall environmental impact of the project on the region by conserving these resources.

Conservation of non-renewable resources was achieved by utilizing crushed concrete to raise and level the final grade of the excavation for construction purposes as opposed to virgin soil. An estimate of the cubic yards of non-renewable resources, the use of which was avoided under this plan, is approximately 1,500 cubic yards.

Recontamination Control. Recontamination after cleanup and redevelopment is completed undermines the value of work performed, may result in a property that is less protective of public health or the environment, and may necessitate additional cleanup work later that could impede future redevelopment. Recontamination can arise from future releases that occur within the property or by influx of existing contamination from off-Site.

The area of the Site that utilizes recontamination controls under this plan is 32,118.19 square feet, or 100% of the project area. The measures taken to prevent site recontamination include the installation of a water-proofing membrane below the cellar slab and along all foundation walls and “Track 1” site remediation assuring that there are is no contaminated soil left on site.

Storm-water Retention. Storm-water retention improves water quality by lowering the rate of combined storm-water and sewer discharges to NYC's sewage treatment plants during periods of precipitation, and reduces the volume of untreated influent to local surface waters.

We are utilizing control flow roof drainage on the main roof which will slowly discharge the buildup of storm water to the city sewer system in a prescribed CFS allowable rate. Based on this the 6,533 sq. ft. green roof will retain 30% of the storm water falling on this roof. Based on this, we can calculate the discharge – 6,533/43560 x 5.95 x 0.70 = 0.62 cfs. C of 1.0 = 0.89 cfs. We effectively are retaining 0.27 cfs or 30%.

Linkage with Green Building. Green buildings provide a multitude of benefits to the city across a broad range of areas, such as reduction of energy consumption, conservation of resources, and reduction in toxic materials use.

260 West 26th Street is aiming for LEED Silver certification, following the protocols of the US Green Building Certification Institute. This includes use of VOC-free materials, regionally manufactured and recycled materials, native plant species, outdoor space for tenants, light controllability, and energy consumption at least 20% below the current ASHRAE baseline.

Paperless Brownfield Cleanup Program. Project participated in OER's Paperless Brownfield Cleanup Program. Under this program, submission of electronic documents replaced submission of hard copies for the review of project documents, communications and milestone reports. A best estimate of the mass of paper saved under this plan is 15 pounds.

Low-Energy Project Management Program. Project participated in OER's low-energy project management program. Under this program, whenever possible, meetings were held using remote communication technologies, such as videoconferencing and teleconferencing to reduce energy consumption and traffic congestion associated with personal transportation. A gross estimate of the number of miles of personal transportation that was conserved in this process is 250 miles.

Trees and Plantings. Trees and other plantings provide habitat and add to NYC's environmental quality in a wide variety of ways. Native plant species and native habitat provide optimal support to local fauna, promote local biodiversity, and require less maintenance. The number of trees planted as part of this redevelopment is 5.

APPENDIX B

Property Redevelopment Plans
(electronic Copies only)

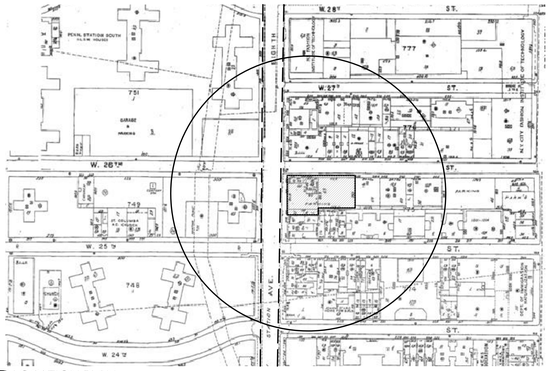

C LOCATION PLAN

NTS

SITE REQUIREMENT NOTES:

ZONING REQUIREMENT:
EVERY 25'-0" OF SIDEWALK.

TOTAL LENGTH OF SIDEWALK:
215'-4" + 123'-3" + 84'-9" (LOT 64) = 423'-4"

TOTAL REQUIRED TREES BASED ON THE STREET LENGTH:
17 STREET TREES REQUIREMENT FOR ENTIRE SITE.

TREE SPACING REQUIREMENTS:
40'-0" MIN. FROM STREET INTERSECTION
7'-0" MIN. FROM CURB CUT OR DRIVEWAY
7'-0" MIN. FROM LIGHT POLE
10'-0" MIN. FROM PHONE BOOTH
25'-0" MIN. FROM STREET LIGHT
5'-0" MIN. FROM FIRE HYDRANT
6'-0" MIN. FROM TRAFFIC SIGN
7'-0" MIN. FROM ELECTRICAL VAULT
NO TREES IN FRONT OF THE BUILDING ENTRANCE

TOTAL PROPOSED STREET TREES BASED ON STREET TREE SPACING REQUIREMENTS LISTED ABOVE:
2 EXISTING + 3 NEW = 5 TOTAL STREET TREES
12 TREES TO BE PLANTED OFF SITE

SITE NOTES:

THE BUILDING NOT LOCATED WITHIN 200'-0" OF ANY MTA TUNNEL.
NO BUILDING WITHIN 90'-0" OF THE SITE ARE LANDMARKED BUILDINGS.

CONCRETE SLAB SIDEWALK NOTES:

1. CONCRETE SLAB PATTERN SHALL BE 5' BY 5'
2. CONCRETE COLOR SHALL BE ORIGINAL

GENERAL NOTES:

1. THE DESIGN, DETAILS AND NOTES INCLUDED HEREIN ARE IN COMPLIANCE WITH LOCAL LAW 17/95 FOR SEISMIC DESIGN.
2. THERE WILL BE NO OFF SITE FILL.
3. ALL DRAINS SHALL BE CONNECTED TO BUILDING SEWER SYSTEM.

NOTE:

1. THE BUILDING IS NOT INSIDE OF THE FLOOD HAZARD AREA.
2. THE BUILDING IS INSIDE OTHER ZONE X. (AREAS TO BE DETERMINED OUTSIDE THE 0.2% CHANCE FLOOD PLAIN.)
3. BASEMENT ELEVATION (LOWEST LEVEL) IS -14'-7 1/4" (9.40')
4. NO MORE THAN 2% SLOPE IN FRONT OF ALL ENTRANCES. SEE 1ST FLOOR PLAN.

LIST OF ESTIMATED QUANTITIES:

NEW CURB: 367 LIN FT
NEW SIDEWALK: 4,898 SQ FT
NEW TREES: 2 EXISTING, 3 NEW, 12 OFF SITE
NEW MANHOLES: N/A
NEW CB'S: N/A

LEGEND

- DETECTABLE WARNING AT SIDEWALK
- ACCESSIBLE PATH AT SIDEWALK
- TREE PIT
- PARKING METER
- HYDRANT
- LIGHT POLE
- POLE
- BIKE RACK
- TRAFFIC FLOW
- TREE

B FLOOD RATE INSURANCE MAP

NTS

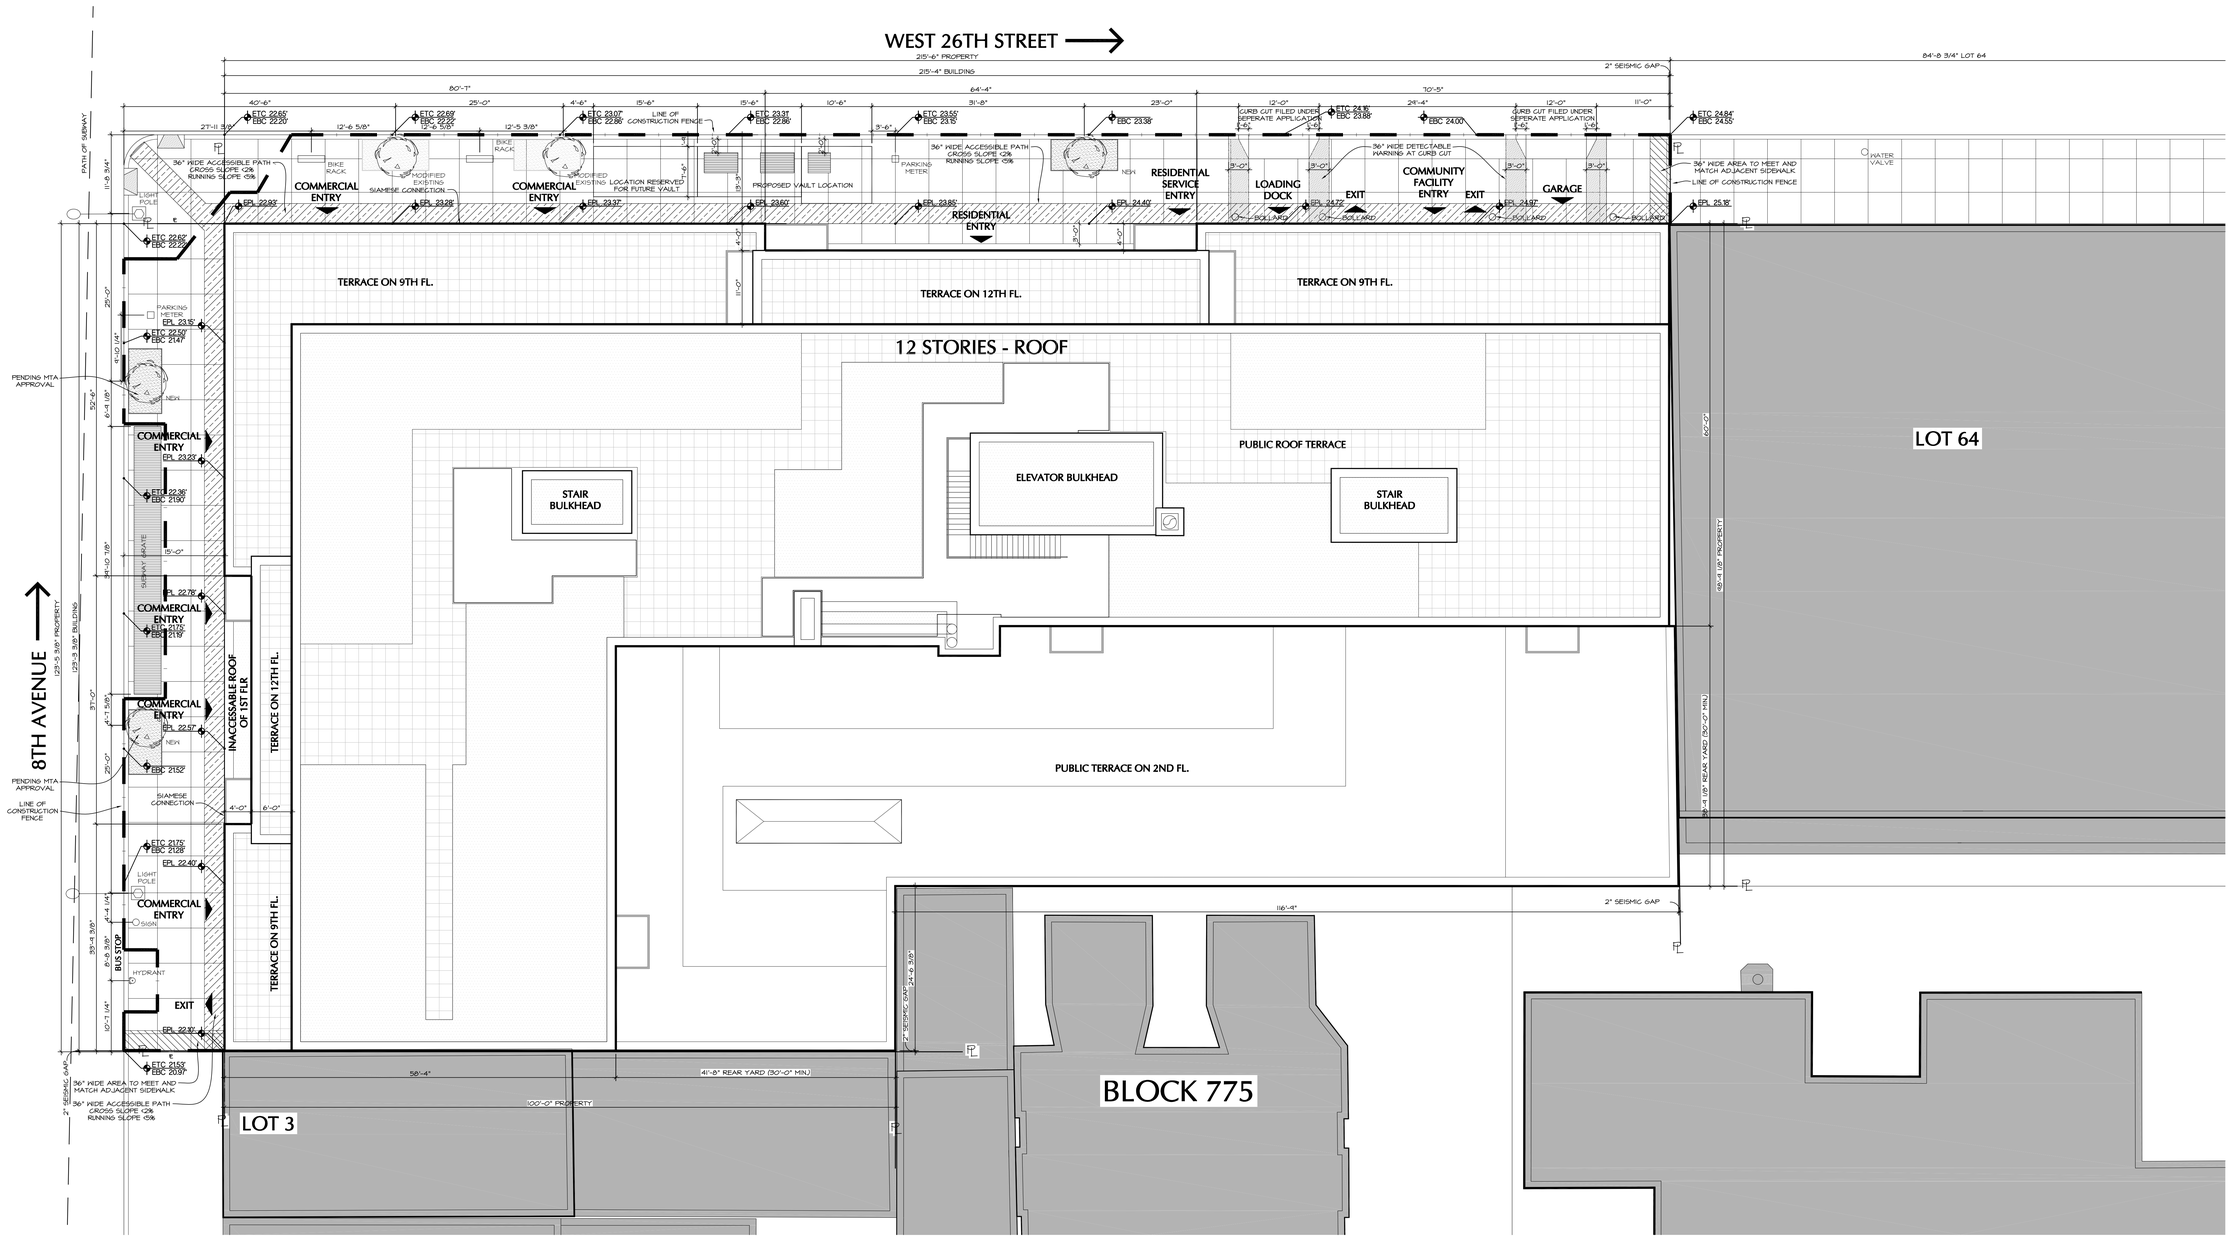

A SITE PLAN

1/8"=1'-0"

GF55 PARTNERS
19 W. 21ST STREET
NEW YORK, N Y 10010
212 352 3099
©GF55 Partners, LLP 2011

260 WEST 26TH STREET
NEW YORK NY 10001

BLOCK: 775
LOT: 4, 69, 77, 78, 79, 80

DEVELOPER
ARTIMUS

STRUCTURAL ENGINEER
ENGINEERING GROUP

MECHANICAL ENGINEER
RODKIN CARDINALE ENGINEERS P.C.

OWNER
CHELSEA W26 LLC

ISSUE
DOB APPROVED SET AUGUST 5, 2011
100% FOUNDATION SET JULY 29, 2011
REVISION 1 SEPT 16, 2011
85% CONSTRUCTION SET SEPTEMBER 21, 2011
100% SUPER STRUCTURE SET SEPT 26, 2011
REVISION 2 NOV 2, 2011
REVISION 3 NOV 14, 2011
100% CONSTRUCTION SET DECEMBER 16, 2011

SCALE
1/8"=1'-0"

PROJECT
260 WEST 26TH STREET

DRAWING
SITE PLAN

SEAL AND SIGNATURE

DATE: 12.16.2011
PROJECT NO: 1574.00
DRAWING BY: JD
CHK BY: MR
DWG NO:
A-100.00
CADD FILE NO: 10 OF 100

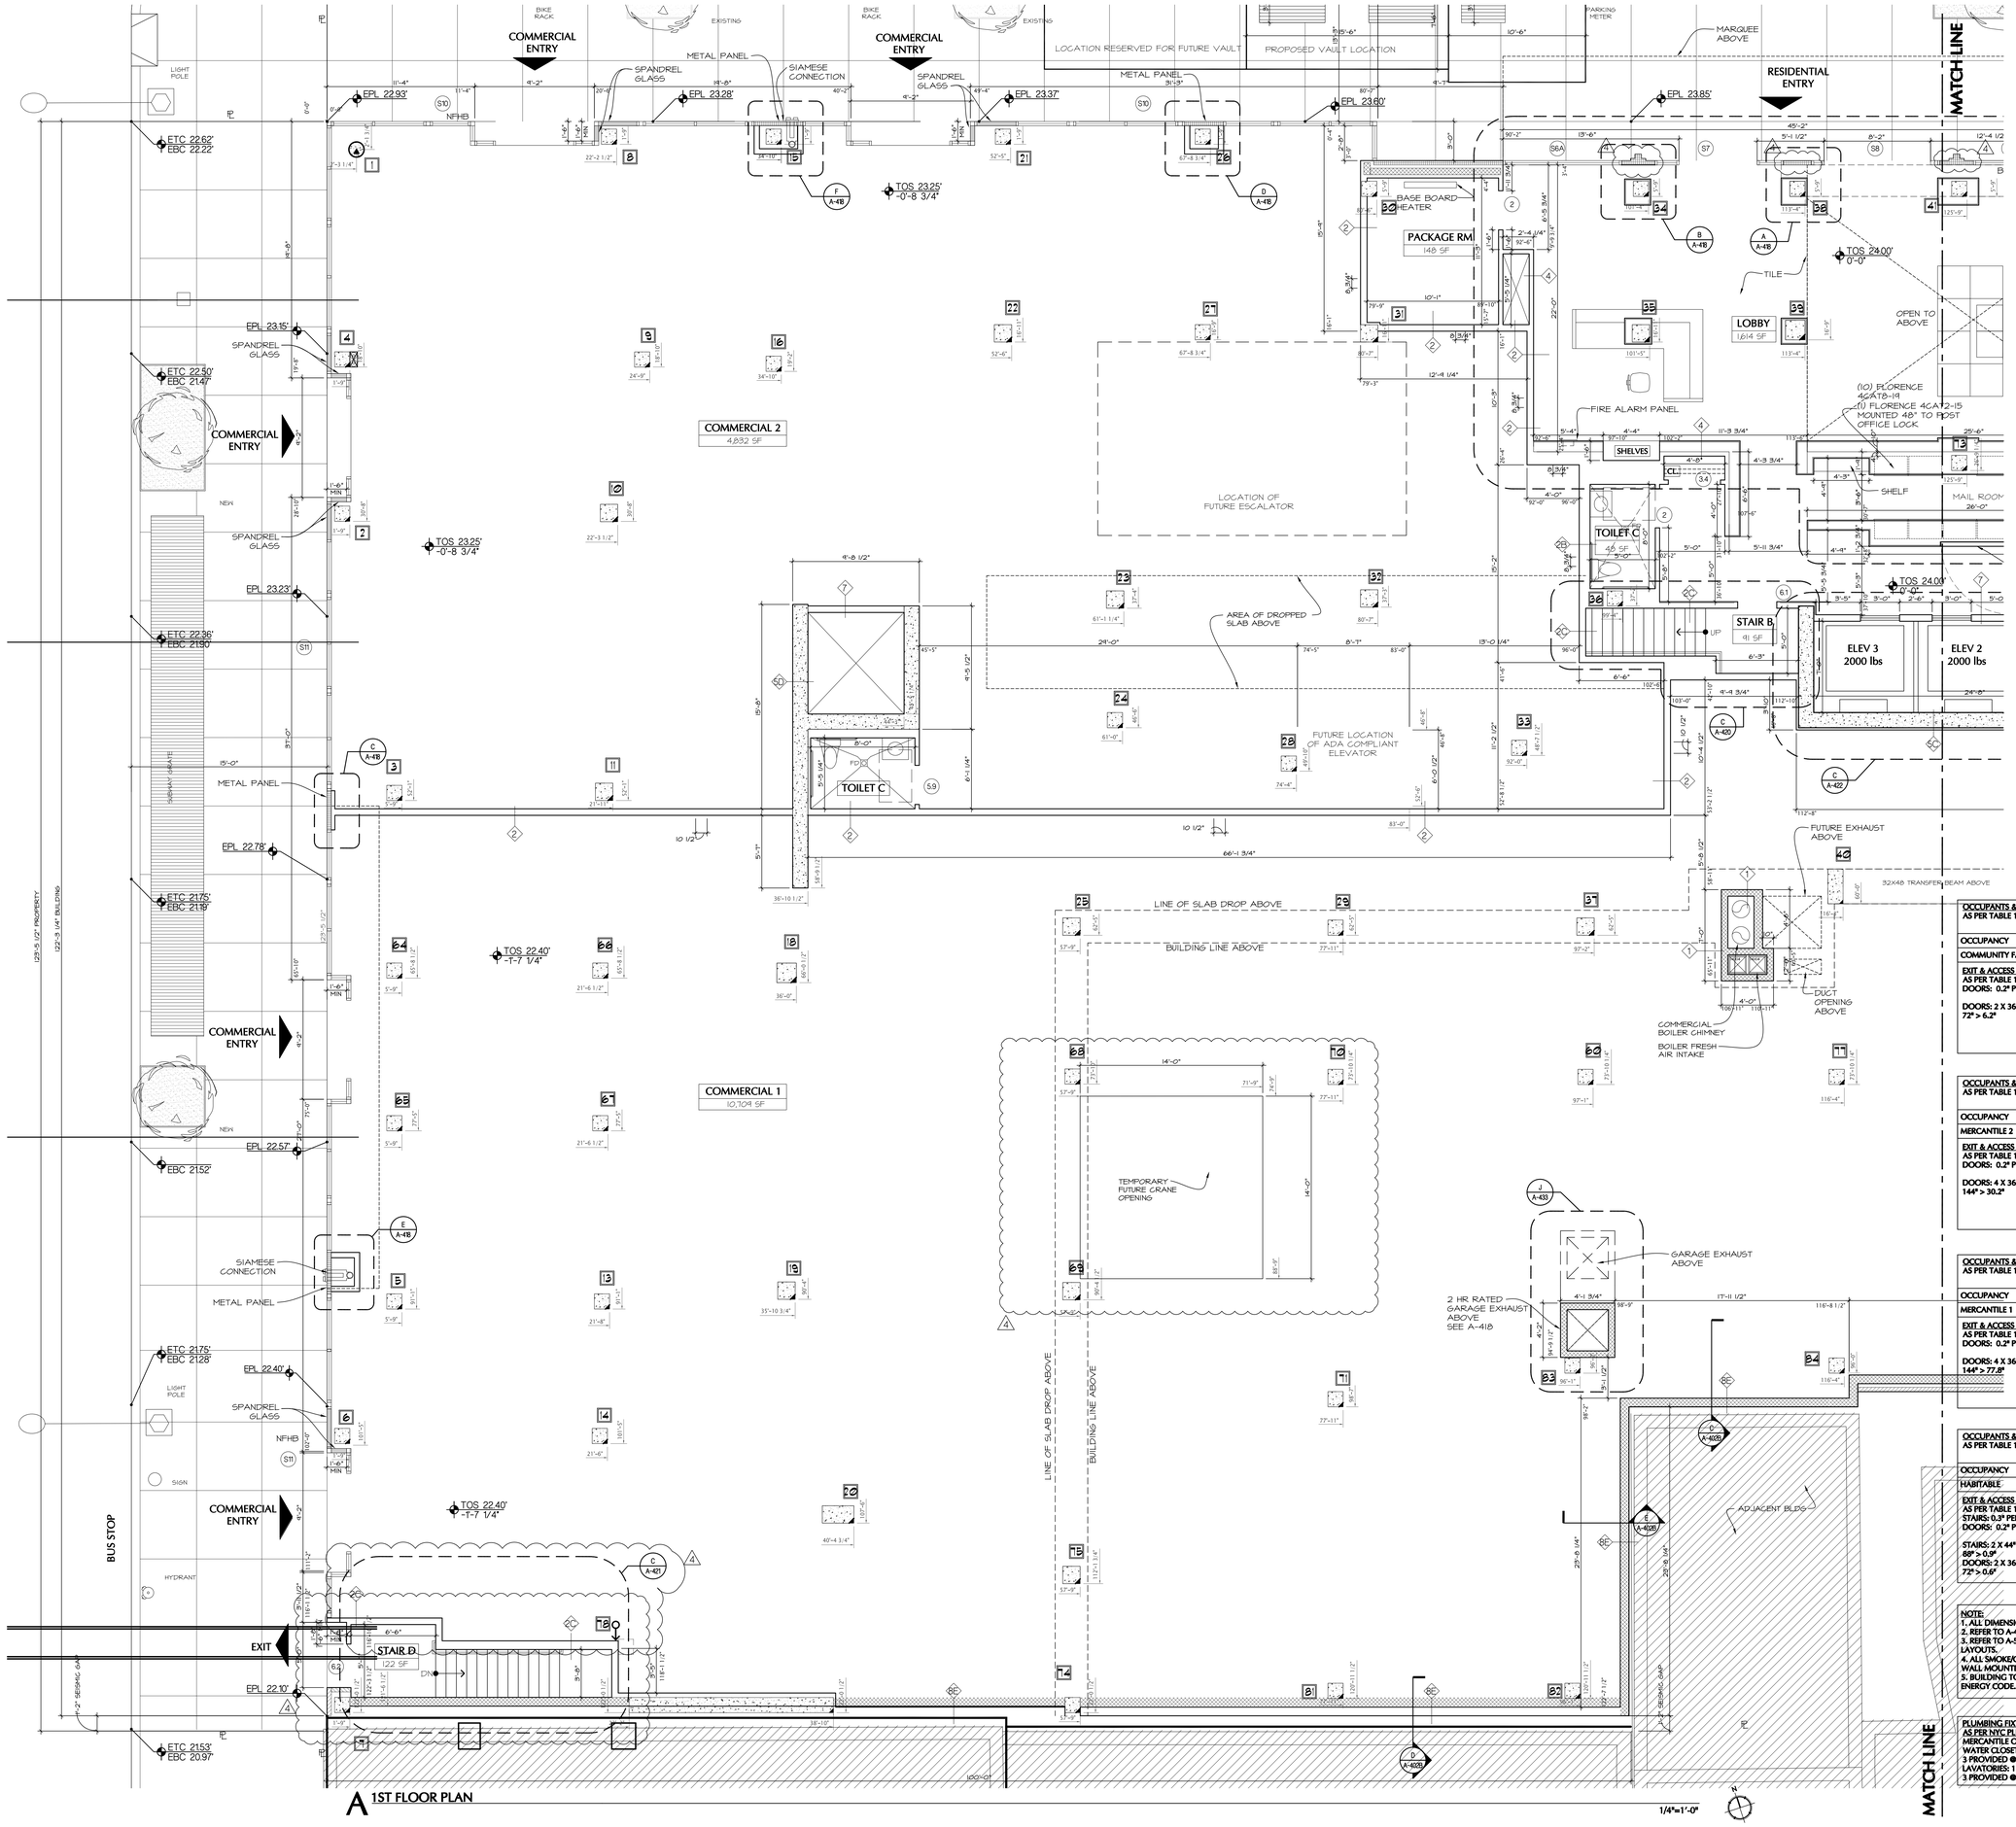

A 1ST FLOOR PLAN

1/4"=1'-0"

MATERIAL LEGEND
BRICK
CMU
PRECAST
SPANDREL
METAL PANEL

OCCUPANTS & LOAD REQUIRMENTS:
AS PER TABLE 1004.1.2

OCCUPANCY	AREA / OCCUPANT	# OF OCCUPANTS
COMMUNITY FACILITY	616 / 20	31

EXIT & ACCESS REQUIREMENTS:
AS PER TABLE 1005.1
DOORS: 0.2" PER OCCUPANT

DOORS: 2 X 36" > 31 X 0.2"
72" > 6.2"

OCCUPANTS & LOAD REQUIRMENTS:
AS PER TABLE 1004.1.2

OCCUPANCY	AREA / OCCUPANT	# OF OCCUPANTS
MERCANTILE 2	4,532 / 30	151

EXIT & ACCESS REQUIREMENTS:
AS PER TABLE 1005.1
DOORS: 0.2" PER OCCUPANT

DOORS: 4 X 36" > 151 X 0.2"
144" > 30.2"

OCCUPANTS & LOAD REQUIRMENTS:
AS PER TABLE 1004.1.2

OCCUPANCY	AREA / OCCUPANT	# OF OCCUPANTS
MERCANTILE 1	11,662 / 30	389

EXIT & ACCESS REQUIREMENTS:
AS PER TABLE 1005.1
DOORS: 0.2" PER OCCUPANT

DOORS: 4 X 36" > 389 X 0.2"
144" > 77.8"

OCCUPANTS & LOAD REQUIRMENTS:
AS PER TABLE 1004.1.2

OCCUPANCY	AREA / OCCUPANT	# OF OCCUPANTS
HABITABLE	465.95 / 200	3

EXIT & ACCESS REQUIREMENTS:
AS PER TABLE 1005.1
STAIRS: 0.3" PER OCCUPANT
DOORS: 0.2" PER OCCUPANT

STAIRS: 2 X 44" > 3 X 0.3"
88" > 0.9"
DOORS: 2 X 36" > 3 X 0.2"
72" > 0.6"

NOTE:
1. ALL DIMENSIONS FROM FINISH TO FINISH.
2. REFER TO A-420, A-421 FOR STAIR DIMENSIONS.
3. REFER TO A-501, A-502 & A-503 FOR KITCHEN & BATH LAYOUTS.
4. ALL SMOKE/CARBON MONOXIDE DETECTORS TO BE WALL MOUNTED.
5. BUILDING TO BE IN FULL COMPLIANCE WITH NYS ENERGY CODE.

PLUMBING FIXTURE REQUIREMENTS:
AS PER NYC PLUMBING CODE TABLE 403.1:
MERCANTILE OCCUPANCY
WATER CLOSET: 1 PER 500 REQUIRED
3 PROVIDED @ 1ST FLOOR
LAVATORIES: 1 PER 750 REQUIRED
3 PROVIDED @ 1ST FLOOR

GF55
PARTNERS
19 W. 21ST STREET
NEW YORK, N Y 10010
212 352 3099
©GF55 Partners, LLP 2012

260 WEST 26TH STREET
NEW YORK NY 10001

BLOCK: 775
LOT: 4, 69, 77, 78, 79, 80

DEVELOPER
ARTIMUS

STRUCTURAL ENGINEER
ENGINEERING GROUP

MECHANICAL ENGINEER
RODKIN CARDINALE ENGINEERS P.C.

OWNER
CHELSEA W26 LLC

ISSUE
DOB APPROVED SET AUGUST 5, 2011
100% FOUNDATION SET JULY 29, 2011
REVISION 1 SEPT 16, 2011
85% CONSTRUCTION SET SEPTEMBER 21, 2011
100% SUPER STRUCTURE SET SEPT 26, 2011
REVISION 2 NOV 2, 2011
REVISION 3 NOV 14, 2011
100% CONSTRUCTION SET DECEMBER 16, 2011
REVISION 4 FEB 3, 2012

SCALE
1/4"=1'-0"

PROJECT
260 WEST 26TH STREET

DRAWING
1ST FLOOR PLAN

SEAL AND SIGNATURE

DATE: 02.03.2012
PROJECT NO: 1374.00
DRAWING BY: JD CC DR
CHK BY: MR
DWG NO:
A-102A
CADD FILE NO: 13 OF 100

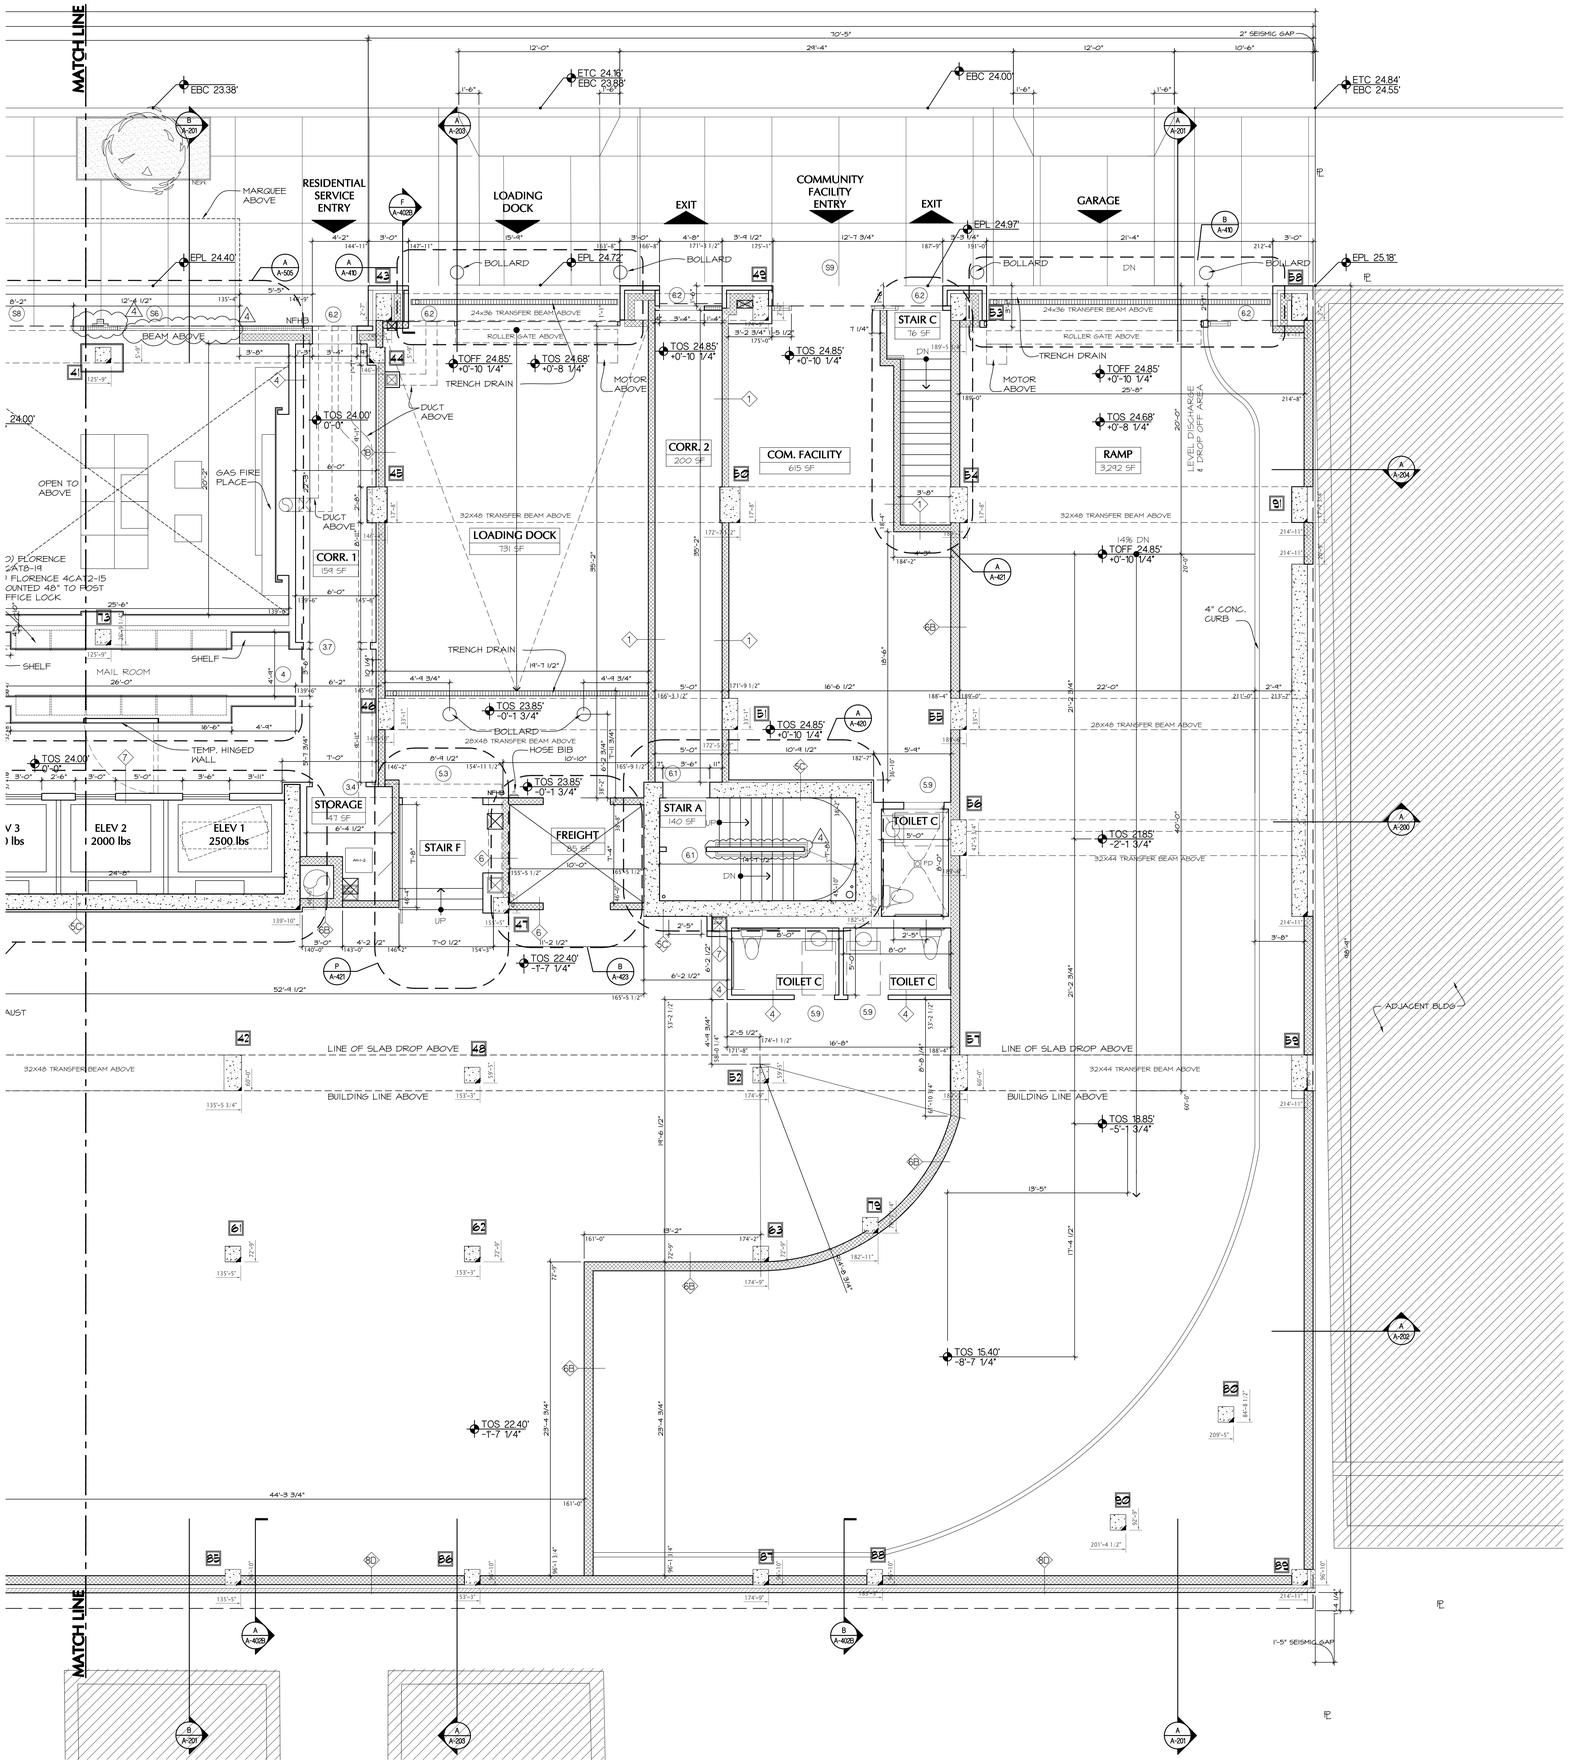

A 1ST FLOOR PLAN

1/4"=1'-0"

MATERIAL LEGEND
BRICK
CMU
PRECAST
SPANDREL
METAL PANEL

OCCUPANTS & LOAD REQUIRMENTS:
AS PER TABLE 1004.1.2

OCCUPANCY	AREA / OCCUPANT	# OF OCCUPANTS
COMMUNITY FACILITY	616 / 20	31

EXIT & ACCESS REQUIREMENTS:
AS PER TABLE 1005.1
DOORS: 0.2" PER OCCUPANT

DOORS: 2 X 36" > 31 X 0.2"
72" > 6.2"

OCCUPANTS & LOAD REQUIRMENTS:
AS PER TABLE 1004.1.2

OCCUPANCY	AREA / OCCUPANT	# OF OCCUPANTS
MERCANTILE 2	4,532 / 30	151

EXIT & ACCESS REQUIREMENTS:
AS PER TABLE 1005.1
DOORS: 0.2" PER OCCUPANT

DOORS: 4 X 36" > 151 X 0.2"
144" > 30.2"

OCCUPANTS & LOAD REQUIRMENTS:
AS PER TABLE 1004.1.2

OCCUPANCY	AREA / OCCUPANT	# OF OCCUPANTS
MERCANTILE 1	11,662 / 30	389

EXIT & ACCESS REQUIREMENTS:
AS PER TABLE 1005.1
DOORS: 0.2" PER OCCUPANT

DOORS: 4 X 36" > 389 X 0.2"
144" > 77.8"

OCCUPANTS & LOAD REQUIRMENTS:
AS PER TABLE 1004.1.2

OCCUPANCY	AREA / OCCUPANT	# OF OCCUPANTS
HABITABLE	465.95 / 200	3

EXIT & ACCESS REQUIREMENTS:
AS PER TABLE 1005.1
STAIRS: 0.3" PER OCCUPANT
DOORS: 0.2" PER OCCUPANT

STAIRS: 2 X 44" > 3 X 0.3"
88" > 0.9"
DOORS: 2 X 36" > 3 X 0.2"
72" > 0.6"

NOTE:
1. ALL DIMENSIONS FROM FINISH TO FINISH.
2. REFER TO A-420 & A-421 FOR STAIR DIMENSIONS.
3. REFER TO A-501,502 & 503 FOR KITCHEN & BATH LAYOUTS.
4. ALL SMOKE/CARBON MONOXIDE DETECTORS TO BE WALL MOUNTED.
5. BUILDING TO BE IN FULL COMPLIANCE WITH NYS ENERGY CODE.

PLUMBING FIXTURE REQUIREMENTS:
AS PER NYC PLUMBING CODE TABLE 403.1:
MERCANTILE OCCUPANCY
WATER CLOSET: 1 PER 500 REQUIRED
3 PROVIDED @ 1ST FLOOR
LAVATORIES: 1 PER 750 REQUIRED
3 PROVIDED @ 1ST FLOOR

GF55
PARTNERS
19 W. 21ST STREET
NEW YORK, N Y 10010
212 352 3099
©GF55 Partners, LLP 2012

260 WEST 26TH STREET
NEW YORK NY 10001

BLOCK: 775
LOT: 4, 69, 77, 78, 79, 80

DEVELOPER
ARTIMUS

STRUCTURAL ENGINEER
ENGINEERING GROUP

MECHANICAL ENGINEER
RODKIN CARDINALE ENGINEERS P.C.

OWNER
CHELSEA W26 LLC

ISSUE
DOB APPROVED SET AUGUST 5, 2011
100% FOUNDATION SET JULY 29, 2011
REVISION 1 SEPT 16, 2011
85% CONSTRUCTION SET SEPTEMBER 21, 2011
100% SUPER STRUCTURE SET SEPT 26, 2011
REVISION 2 NOV 2, 2011
REVISION 3 NOV 14, 2011
100% CONSTRUCTION SET DECEMBER 16, 2011
REVISION 4 FEB 3, 2012

SCALE
1/4"=1'-0"

PROJECT
260 WEST 26TH STREET

DRAWING
1ST FLOOR PLAN

SEAL AND SIGNATURE

DATE: 02.03.2012
PROJECT NO: 1574.00
DRAWING BY: JD CC DR
CHK BY: MR
DWG NO:

A-102B

CADD FILE NO: 14 OF 100

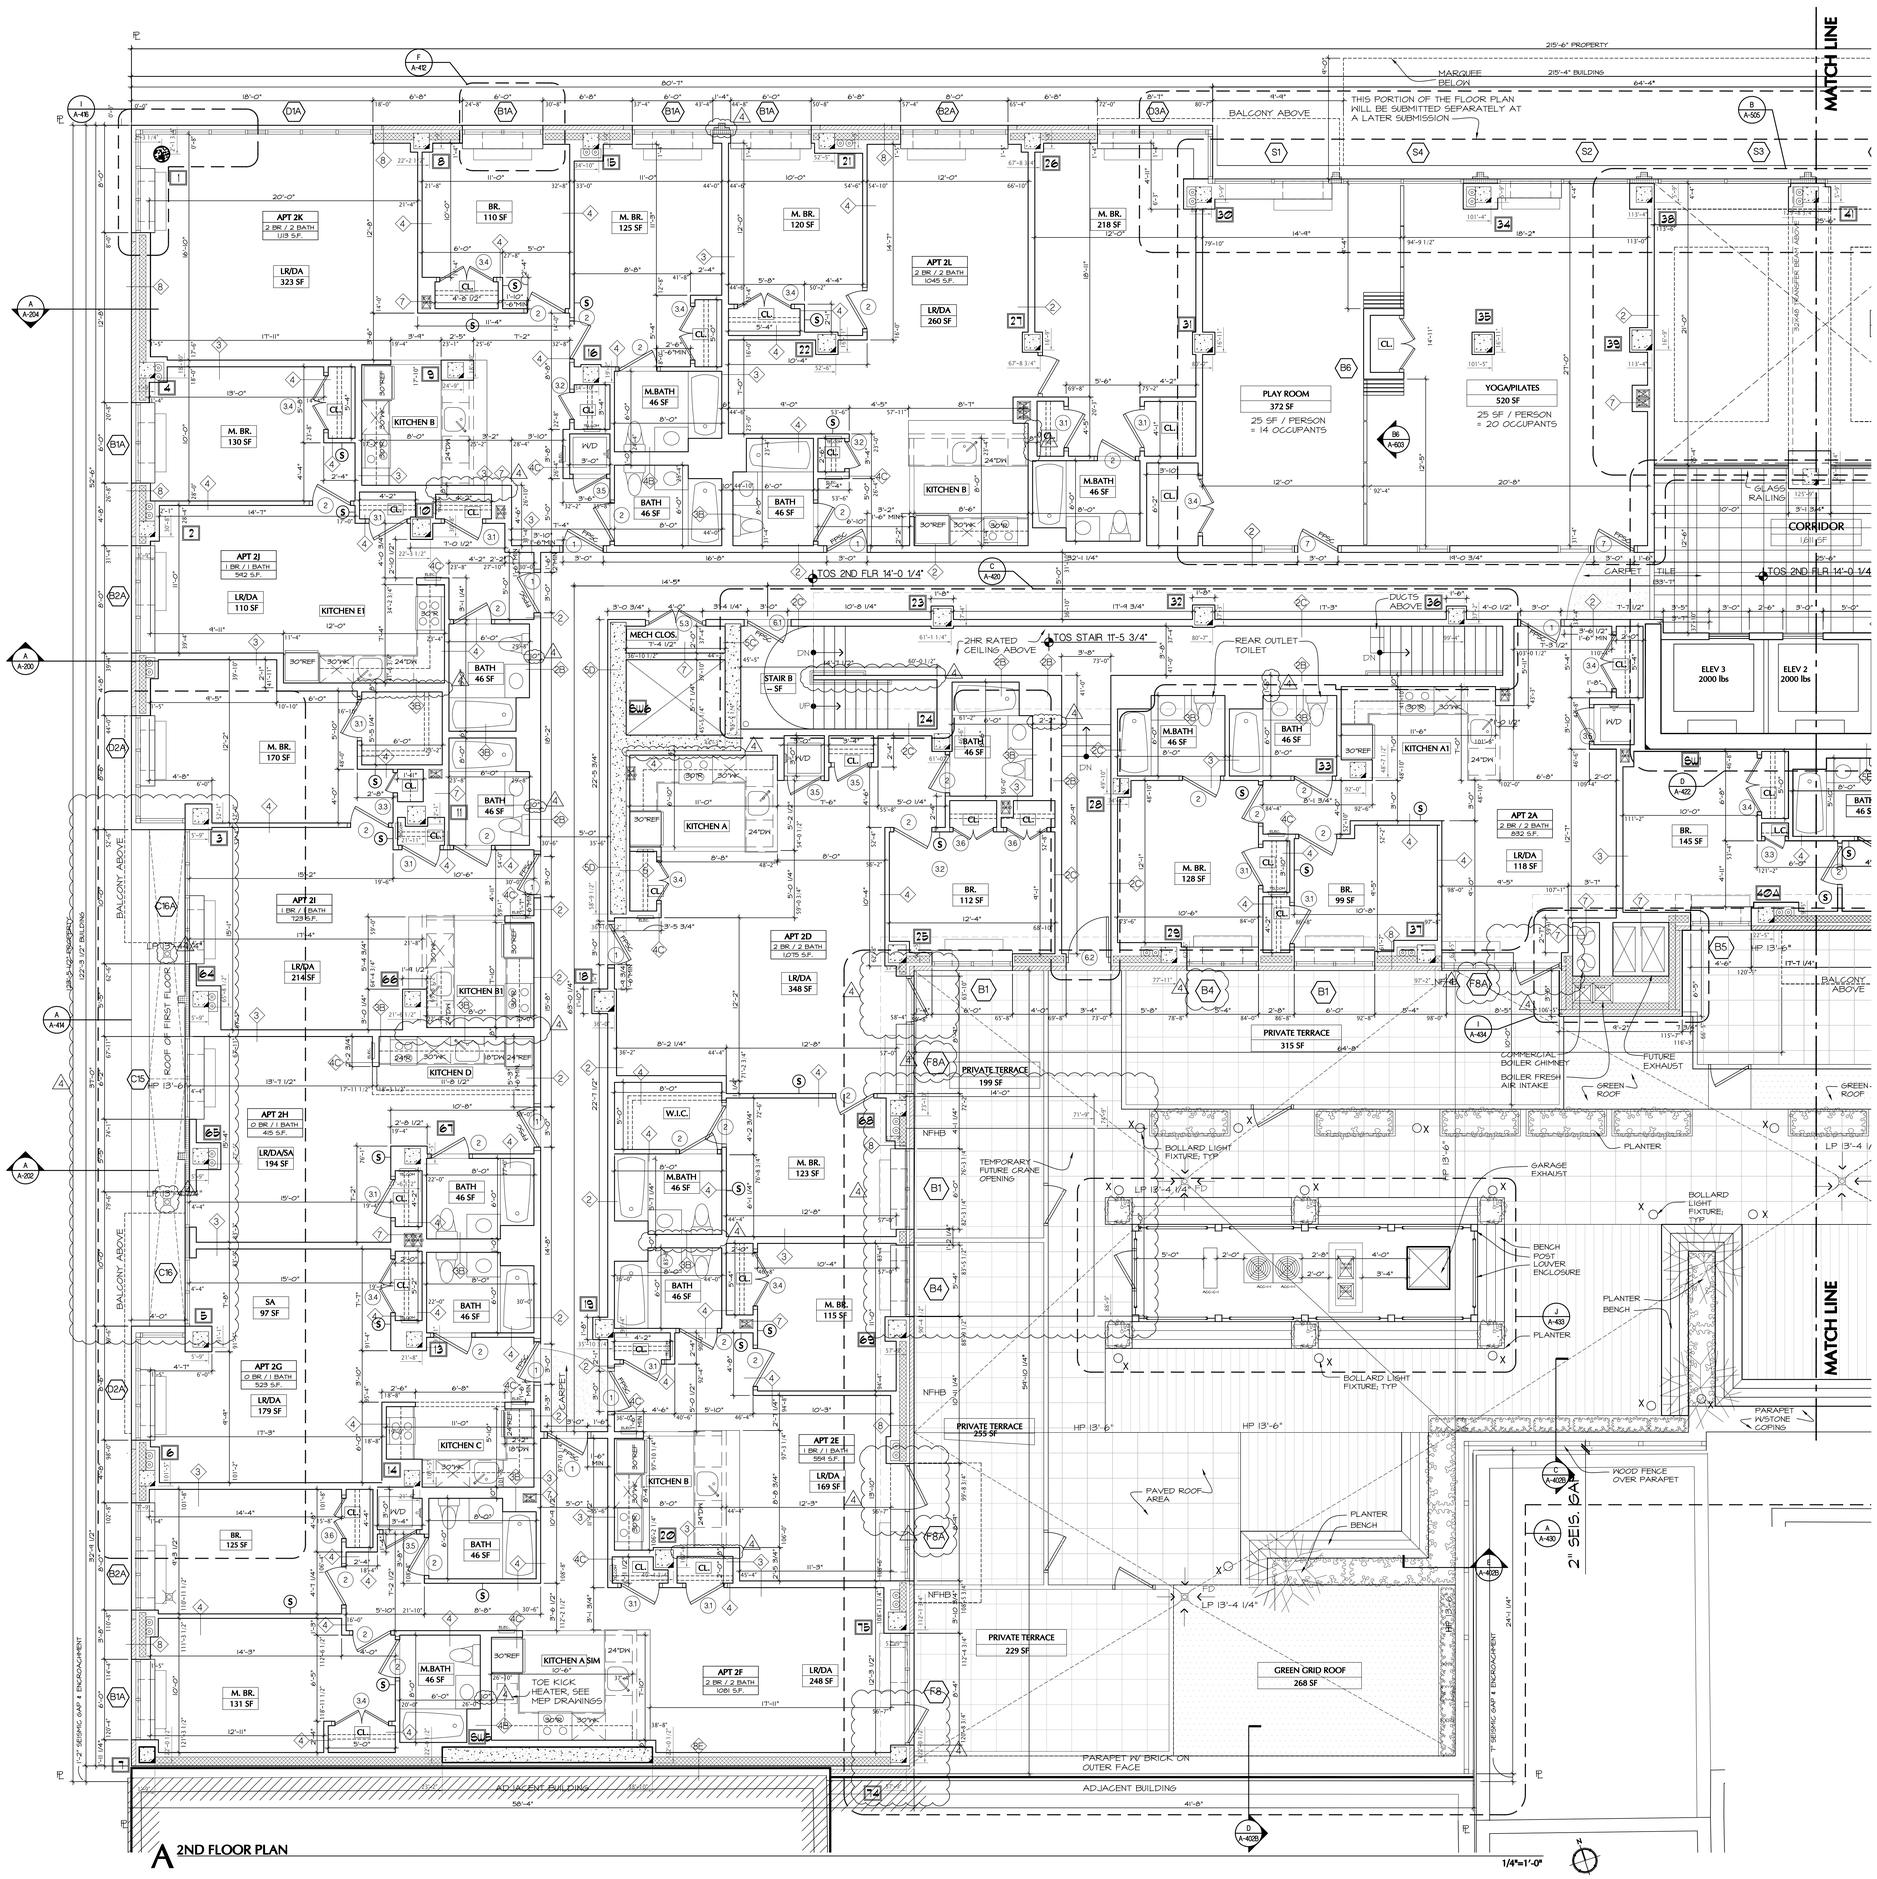

A 2ND FLOOR PLAN

GF55
PARTNERS
19 W. 21ST STREET
NEW YORK, N Y 10010
212 352 3099
©GF55 Partners, LLP 2012

260 WEST 26TH STREET
NEW YORK NY 10001

BLOCK: 775
LOT: 4, 69, 77, 78, 79, 80

DEVELOPER
ARTIMUS

STRUCTURAL ENGINEER
ENGINEERING GROUP

MECHANICAL ENGINEER
RODKIN CARDINALE ENGINEERS P.C.

OWNER
CHELSEA W26 LLC

ISSUE
DOB APPROVED SET AUGUST 5, 2011
100% FOUNDATION SET JULY 29, 2011
REVISION 1 SEPT 16, 2011
85% CONSTRUCTION SET SEPTEMBER 21, 20
100% SUPER STRUCTURE SET SEPT 26, 2011
REVISION 2 NOV 2, 2011
REVISION 3 NOV 14, 2011
100% CONSTRUCTION SET DECEMBER 16, 2
REVISION 4 FEB 3, 2012

SCALE
1/4"=1'-0"

PROJECT
260 WEST 26TH STREET

DRAWING
2ND FLOOR PLAN

SEAL AND SIGNATURE

DATE: 02.03.2012
PROJECT NO: 1574.00
DRAWING BY: JD CC DR
CHK BY: MR
DWG NO:
A-103A
CADD FILE NO: 15 OF 10

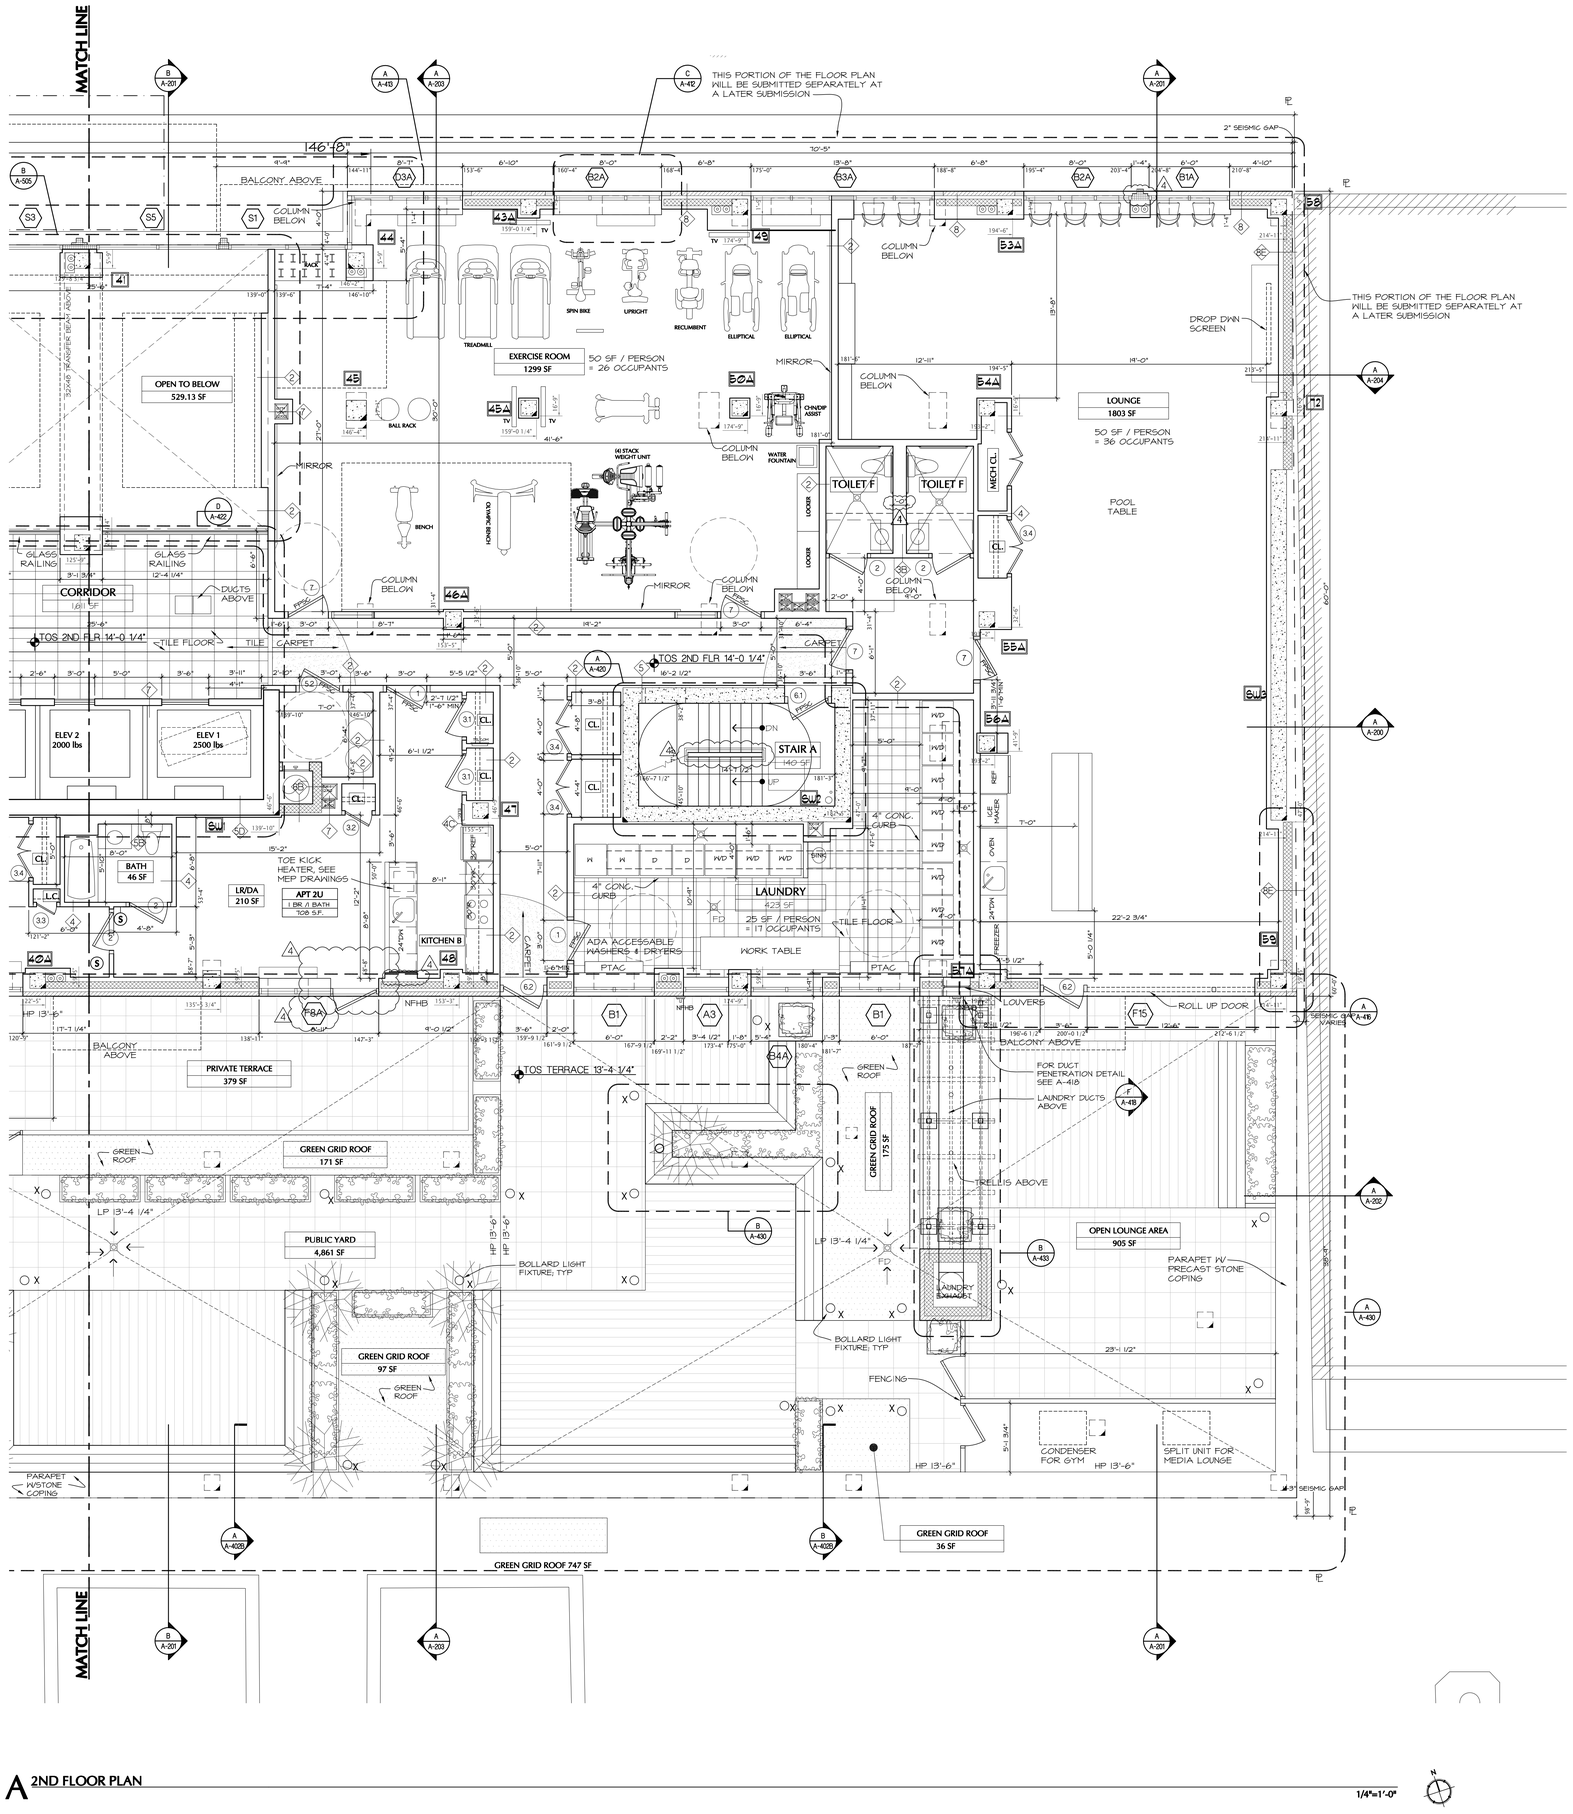

A 2ND FLOOR PLAN

1/4"=1'-0"

GF55
PARTNERS
19 W. 21ST STREET
NEW YORK, N Y 10010
212 352 3099

©GF55Partners, LLP 2012

260 WEST 26TH STREET
NEW YORK NY 10001

BLOCK: 775
LOT: 4, 69, 77, 78, 79, 80

DEVELOPER
ARTIMUS

STRUCTURAL ENGINEER
ENGINEERING GROUP

MECHANICAL ENGINEER
RODKIN CARDINALE ENGINEERS P.C.

OWNER
CHELSEA W26 LLC

ISSUE
DOB APPROVED SET AUGUST 5, 2011
100% FOUNDATION SET JULY 29, 2011
REVISION 1 SEPT 16, 2011
85% CONSTRUCTION SET SEPTEMBER 21, 2011
100% SUPER STRUCTURE SET SEPT 26, 2011
REVISION 2 NOV 2, 2011
REVISION 3 NOV 14, 2011
100% CONSTRUCTION SET DECEMBER 16, 2011
REVISION 4 FEB 3, 2012

SCALE
1/4"=1'-0"

PROJECT
260 WEST 26TH STREET

DRAWING
2ND FLOOR PLAN

SEAL AND SIGNATURE

DATE: 02.03.2012
PROJECT NO: 1574.00
DRAWING BY: JD CC DR
CHK BY: MR
DWG NO:
A-103B
CADD FILE NO: 16 OF 100

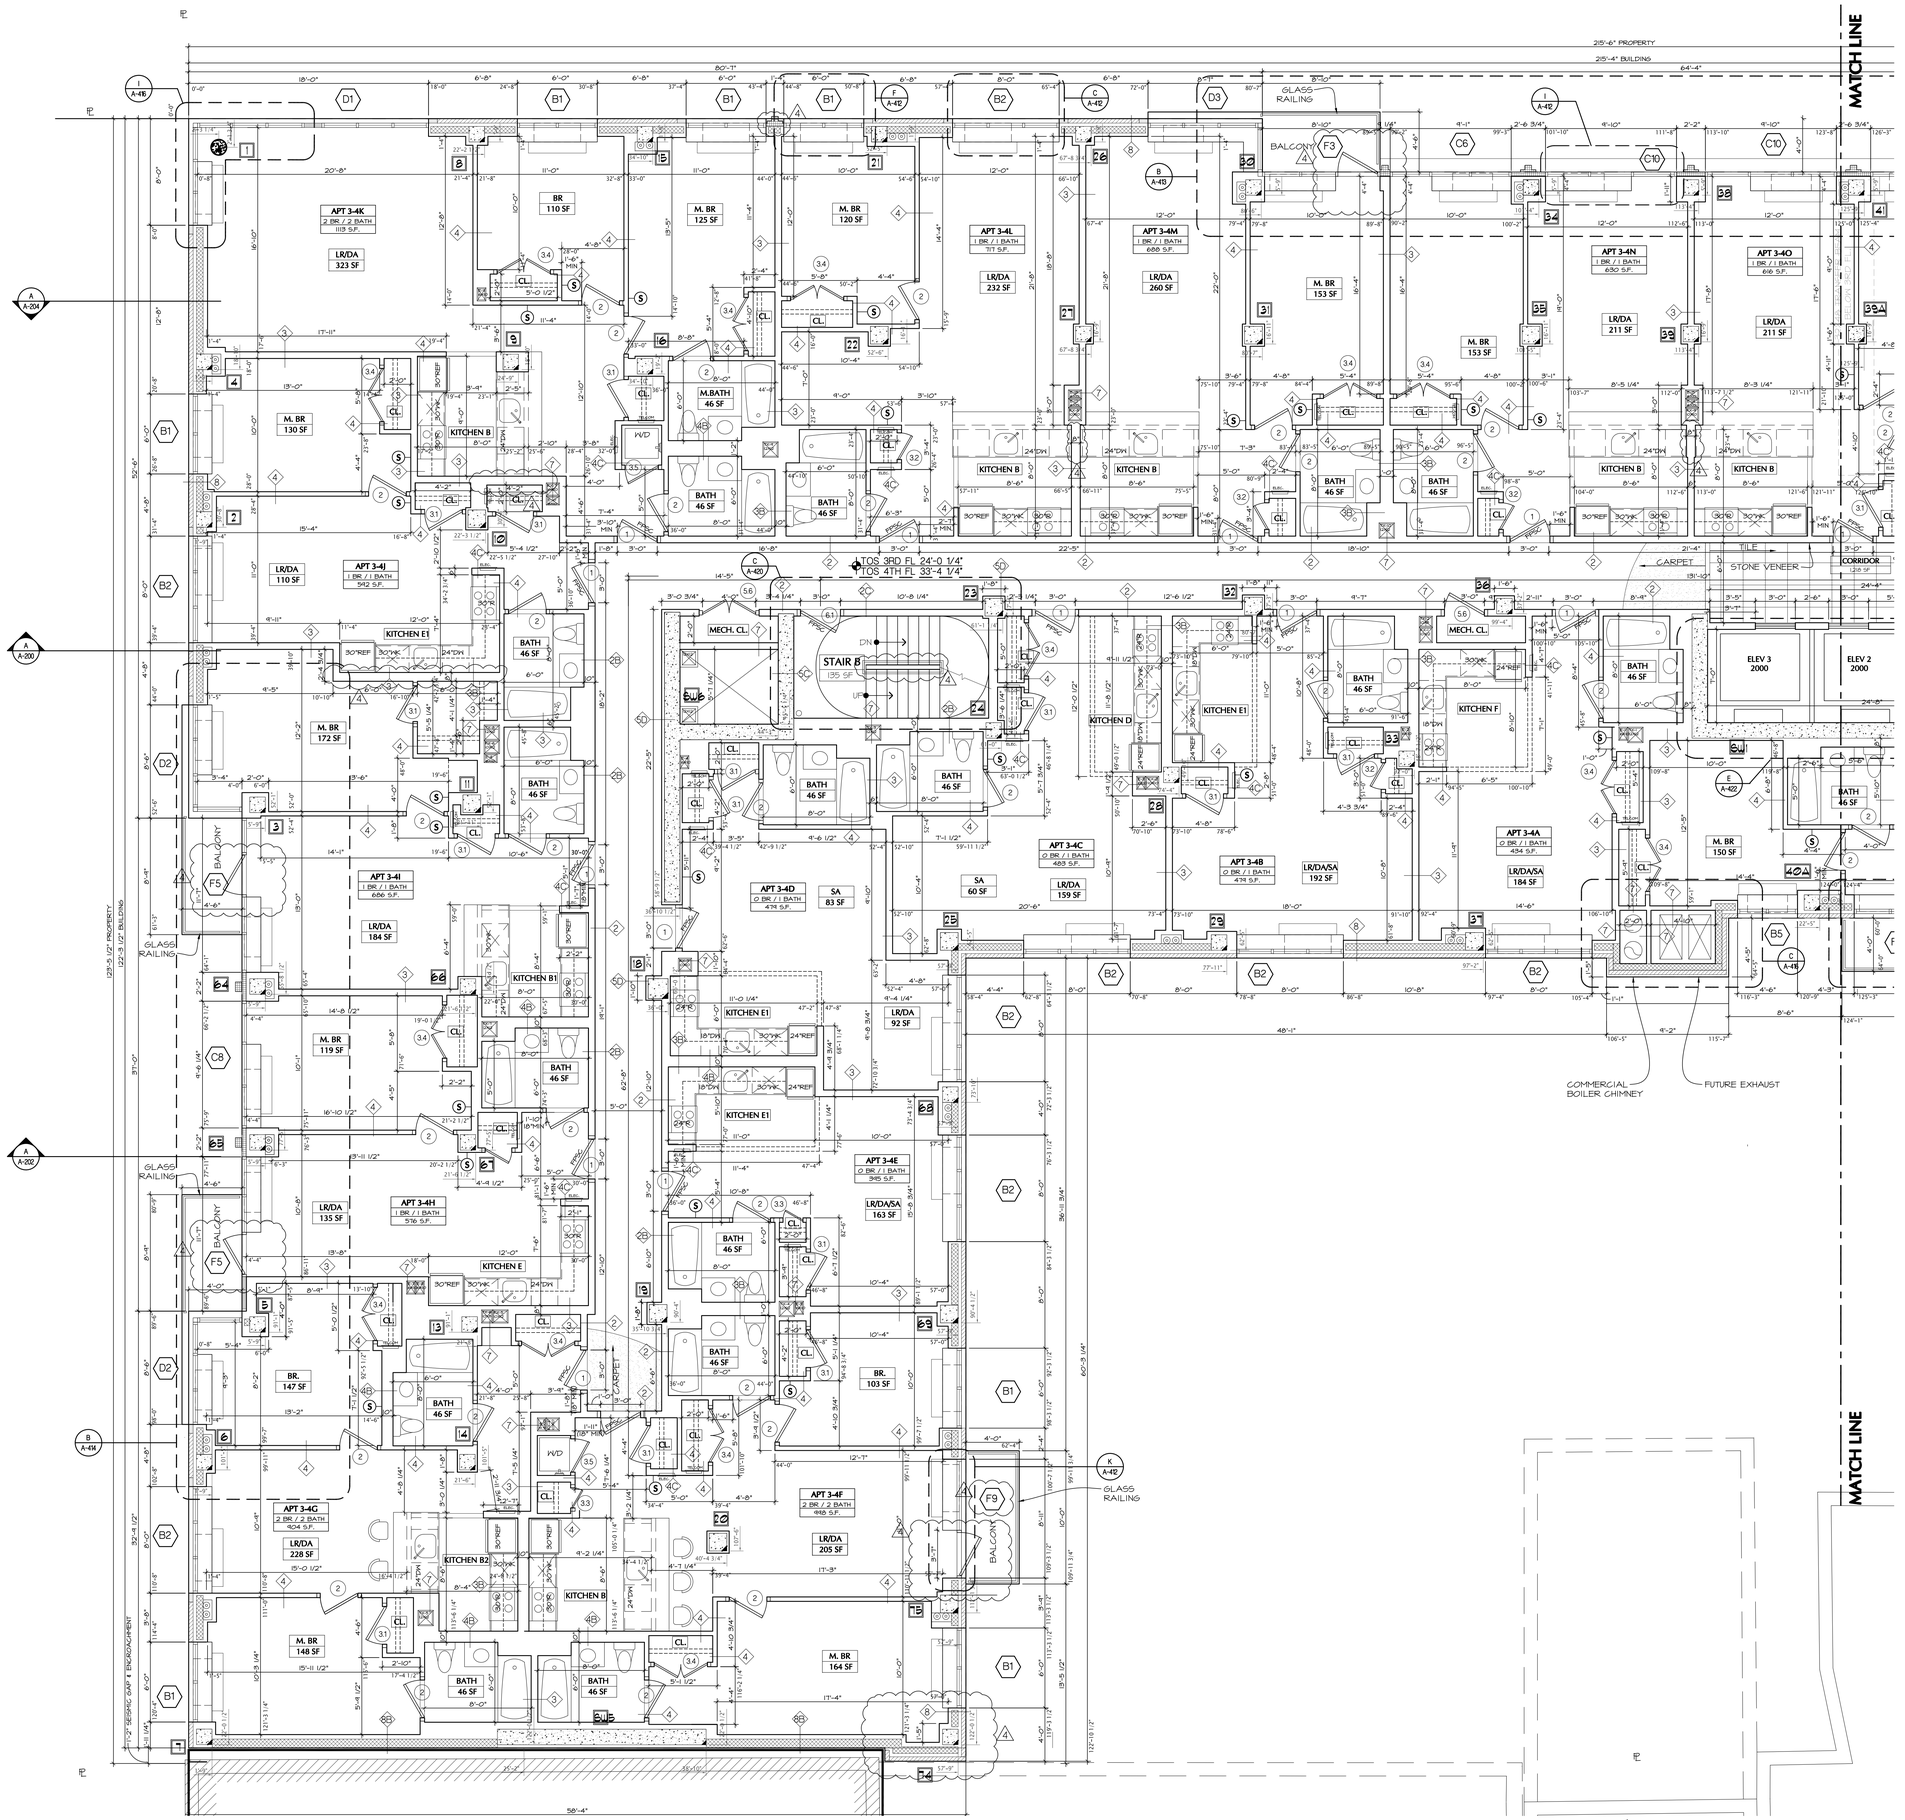

MATERIAL LEGEND
- BRICK
- CMU
- PRECAST
- SPANDREL
- METAL PANEL

GF55
PARTNERS
19 W. 21ST STREET
NEW YORK, N Y 10010
212 352 3099

©GF55 Partners, LLP 2012

260 WEST 26TH STREET
NEW YORK NY 10001

BLOCK: 775
LOT: 4, 69, 77, 78, 79, 80

DEVELOPER
ARTIMUS

STRUCTURAL ENGINEER
ENGINEERING GROUP

MECHANICAL ENGINEER
RODKIN CARDINALE ENGINEERS P.C.

OWNER
CHELSEA W26 LLC

ISSUE
DOB APPROVED SET AUGUST 5, 2011
100% FOUNDATION SET JULY 29, 2011
REVISION 1 SEPT 16, 2011
85% CONSTRUCTION SET SEPTEMBER 21, 2011
100% SUPER STRUCTURE SET SEPT 26, 2011
REVISION 2 NOV 2, 2011
REVISION 3 NOV 14, 2011
100% CONSTRUCTION SET DECEMBER 16, 2011
REVISION 4 FEB 3, 2012

SCALE
1/4"=1'-0"

PROJECT
260 WEST 26TH STREET

DRAWING
3RD - 4TH FLOOR PLAN

SEAL AND SIGNATURE

DATE: 02.03.2012
PROJECT NO: 1574.00
DRAWING BY: JD CC DR
CHK BY: MR
DWG NO:

A-104A

CADD FILE NO: 17 OF 100

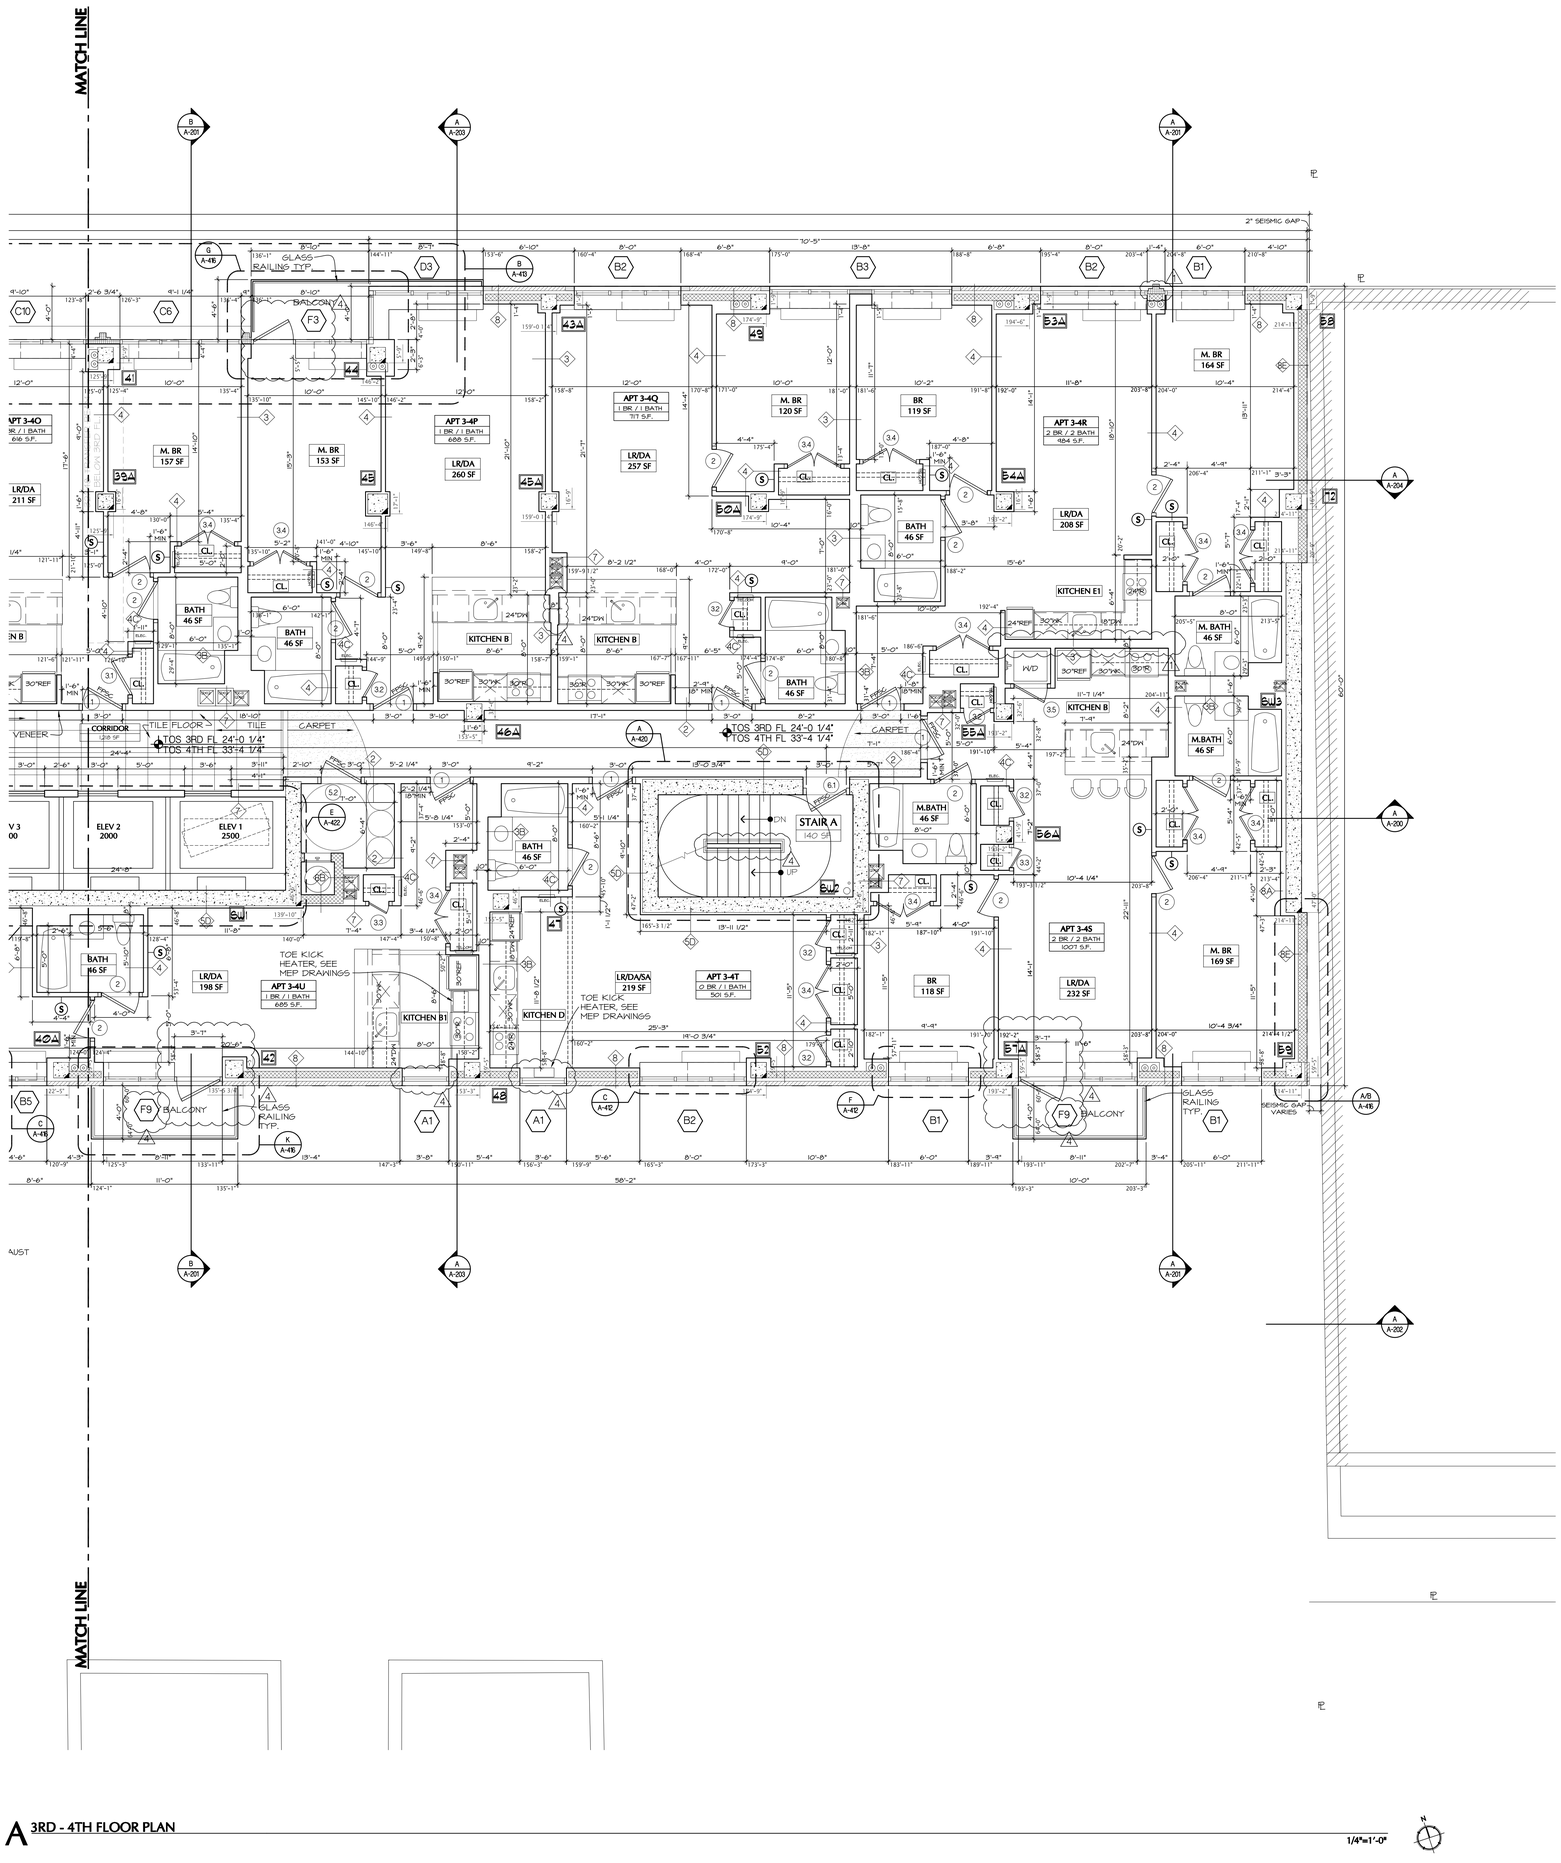

A 3RD - 4TH FLOOR PLAN

1/4"=1'-0"

MATERIAL LEGEND

- BRICK
- CMU
- PRECAST
- SPANDREL
- METAL PANEL

GF55 PARTNERS

19 W. 21ST STREET
NEW YORK, N Y 10010
212 352 3099

©GF55 Partners, LLP 2012

260 WEST 26TH STREET
NEW YORK NY 10001

BLOCK: 775
LOT: 4, 69, 77, 78, 79, 80

DEVELOPER
ARTIMUS

STRUCTURAL ENGINEER
ENGINEERING GROUP

MECHANICAL ENGINEER
RODKIN CARDINALE ENGINEERS P.C.

OWNER
CHELSEA W26 LLC

ISSUE

DOB APPROVED SET AUGUST 5, 2011
100% FOUNDATION SET JULY 29, 2011
REVISION 1 SEPT 16, 2011
85% CONSTRUCTION SET SEPTEMBER 21, 2011
100% SUPER STRUCTURE SET SEPT 26, 2011
REVISION 2 NOV 2, 2011
REVISION 3 NOV 14, 2011
100% CONSTRUCTION SET DECEMBER 16, 2011
REVISION 4 FEB 3, 2012

SCALE
1/4"=1'-0"

PROJECT
260 WEST 26TH STREET

DRAWING
3RD - 4TH FLOOR PLAN

SEAL AND SIGNATURE

DATE: 02.03.2012
PROJECT NO: 1574.00
DRAWING BY: JD CC DR
CHK BY: MR
DWG NO:

A-104B

CADD FILE NO: 18 OF 100

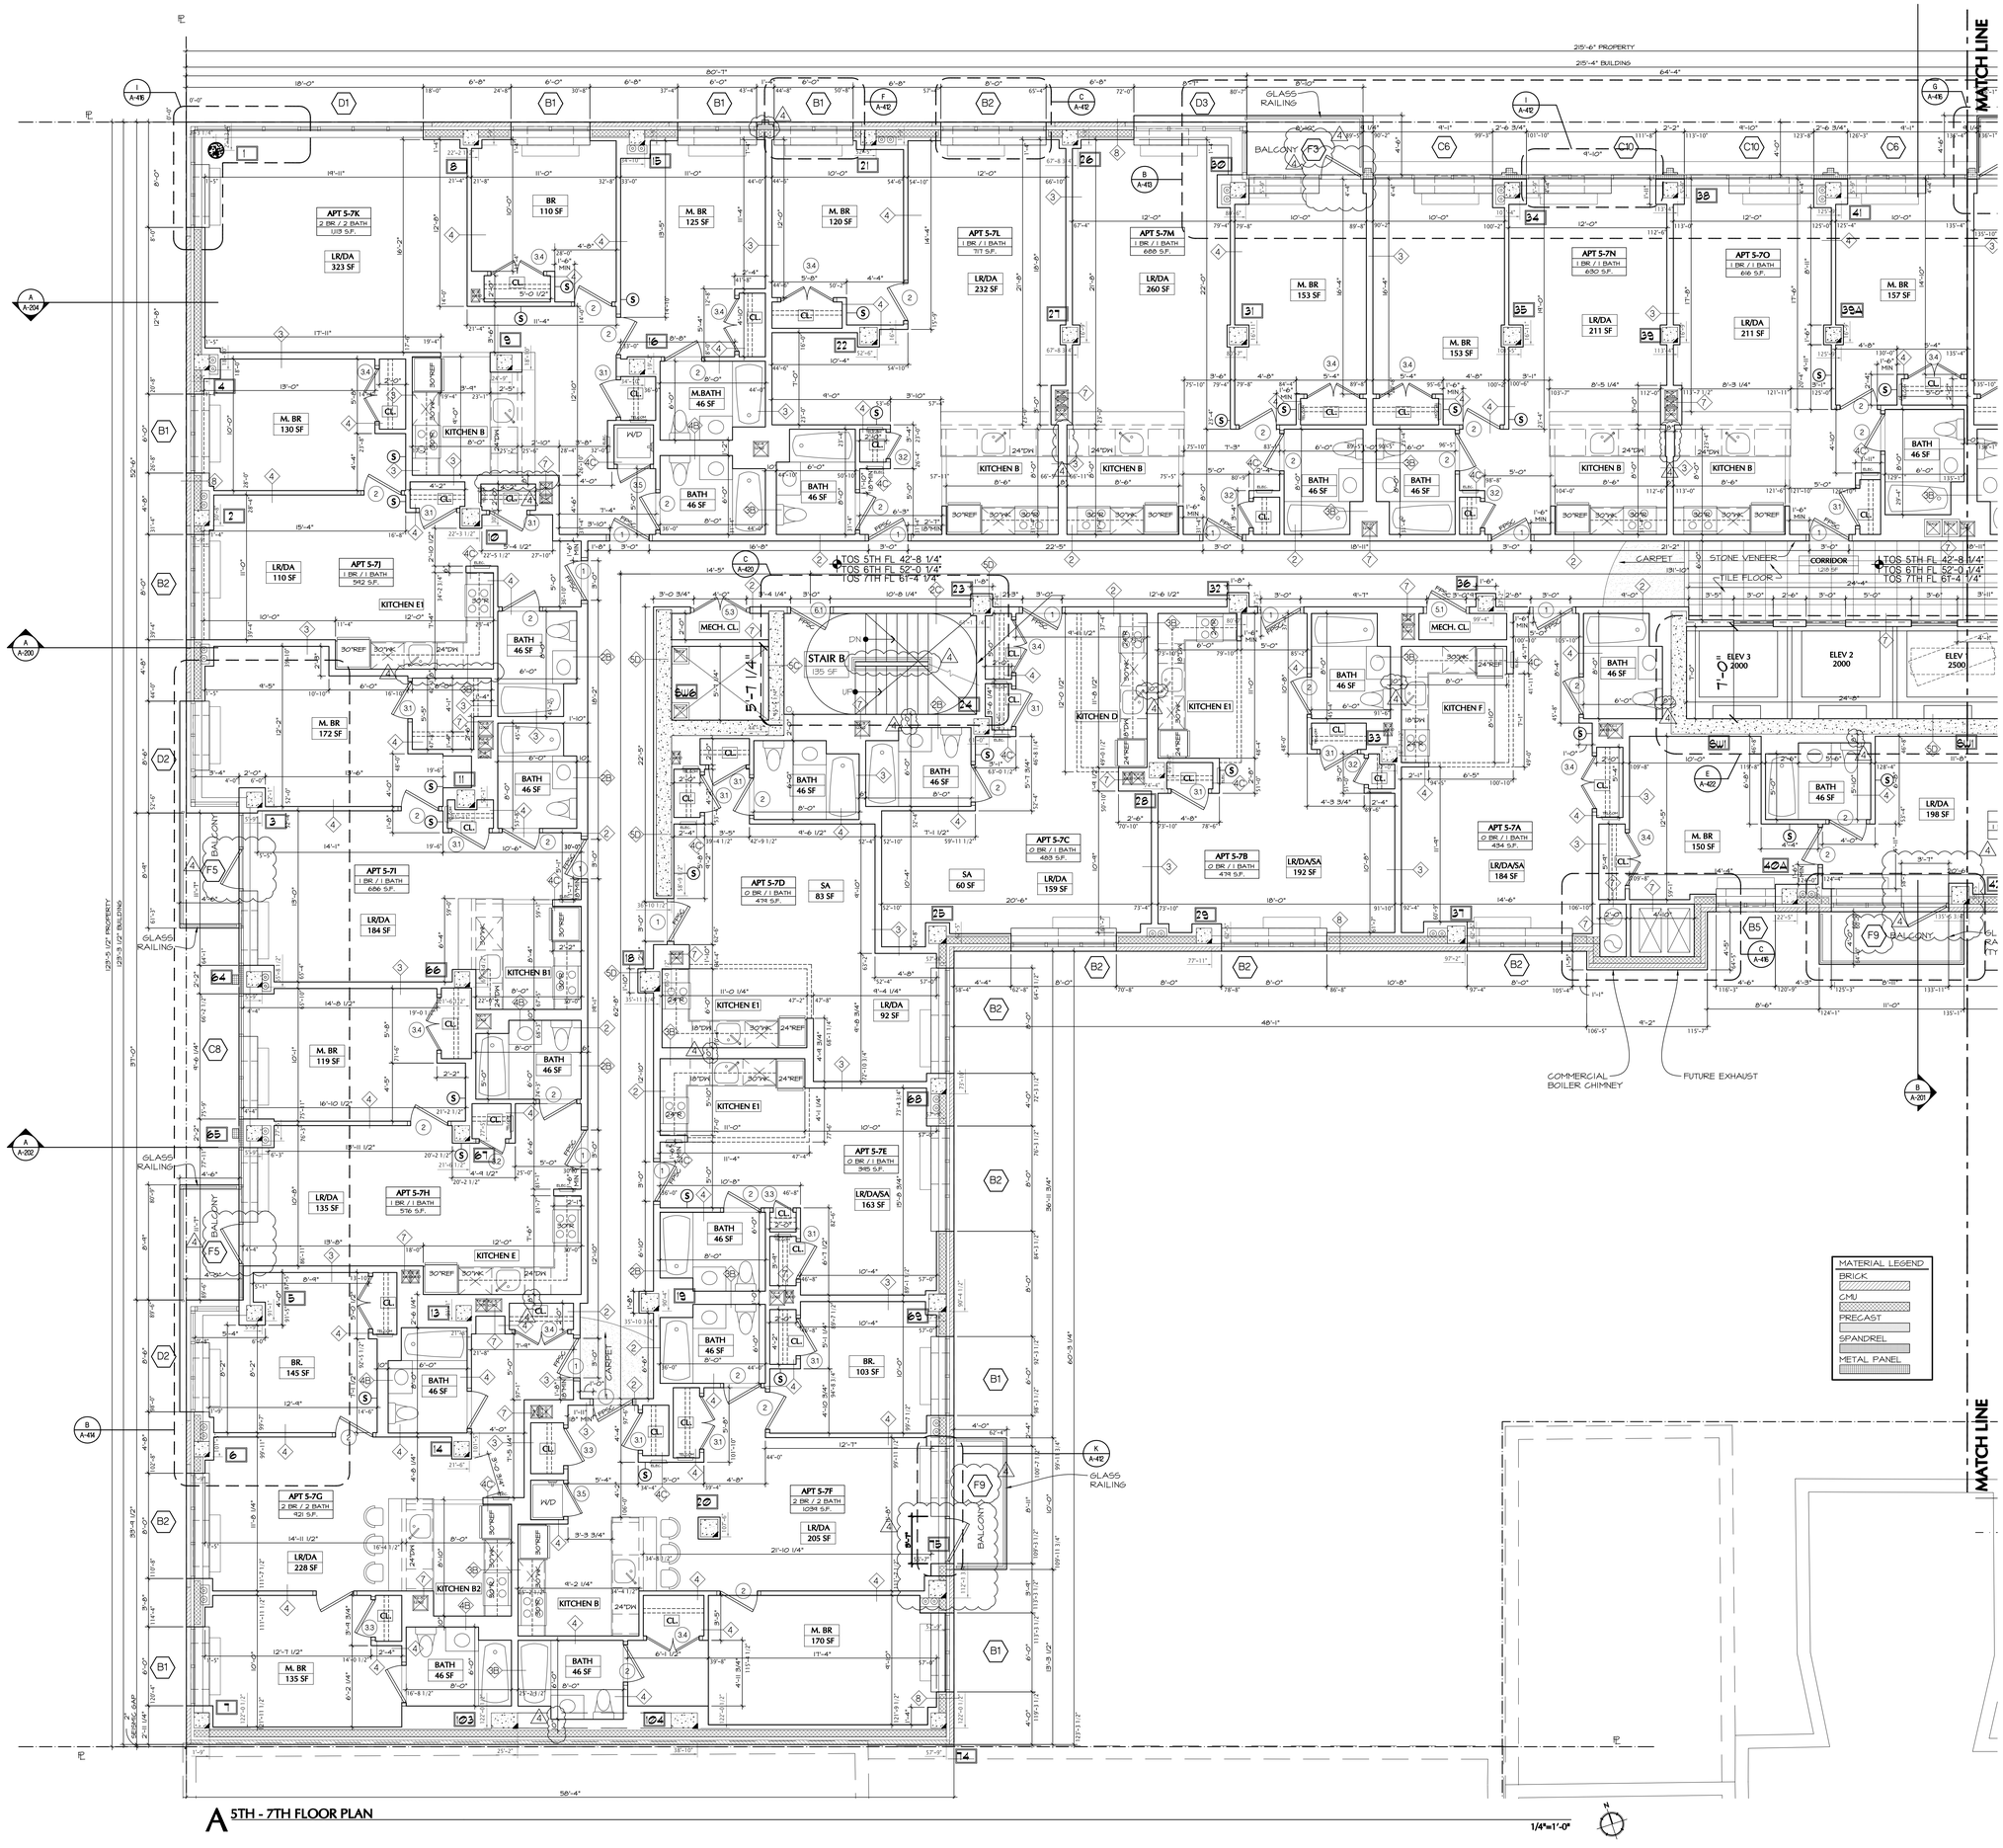

GF55
PARTNERS
19 W. 21ST STREET
NEW YORK, N Y 10010
212 352 3099
©GF55 Partners, LLP 2012

260 WEST 26TH STREET NEW YORK NY 10001

BLOCK: 775
LOT: 4, 69, 77, 78, 79, 80

DEVELOPER
ARTIMUS

STRUCTURAL ENGINEER
ENGINEERING GROUP

MECHANICAL ENGINEER
RODKIN CARDINALE ENGINEERS P.C.

OWNER
CHELSEA W26 LLC

ISSUE
DOB APPROVED SET AUGUST 5, 2011
100% FOUNDATION SET JULY 29, 2011
REVISION 1 SEPT 16, 2011
85% CONSTRUCTION SET SEPTEMBER 21, 2011
100% SUPER STRUCTURE SET SEPT 26, 2011
REVISION 2 NOV 2, 2011
REVISION 3 NOV 14, 2011
100% CONSTRUCTION SET DECEMBER 16, 2011
REVISION 4 FEB 3, 2012

SCALE
1/4"=1'-0"

PROJECT
260 WEST 26TH STREET

DRAWING
5TH - 7TH FLOOR PLAN

SEAL AND SIGNATURE

DATE: 02.03.2012
PROJECT NO: 1574.00
DRAWING BY: JD CC DR
CHK BY: MR
DWG NO:

A-105A

CADD FILE NO: 19 OF 100

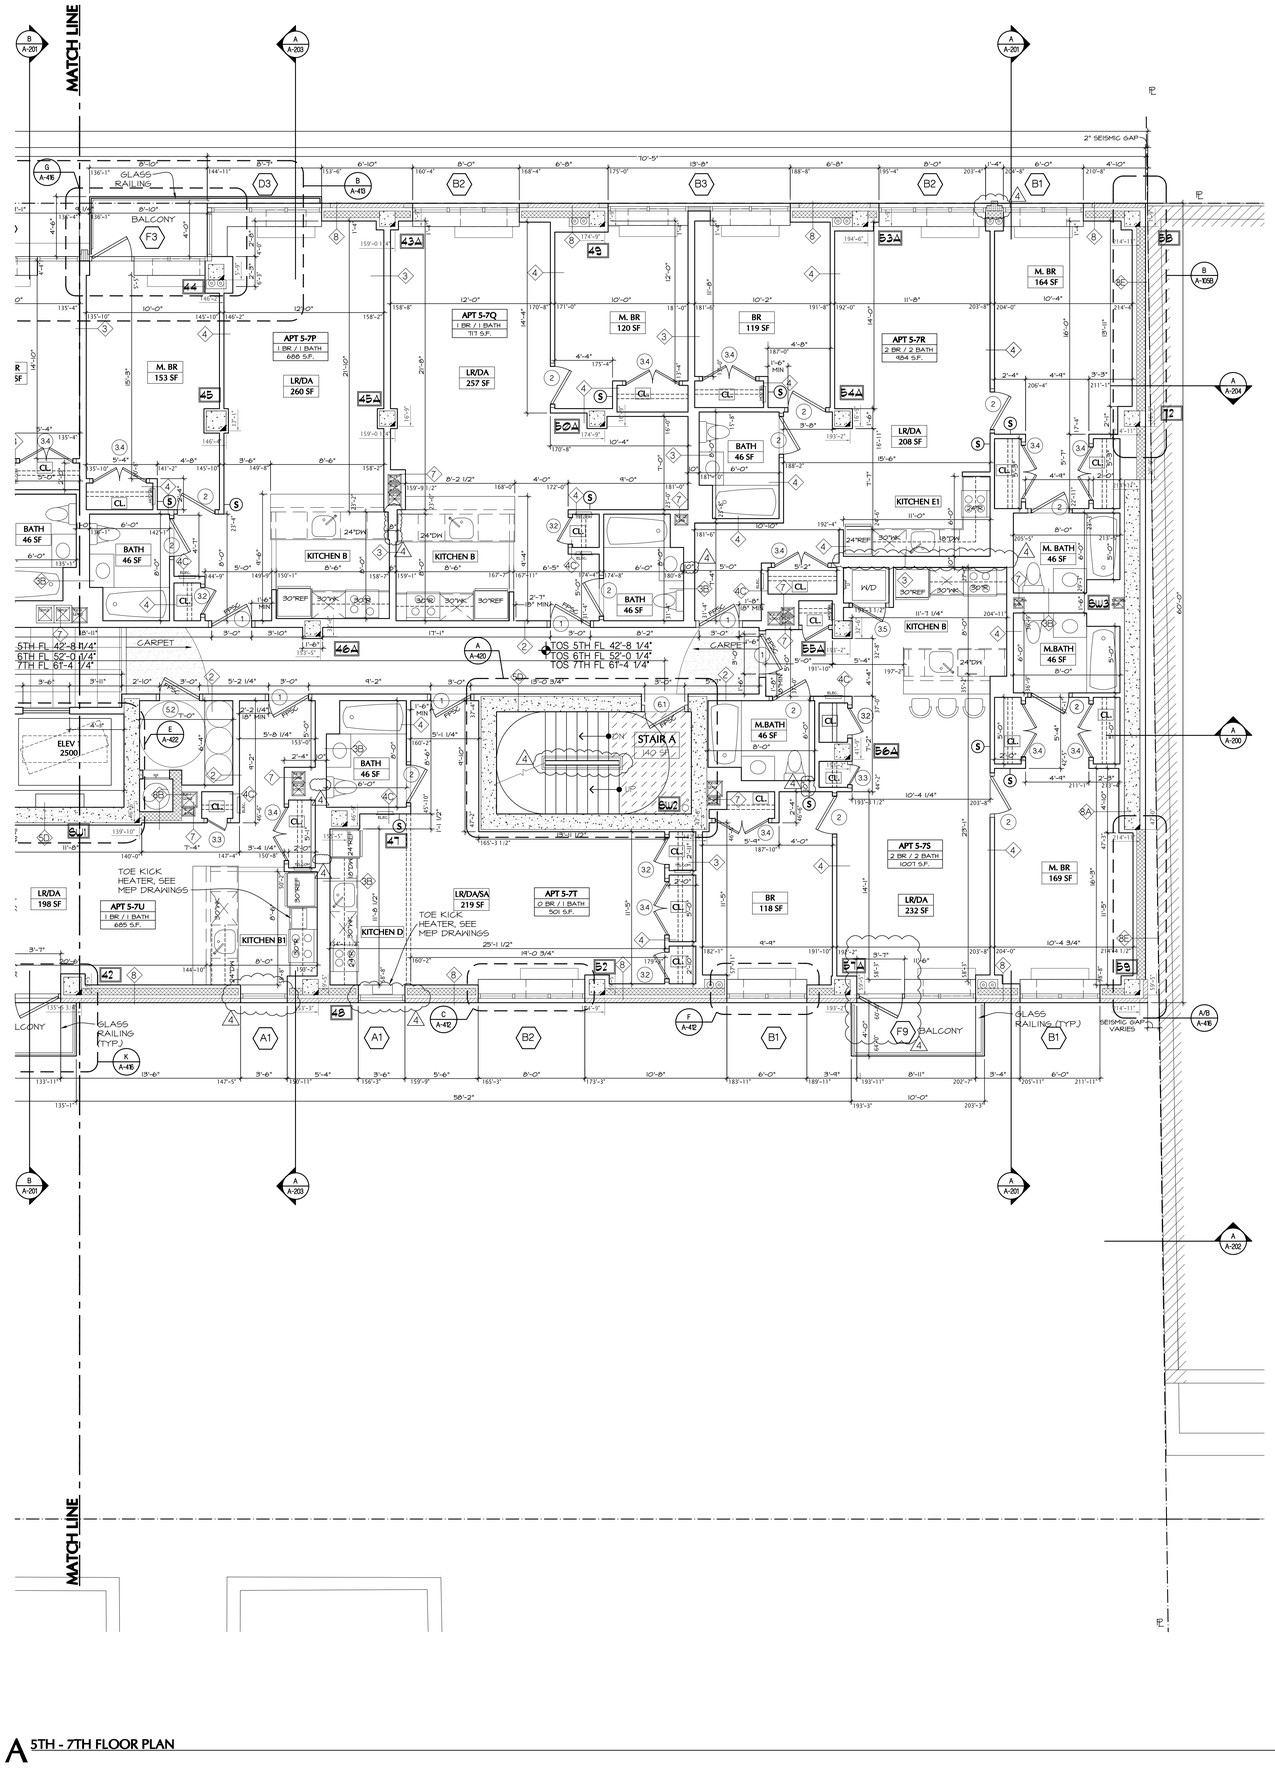

A 5TH - 7TH FLOOR PLAN

1/4"=1'-0"

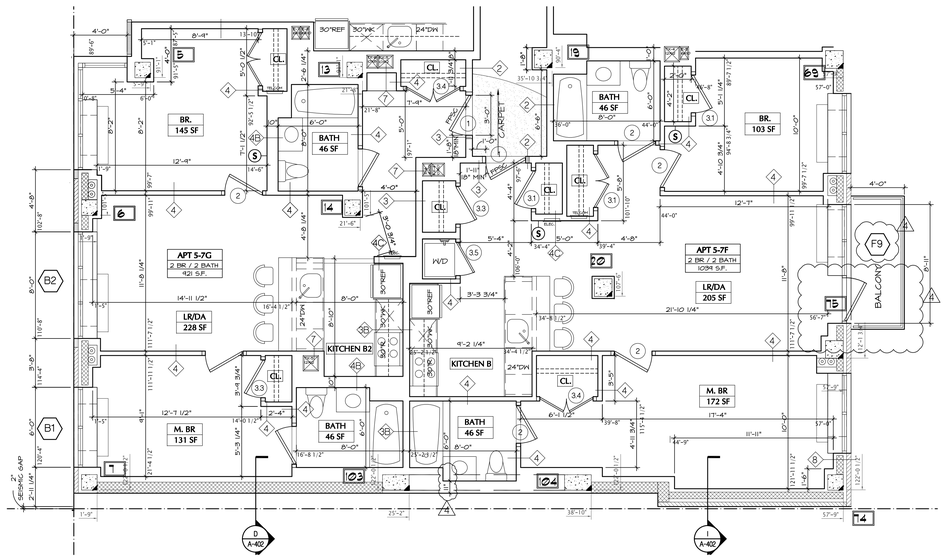

B 5TH FLOOR PLAN

1/4"=1'-0"

MATERIAL LEGEND

- BRICK
- CMU
- PRECAST
- SPANDREL
- METAL PANEL

GF55
PARTNERS
19 W. 21ST STREET
NEW YORK, N Y 10010
212 352 3099
©GF55 Partners, LLP 2012

260 WEST 26TH STREET
NEW YORK NY 10001

BLOCK: 775
LOT: 4, 69, 77, 78, 79, 80

DEVELOPER
ARTIMUS

STRUCTURAL ENGINEER
ENGINEERING GROUP

MECHANICAL ENGINEER
RODKIN CARDINALE ENGINEERS P.C.

OWNER
CHELSEA W26 LLC

ISSUE

DOB APPROVED SET AUGUST 5, 2011
100% FOUNDATION SET JULY 29, 2011
REVISION 1 SEPT 16, 2011
85% CONSTRUCTION SET SEPTEMBER 21, 2011
100% SUPER STRUCTURE SET SEPT 26, 2011
REVISION 2 NOV 2, 2011
REVISION 3 NOV 14, 2011
100% CONSTRUCTION SET DECEMBER 16, 2011
REVISION 4 FEB 3, 2012

SCALE
1/4"=1'-0"

PROJECT
260 WEST 26TH STREET

DRAWING
5TH - 7TH FLOOR PLAN

SEAL AND SIGNATURE

DATE: 02.03.2012
PROJECT NO: 1574.00
DRAWING BY: JD CC DR
CHK BY: MR
DWG NO:

A-105B

CADD FILE NO: 20 OF 100

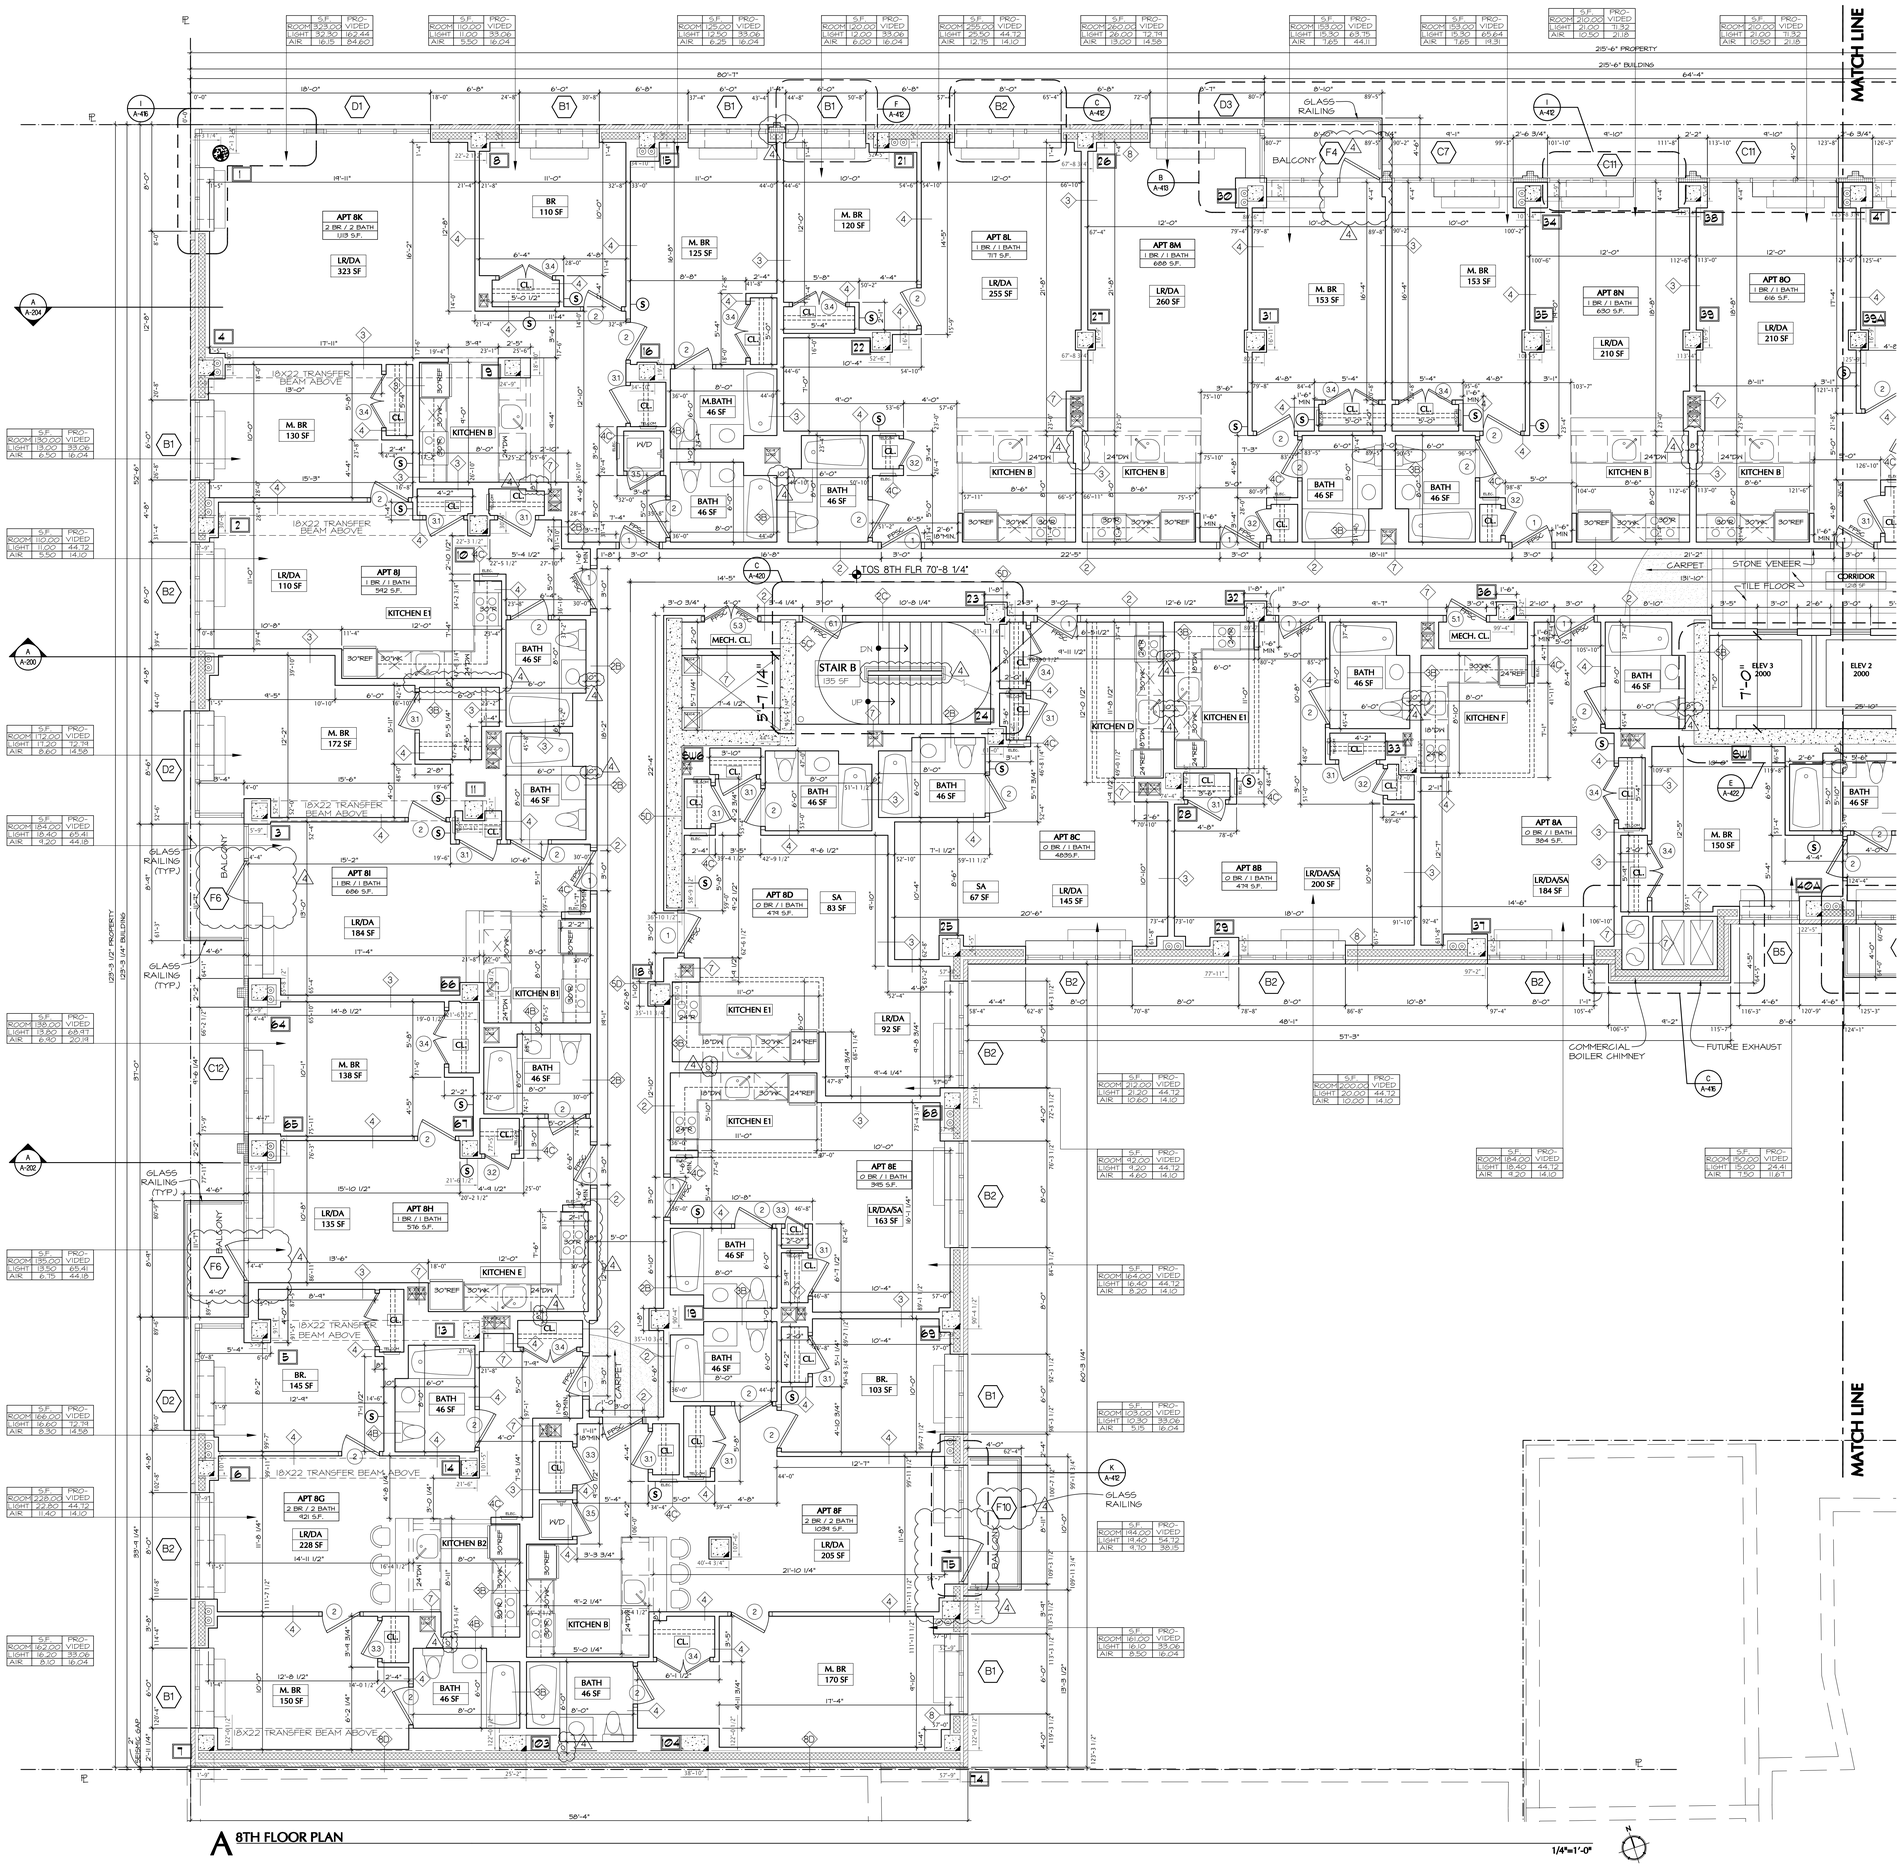

A 8TH FLOOR PLAN

1/4"=1'-0"

GF55
PARTNERS
19 W. 21ST STREET
NEW YORK, N Y 10010
212 352 3099
©GF55 Partners, LLP 2012

260 WEST 26TH STREET
NEW YORK NY 10001

BLOCK: 775
LOT: 4, 69, 77, 78, 79, 80

DEVELOPER
ARTIMUS

STRUCTURAL ENGINEER
ENGINEERING GROUP

MECHANICAL ENGINEER
RODKIN CARDINALE ENGINEERS P.C.

OWNER
CHELSEA W26 LLC

ISSUE
DOB APPROVED SET AUGUST 5, 2011
100% FOUNDATION SET JULY 29, 2011
REVISION 1 SEPT 16, 2011
85% CONSTRUCTION SET SEPTEMBER 21, 2011
100% SUPER STRUCTURE SET SEPT 26, 2011
REVISION 2 NOV 2, 2011
REVISION 3 NOV 14, 2011
100% CONSTRUCTION SET DECEMBER 16, 2011
REVISION 4 FEB 3, 2012

SCALE
1/4"=1'-0"

PROJECT
260 WEST 26TH STREET

DRAWING
8TH FLOOR PLAN

SEAL AND SIGNATURE

DATE: 02.03.2012
PROJECT NO: 1574.00
DRAWING BY: JD CC DR
CHK BY: MR
DWG NO:
A-106A
CADD FILE NO: 21 OF 100

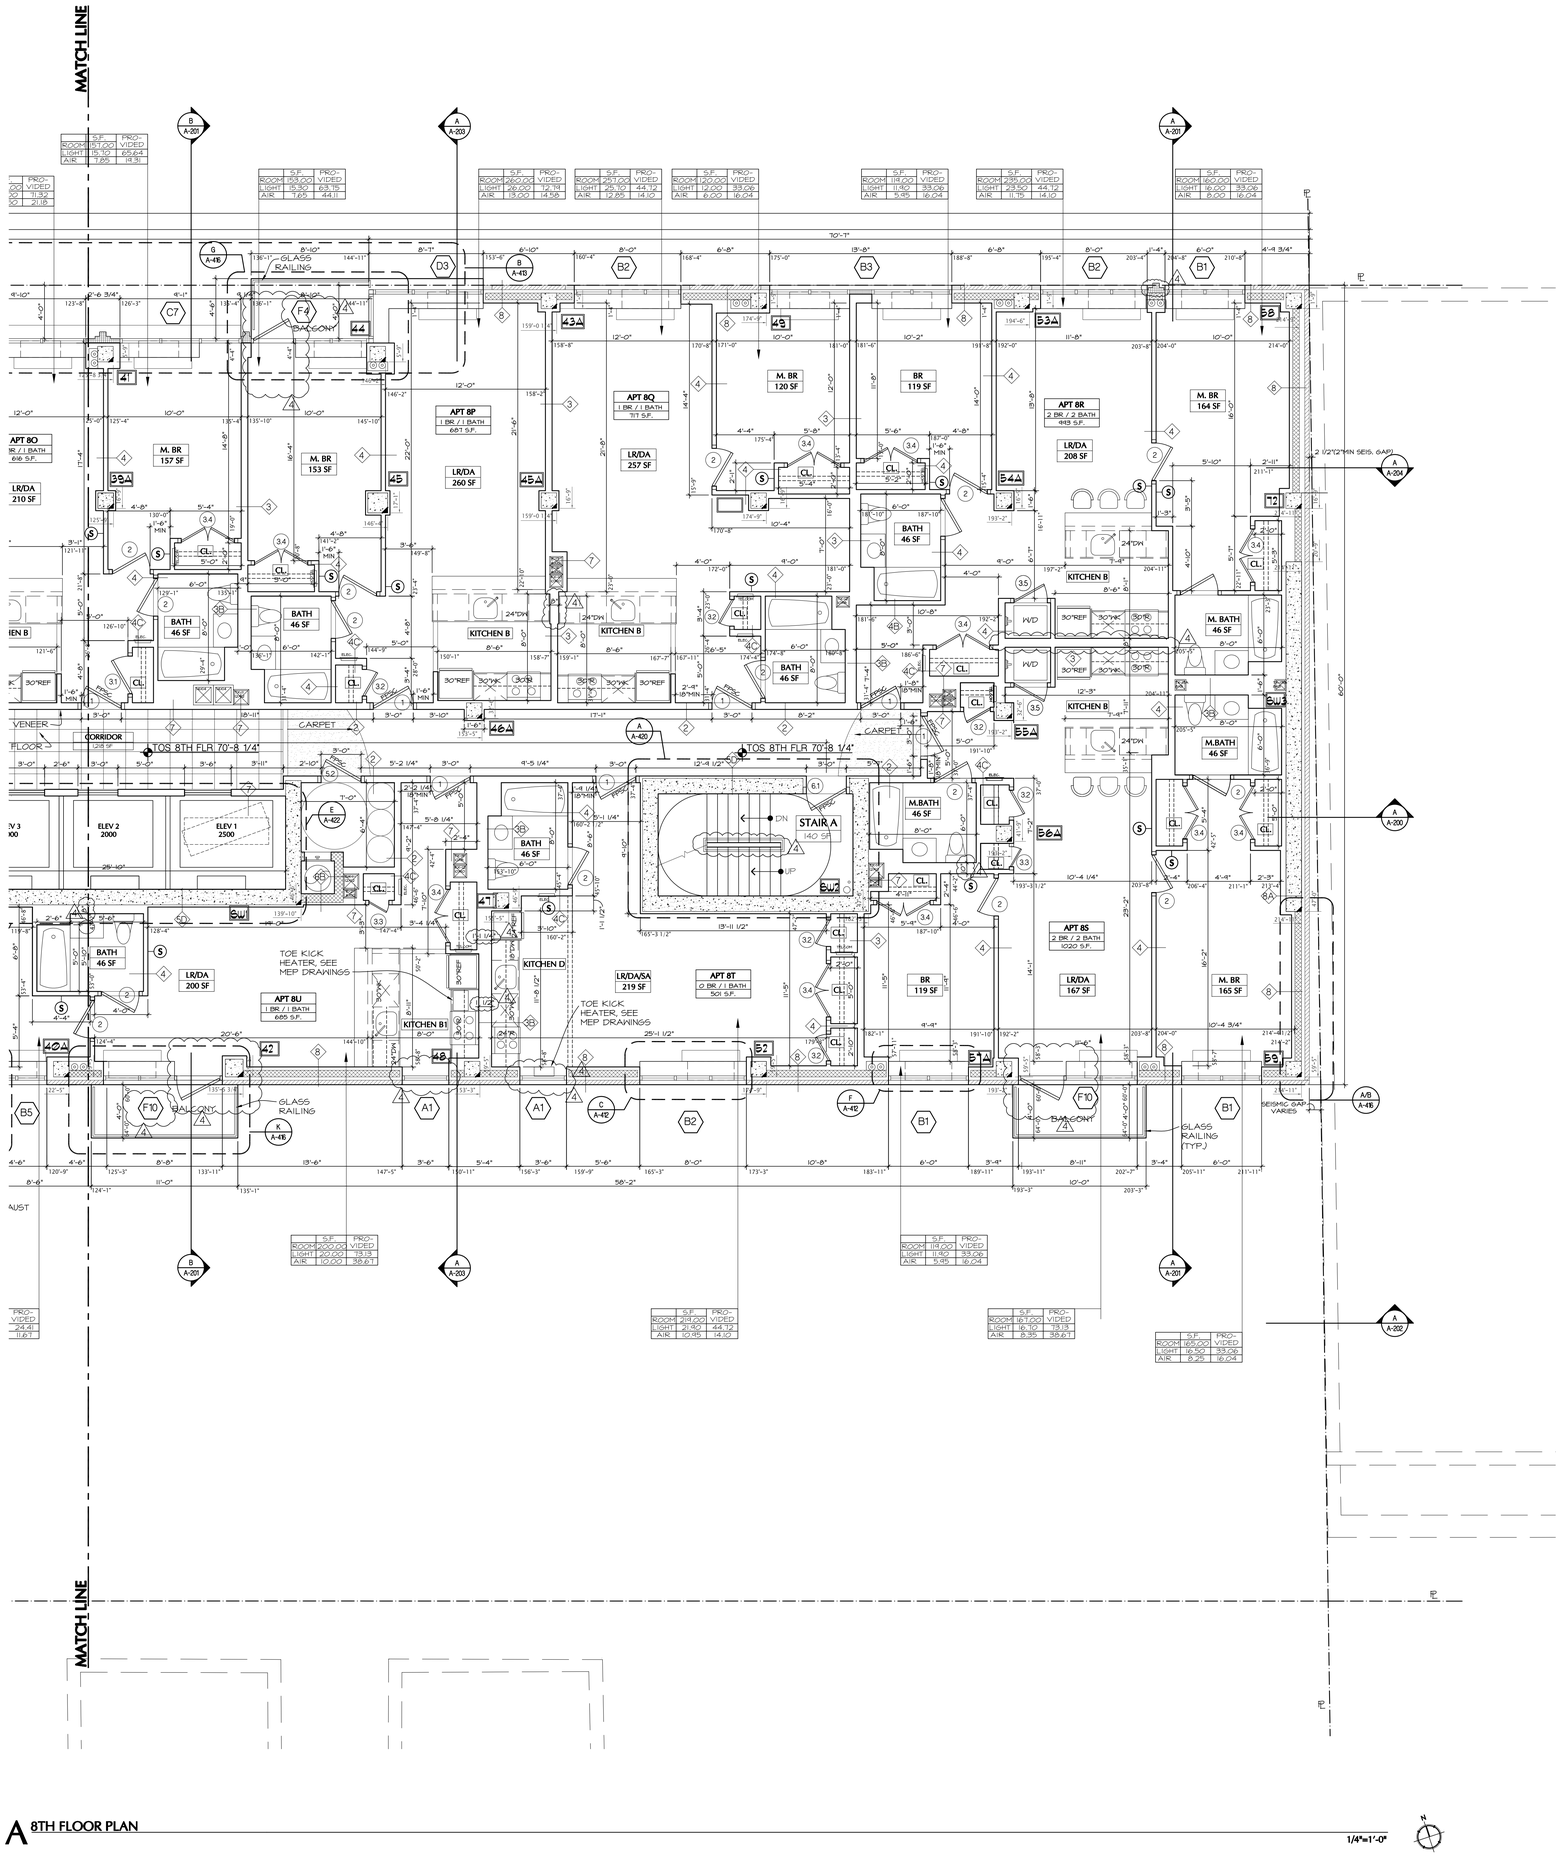

A 8TH FLOOR PLAN

1/4"=1'-0"

MATERIAL LEGEND

- BRICK
- CMU
- PRECAST
- SPANDREL
- METAL PANEL

GF55
PARTNERS
19 W. 21ST STREET
NEW YORK, N Y 10010
212 352 3099
©GF55 Partners, LLP 2012

260 WEST 26TH STREET NEW YORK NY 10001

BLOCK: 775
LOT: 4, 69, 77, 78, 79, 80

DEVELOPER
ARTIMUS

STRUCTURAL ENGINEER
ENGINEERING GROUP

MECHANICAL ENGINEER
RODKIN CARDINALE ENGINEERS P.C.

OWNER
CHELSEA W26 LLC

ISSUE
DOB APPROVED SET AUGUST 5, 2011
100% FOUNDATION SET JULY 29, 2011
REVISION 1 SEPT 16, 2011
85% CONSTRUCTION SET SEPTEMBER 21, 2011
100% SUPER STRUCTURE SET SEPT 26, 2011
REVISION 2 NOV 2, 2011
REVISION 3 NOV 14, 2011
100% CONSTRUCTION SET DECEMBER 16, 2011
REVISION 4 FEB 3, 2012

SCALE
1/4"=1'-0"

PROJECT
260 WEST 26TH STREET

DRAWING
8TH FLOOR PLAN

SEAL AND SIGNATURE

DATE: 02.03.2012
PROJECT NO: 1574.00
DRAWING BY: JD CC DR
CHK BY: MR
DWG NO:

A-106B

CADD FILE NO: 22 OF 100

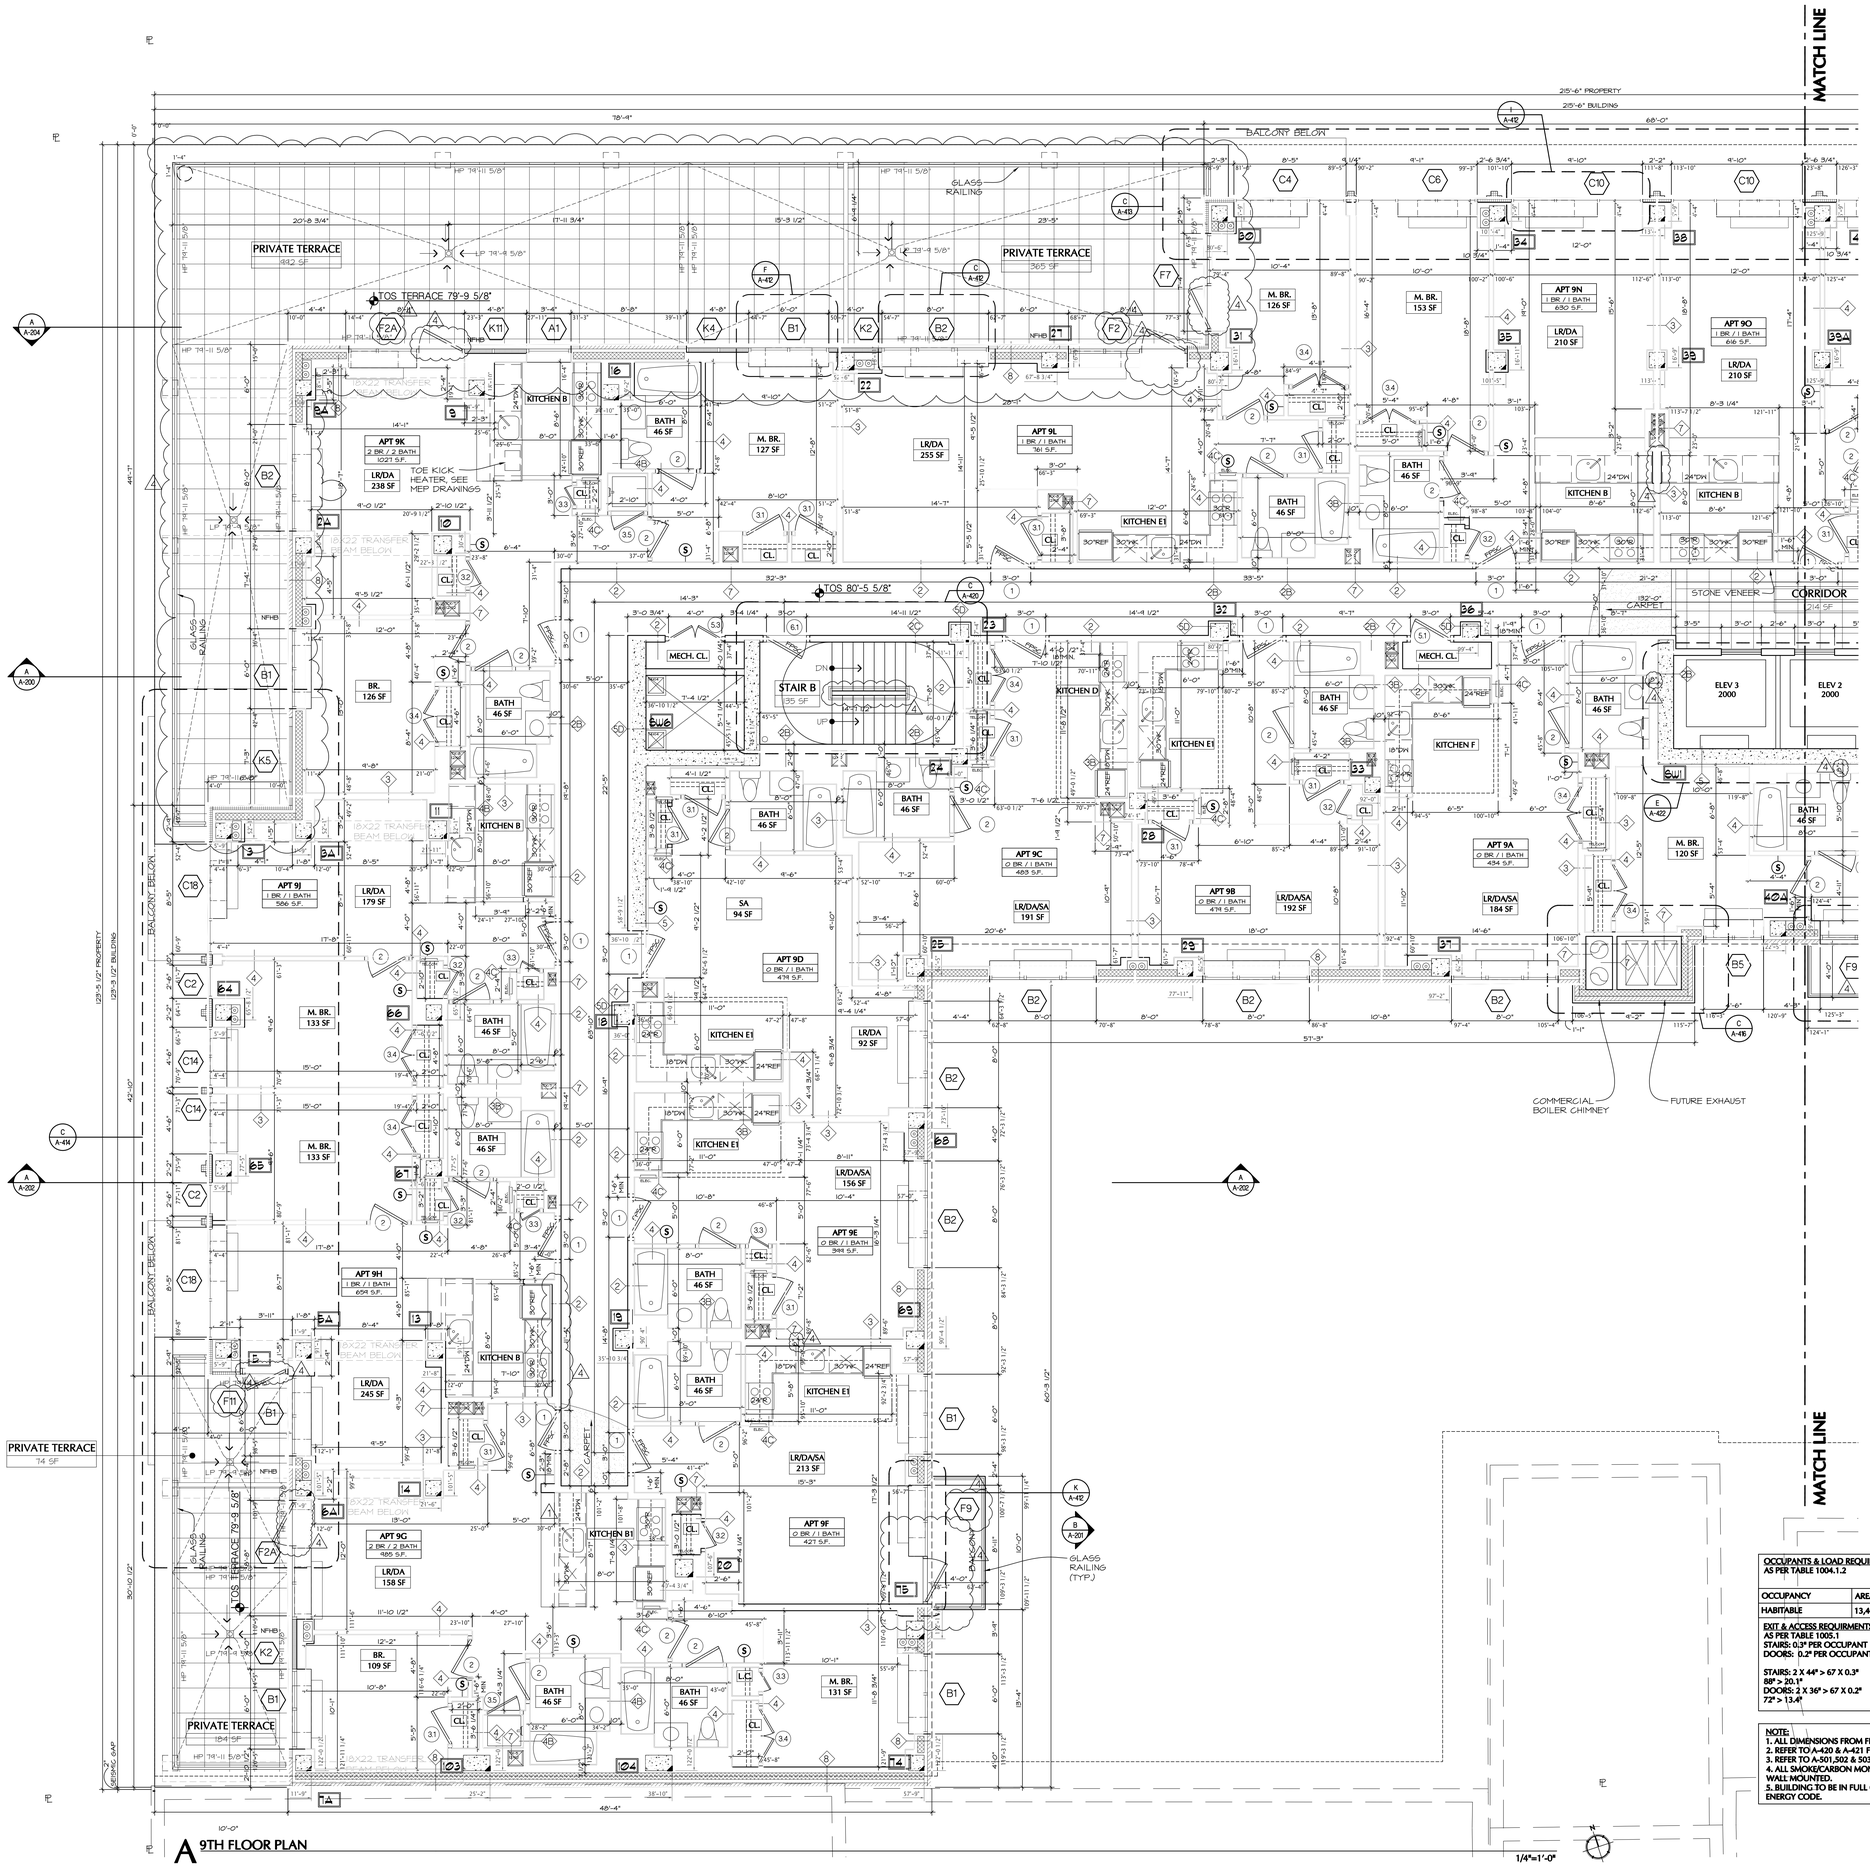

A 9TH FLOOR PLAN

1/4"=1'-0"

MATERIAL LEGEND
BRICK
CMU
PRECAST
SPANDREL
METAL PANEL

OCCUPANTS & LOAD REQUIRMENTS:
AS PER TABLE 1004.1.2

OCCUPANCY	AREA / OCCUPANT	# OF OCCUPANTS
HABITABLE	13,405.95 / 200	67

EXIT & ACCESS REQUIRMENTS:
AS PER TABLE 1005.1
STAIRS: 0.3" PER OCCUPANT
DOORS: 0.2" PER OCCUPANT

STAIRS: 2 X 44" > 67 X 0.3"
88" > 20.1"
DOORS: 2 X 36" > 67 X 0.2"
72" > 13.4"

NOTE:
1. ALL DIMENSIONS FROM FINISH TO FINISH.
2. REFER TO A-420 & A-421 FOR STAIR DIMENSIONS.
3. REFER TO A-501,502 & 503 FOR KITCHEN & BATH LAYOUTS.
4. ALL SMOKE/CARBON MONOXIDE DETECTORS TO BE WALL MOUNTED.
5. BUILDING TO BE IN FULL COMPLIANCE WITH NYS ENERGY CODE.

GF55
PARTNERS
19 W. 21ST STREET
NEW YORK, N Y 10010
212 352 3099

©GF55 Partners, LLP 2012

260 WEST 26TH STREET
NEW YORK NY 10001

BLOCK: 775
LOT: 4, 69, 77, 78, 79, 80

DEVELOPER
ARTIMUS

STRUCTURAL ENGINEER
ENGINEERING GROUP

MECHANICAL ENGINEER
RODKIN CARDINALE ENGINEERS P.C.

OWNER
CHELSEA W26 LLC

ISSUE
DOB APPROVED SET AUGUST 5, 2011
100% FOUNDATION SET JULY 29, 2011
REVISION 1 SEPT 16, 2011
85% CONSTRUCTION SET SEPTEMBER 21, 2011
100% SUPER STRUCTURE SET SEPT 26, 2011
REVISION 2 NOV 2, 2011
REVISION 3 NOV 14, 2011
100% CONSTRUCTION SET DECEMBER 16, 2011
REVISION 4 FEB 3, 2012

SCALE
1/4"=1'-0"

PROJECT
260 WEST 26TH STREET

DRAWING
9TH FLOOR PLAN

SEAL AND SIGNATURE

DATE: 02.03.2012
PROJECT NO: 1374.00
DRAWING BY: JD CC DR
CHK BY: MR
DWG NO:
A-107A
CADD FILE NO: 23 OF 100

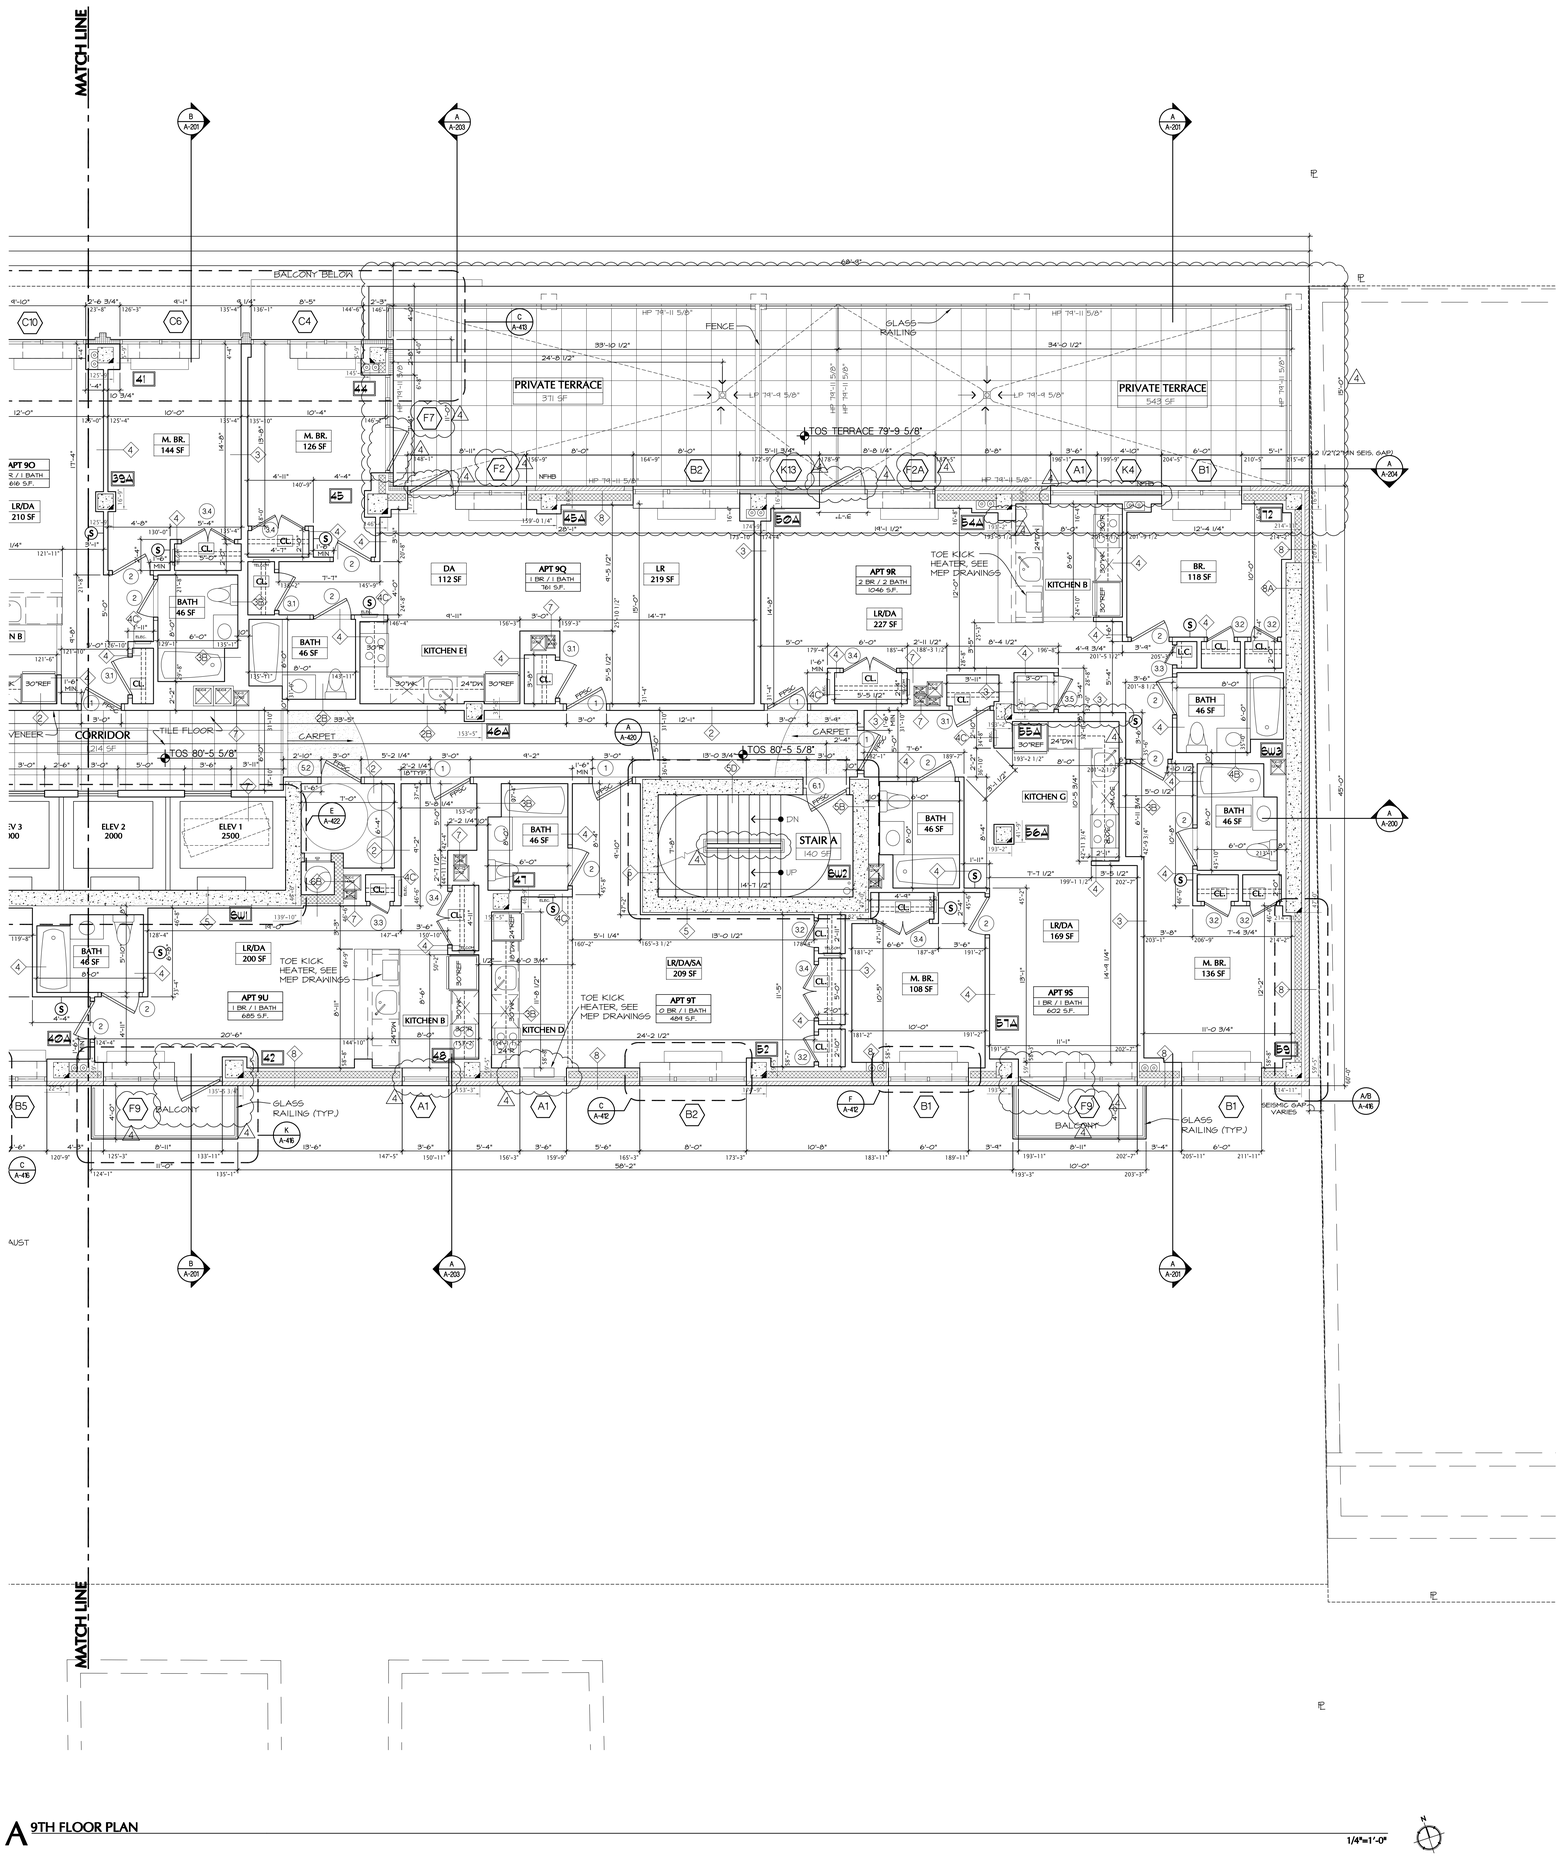

A 9TH FLOOR PLAN

1/4"=1'-0"

MATERIAL LEGEND
- BRICK
- CMU
- PREGAST
- SPANDREL
- METAL PANEL

OCCUPANTS & LOAD REQUIRMENTS:
AS PER TABLE 1004.1.2

OCCUPANCY	AREA / OCCUPANT	# OF OCCUPANTS
HABITABLE	13,405.95 / 200	67

EXIT & ACCESS REQUIRMENTS:
AS PER TABLE 1005.1
STAIRS: 0.3" PER OCCUPANT
DOORS: 0.2" PER OCCUPANT

STAIRS: 2 X 44" > 67 X 0.3"
88" > 20.1"
DOORS: 2 X 36" > 67 X 0.2"
72" > 13.4"

NOTE:
1. ALL DIMENSIONS FROM FINISH TO FINISH.
2. REFER TO A-420 & A-421 FOR STAIR DIMENSIONS.
3. REFER TO A-501,502 & 503 FOR KITCHEN & BATH LAYOUTS.
4. ALL SMOKE/CARBON MONOXIDE DETECTORS TO BE WALL MOUNTED.
5. BUILDING TO BE IN FULL COMPLIANCE WITH NYS ENERGY CODE.

GF55
PARTNERS
19 W. 21ST STREET
NEW YORK, N Y 10010
212 352 3099
©GF55 Partners, LLP 2012

260 WEST 26TH STREET
NEW YORK NY 10001

BLOCK: 775
LOT: 4, 69, 77, 78, 79, 80

DEVELOPER
ARTIMUS

STRUCTURAL ENGINEER
ENGINEERING GROUP

MECHANICAL ENGINEER
RODKIN CARDINALE ENGINEERS P.C.

OWNER
CHELSEA W26 LLC

ISSUE
DOB APPROVED SET AUGUST 5, 2011
100% FOUNDATION SET JULY 29, 2011
REVISION 1 SEPT 16, 2011
85% CONSTRUCTION SET SEPTEMBER 21, 2011
100% SUPER STRUCTURE SET SEPT 26, 2011
REVISION 2 NOV 2, 2011
REVISION 3 NOV 14, 2011
100% CONSTRUCTION SET DECEMBER 16, 2011
REVISION 4 FEB 3, 2012

SCALE
1/4"=1'-0"

PROJECT
260 WEST 26TH STREET

DRAWING
9TH FLOOR PLAN

SEAL AND SIGNATURE

DATE: 02.03.2012
PROJECT NO: 1574.00
DRAWING BY: JD CC DR
CHK BY: MR
DWG NO:
A-107B
CADD FILE NO: 24 OF 100

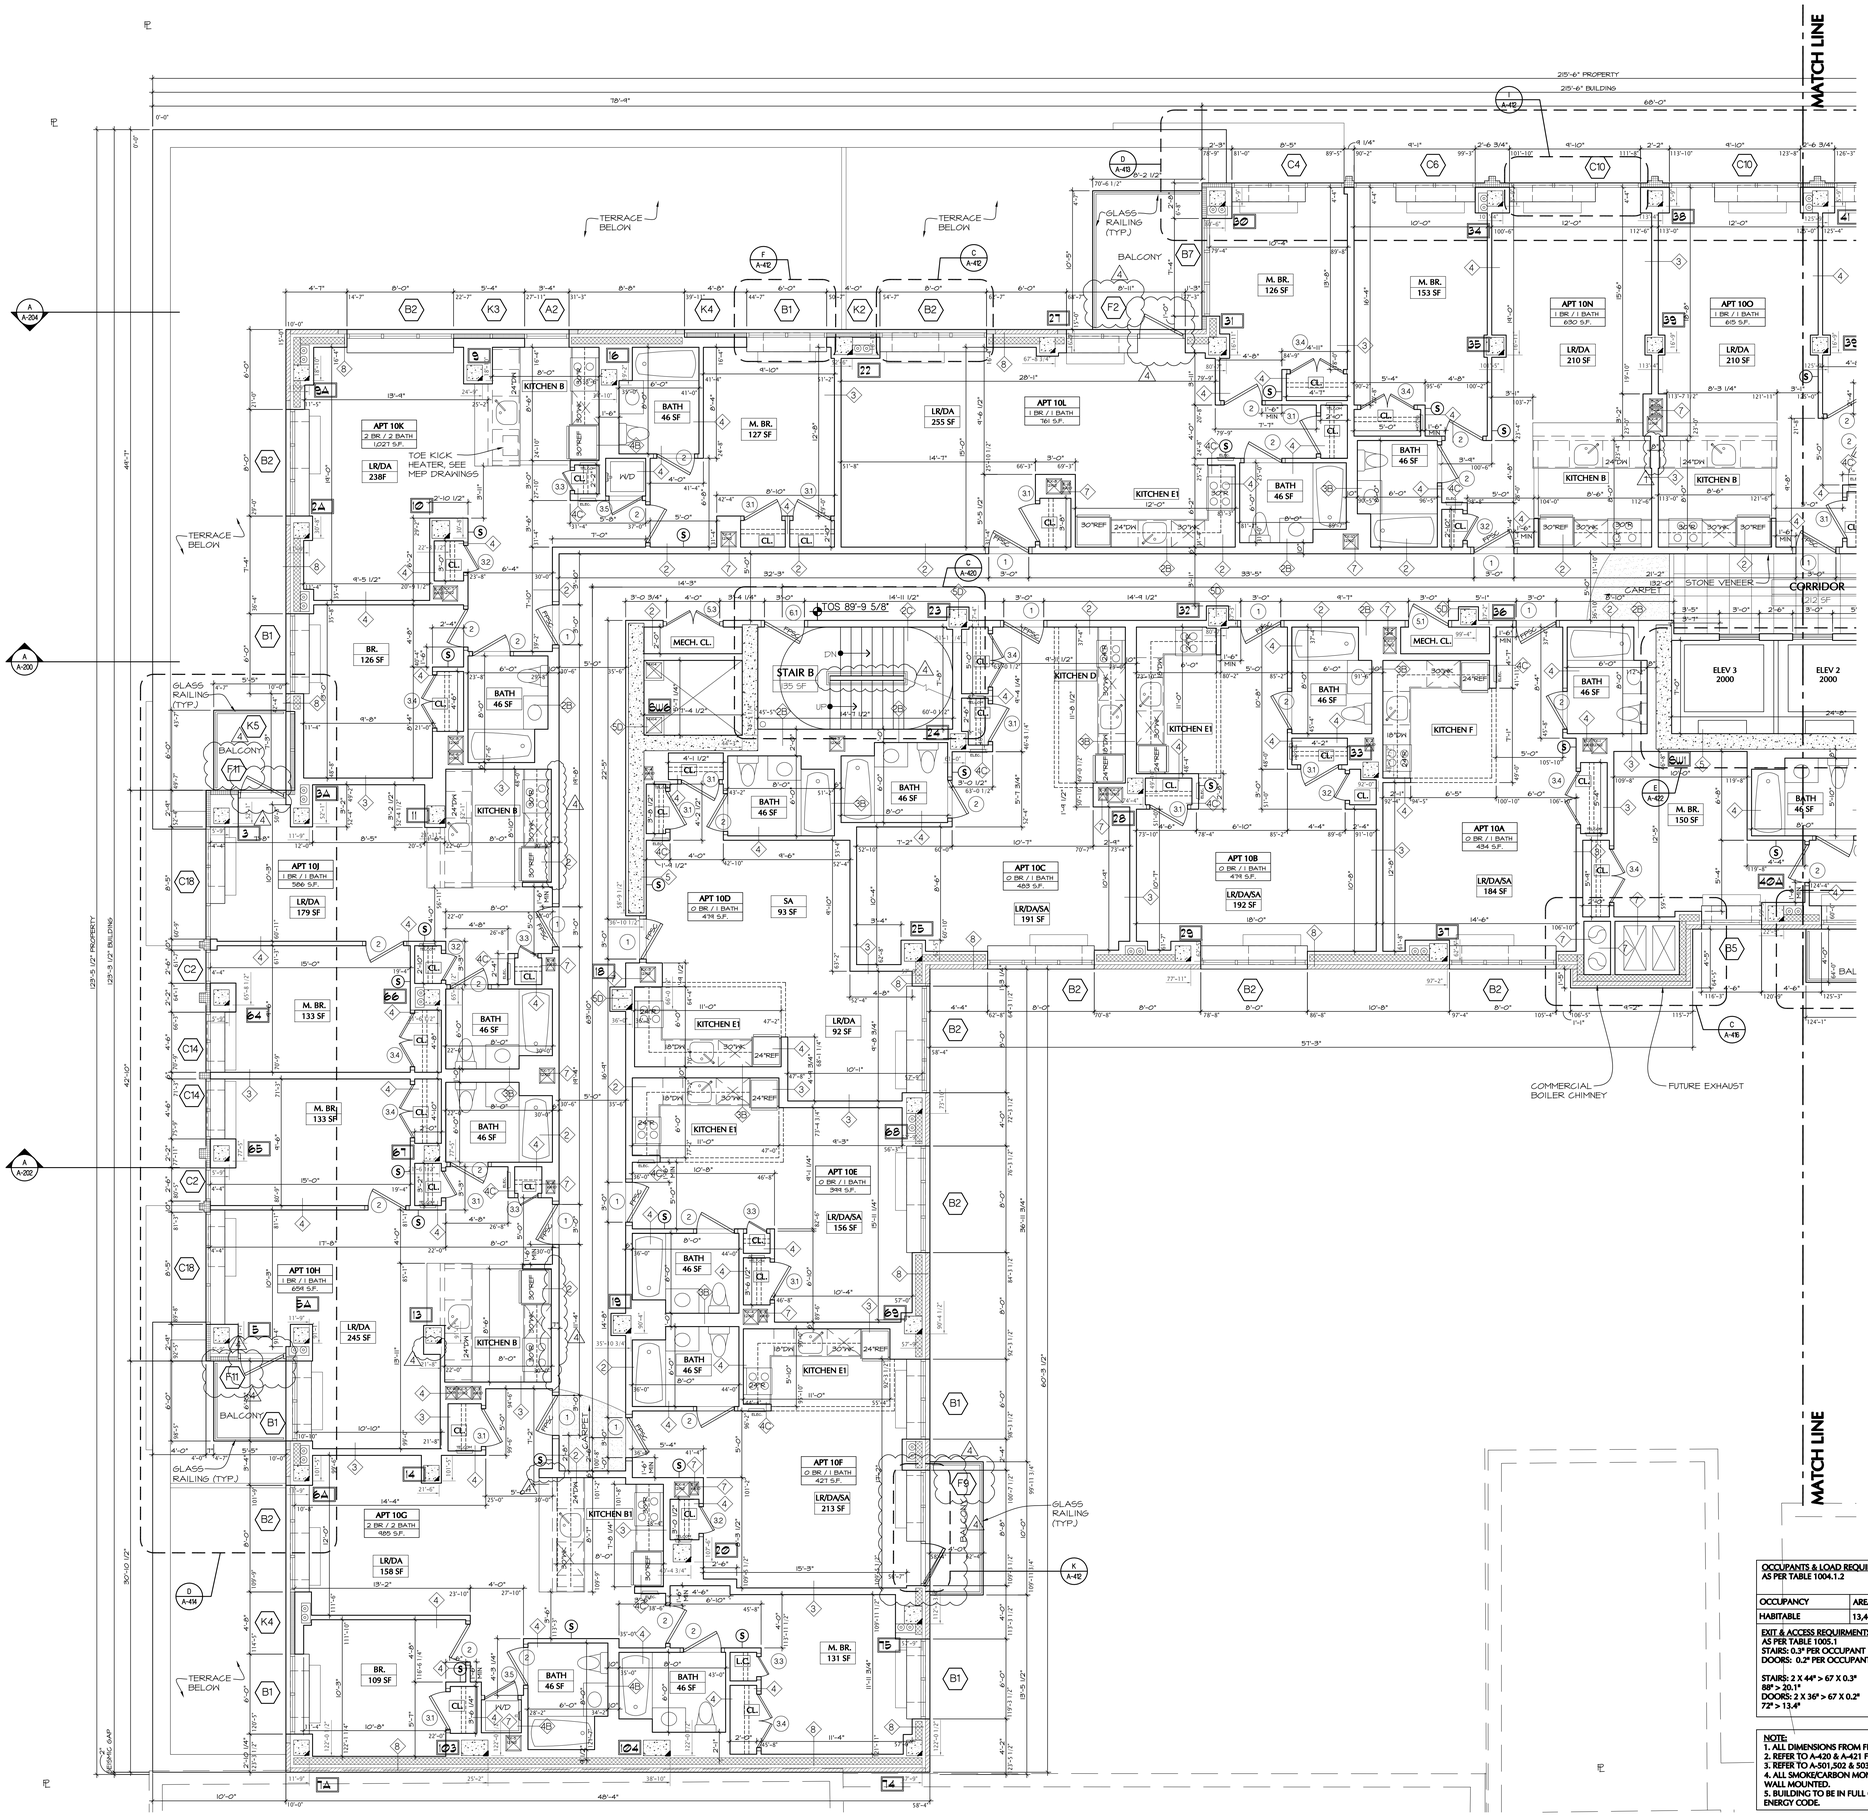
MATCH LINE
TERRACE BELOW
GLASS RAILING (TYP.)
BALCONY
APT 10K
2 BR / 2 BATH
1,021 S.F.
LR/DA
238F
TOE KICK HEATER, SEE MEP DRAWINGS
APT 10L
1 BR / 1 BATH
761 S.F.
LR/DA
255 SF
APT 10N
1 BR / 1 BATH
650 S.F.
LR/DA
210 SF
APT 10O
1 BR / 1 BATH
615 S.F.
LR/DA
210 SF
STAIR B
35 SF
TOS 89'-9 5/8"
CORRIDOR
212 SF
STONE VENEER
CARPET
APT 10J
1 BR / 1 BATH
586 S.F.
LR/DA
179 SF
APT 10H
1 BR / 1 BATH
654 S.F.
LR/DA
245 SF
APT 10G
2 BR / 2 BATH
985 S.F.
LR/DA
158 SF
APT 10D
0 BR / 1 BATH
478 S.F.
SA
93 SF
APT 10C
0 BR / 1 BATH
485 S.F.
LR/DA/SA
191 SF
APT 10B
0 BR / 1 BATH
474 S.F.
LR/DA/SA
192 SF
APT 10A
0 BR / 1 BATH
484 S.F.
LR/DA/SA
184 SF
APT 10E
0 BR / 1 BATH
388 S.F.
LR/DA/SA
156 SF
APT 10F
0 BR / 1 BATH
421 S.F.
LR/DA/SA
213 SF
KITCHEN B
KITCHEN B1
KITCHEN D
KITCHEN E1
KITCHEN F
BATH
46 SF
M. BR.
126 SF
M. BR.
127 SF
M. BR.
153 SF
M. BR.
133 SF
M. BR.
131 SF
M. BR.
150 SF
BR.
126 SF
BR.
109 SF
MECH. CL.
ELEV 3
2000
ELEV 2
2000
COMMERCIAL BOILER CHIMNEY
FUTURE EXHAUST
TERRACE BELOW
GLASS RAILING (TYP.)
BALCONY
CARPET
25'-6" PROPERTY
25'-6" BUILDING
129'-5 1/2" PROPERTY
129'-3 1/2" BUILDING
42'-0"
30'-10 1/2"
49'-7"
78'-4"
0'-0"
48'-4"
10'-0"
58'-4"
57'-3"
60'-3 1/2"
FIRE HOSE CABINET
FIRE HOSE CABINET
FIRE HOSE CABINET

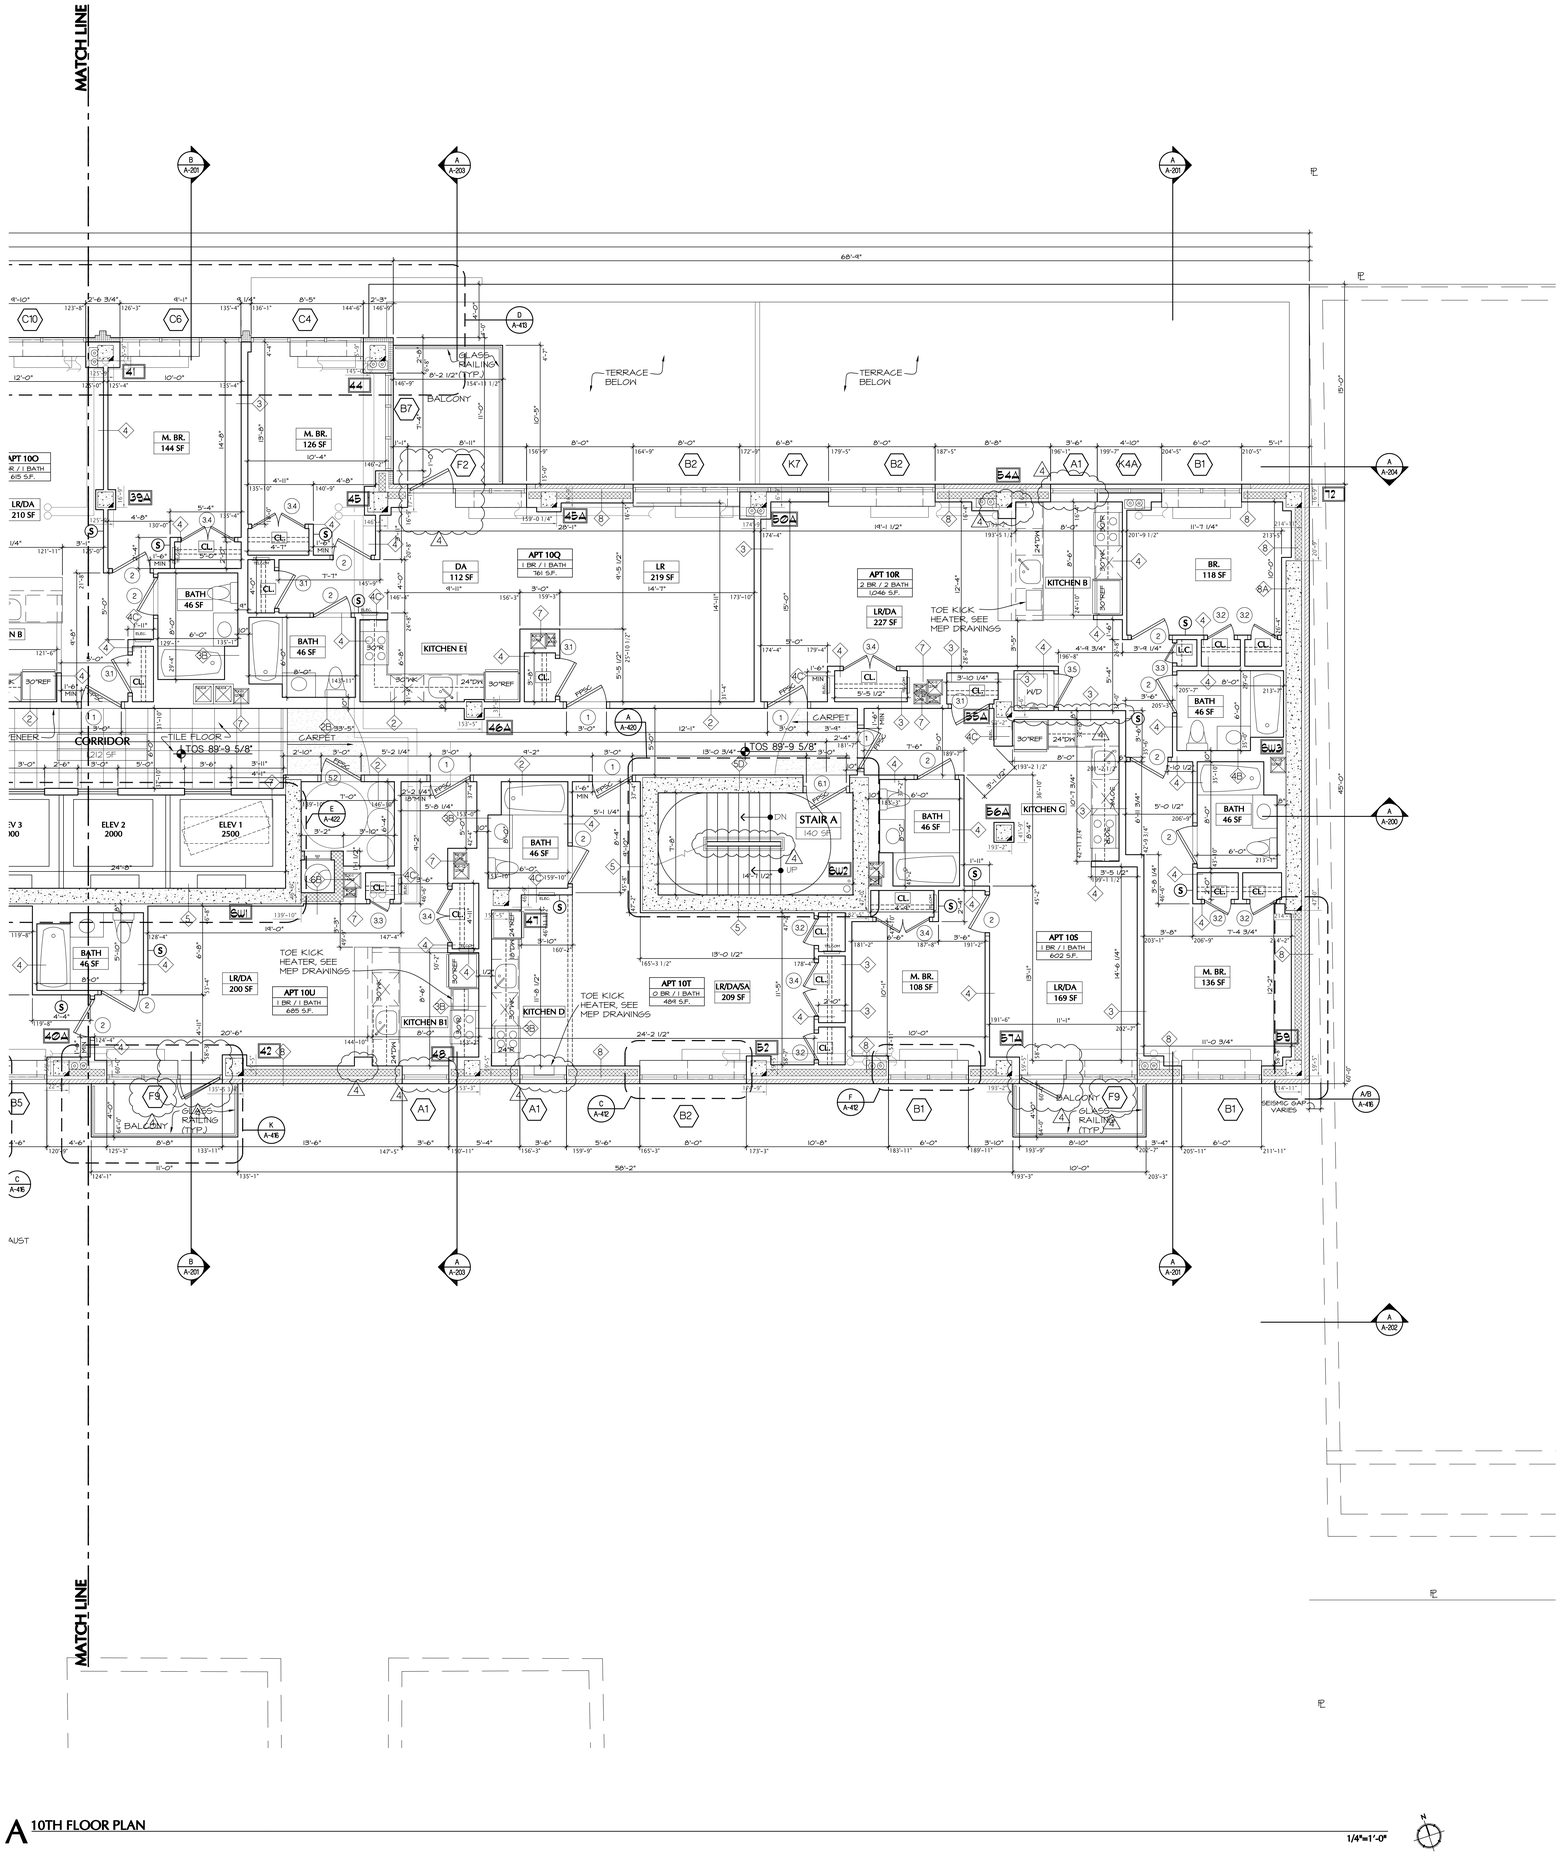

A 10TH FLOOR PLAN

1/4"=1'-0"

MATERIAL LEGEND

- BRICK
- CMU
- PRECAST
- SPANDREL
- METAL PANEL

OCCUPANTS & LOAD REQUIRMENTS:
AS PER TABLE 1004.1.2

OCCUPANCY	AREA / OCCUPANT	# OF OCCUPANTS
HABITABLE	13,405.95 / 200	67

EXIT & ACCESS REQUIRMENTS:
AS PER TABLE 1005.1
STAIRS: 0.3" PER OCCUPANT
DOORS: 0.2" PER OCCUPANT

STAIRS: 2 X 44" > 67 X 0.3"
88" > 20.1"
DOORS: 2 X 36" > 67 X 0.2"
72" > 13.4"

NOTE:
1. ALL DIMENSIONS FROM FINISH TO FINISH.
2. REFER TO A-420 & A-421 FOR STAIR DIMENSIONS.
3. REFER TO A-501,502 & 503 FOR KITCHEN & BATH LAYOUTS.
4. ALL SMOKE/CARBON MONOXIDE DETECTORS TO BE WALL MOUNTED.
5. BUILDING TO BE IN FULL COMPLIANCE WITH NYS ENERGY CODE.

GF55
PARTNERS
19 W. 21ST STREET
NEW YORK, N Y 10010
212 352 3099
©GF55 Partners, LLP 2012

260 WEST 26TH STREET
NEW YORK NY 10001

BLOCK: 775
LOT: 4, 69, 77, 78, 79, 80

DEVELOPER
ARTIMUS

STRUCTURAL ENGINEER
ENGINEERING GROUP

MECHANICAL ENGINEER
RODKIN CARDINALE ENGINEERS P.C.

OWNER
CHELSEA W26 LLC

ISSUE
DOB APPROVED SET AUGUST 5, 2011
100% FOUNDATION SET JULY 29, 2011
REVISION 1 SEPT 16, 2011
85% CONSTRUCTION SET SEPTEMBER 21, 2011
100% SUPER STRUCTURE SET SEPT 26, 2011
REVISION 2 NOV 2, 2011
REVISION 3 NOV 14, 2011
100% CONSTRUCTION SET DECEMBER 16, 2011
REVISION 4 FEB 3, 2012

SCALE
1/4"=1'-0"

PROJECT
260 WEST 26TH STREET

DRAWING
10TH FLOOR PLAN

SEAL AND SIGNATURE

DATE: 02.03.2012
PROJECT NO: 1574.00
DRAWING BY: JD CC DR
CHK BY: MR
DWG NO:

A-108B

CADD FILE NO: 26 OF 100

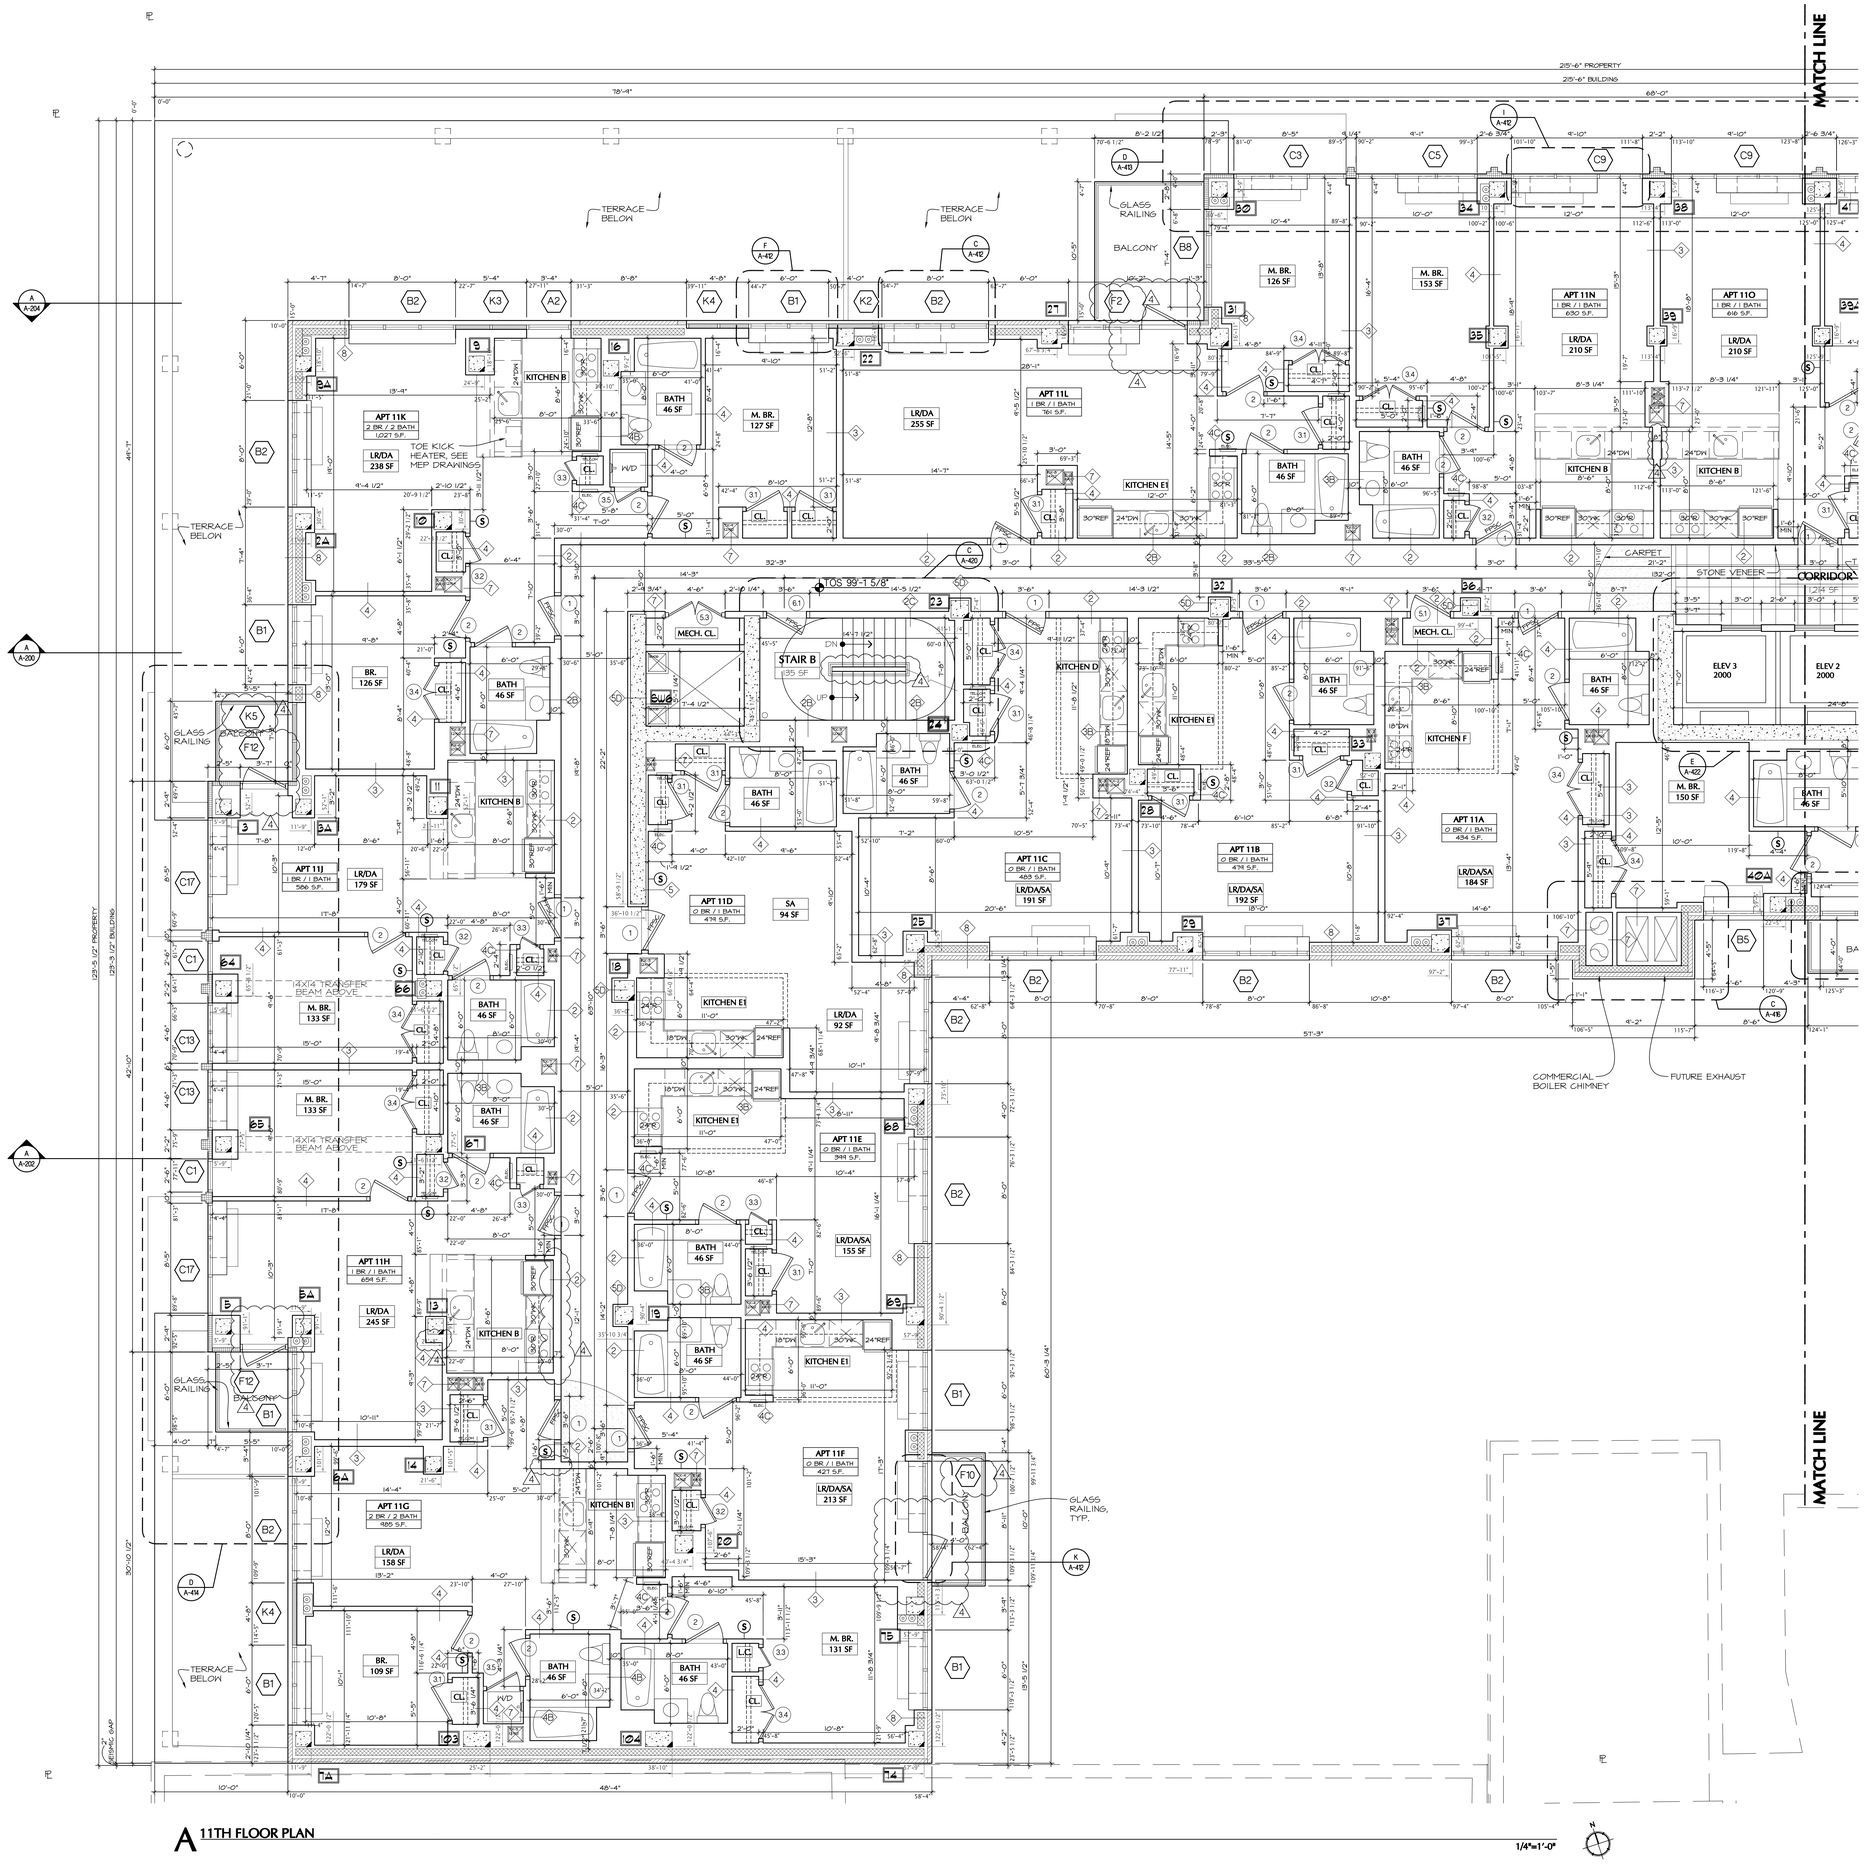

A 11TH FLOOR PLAN

1/4"=1'-0"

GF55
PARTNERS
19 W. 21ST STREET
NEW YORK, N Y 10010
212 352 3099

©GF55 Partners, LLP 2012

260 WEST 26TH STREET
NEW YORK NY 10001

BLOCK: 775
LOT: 4, 69, 77, 78, 79, 80

DEVELOPER
ARTIMUS

STRUCTURAL ENGINEER
ENGINEERING GROUP

MECHANICAL ENGINEER
RODKIN CARDINALE ENGINEERS P.C.

OWNER
CHELSEA W26 LLC

ISSUE
DOB APPROVED SET AUGUST 5, 2011
100% FOUNDATION SET JULY 29, 2011
REVISION 1 SEPT 16, 2011
85% CONSTRUCTION SET SEPTEMBER 21, 2011
100% SUPER STRUCTURE SET SEPT 26, 2011
REVISION 2 NOV 2, 2011
REVISION 3 NOV 14, 2011
100% CONSTRUCTION SET DECEMBER 16, 2011
REVISION 4 FEB 3, 2012

SCALE
1/4"=1'-0"

PROJECT
260 WEST 26TH STREET

DRAWING
11TH FLOOR PLAN

SEAL AND SIGNATURE

DATE: 02.03.2012
PROJECT NO: 1574.00
DRAWING BY: JD CC DR
CHK BY: MR
DWG NO:

A-109A

CADD FILE NO: 37 OF 100

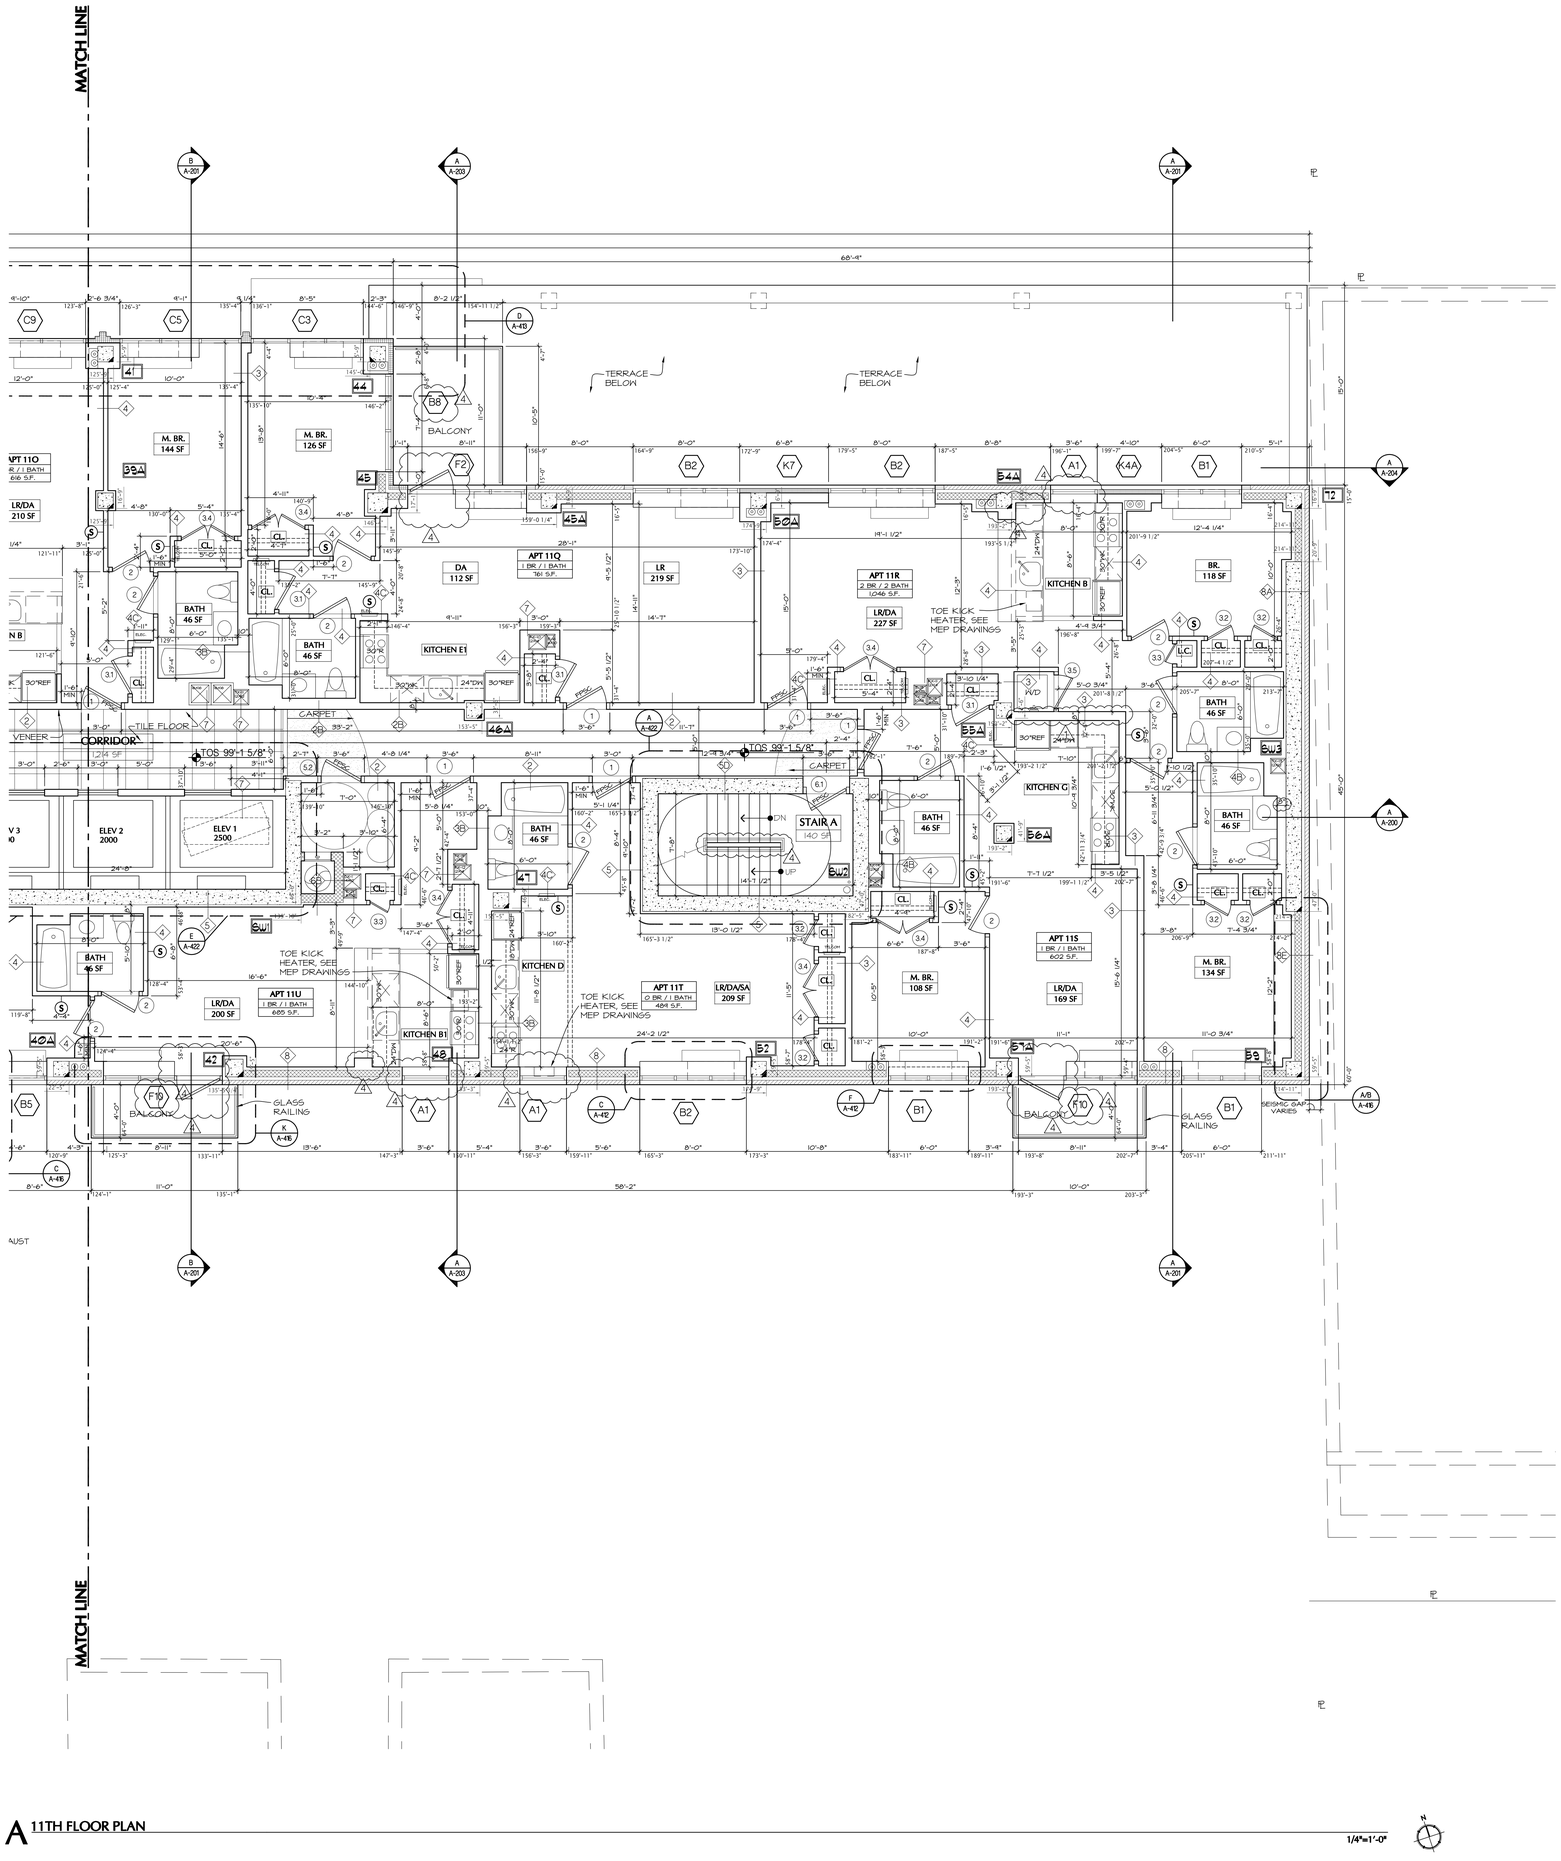

MATERIAL LEGEND
- BRICK
- CMU
- PRECAST
- SPANDREL
- METAL PANEL

A 11TH FLOOR PLAN

1/4"=1'-0"

GF55
PARTNERS
19 W. 21ST STREET
NEW YORK, N Y 10010
212 352 3099
©GF55 Partners, LLP 2012

260 WEST 26TH STREET
NEW YORK NY 10001

BLOCK: 775
LOT: 4, 69, 77, 78, 79, 80

DEVELOPER
ARTIMUS

STRUCTURAL ENGINEER
ENGINEERING GROUP

MECHANICAL ENGINEER
RODKIN CARDINALE ENGINEERS P.C.

OWNER
CHELSEA W26 LLC

ISSUE
DOB APPROVED SET AUGUST 5, 2011
100% FOUNDATION SET JULY 29, 2011
REVISION 1 SEPT 16, 2011
85% CONSTRUCTION SET SEPTEMBER 21, 2011
100% SUPER STRUCTURE SET SEPT 26, 2011
REVISION 2 NOV 2, 2011
REVISION 3 NOV 14, 2011
100% CONSTRUCTION SET DECEMBER 16, 2011
REVISION 4 FEB 3, 2012

SCALE
1/4"=1'-0"

PROJECT
260 WEST 26TH STREET

DRAWING
11TH FLOOR PLAN

SEAL AND SIGNATURE

DATE: 02.03.2012
PROJECT NO: 1574.00
DRAWING BY: JD CC DR
CHK BY: MR
DWG NO:

A-109B

CADD FILE NO: 28 OF 100

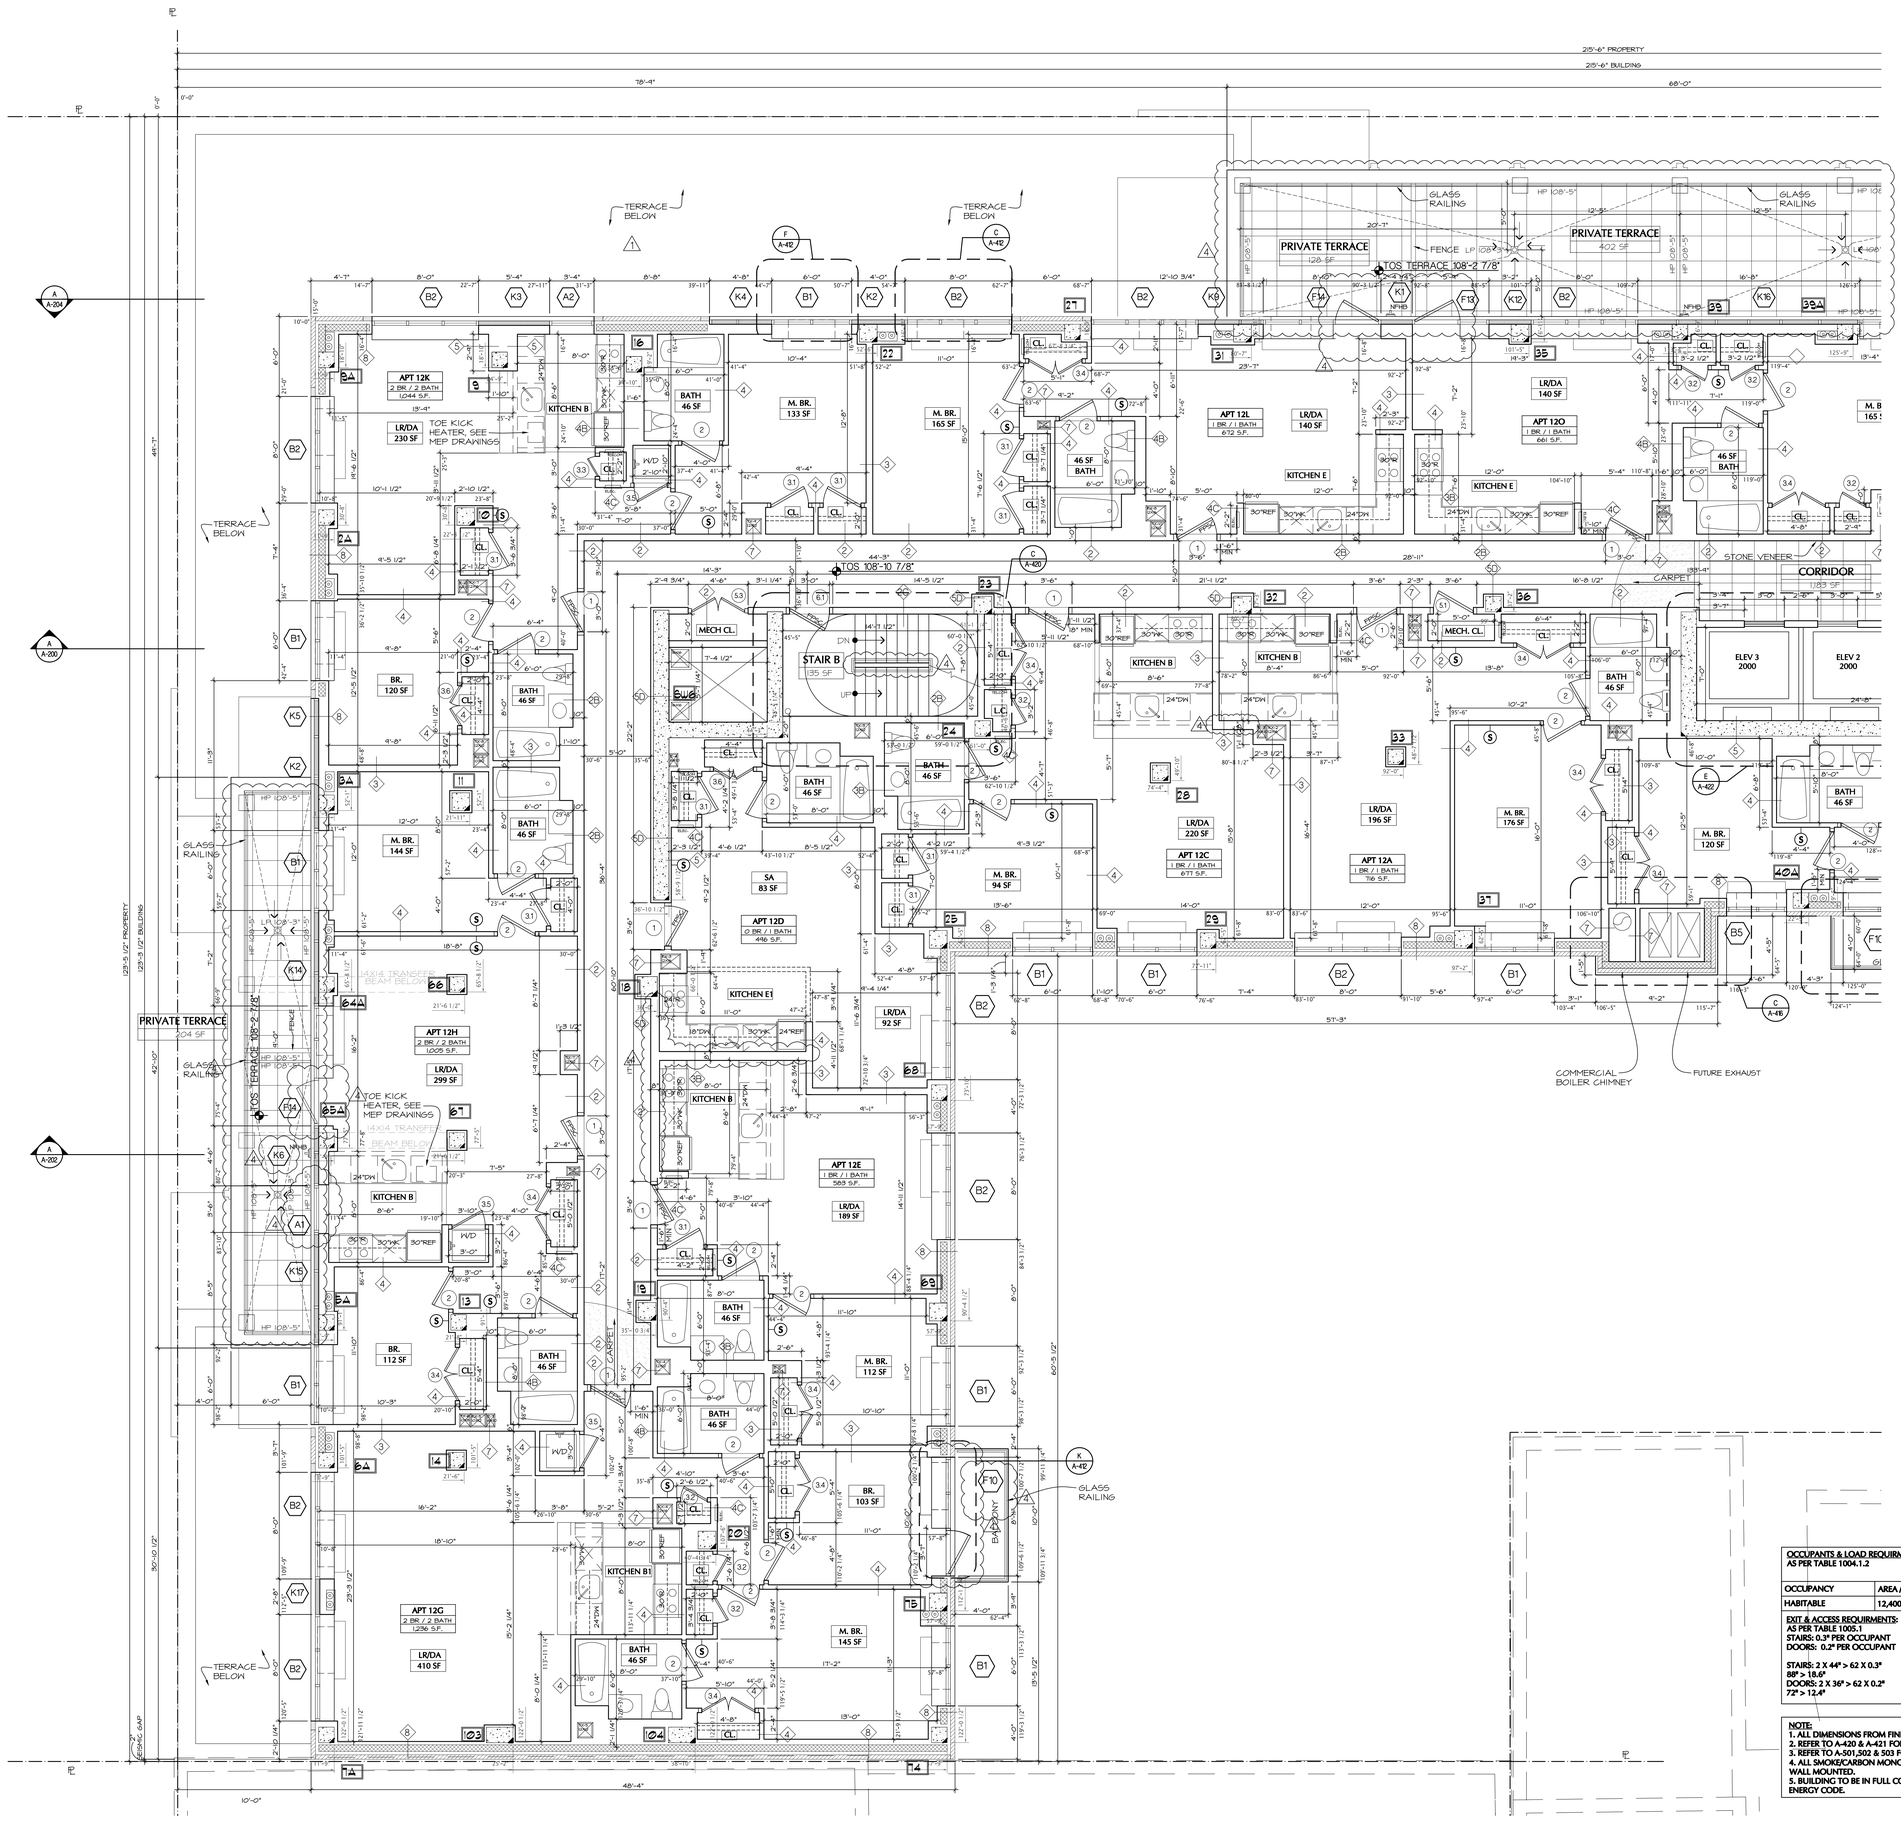

OCCUPANTS & LOAD REQUIRMENTS:
AS PER TABLE 1004.1.2

OCCUPANCY	AREA / OCCUPANT	# OF OCCUPANTS
HABITABLE	12,400.94 / 200	62

EXIT & ACCESS REQUIRMENTS:
AS PER TABLE 1005.1
STAIRS: 0.3" PER OCCUPANT
DOORS: 0.2" PER OCCUPANT

STAIRS: 2 X 44" > 62 X 0.3"
88" > 18.6"
DOORS: 2 X 36" > 62 X 0.2"
72" > 12.4"

NOTE:
1. ALL DIMENSIONS FROM FINISH TO FINISH.
2. REFER TO A-420 & A-421 FOR STAIR DIMENSIONS.
3. REFER TO A-501,502 & 503 FOR KITCHEN & BATH LAYOUTS.
4. ALL SMOKE/CARBON MONOXIDE DETECTORS TO BE WALL MOUNTED.
5. BUILDING TO BE IN FULL COMPLIANCE WITH NYS ENERGY CODE.

GF55
PARTNERS
19 W. 21ST STREET
NEW YORK, N Y 10010
212 352 3099

©GF55 Partners, LLP 2012

260 WEST 26TH STREET
NEW YORK NY 10001

BLOCK: 775
LOT: 4, 69, 77, 78, 79, 80

DEVELOPER
ARTIMUS

STRUCTURAL ENGINEER
ENGINEERING GROUP

MECHANICAL ENGINEER
RODKIN CARDINALE ENGINEERS P.C.

OWNER
CHELSEA W26 LLC

ISSUE
DOB APPROVED SET AUGUST 5, 2011
100% FOUNDATION SET JULY 29, 2011
REVISION 1 SEPT 16, 2011
85% CONSTRUCTION SET SEPTEMBER 21, 2011
100% SUPER STRUCTURE SET SEPT 26, 2011
REVISION 2 NOV 2, 2011
REVISION 3 NOV 14, 2011
100% CONSTRUCTION SET DECEMBER 16, 2011
REVISION 4 FEB 3, 2012

SCALE
1/4"=1'-0"

PROJECT
260 WEST 26TH STREET

DRAWING
12TH FLOOR PLAN

SEAL AND SIGNATURE

DATE: 02.03.2012
PROJECT NO: 1574.00
DRAWING BY: JD CC DR
CHK BY: MR
DWG NO:

A-110A

CADD FILE NO: 29 OF 100

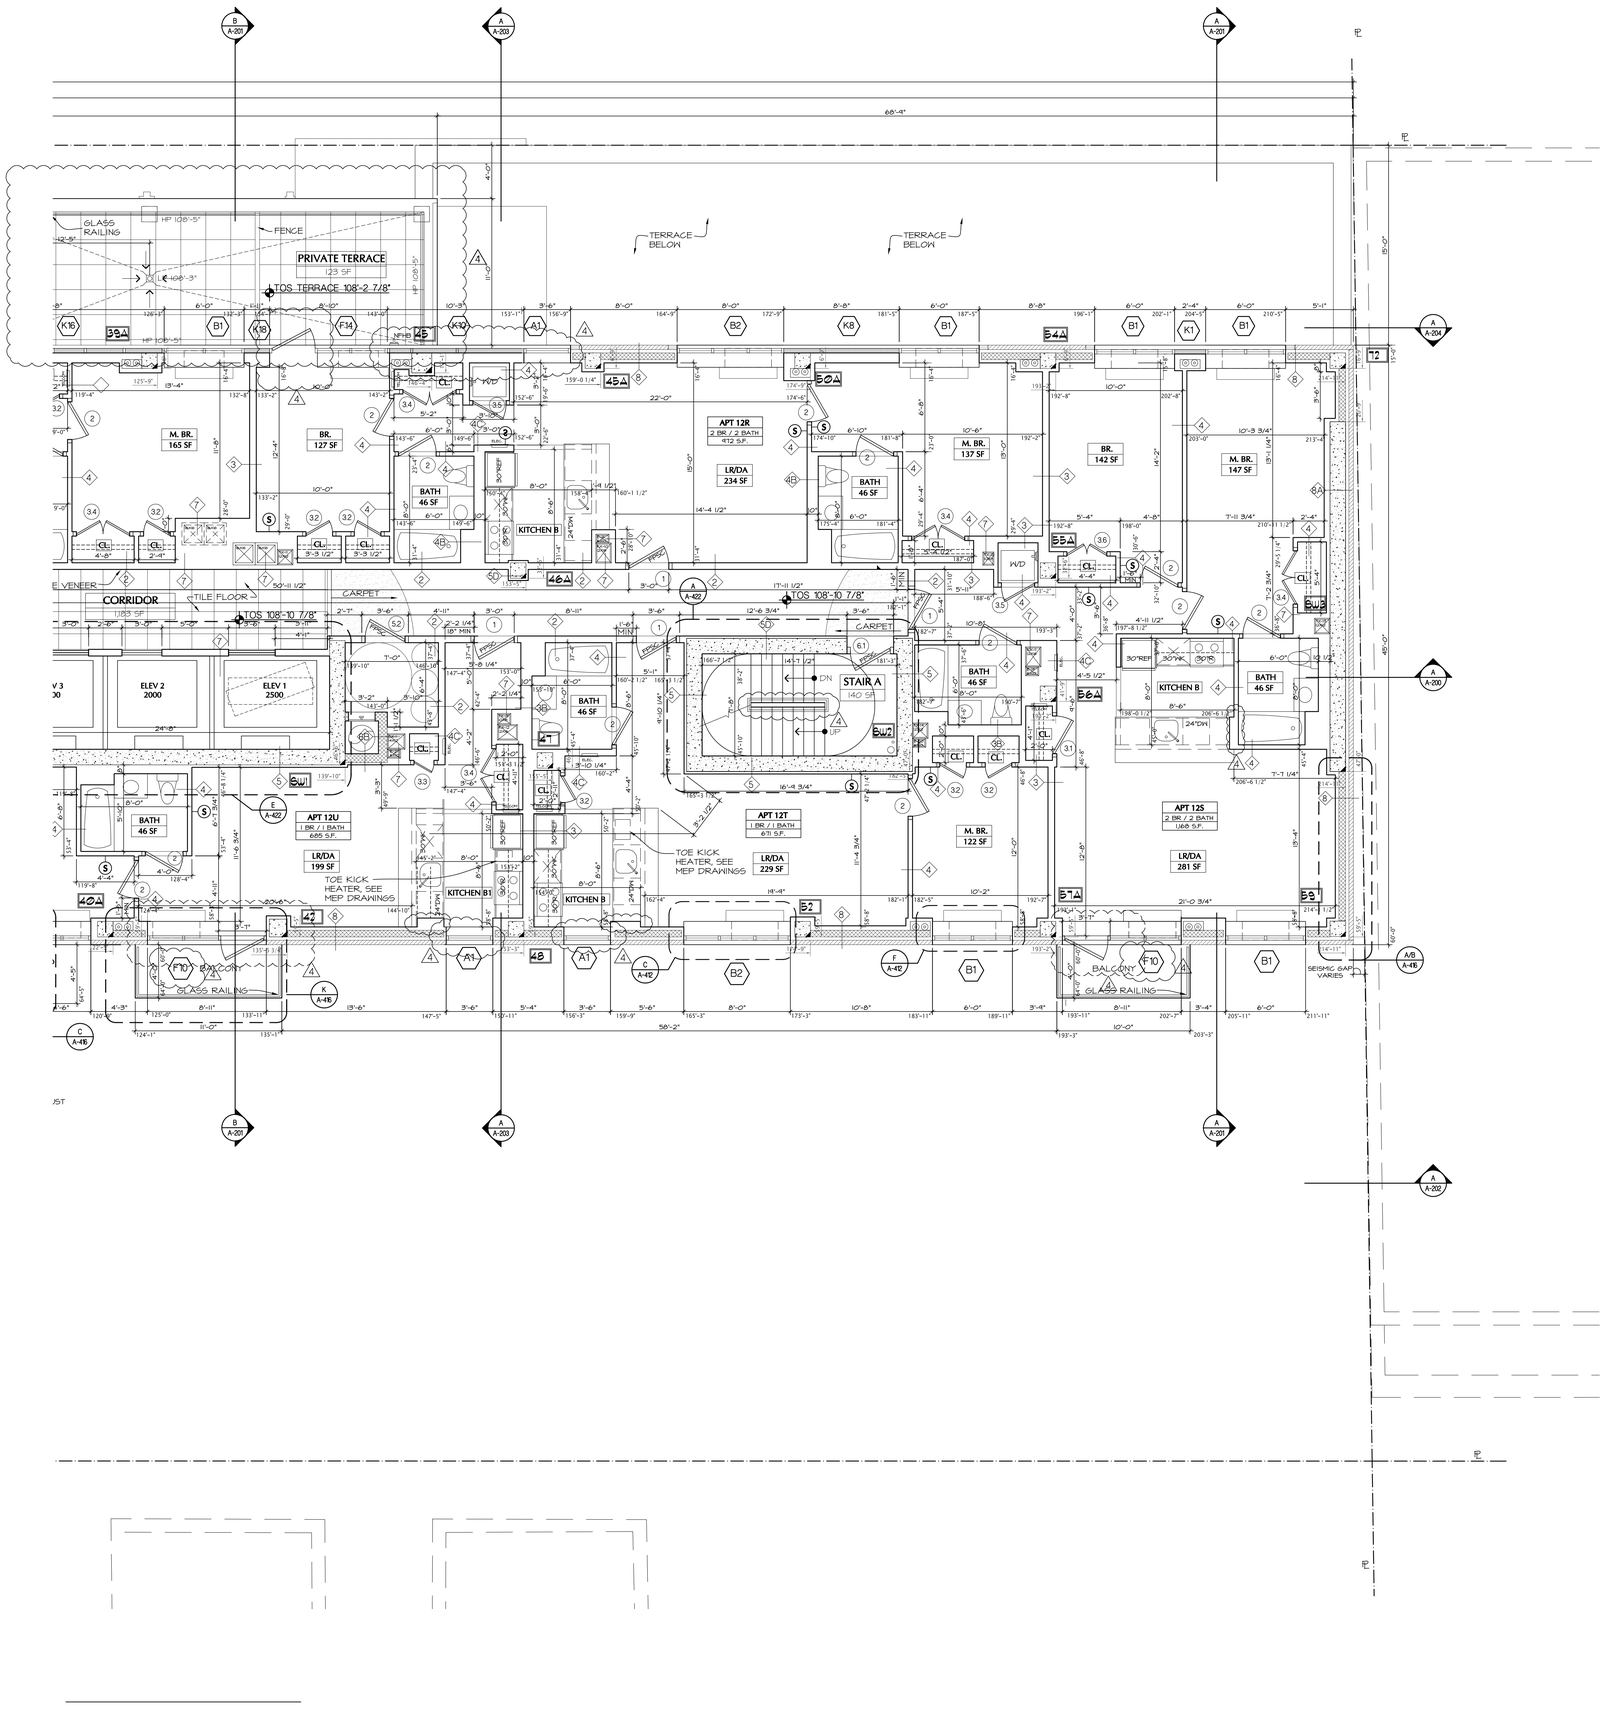

OCCUPANTS & LOAD REQUIREMENTS: AS PER TABLE 1004.1.2		
OCCUPANCY	AREA / OCCUPANT	# OF OCCUPANTS
HABITABLE	12,400.94 / 200	62

EXIT & ACCESS REQUIRMENTS:
AS PER TABLE 1005.1
STAIRS: 0.3" PER OCCUPANT
DOORS: 0.2" PER OCCUPANT

STAIRS: 2 X 44" > 62 X 0.3"
88" > 18.6"
DOORS: 2 X 36" > 62 X 0.2"
72" > 12.4"

NOTE:
1. ALL DIMENSIONS FROM FINISH TO FINISH.
2. REFER TO A-420 & A-421 FOR STAIR DIMENSIONS.
3. REFER TO A-501,502 & 503 FOR KITCHEN & BATH LAYOUTS.
4. ALL SMOKE/CARBON MONOXIDE DETECTORS TO BE WALL MOUNTED.
5. BUILDING TO BE IN FULL COMPLIANCE WITH NYS ENERGY CODE.

GF55
PARTNERS
19 W. 21ST STREET
NEW YORK, N Y 10010
212 352 3099

©GF55 Partners, LLP 2012

260 WEST 26TH STREET NEW YORK NY 10001

BLOCK: 775
LOT: 4, 69, 77, 78, 79, 80

DEVELOPER
ARTIMUS

STRUCTURAL ENGINEER
ENGINEERING GROUP

MECHANICAL ENGINEER
RODKIN CARDINALE ENGINEERS P.C.

OWNER
CHELSEA W26 LLC

ISSUE
DOB APPROVED SET AUGUST 5, 2011
100% FOUNDATION SET JULY 29, 2011
REVISION 1 SEPT 16, 2011
85% CONSTRUCTION SET SEPTEMBER 21, 2011
100% SUPER STRUCTURE SET SEPT 26, 2011
REVISION 2 NOV 2, 2011
REVISION 3 NOV 14, 2011
100% CONSTRUCTION SET DECEMBER 16, 2011
REVISION 4 FEB 3, 2012

SCALE
1/4"=1'-0"

PROJECT
260 WEST 26TH STREET

DRAWING
12TH FLOOR PLAN

SEAL AND SIGNATURE

DATE: 02.03.2012
PROJECT NO: 1574.00
DRAWING BY: JD CC DR
CHK BY: MR
DWG NO:

A-110B

CADD FILE NO: 30 OF 100

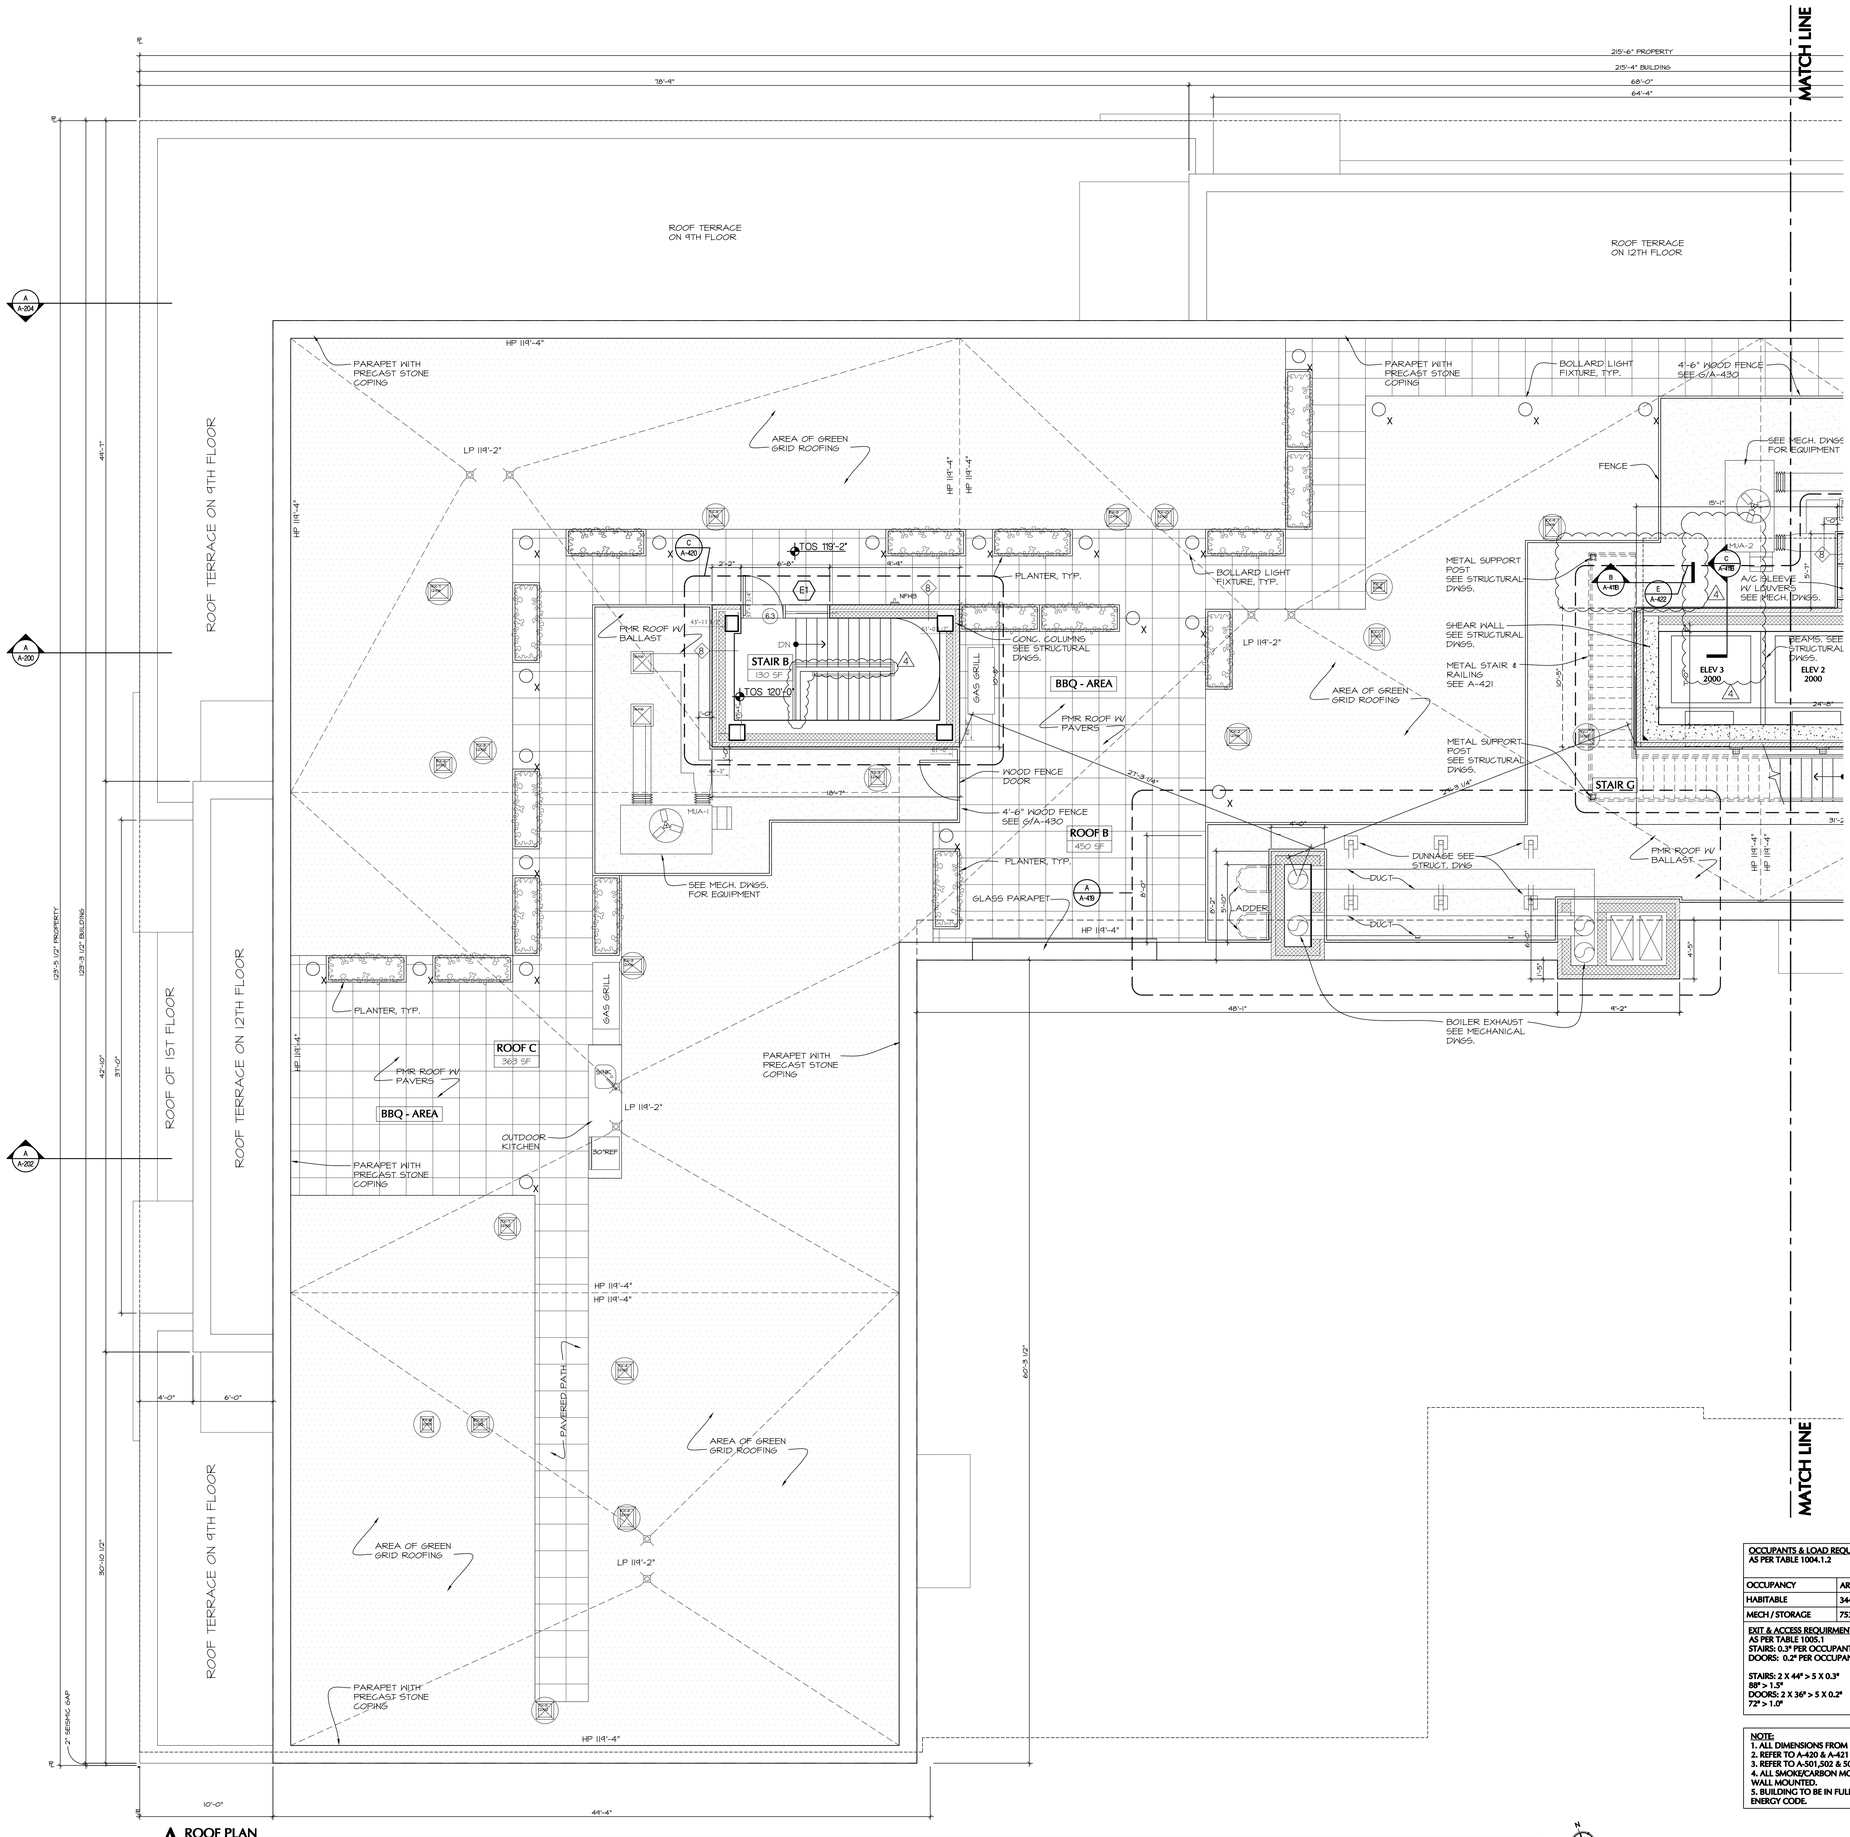

A ROOF PLAN

1/8"=1'-0"

OCCUPANTS & LOAD REQUIRMENTS:
AS PER TABLE 1004.1.2

OCCUPANCY	AREA / OCCUPANT	# OF OCCUPANTS
HABITABLE	344.85 / 200	2
MECH / STORAGE	753 / 300	3

EXIT & ACCESS REQUIRMENTS:
AS PER TABLE 1005.1
STAIRS: 0.3" PER OCCUPANT
DOORS: 0.2" PER OCCUPANT

STAIRS: 2 X 44" > 5 X 0.3"
88" > 1.5"
DOORS: 2 X 36" > 5 X 0.2"
72" > 1.0"

NOTE:
1. ALL DIMENSIONS FROM FINISH TO FINISH.
2. REFER TO A-420 & A-421 FOR STAIR DIMENSIONS.
3. REFER TO A-501,502 & 503 FOR KITCHEN & BATH LAYOUTS.
4. ALL SMOKE/CARBON MONOXIDE DETECTORS TO BE WALL MOUNTED.
5. BUILDING TO BE IN FULL COMPLIANCE WITH NYS ENERGY CODE.

GF55
PARTNERS
19 W. 21ST STREET
NEW YORK, N Y 10010
212 352 3099

©GF55 Partners, LLP 2012

260 WEST 26TH STREET NEW YORK NY 10001

BLOCK: 775
LOT: 4, 69, 77, 78, 79, 80

DEVELOPER
ARTIMUS

STRUCTURAL ENGINEER
ENGINEERING GROUP

MECHANICAL ENGINEER
RODKIN CARDINALE ENGINEERS P.C.

OWNER
CHELSEA W26 LLC

ISSUE
DOB APPROVED SET AUGUST 5, 2011
100% FOUNDATION SET JULY 29, 2011
REVISION 1 SEPT 16, 2011
85% CONSTRUCTION SET SEPTEMBER 21, 2011
100% SUPER STRUCTURE SET SEPT 26, 2011
REVISION 2 NOV 2, 2011
REVISION 3 NOV 14, 2011
100% CONSTRUCTION SET DECEMBER 16, 2011
REVISION 4 FEB 3, 2012

SCALE
1/4"=1'-0"

PROJECT
260 WEST 26TH STREET

DRAWING
ROOF PLAN

SEAL AND SIGNATURE

DATE: 02.03.2012
PROJECT NO: 1574.00
DRAWING BY: JD CC DR
CHK BY: MR
DWG NO:

A-111A

CADD FILE NO: 31 OF 100

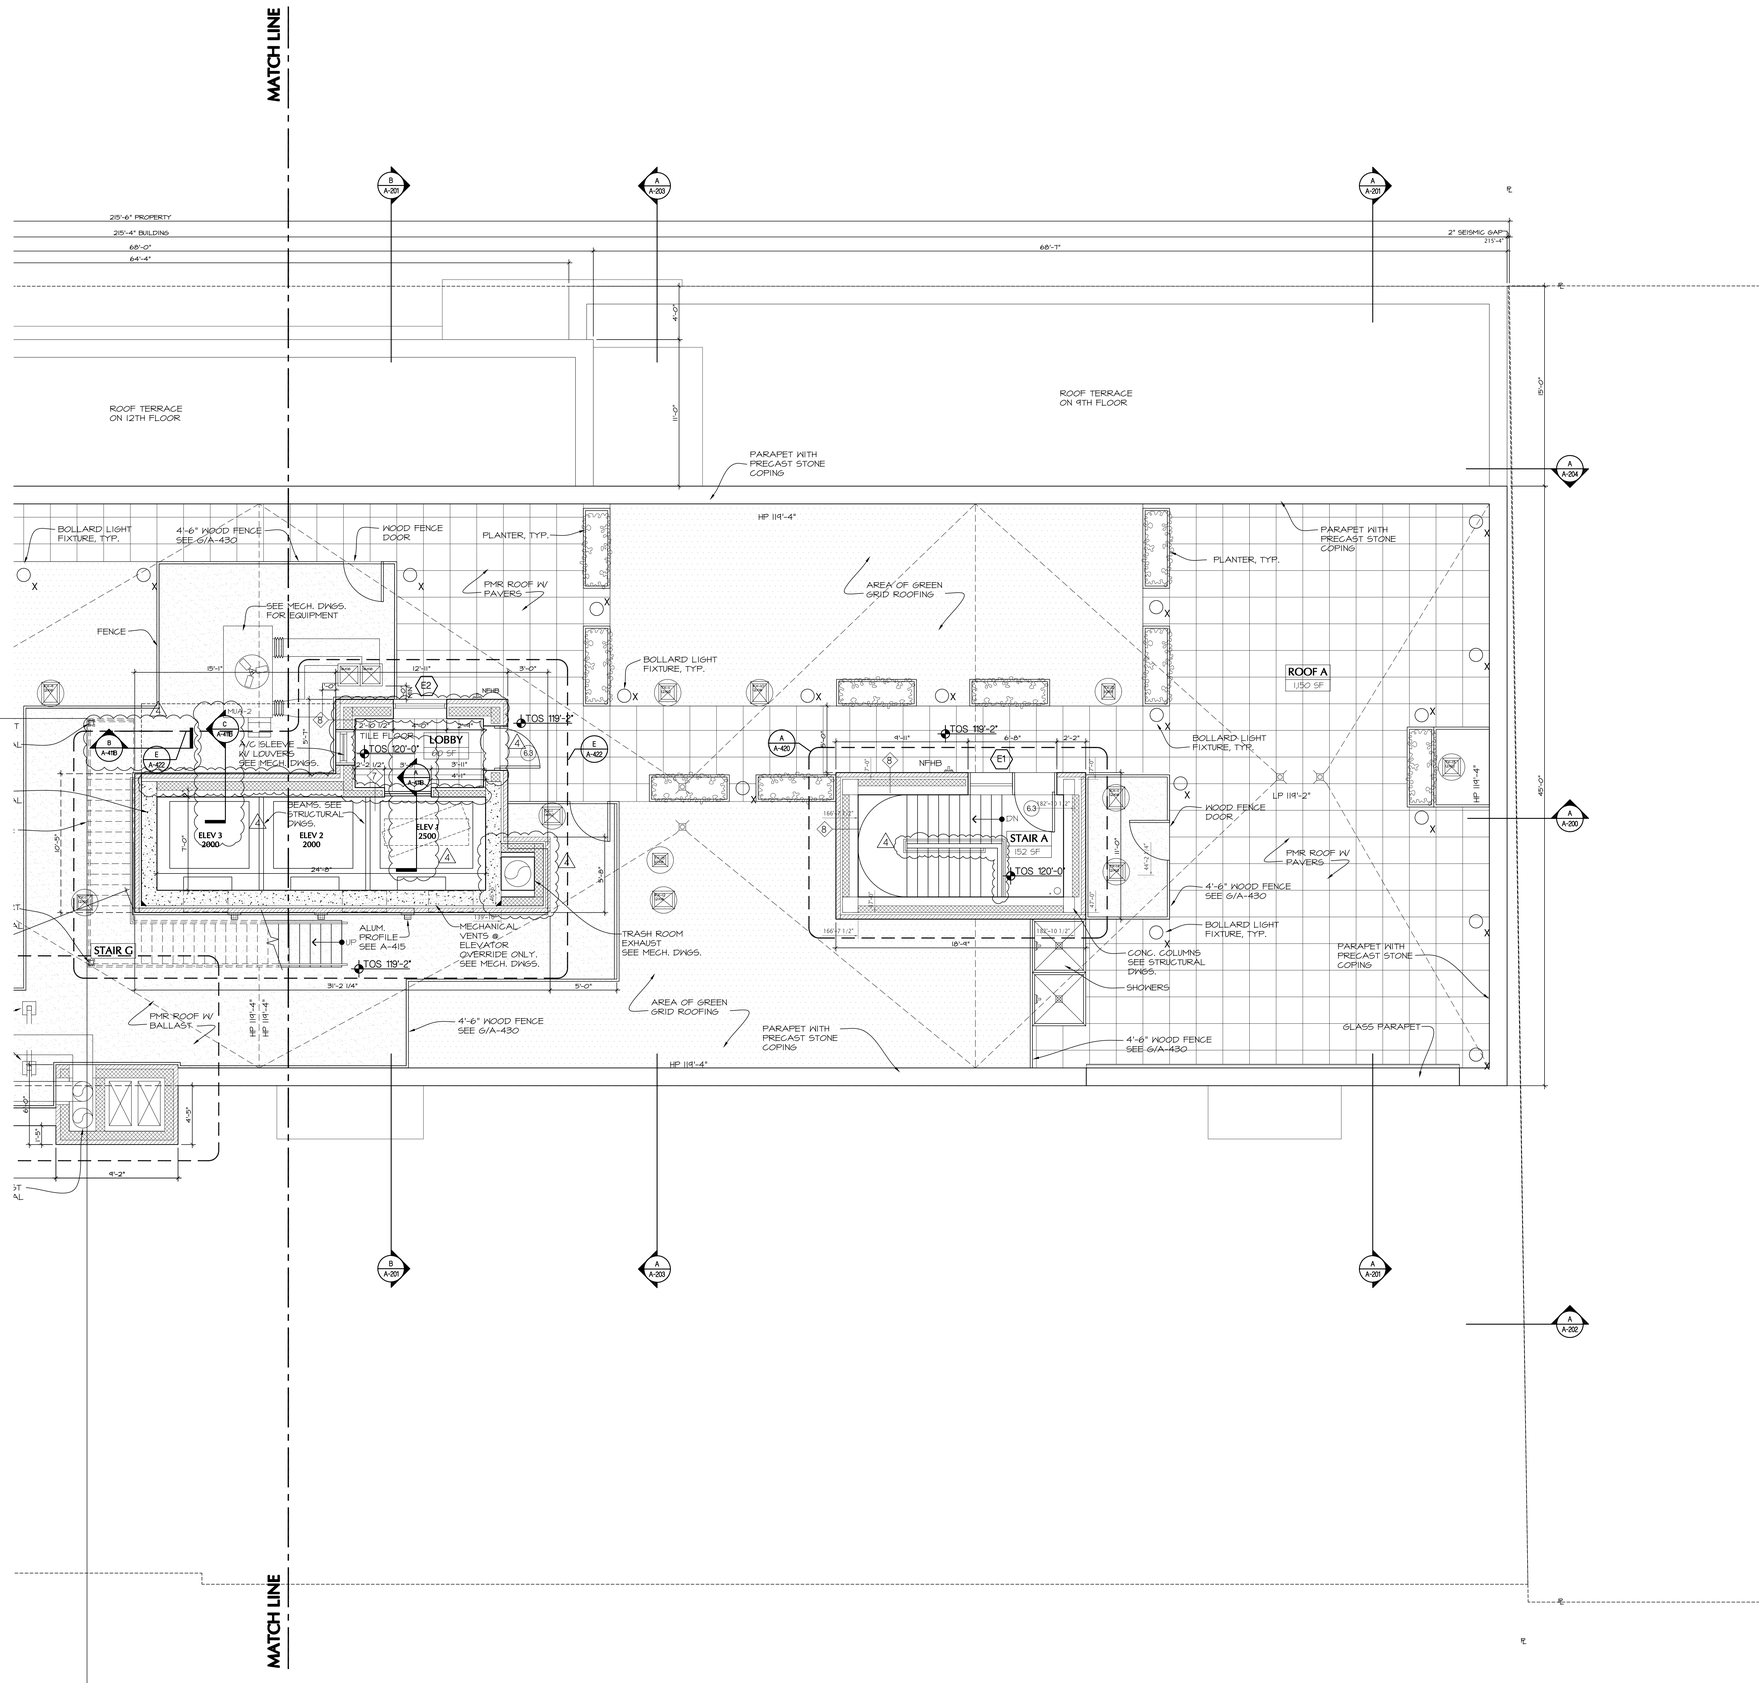

A ROOF PLAN

1/8"=1'-0"

OCCUPANTS & LOAD REQUIRMENTS:
AS PER TABLE 1004.1.2

OCCUPANCY	AREA / OCCUPANT	# OF OCCUPANTS
HABITABLE	344.85 / 200	2
MECH / STORAGE	753 / 300	3

EXIT & ACCESS REQUIRMENTS:
AS PER TABLE 1005.1
STAIRS: 0.3" PER OCCUPANT
DOORS: 0.2" PER OCCUPANT

STAIRS: 2 X 44" > 5 X 0.3"
88" > 1.5"
DOORS: 2 X 36" > 5 X 0.2"
72" > 1.0"

NOTE:
1. ALL DIMENSIONS FROM FINISH TO FINISH.
2. REFER TO A-420 & A-421 FOR STAIR DIMENSIONS.
3. REFER TO A-501,502 & 503 FOR KITCHEN & BATH LAYOUTS.
4. ALL SMOKE/CARBON MONOXIDE DETECTORS TO BE WALL MOUNTED.
5. BUILDING TO BE IN FULL COMPLIANCE WITH NYS ENERGY CODE.

GF55
PARTNERS
19 W. 21ST STREET
NEW YORK, N Y 10010
212 352 3099
©GF55 Partners, LLP 2012

260 WEST 26TH STREET
NEW YORK NY 10001
BLOCK: 775
LOT: 4, 69, 77, 78, 79, 80

DEVELOPER
ARTIMUS

STRUCTURAL ENGINEER
ENGINEERING GROUP

MECHANICAL ENGINEER
RODKIN CARDINALE ENGINEERS P.C.

OWNER
CHELSEA W26 LLC

ISSUE
DOB APPROVED SET AUGUST 5, 2011
100% FOUNDATION SET JULY 29, 2011
REVISION 1 SEPT 16, 2011
85% CONSTRUCTION SET SEPTEMBER 21, 2011
100% SUPER STRUCTURE SET SEPT 26, 2011
REVISION 2 NOV 2, 2011
REVISION 3 NOV 14, 2011
100% CONSTRUCTION SET DECEMBER 16, 2011
REVISION 4 FEB 3, 2012

SCALE
1/4"=1'-0"

PROJECT
260 WEST 26TH STREET

DRAWING
ROOF PLAN

SEAL AND SIGNATURE

DATE: 02.03.2012
PROJECT NO.: 1374.00
DRAWING BY: JD CC DR
CHK BY: MR
DWG NO:
A-111B
CADD FILE NO:
32 OF 100

APPENDIX C

Community Air Monitoring Field Records

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

No PID Readings

Date: 8/30/11
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: Jessica Frosch

TIME	LOCATION A	B	C	D	E	F
7:00	No excavation					
7:30	No excavation					
8:00	No excavation					
8:30	No excavation					
9:00	No excavation					
9:30	.008	0.026	0.016	0.000		
10:00	0.000	0.011	0.002	0.001		
10:30	0.012	0.029	0.000	0.003		
11:00	0.002	0.000	0.018	0.019		
11:30	0.007	0.006	0.041	0.017		
12:00	0.024	0.004	0.000	0.000		
12:30	0.005	0.003	0.000	0.001		
13:00	0.000	0.000	0017	0.006		
13:30	0.000	0.009	0029	0.004		
14:00	0.004	0.017	0.032	0.000		
14:30	0.011	0.000	0.000	0.001		
15:00	0.000	0.000	0.000	0.000		
15:30	Leave Site					
16:00						
16:30						
17:00						

Locations:
A North Property line
B East Property line
C South Property line
D West Property line
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

Date: 09/01/2011
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: Danny Manore

TIME	LOCATION							
	A-Dust	A-VOC	B-Dust	B-VOC	C-Dust	C-VOC	D-Dust	D-VOC
7:00								
7:30	0.007	0.000	0.000	0.000	0.000	0.000	0.002	0.000
8:00	0.007	0.000	0.003	0.000	0.002	0.000	0.005	0.000
8:30	0.042	0.000	0.014	0.000	0.000	0.000	0.000	0.000
9:00	0.059	0.000	0.058	0.000	0.006	0.000	0.009	0.000
9:30	0.015	0.000	0.016	0.000	0.007	0.000	0.040	0.000
10:00	0.030	0.000	0.005	0.000	0.002	0.000	0.004	0.000
10:30	0.000	0.000	0.015	0.000	0.000	0.000	0.000	0.000
11:00	0.008	0.000	0.033	0.000	0.000	0.000	0.000	0.000
11:30	0.008	0.000	0.008	0.000	0.039	0.000	0.000	0.000
12:00	0.011	0.000	0.042	0.000	0.000	0.000	0.000	0.000
12:30	0.018	0.000	0.077	0.000	0.026	0.000	0.000	0.000
13:00	0.007	0.000	0.075	0.000	0.041	0.000	0.004	0.000
13:30	0.003	0.000	0.088	0.000	0.026	0.000	0.016	0.000
14:00	0.005	0.000	0.053	0.000	0.024	0.000	0.008	0.000
14:30	0.053	0.000	0.020	0.000	0.008	0.000	0.020	0.000
15:00								
15:30								
16:00								
16:30								
17:00								

Locations:

A	Along 26th Street - North Property Line
B	East Property Line
C	South Property Line
D	West Property Line

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

Date: 09/02/2011
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: Danny Manore

TIME	LOCATION							
	A-Dust	A-VOC	B-Dust	B-VOC	C-Dust	C-VOC	D-Dust	D-VOC
7:00								
7:30								
8:00								
8:30								
9:00								
9:30								
10:00								
10:30	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
11:00	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
11:30	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
12:00	0.003	0.000	0.000	0.000	0.000	0.000	0.000	0.000
12:30	0.015	0.000	0.000	0.000	0.000	0.000	0.005	0.000
13:00	0.005	0.000	0.000	0.000	0.000	0.000	0.003	0.000
13:30	0.005	0.000	0.000	0.000	0.000	0.000	0.005	0.000
14:00	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
14:30								
15:00								
15:30								
16:00								
16:30								
17:00								

Locations:

A	Along 26th Street - North Property Line
B	East Property Line
C	South Property Line
D	West Property Line

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

Date: 09/06/2011
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: Danny Manore

TIME	LOCATION							
	A-Dust	A-VOC	B-Dust	B-VOC	C-Dust	C-VOC	D-Dust	D-VOC
7:00	**NO DUST/VOC MONITORING DONE TODAY DUE TO RAIN ALL DAY**							
7:30								
8:00								
8:30								
9:00								
9:30								
10:00								
10:30								
11:00								
11:30								
12:00								
12:30								
13:00								
13:30								
14:00								
14:30								
15:00								
15:30								
16:00								
16:30								
17:00								

Locations:

A	Along 26th Street - North Property Line
B	East Property Line
C	South Property Line
D	West Property Line

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

Date: 09/07/2011
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoring: Danny Manore

TIME	LOCATION							
	A-Dust	A-VOC	B-Dust	B-VOC	C-Dust	C-VOC	D-Dust	D-VOC
7:00	**NO DUST/VOC MONITORING DONE TODAY DUE TO RAIN ALL DAY**							
7:30								
8:00								
8:30								
9:00								
9:30								
10:00								
10:30								
11:00								
11:30								
12:00								
12:30								
13:00								
13:30								
14:00								
14:30								
15:00								
15:30								
16:00								
16:30								
17:00								

Locations:

A	Along 26th Street - North Property Line
B	East Property Line
C	South Property Line
D	West Property Line

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

Date: 09/08/2011
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: Danny Manore

TIME	LOCATION							
	A-Dust	A-VOC	B-Dust	B-VOC	C-Dust	C-VOC	D-Dust	D-VOC
7:00								
7:30								
8:00								
8:30								
9:00								
9:30								
10:00	**Digging began at 10:25**							
10:30	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
11:00	0.002	0.000	0.004	0.000	0.000	0.000	0.000	0.000
11:30	0.049	1.200	0.110	0.700	0.005	1.900	0.011	1.200
12:00	0.001	0.000	0.011	0.500	0.000	0.800	0.000	0.700
12:30	0.004	0.000	0.000	0.000	0.000	0.000	0.010	0.000
13:00	**Digging ended at 12:40**							
13:30								
14:00								
14:30								
15:00								
15:30								
16:00								
16:30								
17:00								

Locations:

A	Along 26th Street - North Property Line
B	East Property Line
C	South Property Line
D	West Property Line

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

Date: 09/15/2011
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoring: Danny Manore

TIME	LOCATION							
	A-Dust	A-VOC	B-Dust	B-VOC	C-Dust	C-VOC	D-Dust	D-VOC
7:00	**DUST/VOC MONITORING WAS NOT PERFORMED TODAY. Steve Malinowski from CA Rich Consultants, Inc. advised OER that the dust monitoring activities at the 260 West 26th Street site have been suspended until excavation activities resume. As discussed between Steve and OER, Artimus Construction plans to continue installing HP Soldier piles for the next week or two along the perimeter of the site. The installation process for the piles involves a wet drilling operation into bedrock that does not produce any dust because the material is saturated with water. Once excavation activities resume the CAMP Monitoring procedures will resume.**							
7:30								
8:00								
8:30								
9:00								
9:30								
10:00								
10:30								
11:00								
11:30								
12:00								
12:30								
13:00								
13:30								
14:00								
14:30								
15:00								
15:30								
16:00								
16:30								
17:00								

Locations:

A	Along 26th Street - North Property Line
B	East Property Line
C	South Property Line
D	West Property Line

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

NO PID Readings

Date: 10/5/11
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: Jason Cooper

TIME	LOCATION A	B	C	D	E	F
7:00	No excavation					
7:30	0.018	0.010	0.012	0.008		
8:00	No excavation					
8:30	No excavation					
9:00	No excavation					
9:30	No excavation					
10:00	No excavation					
10:30	0.028	0.074	0.021	0.044		
11:00						
11:30						
12:00						
12:30						
13:00						
13:30						
14:00						
14:30						
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

NO PID Readings

Date: 10/7/11
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: J.P

TIME	LOCATION A	B	C	D	E	F
7:00	0.036	0.010	0.015	0.007		
7:30	0.007	0.024	0.011	0.003		
8:00	NO excavation					
8:30	0.022	0.031	0.007	0.011		
9:00	0.015	0.016	0.027	0.012		
9:30	0.084	0.040	0.028	0.027		
10:00	0.020	0.017	0.009	0.029		
10:30	0.031	0.051	0.049	0.039		
11:00	0.025	0.036	0.028	0.024		
11:30	0.141	0.082	0.062	0.019		
12:00	NO excavation					
12:30	NO excavation					
13:00	0.089	0.069	0.042	0.033		
13:30	0.025	0.024	0.017	0.009		
14:00	Leave site					
14:30						
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

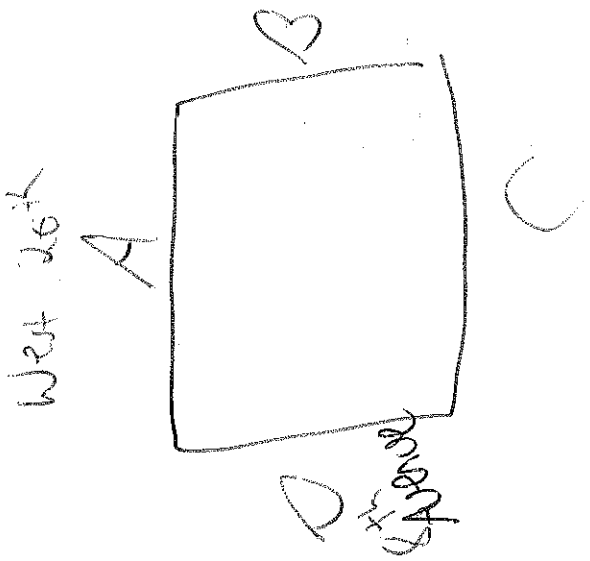

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

NO PID Readings

Date: 10/12/11
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: Jessica Presciá

TIME	LOCATION A	B	C	D	E	F
7:00	No excavation					
7:30	No excavation					
8:00	No excavation					
8:30	No excavation					
9:00	0.007	0.000	0.000	0.000		
9:30	0.003	0.009	0.002	0.000		
10:00	No excavation					
10:30	No excavation					
11:00	No excavation					
11:30						
12:00						
12:30						
13:00						
13:30						
14:00						
14:30						
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

Date: 10/19/11
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: Jessica Proscio

TIME	LOCATION A	B	C	D	E	F
7:00						
7:30						
8:00						
8:30						
9:00						
9:30						
10:00						
10:30						
11:00	NO Dust/VOC Monitoring Today Due to Rain All Day					
11:30						
12:00						
12:30						
13:00						
13:30						
14:00						
14:30						
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

NO PID Readings

Date: 10/21/11
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: JP

TIME	LOCATION A	B	C	D	E	F
7:00	0.166	0.12	0.29	0.003		
7:30	0.56	0.025	0.029	0.009		
8:00	0.000	0.001	0.000	0.007		
8:30	No Excavation					
9:00	0.000	0.000	0.000	0.000		
9:30	0.023	0.016	0.050	0.002		
10:00						
10:30						
11:00						
11:30						
12:00						
12:30	0.012	0.000	0.000	0.009		
13:00	0.016	0.002	0.006	0.007		
13:30	0.051	0.004	0.004	0.000		
14:00	0.022	0.022	0.023	0.002		
14:30	Leave Site					
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

No PID Readings

Date: 10/24/11
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: Jessica Provencia

TIME	LOCATION A	B	C	D	E	F
7:00	No excavation					
7:30	0.019	0.011	0.000	0.004		
8:00	0.002	0.000	0.001	0.001		
8:30	0.000	0.004	0.006	0.000		
9:00	0.005	0.032	0.005	0.002		
9:30	0.007	0.045	0.007	0.011		
10:00	0.001	0.000	0.002	0.000		
10:30	No excavation					
11:00	No excavation					
11:30	No excavation					
12:00	No excavation					
12:30	0.021	0.000	0.005	0.002		
13:00	0.033	0.003	0.002	0.000		
13:30	0.000	0.000	0.001	0.000		
14:00						
14:30						
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

Date: 10/26/11
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: JP

NO PID Readings

TIME	LOCATION A	B	C	D	E	F
7:00	0.029	0.000	0.004	0.007		
7:30	0.051	0.009	0.005	0.022		
8:00	0.031	0.017	0.015	0.039		
8:30	No excavation					
9:00	No excavation					
9:30	No excavation					
10:00	No excavation					
10:30	No excavation					
11:00	No excavation					
11:30	No excavation					
12:00	0.002	0.000	0.004	0.007		
12:30	0.022	0.004	0.001	0.026		
13:00	0.036	0.006	0.006	0.032		
13:30	0.024	0.021	0.005	0.034		
14:00	0.029	0.022	0.008	0.021		
14:30						
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

Date: 10/27/11
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: Jessica Pierra

TIME	LOCATION					
	A	B	C	D	E	F
7:00						
7:30						
8:00						
8:30						
9:00						
9:30	NO Dust/Voc monitoring Today					
10:00	Due to Rain All Day.					
10:30						
11:00						
11:30						
12:00						
12:30						
13:00						
13:30						
14:00						
14:30						
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

NO PID Readings

Date: 8/10/20/11
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: JT

TIME	LOCATION A	B	C	D	E	F
7:00	NO excavation					
7:30	NO excavation					
8:00	0.010	0.009	0.000	0.001		
8:30	0.025	0.019	0.007	0.009		
9:00	NO excavation					
9:30	NO excavation					
10:00	0.020	0.007	0.012	0.015		
10:30	NO excavation					
11:00	NO excavation					
11:30	NO excavation					
12:00	0.002	0.006	0.011	0.009		
12:30	0.007	0.011	0.023	0.007		
13:00	0.025	0.009	0.012	0.011		
13:30	0.008	0.025	0.026	0.033		
14:00	0.029	0.026	0.025	0.031		
14:30	0.019	0.007	0.013	0.022		
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

Date: 10/21/11

NO PID Readings

Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: JP

TIME	LOCATION A	B	C	D	E	F
7:00	0.166	0.12	0.29	0.003		
7:30	0.56	0.025	0.029	0.009		
8:00	0.000	0.001	0.000	0.007		
8:30	No excavation					
9:00	0.000	0.000	0.000	0.000		
9:30	0.023	0.016	0.050	0.002		
10:00						
10:30						
11:00						
11:30						
12:00						
12:30	0.012	0.000	0.000	0.009		
13:00	0.016	0.002	0.006	0.007		
13:30	0.051	0.004	0.004	0.000		
14:00	0.022	0.022	0.023	0.002		
14:30	Leave Site					
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

NO PID Readings

Date: 10/25/11
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: JP

TIME	LOCATION A	B	C	D	E	F
7:00	0.009	0.007	0.025	0.000		
7:30	0.011	0.002	0.012	0.001		
8:00	0.023	0.011	0.026	0.007		
8:30	0.026	0.001	0.000	0.003		
9:00	0.000	0.029	0.000	0.032		
9:30	No excavation					
10:00	No excavation					
10:30	No excavation					
11:00	No excavation					
11:30	No excavation					
12:00	0.022	0.025	0.056	0.001		
12:30	0.032	0.029	0.029	0.006		
13:00	0.018	0.011	0.036	0.023		
13:30	0.056	0.007	0.033	0.022		
14:00	0.011	0.003	0.009	0.051		
14:30	0.009	0.000	0.007	0.027		
15:00	End of day					
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

Date: 10/26/11
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: JP

NO PID Readings

TIME	LOCATION A	B	C	D	E	F
7:00	0.039	0.000	0.004	0.007		
7:30	0.051	0.009	0.006	0.022		
8:00	0.031	0.017	0.015	0.039		
8:30	No excavation					
9:00	No excavation					
9:30	No excavation					
10:00	No excavation					
10:30	No excavation					
11:00	No excavation					
11:30	No excavation					
12:00	0.002	0.000	0.004	0.007		
12:30	0.022	0.004	0.001	0.026		
13:00	0.036	0.006	0.006	0.032		
13:30	0.024	0.021	0.005	0.034		
14:00	0.029	0.022	0.008	0.021		
14:30						
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

NO PID Readings

Date: 11/1/11
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: JP

TIME	LOCATION A	B	C	D	E	F
7:00	0.029	0.001	0.000	0.012		
7:30	0.045	0.011	0.041	0.027		
8:00	0.000	0.023	0.036	0.021		
8:30	0.006	0.039	0.033	0.008		
9:00	0.002	0.063	0.000	0.006		
9:30						
10:00						
10:30						
11:00						
11:30						
12:00						
12:30						
13:00						
13:30						
14:00						
14:30						
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

NO PID Readings

Date: 11/2/11
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: JP

TIME	LOCATION A	B	C	D	E	F
7:00	No excavation					
7:30	0.001	0.003	0.021	0.004		
8:00	0.000	0.006	0.000	0.001		
8:30	No excavation					
9:00	No excavation					
9:30	No excavation					
10:00	0.021	0.000	0.004	0.003		
10:30	0.000	0.006	0.001	0.003		
11:00	No excavation					
11:30	No excavation					
12:00	No excavation					
12:30	No excavation					
13:00	No excavation					
13:30	0.029	0.002	0.004	0.003		
14:00	0.008	0.001	0.021	0.002		
14:30	0.004	0.021	0.003	0.000		
15:00	0.003	0.002	0.002	0.002		
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

NO PID Readings

Date: 11/3/11
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: JF

TIME	LOCATION A	B	C	D	E	F
7:00						
7:30						
8:00						
8:30						
9:00	0.001	0.021	0.032	0.001		
9:30	0.004	0.000	0.031	0.003		
10:00	0.003	0.026	0.000	0.004		
10:30						
11:00						
11:30	0.006	0.000	0.004	0.003		
12:00	NO Excavation					
12:30	NO excavation					
13:00	NO excavation					
13:30	0.000	0.021	0.003	0.000		
14:00	0.002	0.000	0.002	0.004		
14:30	0.001	0.023	0.002	0.003		
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

NO PID Readings

Date: 11/4/11
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: JP

TIME	LOCATION A	B	C	D	E	F
7:00	0.011	0.029	0.009	0.007		
7:30	0.023	0.054	0.005	0.012		
8:00	NO excavation					
8:30	NO excavation					
9:00	NO excavation					
9:30	No excavation					
10:00	Leave Site					
10:30						
11:00						
11:30						
12:00						
12:30						
13:00						
13:30						
14:00						
14:30						
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

NO PID Readings

Date: 11/15/11
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: JP

TIME	LOCATION A	B	C	D	E	F
7:00	0.007	0.000	0.002	0.000		
7:30	0.011	0.029	0.000	0.023		
8:00	0.032	0.045	0.001	0.019		
8:30	No Excavation					
9:00	No Excavation					
9:30	0.017	0.019	0.003	0.000		
10:00	0.007	0.007	0.000	0.007		
10:30	No Excavation					
11:00	No Excavation					
11:30	No Excavation					
12:00	No Excavation					
12:30	No Excavation					
13:00	No Excavation					
13:30	No Excavation					
14:00	0.025	0.021	0.026	0.017		
14:30	0.031	0.018	0.000	0.014		
15:00	0.045	0.000	0.025	0.000		
15:30	End of day					
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

NO PID Readings

Date: 11/17/11
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: JF

TIME	LOCATION A	B	C	D	E	F
7:00	No excavation					
7:30	0.007	0.000	0.025	0.001		
8:00	No excavation					
8:30	No excavation					
9:00	No excavation					
9:30	0.026	0.003	0.003	0.007		
10:00	0.006	0.009	0.001	0.003		
10:30	No excavation					
11:00	Rain					
11:30						
12:00						
12:30						
13:00						
13:30						
14:00						
14:30						
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

NO PID Readings

Date: 11/18/11
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: JC

TIME	LOCATION A	B	C	D	E	F (PID)
7:00	0.0	0.004	0	0	0	0 n/a
7:30	0.0	0.013	0	0	0	0 "
8:00						
8:30	0.0	0.011	0.002	0.0	0.0	0 PID not "
9:00						
9:30	NO excavation stop monitor.					
10:00						
10:30						
11:00						
11:30						
12:00						
12:30						
13:00						
13:30						
14:00						
14:30						
15:00						
15:30						
16:00						
16:30						
17:00						

Start 740

1815 EY Stop

Locations:
A
B
C
D
E
F

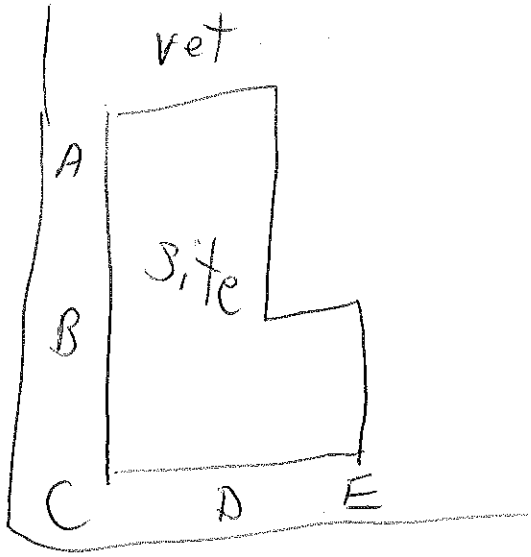

No wind observable in AA

Steel Materials CAT Rich

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

Date: 11/21/11
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: Jessica Proscia

TIME	LOCATION A	B	C	D	E	F
7:00	No Dust/Noc monitoring Today Due to Rain All Day.					
7:30						
8:00						
8:30						
9:00						
9:30						
10:00						
10:30						
11:00						
11:30						
12:00						
12:30						
13:00						
13:30						
14:00						
14:30						
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

Date: 12-06-11
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: Steve Malinowski CAMP

TIME	LOCATION A	B	C	D	E	F
7:00	0	0	0	0	0	0
7:30	0	0	0	0	0	0
8:00	0	0	0	0	0	0
8:30	830 - Excavation steps					
9:00						
9:30	NO excavation					
10:00		Vapor Barrier & Rebar + forms				
10:30						
11:00						
11:30						
12:00						
12:30						
13:00						
13:30	Start today Rain PID 0 →					
14:00						
14:30						
15:00	Stop loading at 245 →					
15:30						
16:00						
16:30						
17:00						

Rain stops 810 820 Rain again

Rain

Locations:
A NE
B N
C NW
D W
E SW
F

Start 7-pre ex. 715 start ex

PID only Raining

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

NO PID Readings

Date: 2/13/11
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: JP

TIME	LOCATION A	B	C	D	E	F
7:00	No excavation					
7:30	No excavation					
8:00	0.006	0.000	0.026	0.000		
8:30	0.004	0.021	0.023	0.001		
9:00	0.022	0.000	0.009	0.004		
9:30	No excavation					
10:00	No excavation					
10:30	No excavation					
11:00	No excavation					
11:30	No excavation					
12:00	No excavation					
12:30	No excavation					
13:00	0.009	0.000	0.000	0.007		
13:30	0.026	0.001	0.000	0.002		
14:00	0.034	0.001	0.000	0.006		
14:30	0.000	0.002	0.001	0.007		
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

NO PID Readings

Date: 12/14/11
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: JP

TIME	LOCATION A	B	C	D	E	F
7:00	NO excavation					
7:30	NO excavation					
8:00	0.045	0.032	0.000	0.001		
8:30	0.032	0.021	0.004	0.023		
9:00	0.021	0.019	0.009	0.021		
9:30	NO excavation					
10:00	NO excavation					
10:30	NO excavation					
11:00	NO excavation					
11:30	NO excavation					
12:00	NO excavation					
12:30	NO excavation					
13:00	0.026	0.012	0.010	0.000		
13:30	0.021	0.011	0.022	0.004		
14:00	0.006	0.012	0.029	0.022		
14:30						
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

NO PID Readings

Date: 12/15/11
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: JP

TIME	LOCATION A	B	C	D	E	F
7:00	No excavation					
7:30	0.042	0.039	0.000	0.004		
8:00	0.078	0.050	0.014	0.009		
8:30	0.017	0.013	0.002	0.021		
9:00	No excavation					
9:30	No excavation					
10:00	No excavation					
10:30	No excavation					
11:00	No excavation					
11:30	0.039	0.033	0.000	0.006		
12:00	0.035	0.000	0.000	0.004		
12:30	0.016	0.004	0.001	0.001		
13:00	0.014	0.002	0.041	0.003		
13:30	0.016	0.012	0.033	0.026		
14:00	0.012	0.016	0.017	0.043		
14:30	0.045	0.017	0.016	0.055		
15:00	0.032	0.039	0.000	0.000		
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

NO PID Readings

Date: 12/27/11
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: JP

TIME	LOCATION A	B	C	D	E	F
7:00	No Excavation					
7:30	0.000	0.000	0.000	0.000		
8:00	0.002	0.004	0.013	0.000		
8:30	No Excavation					
9:00	No Excavation					
9:30	No Excavation					
10:00	No Excavation					
10:30	No Excavation					
11:00	No Excavation					
11:30	No Excavation					
12:00	No Excavation					
12:30	No Excavation					
13:00	No Excavation					
13:30	0.001	0.004	0.026	0.045		
14:00	0.000	0.003	0.000	0.022		
14:30	0.006	0.022	0.019	0.031		
15:00	0.007	0.029	0.011	0.000		
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

NO PID Readings

Date: 12/28/11
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: JE

TIME	LOCATION A	B	C	D	E	F
7:00	NO excavation					
7:30	0.011	0.001	0.003	0.000		
8:00	0.000	0.000	0.002	0.001		
8:30	0.001	0.001	0.0014	0.002		
9:00	0.027	0.002	0.026	0.000		
9:30	NO excavation					
10:00	NO excavation					
10:30	NO excavation					
11:00	NO excavation					
11:30	NO excavation					
12:00	NO excavation					
12:30	NO excavation					
13:00	NO excavation					
13:30	0.004	0.041	0.002	0.004		
14:00	0.011	0.026	0.033	0.007		
14:30	0.017	0.000	0.000	0.000		
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

NO PID Readings

Date: 12/29/11
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: JP

TIME	LOCATION A	B	C	D	E	F
7:00	NO excavation					
7:30	0.007	0.009	0.027	0.000		
8:00	0.011	0.000	0.013	0.001		
8:30	0.012	0.006	0.042	0.004		
9:00	NO excavation					
9:30	NO excavation					
10:00	NO excavation					
10:30	NO excavation					
11:00	NO excavation					
11:30	NO excavation					
12:00	NO excavation					
12:30	NO excavation					
13:00	0.027	0.000	0.033	0.017		
13:30	0.016	0.007	0.030	0.029		
14:00	0.006	0.034	0.041	0.000		
14:30	0.041	0.003	0.017	0.000		
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

Date: 1/9/12
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: JP

NO PID Readings

TIME	LOCATION A	B	C	D	E	F
7:00	No excavation					
7:30	0.001	0.000	0.000	0.007		
8:00	0.000	0.023	0.000	0.001		
8:30	0.000	0.011	0.009	0.000		
9:00	No excavation					
9:30	No excavation					
10:00	No excavation					
10:30	No excavation					
11:00	No excavation					
11:30	No excavation					
12:00	No excavation					
12:30	0.002	0.052	0.007	0.045		
13:00	0.000	0.027	0.000	0.000		
13:30	0.001	0.000	0.001	0.007		
14:00	0.006	0.004	0.023	0.001		
14:30						
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

No PID Readings

Artimus
260 West 26th Street
New York, NY

Date: 1/10/12
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: J.P.

TIME	LOCATION A	B	C	D	E	F
7:00	No excavation					
7:30	No excavation					
8:00	0.009	0.003	0.004	0.003		
8:30	0.014	0.002	0.002	0.001		
9:00	0.002	0.002	0.011	0.000		
9:30	0.010	0.001	0.007	0.000		
10:00	No excavation					
10:30	No excavation					
11:00	No excavation					
11:30	No excavation					
12:00	0.008	0.000	0.010	0.009		
12:30	0.000	0.001	0.000	0.014		
13:00	0.004	0.023	0.000	0.000		
13:30	0.003	0.012	0.008	0.000		
14:00	0.002	0.010	0.001	0.001		
14:30	0.000	0.016	0.015	0.007		
15:00	0.000	0.011	0.010	0.003		
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

No PID readings

Date: 1/11/12
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: JF

TIME	LOCATION A	B	C	D	E	F
7:00	No excavation					
7:30	0.000	0.000	0.001	0.000		
8:00	0.000	0.000	0.011	0.006		
8:30	0.005	0.000	0.002	0.007		
9:00	0.003	0.004	0.004	0.000		
9:30	0.001	0.003	0.000	0.000		
10:00	No excavation					
10:30	No excavation					
11:00	No excavation					
11:30	No excavation					
12:00	No excavation					
12:30	No excavation					
13:00	No excavation					
13:30	0.000	0.000	0.000	0.000		
14:00						
14:30						
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

NO PID Readings

Date: 1/12/12
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: JT

TIME	LOCATION A	B	C	D	E	F
7:00	No excavation					
7:30	0.007	0.000	0.000	0.000		
8:00	0.001	0.000	0.004	0.021		
8:30	0.006	0.001	0.011	0.018		
9:00	0.004	0.007	0.023	0.000		
9:30	0.000	0.006	0.000	0.006		
10:00	0.004	0.000	0.001	0.002		
10:30	No excavation					
11:00	No excavation					
11:30	No excavation					
12:00	No excavation					
12:30	0.000	0.000	0.000	0.000		
13:00	0.002	0.000	0.001	0.000		
13:30	No excavation					
14:00	0.000	0.006	0.005	0.000		
14:30						
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

Date: 1/13/12
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: Jessica Prescig

TIME	LOCATION A	B	C	D	E	F
7:00	NO excavation					
7:30	NO excavation					
8:00	NO excavation					
8:30	NO excavation					
9:00	NO excavation					
9:30	NO excavation					
10:00	NO excavation					
10:30	NO excavation					
11:00	0.000	0.002	0.000	0.024		
11:30	0.004	0.009	0.011	0.032		
12:00	0.003	0.000	0.023	0.000		
12:30						
13:00						
13:30						
14:00						
14:30						
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

NO PID Readings

Date: 1/16/12
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: J.P

TIME	LOCATION A	B	C	D	E	F
7:00	No excavation					
7:30	0.001	0.011	0.018	0.000		
8:00	0.006	0.023	0.027	0.000		
8:30	0.011	0.000	0.016	0.000		
9:00	0.000	0.000	0.018	0.004		
9:30	0.002	0.000	0.000	0.003		
10:00						
10:30						
11:00						
11:30						
12:00						
12:30						
13:00						
13:30						
14:00						
14:30						
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

NO PID Readings

Date: 1/23/17
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: Jessica Prescia

TIME	LOCATION					
	A	B	C	D	E	F
7:00	No excavation					
7:30	No excavation					
8:00	No excavation					
8:30	No excavation		0.026	0.001		
9:00	0.004	0.009	0.045	0.007		
9:30	0.001	0.011	0.000	0.000		
10:00	0.023	0.008	0.000	0.029		
10:30	0.045	0.004	0.008	0.003		
11:00	0.007	0.000	0.001	0.003		
11:30	No excavation					
12:00	No excavation					
12:30	No excavation					
13:00	No excavation					
13:30						
14:00						
14:30						
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

No PID Readings

Artimus
260 West 26th Street
New York, NY

Date: 1/31/12
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: JP

TIME	LOCATION A	B	C	D	E	F
7:00	No excavation					
7:30	0.023	0.000	0.001	0.000		
8:00	0.000	0.000	0.000	0.000		
8:30	No excavation					
9:00	No excavation					
9:30	No excavation					
10:00	No excavation					
10:30	0.000	0.001	0.001	0.000		
11:00	0.000	0.004	0.002	0.009		
11:30	0.007	0.003	0.008	0.000		
12:00	0.007	0.000	0.000	0.000		
12:30	0.000	0.001	0.000	0.000		
13:00						
13:30						
14:00						
14:30						
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

NO PID Readings

Artimus
260 West 26th Street
New York, NY

Date: 2/3/12
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: JE

TIME	LOCATION A	B	C	D	E	F
7:00	No Excavation					
7:30	0.021	0.000	0.007	0.000		
8:00	0.000	0.000	0.007	0.000		
8:30	0.000	0.001	0.001	0.006		
9:00	0.001	0.011	0.006	0.000		
9:30	0.027	0.006	0.000	0.011		
10:00	0.032	0.029	0.000	0.000		
10:30	0.009	0.000	0.000	0.000		
11:00	0.000	0.000	0.000	0.000		
11:30						
12:00						
12:30						
13:00						
13:30						
14:00						
14:30						
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

NO PID Readings

Date: 2/13/12
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: JF

TIME	LOCATION A	B	C	D	E	F
7:00	No excavation					
7:30	0.000	0.000	0.002	0.003		
8:00	0.000	0.006	0.004	0.000		
8:30	0.001	0.004	0.000	0.001		
9:00	0.004	0.000	0.000	0.006		
9:30	0.039	0.026	0.007	0.000		
10:00	0.045	0.003	0.007	0.000		
10:30	No excavation					
11:00	No excavation					
11:30	0.000	0.006	0.001	0.006		
12:00	0.002	0.000	0.003	0.007		
12:30	0.005	0.000	0.004	0.008		
13:00	No excavation					
13:30	0.021	0.004	0.008	0.000		
14:00	0.000	0.000	0.000	0.000		
14:30						
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

Date: 2/14/12 NO PID Readings
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: JE

TIME	LOCATION A	B	C	D	E	F
7:00	No excavation					
7:30	0.000	0.001	0.000	0.007		
8:00	0.004	0.000	0.000	0.009		
8:30	0.022	0.039	0.000	0.003		
9:00	0.007	0.026	0.000	0.000		
9:30	0.000	0.000	0.001	0.000		
10:00	0.001	0.000	0.007	0.001		
10:30	0.026	0.011	0.007	0.000		
11:00	0.007	0.000	0.004	0.000		
11:30	0.004	0.029	0.003	0.023		
12:00						
12:30						
13:00						
13:30						
14:00						
14:30						
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

NO PID Readings

Date: 2/22/12
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: JP

TIME	LOCATION A	B	C	D	E	F
7:00	NO Excavation					
7:30	NO Excavation					
8:00	0.000	0.004	0.002	0.000		
8:30	0.007	0.000	0.025	0.009		
9:00	0.000	0.001	0.009	0.018		
9:30	0.001	0.023	0.000	0.011		
10:00	0.003	0.035	0.001	0.000		
10:30	0.000	0.000	0.000	0.000		
11:00	0.000	0.000	0.000	0.000		
11:30	0.006	0.000	0.000	0.000		
12:00	0.000	0.001	0.003	0.023		
12:30	0.001	0.007	0.006	0.000		
13:00	0.000	0.000	0.000	0.000		
13:30	0.021	0.000	0.001	0.000		
14:00	0.000	0.000	0.000	0.000		
14:30	0.000	0.000	0.000	0.000		
15:00	0.001	0.000	0.000	0.000		
15:30	0.006	0.000	0.036	0.000		
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

Dust Monitoring
(micrograms/cubic meter)

Artimus
260 West 26th Street
New York, NY

NO PID Readings

Date: 2/23/12
Meter Reading: PID (ppm)/Dust Meter ug/cubic meter
Person Conducting Monitoirng: JT

TIME	LOCATION A	B	C	D	E	F
7:00	No excavation					
7:30	No excavation					
8:00	No excavation					
8:30	0.014	0.006	0.000	0.000		
9:00	0.000	0.000	0.000	0.001		
9:30	0.001	0.000	0.001	0.000		
10:00	0.000	0.000	0.002	0.000		
10:30	No excavation					
11:00	No excavation					
11:30	0.007	0.004	0.004	0.000		
12:00						
12:30						
13:00						
13:30						
14:00						
14:30						
15:00						
15:30						
16:00						
16:30						
17:00						

Locations:
A
B
C
D
E
F

APPENDIX D

Project Photographs

Looking east across site prior to redevelopment

Looking down at Site prior to redevelopment

Gravel pad for truck wash.

Truck wash and inspection area

Air monitoirng during excavation

Soil excavation after lead soil removal

Visibly clean soil beneath asphalt of former spill location.

Loading of soil for off-site disposal

Soil excavation

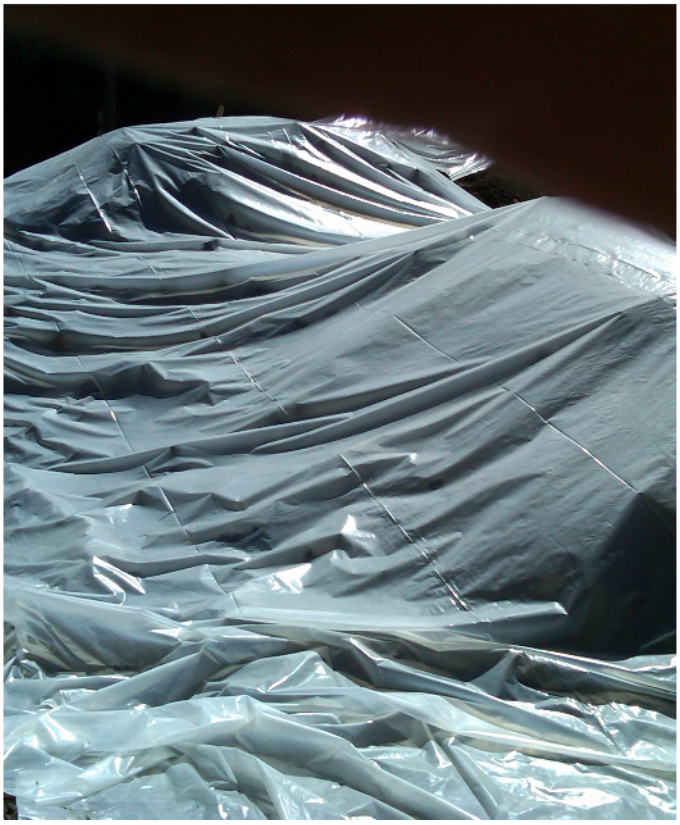

Soil stockpile awaiting disposal

Excavation of bedrock from bottom of excavation

Bedrock exposed along site perimeter

Based of excavation during bedrock removal

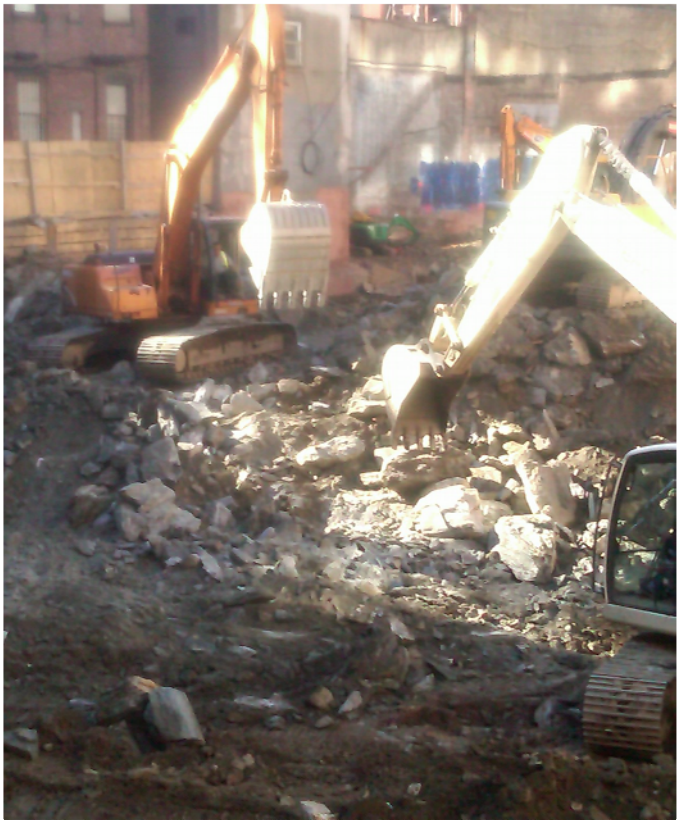

Bedrock excavation activities

Material staged on bedrock at base of excavation

Dewatering pump and filter in use after a rain event

Pooled water ontop of bedrock at base of excavation

Rock exposed at base of excavation in grids B1 and B2

Water-proofing membrane along east wall

Water-proofing membrane along north wall

Water-proofing membrane along east wall

water-proofing membrane covering base of the excavation

APPENDIX E

Laboratory Results for Soil Samples
Prior to Completing the Excavation

New Jersey ACCUTEST LABORATORIES

01/27/12

Technical Report for

C. A. Rich Consultants

Artimus', 260 West 26th Street, New York, NY

Accutest Job Number: JA97114

Sampling Date: 01/13/12

Report to:

SMalinowski@carichinc.com

ATTN: Distribution1

Total number of pages in report: **38**

Test results contained within this data package meet the requirements of the National Environmental Laboratory Accreditation Conference and/or state specific certification programs as applicable.

David N. Speis
VP, Laboratory Director

Client Service contact: Tony Esposito 732-329-0200

Certifications: NJ(12129), NY(10983), CA, CT, DE, FL, IL, IN, KS, KY, LA, MA, MD, MI, MT, NC, PA, RI, SC, TN, VA, WV

This report shall not be reproduced, except in its entirety, without the written approval of Accutest Laboratories. Test results relate only to samples analyzed.

Accutest Laboratories is the sole authority for authorizing edits or modifications to this document. Unauthorized modification of this report is strictly prohibited.

Sections: 1 2 3 4

Table of Contents

-1-

Section 1: Sample Summary **3**

Section 2: Case Narrative/Conformance Summary **4**

Section 3: Sample Results **7**

3.1: JA97114-1: EP-A1(14FT) 8

3.2: JA97114-2: EP-A3(14FT) 13

3.3: JA97114-3: EP-B2(14FT) 18

3.4: JA97114-4: EP-B2G(14FT) 23

3.5: JA97114-5: EP-X 24

3.6: JA97114-6: EP-XX 29

3.7: JA97114-7: FIELD BLANK 1/13/12 30

3.8: JA97114-8: TRIP BLANK 1/13/12 33

Section 4: Misc. Forms **34**

4.1: Chain of Custody 35

Sample Summary

C. A. Rich Consultants

Job No: JA97114

Artimus', 260 West 26th Street, New York, NY

Sample Number	Collected Date	Time	By	Received	Matrix Code	Type	Client Sample ID
JA97114-1	01/13/12	12:00	JP	01/14/12	SO	Soil	EP-A1(14FT)
JA97114-2	01/13/12	12:10	JP	01/14/12	SO	Soil	EP-A3(14FT)
JA97114-2D	01/13/12	12:13	JP	01/14/12	SO	Soil Dup/MSD	EP-A3MSD(14FT)
JA97114-2S	01/13/12	12:12	JP	01/14/12	SO	Soil Matrix Spike	EP-A3MS(14FT)
JA97114-3	01/13/12	12:45	JP	01/14/12	SO	Soil	EP-B2(14FT)
JA97114-4	01/13/12	12:55	JP	01/14/12	SO	Soil	EP-B2G(14FT)
JA97114-4D	01/13/12	12:57	JP	01/14/12	SO	Soil Dup/MSD	EP-B2GMSD(14FT)
JA97114-4S	01/13/12	12:56	JP	01/14/12	SO	Soil Matrix Spike	EP-B2GMS(14FT)
JA97114-5	01/13/12	12:05	JP	01/14/12	SO	Soil	EP-X
JA97114-6	01/13/12	13:00	JP	01/14/12	SO	Soil	EP-XX
JA97114-7	01/13/12	13:15	JP	01/14/12	AQ	Field Blank Soil	FIELD BLANK 1/13/12
JA97114-8	01/13/12	13:15	JP	01/14/12	AQ	Trip Blank Soil	TRIP BLANK 1/13/12

Soil samples reported on a dry weight basis unless otherwise indicated on result page.

CASE NARRATIVE / CONFORMANCE SUMMARY

Client:	C. A. Rich Consultants	**Job No**	JA97114
Site:	Artimus', 260 West 26th Street, New York, NY	**Report Date**	1/25/2012 4:10:19 PM

On 01/14/2012, 6 Sample(s), 1 Trip Blank(s) and 1 Field Blank(s) were received at Accutest Laboratories at a temperature of 2 C. Samples were intact and properly preserved, unless noted below. An Accutest Job Number of JA97114 was assigned to the project. Laboratory sample ID, client sample ID and dates of sample collection are detailed in the report's Results Summary Section.

Specified quality control criteria were achieved for this job except as noted below. For more information, please refer to the analytical results and QC summary pages.

Volatiles by GCMS By Method SW846 8260B

Matrix: AQ **Batch ID:** V2B4135

- All samples were analyzed within the recommended method holding time.
- All method blanks for this batch meet method specific criteria.
- Sample(s) JA97057-1MS, JA97057-1MSD were used as the QC samples indicated.

Matrix: SO **Batch ID:** VV5301

- All samples were analyzed within the recommended method holding time.
- Sample(s) JA97114-4MS, JA97114-4MSD were used as the QC samples indicated.
- All method blanks for this batch meet method specific criteria.

Extractables by GCMS By Method SW846 8270D

Matrix: SO **Batch ID:** OP54262

- All samples were extracted within the recommended method holding time.
- Sample(s) JA97114-2MS, JA97114-2MSD were used as the QC samples indicated.
- All method blanks for this batch meet method specific criteria.
- Blank Spike Recovery(s) for 3,3'-Dichlorobenzidine are outside control limits. Outside of in house control limits.
- RPD(s) for MS/MSD for 4,6-Dinitro-o-cresol are outside control limits for sample OP54262-MSD. Outside control limits due to matrix interference.

Extractables by GC By Method SW846 8081B

Matrix: AQ **Batch ID:** OP54286

- All samples were extracted within the recommended method holding time.
- All method blanks for this batch meet method specific criteria.

Matrix: SO **Batch ID:** OP54255

- All samples were extracted within the recommended method holding time.
- Sample(s) JA97114-2MS, JA97114-2MSD were used as the QC samples indicated.
- All method blanks for this batch meet method specific criteria.
- JA97114-2 for 4,4'-DDD: More than 40 % RPD for detected concentrations between the two GC columns.
- JA97114-3 for gamma-Chlordane: More than 40 % RPD for detected concentrations between the two GC columns.
- JA97114-2 for 4,4'-DDE: More than 40 % RPD for detected concentrations between the two GC columns.
- JA97114-1 for gamma-Chlordane: More than 40 % RPD for detected concentrations between the two GC columns.
- JA97114-1 for alpha-Chlordane: Reported from 2nd signal due to interference on 1st signal.
- JA97114-3 for 4,4'-DDD: Reported from 2nd signal. %D of check on 1st signal excess method criteria (20 %) so using for confirmation only.

Metals By Method SW846 6010C

Matrix: AQ **Batch ID:** MP62282

- All samples were digested within the recommended method holding time.
- All method blanks for this batch meet method specific criteria.
- Sample(s) JA96826-1MS, JA96826-1MSD, JA96826-1SDL were used as the QC samples for metals.
- Matrix Spike Recovery(s) for Sodium are outside control limits. Spike amount low relative to the sample amount. Refer to lab control or spike blank for recovery information.
- RPD(s) for Serial Dilution for Antimony, Chromium, Copper, Lead, Magnesium, Nickel, Selenium, Silver, Zinc are outside control limits for sample MP62282-SD1. Percent difference acceptable due to low initial sample concentration (< 50 times IDL).
- MP62282-SD1 for Manganese: Serial dilution indicates possible matrix interference.
- MP62282-SD1 for Calcium: Serial dilution indicates possible matrix interference.

Matrix: SO **Batch ID:** MP62283

- All samples were digested within the recommended method holding time.
- All method blanks for this batch meet method specific criteria.
- Sample(s) JA97114-2SDL, JA97114-2MS, JA97114-2MSD were used as the QC samples for metals.
- Matrix Spike Recovery(s) for Antimony, Iron, Manganese, Zinc are outside control limits. Spike recovery indicates possible matrix interference and/or sample nonhomogeneity.
- Matrix Spike Duplicate Recovery(s) for Antimony, Chromium, Iron, Manganese are outside control limits. Spike recovery indicates possible matrix interference and/or sample nonhomogeneity.
- Matrix Spike Recovery(s) for Magnesium, Potassium are outside control limits. Spike amount low relative to the sample amount. Refer to lab control or spike blank for recovery information.
- RPD(s) for MS/MSD for Zinc are outside control limits for sample MP62283-S2. High rpd due to possible sample nonhomogeneity.
- RPD(s) for Serial Dilution for Cadmium are outside control limits for sample MP62283-SD1. Percent difference acceptable due to low initial sample concentration (< 50 times IDL).
- MP62283-SD1 for Iron: Serial dilution indicates possible matrix interference.

Metals By Method SW846 7470A

Matrix:	AQ	Batch ID:	MP62139

- All samples were digested within the recommended method holding time.
- All method blanks for this batch meet method specific criteria.
- Sample(s) JA95379-3MS, JA95379-3MSD were used as the QC samples for metals.

Metals By Method SW846 7471B

Matrix:	SO	Batch ID:	MP62287

- All samples were digested within the recommended method holding time.
- All method blanks for this batch meet method specific criteria.
- Sample(s) JA97114-2MS, JA97114-2MSD were used as the QC samples for metals.

Wet Chemistry By Method SM18 2540G

Matrix:	SO	Batch ID:	GN60475

- The data for SM18 2540G meets quality control requirements.

Matrix:	SO	Batch ID:	GN60478

- The data for SM18 2540G meets quality control requirements.

Matrix:	SO	Batch ID:	GN60488

- The data for SM18 2540G meets quality control requirements.

Accutest certifies that data reported for samples received, listed on the associated custody chain or analytical task order, were produced to specifications meeting Accutest's Quality System precision, accuracy and completeness objectives except as noted.

Estimated non-standard method measurement uncertainty data is available on request, based on quality control bias and implicit for standard methods. Acceptable uncertainty requires tested parameter quality control data to meet method criteria.

Accutest Laboratories is not responsible for data quality assumptions if partial reports are used and recommends that this report be used in its entirety. Data release is authorized by Accutest Laboratories indicated via signature on the report cover

Sample Results

Report of Analysis

Report of Analysis

Client Sample ID: EP-A1(14FT)
Lab Sample ID: JA97114-1
Matrix: SO - Soil
Method: SW846 8270D SW846 3550C
Project: Artimus', 260 West 26th Street, New York, NY

Date Sampled: 01/13/12
Date Received: 01/14/12
Percent Solids: 87.5

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	3E38981.D	1	01/18/12	OYA	01/17/12	OP54262	E3E1713
Run #2							

	Initial Weight	Final Volume
Run #1	35.7 g	1.0 ml
Run #2		

ABN TCL List (SOM0 1.1)

CAS No.	Compound	Result	RL	MDL	Units	Q
95-57-8	2-Chlorophenol	ND	160	32	ug/kg	
59-50-7	4-Chloro-3-methyl phenol	ND	160	32	ug/kg	
120-83-2	2,4-Dichlorophenol	ND	160	52	ug/kg	
105-67-9	2,4-Dimethylphenol	ND	160	54	ug/kg	
51-28-5	2,4-Dinitrophenol	ND	640	39	ug/kg	
534-52-1	4,6-Dinitro-o-cresol	ND	640	39	ug/kg	
95-48-7	2-Methylphenol	ND	64	36	ug/kg	
	3&4-Methylphenol	ND	64	41	ug/kg	
88-75-5	2-Nitrophenol	ND	160	34	ug/kg	
100-02-7	4-Nitrophenol	ND	320	54	ug/kg	
87-86-5	Pentachlorophenol	ND	320	55	ug/kg	
108-95-2	Phenol	ND	64	34	ug/kg	
58-90-2	2,3,4,6-Tetrachlorophenol	ND	160	33	ug/kg	
95-95-4	2,4,5-Trichlorophenol	ND	160	37	ug/kg	
88-06-2	2,4,6-Trichlorophenol	ND	160	30	ug/kg	
83-32-9	Acenaphthene	30.9	32	9.3	ug/kg	J
208-96-8	Acenaphthylene	ND	32	10	ug/kg	
98-86-2	Acetophenone	ND	160	5.6	ug/kg	
120-12-7	Anthracene	59.9	32	11	ug/kg	
1912-24-9	Atrazine	ND	160	6.3	ug/kg	
56-55-3	Benzo(a)anthracene	135	32	10	ug/kg	
50-32-8	Benzo(a)pyrene	122	32	9.8	ug/kg	
205-99-2	Benzo(b)fluoranthene	109	32	11	ug/kg	
191-24-2	Benzo(g,h,i)perylene	69.6	32	12	ug/kg	
207-08-9	Benzo(k)fluoranthene	83.9	32	12	ug/kg	
101-55-3	4-Bromophenyl phenyl ether	ND	64	12	ug/kg	
85-68-7	Butyl benzyl phthalate	ND	64	19	ug/kg	
92-52-4	1,1'-Biphenyl	ND	64	3.7	ug/kg	
100-52-7	Benzaldehyde	ND	160	7.4	ug/kg	
91-58-7	2-Chloronaphthalene	ND	64	9.9	ug/kg	
106-47-8	4-Chloroaniline	ND	160	10	ug/kg	
86-74-8	Carbazole	23.7	64	15	ug/kg	J

ND = Not detected MDL - Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID: EP-A1(14FT)
Lab Sample ID: JA97114-1
Matrix: SO - Soil
Method: SW846 8270D SW846 3550C
Project: Artimus', 260 West 26th Street, New York, NY

Date Sampled: 01/13/12
Date Received: 01/14/12
Percent Solids: 87.5

ABN TCL List (SOM0 1.1)

CAS No.	Compound	Result	RL	MDL	Units	Q
105-60-2	Caprolactam	ND	64	10	ug/kg	
218-01-9	Chrysene	126	32	11	ug/kg	
111-91-1	bis(2-Chloroethoxy)methane	ND	64	13	ug/kg	
111-44-4	bis(2-Chloroethyl)ether	ND	64	9.6	ug/kg	
108-60-1	bis(2-Chloroisopropyl)ether	ND	64	9.5	ug/kg	
7005-72-3	4-Chlorophenyl phenyl ether	ND	64	9.6	ug/kg	
121-14-2	2,4-Dinitrotoluene	ND	64	14	ug/kg	
606-20-2	2,6-Dinitrotoluene	ND	64	12	ug/kg	
91-94-1	3,3'-Dichlorobenzidine	ND	160	8.1	ug/kg	
53-70-3	Dibenzo(a,h)anthracene	15.6	32	11	ug/kg	J
132-64-9	Dibenzofuran	19.5	64	9.5	ug/kg	J
84-74-2	Di-n-butyl phthalate	ND	64	7.1	ug/kg	
117-84-0	Di-n-octyl phthalate	ND	64	16	ug/kg	
84-66-2	Diethyl phthalate	ND	64	11	ug/kg	
131-11-3	Dimethyl phthalate	ND	64	11	ug/kg	
117-81-7	bis(2-Ethylhexyl)phthalate	93.6	64	28	ug/kg	
206-44-0	Fluoranthene	306	32	14	ug/kg	
86-73-7	Fluorene	32.1	32	11	ug/kg	
118-74-1	Hexachlorobenzene	ND	64	10	ug/kg	
87-68-3	Hexachlorobutadiene	ND	32	8.9	ug/kg	
77-47-4	Hexachlorocyclopentadiene	ND	640	33	ug/kg	
67-72-1	Hexachloroethane	ND	160	8.9	ug/kg	
193-39-5	Indeno(1,2,3-cd)pyrene	62.5	32	11	ug/kg	
78-59-1	Isophorone	ND	64	8.6	ug/kg	
91-57-6	2-Methylnaphthalene	ND	64	18	ug/kg	
88-74-4	2-Nitroaniline	ND	160	14	ug/kg	
99-09-2	3-Nitroaniline	ND	160	13	ug/kg	
100-01-6	4-Nitroaniline	ND	160	12	ug/kg	
91-20-3	Naphthalene	24.9	32	8.7	ug/kg	J
98-95-3	Nitrobenzene	ND	64	9.3	ug/kg	
621-64-7	N-Nitroso-di-n-propylamine	ND	64	7.8	ug/kg	
86-30-6	N-Nitrosodiphenylamine	ND	160	19	ug/kg	
85-01-8	Phenanthrene	237	32	15	ug/kg	
129-00-0	Pyrene	253	32	12	ug/kg	
95-94-3	1,2,4,5-Tetrachlorobenzene	ND	160	9.8	ug/kg	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
367-12-4	2-Fluorophenol	75%		21-116%
4165-62-2	Phenol-d5	73%		19-117%

ND = Not detected MDL - Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	EP-A1(14FT)		
Lab Sample ID:	JA97114-1	**Date Sampled:**	01/13/12
Matrix:	SO - Soil	**Date Received:**	01/14/12
Method:	SW846 8270D SW846 3550C	**Percent Solids:**	87.5
Project:	Artimus', 260 West 26th Street, New York, NY		

ABN TCL List (SOM0 1.1)

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
118-79-6	2,4,6-Tribromophenol	79%		24-136%
4165-60-0	Nitrobenzene-d5	69%		21-122%
321-60-8	2-Fluorobiphenyl	70%		30-117%
1718-51-0	Terphenyl-d14	83%		31-129%

ND = Not detected MDL - Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID: EP-A1(14FT)
Lab Sample ID: JA97114-1
Matrix: SO - Soil
Method: SW846 8081B SW846 3545A
Project: Artimus', 260 West 26th Street, New York, NY

Date Sampled: 01/13/12
Date Received: 01/14/12
Percent Solids: 87.5

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	4G14008.D	1	01/18/12	CT	01/16/12	OP54255	G4G394
Run #2	4G14063.D	5	01/19/12	CT	01/16/12	OP54255	G4G395

	Initial Weight	Final Volume
Run #1	17.0 g	10.0 ml
Run #2	17.0 g	10.0 ml

Pesticide TCL List

CAS No.	Compound	Result	RL	MDL	Units	Q
309-00-2	Aldrin	ND	0.67	0.34	ug/kg	
319-84-6	alpha-BHC	ND	0.67	0.50	ug/kg	
319-85-7	beta-BHC	ND	0.67	0.47	ug/kg	
319-86-8	delta-BHC	ND	0.67	0.39	ug/kg	
58-89-9	gamma-BHC (Lindane)	ND	0.67	0.31	ug/kg	
5103-71-9	alpha-Chlordane [a]	2.6	0.67	0.44	ug/kg	
5103-74-2	gamma-Chlordane [b]	2.6	0.67	0.34	ug/kg	
60-57-1	Dieldrin	ND	0.67	0.52	ug/kg	
72-54-8	4,4'-DDD	6.3	0.67	0.34	ug/kg	
72-55-9	4,4'-DDE	10.6	0.67	0.40	ug/kg	
50-29-3	4,4'-DDT	82.7 [c]	3.4	2.5	ug/kg	
72-20-8	Endrin	ND	0.67	0.34	ug/kg	
1031-07-8	Endosulfan sulfate	ND	0.67	0.61	ug/kg	
7421-93-4	Endrin aldehyde	ND	0.67	0.64	ug/kg	
959-98-8	Endosulfan-I	ND	0.67	0.33	ug/kg	
33213-65-9	Endosulfan-II	ND	0.67	0.44	ug/kg	
76-44-8	Heptachlor	ND	0.67	0.41	ug/kg	
1024-57-3	Heptachlor epoxide	ND	0.67	0.33	ug/kg	
72-43-5	Methoxychlor	ND	1.3	0.47	ug/kg	
53494-70-5	Endrin ketone	ND	0.67	0.44	ug/kg	
8001-35-2	Toxaphene	ND	17	8.5	ug/kg	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
877-09-8	Tetrachloro-m-xylene	108%	99%	23-137%
877-09-8	Tetrachloro-m-xylene	102%	95%	23-137%
2051-24-3	Decachlorobiphenyl	114%	110%	22-160%
2051-24-3	Decachlorobiphenyl	108%	100%	22-160%

(a) Reported from 2nd signal due to interference on 1st signal.
(b) More than 40 % RPD for detected concentrations between the two GC columns.
(c) Result is from Run# 2

ND = Not detected MDL - Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	EP-A1(14FT)		
Lab Sample ID:	JA97114-1	**Date Sampled:**	01/13/12
Matrix:	SO - Soil	**Date Received:**	01/14/12
		Percent Solids:	87.5
Project:	Artimus', 260 West 26th Street, New York, NY		

Metals Analysis

Analyte	Result	RL	Units	DF	Prep	Analyzed	By	Method	Prep Method
Aluminum	6770	54	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Antimony	< 2.2	2.2	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Arsenic	< 2.2	2.2	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Barium	96.1	22	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Beryllium	0.35	0.22	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Cadmium	< 0.54	0.54	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Calcium	7290	540	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Chromium	17.6	1.1	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Cobalt	5.7	5.4	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Copper	14.1	2.7	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Iron	11500	54	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Lead	40.4	2.2	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Magnesium	4110	540	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Manganese	269	1.6	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Mercury	0.14	0.037	mg/kg	1	01/16/12	01/16/12	JW	SW846 7471B [1]	SW846 7471B [4]
Nickel	24.4	4.3	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Potassium	2750	1100	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Selenium	< 2.2	2.2	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Silver	< 0.54	0.54	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Sodium	< 1100	1100	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Thallium	< 1.1	1.1	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Vanadium	21.2	5.4	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Zinc	42.2	2.2	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]

(1) Instrument QC Batch: MA27781
(2) Instrument QC Batch: MA27784
(3) Prep QC Batch: MP62283
(4) Prep QC Batch: MP62287

RL = Reporting Limit

Report of Analysis

Client Sample ID: EP-A3(14FT)
Lab Sample ID: JA97114-2
Matrix: SO - Soil
Method: SW846 8270D SW846 3550C
Project: Artimus', 260 West 26th Street, New York, NY

Date Sampled: 01/13/12
Date Received: 01/14/12
Percent Solids: 85.1

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	3E38982.D	1	01/18/12	OYA	01/17/12	OP54262	E3E1713
Run #2							

	Initial Weight	Final Volume
Run #1	35.1 g	1.0 ml
Run #2		

ABN TCL List (SOM0 1.1)

CAS No.	Compound	Result	RL	MDL	Units	Q
95-57-8	2-Chlorophenol	ND	170	34	ug/kg	
59-50-7	4-Chloro-3-methyl phenol	ND	170	33	ug/kg	
120-83-2	2,4-Dichlorophenol	ND	170	54	ug/kg	
105-67-9	2,4-Dimethylphenol	ND	170	56	ug/kg	
51-28-5	2,4-Dinitrophenol	ND	670	41	ug/kg	
534-52-1	4,6-Dinitro-o-cresol	ND	670	41	ug/kg	
95-48-7	2-Methylphenol	ND	67	38	ug/kg	
	3&4-Methylphenol	ND	67	43	ug/kg	
88-75-5	2-Nitrophenol	ND	170	35	ug/kg	
100-02-7	4-Nitrophenol	ND	330	57	ug/kg	
87-86-5	Pentachlorophenol	ND	330	57	ug/kg	
108-95-2	Phenol	ND	67	35	ug/kg	
58-90-2	2,3,4,6-Tetrachlorophenol	ND	170	34	ug/kg	
95-95-4	2,4,5-Trichlorophenol	ND	170	39	ug/kg	
88-06-2	2,4,6-Trichlorophenol	ND	170	31	ug/kg	
83-32-9	Acenaphthene	58.7	33	9.7	ug/kg	
208-96-8	Acenaphthylene	26.3	33	11	ug/kg	J
98-86-2	Acetophenone	ND	170	5.9	ug/kg	
120-12-7	Anthracene	146	33	12	ug/kg	
1912-24-9	Atrazine	ND	170	6.6	ug/kg	
56-55-3	Benzo(a)anthracene	304	33	11	ug/kg	
50-32-8	Benzo(a)pyrene	271	33	10	ug/kg	
205-99-2	Benzo(b)fluoranthene	256	33	11	ug/kg	
191-24-2	Benzo(g,h,i)perylene	168	33	12	ug/kg	
207-08-9	Benzo(k)fluoranthene	154	33	13	ug/kg	
101-55-3	4-Bromophenyl phenyl ether	ND	67	12	ug/kg	
85-68-7	Butyl benzyl phthalate	ND	67	19	ug/kg	
92-52-4	1,1'-Biphenyl	ND	67	3.9	ug/kg	
100-52-7	Benzaldehyde	ND	170	7.7	ug/kg	
91-58-7	2-Chloronaphthalene	ND	67	10	ug/kg	
106-47-8	4-Chloroaniline	ND	170	11	ug/kg	
86-74-8	Carbazole	72.0	67	16	ug/kg	

ND = Not detected MDL - Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID: EP-A3(14FT)
Lab Sample ID: JA97114-2
Matrix: SO - Soil
Method: SW846 8270D SW846 3550C
Project: Artimus', 260 West 26th Street, New York, NY

Date Sampled: 01/13/12
Date Received: 01/14/12
Percent Solids: 85.1

ABN TCL List (SOM0 1.1)

CAS No.	Compound	Result	RL	MDL	Units	Q
105-60-2	Caprolactam	ND	67	11	ug/kg	
218-01-9	Chrysene	291	33	11	ug/kg	
111-91-1	bis(2-Chloroethoxy)methane	ND	67	14	ug/kg	
111-44-4	bis(2-Chloroethyl)ether	ND	67	10	ug/kg	
108-60-1	bis(2-Chloroisopropyl)ether	ND	67	9.9	ug/kg	
7005-72-3	4-Chlorophenyl phenyl ether	ND	67	10	ug/kg	
121-14-2	2,4-Dinitrotoluene	ND	67	15	ug/kg	
606-20-2	2,6-Dinitrotoluene	ND	67	13	ug/kg	
91-94-1	3,3'-Dichlorobenzidine	ND	170	8.5	ug/kg	
53-70-3	Dibenzo(a,h)anthracene	40.2	33	11	ug/kg	
132-64-9	Dibenzofuran	51.6	67	9.9	ug/kg	J
84-74-2	Di-n-butyl phthalate	ND	67	7.4	ug/kg	
117-84-0	Di-n-octyl phthalate	ND	67	16	ug/kg	
84-66-2	Diethyl phthalate	ND	67	11	ug/kg	
131-11-3	Dimethyl phthalate	ND	67	12	ug/kg	
117-81-7	bis(2-Ethylhexyl)phthalate	133	67	30	ug/kg	
206-44-0	Fluoranthene	727	33	15	ug/kg	
86-73-7	Fluorene	73.9	33	11	ug/kg	
118-74-1	Hexachlorobenzene	ND	67	11	ug/kg	
87-68-3	Hexachlorobutadiene	ND	33	9.3	ug/kg	
77-47-4	Hexachlorocyclopentadiene	ND	670	34	ug/kg	
67-72-1	Hexachloroethane	ND	170	9.3	ug/kg	
193-39-5	Indeno(1,2,3-cd)pyrene	144	33	12	ug/kg	
78-59-1	Isophorone	ND	67	9.0	ug/kg	
91-57-6	2-Methylnaphthalene	31.1	67	19	ug/kg	J
88-74-4	2-Nitroaniline	ND	170	15	ug/kg	
99-09-2	3-Nitroaniline	ND	170	13	ug/kg	
100-01-6	4-Nitroaniline	ND	170	13	ug/kg	
91-20-3	Naphthalene	49.3	33	9.1	ug/kg	
98-95-3	Nitrobenzene	ND	67	9.7	ug/kg	
621-64-7	N-Nitroso-di-n-propylamine	ND	67	8.2	ug/kg	
86-30-6	N-Nitrosodiphenylamine	ND	170	20	ug/kg	
85-01-8	Phenanthrene	692	33	15	ug/kg	
129-00-0	Pyrene	640	33	13	ug/kg	
95-94-3	1,2,4,5-Tetrachlorobenzene	ND	170	10	ug/kg	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
367-12-4	2-Fluorophenol	65%		21-116%
4165-62-2	Phenol-d5	63%		19-117%

ND = Not detected MDL - Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	EP-A3(14FT)		
Lab Sample ID:	JA97114-2	**Date Sampled:**	01/13/12
Matrix:	SO - Soil	**Date Received:**	01/14/12
Method:	SW846 8270D SW846 3550C	**Percent Solids:**	85.1
Project:	Artimus', 260 West 26th Street, New York, NY		

ABN TCL List (SOM0 1.1)

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
118-79-6	2,4,6-Tribromophenol	75%		24-136%
4165-60-0	Nitrobenzene-d5	63%		21-122%
321-60-8	2-Fluorobiphenyl	66%		30-117%
1718-51-0	Terphenyl-d14	79%		31-129%

ND = Not detected MDL - Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	EP-A3(14FT)		
Lab Sample ID:	JA97114-2	**Date Sampled:**	01/13/12
Matrix:	SO - Soil	**Date Received:**	01/14/12
Method:	SW846 8081B SW846 3545A	**Percent Solids:**	85.1
Project:	Artimus', 260 West 26th Street, New York, NY		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	4G14009.D	1	01/18/12	CT	01/16/12	OP54255	G4G394
Run #2							

	Initial Weight	Final Volume
Run #1	17.1 g	10.0 ml
Run #2		

Pesticide TCL List

CAS No.	Compound	Result	RL	MDL	Units	Q
309-00-2	Aldrin	ND	0.69	0.34	ug/kg	
319-84-6	alpha-BHC	ND	0.69	0.51	ug/kg	
319-85-7	beta-BHC	ND	0.69	0.48	ug/kg	
319-86-8	delta-BHC	ND	0.69	0.40	ug/kg	
58-89-9	gamma-BHC (Lindane)	ND	0.69	0.31	ug/kg	
5103-71-9	alpha-Chlordane	ND	0.69	0.45	ug/kg	
5103-74-2	gamma-Chlordane	ND	0.69	0.35	ug/kg	
60-57-1	Dieldrin	ND	0.69	0.53	ug/kg	
72-54-8	4,4'-DDD [a]	3.1	0.69	0.35	ug/kg	
72-55-9	4,4'-DDE [a]	4.5	0.69	0.41	ug/kg	
50-29-3	4,4'-DDT	16.8	0.69	0.50	ug/kg	
72-20-8	Endrin	ND	0.69	0.35	ug/kg	
1031-07-8	Endosulfan sulfate	ND	0.69	0.62	ug/kg	
7421-93-4	Endrin aldehyde	ND	0.69	0.65	ug/kg	
959-98-8	Endosulfan-I	ND	0.69	0.33	ug/kg	
33213-65-9	Endosulfan-II	ND	0.69	0.45	ug/kg	
76-44-8	Heptachlor	ND	0.69	0.42	ug/kg	
1024-57-3	Heptachlor epoxide	ND	0.69	0.34	ug/kg	
72-43-5	Methoxychlor	ND	1.4	0.49	ug/kg	
53494-70-5	Endrin ketone	ND	0.69	0.45	ug/kg	
8001-35-2	Toxaphene	ND	17	8.7	ug/kg	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
877-09-8	Tetrachloro-m-xylene	119%		23-137%
877-09-8	Tetrachloro-m-xylene	131%		23-137%
2051-24-3	Decachlorobiphenyl	155%		22-160%
2051-24-3	Decachlorobiphenyl	139%		22-160%

(a) More than 40 % RPD for detected concentrations between the two GC columns.

ND = Not detected MDL - Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID: EP-A3(14FT)
Lab Sample ID: JA97114-2
Matrix: SO - Soil
Project: Artimus', 260 West 26th Street, New York, NY

Date Sampled: 01/13/12
Date Received: 01/14/12
Percent Solids: 85.1

Metals Analysis

Analyte	Result	RL	Units	DF	Prep	Analyzed	By	Method	Prep Method
Aluminum	11300	55	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [4]
Antimony	< 2.2	2.2	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [3]	SW846 3050B [4]
Arsenic	2.4	2.2	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [4]
Barium	211	22	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [4]
Beryllium	0.41	0.22	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [4]
Cadmium	< 0.55	0.55	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [4]
Calcium	9900	550	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [4]
Chromium	22.4	1.1	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [4]
Cobalt	9.3	5.5	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [4]
Copper	35.0	2.8	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [4]
Iron	20600	55	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [4]
Lead	104	2.2	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [4]
Magnesium	6490	550	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [4]
Manganese	321	1.7	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [4]
Mercury	0.17	0.039	mg/kg	1	01/16/12	01/16/12	JW	SW846 7471B [1]	SW846 7471B [5]
Nickel	22.4	4.4	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [4]
Potassium	6440	1100	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [4]
Selenium	< 2.2	2.2	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [4]
Silver	< 0.55	0.55	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [4]
Sodium	< 1100	1100	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [4]
Thallium	< 1.1	1.1	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [4]
Vanadium	42.7	5.5	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [4]
Zinc	127	2.2	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [4]

(1) Instrument QC Batch: MA27781
(2) Instrument QC Batch: MA27784
(3) Instrument QC Batch: MA27791
(4) Prep QC Batch: MP62283
(5) Prep QC Batch: MP62287

RL = Reporting Limit

Report of Analysis

Client Sample ID: EP-B2(14FT)
Lab Sample ID: JA97114-3
Matrix: SO - Soil
Method: SW846 8270D SW846 3550C
Project: Artimus', 260 West 26th Street, New York, NY

Date Sampled: 01/13/12
Date Received: 01/14/12
Percent Solids: 87.5

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	3E38983.D	1	01/18/12	OYA	01/17/12	OP54262	E3E1713
Run #2							

	Initial Weight	Final Volume
Run #1	35.0 g	1.0 ml
Run #2		

ABN TCL List (SOM0 1.1)

CAS No.	Compound	Result	RL	MDL	Units	Q
95-57-8	2-Chlorophenol	ND	160	33	ug/kg	
59-50-7	4-Chloro-3-methyl phenol	ND	160	33	ug/kg	
120-83-2	2,4-Dichlorophenol	ND	160	53	ug/kg	
105-67-9	2,4-Dimethylphenol	ND	160	55	ug/kg	
51-28-5	2,4-Dinitrophenol	ND	650	40	ug/kg	
534-52-1	4,6-Dinitro-o-cresol	ND	650	40	ug/kg	
95-48-7	2-Methylphenol	ND	65	37	ug/kg	
	3&4-Methylphenol	ND	65	41	ug/kg	
88-75-5	2-Nitrophenol	ND	160	35	ug/kg	
100-02-7	4-Nitrophenol	ND	330	55	ug/kg	
87-86-5	Pentachlorophenol	ND	330	56	ug/kg	
108-95-2	Phenol	ND	65	34	ug/kg	
58-90-2	2,3,4,6-Tetrachlorophenol	ND	160	34	ug/kg	
95-95-4	2,4,5-Trichlorophenol	ND	160	38	ug/kg	
88-06-2	2,4,6-Trichlorophenol	ND	160	31	ug/kg	
83-32-9	Acenaphthene	52.5	33	9.5	ug/kg	
208-96-8	Acenaphthylene	28.4	33	10	ug/kg	J
98-86-2	Acetophenone	ND	160	5.7	ug/kg	
120-12-7	Anthracene	146	33	11	ug/kg	
1912-24-9	Atrazine	ND	160	6.4	ug/kg	
56-55-3	Benzo(a)anthracene	348	33	11	ug/kg	
50-32-8	Benzo(a)pyrene	314	33	10	ug/kg	
205-99-2	Benzo(b)fluoranthene	315	33	11	ug/kg	
191-24-2	Benzo(g,h,i)perylene	199	33	12	ug/kg	
207-08-9	Benzo(k)fluoranthene	180	33	12	ug/kg	
101-55-3	4-Bromophenyl phenyl ether	ND	65	12	ug/kg	
85-68-7	Butyl benzyl phthalate	ND	65	19	ug/kg	
92-52-4	1,1'-Biphenyl	ND	65	3.8	ug/kg	
100-52-7	Benzaldehyde	ND	160	7.5	ug/kg	
91-58-7	2-Chloronaphthalene	ND	65	10	ug/kg	
106-47-8	4-Chloroaniline	ND	160	10	ug/kg	
86-74-8	Carbazole	70.0	65	15	ug/kg	

ND = Not detected MDL - Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID: EP-B2(14FT)
Lab Sample ID: JA97114-3
Matrix: SO - Soil
Method: SW846 8270D SW846 3550C
Project: Artimus', 260 West 26th Street, New York, NY

Date Sampled: 01/13/12
Date Received: 01/14/12
Percent Solids: 87.5

ABN TCL List (SOM0 1.1)

CAS No.	Compound	Result	RL	MDL	Units	Q
105-60-2	Caprolactam	ND	65	10	ug/kg	
218-01-9	Chrysene	325	33	11	ug/kg	
111-91-1	bis(2-Chloroethoxy)methane	ND	65	13	ug/kg	
111-44-4	bis(2-Chloroethyl)ether	ND	65	9.8	ug/kg	
108-60-1	bis(2-Chloroisopropyl)ether	ND	65	9.7	ug/kg	
7005-72-3	4-Chlorophenyl phenyl ether	ND	65	9.8	ug/kg	
121-14-2	2,4-Dinitrotoluene	ND	65	14	ug/kg	
606-20-2	2,6-Dinitrotoluene	ND	65	12	ug/kg	
91-94-1	3,3'-Dichlorobenzidine	ND	160	8.3	ug/kg	
53-70-3	Dibenzo(a,h)anthracene	48.5	33	11	ug/kg	
132-64-9	Dibenzofuran	49.9	65	9.7	ug/kg	J
84-74-2	Di-n-butyl phthalate	ND	65	7.2	ug/kg	
117-84-0	Di-n-octyl phthalate	ND	65	16	ug/kg	
84-66-2	Diethyl phthalate	ND	65	11	ug/kg	
131-11-3	Dimethyl phthalate	ND	65	11	ug/kg	
117-81-7	bis(2-Ethylhexyl)phthalate	109	65	29	ug/kg	
206-44-0	Fluoranthene	813	33	14	ug/kg	
86-73-7	Fluorene	67.7	33	11	ug/kg	
118-74-1	Hexachlorobenzene	ND	65	11	ug/kg	
87-68-3	Hexachlorobutadiene	ND	33	9.1	ug/kg	
77-47-4	Hexachlorocyclopentadiene	ND	650	33	ug/kg	
67-72-1	Hexachloroethane	ND	160	9.1	ug/kg	
193-39-5	Indeno(1,2,3-cd)pyrene	178	33	11	ug/kg	
78-59-1	Isophorone	ND	65	8.8	ug/kg	
91-57-6	2-Methylnaphthalene	19.7	65	18	ug/kg	J
88-74-4	2-Nitroaniline	ND	160	14	ug/kg	
99-09-2	3-Nitroaniline	ND	160	13	ug/kg	
100-01-6	4-Nitroaniline	ND	160	13	ug/kg	
91-20-3	Naphthalene	30.7	33	8.9	ug/kg	J
98-95-3	Nitrobenzene	ND	65	9.4	ug/kg	
621-64-7	N-Nitroso-di-n-propylamine	ND	65	8.0	ug/kg	
86-30-6	N-Nitrosodiphenylamine	ND	160	19	ug/kg	
85-01-8	Phenanthrene	683	33	15	ug/kg	
129-00-0	Pyrene	687	33	13	ug/kg	
95-94-3	1,2,4,5-Tetrachlorobenzene	ND	160	10	ug/kg	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
367-12-4	2-Fluorophenol	58%		21-116%
4165-62-2	Phenol-d5	59%		19-117%

ND = Not detected MDL - Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	EP-B2(14FT)		
Lab Sample ID:	JA97114-3	**Date Sampled:**	01/13/12
Matrix:	SO - Soil	**Date Received:**	01/14/12
Method:	SW846 8270D SW846 3550C	**Percent Solids:**	87.5
Project:	Artimus', 260 West 26th Street, New York, NY		

ABN TCL List (SOM0 1.1)

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
118-79-6	2,4,6-Tribromophenol	74%		24-136%
4165-60-0	Nitrobenzene-d5	56%		21-122%
321-60-8	2-Fluorobiphenyl	61%		30-117%
1718-51-0	Terphenyl-d14	78%		31-129%

ND = Not detected MDL - Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	EP-B2(14FT)		
Lab Sample ID:	JA97114-3	**Date Sampled:**	01/13/12
Matrix:	SO - Soil	**Date Received:**	01/14/12
Method:	SW846 8081B SW846 3545A	**Percent Solids:**	87.5
Project:	Artimus', 260 West 26th Street, New York, NY		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	4G14012.D	1	01/18/12	CT	01/16/12	OP54255	G4G394
Run #2							

	Initial Weight	Final Volume
Run #1	17.2 g	10.0 ml
Run #2		

Pesticide TCL List

CAS No.	Compound	Result	RL	MDL	Units	Q
309-00-2	Aldrin	ND	0.66	0.33	ug/kg	
319-84-6	alpha-BHC	ND	0.66	0.50	ug/kg	
319-85-7	beta-BHC	ND	0.66	0.47	ug/kg	
319-86-8	delta-BHC	ND	0.66	0.39	ug/kg	
58-89-9	gamma-BHC (Lindane)	ND	0.66	0.30	ug/kg	
5103-71-9	alpha-Chlordane	2.4	0.66	0.43	ug/kg	
5103-74-2	gamma-Chlordane [a]	3.0	0.66	0.34	ug/kg	
60-57-1	Dieldrin	ND	0.66	0.51	ug/kg	
72-54-8	4,4'-DDD [b]	3.4	0.66	0.34	ug/kg	
72-55-9	4,4'-DDE	7.3	0.66	0.39	ug/kg	
50-29-3	4,4'-DDT	29.1	0.66	0.49	ug/kg	
72-20-8	Endrin	ND	0.66	0.34	ug/kg	
1031-07-8	Endosulfan sulfate	ND	0.66	0.60	ug/kg	
7421-93-4	Endrin aldehyde	ND	0.66	0.63	ug/kg	
959-98-8	Endosulfan-I	ND	0.66	0.32	ug/kg	
33213-65-9	Endosulfan-II	ND	0.66	0.44	ug/kg	
76-44-8	Heptachlor	ND	0.66	0.41	ug/kg	
1024-57-3	Heptachlor epoxide	ND	0.66	0.33	ug/kg	
72-43-5	Methoxychlor	ND	1.3	0.47	ug/kg	
53494-70-5	Endrin ketone	ND	0.66	0.43	ug/kg	
8001-35-2	Toxaphene	ND	17	8.4	ug/kg	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
877-09-8	Tetrachloro-m-xylene	106%		23-137%
877-09-8	Tetrachloro-m-xylene	98%		23-137%
2051-24-3	Decachlorobiphenyl	135%		22-160%
2051-24-3	Decachlorobiphenyl	123%		22-160%

(a) More than 40 % RPD for detected concentrations between the two GC columns.
(b) Reported from 2nd signal. %D of check on 1st signal excess method criteria (20 %) so using for confirmation only.

ND = Not detected MDL - Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID: EP-B2(14FT)
Lab Sample ID: JA97114-3
Matrix: SO - Soil
Project: Artimus', 260 West 26th Street, New York, NY

Date Sampled: 01/13/12
Date Received: 01/14/12
Percent Solids: 87.5

Metals Analysis

Analyte	Result	RL	Units	DF	Prep	Analyzed	By	Method	Prep Method
Aluminum	7510	59	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Antimony	< 2.4	2.4	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Arsenic	< 2.4	2.4	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Barium	136	24	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Beryllium	0.39	0.24	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Cadmium	< 0.59	0.59	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Calcium	6730	590	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Chromium	18.6	1.2	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Cobalt	6.6	5.9	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Copper	17.4	3.0	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Iron	13700	59	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Lead	55.4	2.4	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Magnesium	4170	590	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Manganese	322	1.8	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Mercury	0.20	0.038	mg/kg	1	01/16/12	01/16/12	JW	SW846 7471B [1]	SW846 7471B [4]
Nickel	21.7	4.7	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Potassium	3610	1200	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Selenium	< 2.4	2.4	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Silver	< 0.59	0.59	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Sodium	< 1200	1200	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Thallium	< 1.2	1.2	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Vanadium	26.7	5.9	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Zinc	58.2	2.4	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]

(1) Instrument QC Batch: MA27781
(2) Instrument QC Batch: MA27784
(3) Prep QC Batch: MP62283
(4) Prep QC Batch: MP62287

RL = Reporting Limit

Report of Analysis

Client Sample ID:	EP-B2G(14FT)		
Lab Sample ID:	JA97114-4	**Date Sampled:**	01/13/12
Matrix:	SO - Soil	**Date Received:**	01/14/12
Method:	SW846 8260B	**Percent Solids:**	89.2
Project:	Artimus', 260 West 26th Street, New York, NY		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	V123366.D	1	01/16/12	CL	n/a	n/a	VV5301
Run #2							

	Initial Weight
Run #1	4.5 g
Run #2	

VOA STARS List

CAS No.	Compound	Result	RL	MDL	Units	Q
71-43-2	Benzene	ND	1.2	0.17	ug/kg	
104-51-8	n-Butylbenzene	ND	6.2	0.29	ug/kg	
135-98-8	sec-Butylbenzene	ND	6.2	0.20	ug/kg	
98-06-6	tert-Butylbenzene	ND	6.2	0.17	ug/kg	
100-41-4	Ethylbenzene	0.35	1.2	0.18	ug/kg	J
98-82-8	Isopropylbenzene	ND	6.2	0.17	ug/kg	
99-87-6	p-Isopropyltoluene	3.8	6.2	0.37	ug/kg	J
1634-04-4	Methyl Tert Butyl Ether	ND	1.2	0.22	ug/kg	
91-20-3	Naphthalene	2.0	6.2	1.3	ug/kg	J
103-65-1	n-Propylbenzene	ND	6.2	0.43	ug/kg	
108-88-3	Toluene	ND	1.2	0.47	ug/kg	
95-63-6	1,2,4-Trimethylbenzene	ND	6.2	1.4	ug/kg	
108-67-8	1,3,5-Trimethylbenzene	ND	6.2	0.16	ug/kg	
	m,p-Xylene	0.80	1.2	0.39	ug/kg	J
95-47-6	o-Xylene	0.34	1.2	0.23	ug/kg	J
1330-20-7	Xylene (total)	1.1	1.2	0.23	ug/kg	J

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	106%		67-131%
17060-07-0	1,2-Dichloroethane-D4	95%		66-130%
2037-26-5	Toluene-D8	105%		76-125%
460-00-4	4-Bromofluorobenzene	100%		53-142%

ND = Not detected MDL - Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	EP-X		
Lab Sample ID:	JA97114-5	**Date Sampled:**	01/13/12
Matrix:	SO - Soil	**Date Received:**	01/14/12
Method:	SW846 8270D SW846 3550C	**Percent Solids:**	89.4
Project:	Artimus', 260 West 26th Street, New York, NY		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	3E38984.D	1	01/18/12	OYA	01/17/12	OP54262	E3E1713
Run #2							

	Initial Weight	Final Volume
Run #1	35.1 g	1.0 ml
Run #2		

ABN TCL List (SOM0 1.1)

CAS No.	Compound	Result	RL	MDL	Units	Q
95-57-8	2-Chlorophenol	ND	160	32	ug/kg	
59-50-7	4-Chloro-3-methyl phenol	ND	160	32	ug/kg	
120-83-2	2,4-Dichlorophenol	ND	160	51	ug/kg	
105-67-9	2,4-Dimethylphenol	ND	160	54	ug/kg	
51-28-5	2,4-Dinitrophenol	ND	640	39	ug/kg	
534-52-1	4,6-Dinitro-o-cresol	ND	640	39	ug/kg	
95-48-7	2-Methylphenol	ND	64	36	ug/kg	
	3&4-Methylphenol	ND	64	40	ug/kg	
88-75-5	2-Nitrophenol	ND	160	34	ug/kg	
100-02-7	4-Nitrophenol	ND	320	54	ug/kg	
87-86-5	Pentachlorophenol	ND	320	54	ug/kg	
108-95-2	Phenol	ND	64	33	ug/kg	
58-90-2	2,3,4,6-Tetrachlorophenol	ND	160	33	ug/kg	
95-95-4	2,4,5-Trichlorophenol	ND	160	37	ug/kg	
88-06-2	2,4,6-Trichlorophenol	ND	160	30	ug/kg	
83-32-9	Acenaphthene	ND	32	9.2	ug/kg	
208-96-8	Acenaphthylene	ND	32	10	ug/kg	
98-86-2	Acetophenone	ND	160	5.6	ug/kg	
120-12-7	Anthracene	15.9	32	11	ug/kg	J
1912-24-9	Atrazine	ND	160	6.3	ug/kg	
56-55-3	Benzo(a)anthracene	71.8	32	10	ug/kg	
50-32-8	Benzo(a)pyrene	67.4	32	9.7	ug/kg	
205-99-2	Benzo(b)fluoranthene	60.4	32	11	ug/kg	
191-24-2	Benzo(g,h,i)perylene	43.1	32	12	ug/kg	
207-08-9	Benzo(k)fluoranthene	44.4	32	12	ug/kg	
101-55-3	4-Bromophenyl phenyl ether	ND	64	12	ug/kg	
85-68-7	Butyl benzyl phthalate	ND	64	18	ug/kg	
92-52-4	1,1'-Biphenyl	ND	64	3.7	ug/kg	
100-52-7	Benzaldehyde	ND	160	7.3	ug/kg	
91-58-7	2-Chloronaphthalene	ND	64	9.9	ug/kg	
106-47-8	4-Chloroaniline	ND	160	10	ug/kg	
86-74-8	Carbazole	ND	64	15	ug/kg	

ND = Not detected MDL - Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID: EP-X
Lab Sample ID: JA97114-5
Matrix: SO - Soil
Method: SW846 8270D SW846 3550C
Project: Artimus', 260 West 26th Street, New York, NY

Date Sampled: 01/13/12
Date Received: 01/14/12
Percent Solids: 89.4

ABN TCL List (SOM0 1.1)

CAS No.	Compound	Result	RL	MDL	Units	Q
105-60-2	Caprolactam	ND	64	10	ug/kg	
218-01-9	Chrysene	64.1	32	11	ug/kg	
111-91-1	bis(2-Chloroethoxy)methane	ND	64	13	ug/kg	
111-44-4	bis(2-Chloroethyl)ether	ND	64	9.6	ug/kg	
108-60-1	bis(2-Chloroisopropyl)ether	ND	64	9.5	ug/kg	
7005-72-3	4-Chlorophenyl phenyl ether	ND	64	9.6	ug/kg	
121-14-2	2,4-Dinitrotoluene	ND	64	14	ug/kg	
606-20-2	2,6-Dinitrotoluene	ND	64	12	ug/kg	
91-94-1	3,3'-Dichlorobenzidine	ND	160	8.1	ug/kg	
53-70-3	Dibenzo(a,h)anthracene	ND	32	11	ug/kg	
132-64-9	Dibenzofuran	ND	64	9.5	ug/kg	
84-74-2	Di-n-butyl phthalate	ND	64	7.1	ug/kg	
117-84-0	Di-n-octyl phthalate	ND	64	16	ug/kg	
84-66-2	Diethyl phthalate	ND	64	11	ug/kg	
131-11-3	Dimethyl phthalate	ND	64	11	ug/kg	
117-81-7	bis(2-Ethylhexyl)phthalate	69.4	64	28	ug/kg	
206-44-0	Fluoranthene	131	32	14	ug/kg	
86-73-7	Fluorene	ND	32	10	ug/kg	
118-74-1	Hexachlorobenzene	ND	64	10	ug/kg	
87-68-3	Hexachlorobutadiene	ND	32	8.9	ug/kg	
77-47-4	Hexachlorocyclopentadiene	ND	640	33	ug/kg	
67-72-1	Hexachloroethane	ND	160	8.9	ug/kg	
193-39-5	Indeno(1,2,3-cd)pyrene	37.8	32	11	ug/kg	
78-59-1	Isophorone	ND	64	8.6	ug/kg	
91-57-6	2-Methylnaphthalene	ND	64	18	ug/kg	
88-74-4	2-Nitroaniline	ND	160	14	ug/kg	
99-09-2	3-Nitroaniline	ND	160	13	ug/kg	
100-01-6	4-Nitroaniline	ND	160	12	ug/kg	
91-20-3	Naphthalene	ND	32	8.7	ug/kg	
98-95-3	Nitrobenzene	ND	64	9.2	ug/kg	
621-64-7	N-Nitroso-di-n-propylamine	ND	64	7.8	ug/kg	
86-30-6	N-Nitrosodiphenylamine	ND	160	19	ug/kg	
85-01-8	Phenanthrene	72.6	32	14	ug/kg	
129-00-0	Pyrene	131	32	12	ug/kg	
95-94-3	1,2,4,5-Tetrachlorobenzene	ND	160	9.8	ug/kg	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
367-12-4	2-Fluorophenol	75%		21-116%
4165-62-2	Phenol-d5	78%		19-117%

ND = Not detected MDL - Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	EP-X		
Lab Sample ID:	JA97114-5	**Date Sampled:**	01/13/12
Matrix:	SO - Soil	**Date Received:**	01/14/12
Method:	SW846 8270D SW846 3550C	**Percent Solids:**	89.4
Project:	Artimus', 260 West 26th Street, New York, NY		

ABN TCL List (SOM0 1.1)

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
118-79-6	2,4,6-Tribromophenol	88%		24-136%
4165-60-0	Nitrobenzene-d5	66%		21-122%
321-60-8	2-Fluorobiphenyl	70%		30-117%
1718-51-0	Terphenyl-d14	89%		31-129%

ND = Not detected MDL - Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	EP-X		
Lab Sample ID:	JA97114-5	**Date Sampled:**	01/13/12
Matrix:	SO - Soil	**Date Received:**	01/14/12
Method:	SW846 8081B SW846 3545A	**Percent Solids:**	89.4
Project:	Artimus', 260 West 26th Street, New York, NY		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	4G14013.D	1	01/18/12	CT	01/16/12	OP54255	G4G394
Run #2							

	Initial Weight	Final Volume
Run #1	17.0 g	10.0 ml
Run #2		

Pesticide TCL List

CAS No.	Compound	Result	RL	MDL	Units	Q
309-00-2	Aldrin	ND	0.66	0.33	ug/kg	
319-84-6	alpha-BHC	ND	0.66	0.49	ug/kg	
319-85-7	beta-BHC	ND	0.66	0.46	ug/kg	
319-86-8	delta-BHC	ND	0.66	0.38	ug/kg	
58-89-9	gamma-BHC (Lindane)	ND	0.66	0.30	ug/kg	
5103-71-9	alpha-Chlordane	3.3	0.66	0.43	ug/kg	
5103-74-2	gamma-Chlordane	3.9	0.66	0.34	ug/kg	
60-57-1	Dieldrin	ND	0.66	0.51	ug/kg	
72-54-8	4,4'-DDD	1.6	0.66	0.34	ug/kg	
72-55-9	4,4'-DDE	3.8	0.66	0.39	ug/kg	
50-29-3	4,4'-DDT	18.2	0.66	0.48	ug/kg	
72-20-8	Endrin	ND	0.66	0.34	ug/kg	
1031-07-8	Endosulfan sulfate	ND	0.66	0.60	ug/kg	
7421-93-4	Endrin aldehyde	ND	0.66	0.62	ug/kg	
959-98-8	Endosulfan-I	ND	0.66	0.32	ug/kg	
33213-65-9	Endosulfan-II	ND	0.66	0.43	ug/kg	
76-44-8	Heptachlor	ND	0.66	0.40	ug/kg	
1024-57-3	Heptachlor epoxide	ND	0.66	0.32	ug/kg	
72-43-5	Methoxychlor	ND	1.3	0.46	ug/kg	
53494-70-5	Endrin ketone	ND	0.66	0.43	ug/kg	
8001-35-2	Toxaphene	ND	16	8.3	ug/kg	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
877-09-8	Tetrachloro-m-xylene	116%		23-137%
877-09-8	Tetrachloro-m-xylene	104%		23-137%
2051-24-3	Decachlorobiphenyl	123%		22-160%
2051-24-3	Decachlorobiphenyl	109%		22-160%

ND = Not detected MDL - Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	EP-X		
Lab Sample ID:	JA97114-5	**Date Sampled:**	01/13/12
Matrix:	SO - Soil	**Date Received:**	01/14/12
		Percent Solids:	89.4
Project:	Artimus', 260 West 26th Street, New York, NY		

Metals Analysis

Analyte	Result	RL	Units	DF	Prep	Analyzed	By	Method	Prep Method
Aluminum	6180	56	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Antimony	< 2.3	2.3	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Arsenic	< 2.3	2.3	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Barium	81.8	23	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Beryllium	0.32	0.23	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Cadmium	< 0.56	0.56	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Calcium	6020	560	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Chromium	17.7	1.1	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Cobalt	< 5.6	5.6	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Copper	10	2.8	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Iron	10900	56	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Lead	21.4	2.3	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Magnesium	3630	560	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Manganese	299	1.7	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Mercury	0.048	0.033	mg/kg	1	01/16/12	01/16/12	JW	SW846 7471B [1]	SW846 7471B [4]
Nickel	23.4	4.5	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Potassium	2890	1100	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Selenium	< 2.3	2.3	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Silver	< 0.56	0.56	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Sodium	< 1100	1100	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Thallium	< 1.1	1.1	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Vanadium	20.6	5.6	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]
Zinc	36.1	2.3	mg/kg	1	01/16/12	01/17/12	VC	SW846 6010C [2]	SW846 3050B [3]

(1) Instrument QC Batch: MA27781
(2) Instrument QC Batch: MA27784
(3) Prep QC Batch: MP62283
(4) Prep QC Batch: MP62287

RL = Reporting Limit

Report of Analysis

Client Sample ID:	EP-XX		
Lab Sample ID:	JA97114-6	**Date Sampled:**	01/13/12
Matrix:	SO - Soil	**Date Received:**	01/14/12
Method:	SW846 8260B	**Percent Solids:**	90.7
Project:	Artimus', 260 West 26th Street, New York, NY		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	V123367.D	1	01/16/12	CL	n/a	n/a	VV5301
Run #2							

	Initial Weight
Run #1	4.6 g
Run #2	

VOA STARS List

CAS No.	Compound	Result	RL	MDL	Units	Q
71-43-2	Benzene	ND	1.2	0.16	ug/kg	
104-51-8	n-Butylbenzene	ND	6.0	0.28	ug/kg	
135-98-8	sec-Butylbenzene	ND	6.0	0.19	ug/kg	
98-06-6	tert-Butylbenzene	ND	6.0	0.17	ug/kg	
100-41-4	Ethylbenzene	0.25	1.2	0.18	ug/kg	J
98-82-8	Isopropylbenzene	ND	6.0	0.16	ug/kg	
99-87-6	p-Isopropyltoluene	1.2	6.0	0.35	ug/kg	J
1634-04-4	Methyl Tert Butyl Ether	ND	1.2	0.21	ug/kg	
91-20-3	Naphthalene	1.8	6.0	1.3	ug/kg	J
103-65-1	n-Propylbenzene	ND	6.0	0.41	ug/kg	
108-88-3	Toluene	ND	1.2	0.45	ug/kg	
95-63-6	1,2,4-Trimethylbenzene	ND	6.0	1.3	ug/kg	
108-67-8	1,3,5-Trimethylbenzene	0.27	6.0	0.15	ug/kg	J
	m,p-Xylene	0.53	1.2	0.38	ug/kg	J
95-47-6	o-Xylene	0.26	1.2	0.22	ug/kg	J
1330-20-7	Xylene (total)	0.79	1.2	0.22	ug/kg	J

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	104%		67-131%
17060-07-0	1,2-Dichloroethane-D4	94%		66-130%
2037-26-5	Toluene-D8	106%		76-125%
460-00-4	4-Bromofluorobenzene	98%		53-142%

ND = Not detected MDL - Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	FIELD BLANK 1/13/12		
Lab Sample ID:	JA97114-7	**Date Sampled:**	01/13/12
Matrix:	AQ - Field Blank Soil	**Date Received:**	01/14/12
Method:	SW846 8260B	**Percent Solids:**	n/a
Project:	Artimus', 260 West 26th Street, New York, NY		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	2B91929.D	1	01/17/12	DR	n/a	n/a	V2B4135
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA STARS List

CAS No.	Compound	Result	RL	MDL	Units	Q
71-43-2	Benzene	ND	1.0	0.22	ug/l	
104-51-8	n-Butylbenzene	ND	5.0	0.33	ug/l	
135-98-8	sec-Butylbenzene	ND	5.0	0.20	ug/l	
98-06-6	tert-Butylbenzene	ND	5.0	0.24	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.21	ug/l	
98-82-8	Isopropylbenzene	ND	2.0	0.19	ug/l	
99-87-6	p-Isopropyltoluene	ND	5.0	0.19	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.18	ug/l	
91-20-3	Naphthalene	ND	5.0	0.68	ug/l	
103-65-1	n-Propylbenzene	ND	5.0	0.17	ug/l	
108-88-3	Toluene	ND	1.0	0.15	ug/l	
95-63-6	1,2,4-Trimethylbenzene	ND	2.0	0.18	ug/l	
108-67-8	1,3,5-Trimethylbenzene	ND	2.0	0.23	ug/l	
	m,p-Xylene	ND	1.0	0.32	ug/l	
95-47-6	o-Xylene	ND	1.0	0.17	ug/l	
1330-20-7	Xylene (total)	ND	1.0	0.17	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	96%		77-120%
17060-07-0	1,2-Dichloroethane-D4	99%		70-127%
2037-26-5	Toluene-D8	102%		79-120%
460-00-4	4-Bromofluorobenzene	104%		76-118%

ND = Not detected MDL - Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	FIELD BLANK 1/13/12		
Lab Sample ID:	JA97114-7	**Date Sampled:**	01/13/12
Matrix:	AQ - Field Blank Soil	**Date Received:**	01/14/12
Method:	SW846 8081B SW846 3510C	**Percent Solids:**	n/a
Project:	Artimus', 260 West 26th Street, New York, NY		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	1G70694.D	1	01/18/12	CT	01/17/12	OP54286	G1G2547
Run #2							

	Initial Volume	Final Volume
Run #1	1000 ml	10.0 ml
Run #2		

Pesticide TCL List

CAS No.	Compound	Result	RL	MDL	Units	Q
309-00-2	Aldrin	ND	0.010	0.0095	ug/l	
319-84-6	alpha-BHC	ND	0.010	0.0040	ug/l	
319-85-7	beta-BHC	ND	0.010	0.0038	ug/l	
319-86-8	delta-BHC	ND	0.010	0.0062	ug/l	
58-89-9	gamma-BHC (Lindane)	ND	0.010	0.0041	ug/l	
5103-71-9	alpha-Chlordane	ND	0.010	0.0050	ug/l	
5103-74-2	gamma-Chlordane	ND	0.010	0.0023	ug/l	
60-57-1	Dieldrin	ND	0.010	0.0033	ug/l	
72-54-8	4,4'-DDD	ND	0.010	0.0036	ug/l	
72-55-9	4,4'-DDE	ND	0.010	0.0030	ug/l	
50-29-3	4,4'-DDT	ND	0.010	0.0060	ug/l	
72-20-8	Endrin	ND	0.010	0.0064	ug/l	
1031-07-8	Endosulfan sulfate	ND	0.010	0.0064	ug/l	
7421-93-4	Endrin aldehyde	ND	0.010	0.0029	ug/l	
53494-70-5	Endrin ketone	ND	0.010	0.0041	ug/l	
959-98-8	Endosulfan-I	ND	0.010	0.0030	ug/l	
33213-65-9	Endosulfan-II	ND	0.010	0.0028	ug/l	
76-44-8	Heptachlor	ND	0.010	0.0084	ug/l	
1024-57-3	Heptachlor epoxide	ND	0.010	0.0038	ug/l	
72-43-5	Methoxychlor	ND	0.020	0.0082	ug/l	
8001-35-2	Toxaphene	ND	0.25	0.15	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
877-09-8	Tetrachloro-m-xylene	82%		26-145%
877-09-8	Tetrachloro-m-xylene	87%		26-145%
2051-24-3	Decachlorobiphenyl	74%		10-141%
2051-24-3	Decachlorobiphenyl	90%		10-141%

ND = Not detected MDL - Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID: FIELD BLANK 1/13/12
Lab Sample ID: JA97114-7
Matrix: AQ - Field Blank Soil
Project: Artimus', 260 West 26th Street, New York, NY

Date Sampled: 01/13/12
Date Received: 01/14/12
Percent Solids: n/a

Total Metals Analysis

Analyte	Result	RL	Units	DF	Prep	Analyzed	By	Method	Prep Method
Aluminum	< 200	200	ug/l	1	01/16/12	01/16/12	VC	SW846 6010C [1]	SW846 3010A [5]
Antimony	< 6.0	6.0	ug/l	1	01/16/12	01/16/12	VC	SW846 6010C [1]	SW846 3010A [5]
Arsenic	< 3.0	3.0	ug/l	1	01/16/12	01/16/12	VC	SW846 6010C [1]	SW846 3010A [5]
Barium	< 200	200	ug/l	1	01/16/12	01/16/12	VC	SW846 6010C [1]	SW846 3010A [5]
Beryllium	< 1.0	1.0	ug/l	1	01/16/12	01/16/12	VC	SW846 6010C [1]	SW846 3010A [5]
Cadmium	< 3.0	3.0	ug/l	1	01/16/12	01/16/12	VC	SW846 6010C [1]	SW846 3010A [5]
Calcium	< 5000	5000	ug/l	1	01/16/12	01/16/12	VC	SW846 6010C [1]	SW846 3010A [5]
Chromium	< 10	10	ug/l	1	01/16/12	01/16/12	VC	SW846 6010C [1]	SW846 3010A [5]
Cobalt	< 50	50	ug/l	1	01/16/12	01/16/12	VC	SW846 6010C [1]	SW846 3010A [5]
Copper	< 10	10	ug/l	1	01/16/12	01/16/12	VC	SW846 6010C [1]	SW846 3010A [5]
Iron	< 100	100	ug/l	1	01/16/12	01/16/12	VC	SW846 6010C [1]	SW846 3010A [5]
Lead	< 3.0	3.0	ug/l	1	01/16/12	01/16/12	VC	SW846 6010C [1]	SW846 3010A [5]
Magnesium	< 5000	5000	ug/l	1	01/16/12	01/16/12	VC	SW846 6010C [1]	SW846 3010A [5]
Manganese	< 15	15	ug/l	1	01/16/12	01/16/12	VC	SW846 6010C [1]	SW846 3010A [5]
Mercury	< 0.20	0.20	ug/l	1	01/16/12	01/16/12	MP	SW846 7470A [2]	SW846 7470A [4]
Nickel	< 10	10	ug/l	1	01/16/12	01/16/12	VC	SW846 6010C [1]	SW846 3010A [5]
Potassium	< 10000	10000	ug/l	1	01/16/12	01/16/12	VC	SW846 6010C [1]	SW846 3010A [5]
Selenium	< 10	10	ug/l	1	01/16/12	01/16/12	VC	SW846 6010C [1]	SW846 3010A [5]
Silver	< 10	10	ug/l	1	01/16/12	01/16/12	VC	SW846 6010C [1]	SW846 3010A [5]
Sodium	< 10000	10000	ug/l	1	01/16/12	01/16/12	VC	SW846 6010C [1]	SW846 3010A [5]
Thallium	< 2.0	2.0	ug/l	1	01/16/12	01/17/12	VC	SW846 6010C [3]	SW846 3010A [5]
Vanadium	< 50	50	ug/l	1	01/16/12	01/16/12	VC	SW846 6010C [1]	SW846 3010A [5]
Zinc	< 20	20	ug/l	1	01/16/12	01/16/12	VC	SW846 6010C [1]	SW846 3010A [5]

(1) Instrument QC Batch: MA27784
(2) Instrument QC Batch: MA27786
(3) Instrument QC Batch: MA27791
(4) Prep QC Batch: MP62139
(5) Prep QC Batch: MP62282

RL = Reporting Limit

Report of Analysis

Client Sample ID:	TRIP BLANK 1/13/12		
Lab Sample ID:	JA97114-8	**Date Sampled:**	01/13/12
Matrix:	AQ - Trip Blank Soil	**Date Received:**	01/14/12
Method:	SW846 8260B	**Percent Solids:**	n/a
Project:	Artimus', 260 West 26th Street, New York, NY		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	2B91930.D	1	01/17/12	DR	n/a	n/a	V2B4135
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA STARS List

CAS No.	Compound	Result	RL	MDL	Units	Q
71-43-2	Benzene	ND	1.0	0.22	ug/l	
104-51-8	n-Butylbenzene	ND	5.0	0.33	ug/l	
135-98-8	sec-Butylbenzene	ND	5.0	0.20	ug/l	
98-06-6	tert-Butylbenzene	ND	5.0	0.24	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.21	ug/l	
98-82-8	Isopropylbenzene	ND	2.0	0.19	ug/l	
99-87-6	p-Isopropyltoluene	ND	5.0	0.19	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.18	ug/l	
91-20-3	Naphthalene	ND	5.0	0.68	ug/l	
103-65-1	n-Propylbenzene	ND	5.0	0.17	ug/l	
108-88-3	Toluene	ND	1.0	0.15	ug/l	
95-63-6	1,2,4-Trimethylbenzene	ND	2.0	0.18	ug/l	
108-67-8	1,3,5-Trimethylbenzene	ND	2.0	0.23	ug/l	
	m,p-Xylene	ND	1.0	0.32	ug/l	
95-47-6	o-Xylene	ND	1.0	0.17	ug/l	
1330-20-7	Xylene (total)	ND	1.0	0.17	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	96%		77-120%
17060-07-0	1,2-Dichloroethane-D4	99%		70-127%
2037-26-5	Toluene-D8	102%		79-120%
460-00-4	4-Bromofluorobenzene	104%		76-118%

ND = Not detected MDL - Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

New Jersey ACCUTEST LABORATORIES

Misc. Forms

Custody Documents and Other Forms

Includes the following where applicable:

- Chain of Custody

ACCUTEST LABORATORIES

SO FB STB

CHAIN OF CUSTODY

2235 Route 130, Dayton, NJ 08810
Tel: 732-329-0200 FAX: 732-329-3499/3480
www.acutest.com

PAGE 1 OF 4

FED-EX Tracking # 7731 1591 7745 | Bottle Order Control #
Acutest Quote # | Acutest Job # JA97114

Client / Reporting Information

Company Name: Ca Rich Consultants
Street Address: 17 DuPont Street
City: Plainview State: NY Zip:
Project Contact: Steve Malinowski E-mail:
Phone #: (516) 576-8844 Fax #:
Sampler(s) Name(s): Jessica Prescia Phone #:

Project Information

Project Name: Artimus'
Street: 260 West 28th St
City: NY State: NY
Project #:
Client Purchase Order #:
Project Manager:
Attention:

Billing Information (if different from Report to)
Company Name:
Street Address:
City State Zip:

Requested Analysis (see TEST CODE sheet)

VOCs 8260 CP51 List | SVOCs 8270 PCBs PUBS | TAL Metals | Pesticides

Matrix Codes

DW - Drinking Water
GW - Ground Water
WW - Water
SW - Surface Water
SO - Soil
SL - Sludge
SED-Sediment
OI - Oil
LIQ - Other Liquid
AIR - Air
SOL - Other Solid
WP - Wipe
FB-Field Blank
EB-Equipment Blank
RB- Rinse Blank
TB-Trip Blank

Acutest Sample #	Field ID / Point of Collection	MEOH/DI Vial #	Collection Date	Collection Time	Sampled by	Matrix	# of bottles	Number of preserved Bottles: HCl	NaOH	HNO3	H2SO4	NONE	DI Water	MEOH	ENCORE	LAB USE ONLY
-1	EP-A1 (14ft)		1/13/12	12	JP	SO	1					X				
	EP-A3 (14ft)		1/13/12	12:10	JP	SO	1					1				EX94
-2	EP-A3MS (14ft)		1/13/12	12:12	JP	SO	1					1				19C6
	EP-A3MSD (14ft)		1/13/12	12:13	JP	SO	1					1				9055
-3	EP-B2 (14ft)		1/13/12	12:45	JP	SO	1					1				EX11
-4	EP-B2G (14ft)		1/13/12	12:55	JP	SO	2					1				AMET9
	EP-B2GMS (14ft)		1/13/12	12:56	JP	SO	2					1				429
	EP-B2GMSD (14ft)		1/13/12	12:57	JP	SO	2					1				
-5	EP-X		1/13/12	12:05	JP	SO	1					1				
-6	EP-XG		1/13/12	1:PM	JP	SO	2					1				
-7	Field Blank 1/13/12		1/13/12	1:15PM	JP	FB	5	2		1		2				VOCs only
-8	TRIP Blank 1/13/12		1/13/12		JP	TB	2					X				

Turnaround Time (Business days)

- [ ] Std. 15 Business Days
- [ ] Std. 10 Business Days (by Contract only)
- [ ] 10 Day RUSH
- [ ] 5 Day RUSH
- [ ] 3 Day EMERGENCY
- [x] 2 Day EMERGENCY
- [ ] 1 Day EMERGENCY

Emergency & Rush T/A data available VIA Lablink

Approved By (Accutest PM): / Date:

Data Deliverable Information

- [ ] Commercial "A" (Level 1)
- [ ] Commercial "B" (Level 2)
- [ ] FULLT1 (Level 3+4)
- [ ] NJ Reduced
- [ ] Commercial "C"
- [ ] NYASP Category A
- [x] NYASP Category B
- [ ] State Forms
- [ ] EDD Format
- [ ] Other

Commercial "A" = Results Only
Commercial "B" = Results + QC Summary
NJ Reduced = Results + QC Summary + Partial Raw data

Comments / Special Instructions

SMalinowski@CarichInc.com
• filled on 11/22/11 @ 0700
Please provide excel EDD with Comparison to Part 375 unrestricted-SCOs

Sample Custody must be documented below each time samples change possession, including courier delivery.

	Relinquished by Sampler:	Date Time:	Received By:	Relinquished By:	Date Time:	Received By:
1		1/13/12	Fed Ex	Fed Ex	1/14/12 0930	
2	Relinquished by Sampler:	Date Time:	Received By:	Relinquished By:	Date Time:	Received By:
3						
4	Relinquished by:	Date Time:	Received By:	Custody Seal #	Intact / Not Intact	Preserved where applicable: X (3 JC)
5						On Ice: X Cooler Temp: 2.0°C B

1B

(32)

JA97114: Chain of Custody
Page 1 of 4

JA97114
COE

ACCUTEST.

Sample Log-In Summary

Lab Name: Accutest Page 1 of 1

Received by (Print Name): Steve Cannon Log-in Date: 1/14/2012

Received by (Signature):

Case Number: N/A
SDG Number: N/A
SAS Number: N/A

REMARKS:

1. Custody Seal(s) Present/Absent* Intact/Broken
2. Custody Seal Numbers: N/A
3. Chain-of-Custody Records Present/Absent*
4. Contract Lab Sample Inform. Sheet (CLSIS) Present/Absent*
5. Airbill Airbill/Sticker Present/Absent*
6. Airbill No.: 7931 1591 7745
7. Sample Tags Present/Absent* Sample Tag Nos. Listed/Not Listed on Chain-of-Custody
8. Sample Condition Intact/Broken*/ Leaking
9. Does Information on custody rec., CLSIS, & sample tags agree Label + CoC Info. Agree Yes/No*
10. Date received at Lab: 1/14/2012
11. Time Received: 0930
12. Do aqueous VOC vials have headspace? Yes/No* N/A
13. Are preserved voc soil samples fully immersed in preservative? Yes/No* N/A

Sample Transfer

Fraction: See Internal
Area #:
By:
On: Chain of Custody

Contract BTSR and attach record of resolution
Reviewed By:
Date:

Logbook No.: N/A
Logbook Page No.: N/A

NYSDEC SAMPLE #	CORRESPONDING: SAMPLE TAG #	CORRESPONDING: ASSIGNED LAB #	REMARKS: CONDITION OF SAMPLE SHIPMENT, ETC.
N/A		JA97114-1	OK
N/A		-2	
N/A		-3	
N/A		-4	
N/A		-5	
N/A		-6	
N/A		-7	
N/A		-8	
N/A			
N/A			
N/A	

Accutest Laboratories Sample Receipt Summary

Accutest Job Number: JA97114 **Client:** CA RICH CONSULTANTS **Immediate Client Services Action Required:** No

Date / Time Received: 1/14/2012 0930 **Delivery Method:** FedEx **Client Service Action Required at Login:** Yes

Project: ARTIMUS **No. Coolers:** 1 **Airbill #'s:** 7931 1591 7745

Cooler Security

	Y	or	N		Y	or	N
1. Custody Seals Present:	☑		☐	3. COC Present:	☑		☐
2. Custody Seals Intact:	☑		☐	4. Smpl Dates/Time OK	☑		☐

Cooler Temperature

	Y	or	N
1. Temp criteria achieved:	☑		☐

2. Cooler temp verification: Bar Therm

3. Cooler media: Ice (Bag)

Quality Control Preservation

	Y	N	N/A
1. Trip Blank present / cooler:	☑	☐	☐
2. Trip Blank listed on COC:	☑	☐	☐
3. Samples preserved properly:	☑	☐	
4. VOCs headspace free:	☑	☐	☐

Sample Integrity - Documentation

	Y	or	N
1. Sample labels present on bottles:	☑		☐
2. Container labeling complete:	☑		☐
3. Sample container label / COC agree:	☑		☐

Sample Integrity - Condition

	Y	or	N
1. Sample recvd within HT:	☑		☐
2. All containers accounted for:	☑		☐

3. Condition of sample: Broken / Leaking

Sample Integrity - Instructions

	Y	N	N/A
1. Analysis requested is clear:	☑	☐	
2. Bottles received for unspecified tests	☐	☑	
3. Sufficient volume recvd for analysis:	☑	☐	
4. Compositing instructions clear:	☐	☐	☑
5. Filtering instructions clear:	☐	☐	☑

Comments

-2 "EP-A3 MS(14 FT)" REC'D BROKEN, SALVAGED IN SM.

Accutest Laboratories
V:732.329.0200

2235 US Highway 130
F: 732.329.3499

Dayton, New Jersey
www/accutest.com

JA97114: Chain of Custody
Page 3 of 4

Sample Receipt Summary - Problem Resolution

Accutest Job Number: JA97114

CSR: Tony Esposito **Response Date:** 1/16/2012

Response: Client notified. Use intact volumes if possible and proceed with all analysis.

Accutest Laboratories
V:732.329.0200

2235 US Highway 130
F: 732.329.3499

Dayton, New Jersey
www/accutest.com

JA97114: Chain of Custody
Page 4 of 4

New Jersey ACCUTEST LABORATORIES

03/08/12

Technical Report for

C. A. Rich Consultants

Artimus', 260 West 26th Street, New York, NY

Accutest Job Number: JA97713

Sampling Date: 01/23/12

Report to:

C. A. Rich Consultants

smalinowski@carichinc.com

ATTN: Steve Malinowski

Total number of pages in report: **10**

ACCREDITED IN ACCORDANCE WITH nelac

Test results contained within this data package meet the requirements of the National Environmental Laboratory Accreditation Conference and/or state specific certification programs as applicable.

Paul Ioannidis
Lab Director

Client Service contact: Tony Esposito 732-329-0200

Certifications: NJ(12129), NY(10983), CA, CT, DE, FL, IL, IN, KS, KY, LA, MA, MD, MI, MT, NC, OH VAP (CL0056), PA, RI, SC, TN, VA, WV

This report shall not be reproduced, except in its entirety, without the written approval of Accutest Laboratories. Test results relate only to samples analyzed.

Accutest Laboratories is the sole authority for authorizing edits or modifications to this document. Unauthorized modification of this report is strictly prohibited.

Sections: 1 2 3 4

Table of Contents

Section 1: Sample Summary **3**
Section 2: Case Narrative/Conformance Summary **4**
Section 3: Sample Results **5**
3.1: JA97713-1: GP-A1-1/23/12 (16FT) 6
Section 4: Misc. Forms **7**
4.1: Chain of Custody 8

Sample Summary

C. A. Rich Consultants

Job No: JA97713

Artimus', 260 West 26th Street, New York, NY

Sample Number	Collected Date	Time	By	Received	Matrix Code	Type	Client Sample ID
JA97713-1	01/23/12	12:30	JP	01/24/12	SO	Soil	GP-A1-1/23/12 (16FT)

Soil samples reported on a dry weight basis unless otherwise indicated on result page.

CASE NARRATIVE / CONFORMANCE SUMMARY

Client:	C. A. Rich Consultants	**Job No**	JA97713
Site:	Artimus', 260 West 26th Street, New York, NY	**Report Date**	1/31/2012 11:48:06 A

On 01/24/2012, 1 Sample(s), 0 Trip Blank(s) and 0 Field Blank(s) were received at Accutest Laboratories at a temperature of 4 C. Samples were intact and properly preserved, unless noted below. An Accutest Job Number of JA97713 was assigned to the project. Laboratory sample ID, client sample ID and dates of sample collection are detailed in the report's Results Summary Section.

Specified quality control criteria were achieved for this job except as noted below. For more information, please refer to the analytical results and QC summary pages.

Extractables by GC By Method SW846 8081B

Matrix: SO **Batch ID:** OP54429

- All samples were extracted within the recommended method holding time.
- All method blanks for this batch meet method specific criteria.
- Sample(s) JA97713-1MS, JA97713-1MSD, OP54429-MSMSD were used as the QC samples indicated.
- Matrix Spike Recovery(s) for 4,4'-DDT are outside control limits. Outside control limits due to high level in sample relative to spike amount.
- JA97713-1 for alpha-Chlordane: Reported from 2nd signal due to interference on 1st signal.

Wet Chemistry By Method SM18 2540G

Matrix: SO **Batch ID:** GN60838

- The data for SM18 2540G meets quality control requirements.

Accutest certifies that data reported for samples received, listed on the associated custody chain or analytical task order, were produced to specifications meeting Accutest's Quality System precision, accuracy and completeness objectives except as noted.

Estimated non-standard method measurement uncertainty data is available on request, based on quality control bias and implicit for standard methods. Acceptable uncertainty requires tested parameter quality control data to meet method criteria.

Accutest Laboratories is not responsible for data quality assumptions if partial reports are used and recommends that this report be used in its entirety. Data release is authorized by Accutest Laboratories indicated via signature on the report cover

Sample Results

Report of Analysis

Report of Analysis

Client Sample ID:	GP-A1-1/23/12 (16FT)		
Lab Sample ID:	JA97713-1	**Date Sampled:**	01/23/12
Matrix:	SO - Soil	**Date Received:**	01/24/12
Method:	SW846 8081B SW846 3545A	**Percent Solids:**	89.7
Project:	Artimus', 260 West 26th Street, New York, NY		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	1G70920.D	1	01/26/12	DS	01/25/12	OP54429	G1G2556
Run #2	1G70941.D	4	01/26/12	DS	01/25/12	OP54429	G1G2556

	Initial Weight	Final Volume
Run #1	17.1 g	10.0 ml
Run #2	17.1 g	10.0 ml

Pesticide TCL List

CAS No.	Compound	Result	RL	MDL	Units	Q
309-00-2	Aldrin	ND	0.65	0.33	ug/kg	
319-84-6	alpha-BHC	ND	0.65	0.49	ug/kg	
319-85-7	beta-BHC	ND	0.65	0.46	ug/kg	
319-86-8	delta-BHC	ND	0.65	0.38	ug/kg	
58-89-9	gamma-BHC (Lindane)	ND	0.65	0.30	ug/kg	
5103-71-9	alpha-Chlordane [a]	2.8	0.65	0.42	ug/kg	
5103-74-2	gamma-Chlordane	2.6	0.65	0.33	ug/kg	
60-57-1	Dieldrin	ND	0.65	0.50	ug/kg	
72-54-8	4,4'-DDD	2.2	0.65	0.33	ug/kg	
72-55-9	4,4'-DDE	5.6	0.65	0.38	ug/kg	
50-29-3	4,4'-DDT	57.4 [b]	2.6	1.9	ug/kg	
72-20-8	Endrin	ND	0.65	0.33	ug/kg	
1031-07-8	Endosulfan sulfate	ND	0.65	0.59	ug/kg	
7421-93-4	Endrin aldehyde	ND	0.65	0.62	ug/kg	
959-98-8	Endosulfan-I	ND	0.65	0.32	ug/kg	
33213-65-9	Endosulfan-II	ND	0.65	0.43	ug/kg	
76-44-8	Heptachlor	ND	0.65	0.40	ug/kg	
1024-57-3	Heptachlor epoxide	ND	0.65	0.32	ug/kg	
72-43-5	Methoxychlor	ND	1.3	0.46	ug/kg	
53494-70-5	Endrin ketone	ND	0.65	0.42	ug/kg	
8001-35-2	Toxaphene	ND	16	8.2	ug/kg	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
877-09-8	Tetrachloro-m-xylene	68%	88%	23-137%
877-09-8	Tetrachloro-m-xylene	66%	87%	23-137%
2051-24-3	Decachlorobiphenyl	49%	71%	22-160%
2051-24-3	Decachlorobiphenyl	87%	90%	22-160%

(a) Reported from 2nd signal due to interference on 1st signal.
(b) Result is from Run# 2

ND = Not detected MDL - Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

New Jersey ACCUTEST LABORATORIES

Misc. Forms

Custody Documents and Other Forms

Includes the following where applicable:

- Chain of Custody

ACCUTEST

CHAIN OF CUSTODY

FRESH PONDS CORPORATE VILLAGE, BUILDING B
2235 ROUTE 130, DAYTON, NJ 08810
908-329-0200 FAX: 908-329-3499/3480

ACCUTEST JOB #: JA97713
ACCUTEST QUOTE #:

CLIENT INFORMATION

NAME: CaRich Consultants, INC
ADDRESS: 17 DuPont Street
CITY: Plainview STATE: NY ZIP: 11803
SEND REPORT TO: Smalinowski@CaRichInc.com
PHONE #: (516) 576-8849

FACILITY INFORMATION

PROJECT NAME: Artimus
LOCATION: 260 West 26th Street NY, NY
PROJECT NO.:
FAX #:

ANALYTICAL INFORMATION

Pesticides

MATRIX CODES

DW - DRINKING WATER
GW - GROUND WATER
WW - WASTE WATER
SO - SOIL
SL - SLUDGE
OI - OIL
LIQ - OTHER LIQUID
SOL - OTHER SOLID

ACCUTEST SAMPLE #	FIELD ID / POINT OF COLLECTION	COLLECTION DATE	COLLECTION TIME	SAMPLED BY:	MATRIX	# OF BOTTLES	PRESERVATION HCl	NaOH	HNO3	H2SO4	NONE	Pesticides	LAB USE ONLY
-1	EP-A1-1123112 (16ft)	11/23/12	12:30	JP	S	1					1	X	UTC 6

DATA TURNAROUND INFORMATION

- ☐ 21 DAYS STANDARD
- ☐ 14 DAYS *RUSH*
- ☐ 7 DAYS *EMERGENCY*
- ☐ OTHER

APPROVED BY: 2day!

21 DAY TURNAROUND HARDCOPY. EMERGENCY OR RUSH IS FAX DATA UNLESS PREVIOUSLY APPROVED

DATA DELIVERABLE INFORMATION

- ☐ NJ REDUCED
- ☐ NJ Full
- ☐ FULL CLP
- ☐ DISK DELIVERABLE
- ☐ OTHER (SPECIFY) ASP Cat B
- ☐ COMMERCIAL "A"
- ☐ COMMERCIAL "B"
- ☐ STATE FORMS

COMMENTS/REMARKS

2 day TAT

Fax # 7979753316 86

SAMPLE CUSTODY MUST BE DOCUMENTED BELOW EACH TIME SAMPLES CHANGE POSSESION, INCLUDING COURIER DELIVERY

RELINQUISHED BY SAMPLER:	DATE TIME:	RECEIVED BY:	RELINQUISHED BY:	DATE TIME:	RECEIVED BY:
1.	11/23/12	1. Fed Ex	2. Fed Ex	11/24/12 1000	2.
RELINQUISHED BY:	DATE TIME:	RECEIVED BY:	RELINQUISHED BY:	DATE TIME:	RECEIVED BY:
3.		3.	4.		4.
RELINQUISHED BY:	DATE TIME:	RECEIVED BY:	SEAL #	PRESERVE WHERE APPLICABLE ☐	ON ICE ☒ TEMPERATURE 4.0°C
5.		5.			

4.1 4

JA97713: Chain of Custody
Page 1 of 3

JA97713: Chain of Custody

Page 2 of 3

ACCUTEST.

Sample Log-In Summary

JA97713 COC

Lab Name: Accutest Page ___ of ___

Received by (Print Name): Tim Hudson Log-in Date: ___

Received by (Signature): [signature]

Case Number: N/A
SDG Number:
SAS Number: N/A

REMARKS:		NYSDEC SAMPLE #	CORRESPONDING: SAMPLE TAG #	CORRESPONDING: ASSIGNED LAB #	REMARKS: CONDITION OF SAMPLE SHIPMENT, ETC.
		N/A		JA97713-1	OK
1. Custody Seal(s)	Present/~~Absent~~* Intact/Broken	N/A			
2. Custody Seal Numbers:		N/A			
3. Chain-of-Custody Records	Present/Absent*	N/A			
4. Contract Lab Sample Inform. Sheet (CLSIS)	Present/Absent*	N/A			
5. Airbill	Airbill/Sticker Present/Absent*	N/A			
6. Airbill No.:	7979 7533 1686	N/A			
7. Sample Tags Sample Tag Nos.	Present/Absent* Listed/Not Listed on Chain-of-Custody	N/A			
8. Sample Condition	Intact/Broken*/ Leaking	N/A			
9. Does Information on custody rec., CLSIS, & sample tags agree	Yes/No*	N/A			
10. Date received at Lab:	1-24-12 1000	N/A			
11. Time Received:		N/A			
12. Do aqueous VOC vials have headspace?	Yes/No*				
13. Are preserved voc soil samples fully immersed in preservative?	Yes/No* N/A	N/A			
Sample Transfer					
Fraction:	See Internal				
Area #:					
By:					
On:	Chain of Custody				

Contract BTSR and attach record of resolution

Reviewed By: ___

Date: ___

Logbook No.: N/A

Logbook Page No.: N/A

Form: SM10-02

Accutest Laboratories Sample Receipt Summary

Accutest Job Number: JA97713 **Client:**

Date / Time Received: 1/24/2012 **Project:**

No. Coolers: 1 **Airbill #'s:** **Delivery Method:**

Cooler Security	Y	or	N		Y	or	N
1. Custody Seals Present:	☑		☐	3. COC Present:	☑		☐
2. Custody Seals Intact:	☑		☐	4. Smpl Dates/Time OK	☑		☐

Cooler Temperature	Y	or	N
1. Temp criteria achieved:	☑		☐
2. Cooler temp verification:			
3. Cooler media:	Ice (Bag)		

Quality Control Preservatio	Y	or	N	N/A
1. Trip Blank present / cooler:	☐		☑	☐
2. Trip Blank listed on COC:	☐		☑	☐
3. Samples preserved properly:	☑		☐	
4. VOCs headspace free:	☐		☐	☑

Sample Integrity - Documentation	Y	or	N
1. Sample labels present on bottles:	☑		☐
2. Container labeling complete:	☑		☐
3. Sample container label / COC agree:	☑		☐

Sample Integrity - Condition	Y	or	N
1. Sample recvd within HT:	☑		☐
2. All containers accounted for:	☑		☐
3. Condition of sample:	Intact		

Sample Integrity - Instructions	Y	or	N	N/A
1. Analysis requested is clear:	☑		☐	
2. Bottles received for unspecified tests	☐		☑	
3. Sufficient volume recvd for analysis:	☑		☐	
4. Compositing instructions clear:	☐		☐	☑
5. Filtering instructions clear:	☐		☐	☑

Comments

Accutest Laboratories
V:732.329.0200

2235 US Highway 130
F: 732.329.3499

Dayton, New Jersey
www/accutest.com

JA97713: Chain of Custody
Page 3 of 3

APPENDIX F

Daily Reports
(electronic copies)

DAILY STATUS REPORT

Prepared By: Steve Malinowski of CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50		50-70		70-85	X	>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	8-30-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):
Conducted test pit activities to classify soil for disposal. Eight test pits were dug from grade to bedrock or 14-feet deep (whichever was deeper).
SVOCs (NJDEP Soil Cleanup List + TCL/TAL), Total Metals (TAL) + Cyanide and Hexavalant Chromium, PCBs, Herbidies/Pesticides (NJDEP Soil Cleanup List+TCL/TAL), Full TCLP (VOCs, SVOCs, Metals, Herbs/Pest and RCRA Characteristics)

Working In Grid #: All – test pits installed across entire site

Samples Collected (Since Last Report): 12 grab samples were collected for VOCs, 12 composite samples were collected for Total Petroleum Hydrocarbons (TPH) and 12 additional composite samples were collected for TPH, SVOCs (NJDEP Soil Cleanup List + TCL/TAL), Total Metals (TAL) + Cyanide and Hexavalant Chromium, PCBs, Herbidies/Pesticides (NJDEP Soil Cleanup List+TCL/TAL), Full TCLP (VOCs, SVOCs, Metals, Herbs/Pest and RCRA Characteristics)

Air Monitoring (Since Last Report):
Air monitoring started today, no problems.

Problems Encountered:
None

Planned Activities for Next Week:
Tomorrow the development team plans to install additional test pits for Geotechnical purposes. No soil sampling is planned. We also plan to collect a groundwater sample in preparation of a dewatering application to NYCDEP.

 File Name: _____

Example:

Facility # Name/ location type of waste	Solid		Solid		Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
Totals (trucks, cu.yds.)										

Site Grid Map

Draft map with grids attached

 File Name: _____

Photo Log

Photo 1 – Excavation in area of stained asphalt near former automobile lift. Soil beneath the asphalt did not contain soil displaying hydraulic oil contamination.	
Photo 2 – Test pit TP-2 reveals the presence of buried brick foundations.	

 File Name: _____

Photo 3 – Soil pile removed from test pit location TP-3.	

 File Name: _____

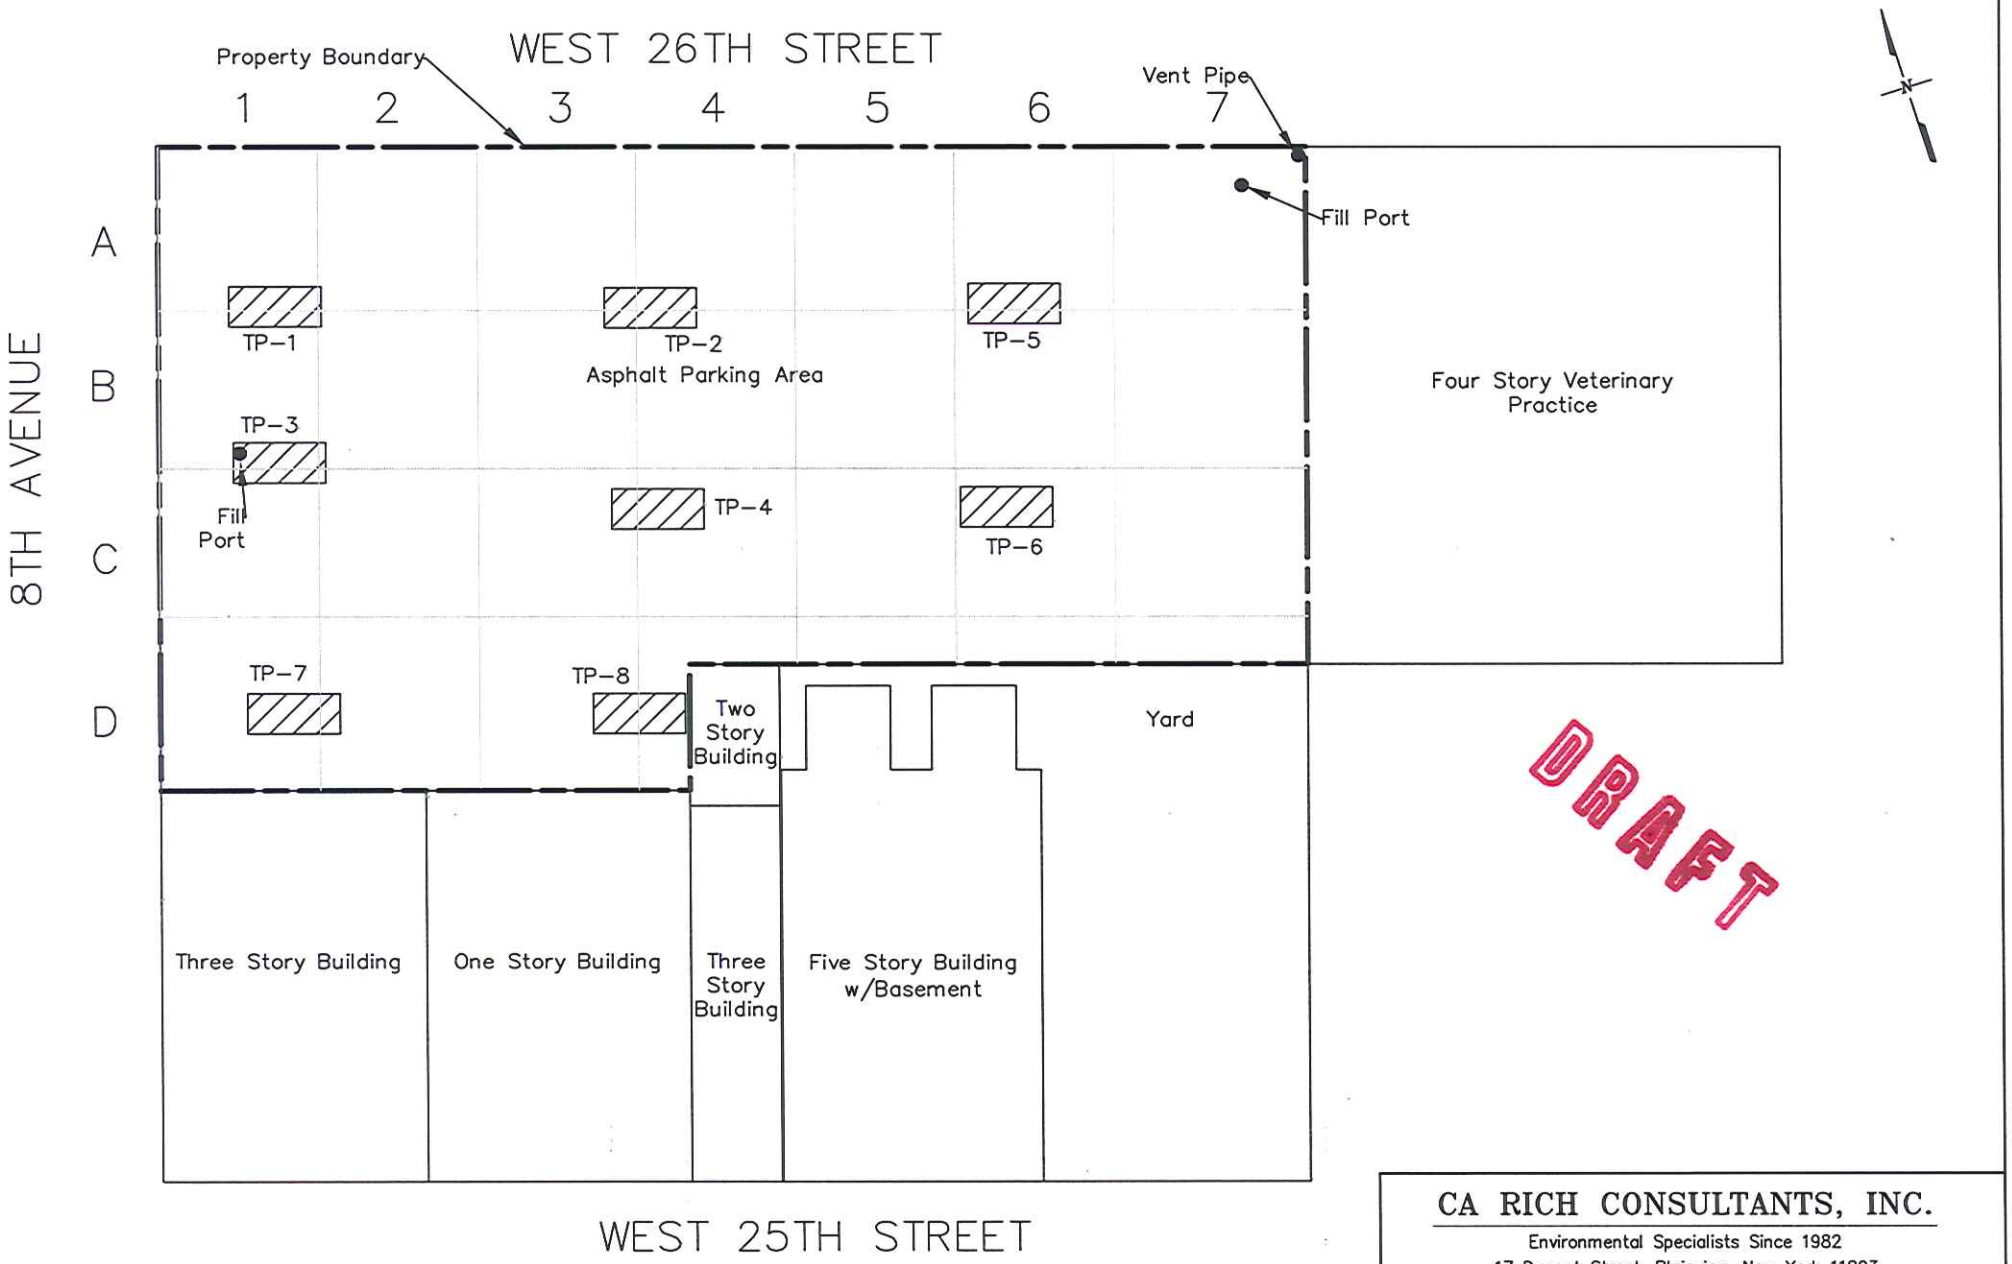

LEGEND

Alphanumeric Grid Are Approximately 30–Feet by 30–Feet

Proposed Test Pit Location for Soil Waste Classification Purposes
Test Pits to Extend to Bedrock or 15 Feet Below Grade

0 10 20 40
Graphic Scale in Feet

CA RICH CONSULTANTS, INC.
Environmental Specialists Since 1982
17 Dupont Street, Plainview, New York 11803

TITLE: SITE PLAN with ALPHANUMERIC GRID		DATE: 8/30/2011
		SCALE: As Shown
FIGURE: 1	260 West 26th Street Manhattan, New York	DRAWN BY: J.T.C.
DRAWING NO: 2011–M1A		APPR. BY: S.T.M.

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50		50-70		70-85	X	>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	8-31-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	
Work Activities Performed (Since Last Report): (4) Test Pits dug and backfilled for Geotechnical purposes.	
Working In Grid #: 7B, 7C, D2, D3	

Four test pits were dug for Geotechnical purposes. Please see Site Grid Map for specific locations.

Air Monitoring (Since Last Report):

Air Monitoring was taken during excavation of test pits, no problems.

Problems Encountered:

None

Planned Activities for Next Week:

Trenching to begin along property lines. Any soil trenched will be stockpiled, covered, and monitored as indicated in the Remedial Work Action Plan.

CA Rich to be on site to collect a groundwater sample in preparation of a dewatering application to NYCDEP.

Example:

 File Name: _____

Facility # Name/ location type of waste	Solid		Solid		Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
Totals (trucks, cu.yds.)										

Site Grid Map

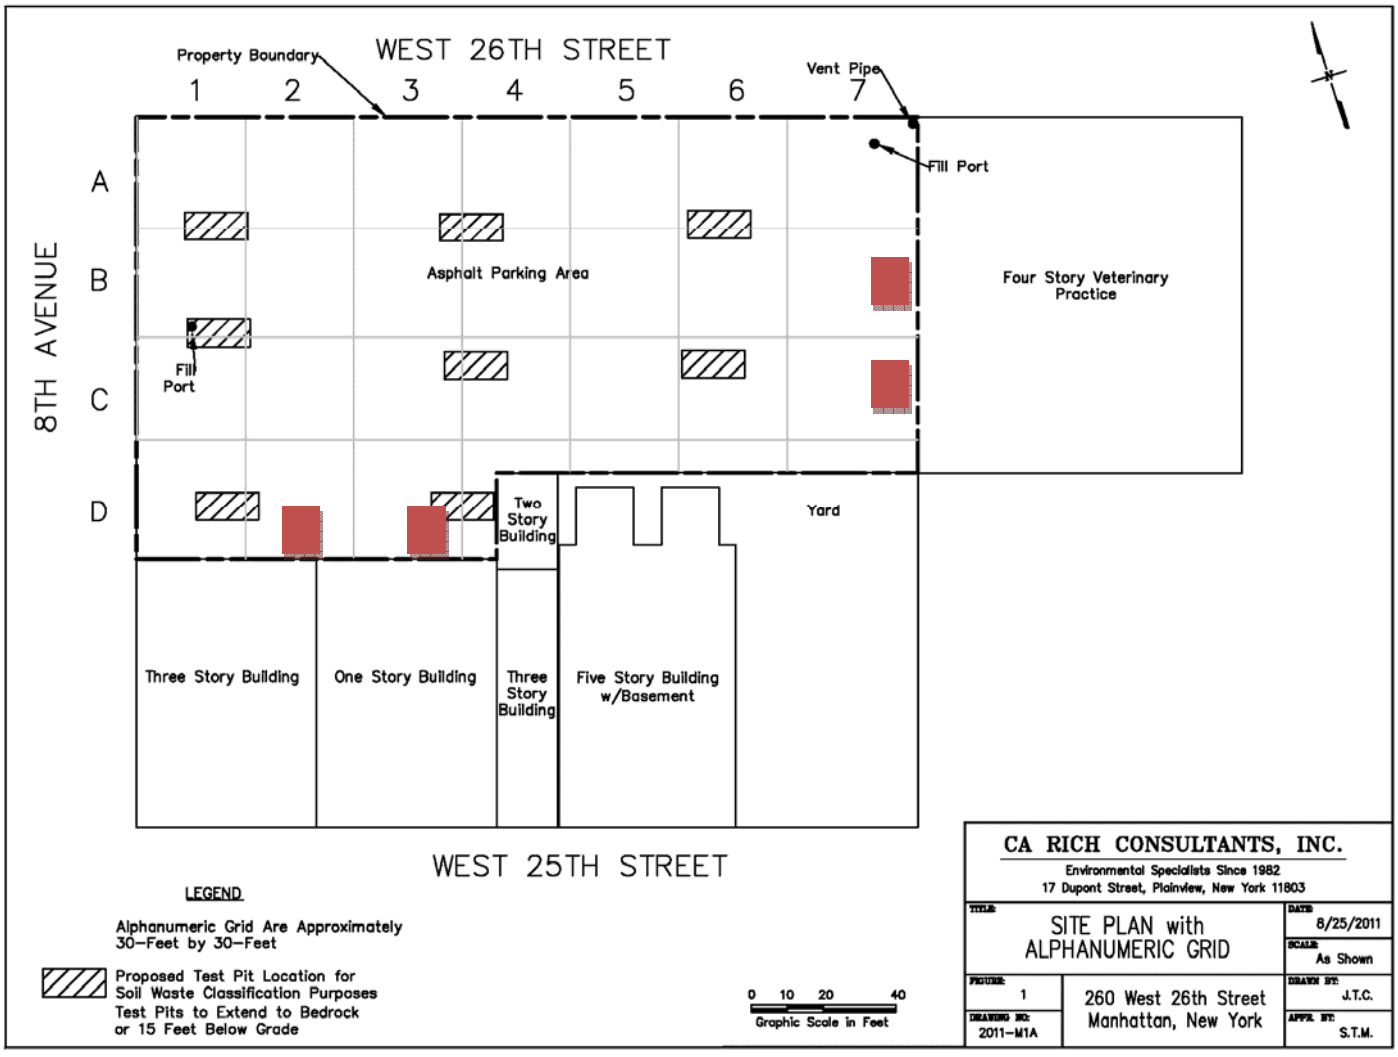

 File Name: _____

Photo Log

Photo 1 – Test Pit in Area 7B dug to reveal foundation of neighboring building to the east.	
Photo 2 – Test Pits in Areas 7B and 7C were back-filled completely before end of the day.	
Photo 3 – Test pit in Area D-2 done to reveal foundation of neighboring building to the south. Test pit was completely backfilled before end of the day.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50		50-70		70-85	X	>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	9-01-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	
Work Activities Performed (Since Last Report): Concrete sidewalk and top layer of asphalt was removed and stockpiled. Fence was built along south property line.	
Working In Grid #: A3, A4, A5, A6, A7, B6, B7, C6, C7	

Concrete sidewalk and top layer of asphalt was removed and stockpiled.

Air Monitoring (Since Last Report):

Air Monitoring was taken during sidewalk and asphalt removal, no problems.

Problems Encountered:

None

Planned Activities for Next Week:

Only Concrete and Asphalt will be removed from the site and trucked to a recycling facility. No soil will be removed from the site. All trucks will be properly cleaned and inspected before leaving the site.

Trenching to continue along property lines. Any soil trenched will be stockpiled, covered, and monitored as indicated in the Remedial Work Action Plan.

CA Rich to be on site to collect a groundwater sample in preparation of a dewatering application to NYCDEP.

Example:

 File Name: _____

Facility # Name/ location type of waste	Solid		Solid		Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
Totals (trucks, cu.yds.)										

Site Grid Map

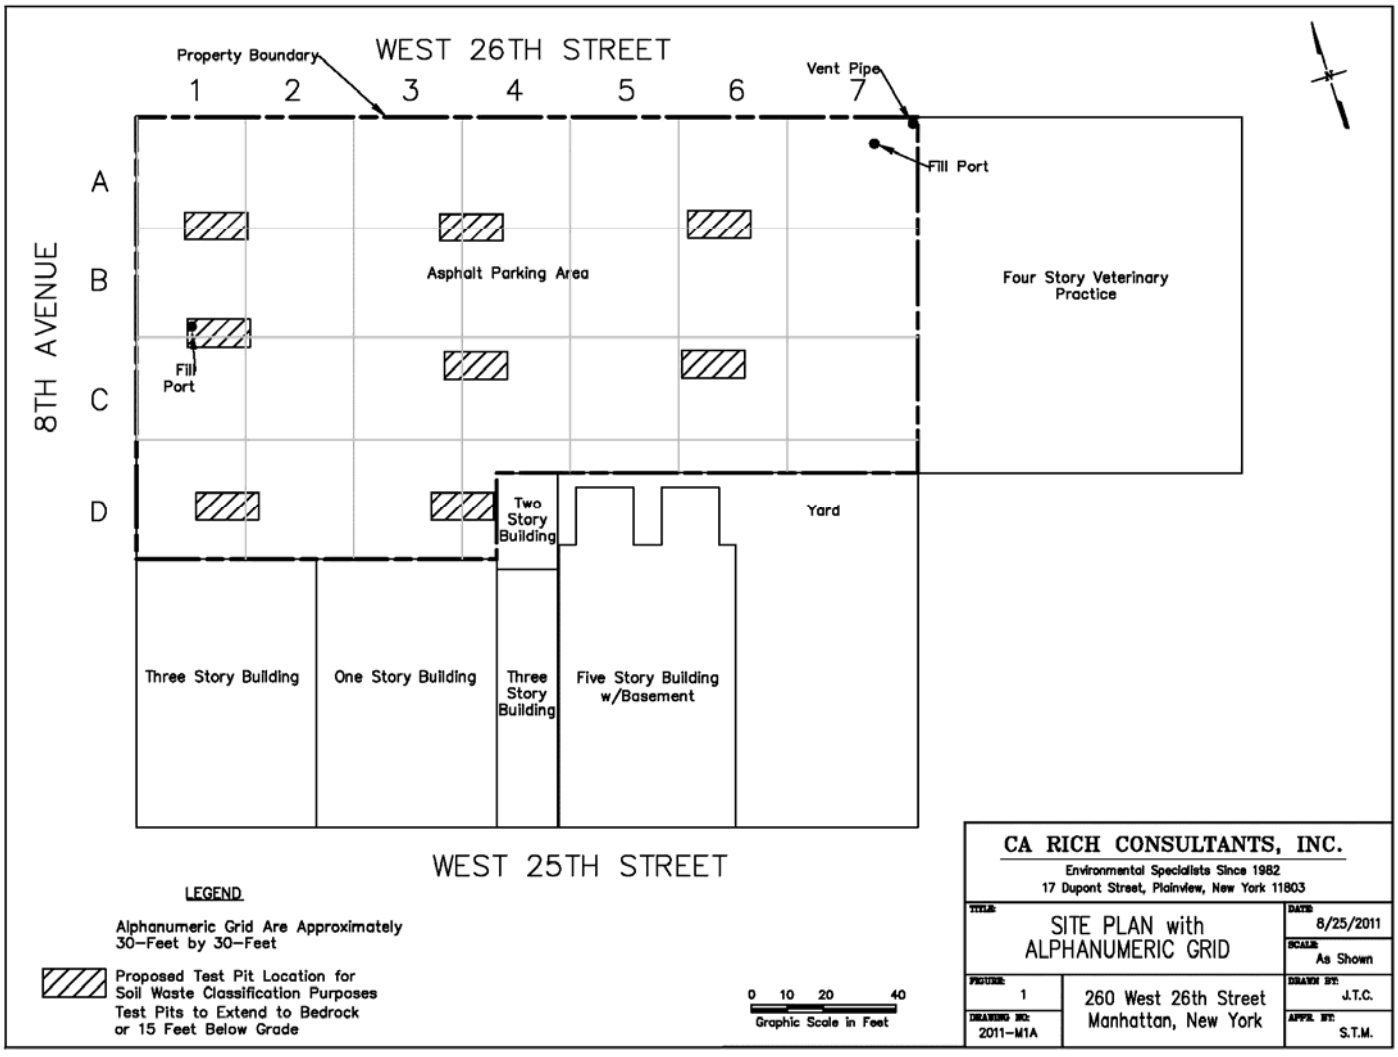

 File Name: _____

Photo Log

Photo 1 – Sidewalk along 26th Street was carefully removed. All concrete was stockpiled.	
Photo 2 – Concrete Sidewalk stockpile.	
Photo 3 – Top layer of asphalt stockpiled.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50		50-70		70-85	X	>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	9-02-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Trenching along property line.

Working In Grid #: A1, A2, A3, A4, A5, A6, A7, B1

Air Monitoring (Since Last Report):

Air Monitoring was taken during trenching, no problems.

Problems Encountered:

None

Planned Activities for Next Week:

Only Concrete and Asphalt will be removed from the site and trucked to a recycling facility. No soil will be removed from the site. All trucks will be properly cleaned and inspected before leaving the site.

Trenching to continue along property lines. Any soil trenched will be stockpiled, covered, and monitored as indicated in the Remedial Work Action Plan.

To begin piledriving.

Example:

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Solid		Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
	6	150								
Totals (trucks, cu.yds.)										

Site Grid Map

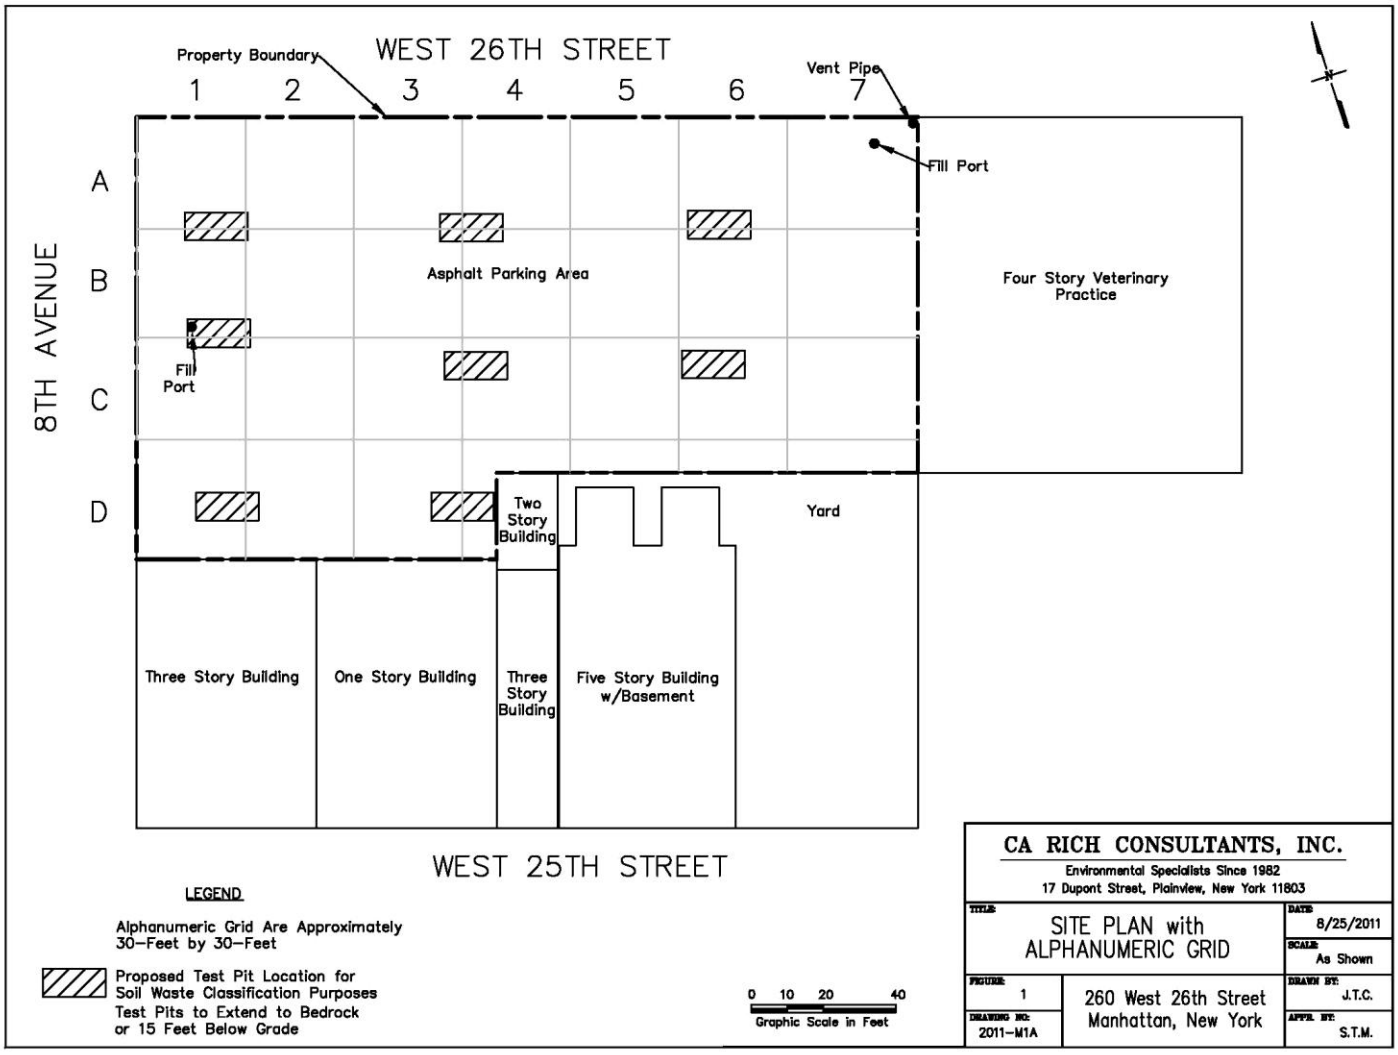

 File Name: _____

Photo Log

Photo 1 – Trenching along the north side of the site facing east.	
Photo 2 – Trenching along the north side of the site facing north.	
Photo 3 – Trenching on east side of Site.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain	X	Overcast		Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	9-06-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Continued trenching along property lines and solid waste such as concrete, brick, and asphalt was sorted and trucked off site to a recycling facility. No soil was removed from the site, and all soil remained in its original location.

Working In Grid #: A1, A2, A3, A4, A5, A6, A7, B1, C1

Air Monitoring (Since Last Report):

No Air Monitoring was done today due to a steady rain all day.

Problems Encountered:

DOB inspector Williamson came to the site today. He issued 2 violations, one was to provide updated plans for underpinning the South Neighboring Building and to provide updated plans detailing an old foundation wall along 8th Avenue. The other was to cut our neighbors trees down due to its instability.

Planned Activities for Next Week:

Only Concrete and Asphalt will be removed from the site and trucked to a recycling facility. No soil will be removed from the site. All trucks will be properly cleaned and inspected before leaving the site.

Trenching to continue along property lines. Any soil trenched will be stockpiled, covered, and monitored as indicated in the Remedial Work Action Plan.

To begin piledriving.

Example:

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Solid		Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
	9	225								
Totals (trucks, cu.yds.)	15	375								

Site Grid Map

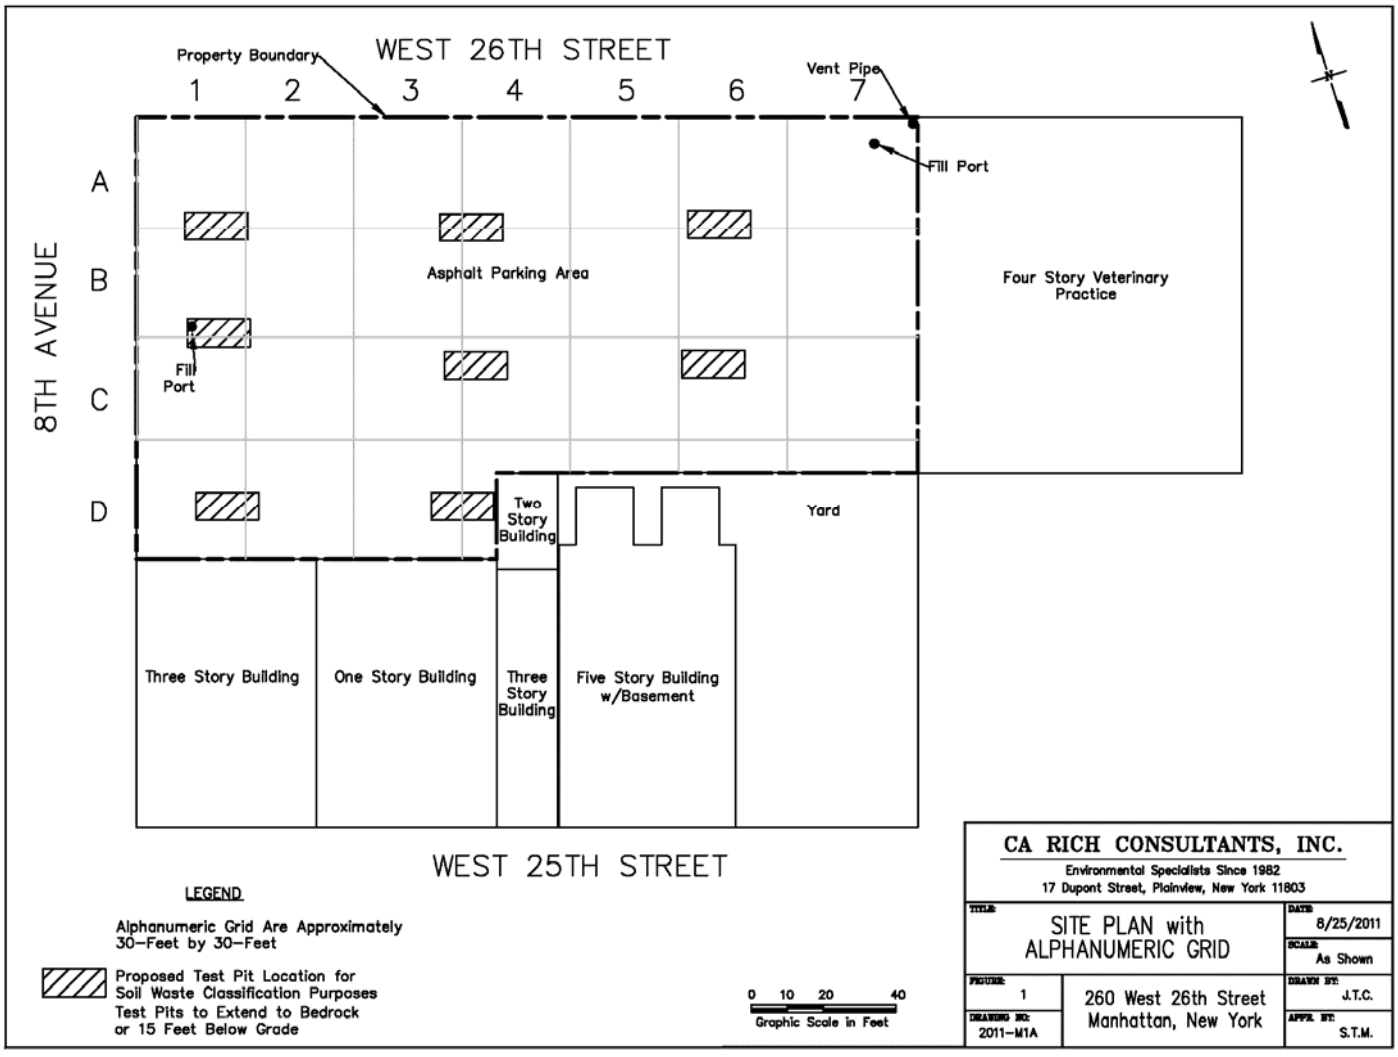

 File Name: _____

Photo Log

Photo 1 – All trucks were thoroughly washed and inspected before leaving the site.	
Photo 2 – All solid waste (ex: brick, rock, concrete, asphalt) was carefully separated from soil and trucked off the site to a recycling facility. <u>No</u> soil was removed from the site. All soil remained in its original location.	
Photo 3 – Trenching continued along 8th Ave. All solid waste was removed, and the remaining soil was filled back in.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain	X	Overcast		Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	9-07-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Continued trenching along 26th Street and preparing the site to install soldier piles. Two truck loads of HP Soldier Piles were delivered to site today. Asphalt, concrete and bricks continued to be trucked off site to a recycling facility. No soil was removed from the site, and all soil remained in its original location. Trees along the south property line were removed.

Working In Grid #: A3, A4, A5, A6, A7, D5, D6, D7

Air Monitoring (Since Last Report):

No Air Monitoring was done today due to a steady rain all day.

Problems Encountered:

No problems were encountered today.

Planned Activities for Next Week:

Only Concrete, Asphalt, and Brick will be removed from the site and trucked to a recycling facility. No soil will be removed from the site. All trucks will be properly cleaned and inspected before leaving the site. Due to heavy rains, a truck load of gravel was delivered to keep the truck station free of mud.

Trenching to continue along property lines. Any soil trenched will be stockpiled, covered, and monitored as indicated in the Remedial Work Action Plan.

To begin piledriving.

Example:

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Solid		Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
	11	275								
Totals (trucks, cu.yds.)	26	650								

Site Grid Map

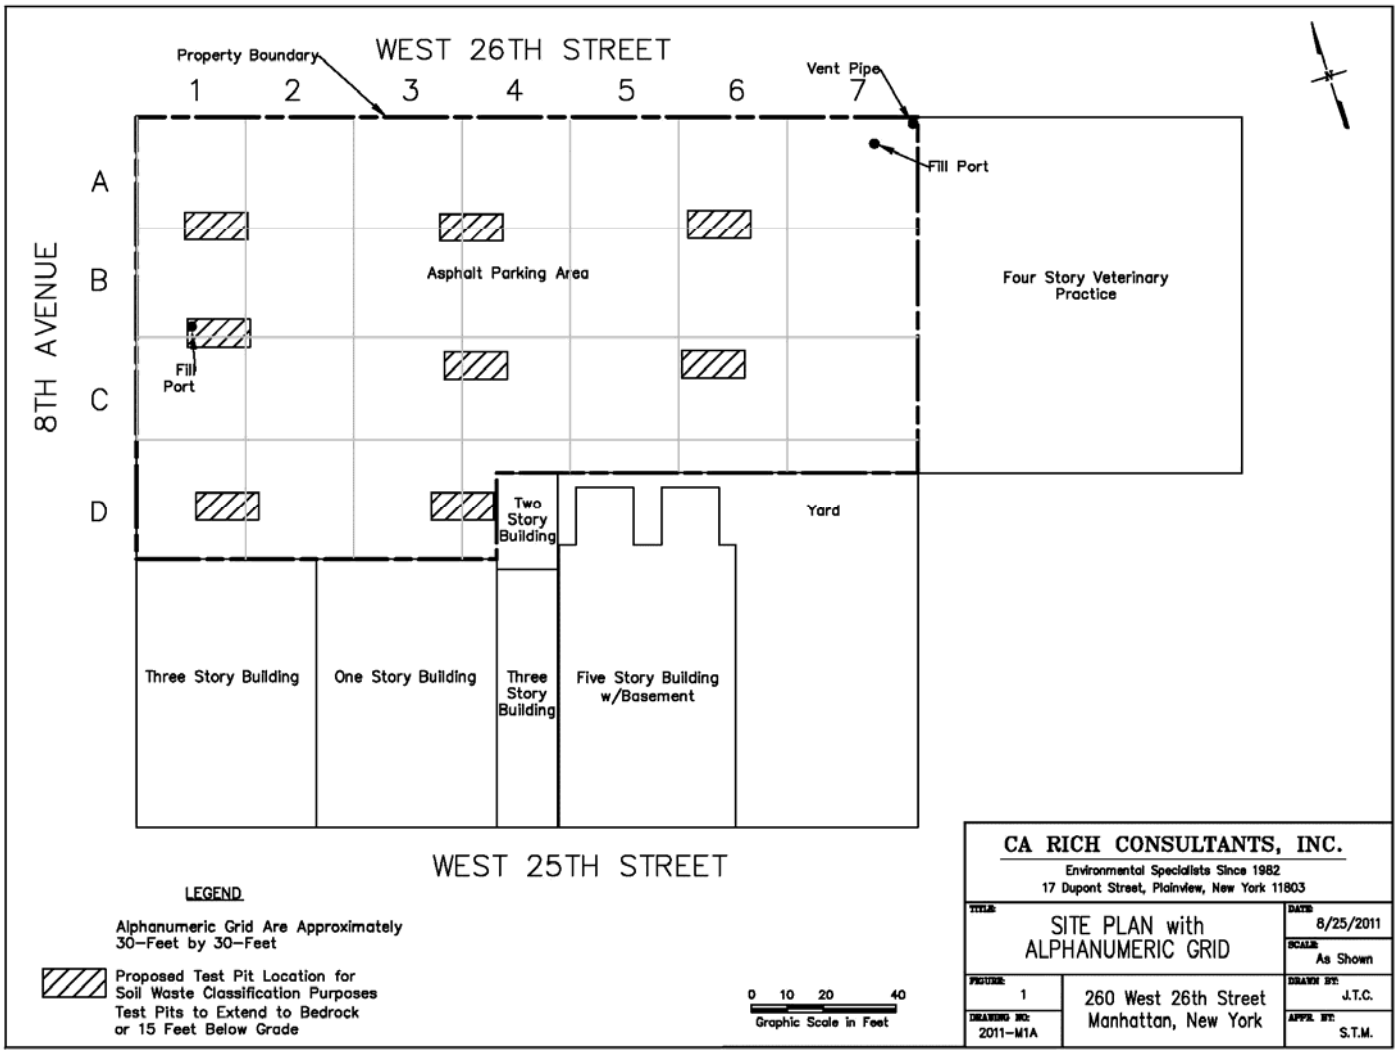

 File Name: _____

Photo Log

Photo 1 – Due to the heavy rains, gravel was delivered to the site for the truck wash station. All trucks were thoroughly washed and inspected before leaving the site.	
Photo 2 – Site was properly graded along 26th street to prepare for soldier piles to be installed next week.	
Photo 3 – Fence was built along the south property line and trees were carefully removed from site.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain		Overcast	X	Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50		50-70		70-85	X	>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	9-08-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

A fence was built along the south property line. Asphalt, concrete and bricks continued to be trucked off site to a recycling facility. No soil was removed from the site, and all soil remained in its original location. Trees along the south property line were removed.

Working In Grid #: C5, C6, C7, D5, D6, D7

Air Monitoring (Since Last Report):

Air Monitoring was taken, no problems.

Problems Encountered:

No problems were encountered today.

Planned Activities for Next Week:

Only Concrete, Asphalt, and Brick will be removed from the site and trucked to a recycling facility. No soil will be removed from the site. All trucks will be properly cleaned and inspected before leaving the site. Due to heavy rains, a truck load of gravel was delivered to keep the truck station free of mud.

Trenching to continue along property lines. Any soil trenched will be stockpiled, covered, and monitored as indicated in the Remedial Work Action Plan.

To begin piledriving.

Example:

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Solid		Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
	4	100								
Totals (trucks, cu.yds.)	30	750								

Site Grid Map

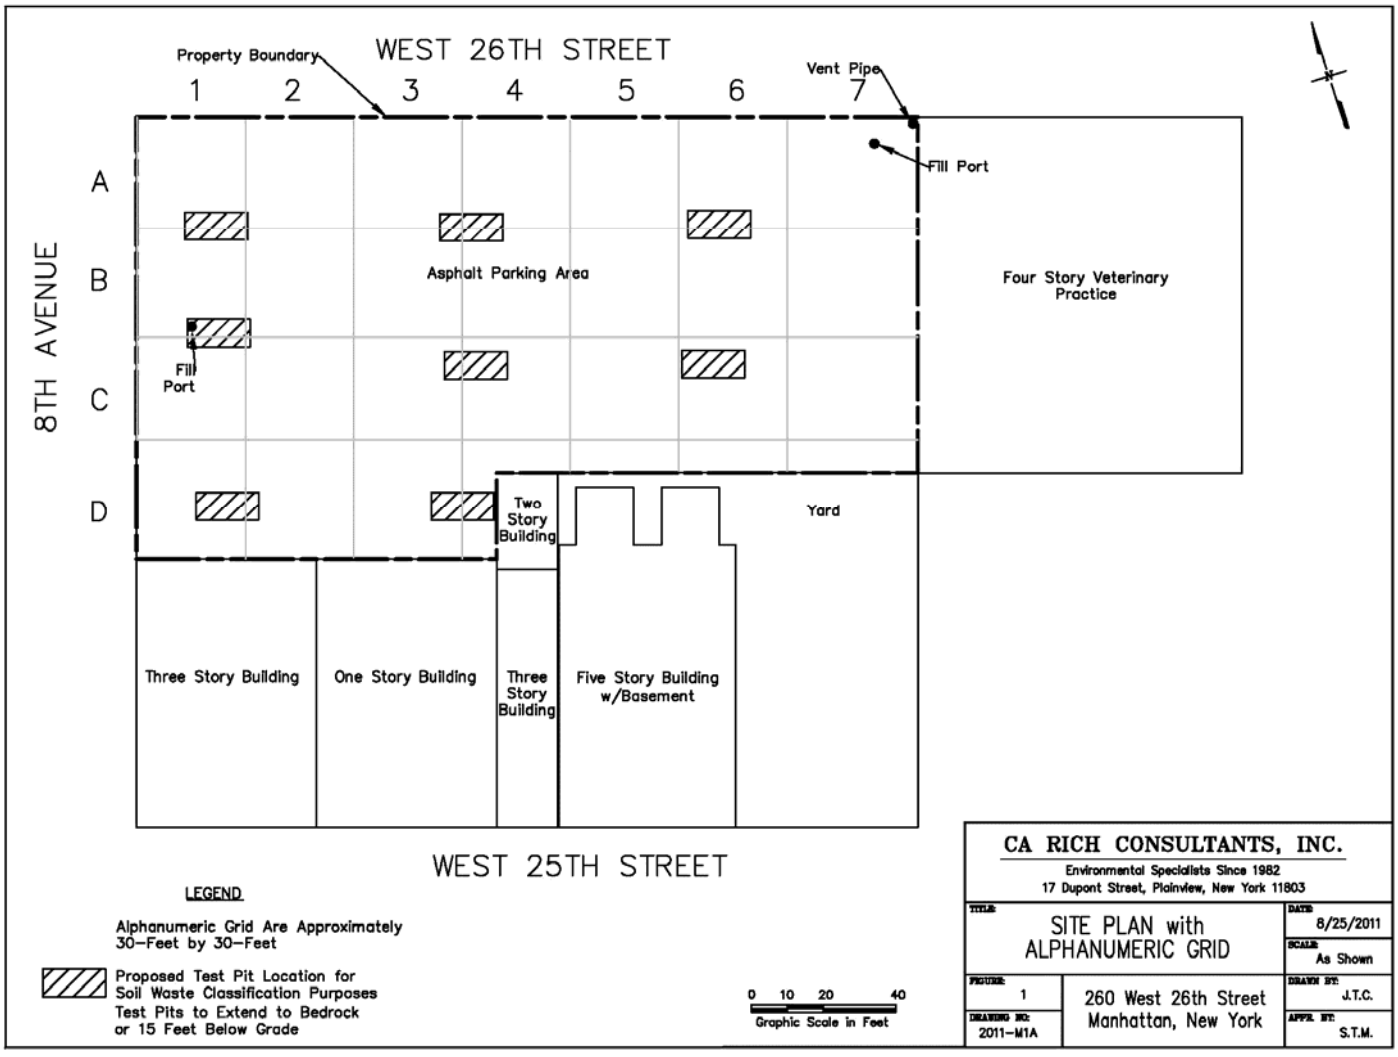

 File Name: _____

Photo Log

Photo 1 – Soldier Piles and equipment were delivered to the site today in preparation for pile driving next week.	
Photo 2 – Truck wash area. All trucks/vehicles were washed thoroughly before leaving the site. All streets and sidewalks were also thoroughly swept and washed.	
Photo 3 – Fence continued to be built along the south property line in preparation for solider pile install next week.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Steve Malinowski of CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50		50-70		70-85	X	>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	9-9-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	
Work Activities Performed (Since Last Report):	
Working In Grid #: B4 and 5	

CA RICH collected a groundwater sample from stormwater pooled on-site. The sample will be submitted to America Analytical of Farmingdale, NY and tested for the NYCDEP list of effluent parameters.

A stockpile of soil that was removed from the surface along the site perimeter to level grids A1 through A7 stockpiled was covered in plastic and posted to identify the area it was removed from.

Air Monitoring (Since Last Report):

No excavation work was performed today therefore dust and VOC monitoring was not performed.

Problems Encountered:
None

Planned Activities for Next Week:
HT-solder piles are planned to be drilled along the perimeter starting in the northwest corner.

Example:

 File Name: _____

Facility # Name/ location type of waste	Solid		Solid		Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
Totals (trucks, cu.yds.)										

Site Grid Map

Draft map with grids attached

 File Name: _____

Photo Log

Photo 1 – Soil stockpile covered with plastic.	
Photo 2 – Soil stockpile from test pit TP-5 covered with plastic.	

 File Name: _____

Photo 3 – Stormwater ponding after rainy week	

 File Name: _____

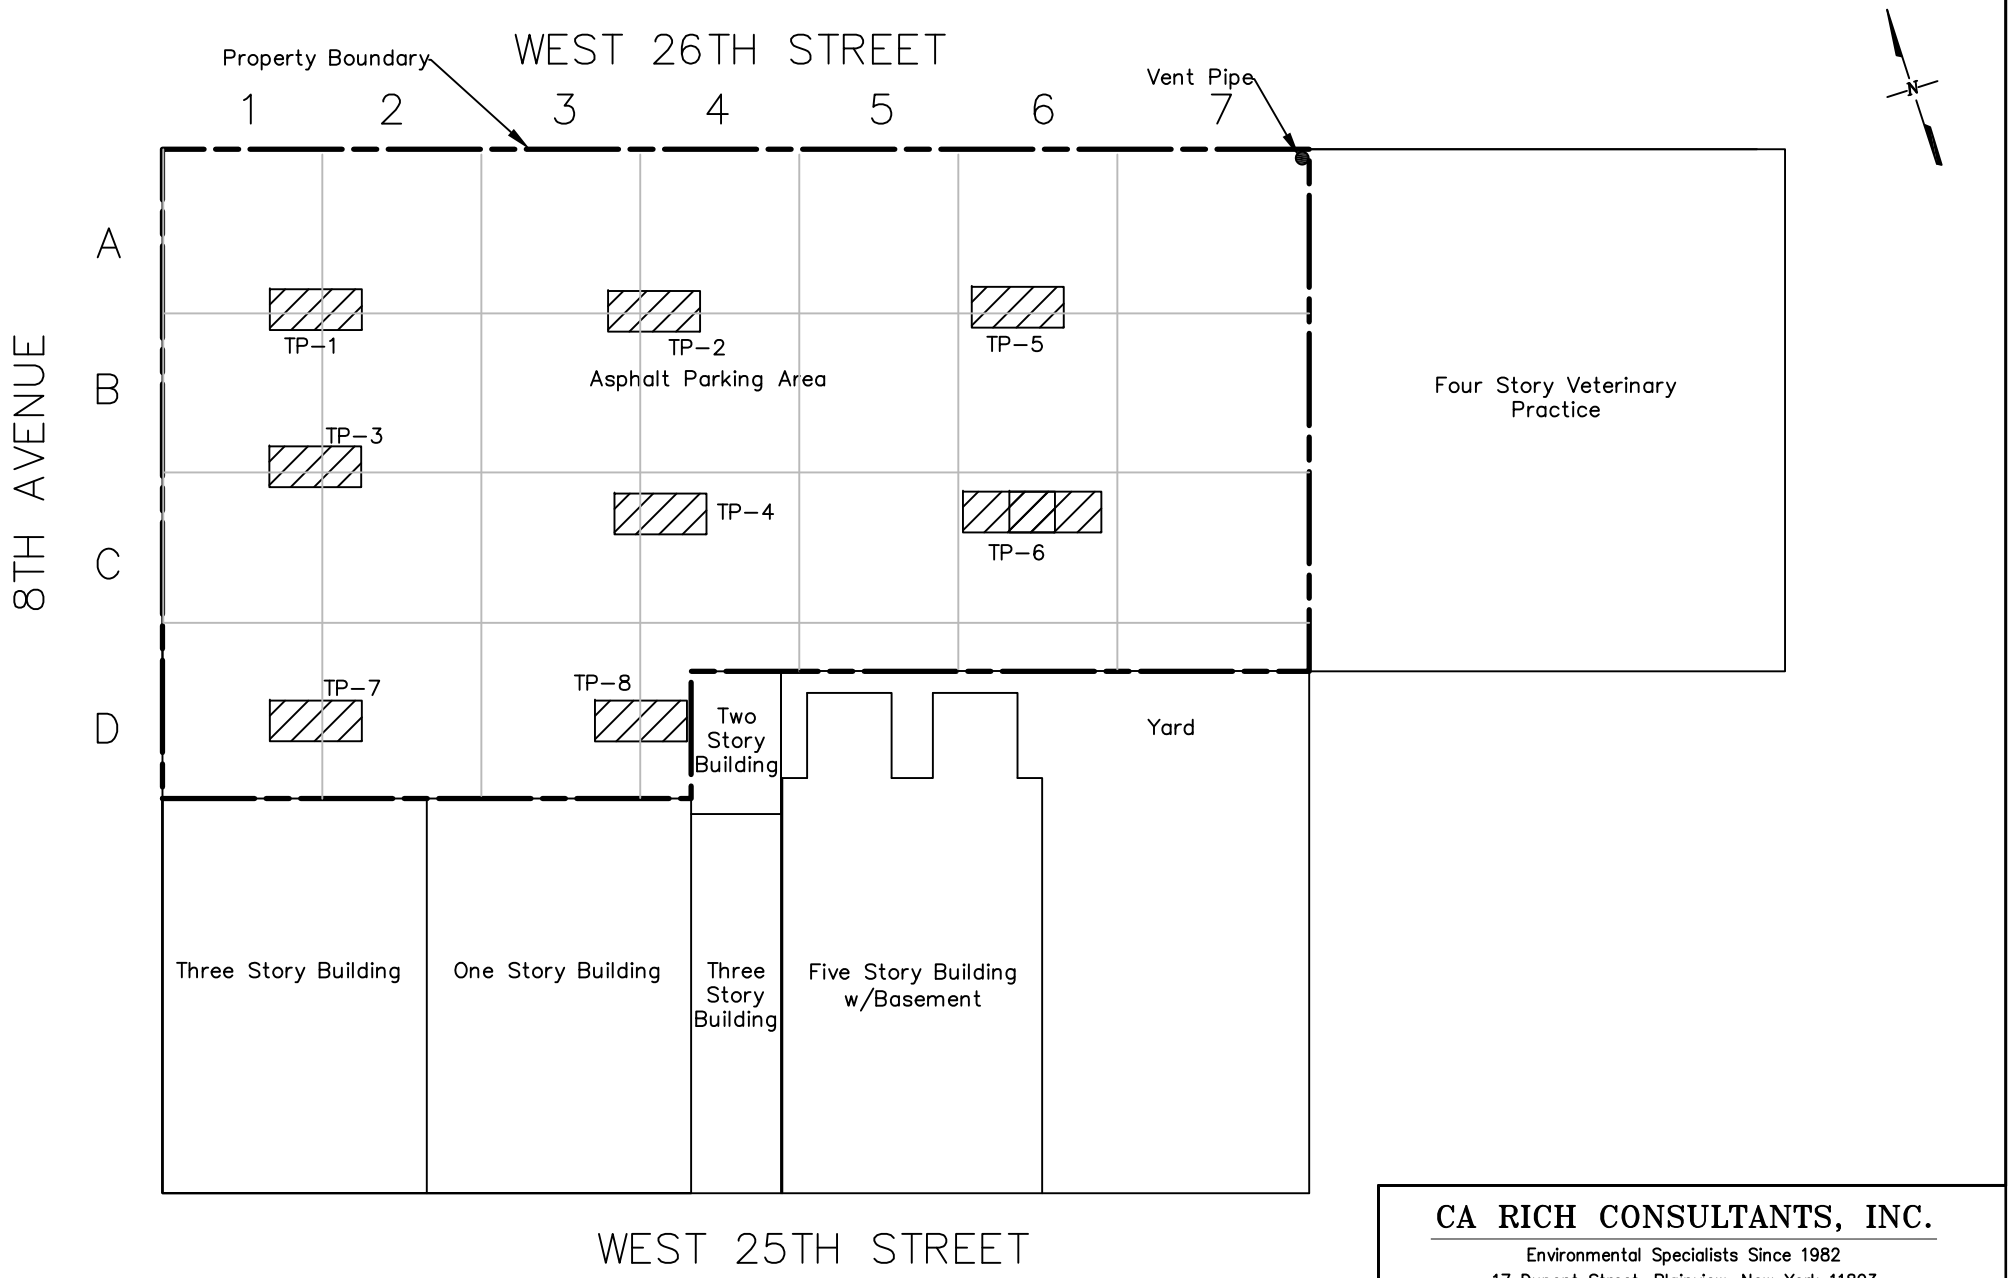

LEGEND

Alphanumeric Grid Are Approximately 30-Feet by 30-Feet

Proposed Test Pit Location for Soil Waste Classification Purposes
Test Pits to Extend to Bedrock or 15 Feet Below Grade

0 10 20 40
Graphic Scale in Feet

CA RICH CONSULTANTS, INC.

Environmental Specialists Since 1982
17 Dupont Street, Plainview, New York 11803

TITLE: SITE PLAN with ALPHANUMERIC GRID	DATE: 9/9/2011
	SCALE: As Shown
FIGURE: 1	DRAWN BY: J.T.C.
DRAWING NO: 2011-M1A	260 West 26th Street Manhattan, New York
	APPR. BY: S.T.M.

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70		70-85	X	>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	9-12-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Began to install HP Soldier Piles along 26th Street. (1) Pile was installed.

Working In Grid #: A6,A7

Air Monitoring (Since Last Report):

Air Monitoring was taken, no problems.

Problems Encountered:

No problems were encountered today.

Planned Activities for Next Week:

HP Soldier Piles will continue to be installed along 26th Street all week.

 File Name: _____

Example:

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Solid		Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
Totals (trucks, cu.yds.)	30	750								

Site Grid Map

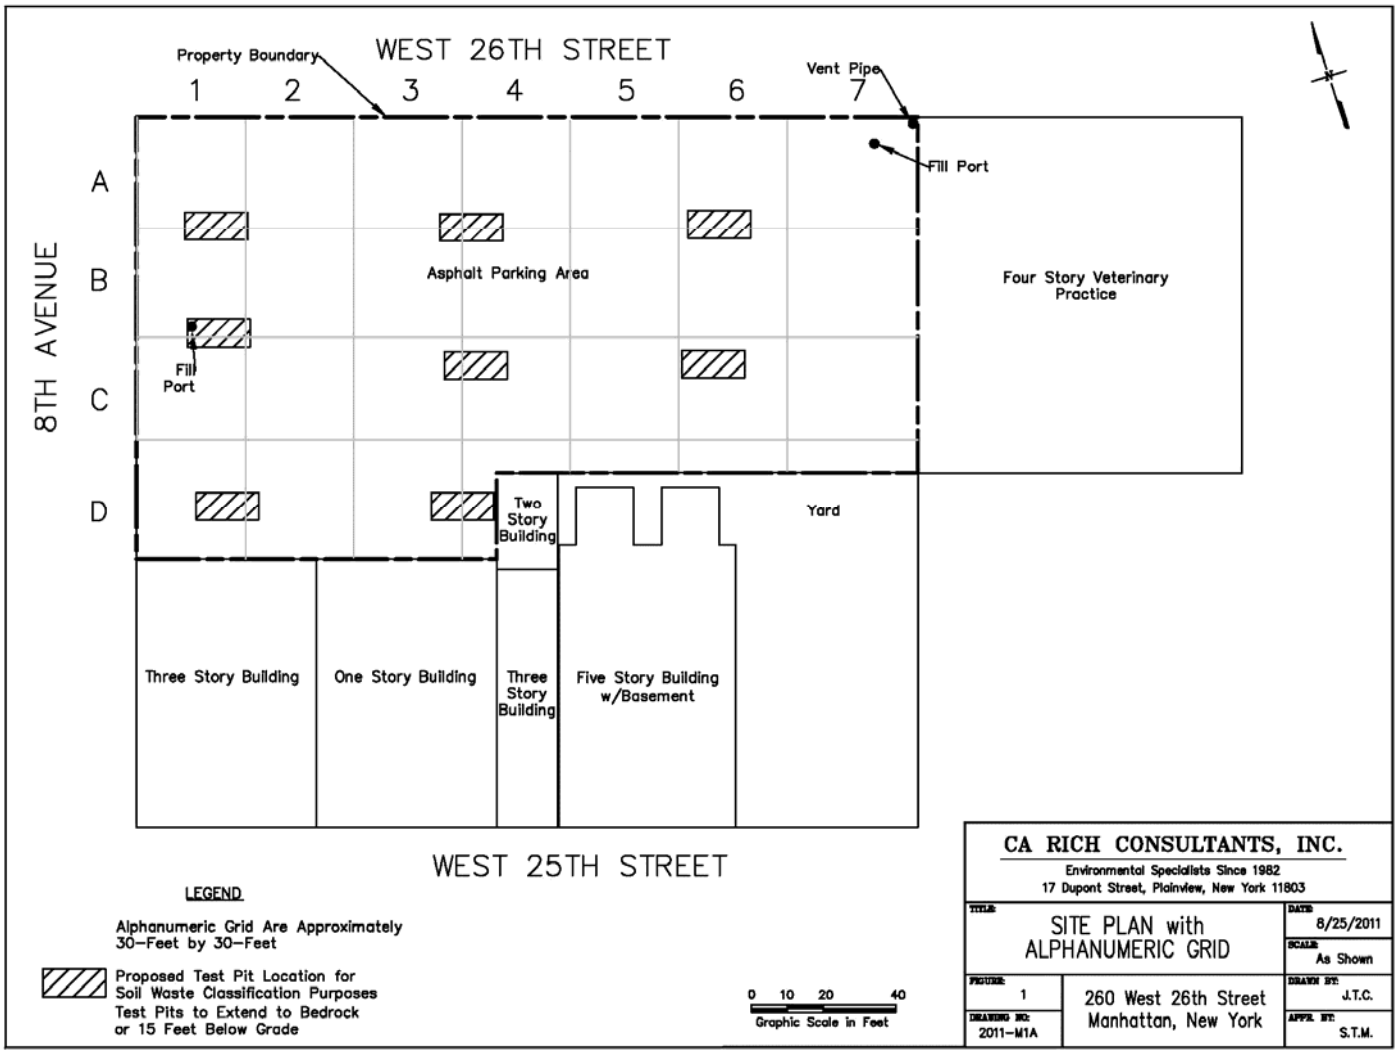

 File Name: _____

Photo Log

Photo 1 – Drill machine used to install HP Soldier Piles.	
Photo 2 – Beginning to install the first HP Soldier Pile along 26th Street. All stockpiled soil on site remains covered in plastic and labeled to identify the area it was removed from.	
Photo 3 – Stockpile of HP Soilder Piles.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70		70-85	X	>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	9-13-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Continued installing HP Soldier Piles along 26th Street. (1) Pile was completed, beam was installed, casing still needs to be removed.

Soil Stockpiles on site continue to remain covered and are inspected daily. No problems thus far.

Working In Grid #: A6,A7

Air Monitoring (Since Last Report):

Air Monitoring was taken, no problems.

Problems Encountered:

No problems were encountered today.

Planned Activities for Next Week:

HP Soldier Piles will continue to be installed along 26th Street all week.

 File Name: _____

Example:										
Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Solid		Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
Totals (trucks, cu.yds.)	30	750								

Site Grid Map

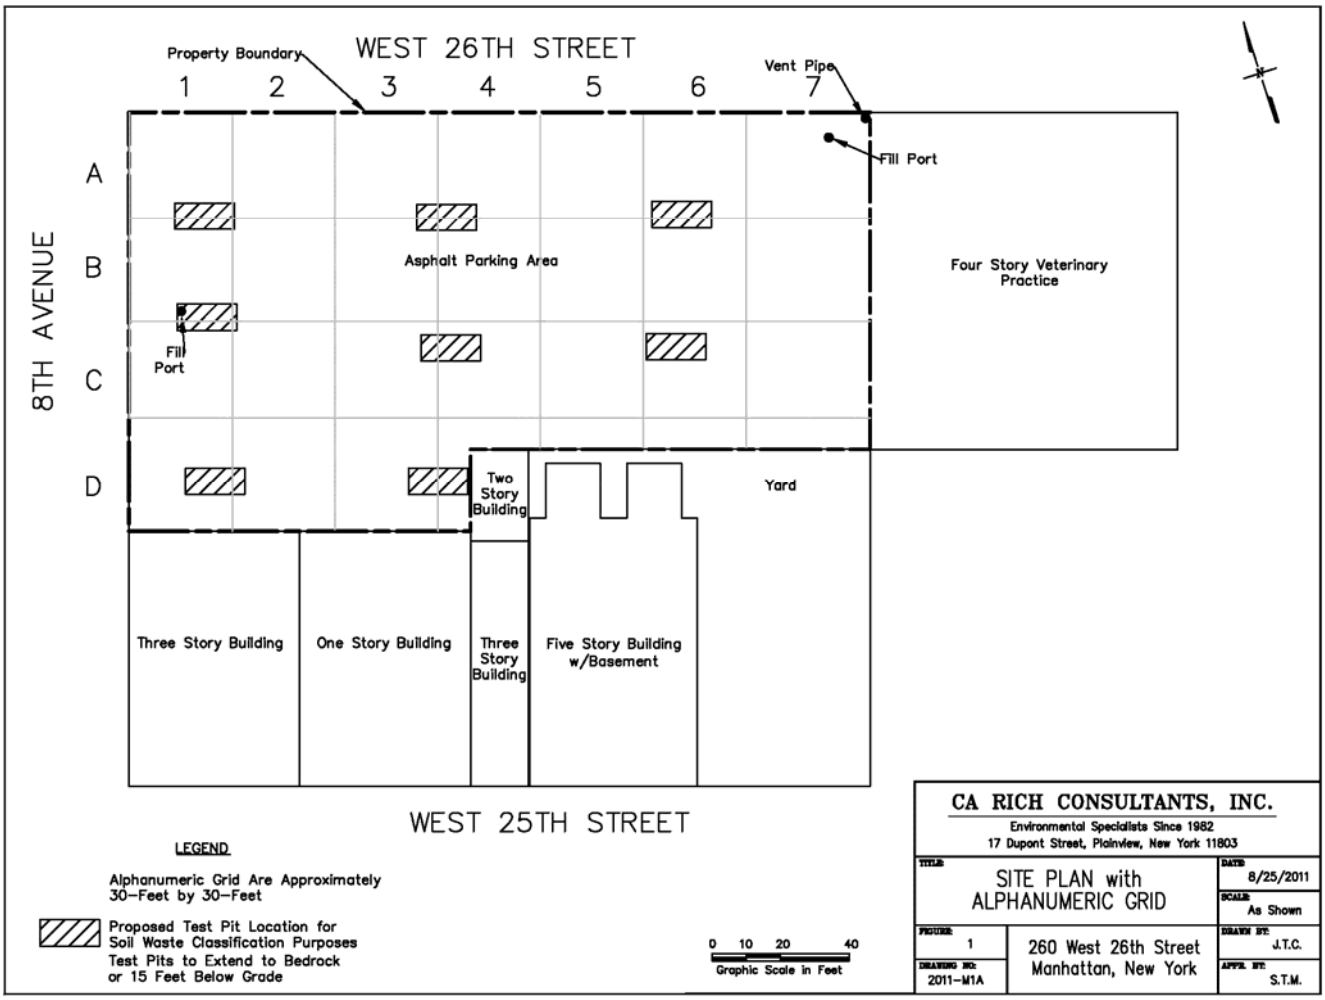

 File Name: _____

Photo Log

Photo 1 – Drill machine used to install HP Soldier Piles. A black mesh fence was built and installed to protect the public of any debris when drilling piles.	
Photo 2 – Continuing to install the first HP Soldier Pile along 26th Street.	
Photo 3 – Stockpiles of soil remain covered while HP Soldier piles continue to be installed. Soil stockpiles were inspected and there are no problems.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70		70-85	X	>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	9-14-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Continued installing HP Soldier Piles along 26th Street. Casing was removed from first pile today. (See photo 2 below.)

Soil Stockpiles on site continue to remain covered. They were inspected today, and no problems have occurred.

Working In Grid #: A6,A7

Air Monitoring (Since Last Report):

No Air Monitoring was done today because no drilling or excavation took place.

Problems Encountered:

No problems were encountered today.

Planned Activities for Next Week:

HP Soldier Piles will continue to be installed along 26th Street all week.

 File Name: _____

									Example:	
Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Solid		Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
Totals (trucks, cu.yds.)	30	750								

Site Grid

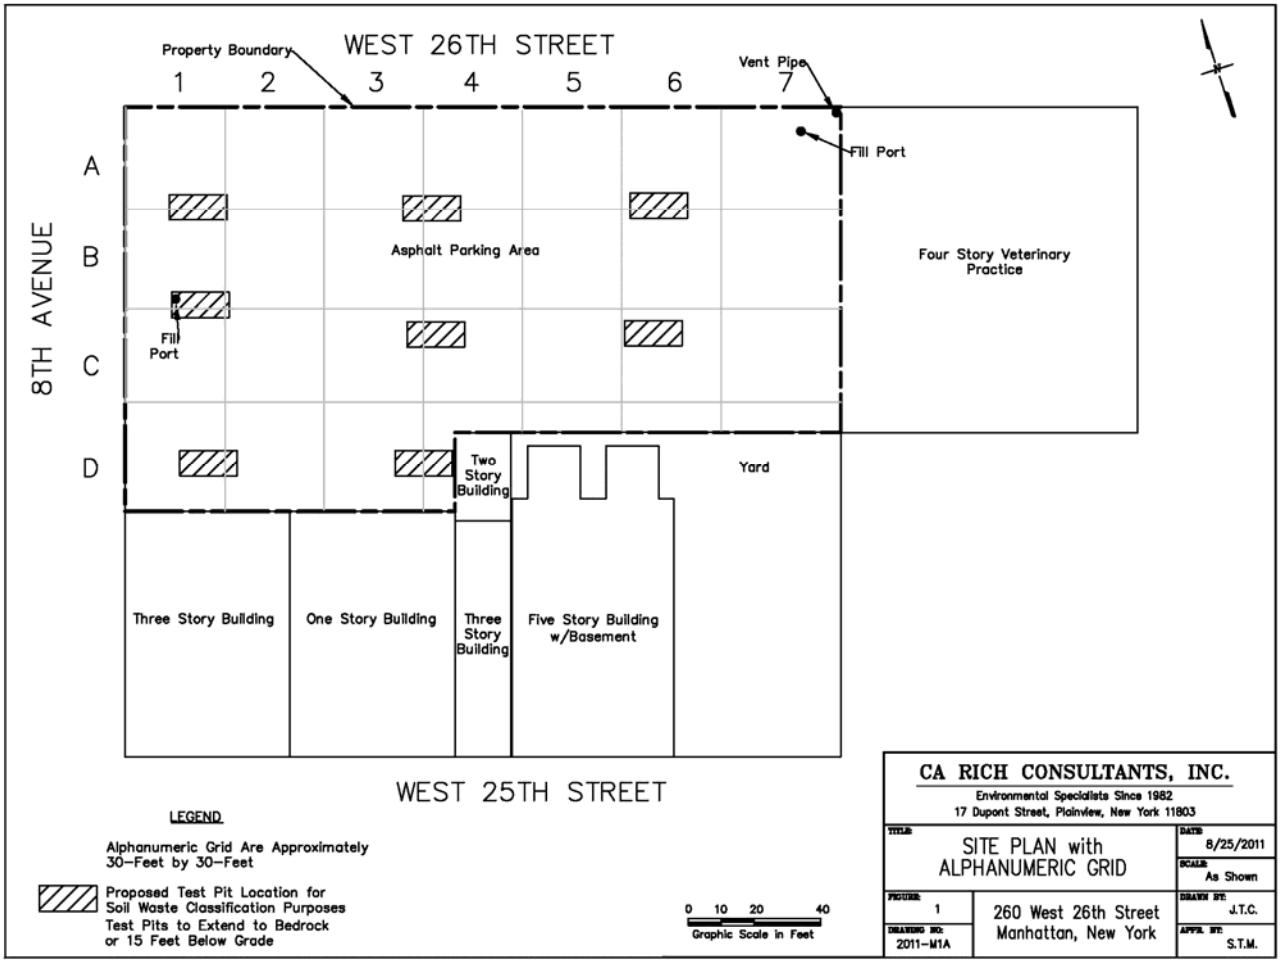

Map

 File Name: _____

Photo Log

Photo 1 – Drill machine and equipment used to install HP Soldier Piles.	
Photo 2 – Installation of (1) HP Soldier Pile Complete.	
Photo 3 – Stockpiles of soil remain covered while HP Soldier piles continue to be installed. Soil stockpiles continue to be inspected and there are no problems.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain	X	Overcast	X	Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50		50-70		70-85	X	>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	9-15-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Continued installing HP Soldier Piles along 26th Street. Four additional piles were installed today for a total of five HP Soldier Piles installed on site.

DOB inspector on site, updated plans shown to DOB inspector to answer questions from the inspection September 6 2011, all ok. DOB inspector also did complete site walkthrough, all ok for Artimus; one violation issued to pile company, issue was already corrected.

Soil Stockpiles on site continue to remain covered. They were inspected today, and no problems have occurred.

Working In Grid #: A6,A7

Air Monitoring (Since Last Report):

No problems with Air Monitoring.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

HP Soldier Piles will continue to be installed along 26th Street all week.

 File Name: _____

Example:

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Solid		Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
Totals (trucks, cu.yds.)	30	750								

Site GridMap

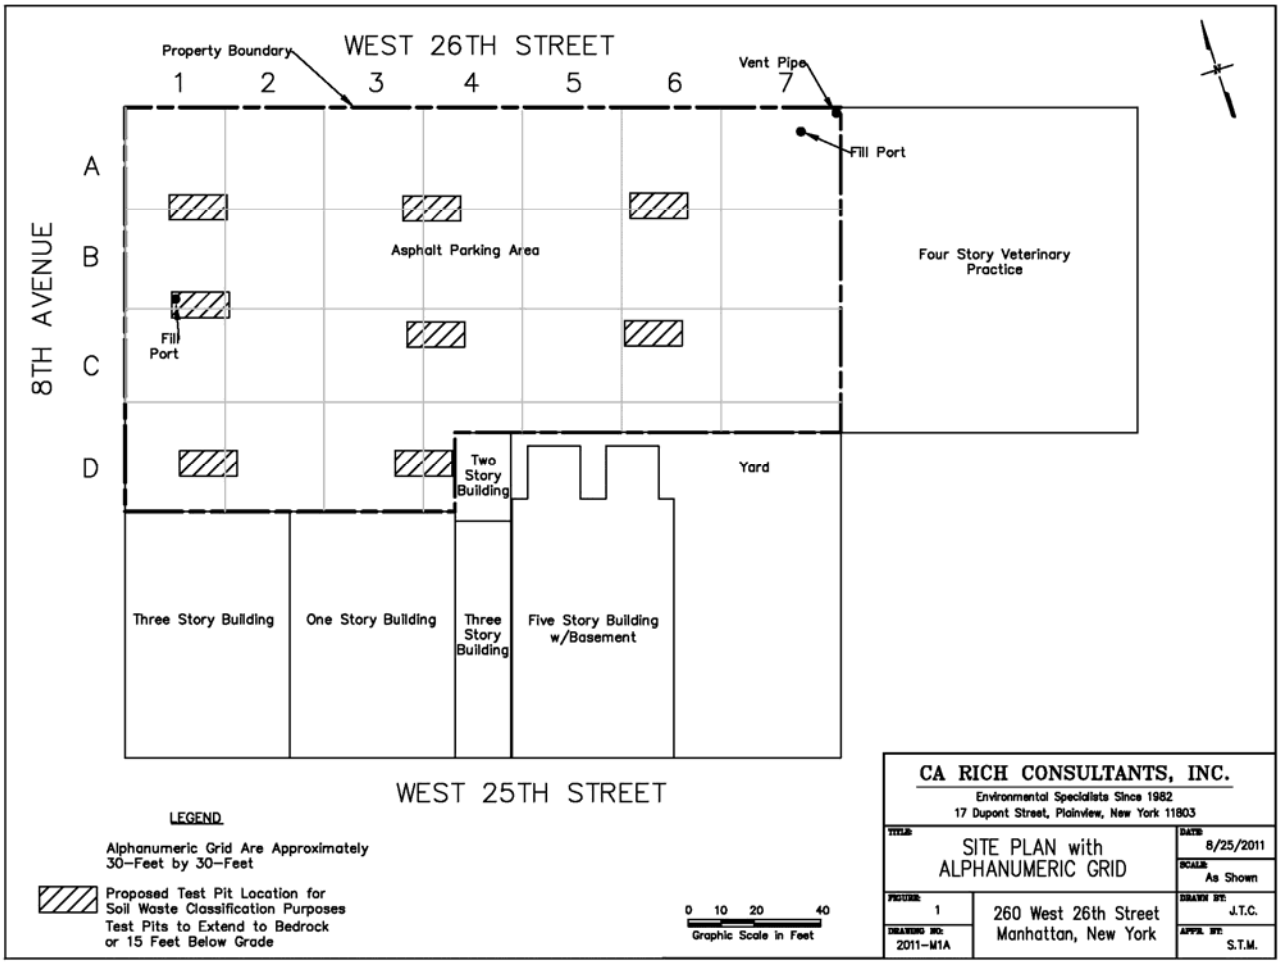

 File Name: _____

Photo Log

Photo 1 – Drill machine driving HP Soldier Pile into rock.	
Photo 2 – Dropping HP Soldier Pile in Casing.	
Photo 3 – Men working to install the fifth HP Soldier Pile today.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	9-16-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Continued installing HP Soldier Piles along 26th Street. Four additional piles were installed today for a total of nine HP Soldier Piles installed on site.

Soil Stockpiles on site continue to remain covered. They were inspected today, and no problems have occurred.

Working In Grid #: A5, A6, A7

Air Monitoring (Since Last Report):

No Air Monitoring was taken today. Steve Malinowski from CA Rich Consultants, Inc. advised OER that the dust monitoring activities at the 260 West 26th Street Site have been suspended until excavation activities resume. As discussed between Steve and OER, Artimus Construction plans to continue installing HP Soldier piles for the next week or two along the perimeter of the site. The installation process for the piles involves a wet drilling operation into bedrock that does not produce any dust because the material is saturated with water. Once excavation activities resume the CAMP monitoring procedures will resume.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

HP Soldier Piles will continue to be installed along 26th Street all next week.

 File Name: _____

Example:

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Solid		Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
Totals (trucks, cu.yds.)	30	750								

Site GridMap

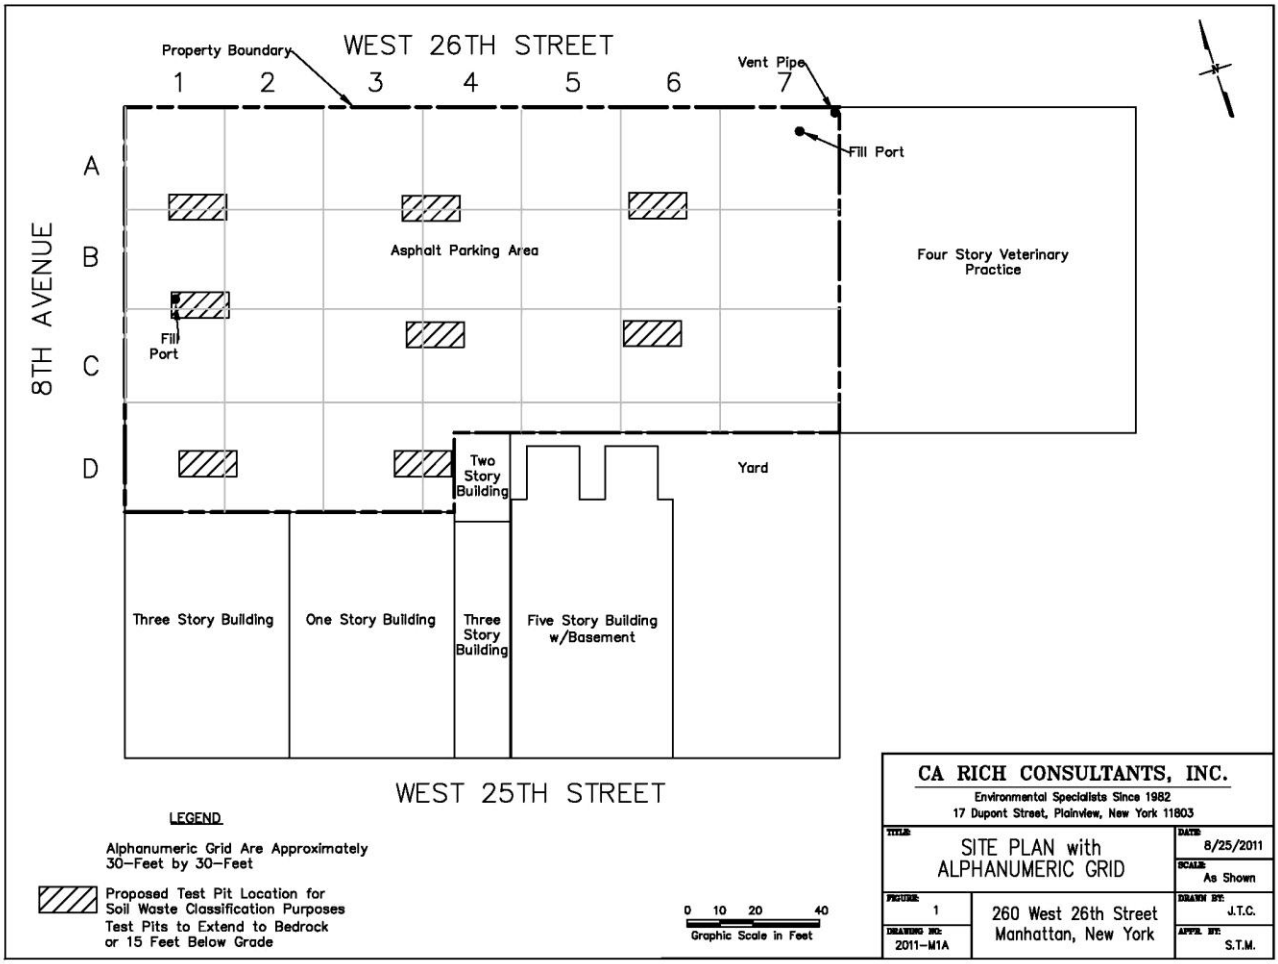

 File Name: _____

Photo Log

Photo 1 – Drilling rock for HP Soldier Pile to be installed.	
Photo 2 – Hoisting HP Solider Pile up to place into casing.	
Photo 3 – Lowering HP Soldier Pile into casing.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70		70-85	X	>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	9-19-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Continued installing HP Soldier Piles along 26th Street. Three additional piles were installed today for a total of twelve HP Soldier Piles installed on site.

Soil Stockpiles on site continue to remain covered. They were inspected today, and no problems have occurred.

Working In Grid #: A4, A5

Air Monitoring (Since Last Report):

No Air Monitoring was taken today. Air Monitoring is currently suspended until excavation activities resume. Once excavation activities resume the CAMP monitoring procedures will resume.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

HP Soldier Piles will continue to be installed along 26th Street all week.

File Name: Example:

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Solid		Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
Totals (trucks, cu.yds.)	30	750								

Site GridMap

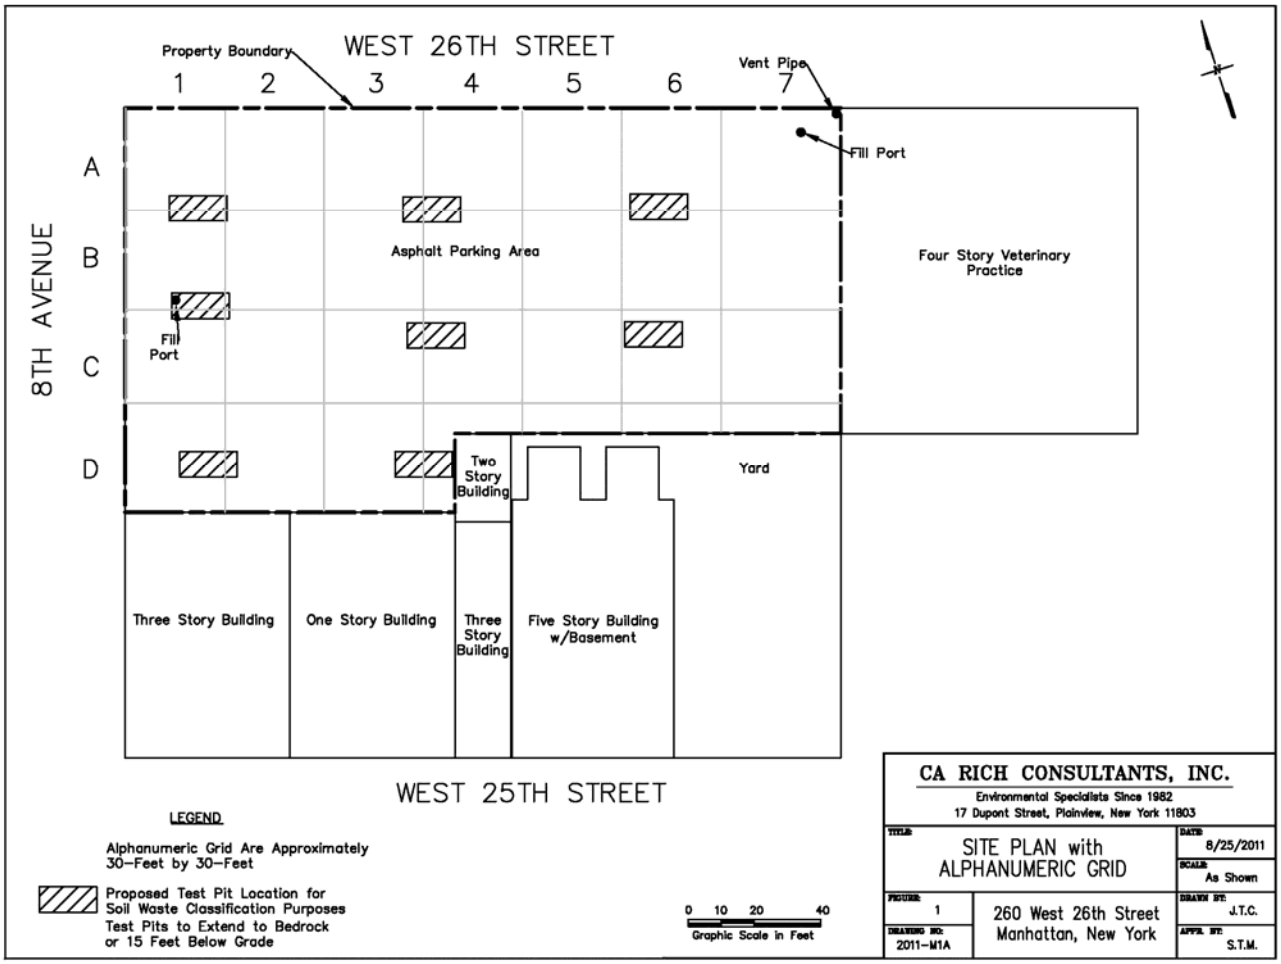

Photo Log

 File Name: _____

Photo 1 – Plastic and Netting to protect public from any debris or water spewing from drilling machine.	
Photo 2 – Men working on drilling machine.	
Photo 3 – Driving Soldier Pile. Plywood was placed in front of machine to help control water spraying from machine.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain	X	Overcast	X	Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50		50-70		70-85	X	>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	9-20-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Continued installing HP Soldier Piles along 26th Street. Four additional piles were installed today for a total of sixteen HP Soldier Piles installed on site.

Soil Stockpiles on site continue to remain covered. They were inspected today, and no problems have occurred.

Working In Grid #: A3, A4

Air Monitoring (Since Last Report):

No Air Monitoring was taken today. Air Monitoring is currently suspended until excavation activities resume. Once excavation activities resume the CAMP monitoring procedures will resume.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

HP Soldier Piles will continue to be installed along 26th Street all week.

File Name: Example:

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Solid		Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
Totals (trucks, cu.yds.)	30	750								

Site Grid Map

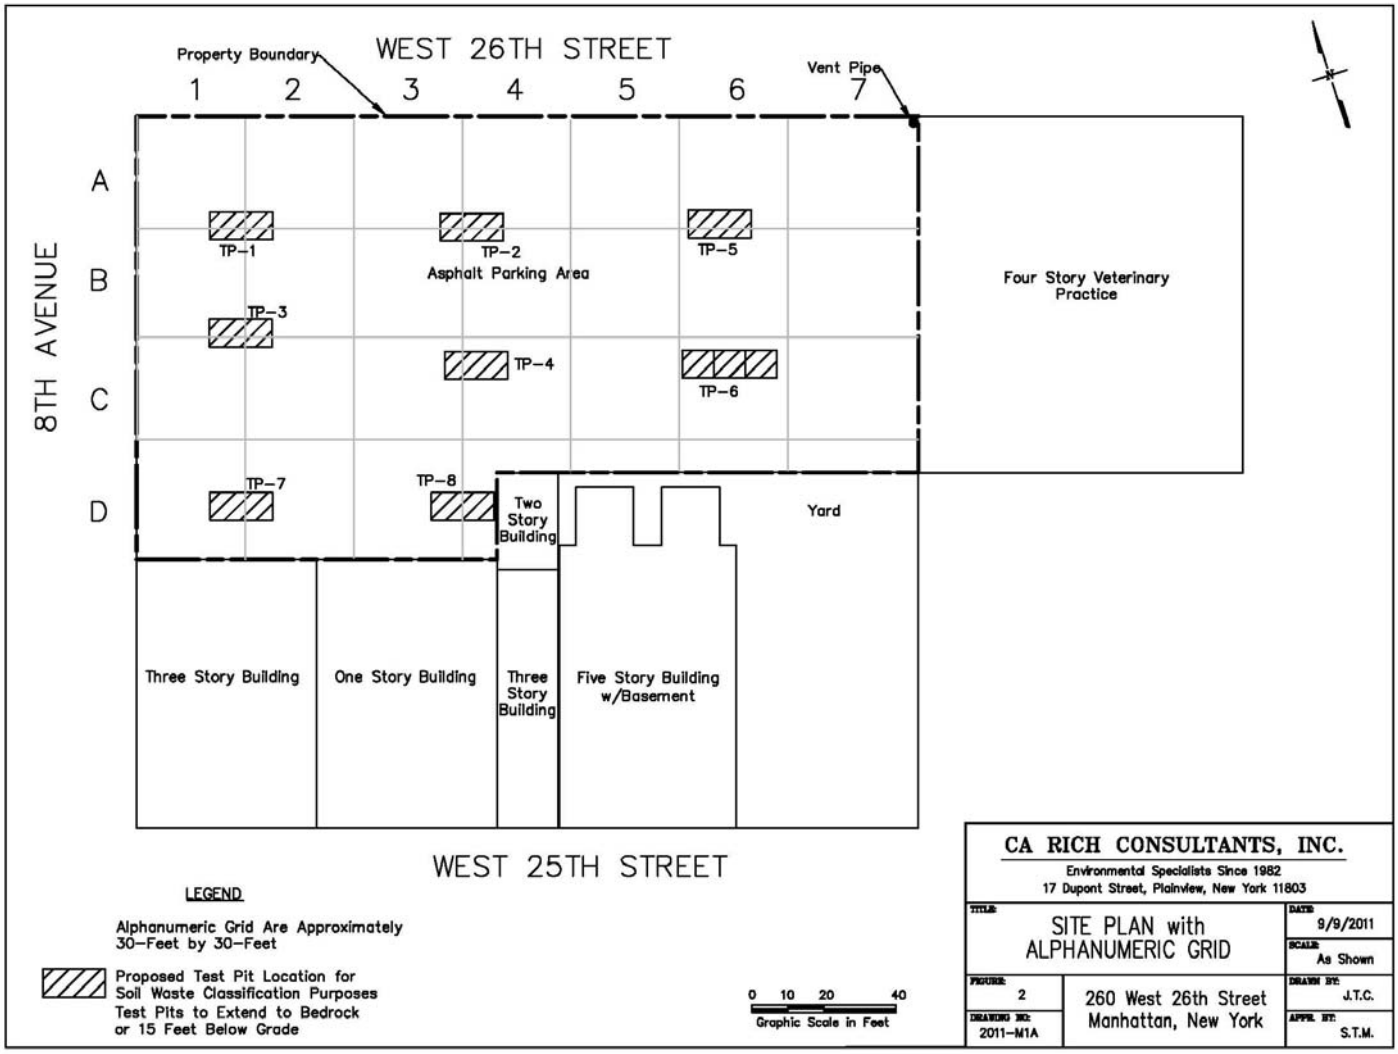

 File Name: _____

Photo Log

Photo 1 – Machine drilling HP Soldier Pile.	
Photo 2 – HP Soldier Piles currently installed along the North property line of the site.	
Photo 3 – HP Soldier Pile grouted in place.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50		50-70		70-85	X	>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	9-21-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Continued installing HP Soldier Piles along 26th Street. Four additional piles were installed today for a total of twenty HP Soldier Piles installed on site.

Soil Stockpiles on site continue to remain covered. They were inspected today, and no problems have occurred.

Working In Grid #: A3, A4

Air Monitoring (Since Last Report):

No Air Monitoring was taken today. Air Monitoring is currently suspended until excavation activities resume. Once excavation activities resume the CAMP monitoring procedures will resume.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

HP Soldier Piles will continue to be installed along 26th Street and 8th Ave.

The waste classification soil results have been received. The results along with waste profiles have been submitted to various facilities for disposal approval. Once approval is received, the approval letters will be forwarded to OER and arrangements will be made to commence excavation activities after the soldier piles are completed.

 File Name: Example:

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Solid		Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
Totals (trucks, cu.yds.)	30	750								

Site Grid Map

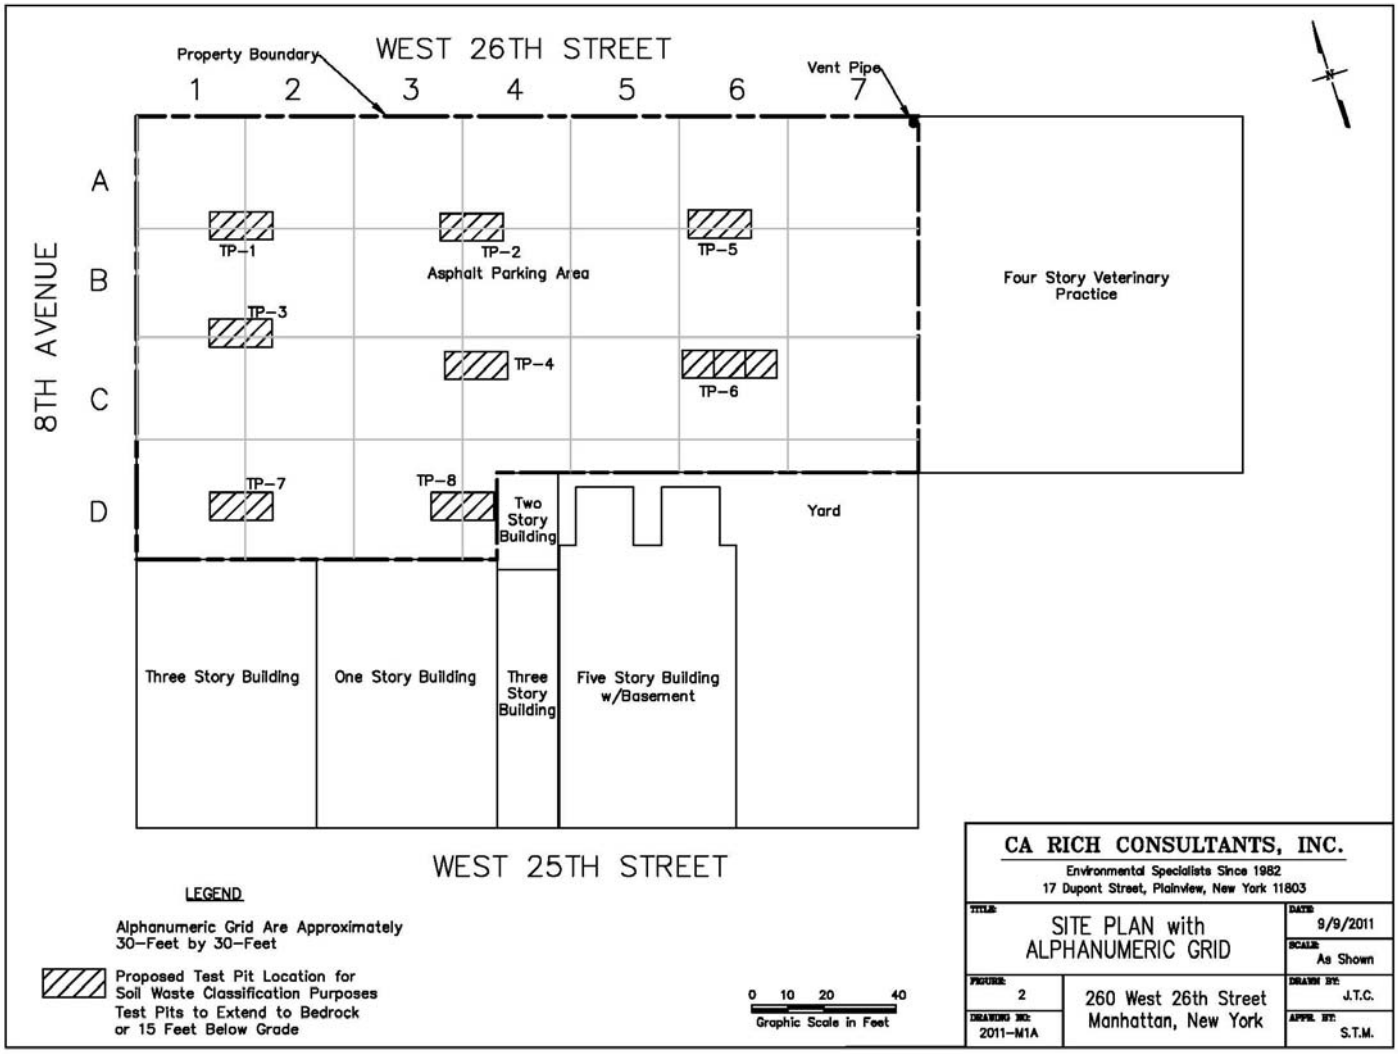

 File Name: _____

Photo Log

Photo 1 – Verifying Piles are located on the edge of the property line. (Red String represents property line)	
Photo 2 – Excavator moving metal casings for drilling machine.	
Photo 3 – Drilling machine moving to set up to drill next pile location.	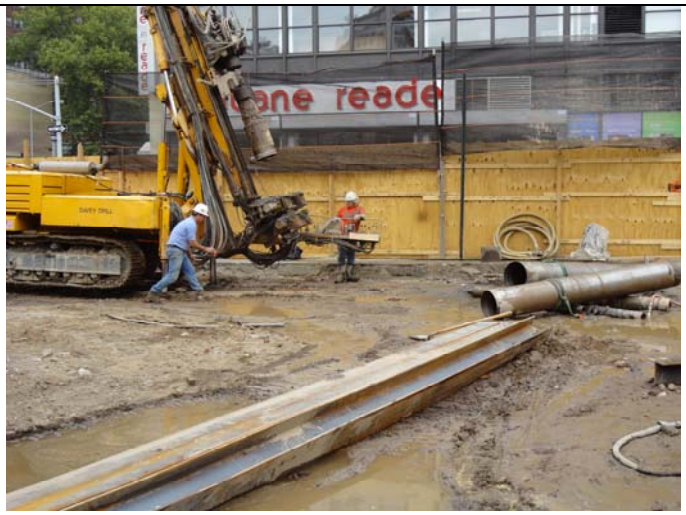

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50		50-70		70-85	X	>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	9-22-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Continued installing HP Soldier Piles along 26th Street. Three additional piles were installed today for a total of twenty-three HP Soldier Piles installed on site.

Since piles were driven within 50'-0" of the MTA Subway line, both an MTA inspector and a Vibration Monitoring Company were on site oversee and monitor all Piles being driven close to the subway tunnel.

Soil Stockpiles on site continue to remain covered. They were inspected today, and no problems have occurred.

Working In Grid #: A1, A2

Air Monitoring (Since Last Report):

No Air Monitoring was taken today. Air Monitoring is currently suspended until excavation activities resume. Once excavation activities resume the CAMP monitoring procedures will resume.

Problems Encountered:
No problems were encountered.

Planned Activities for Next Week:

HP Soldier Piles will continue to be installed along 26th Street and 8th Ave.

The waste classification soil results have been received. The results along with waste profiles have been submitted to various facilities for disposal approval. Once approval is received, the approval letters will be forwarded to OER and arrangements will be made to commence excavation activities after the soldier piles are completed.

 File Name: _____

Example:

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Solid		Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
Totals (trucks, cu.yds.)	30	750								

Site Grid Map

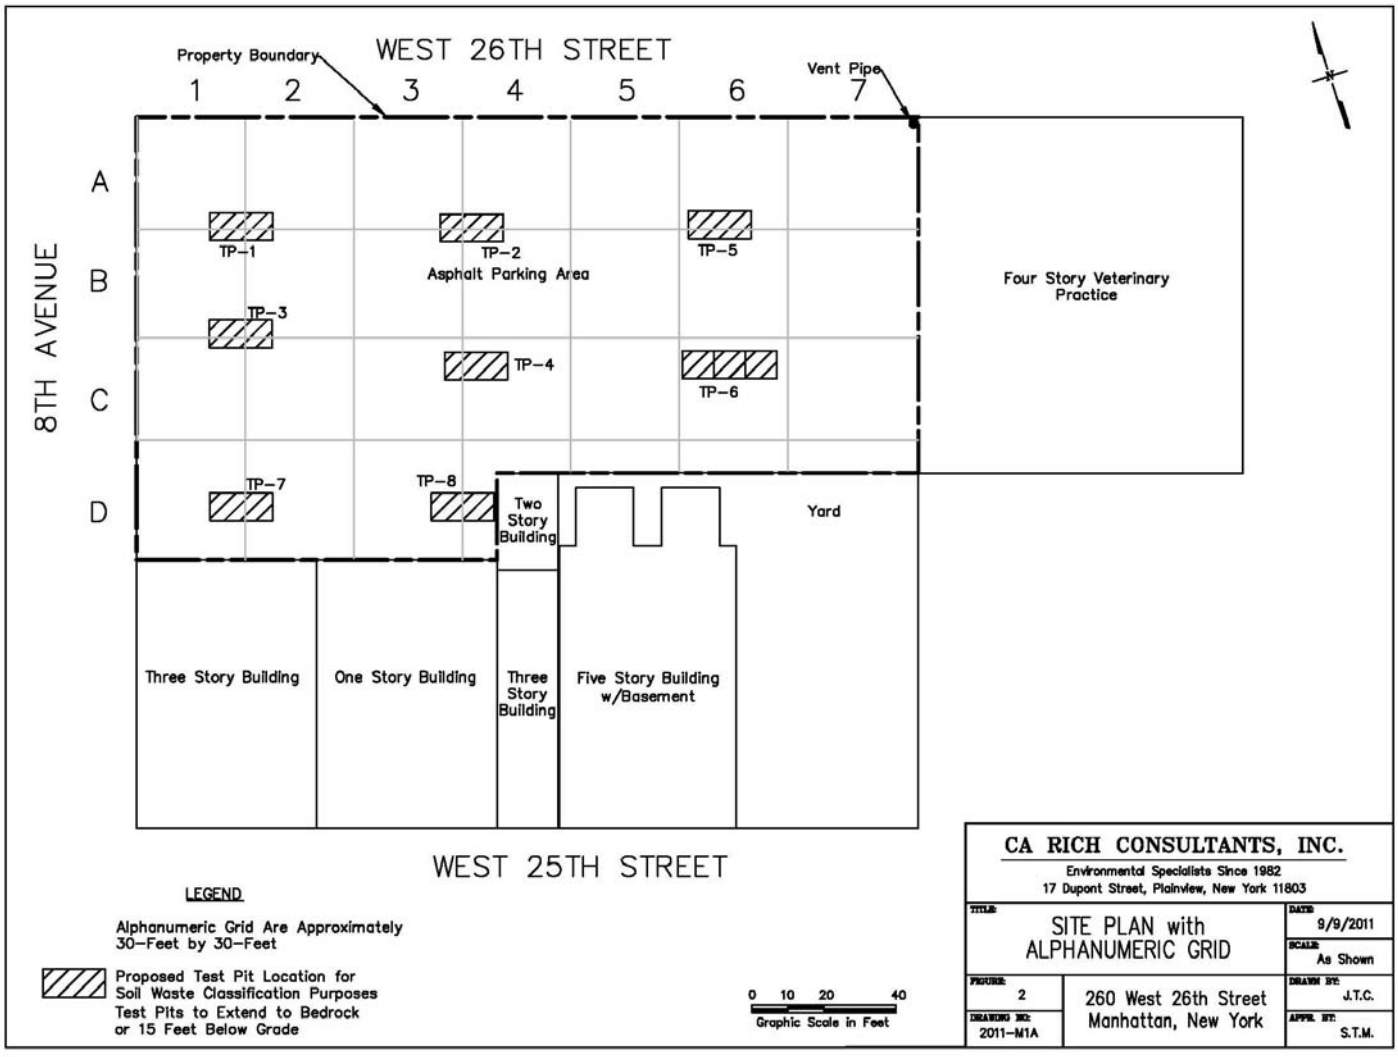

 File Name: _____

Photo Log

Photo 1 – (23) HP Soldier Piles are currently installed along 26th Street. Soil Stockpiles remain covered and are inspected on a daily basis. No problems have occurred.	
Photo 2 – Machine drilling Pile #28.	
Photo 3 – West Property Line was marked today (pink string) in preparation to begin piles along 8th Ave. tomorrow and next week.	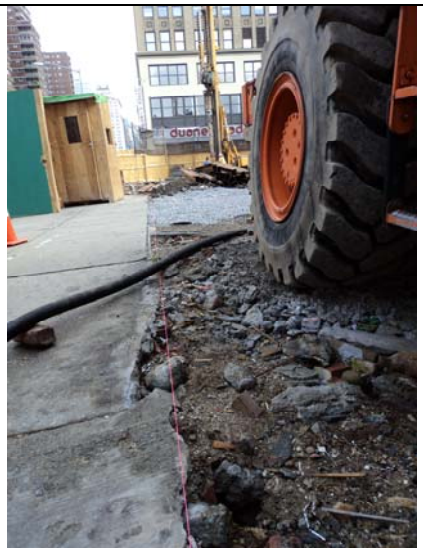

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain	X	Overcast		Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50		50-70		70-85	X	>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	9-23-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Continued installing HP Soldier Piles along 26th Street. Three additional piles were installed today for a total of twenty-six HP Soldier Piles installed on site.

Since piles were driven within 50'-0" of the MTA Subway line, both an MTA inspector and a Vibration Monitoring Company were on site oversee and monitor all Piles being driven close to the subway tunnel.

Soil Stockpiles on site continue to remain covered. They were inspected today, and no problems have occurred.

Working In Grid #: A1, A2

Air Monitoring (Since Last Report):

No Air Monitoring was taken today. Air Monitoring is currently suspended until excavation activities resume. Once excavation activities resume the CAMP monitoring procedures will resume.

Problems Encountered:
No problems were encountered.

Planned Activities for Next Week:

HP Soldier Piles will continue to be installed along 26th Street and 8th Ave.

The waste classification soil results have been received. The results along with waste profiles have been submitted to various facilities for disposal approval. Once approval is received, the approval letters will be forwarded to OER and arrangements will be made to commence excavation activities after the soldier piles are completed.

 File Name: _____

Example:

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Solid		Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
Totals (trucks, cu.yds.)	30	750								

Site Grid Map

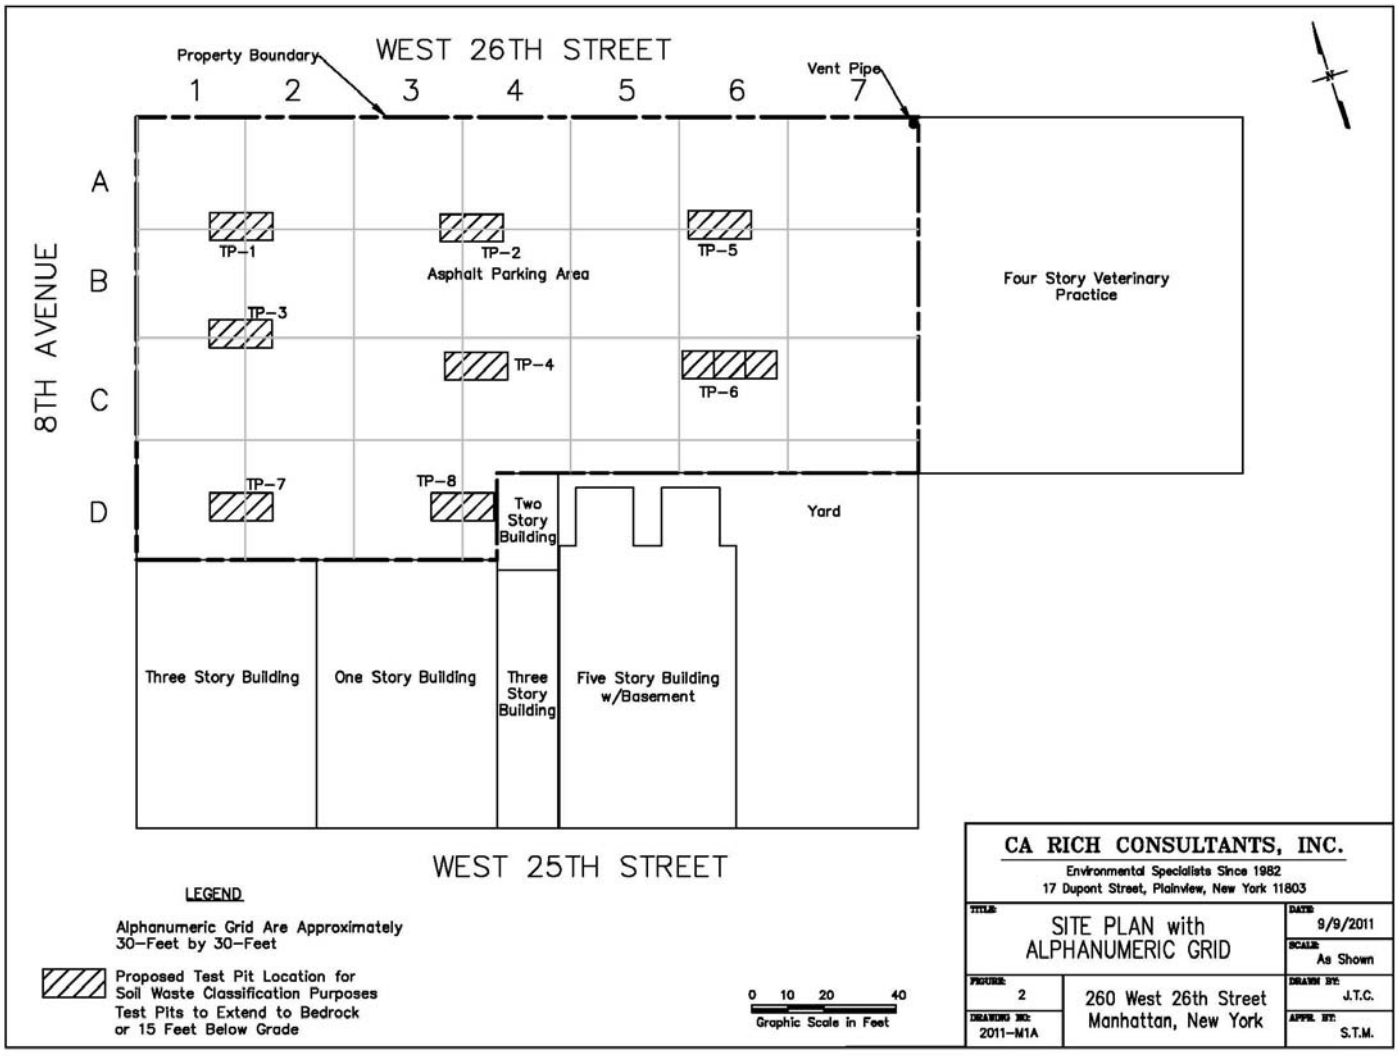

 File Name: _____

Photo Log

Photo 1 – Soil Stockpiles remain fully covered. Stockpiles were inspected multiple times today due to the large amount of rain. No problems have occurred.	
Photo 2 – Machine drilling Pile #27.	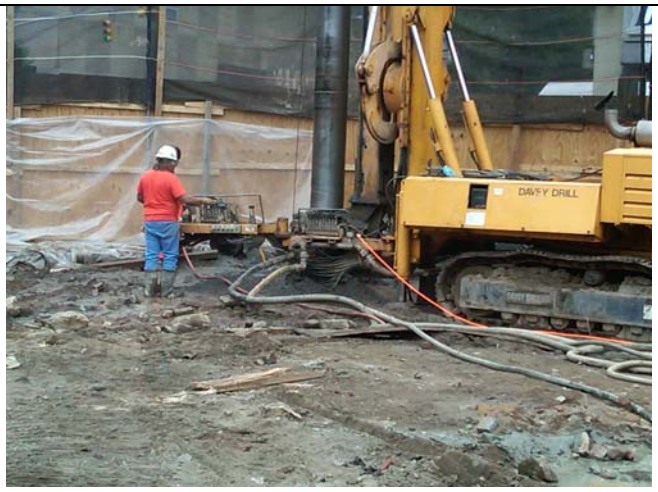
Photo 3 – Workers preparing to drill Pile #29.	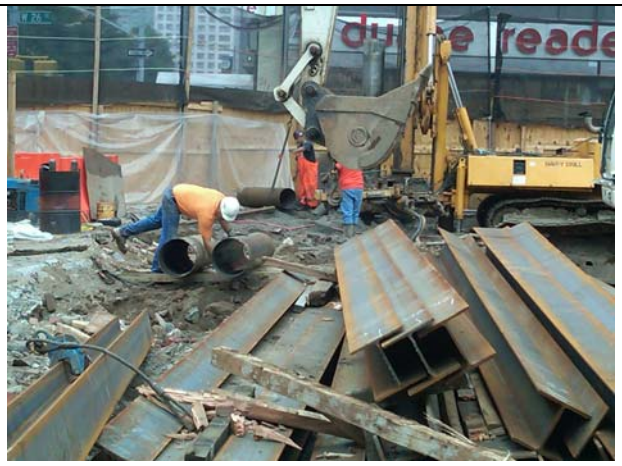

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70		70-85	X	>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	9-26-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Continued installing HP Soldier Piles along 26th Street. One additional pile was installed today for a total of twenty-seven HP Soldier Piles installed on site.

Since piles were driven within 50'-0" of the MTA Subway line, both an MTA inspector and a Vibration Monitoring Company were on site oversee and monitor all Piles being driven close to the subway tunnel.

Soil Stockpiles on site continue to remain covered. They were inspected today, and no problems have occurred.

Working In Grid #: A1

Air Monitoring (Since Last Report):

No Air Monitoring was taken today. Air Monitoring is currently suspended until excavation activities resume. Once excavation activities resume the CAMP monitoring procedures will resume.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

HP Soldier Piles will be completed along 26th Street. Piles to continue to be installed along 8th Ave and begin being installed along the South Property Line.

The waste classification soil results have been received. The results along with waste profiles have been submitted to various facilities for disposal approval. Once approval is received, the approval letters will be forwarded to OER and arrangements will be made to commence excavation activities after the soldier piles are completed.

 File Name: _____

Example:

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Solid		Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
Totals (trucks, cu.yds.)	30	750								

Site Grid Map

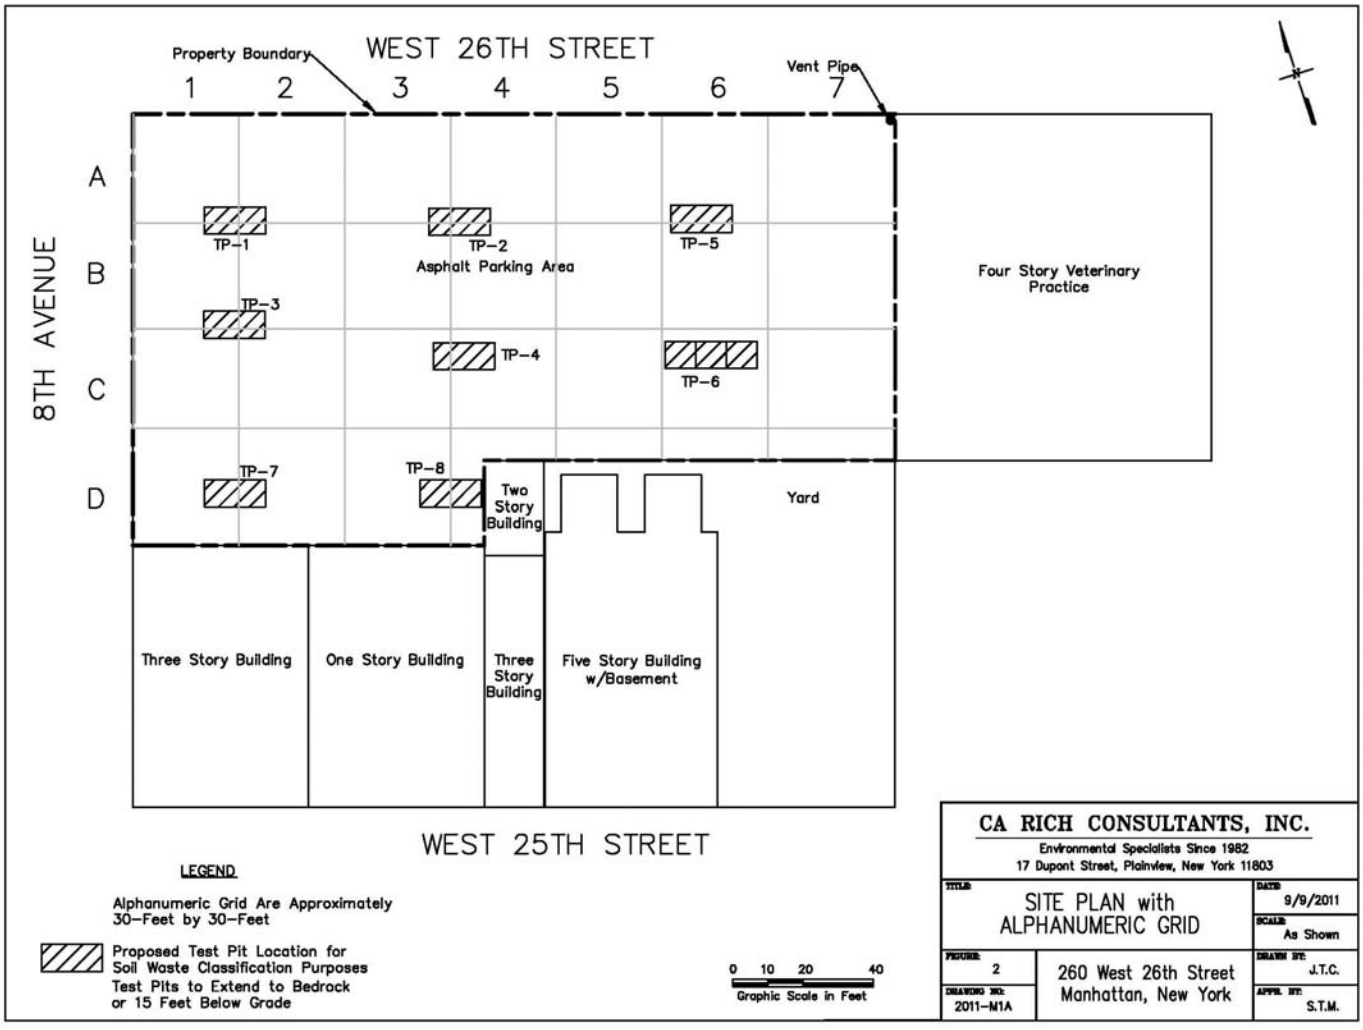

 File Name: _____

Photo Log

Photo 1 – Workers lowering HP Pile #23 along 26th Street into casing.	
Photo 2 – Marking out location where HP Piles are to be installed along 8th Ave.	
Photo 3 – Workers drilling first pile along 8th Ave.	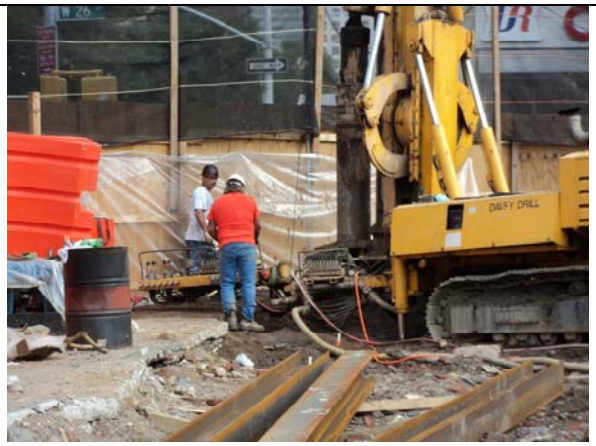

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70		70-85	X	>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	9-27-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Continued installing HP Soldier Piles along 26th Street. Three additional piles were installed today for a total of thirty HP Soldier Piles installed on site. All piles along 26th Street have been installed. Tomorrow we will begin installing piles along the south property line.

There was a planned DOB site visit today.

Soil Stockpiles on site continue to remain covered. They were inspected today, and no problems have occurred.

Working In Grid #: A7

Air Monitoring (Since Last Report):

No Air Monitoring was taken today. Air Monitoring is currently suspended until excavation activities resume. Once excavation activities resume the CAMP monitoring procedures will resume.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

Piles to be installed along the south property line and along 8th Ave.

The waste classification soil results have been received. The results along with waste profiles have been submitted to various facilities for disposal approval. Once approval is received, the approval letters will be forwarded to OER and arrangements will be made to commence excavation activities after the soldier piles are completed.

 File Name: _____

Example:

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Solid		Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
Totals (trucks, cu.yds.)	30	750								

Site Grid Map

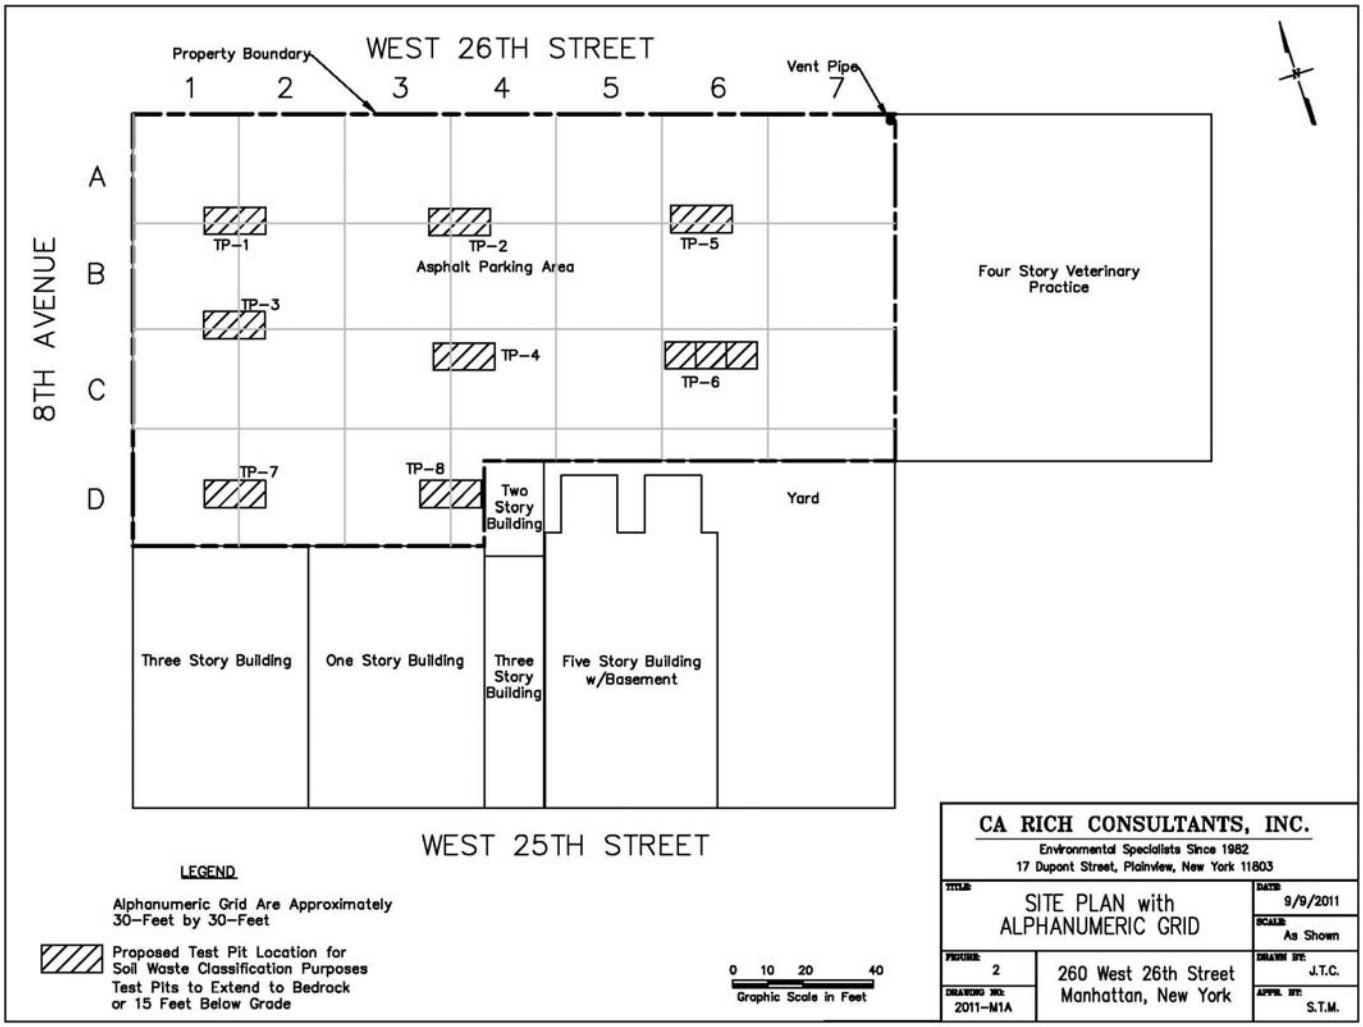

 File Name: _____

Photo Log

Photo 1 – Workers lowering #3 HP Pile into metal casing.	
Photo 2 – Soil Stockpiles remain fully covered and are inspected daily. No problems have occurred.	
Photo 3 – Workers drilling Pile #1 in Northeast corner of site.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain		Overcast	X	Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50		50-70		70-85	X	>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	9-28-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Began installing piles along south property line. Three piles were installed today for a total of 33 piles installed on site. Tomorrow we will continue to install piles along the south property line.

Soil Stockpiles on site continue to remain covered. They were inspected today, and no problems have occurred.

Working In Grid #: D7

Air Monitoring (Since Last Report):

No Air Monitoring was taken today. Air Monitoring is currently suspended until excavation activities resume. Once excavation activities resume the CAMP monitoring procedures will resume.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

Piles to be installed along the south property line and along 8th Ave.

The waste classification soil results have been received. The results along with waste profiles have been submitted to various facilities for disposal approval. Once approval is received, the approval letters will be forwarded to OER and arrangements will be made to commence excavation activities after the soldier piles are completed.

Example:

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Solid		Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
Totals (trucks, cu.yds.)	30	750								

Site Grid Map

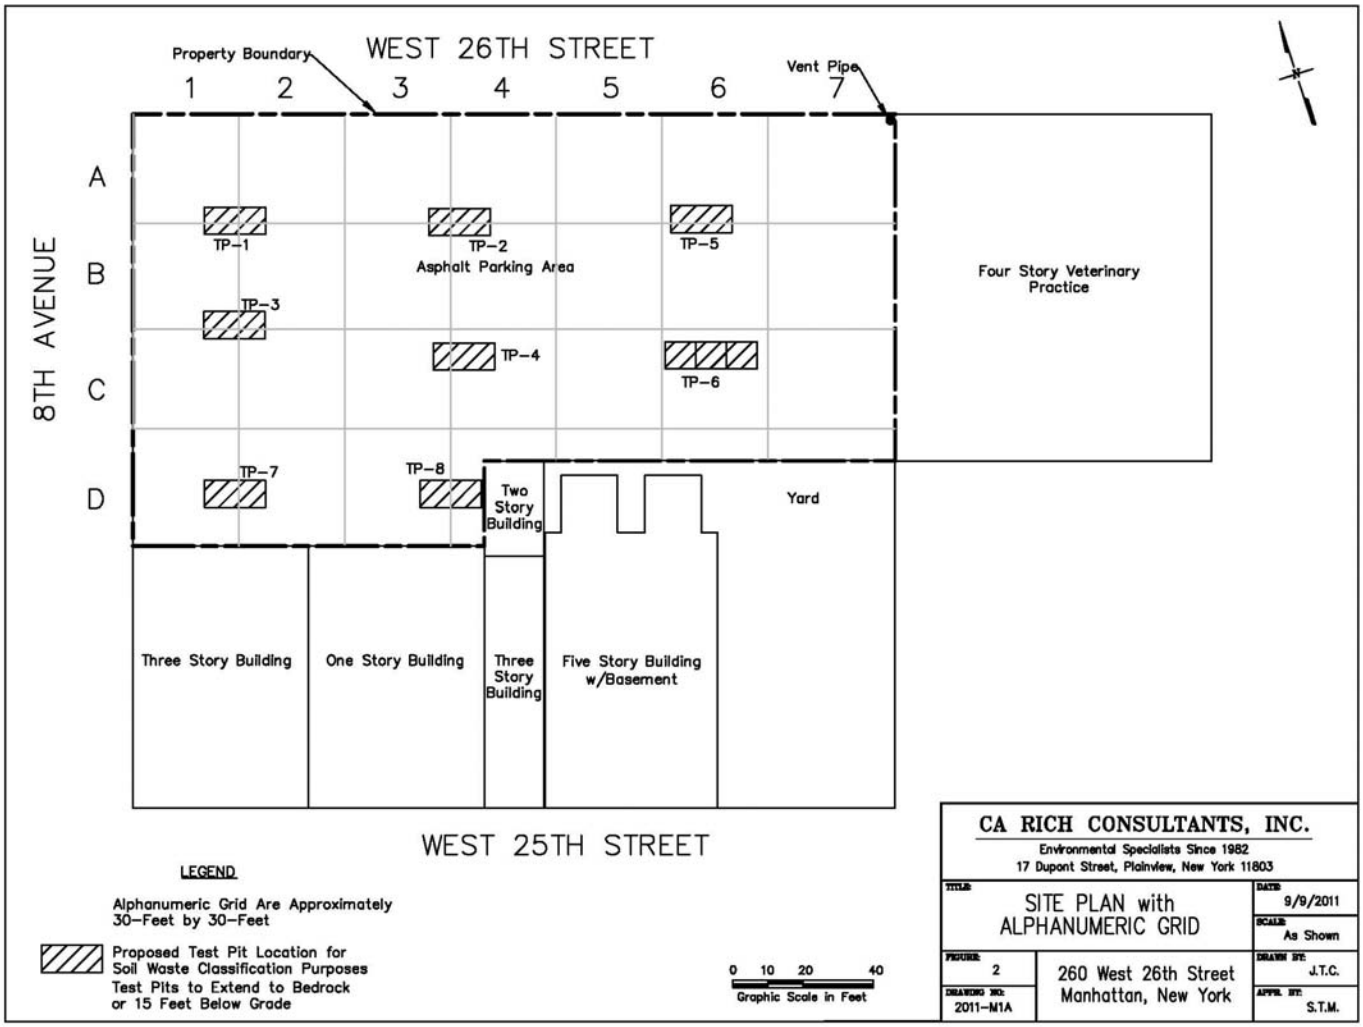

 File Name: _____

Photo Log

Photo 1 – Drilling machine setting up to drill the first HP Pile along the South Property line. Stakes in ground represent location of future piles to be installed later this week.	
Photo 2 – Drilling machine drilling Pile #1 along south property line.	
Photo 3 – Piles #2 and #3 installed along the south property line. Drilling machine is setting up to drill Pile #4.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain		Overcast	X	Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50		50-70		70-85	X	>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	9-29-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Continued installing piles along south property line. Four piles were installed today for a total of 37 piles installed on site. Tomorrow we will continue to install piles along the south property line.

Soil Stockpiles on site continue to remain covered. They were inspected today, and no problems have occurred.

Working In Grid #: D6 & D7

Air Monitoring (Since Last Report):

No Air Monitoring was taken today. Air Monitoring is currently suspended until excavation activities resume. Once excavation activities resume the CAMP monitoring procedures will resume.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

Piles to be installed along the south property line and along 8th Ave.

The waste classification soil results have been received. The results along with waste profiles have been submitted to various facilities for disposal approval. Once approval is received, the approval letters will be forwarded to OER and arrangements will be made to commence excavation activities after the soldier piles are completed.

Example:

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Solid		Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
Totals (trucks, cu.yds.)	30	750								

Site Grid Map

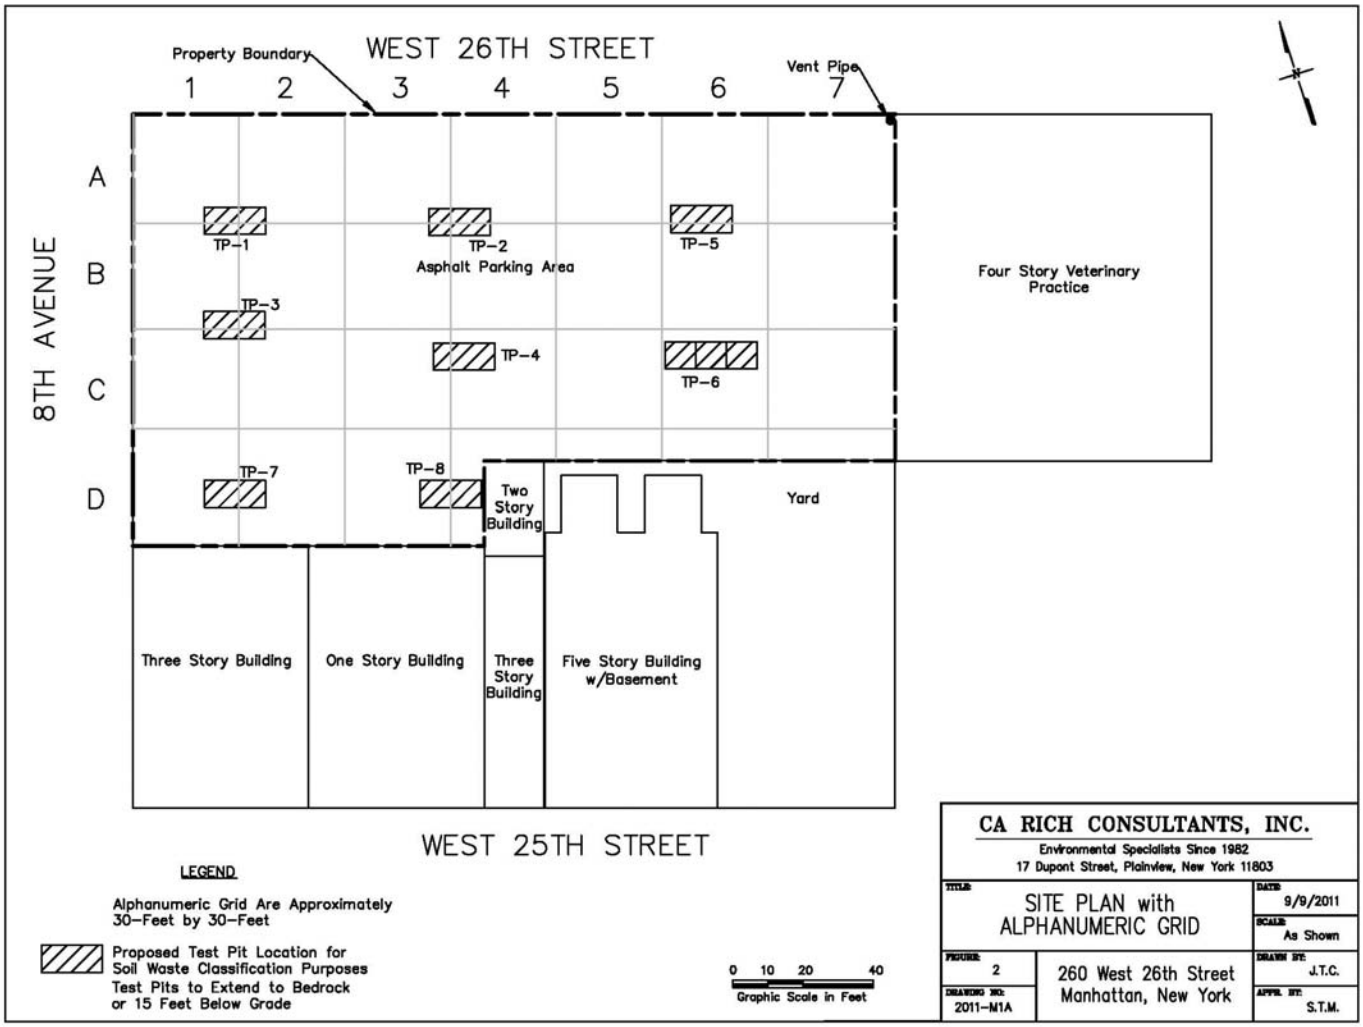

 File Name: _____

Photo Log

Photo 1 – Drilling machine lowering in HP Pile for Pile #4 along South Property Line.	
Photo 2 – Drilling machine drilling Pile #6 along south property line.	
Photo 3 – Plastic installed to keep all soil, water, etc. from going under construction fence into neighbor's property when future HP Piles are drilled.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70		70-85	X	>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	9-30-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Continued installing piles along south property line. Three piles were installed today for a total of 40 piles installed on site. Tomorrow we will continue to install piles along the south property line.

Soil Stockpiles on site continue to remain covered. They were inspected today, and no problems have occurred.

Working In Grid #: D6

Air Monitoring (Since Last Report):

No Air Monitoring was taken today. Air Monitoring is currently suspended until excavation activities resume. Once excavation activities resume the CAMP monitoring procedures will resume.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

Piles to be installed along the south property line and along 8th Ave.

The waste classification soil results have been received. The results along with waste profiles have been submitted to various facilities for disposal approval. Once approval is received, the approval letters will be forwarded to OER and arrangements will be made to commence excavation activities after the soldier piles are completed.

Example:

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Solid		Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
Totals (trucks, cu.yds.)	30	750								

Site Grid Map

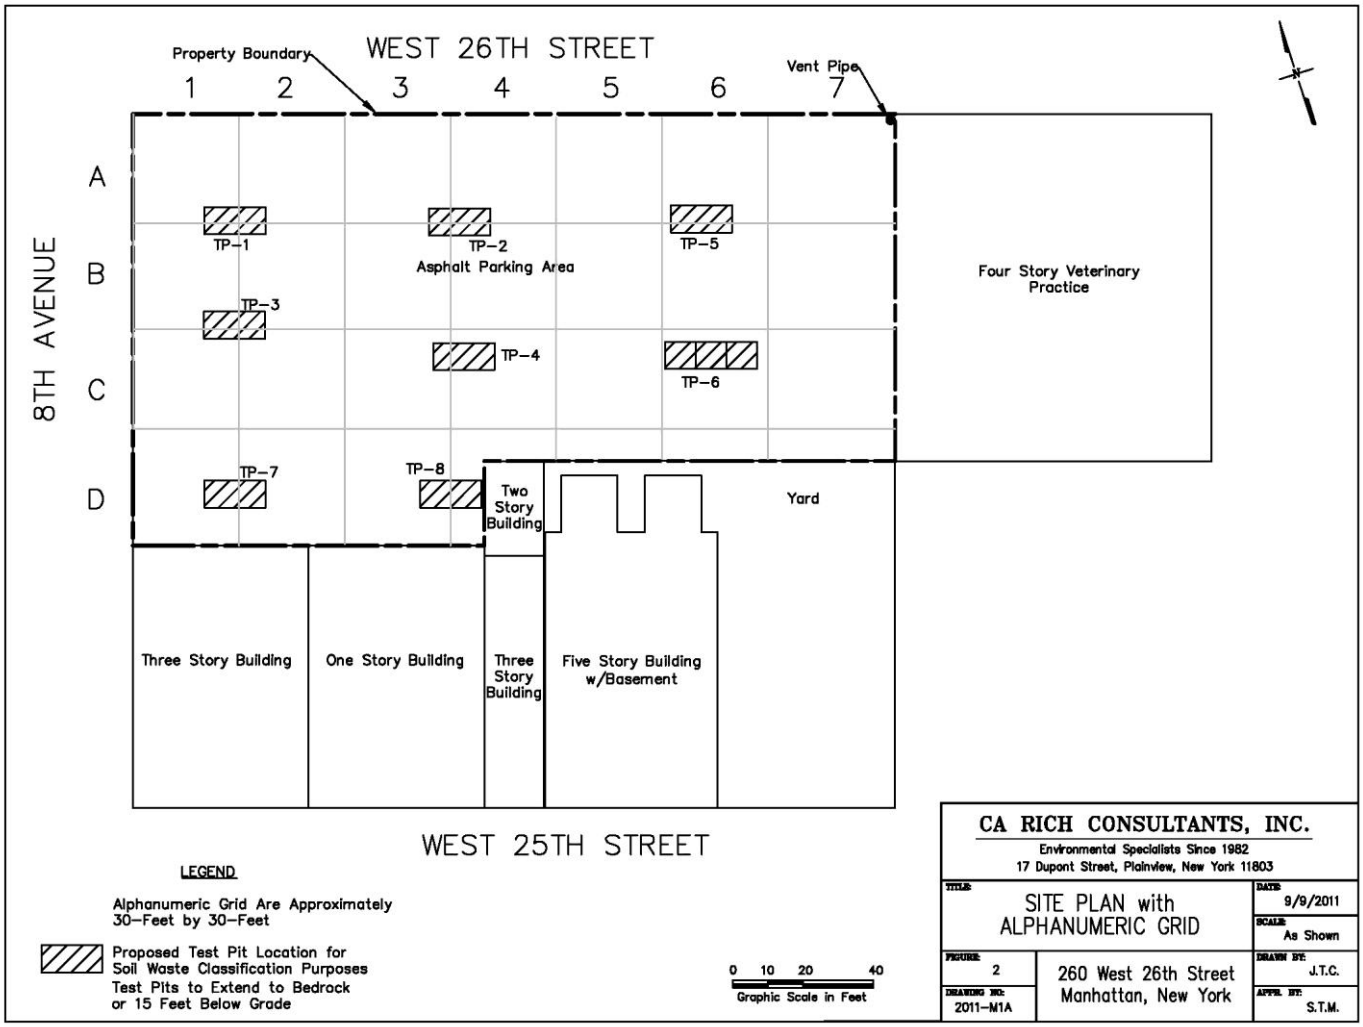

 File Name: _____

Photo Log

Photo 1 – HP Soldier Piles currently installed along south property line.	
Photo 2 – Drilling machine drilling Pile #9 along south property line.	
Photo 3 – Drilling machine lowering HP Soldier Pile #9 into metal casing.	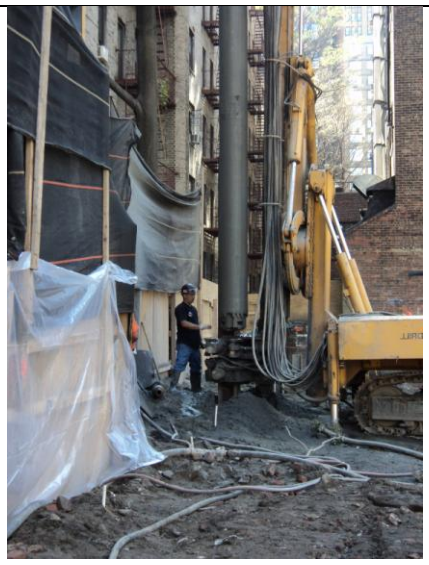

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	10-03-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Continued installing piles along south property line. Three piles were installed today for a total of 43 piles installed on site. Tomorrow we will continue to install piles along the south property line.

Soil Stockpiles on site continue to remain covered. They were inspected today, and no problems have occurred.

Working In Grid #: D5 & D6

Air Monitoring (Since Last Report):

No Air Monitoring was taken today. Air Monitoring is currently suspended until excavation activities resume. Once excavation activities resume the CAMP monitoring procedures will resume.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

Piles to be installed along the south property line and along 8th Ave.

The waste classification soil results have been received. The results along with waste profiles have been submitted to various facilities for disposal approval. Once approval is received, the approval letters will be forwarded to OER and arrangements will be made to commence excavation activities after the soldier piles are completed.

Example:

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Solid		Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
Totals (trucks, cu.yds.)	30	750								

Site Grid Map

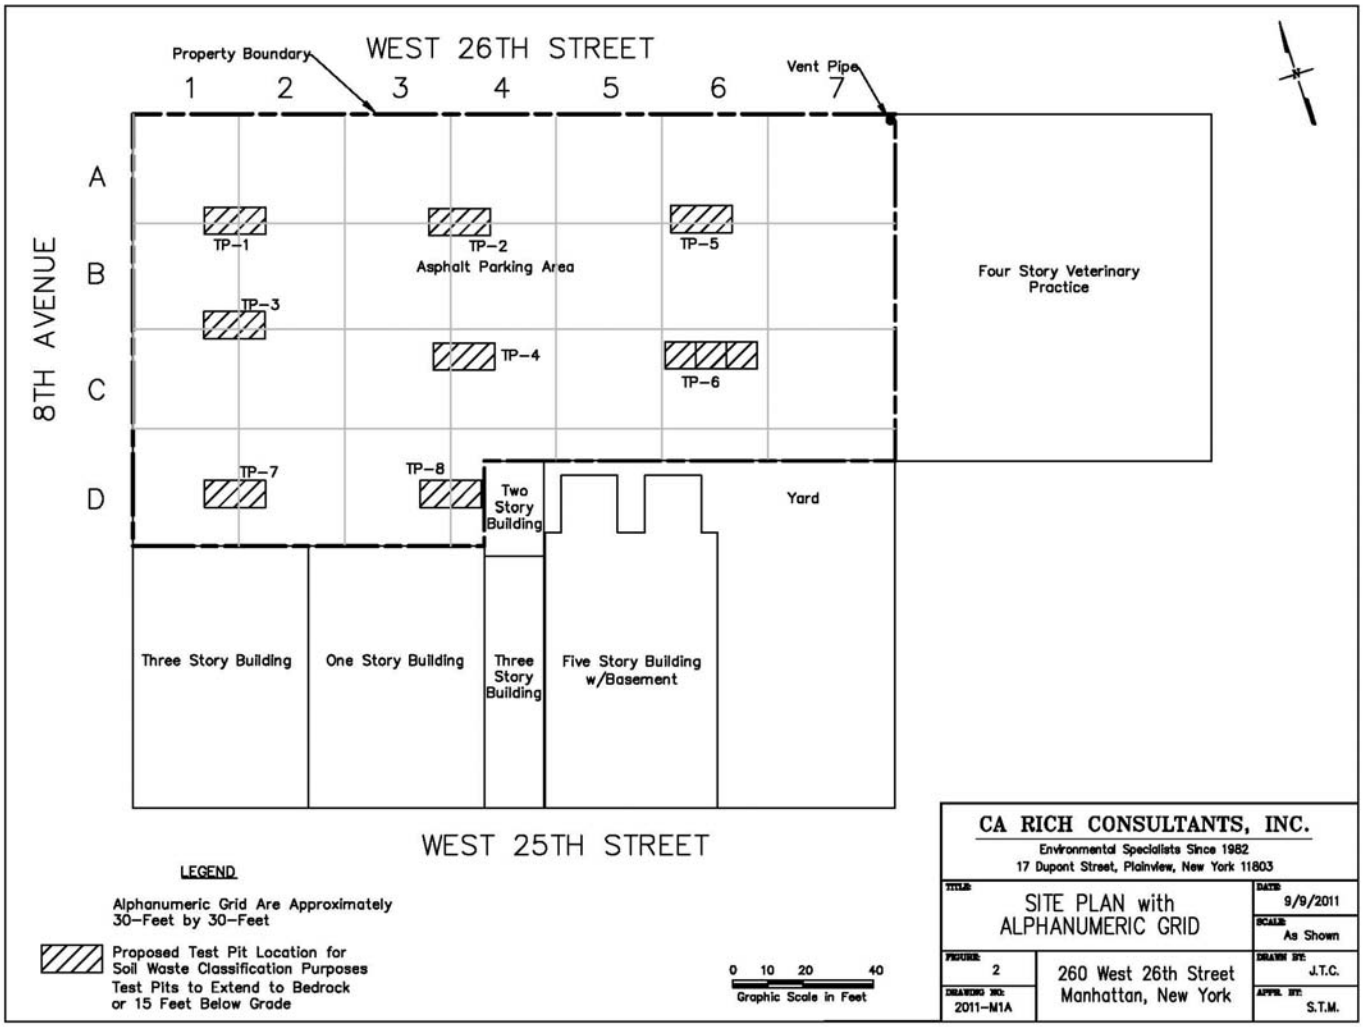

 File Name: _____

Photo Log

Photo 1 – Drilling machine lining up to drill HP Pile #12 along the South Property line.	
Photo 2 – Drilling machine lowering HP Pile #12 into metal casing.	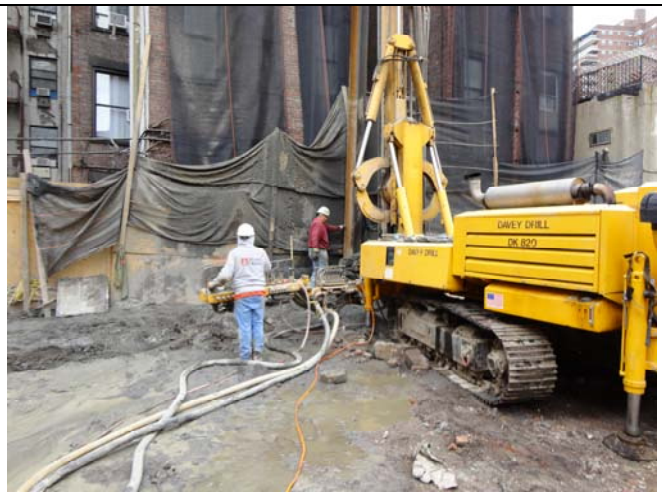
Photo 3 – Machine drilling HP Pile #11 along South Property line.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	10-04-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Completed piles along south property line. Four piles were installed today for a total of 47 piles installed on site. Tomorrow three truckloads of soil from test pits TP-5 and TP-7 will be excavated and transported to the Clean Earth of North Jersey site as soil containing hazardous levels of lead. During this activity CA RICH Consultants will be on-site to oversee the excavation activities and conduct the CAMP monitoring. After the soil removal, confirmatory soil samples will be collected from the excavation perimeter to confirm the lead contaminated soil has been adequately removed.

Soil Stockpiles on site continue to remain covered. They were inspected today, and no problems have occurred.

Working In Grid #: D5

Air Monitoring (Since Last Report):

No Air Monitoring was taken today. Air Monitoring is currently suspended until excavation activities resume. Once excavation activities resume the CAMP monitoring procedures will resume.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

HP Soldier Piles will begin to be installed along 8th Ave.

The waste classification soil results have been received. The results along with waste profiles have been submitted to various facilities for disposal approval. Once approval is received, the approval letters will be forwarded to OER and arrangements will be made to commence excavation activities after the soldier piles are completed.

 File Name: _____

Example:

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Solid		Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
Totals (trucks, cu.yds.)	30	750								

Site Grid Map

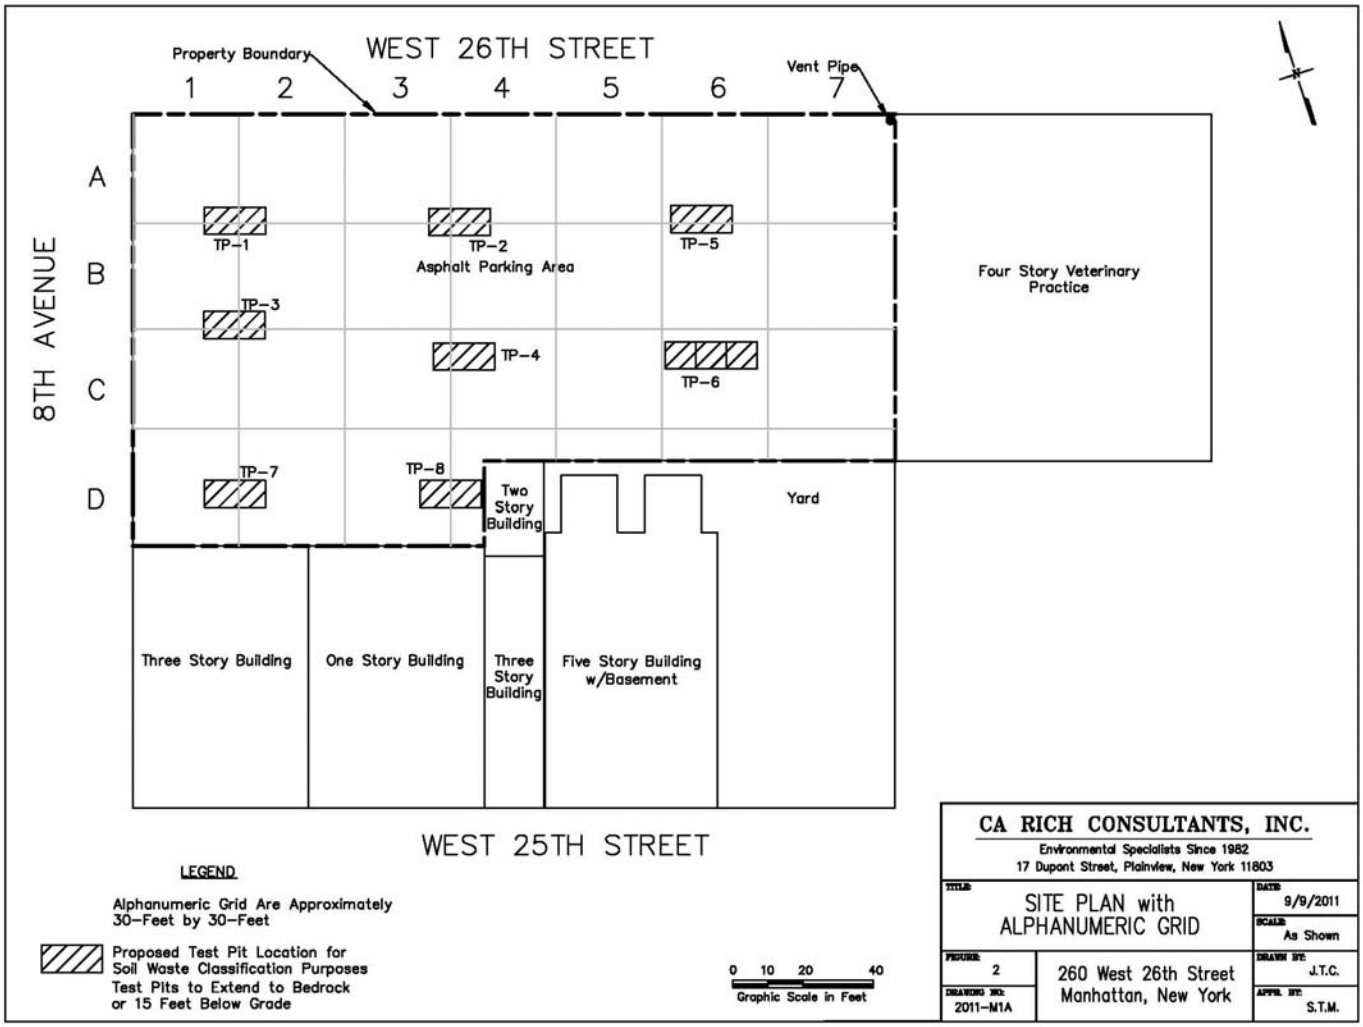

 File Name: _____

Photo Log

Photo 1 – Machine drilling HP Pile #14 along South Property line.	
Photo 2 – Drilling machine setting up to drill Pile #15.	
Photo 3 – HP Pile #15 grouted into place along South Property line.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Steve Malinowski of CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	10-05-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jason Cooper
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Three truckloads of soil from test pits TP-5 and TP-7 were excavated and transported to the Clean Earth of North Jersey site as soil containing hazardous levels of lead. After the soil removal, confirmatory soil samples were collected from the excavation perimeter to confirm the lead contaminated soil has been adequately removed. A small pile of additional soil stockpiled and covered for disposal at a later date.

Soil Stockpiles on-site continue to remain covered. They were inspected today, and no problems have occurred.

Working In Grids #: A6, B6, D1 and D2

Air Monitoring (Since Last Report):

Air Monitoring was conducted during today's excavation activities. No problems were encountered.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

HP Soldier Piles will begin to be installed along 8th Ave.

Example:

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
			3	Appr. 70						
Totals (trucks, cu.yds.)	30	750								

Site Grid Map

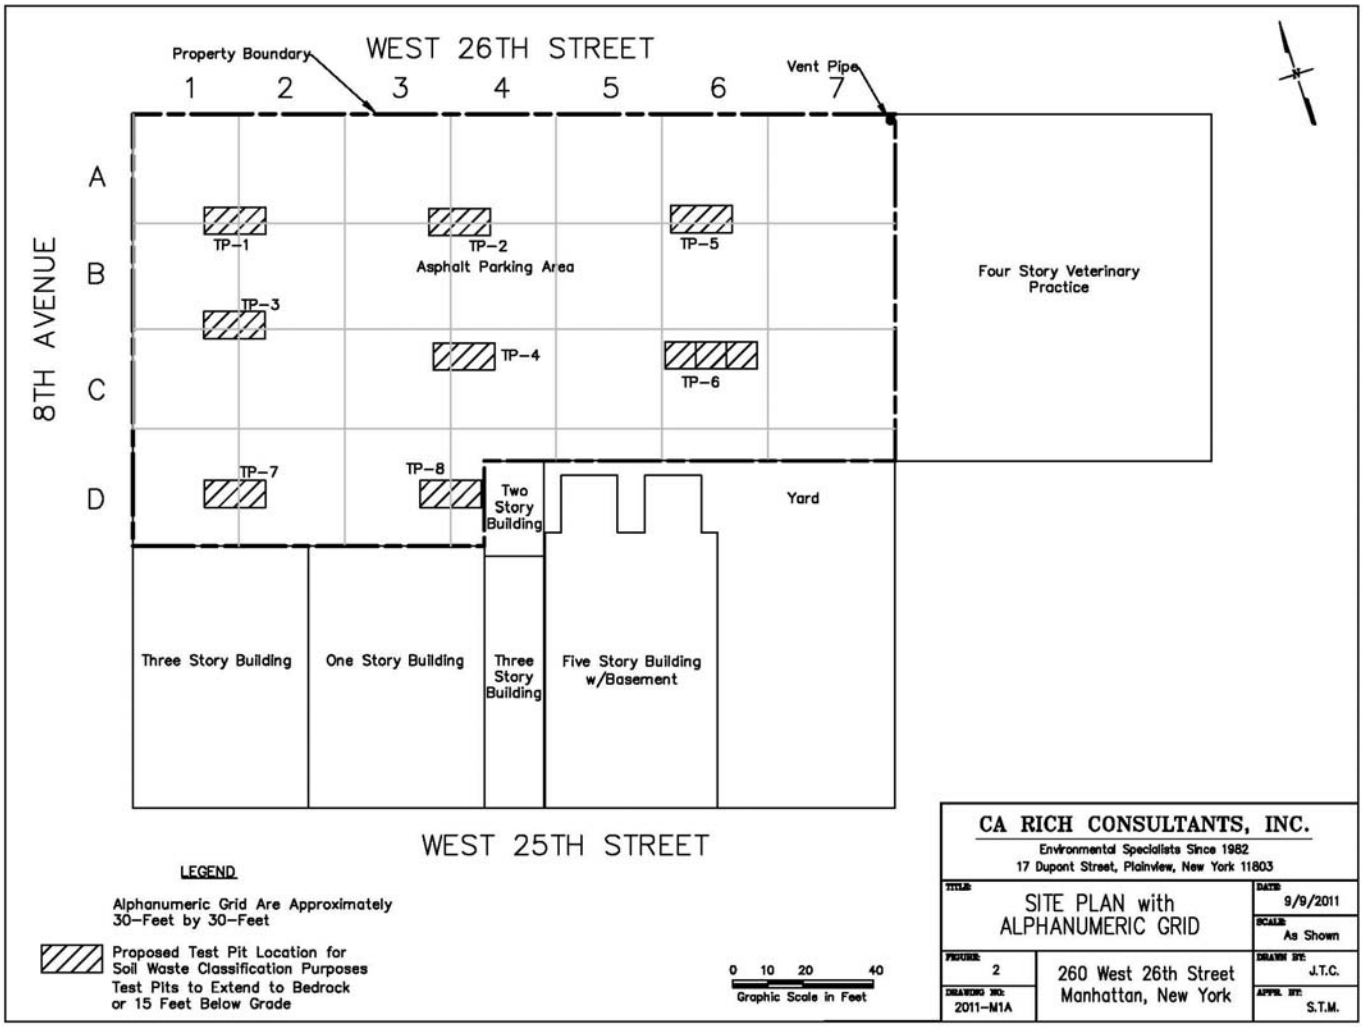

 File Name: _____

Photo Log

Photo 1 –	
Photo 2 – .	
Photo 3 –	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	10-06-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

CA Rich received the results for the soil samples collected after the removal of the haz-lead test pits yesterday. Two samples failed for TCLP lead indicating additional haz-lead soil is still present in TP-7 east and TP-5 north. Tomorrow after the first truck is loaded from the current stockpile, CA Rich will remove an additional five feet of soil from the east sidewall of test pit TP-7 and the north sidewall of test pit TP-5. The soil will be sent to Clean Earth of North Jersey. After the soil removal, confirmatory soil samples will be collected from the excavation perimeter to confirm the remaining lead contaminated soil has been adequately removed.

On site today, brick, concrete, asphalt, etc. was separated from the soil stockpiles. Also, a test pit was dug next to a neighboring building to verify if underpinning would be needed when excavation occurs in the weeks to come.

A note that was not included in yesterday's report: FDNY was on site yesterday to inspect. They issued a warning because a Fire Safety Manager was not present on site at the time. The warning states the issue must be taken care of within 30 days, and Artimus Construction ensures this will be resolved immediately.

Soil Stockpiles on site continue to remain covered. They were inspected today, and no problems have occurred.

Working In Grid #: B3, B4, B5, C3, C4, C5, D3, D4, D5,

Air Monitoring (Since Last Report):

Air monitoring was conducted today, no problems were encountered.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

HP Soldier Piles will begin to be installed along 8th Ave.

 File Name: _____

Example:

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
			3	Appr. 70						
Totals (trucks, cu.yds.)	30	750	3	70						

Site Grid Map

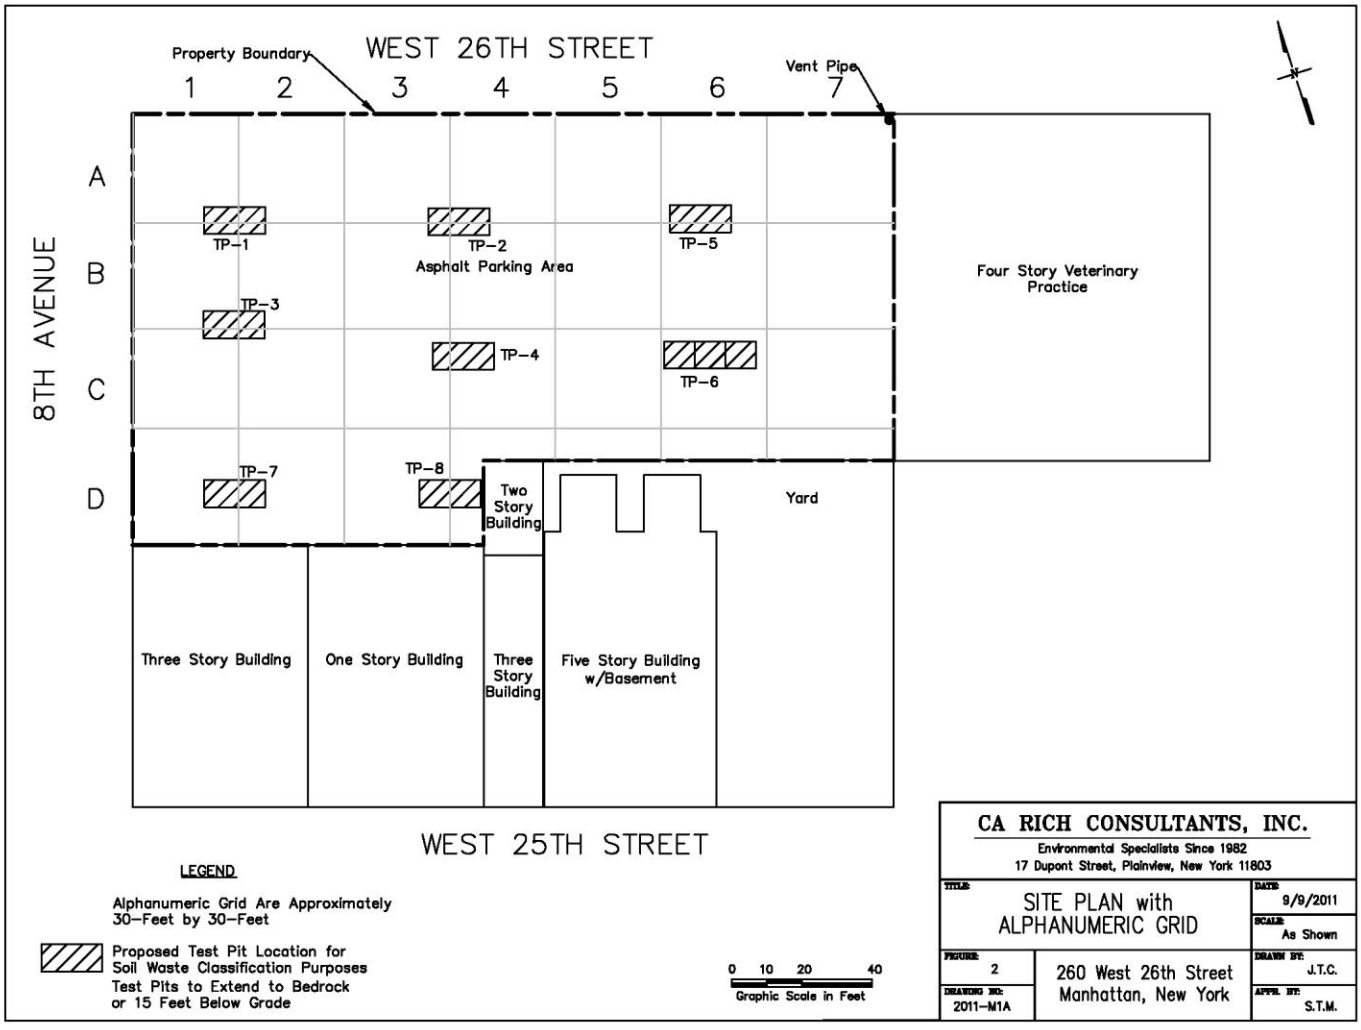

 File Name: _____

Photo Log

Photo 1 – Removing lead contaminated soil in TP-5 and filling truck to properly dispose of soil at Clean Earth of North Jersey.	
Photo 2 – Ensuring all contaminated soil is washed off truck's tires and undercarriage before trucks leave the site.	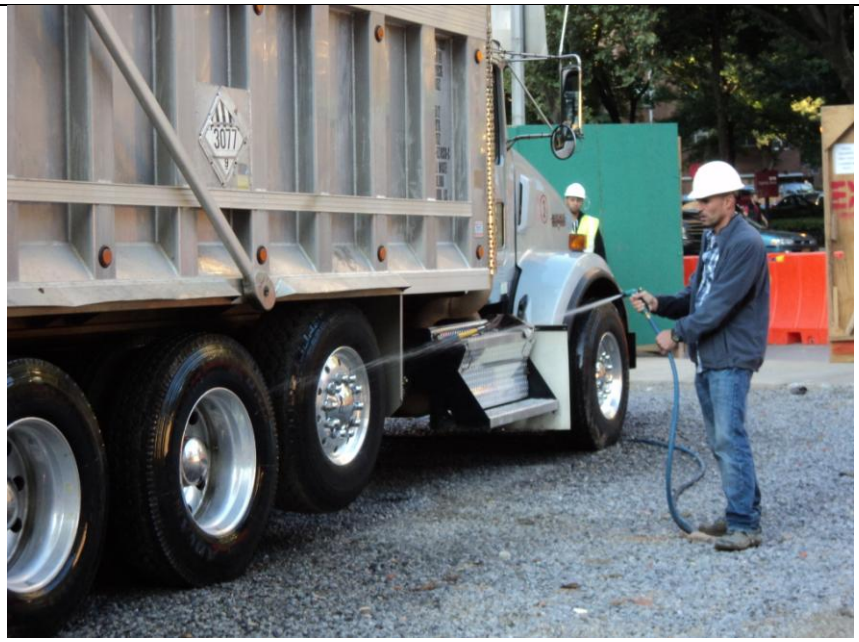

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70		70-85	X	>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	10-08-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Six truckloads of brick, asphalt, and concrete were transported to Bayshore Recycling in Woodbridge, NJ. No soil was removed from the site.

Lagging along the south property line began. Minor excavation of soil from TP-6 area occurred due to lagging being installed. Soil was sorted and stockpiled to be transported to Soil Safe on Monday morning.

Working In Grid #: D5, D6, D7

Air Monitoring (Since Last Report):

Air Monitoring was conducted during today's excavation activities. No problems were encountered.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

HP Soldier Piles will begin to be installed along 8th Ave.

Soil will continued to be sorted and stockpiled and transported to the approved the approved. CA Rich will be on site during all excavation activities to oversee and ensure the Remedial Action Work Plan and CAMP Air Monitoring Plan is carried out according to OER specifications.

Example:

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
	6	150								
Totals (trucks, cu.yds.)	30	750	7	175	7	175				

Site Grid Map

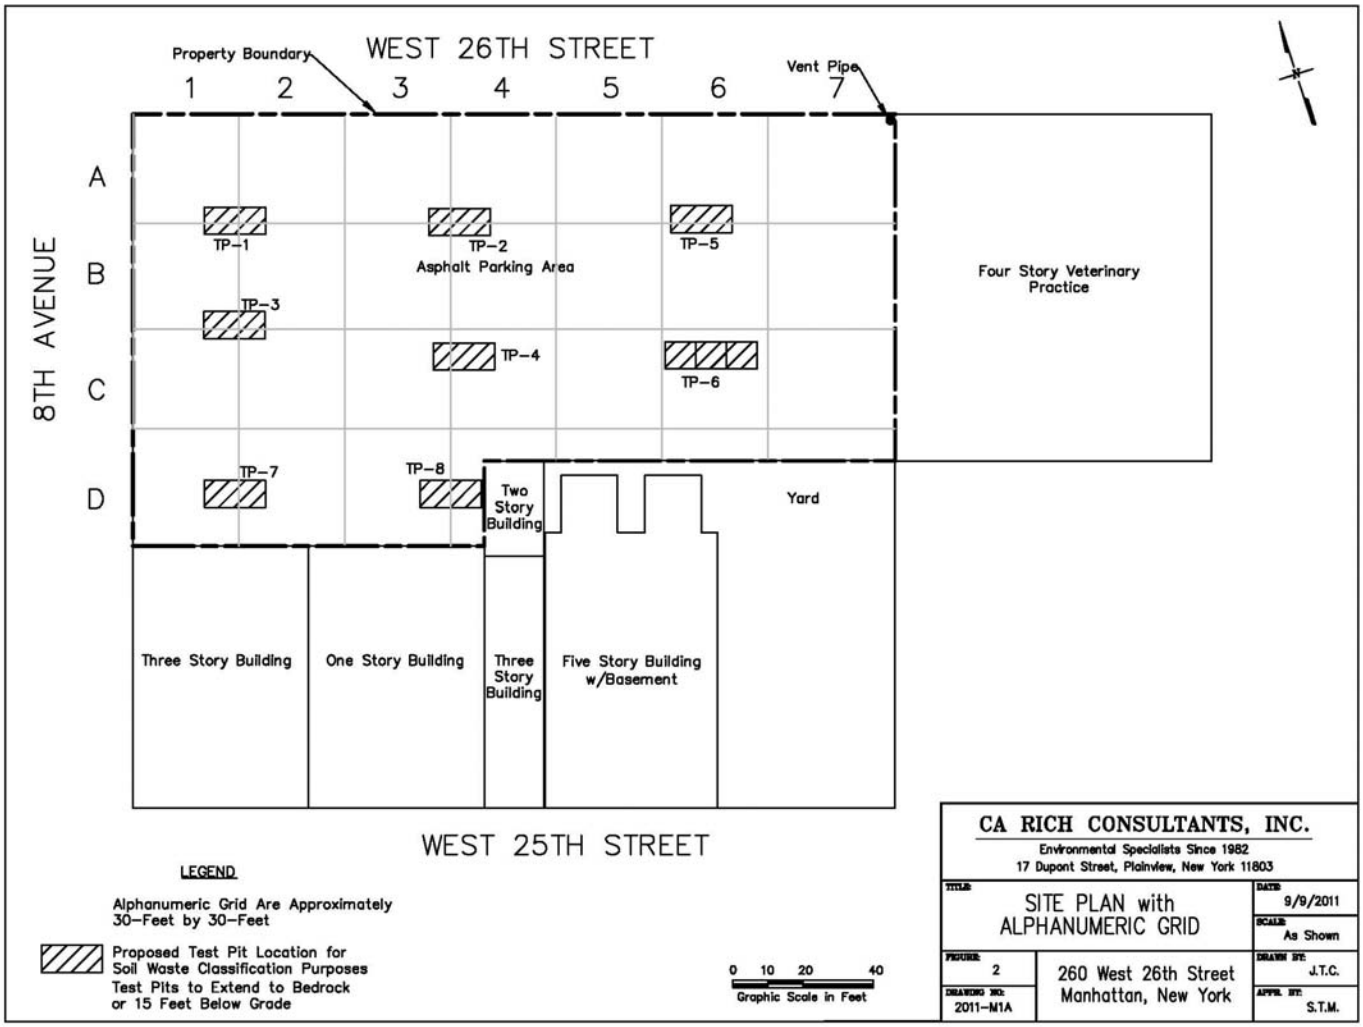

 File Name: _____

Photo Log

Photo 1 – Trucks were filled with Brick, concrete, and asphalt that was sorted from the soil. The solid material was transported to Bayshore for recycling. No soil was removed from the site.	
Photo 2 – Truck loads were covered and trucks undercarriage and wheels were thoroughly washed before they left the site.	
Photo 3 – Lagging began along the south property line.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	10-10-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Nine truckloads of TP-1 and TP-2 and six truckloads of TP-6 were transported to the Soil Safe Facility in Logan Township, NJ as non-hazardous waste.

Results were obtained from the samples of the north sidewall of TP-5 and the east sidewall of TP-7 that were submitted to the American Analytical Laboratory last Friday. Results confirmed that TCLP lead hazardous soil has been completely removed from TP-5 and TP-7. After confirmation, the open test pits were then covered with nearby soil.

Working In Grid #: A6, B6, C6, C7, D6, D7, D1, D2

Air Monitoring (Since Last Report):

Air Monitoring was conducted during today's excavation activities. No problems were encountered.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

HP Soldier Piles will begin to be installed along 8th Ave.

Soil will continued to be sorted and stockpiled and transported to the approved the approved. CA Rich will be on site during all excavation activities to oversee and ensure the Remedial Action Work Plan and CAMP Air Monitoring Plan is carried out according to OER specifications.

Example:

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
					15	375				
Totals (trucks, cu.yds.)	36	900	7	175	22	550				

Site Grid Map

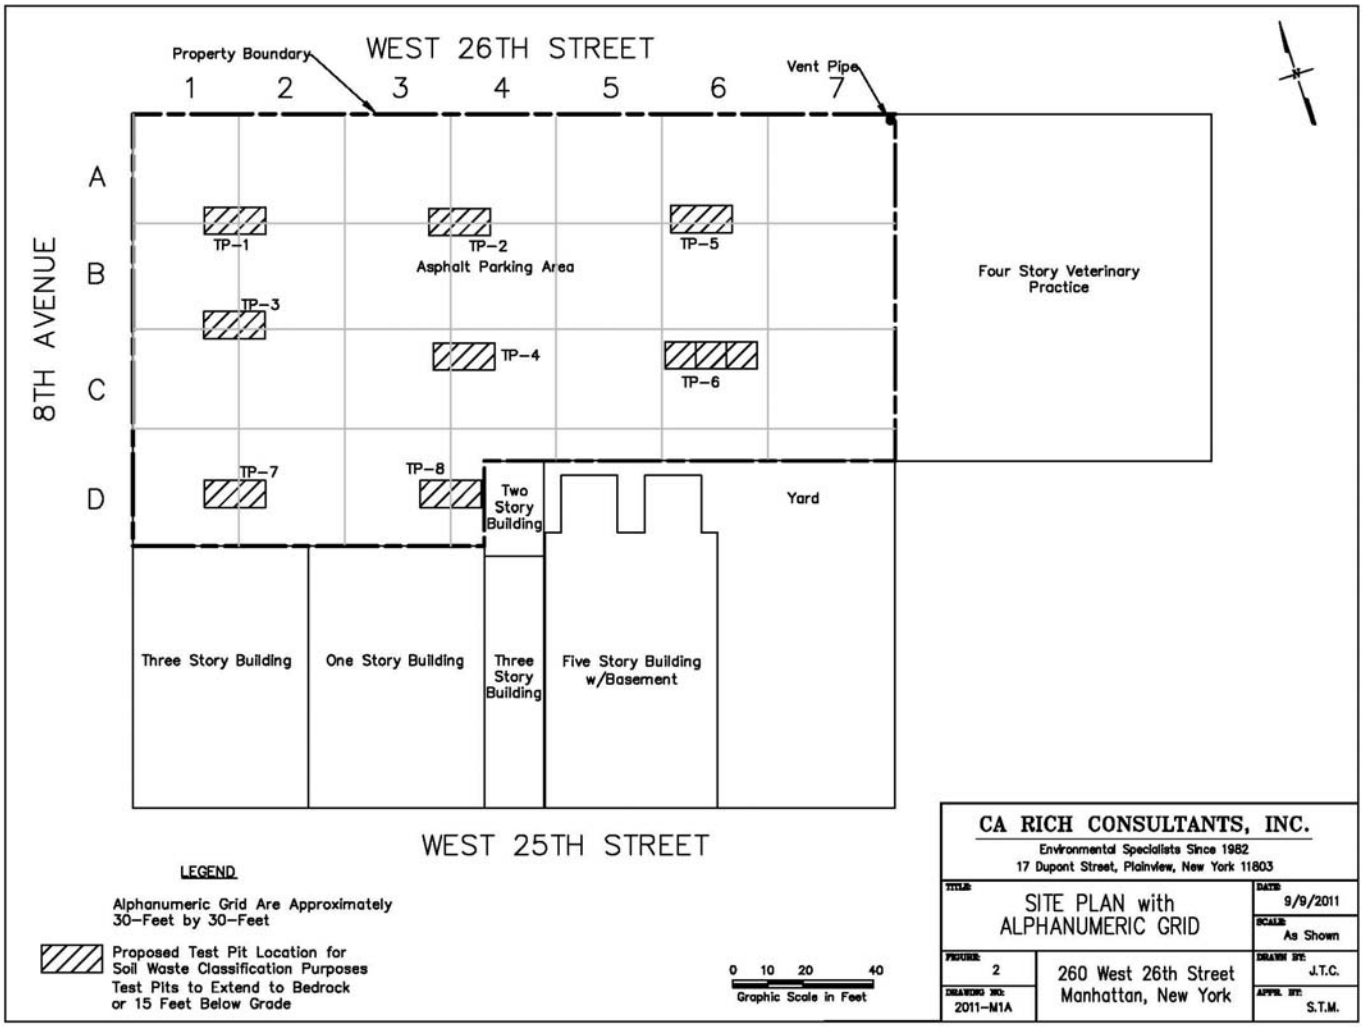

 File Name: _____

Photo Log

Photo 1 – Stockpile of TP-1 and TP-2 Soil that was transported to Soil Safe today.	
Photo 2 – Laborers constructing a gate for future use.	
Photo 3 – Excavating near TP-6. Soil is placed through the sorter to remove all brick, concrete, etc. and then stockpiled to be transported to Soil Safe.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70		70-85	X	>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	10-11-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Soil Solutions mobilized back on site to finish up the HP Soldier Piles along 8th Ave. They started the first pile at the corner of 26th Street and 8th Ave. Dinan and MTA were both on site to monitor the vibration of the subway tunnel.

(2) Truckloads of brick/concrete/stone etc. were transported to Bayshore Recycling. No soil was removed from the site.

A correction to yesterday's report:
Nine truckloads of TP-1 and TP-2 and **eight** truckloads of TP-6 were transported to the Soil Safe Facility in Logan Township, NJ as non-hazardous waste. (A total of 17 trucks yesterday)

The DOB was on site today responding to a neighbor's complaint due to proposed underpinning planning.

Working In Grid #: A1

Air Monitoring (Since Last Report):

No Air Monitoring was taken today. Air Monitoring is currently suspended until excavation activities resume. Once excavation activities resume the CAMP monitoring procedures will resume.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

HP Soldier Piles will begin to be installed along 8th Ave.

Soil will continued to be sorted and stockpiled and transported to the approved the approved. CA Rich will be on site during all excavation activities to oversee and ensure the Remedial Action Work Plan and CAMP Air Monitoring Plan is carried out according to OER specifications.

 File Name: _____

Example:

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
	2	50								
Totals (trucks, cu.yds.)	38	950	7	175	**39***	**975***				

(*Soil Safe Updated w/ 2 trucks that were forgotten yesterday)

Site Grid Map

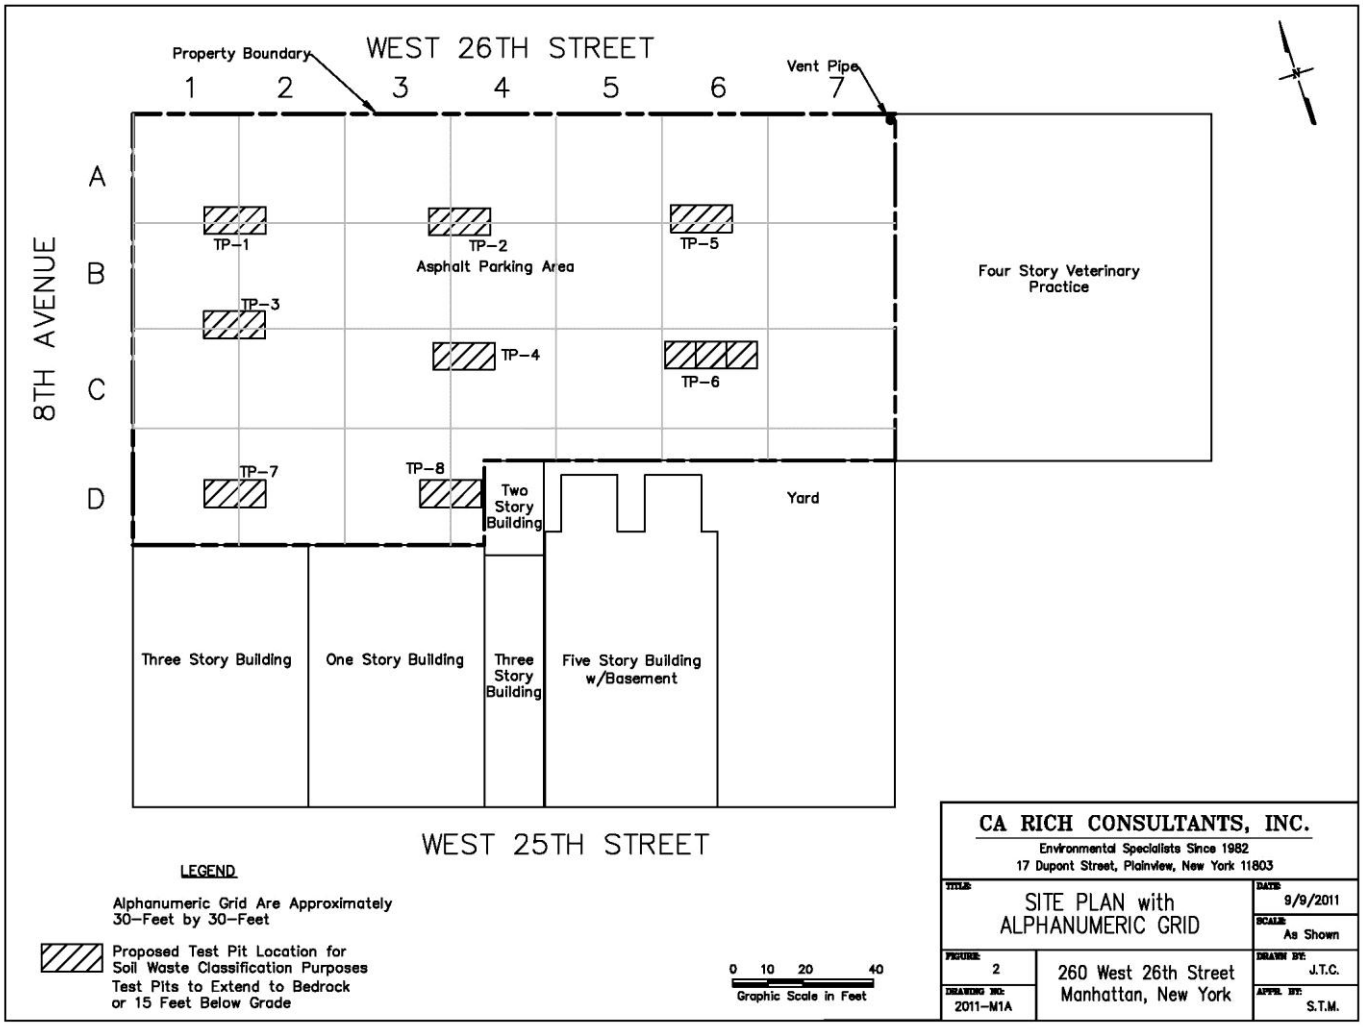

 File Name: _____

Photo Log

Photo 1 – Staking out location where HP Soldier Piles are to be installed along 8th Ave.	
Photo 2 – Machine Drilling 1st pile along 8th Ave.	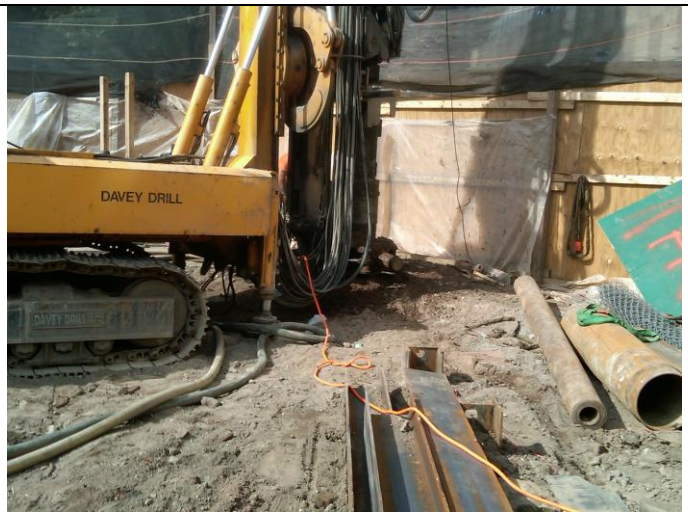
Photo 3 – HP Soldier Piles were delivered to site today. Piles were originally too short and had to be extended to 30'-0" long to be installed along 8th Ave.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain		Overcast	X	Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	10-12-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Soil Solutions completed (2) piles along 8th Ave. Dinan and MTA were both on site to monitor the vibration of the subway tunnel.

Soil around the areas of TP-4 and TP-6 was screened and stockpiled and is waiting disposal. All Brick and stone that was sorted from the soil was transported to Bayshore Recycling.

Disposal Approval to Bellmawr Waterfront Redevelopment was received and will be forwarded to OER.

Working In Grid #: A1, C4, C5, C6, C7, D4, D5, D6, D7

Air Monitoring (Since Last Report):

Air Monitoring was taken today. No problems were encountered.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

HP Soldier Piles will continue to be installed along 8th Ave.

Example:

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
	12	300								
Totals (trucks, cu.yds.)	40	1000	7	175	39	975				

Site Grid Map

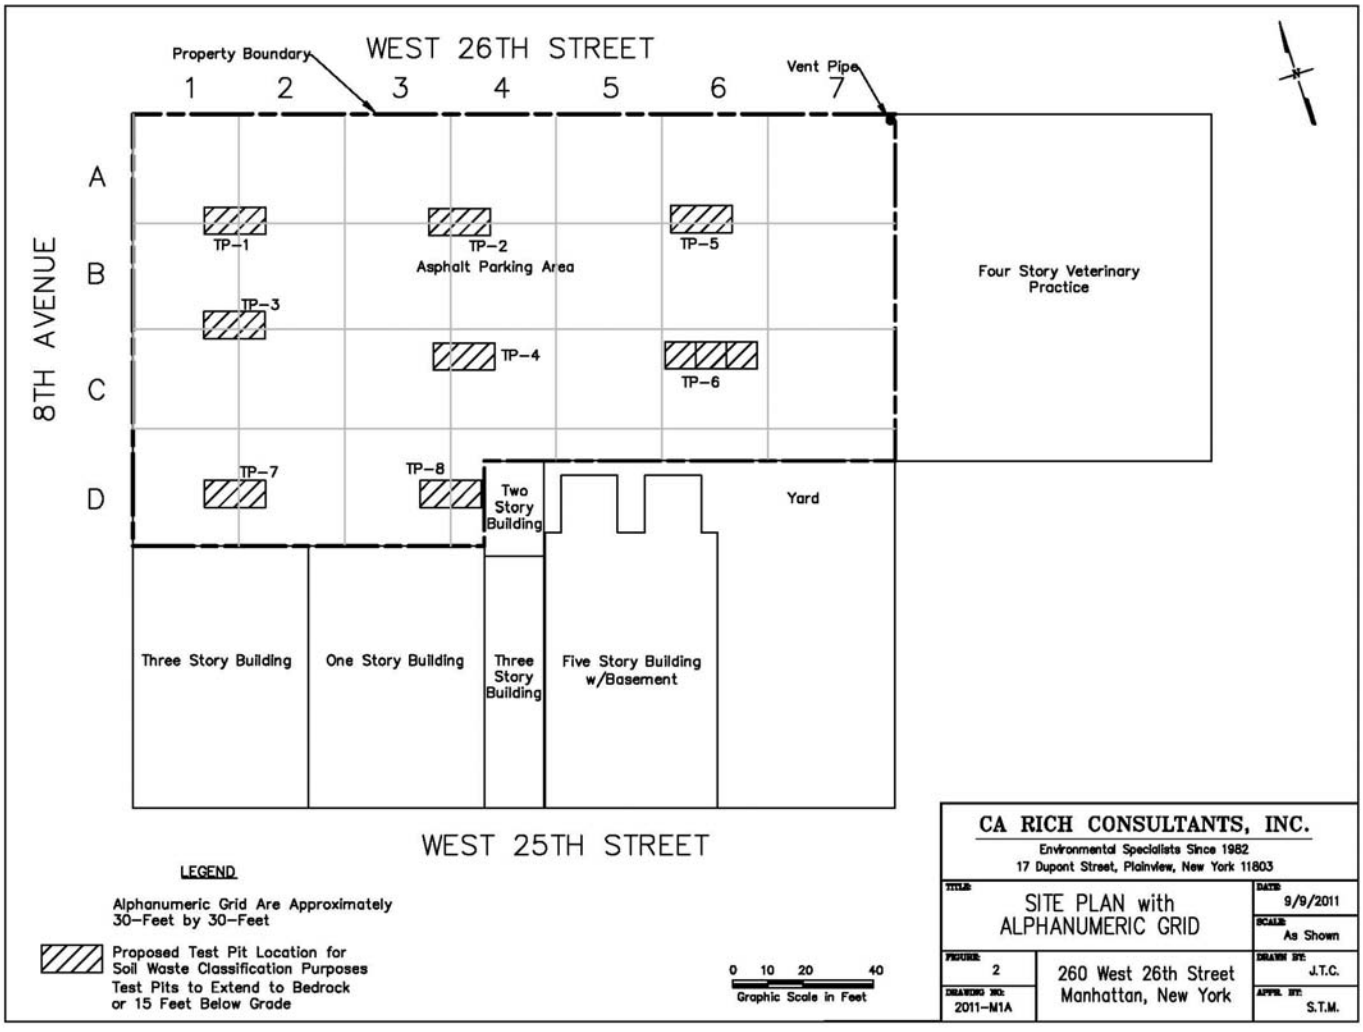

 File Name: _____

Photo Log

Photo 1 – HP Soldier Pile #4 installed along 8th Ave. Workers working on completing HP Soldier Pile #1 in the background.	
Photo 2 – More Gravel was delivered today to make a second truck washing station. All trucks were thoroughly washed and inspected before leaving the site.	
Photo 3 – HP Soldier Pile #1 installed along 8th Ave.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain	X	Overcast		Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	10-13-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Soil Solutions completed 4 piles for a total of 6 piles installed along 8th Ave. Dinan and MTA were both on site to monitor the vibration of the subway tunnel.

Working In Grid #: B1, C1

Air Monitoring (Since Last Report):

No excavation was done today, therefore no air monitoring took place. Air monitoring will resume when excavation activities resume next week.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

HP Soldier Piles will continue to be installed along 8th Ave.

Example:

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
Totals (trucks, cu.yds.)	52	1300	7	175	39	975				

Site Grid Map

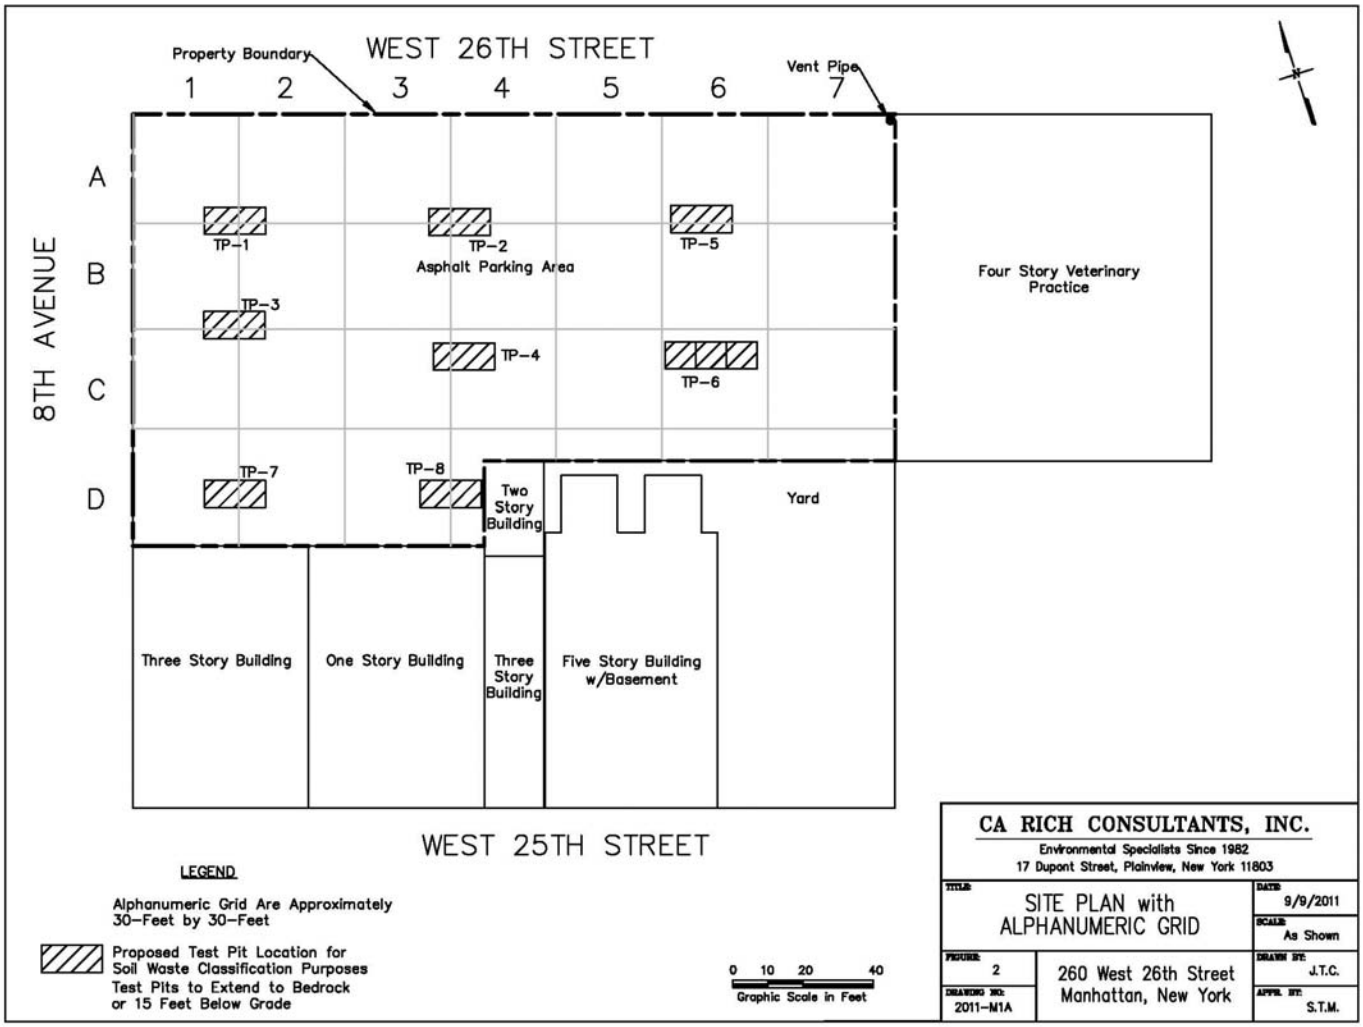

 File Name: _____

Photo Log

Photo 1 – HP Soldier Piles #1,2,3, and 4 installed along 8th Ave.	
Photo 2 – Machine Drilling Pile #6 along 8th Ave.	
Photo 3 – HP Soldier Piles #3,4,5, and 6 installed along 8th Ave. Workers mobilizing equipment in background to set up to Drill Pile #7 tomorrow.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain	X	Overcast		Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	10-14-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Soil Solutions completed 3 piles for a total of 9 piles installed along 8th Ave. Dinan and MTA were both on site to monitor the vibration of the subway tunnel.

Working In Grid #: C1

Air Monitoring (Since Last Report):

No excavation was done today, therefore no air monitoring took place. Air monitoring will resume when excavation activities resume next week.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

HP Soldier Piles will continue to be installed along 8th Ave.

Example:

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
Totals (trucks, cu.yds.)	52	1300	7	175	39	975				

Site Grid Map

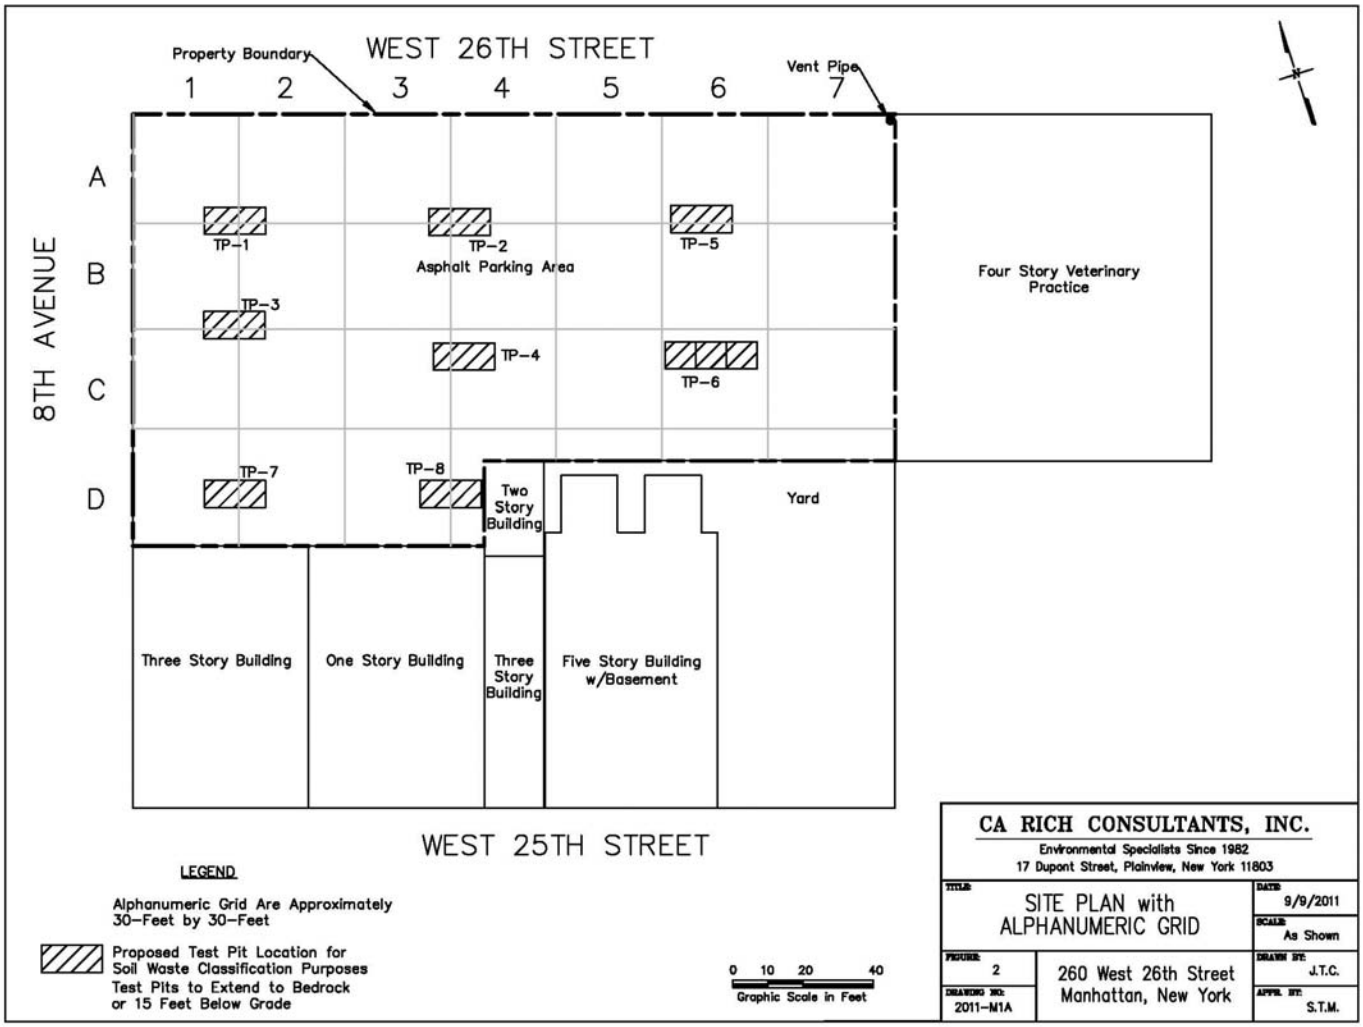

 File Name: _____

Photo Log

Photo 1 – HP Soldier Piles 6,7, and 8 installed along 8th Ave.	
Photo 2 – Machine Drilling HP Soldier Pile #8 along 8th Ave.	
Photo 3 – Machine Drilling HP Soldier Pile #9 along 8th Ave.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	10-17-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Soil Solutions completed 4 piles for a total of 13 piles installed along 8th Ave. Dinan and MTA were both on site to monitor the vibration of the subway tunnel.

Stockpiles on site remain covered and are inspected daily. No problems have been encountered.

Working In Grid #: C1, D1

Air Monitoring (Since Last Report):

No excavation was done today, therefore no air monitoring took place. Air monitoring will resume when excavation activities resume next week.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

HP Soldier Piles will be complete by the end of this week. Excavation of soil to resume by the end of this week and continue all next week. Soil to be transported to the approved facilities.

Example:

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
Totals (trucks, cu.yds.)	52	1300	7	175	39	975				

Site Grid Map

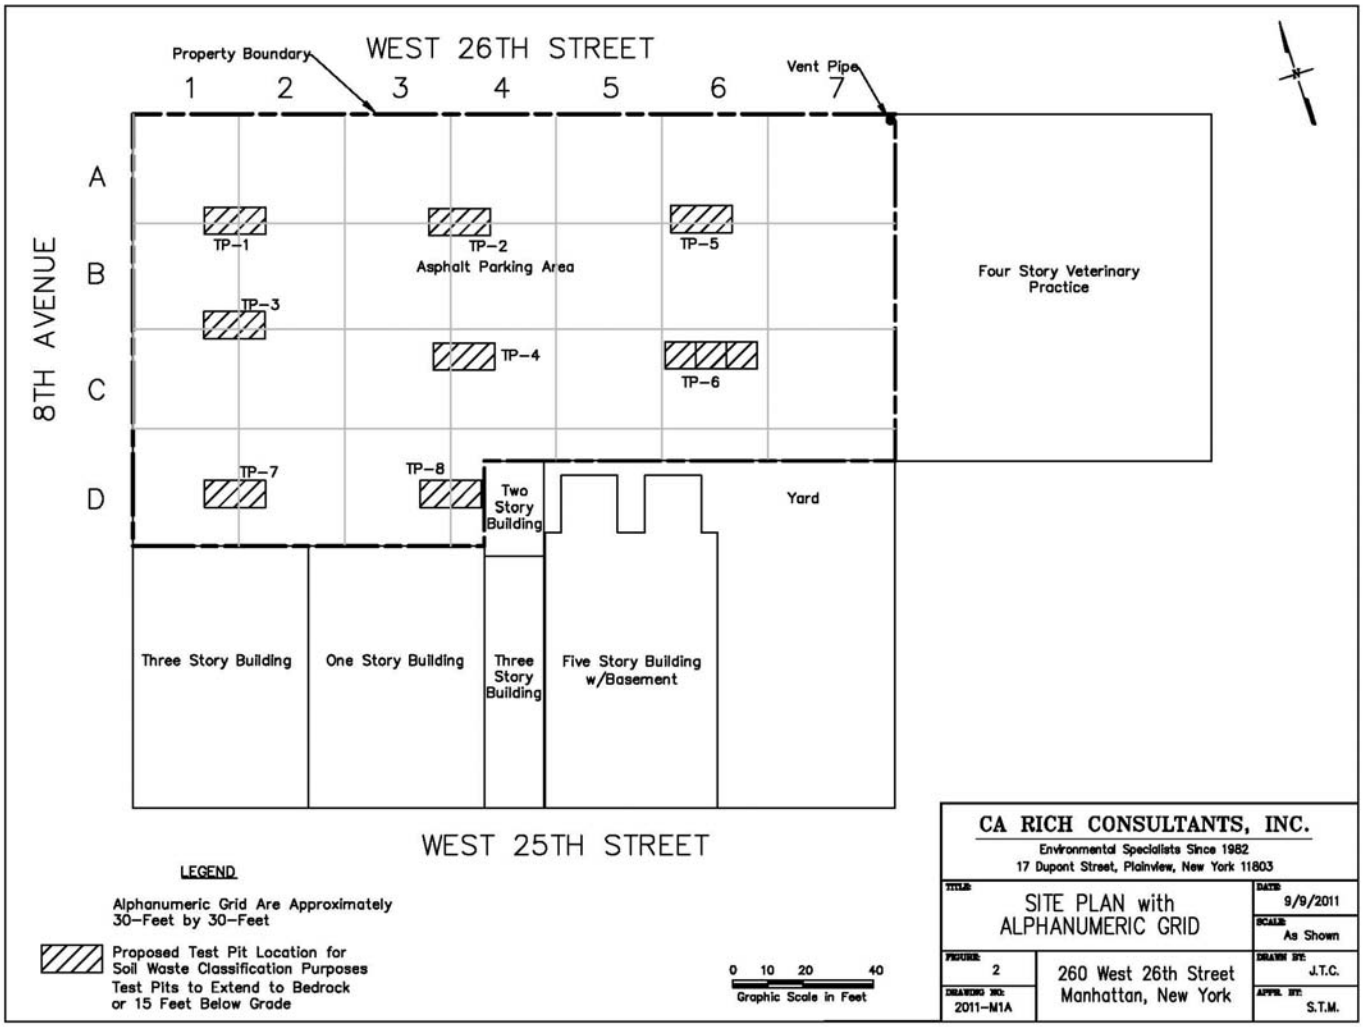

 File Name: _____

Photo Log

Photo 1 – Machine setting up to drill Pile in southwest corner of site.	
Photo 2 – Soil stockpiles on site remain covered and are inspected daily. Soil to be transported to the approved facility by the end of the week.	
Photo 3 – Machine Drilling HP Soldier Pile #15 along 8th Ave.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	10-18-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Soil Solutions completed 3 piles for a total of 16 piles installed along 8th Ave. As a result, all HP Soldier Piles on site are complete. Dinan and MTA were both on site to monitor the vibration of the subway tunnel.

Stockpiles on site remain covered and are inspected daily. No problems have been encountered.

OER on site today to video tape an example of a Brownfield Cleanup site.

Working In Grid #: C1, D1

Air Monitoring (Since Last Report):

No excavation was done today, therefore no air monitoring took place. Air monitoring will resume when excavation activities resume next week.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

HP Soldier Piles are complete. Excavation of soil to resume tomorrow and continue all next week. Soil to be transported to the approved facilities.

 File Name: _____

Example:

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Liquid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
Totals (trucks, cu.yds.)	52	1300	7	175	39	975				

Site Grid Map

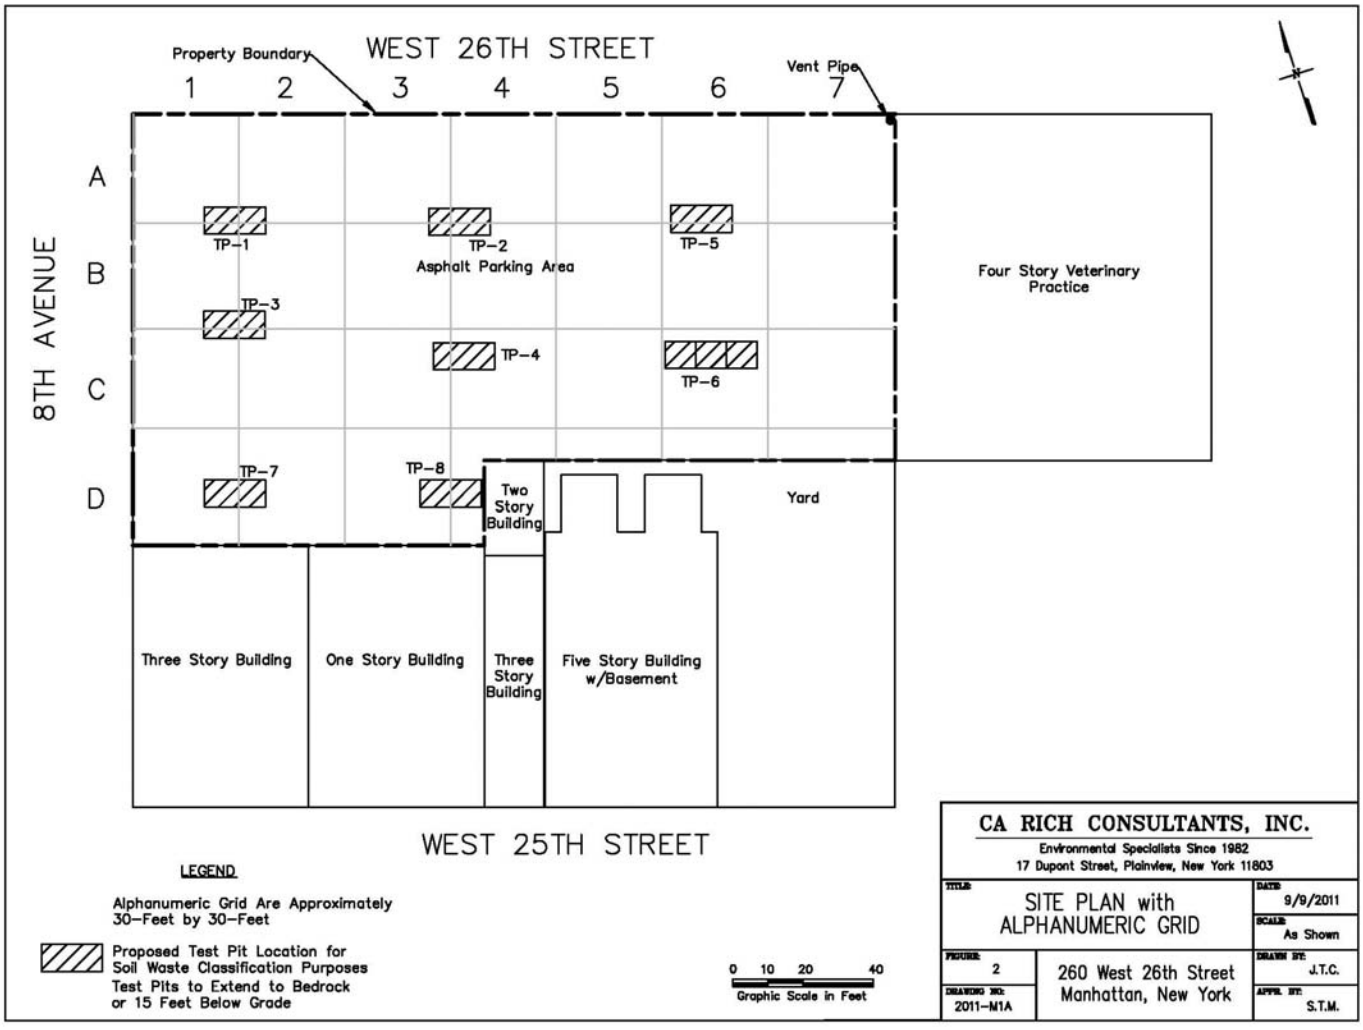

 File Name: _____

Photo Log

Photo 1 – Machine drilling final HP Soldier Pile along 8th Ave.	
Photo 2 – Picture of all HP Soldier Piles along 8th Ave. As of today, all piles have been completed on site.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Steve Malinowski of CA RICH

WEATHER	Snow		Rain	X	Overcast		Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50		50-70	x	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	10-19-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Twenty five loads of brick were transported off-site to the Bay Shore Recycling facility. Ten loads of soil was transported to the Bellmarw Waterfront Redevelopment Site as non-hazardous waste.

Working In Grids #: C5 and C6

Air Monitoring (Since Last Report):

Air Monitoring was no conducted today's loading activities because of heavy rain throughout the day. Air monitoring will resume once the rain ends. No problems were encountered.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

Tomorrow we plan to excavate material for disposal at the Soil Safe Facility in Logan, NJ. The soldier pile installation is complete. The construction team will begin installing lagging and the perimeter as the excavation proceeds.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds. *Or* Gallons
	25	625					10	Appr. 250		
Totals (trucks, cu.yds.)	77	1,925	7	175	39	Appr. 175				

Site Grid Map

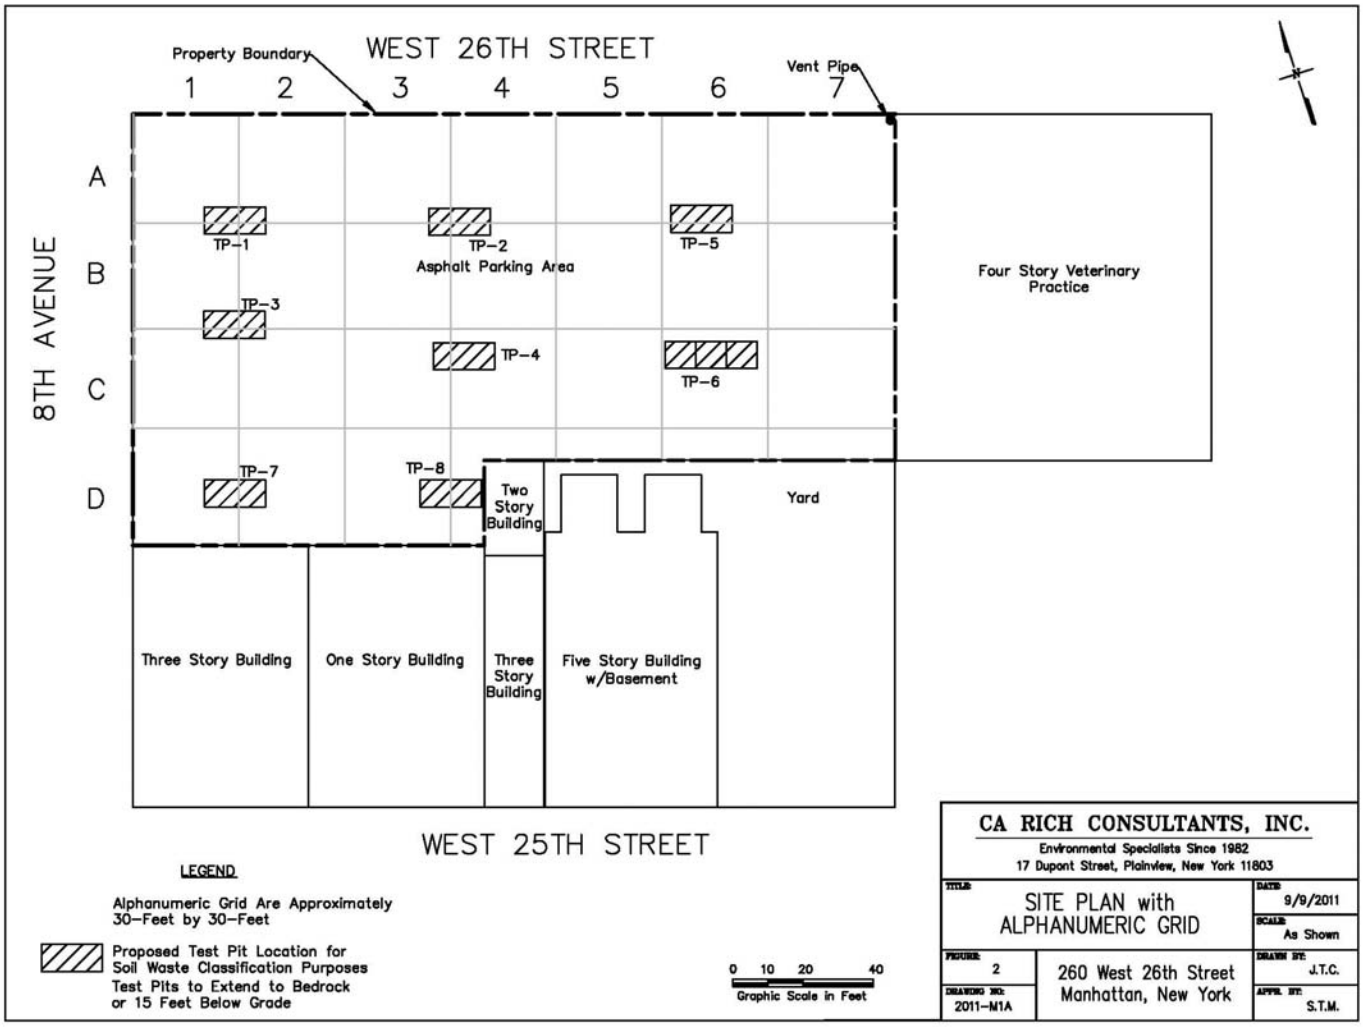

 File Name: _____

Photo Log

Photo 1 – Soil Stockpile for Bellmarw after 1st round of trucks	
Photo 2 – Loading of soil for disposal at Bellmarw	
Photo 3 – Rinsing mud from truck tires before leaving job-site	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Steve Malinowski of CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy	x	Bright Sun	
TEMP.	TO 32		32-50		50-70	x	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	10-20-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Two loads of brick were transported off-site to the Bay Shore Recycling facility. Twenty-three truckloads of soil wee excavated from grids A1, B1, and A2 to the Soil Safe Facility in Logan, New Jersey as non-hazardous waste.

Working In Grids #: A1, B1, and A2

Air Monitoring (Since Last Report):

Air Monitoring was during today's work activities. No problems were encountered.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

Tomorrow we plan to continue excavation activities with disposal to the Soil Safe Facility in Logan, NJ. The construction team will also be installing lagging as needed along the perimeter as the excavation proceeds.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds. *Or* Gallons
	2	50			23	Appr. 575				
Totals (trucks, cu.yds.)	102	2,550	7	175	39	Appr. 175	10	Appr. 250		

Site Grid Map

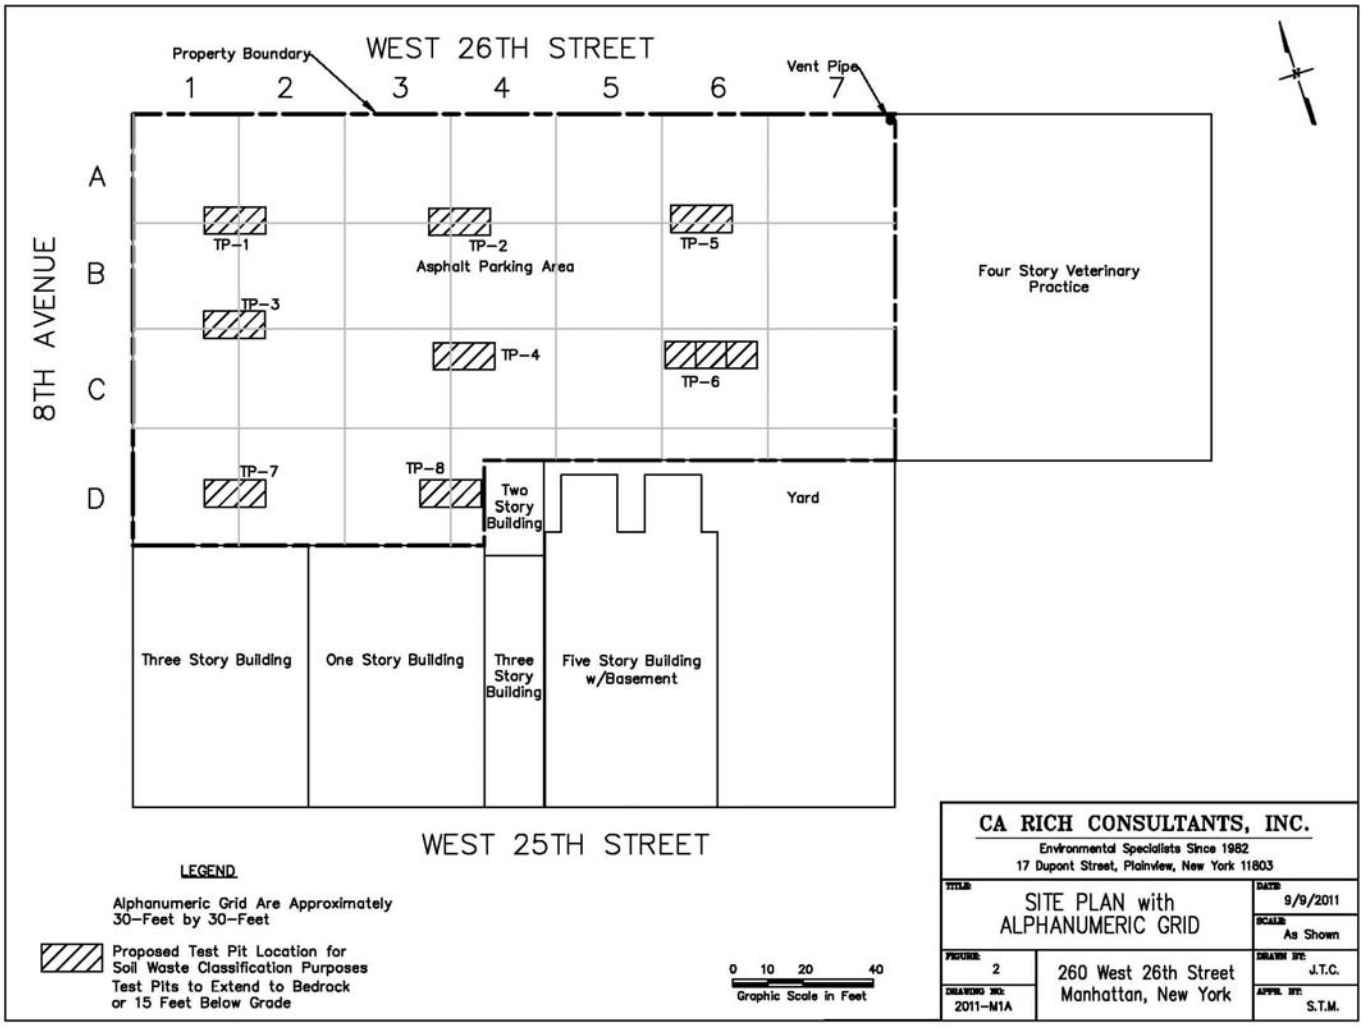

 File Name: _____

Photo Log

Photo 1 – Looking west across excavation area towards 8th Avenue	
Photo 2 – Placing additional gravel near truck entrance/exist for truck washing pad	
Photo 3 – Looking east across excavation area	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Steve Malinowski of CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy	x	Bright Sun	
TEMP.	TO 32		32-50		50-70	x	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	10-21-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):
Thirty-three truckloads of soil were excavated from grids A1 through 5, B1, and D-4 and D-5 for disposal at the Soil Safe Facility in Logan, New Jersey as non-hazardous waste.

A soil sample was collected from approximately 2-feet below the land surface in the area of the hydraulic oil stain on the former asphalt surface. CA RICH will discuss analysis of the sample with OER and NYSDEC prior to submittal for chemical analysis.

Working In Grids #: A1 through 5, B1, D2 through D-5

Air Monitoring (Since Last Report):

Air Monitoring was performed during today's work activities. No problems were encountered.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

Next week we plan to continue excavation with the disposal of soil at both the Soil Safe Facility in Logan, NJ and the Bellmarw Waterfront Redevelopment Site. The construction team will also be installing lagging as needed along the perimeter as the excavation proceeds.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds. *Or* Gallons
					33	Appr. 825				
Totals (trucks, cu.yds.)	104	2,600	7	175	62	Appr. 750	10	Appr. 250		

Site Grid Map

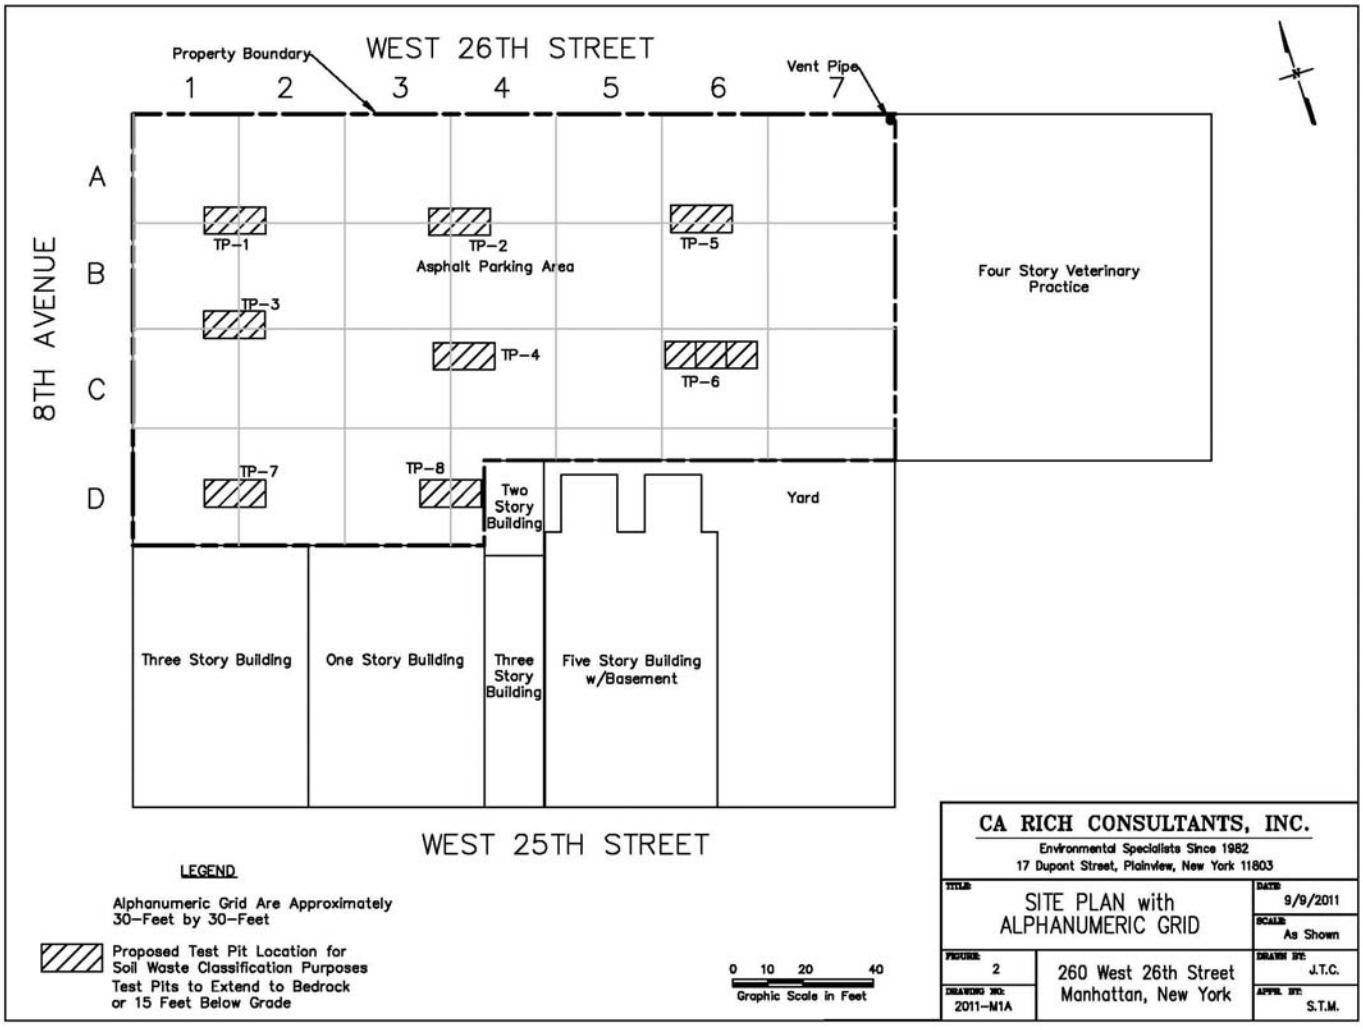

 File Name: _____

Photo Log

Photo 1 – Trucks being loaded with material for disposal at Soil Safe in Logan, NJ	
Photo 2 – Screening brick and concrete from soil in grids D-2, D-3 and D-4. Screened soil to be transported on Monday to the Bellmarw Waterfront Redevelopment Site	
Photo 3 – Dust monitoring along Site perimeter	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	10-22-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Seven truckloads of brick and concrete were transported to Bayshore Recycling. No soil was removed from the site.

Installation of lagging continued on site along 26th Street.

Working In Grid #: C1, D1

Air Monitoring (Since Last Report):

Air Monitoring was performed during today's work activities. No problems were encountered.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

Next week we plan to continue excavation with the disposal of soil at both the Soil Safe Facility in Logan, NJ and the Bellmarw Waterfront Redevelopment Site. The construction team will also be installing lagging as needed along the perimeter as the excavation proceeds.

Example:

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
	7									
Totals (trucks, cu.yds.)	84	2100	5	125	80	2000	10	250		

Site Grid Map

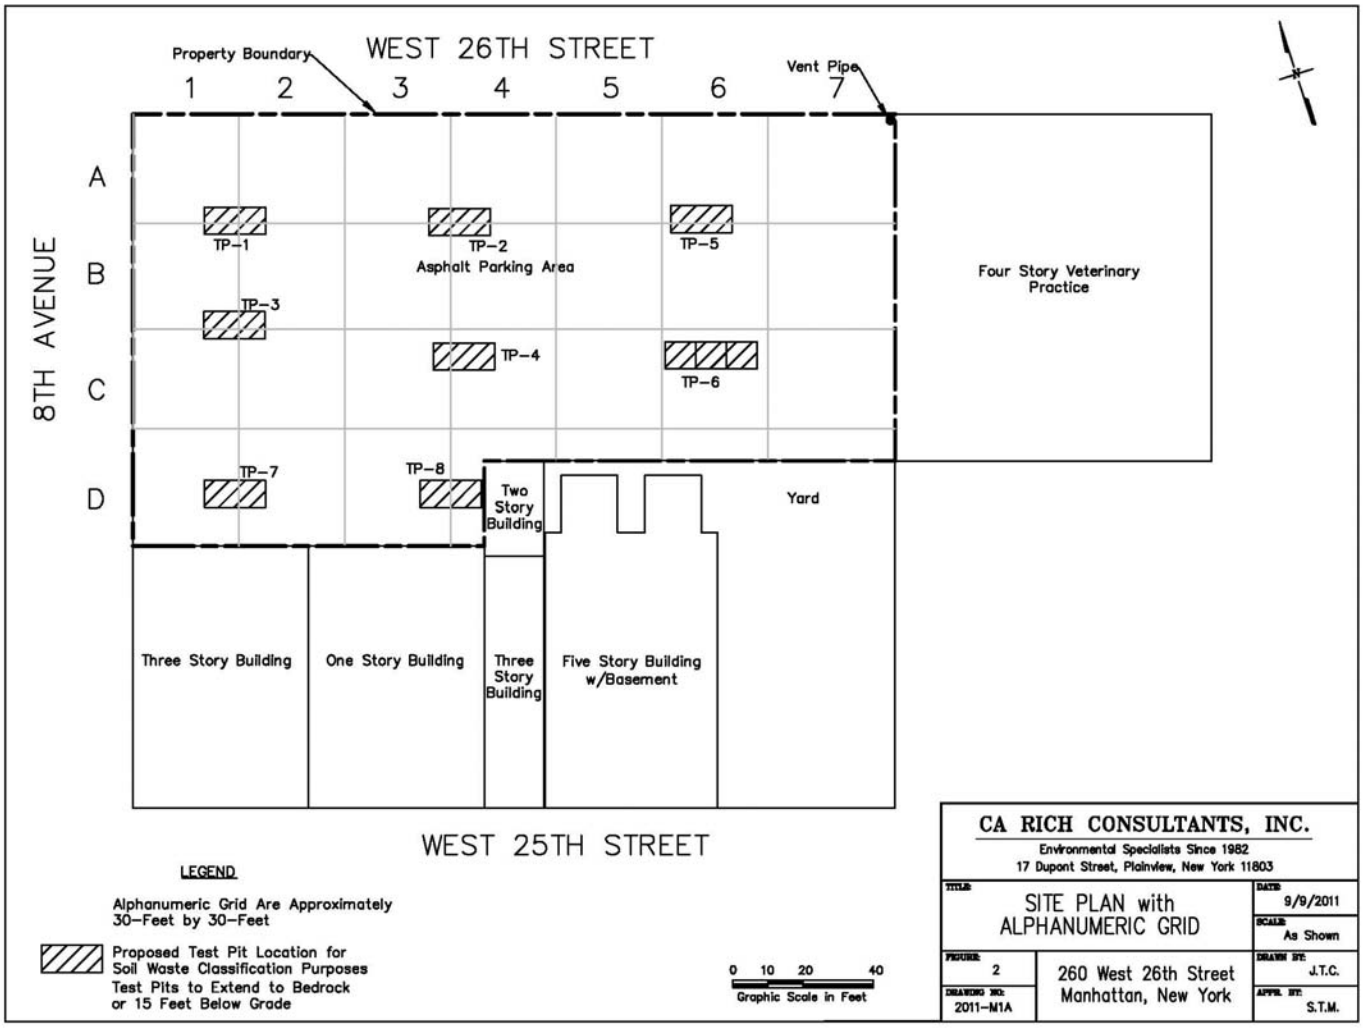

 File Name: _____

Photo Log

Photo 1 – Lagging beginning to be installed on site. Barricades were installed as a safety measure.	
Photo 2 – Picture of men installing lagging along 26th street	
Photo 3 -- All lagging installed along 26th at the end of the day.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Steve Malinowski of CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy	x	Bright Sun	
TEMP.	TO 32		32-50		50-70	x	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	10-24-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Eight truckloads of soil were transported to the Bellarw Waterfront Redevelopment Site in New Jersey as non-hazardous waste. Thirty-two truckloads of soil were excavated for disposal at the Soil Safe Facility in Logan, New Jersey as non-hazardous waste.

Working In Grids #: B1, B2, B3, C1, D2, D3 and D4

Air Monitoring (Since Last Report):

Air Monitoring was performed during today's work activities. No problems were encountered.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

This week we plan to continue excavation with the disposal of soil at both the Soil Safe Facility in Logan, NJ and the Bellmarw Waterfront Redevelopment Site. The construction team will also be installing lagging as needed along the perimeter as the excavation proceeds.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds. *Or* Gallons
					32	Appr. 800	8	Appr. 200		
Totals (trucks, cu.yds.)	111	2,775	7	175	95	Appr. 1,575	10	Appr. 250		

Site Grid Map

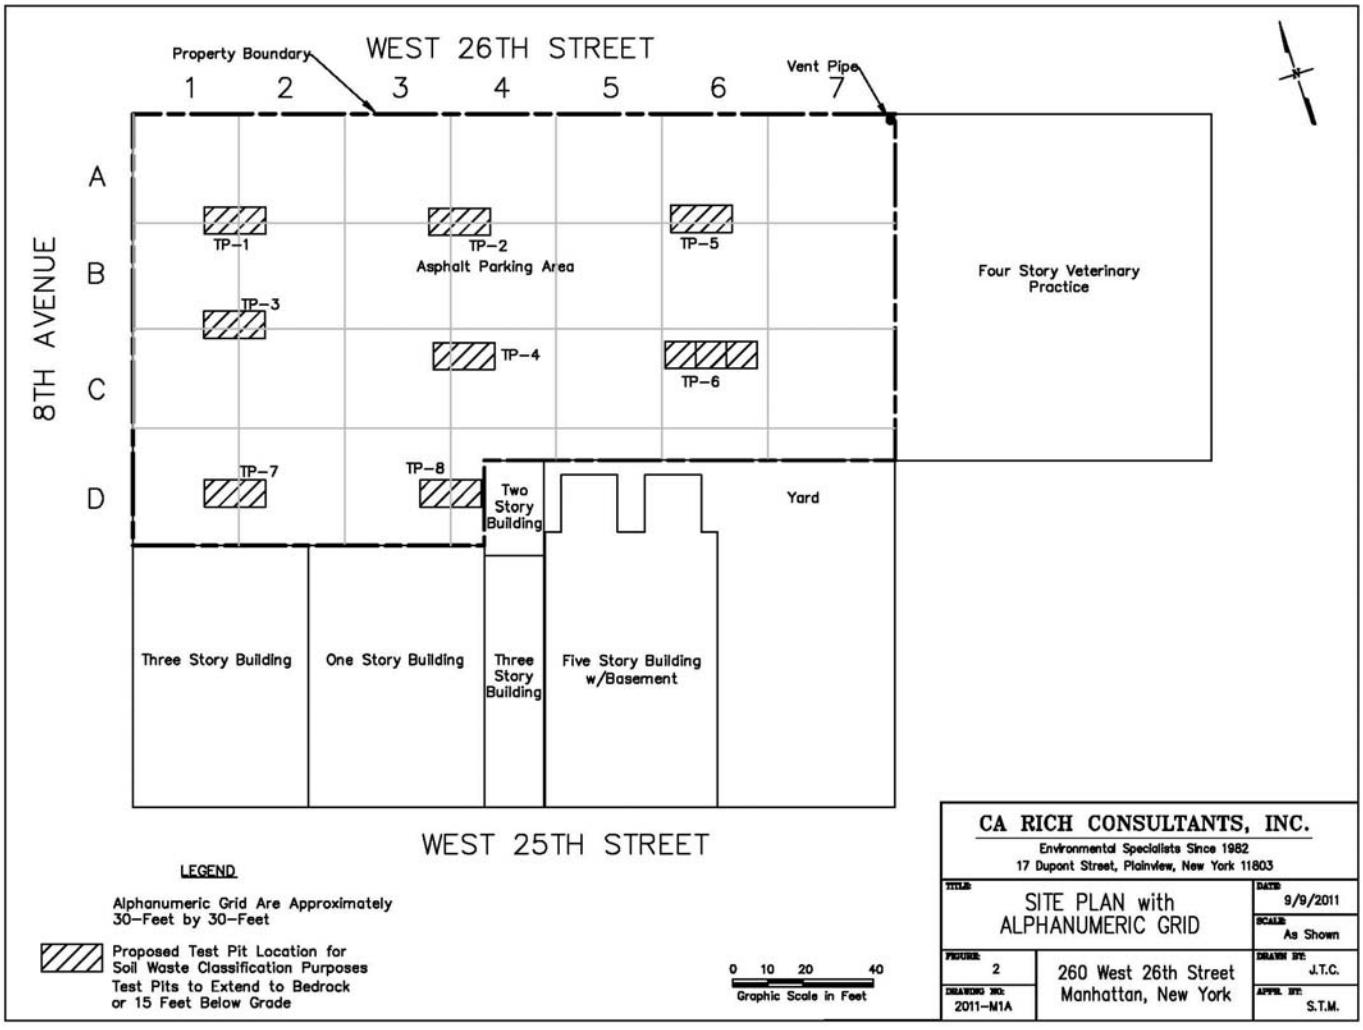

 File Name: _____

Photo Log

Photo 1 – Truck being loaded with material for disposal at Soil Safe in Logan, NJ	
Photo 2 – Looking west across site excavation at excavator directly loading soil into truck for disposal at Soil Safe in Logan, NJ	
Photo 3 – Soil excavation in the area of former test pit TP-3.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Steve Malinowski of CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70	x	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	10-25-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Thirty-five truckloads of soil were excavated for from grids A1,B1, B4, B5 and transported to the Soil Safe Facility in Logan, New Jersey for disposal as non-hazardous waste.

Working In Grids #: A1, B1, B4, and B5

Air Monitoring (Since Last Report):

Air Monitoring was performed during today's work activities. No problems were encountered.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

Tomorrow we plan to continue excavation with the disposal of soil at the Soil Safe Facility in Logan, NJ. The construction team will continue to install lagging as needed along the perimeter as the excavation proceeds.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds. *Or* Gallons
					35	Appr. 875				
Totals (trucks, cu.yds.)	84	2,100	5	Appr 125	112	Appr. 2,800	18	Appr. 450		

Site Grid Map

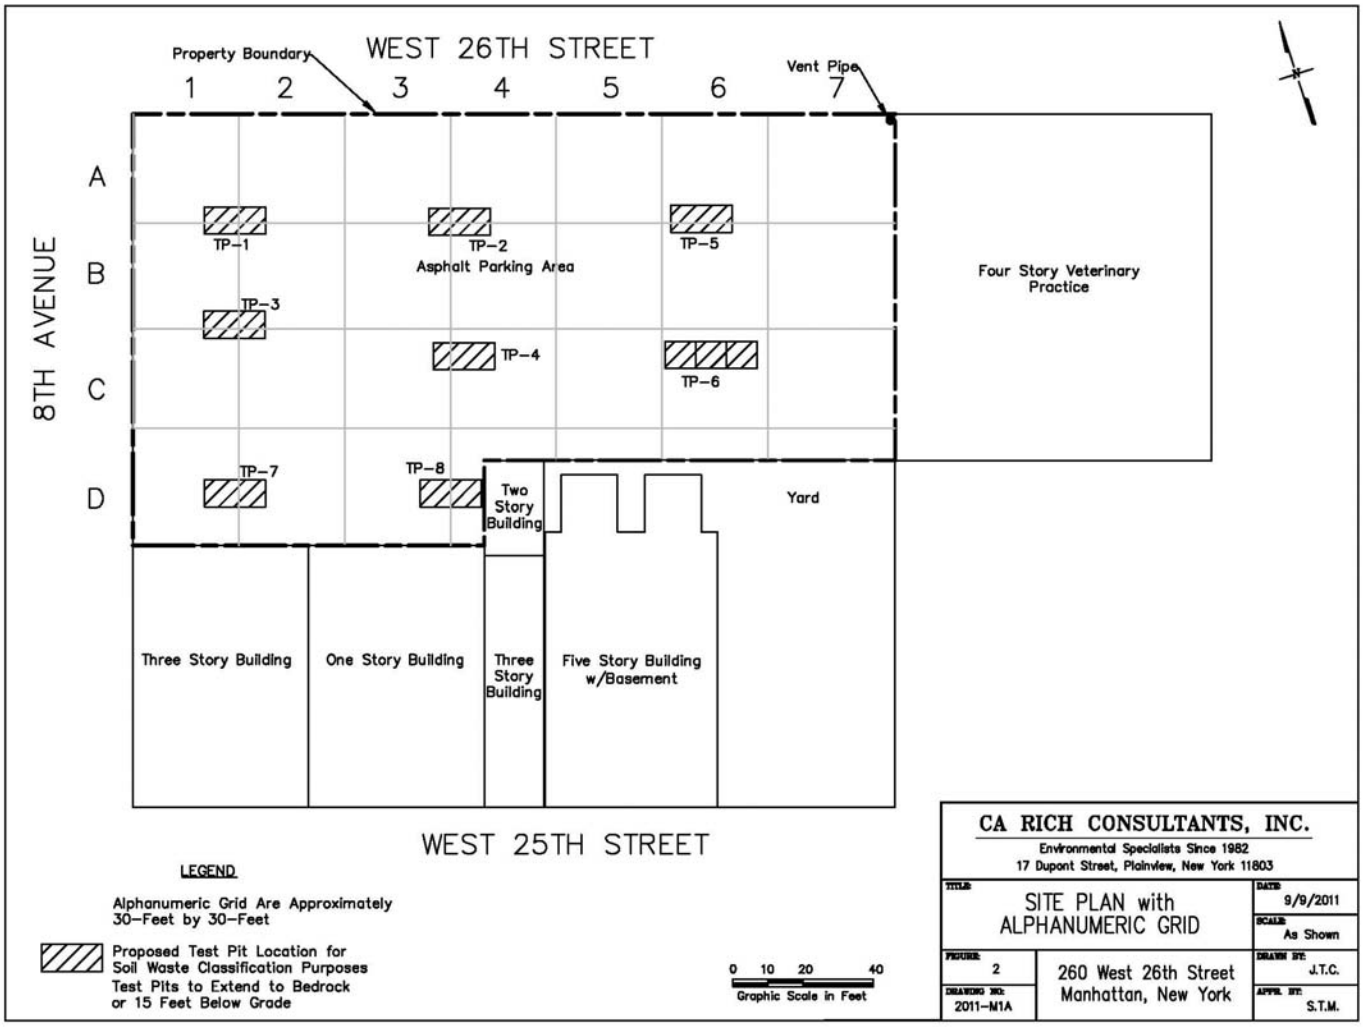

 File Name: _____

Photo Log

Photo 1 – Truck being loaded with material for disposal at Soil Safe in Logan, NJ	
Photo 2 – Excavation of soil from northwest corner of Site.	
Photo 3 – Soil excavation in the area of former test pits TP-1 and TP-3.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Steve Malinowski of CA RICH

WEATHER	Snow		Rain		Overcast	x	Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50		50-70	x	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	10-26-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Fourteen truckloads of soil were excavated for from grids A6,A7, B6 and B7 and transported to the Soil Safe Facility in Logan, New Jersey for disposal as non-hazardous waste.

Working In Grids #: A6,A7, B6 and B7

Air Monitoring (Since Last Report):

Air Monitoring was performed during today's work activities. No problems were encountered.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

Tomorrow we plan to continue excavation. The construction team will screen out bricks and concrete to prepare soil for delivery to Bellmarw. The construction team will continue to install lagging as needed along the perimeter as the excavation proceeds.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds. *Or* Gallons
					14	Appr. 350				
Totals (trucks, cu.yds.)	84	2,100	5	Appr 125	147	Appr. 3,675	18	Appr. 450		

Site Grid Map

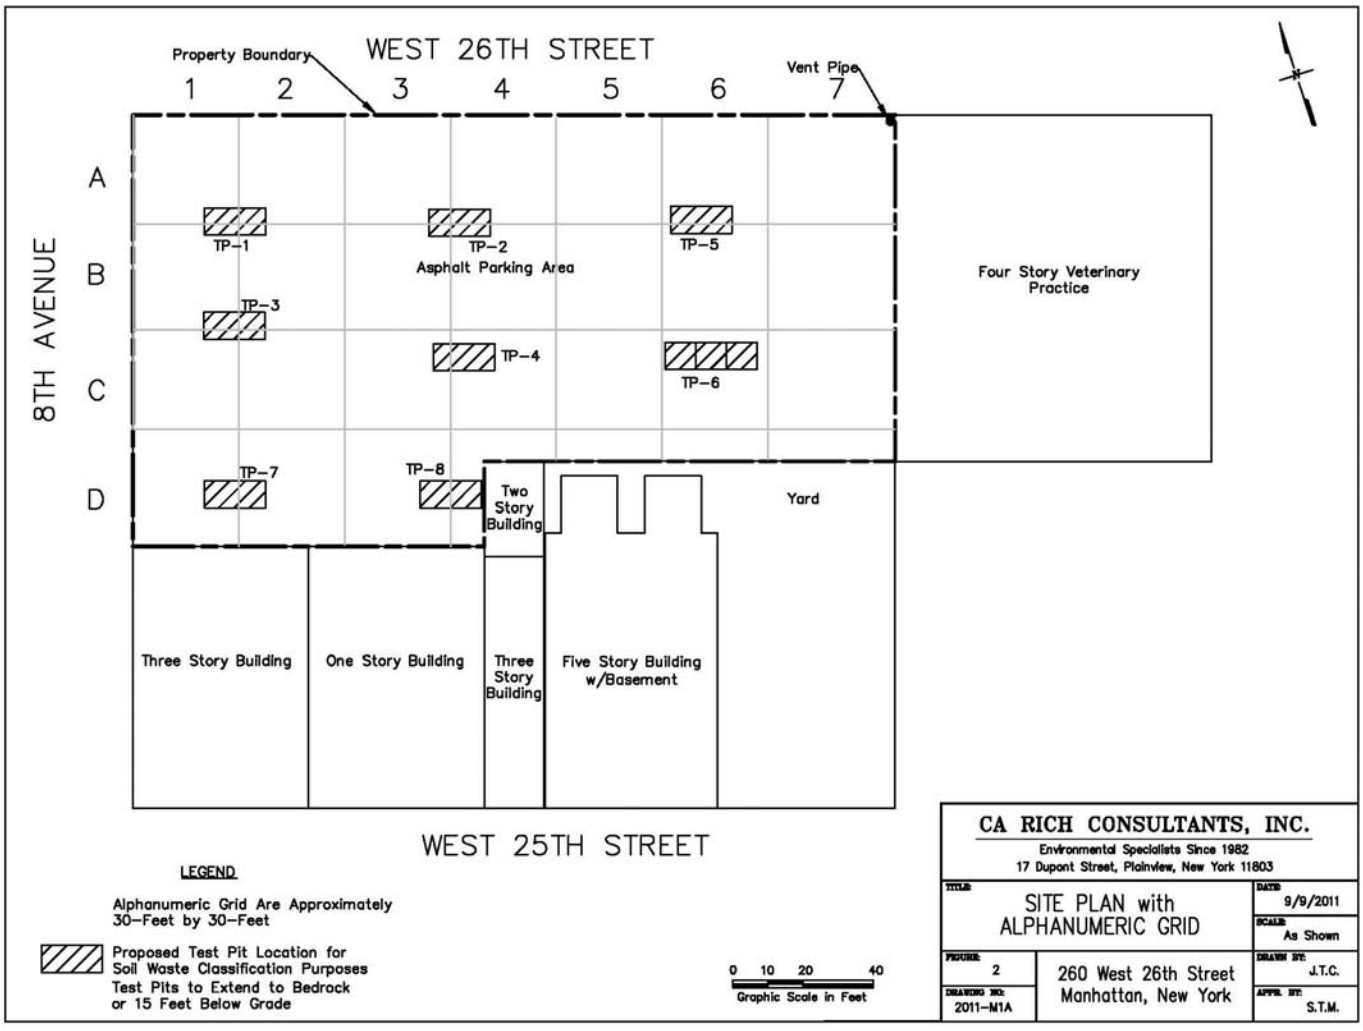

 File Name: _____

Photo Log

Photo 1 – Truck being loaded with material for grids A-6 and A-7 for disposal at Soil Safe in Logan, NJ	
Photo 2 – Truck being loaded with material for grid B-7 for disposal at Soil Safe in Logan, NJ	
Photo 3 – Soil excavation in grids A-7 and B-7.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain	X	Overcast		Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	10-27-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Test Pits were dug for the engineer to design the underpinning along the neighboring buildings. Parging was installed along the neighboring buildings to protect the existing brick.

Working In Grid #: A7, B7, C7, D7, D2, D3, D4

Air Monitoring (Since Last Report):

Air Monitoring was not performed today due to rain all day long.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

Next week we plan to continue excavation with the disposal of soil at both the Soil Safe Facility in Logan, NJ and the Bellmarw Waterfront Redevelopment Site. The construction team will also be installing lagging as needed along the perimeter as the excavation proceeds.

Example:

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
Totals (trucks, cu.yds.)	84	2100	5	125	161	4025	18	450		

Site Grid Map

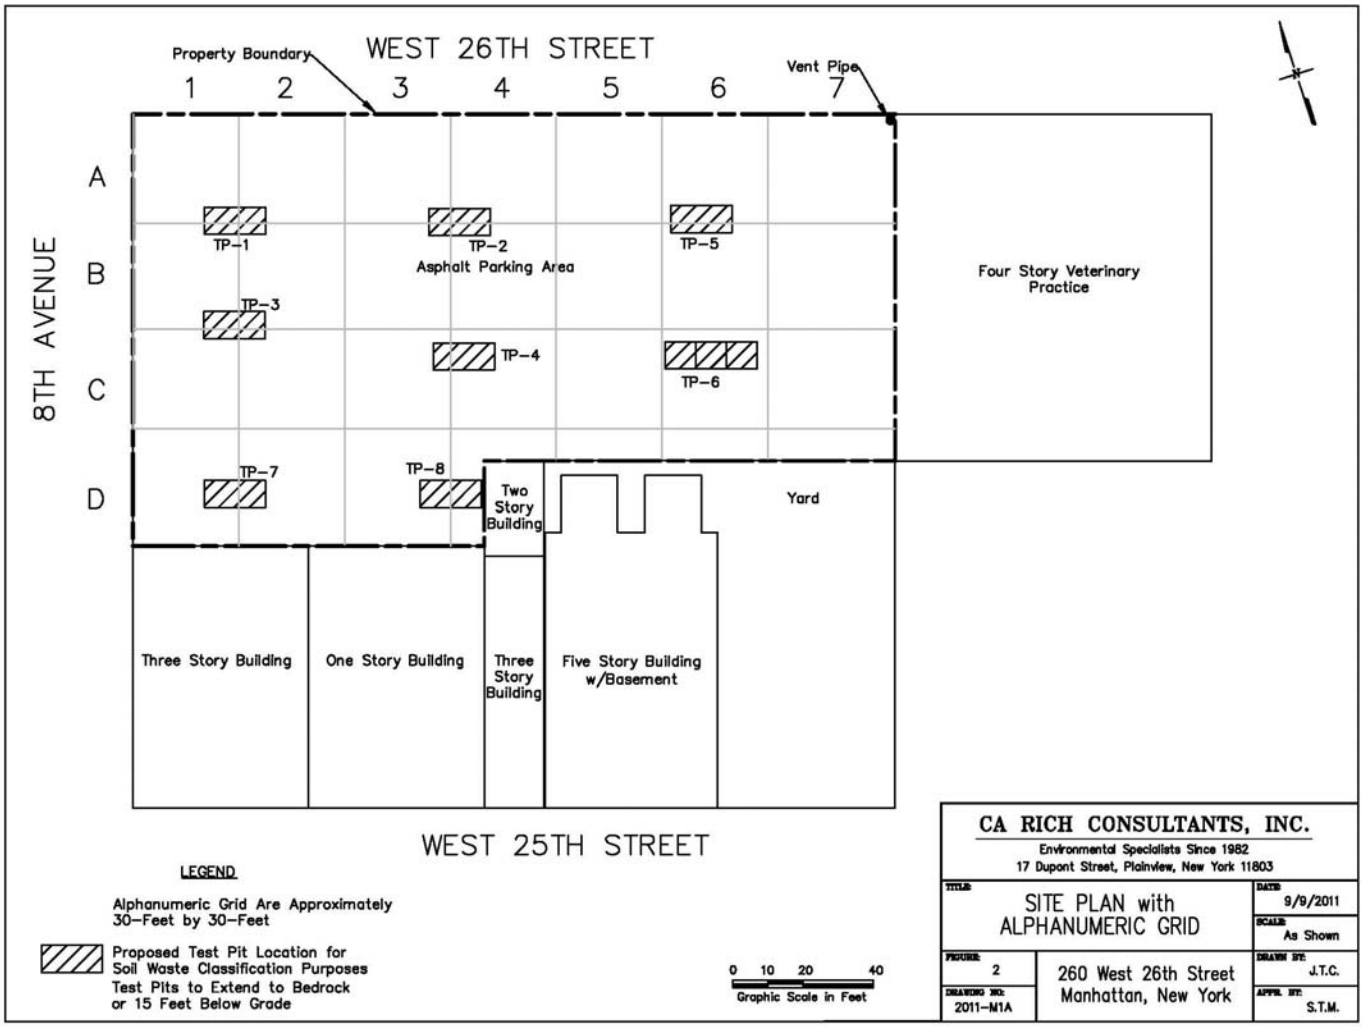

 File Name: _____

Photo Log

Photo 1 – A test pit was dug along the building to the neighboring building to the east for the engineer to design the proper underpinning.	
Photo 2 – A test pit was dug along the neighboring building on the south property line for the engineer to design the underpinning that will be required.	
Photo 3 -- Parging was installed along the south building to protect the their existing brick wall.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	10-28-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Rock chopping began in southeast corner of site.

Working In Grid #: C5, C6, C7

Air Monitoring (Since Last Report):

Air Monitoring was not performed today because no soil excavation took place. Monitoring will resume next week.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

Next week we plan to continue rock chopping and excavation with the disposal of soil at both the Soil Safe Facility in Logan, NJ and the Bellmarw Waterfront Redevelopment Site. The construction team will also be installing lagging as needed along the perimeter as the excavation proceeds.

Example:

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
Totals (trucks, cu.yds.)	84	2100	5	125	161	4025	18	450		

Site Grid Map

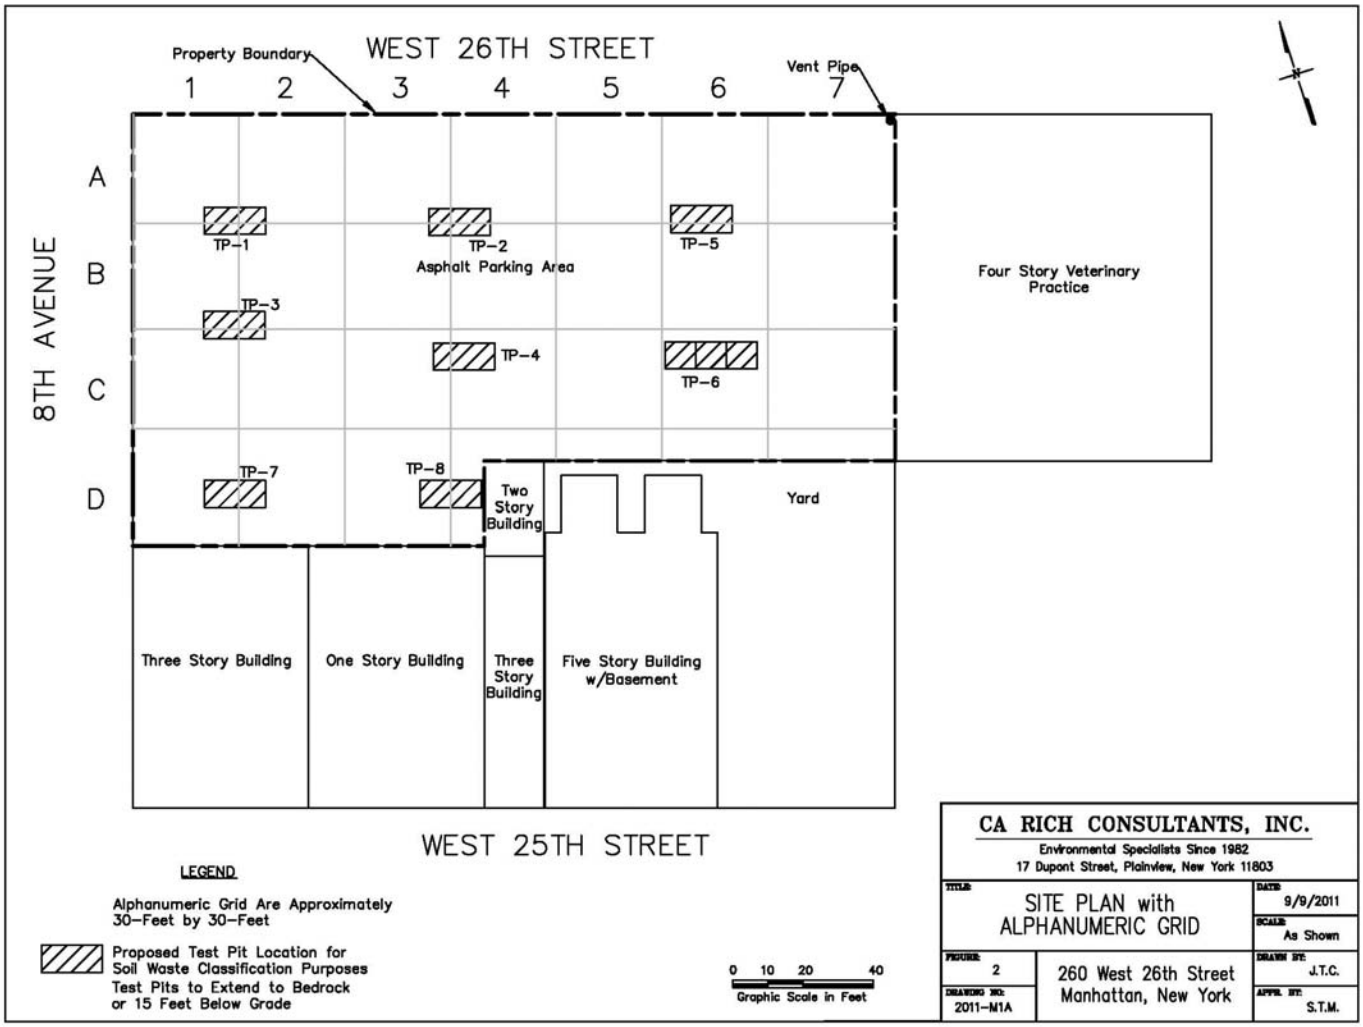

 File Name: _____

Photo Log

Photo 1 – Rock Chopping began in Southeast corner of site.	
Photo 2 – Rock chopping continued throughout the day, rocks were stockpiled and will be trucked to a recycling plant next week.	

 File Name: _____

Photo 3 -- Parging was installed along the south building to protect the their existing brick wall.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Danny Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	10-31-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Rock chopping continued on east side of site. Rock was stockpiled.

Working In Grid #: C5, C6, A5, A6, B5, B6

Air Monitoring (Since Last Report):

Air Monitoring was not performed today because no soil excavation took place. Monitoring will resume when soil excavation resumes tomorrow.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

Next week we plan to continue rock chopping and excavation with the disposal of soil at both the Soil Safe Facility in Logan, NJ and the Bellmarw Waterfront Redevelopment Site. The construction team will also be installing lagging as needed along the perimeter as the excavation proceeds.

Example:

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Solid *Or* Liquid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Gallons	Trucks	Cu. Yds. *Or* Gallons
Totals (trucks, cu.yds.)	84	2100	5	125	161	4025	18	450		

Site Grid Map

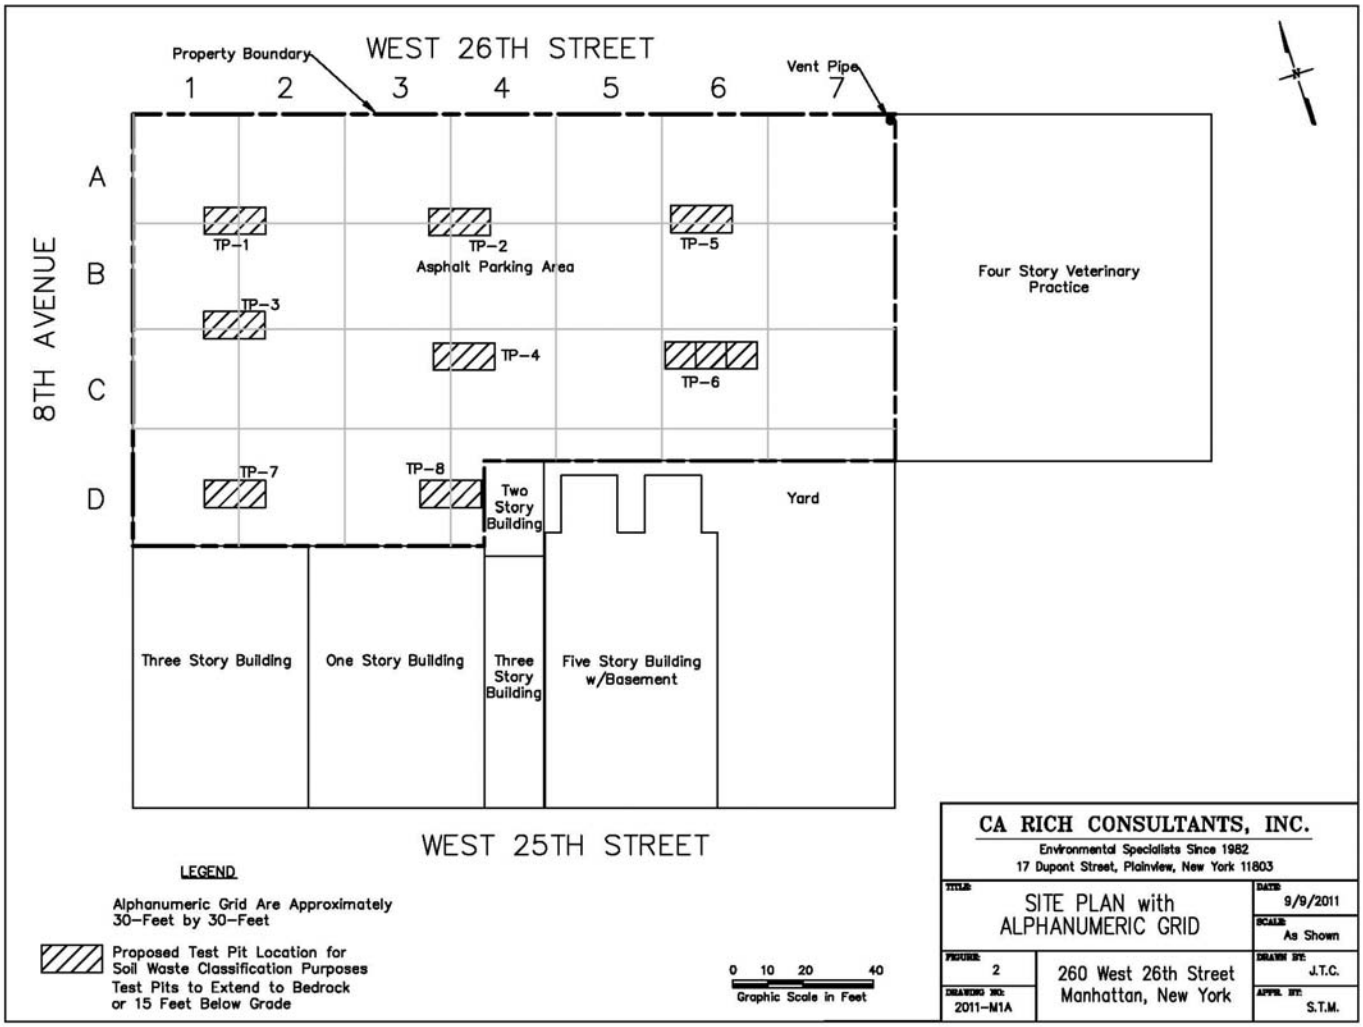

 File Name: _____

Photo Log

Photo 1 – Rock Chopping continued on site today. Rocks were stockpiled.	
Photo 2 – An old foundation wall from a demolished building was carefully removed.	
Photo 3 -- Rock Chopping near 26th Street on east half of site.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Steve Malinowski of CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy	x	Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	11-1-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Six truckloads of soil were excavated for from grids A7 and B7 and transported to the Soil Safe Facility in Logan, New Jersey for disposal as non-hazardous waste. Six truckloads of bedrock were transported to the Pave Co Facility in Medford< New York.

Working In Grids #: A7 and B7

Air Monitoring (Since Last Report):

Air Monitoring was performed during today's work activities. No problems were encountered.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

Tomorrow we plan to continue excavation and chopping of bedrock. The construction team will continue to install lagging as needed along the perimeter as the excavation proceeds.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.
					6	Appr. 150			6	Appr. 150
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	161	Appr. 4,025	18	Appr. 450	6	Appr. 150

Site Grid Map

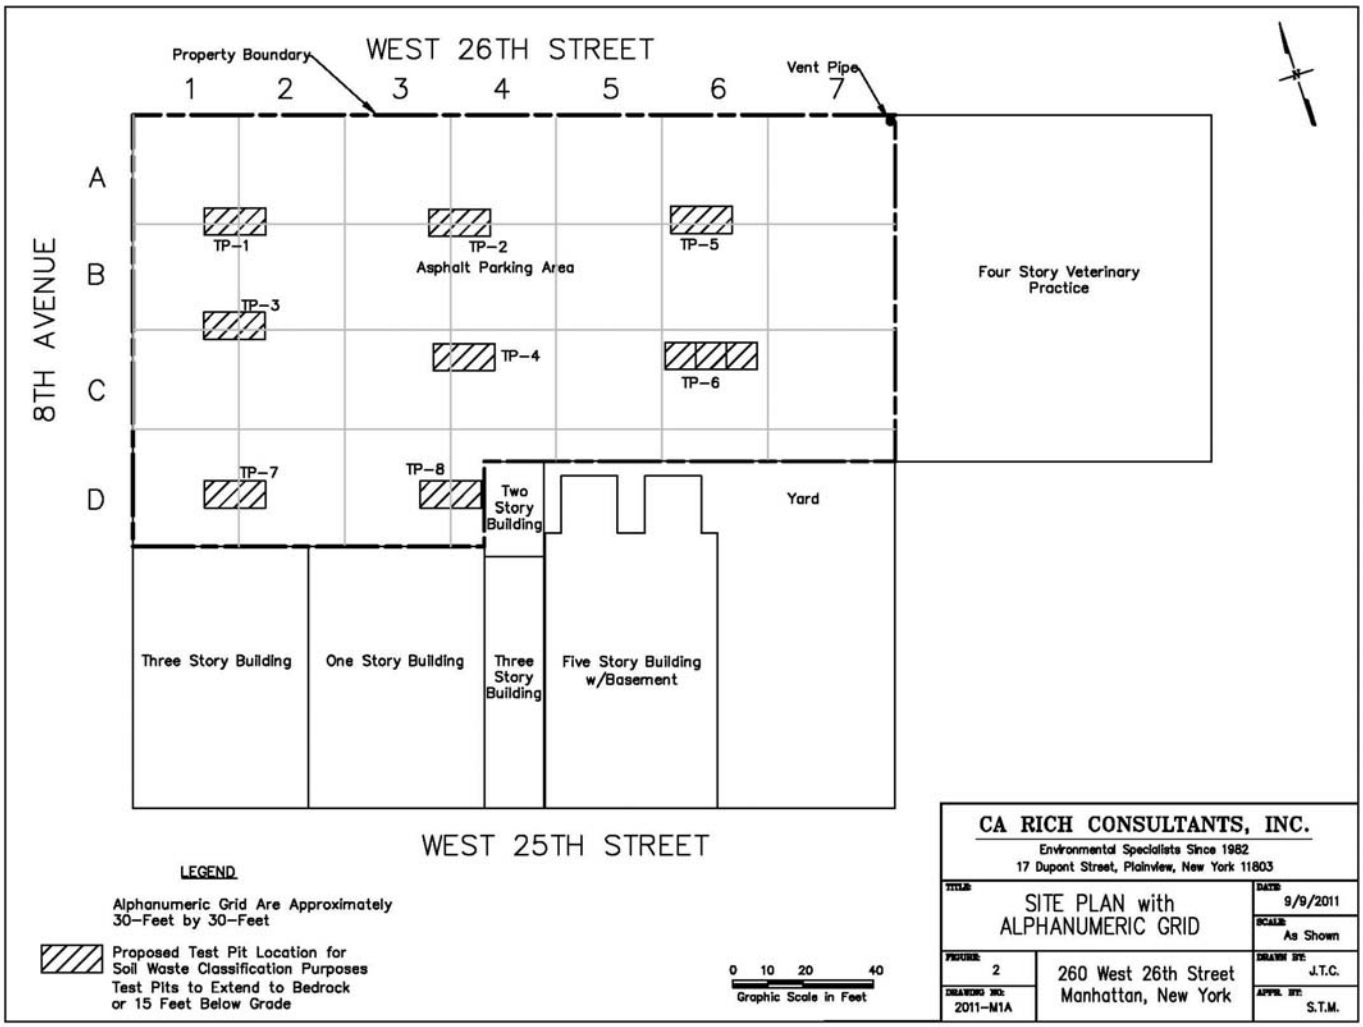

 File Name: _____

Photo Log

Photo 1 – Truck being loaded with material for grid A-7 for disposal at Soil Safe in Logan, NJ	
Photo 2 – Truck being loaded with material for grid A-7 for disposal at Soil Safe in Logan, NJ	
Photo 3 – Soil excavation along eastern site boundary.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Steve Malinowski of CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	11-2-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Twelve truckloads of soil were excavated from grids A6, A7, B6 and B7 and transported to the Soil Safe Facility in Logan, New Jersey for disposal as non-hazardous. Twenty-seven truckloads of bedrock were transported to the Pave Co Facility in Medford, New York and the Red Roc Materials Facility in Lyndhurst, NJ.

Working In Grids #: A6, A7, B6 and B7

Air Monitoring (Since Last Report):

Air Monitoring was performed during today's excavation activities. No problems were encountered.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

Tomorrow we plan to continue soil excavation and disposal activities to Soil Safe in Logan Township, New Jersey. Chipping and removal of bedrock will also continue. The construction team will install lagging as needed along the perimeter as the excavation proceeds.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks		Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
					12	Appr. 300			6	Appr. 150	21	Appr. 525
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	179	Appr. 4,475	18	Appr. 450	12	Appr. 300	21	Appr. 525

Site Grid Map

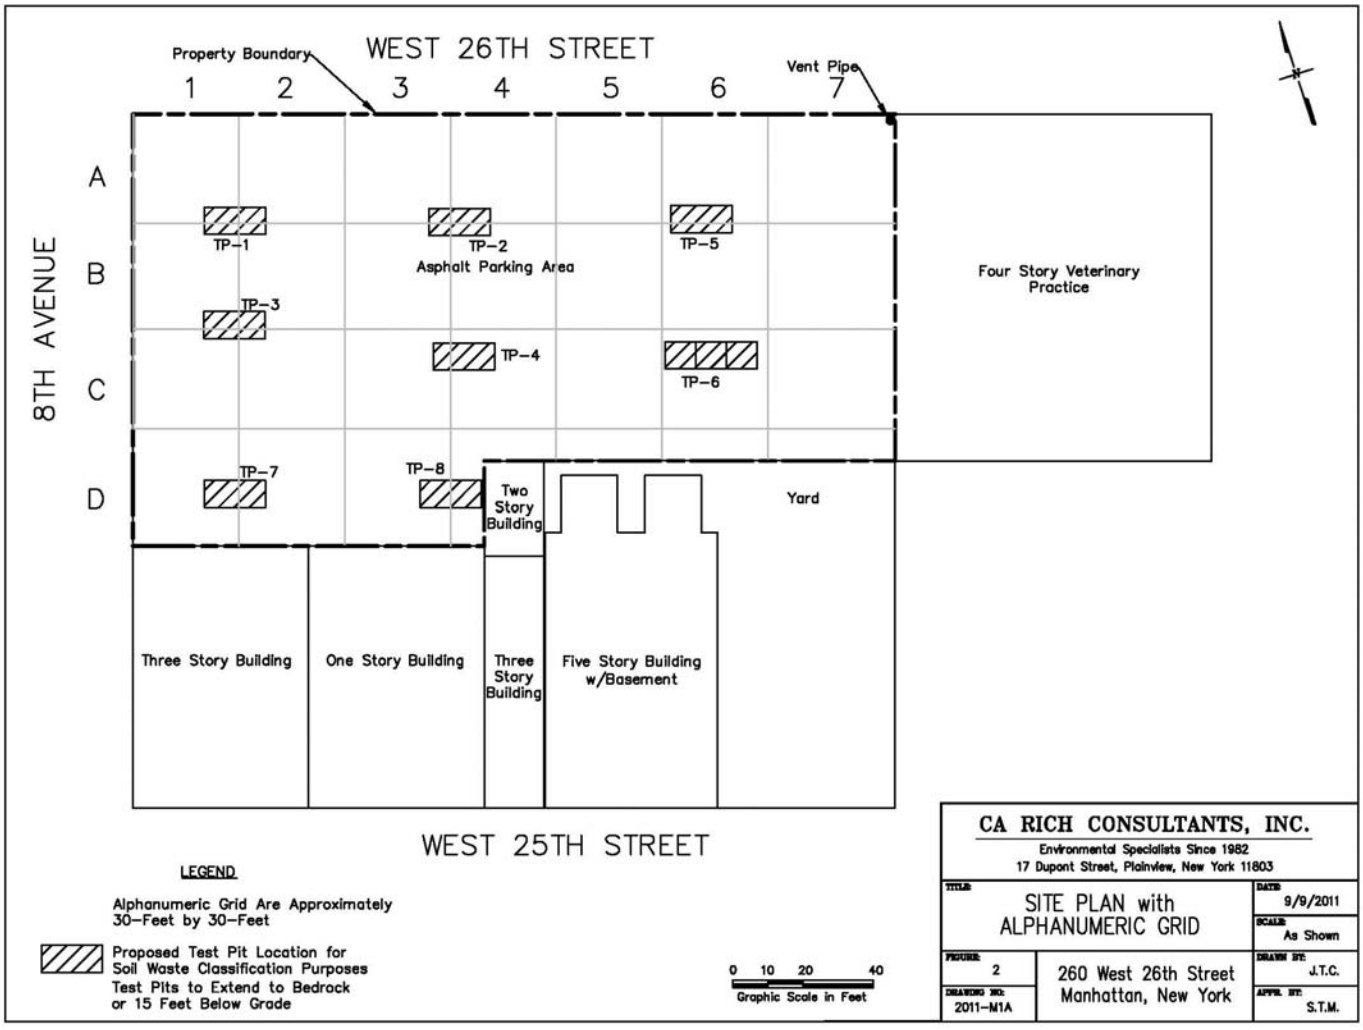

 File Name: _____

Photo Log

Photo 1 – Excavation of soil and exposed bedrock near southeast corner of site.	
Photo 2 – Chipping away at exposed bedrock near southeast corner of the site.	
Photo 3 – Chipping exposed bedrock and excavating near the northeast corner of the site.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Steve Malinowski of CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	11-3-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Eleven truckloads of soil were excavated from grids A6, A7, B6 and B7 and transported to the Soil Safe Facility in Logan, New Jersey for disposal as non-hazardous. Eleven truckloads of bedrock were transported to the Pave Co Facility in Medford, New York and the Red Roc Materials Facility in Lyndhurst, NJ.

Working In Grids #: A6, A7, B6 and B7

Air Monitoring (Since Last Report):

Air Monitoring was performed during today's excavation activities. No problems were encountered.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

Tomorrow we plan to continue soil excavation and disposal activities to Soil Safe in Logan Township, New Jersey. Chipping and removal of bedrock will also continue. The construction team will install lagging as needed along the perimeter as the excavation proceeds.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
					11	Appr. 275			5	Appr. 125	6	Appr. 150
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	190	Appr. 4,750	18	Appr. 450	17	Appr. 425	27	Appr. 675

Site Grid Map

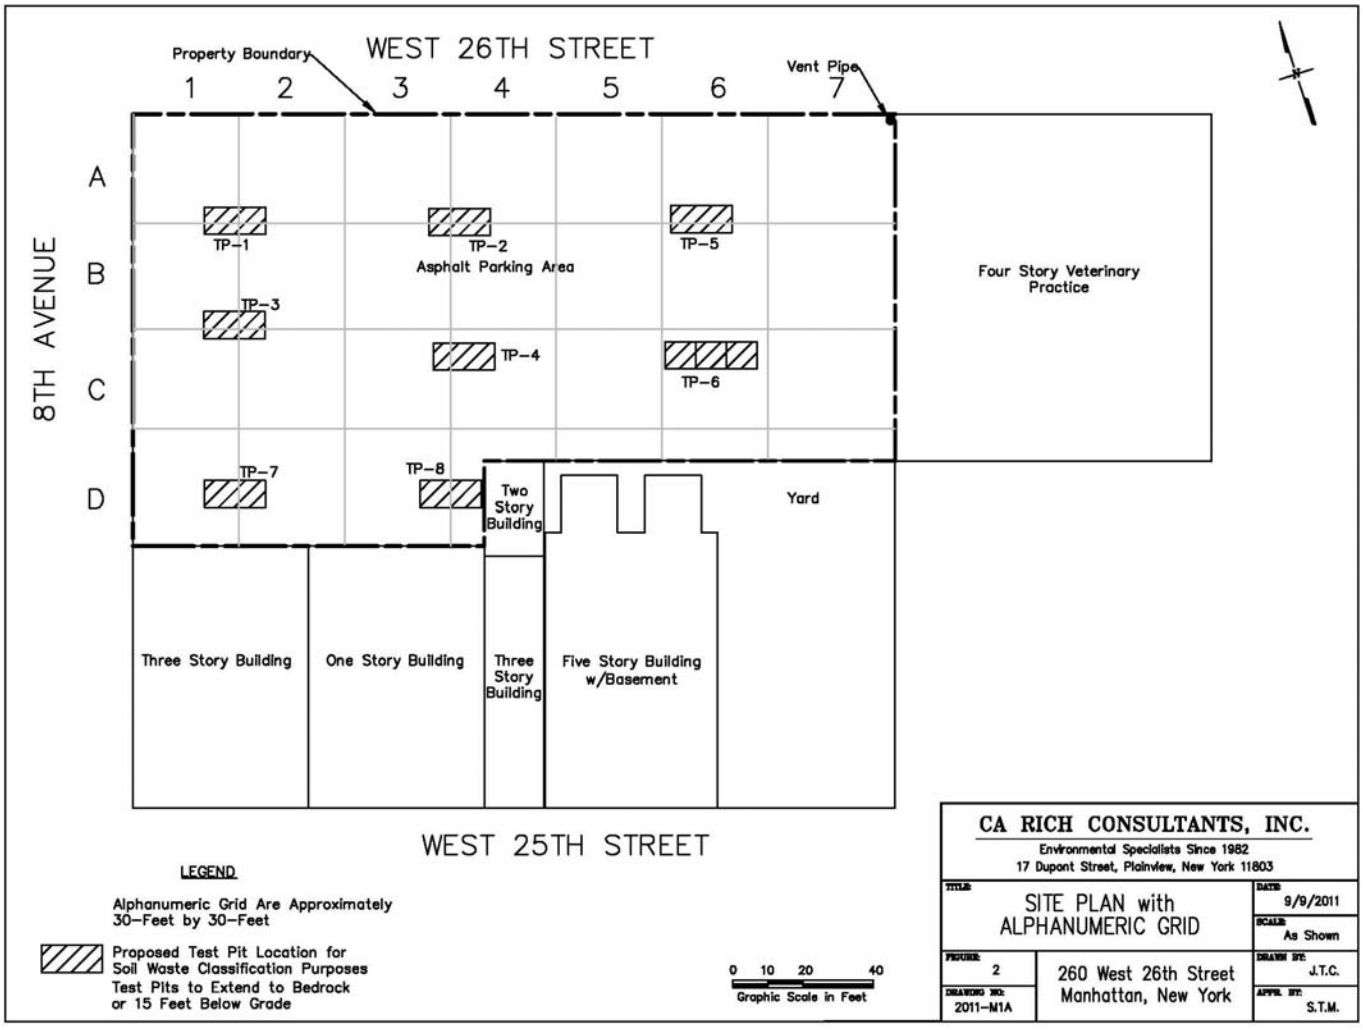

 File Name: _____

Photo Log

Photo 1 – Excavation of soil and exposed bedrock near southeast corner of site.	
Photo 2 – Preliminary setup of dewatering pump and bag filtration system for test run.	
Photo 3 – Chipping exposed bedrock and excavating near the northeast corner of the site.	

File Name: _____

DAILY STATUS REPORT

Prepared By: Steve Malinowski of CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	11-4-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Three truckloads of soil were excavated from grids A7 and B7 and transported to the Soil Safe Facility in Logan, New Jersey for disposal as non-hazardous. Forty-one truckloads of bedrock were transported to the Pave Co Facility in Medford, New York and the Red Roc Materials Facility in Lyndhurst, NJ.

A pump and bag filter system was delivered to the site and utilized to facilitate the collection of a water sample for metals to satisfy a request by NYCDEP. The construction team has applied to NYCDEP for a permit to discharge stormwater and groundwater from the site to the NYC sewer.

Working In Grids #: A6, A7, B6 and B7

Air Monitoring (Since Last Report):

Air Monitoring was performed during today's excavation activities. No problems were encountered.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

Next week we plan to continue soil excavation and disposal activities to Soil Safe in Logan Township, New Jersey. Chipping and removal of bedrock will also continue. The construction team will install lagging as needed along the perimeter as the excavation proceeds.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
					3	Appr. 75			5	Appr. 125	36	Appr. 900
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	193	Appr. 4,825	18	Appr. 450	22	Appr. 430	63	Appr. 675

Site Grid Map

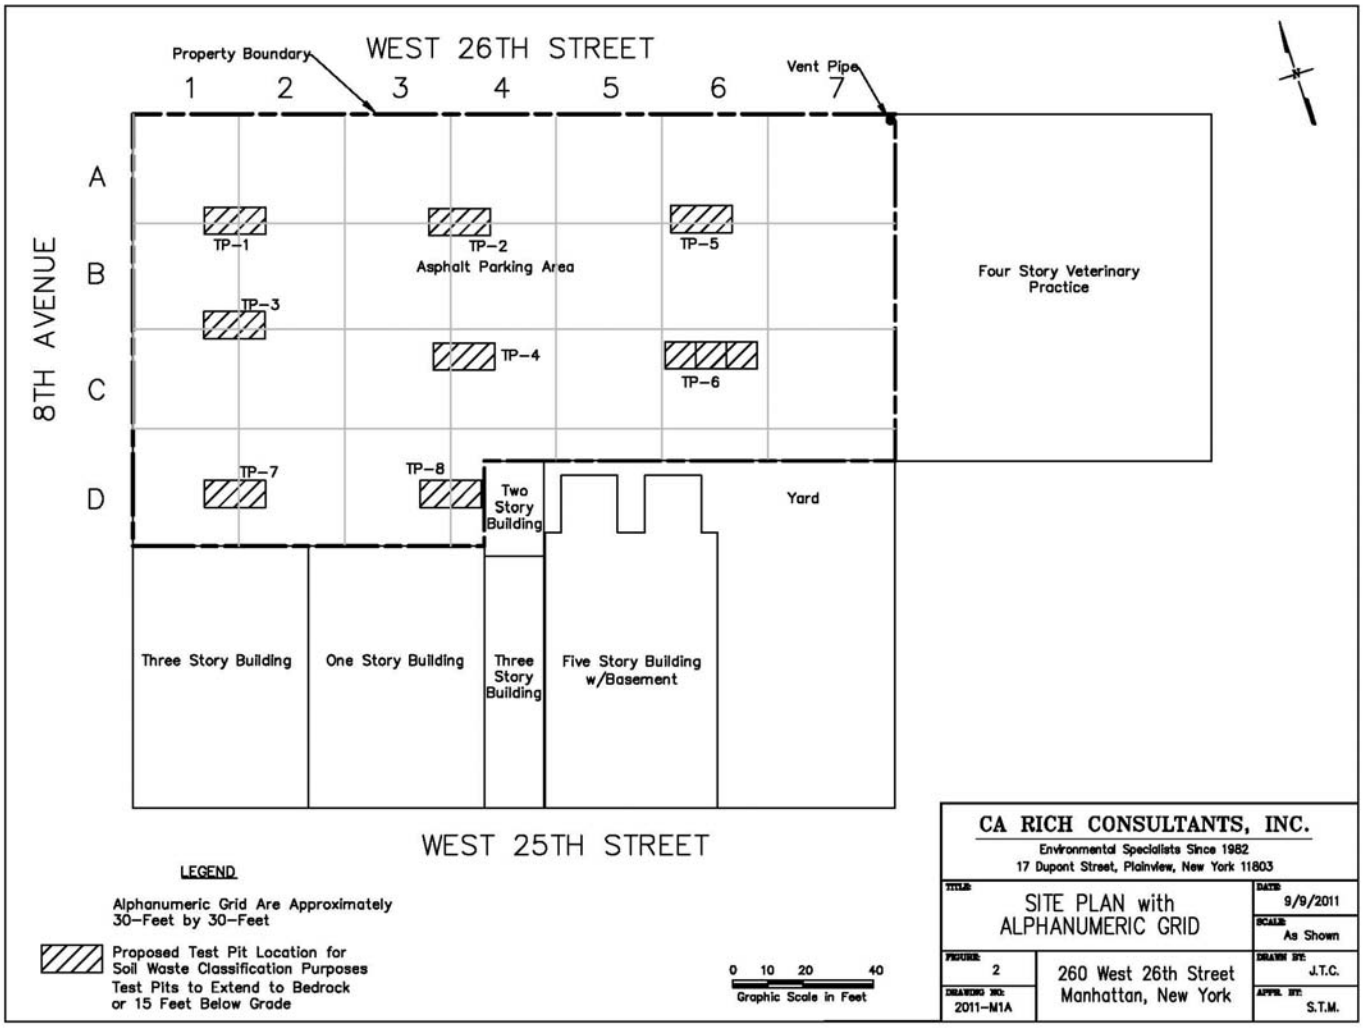

 File Name: _____

Photo Log

Photo 1 – Looking east across site at excavation equipment chopping bedrock.	
Photo 2 – Excavation equipment sorting bedrock pieces.	
Photo 3 – Collection of groundwater sample for NYCDEP permit from effluent after pumping through bag filtration system.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Steve Malinowski of CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	11-5-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Twenty-five truckloads of bedrock were transported to the Red Roc Materials Facility in Lyndhurst, NJ.

Lagging boards were delivered to the site. Lagging continued along 26th Street and the South Property Line

Working In Grids #: A5, A6, A7, B5, B6, B7, C5, C6, C7

Air Monitoring (Since Last Report):

No Air Monitoring was conducted today because excavation did not occur.

Problems Encountered:

No problems were encountered.

Planned Activities for Next Week:

Next week we plan to continue soil excavation and disposal activities to Soil Safe in Logan Township, New Jersey. Chipping and removal of bedrock will also continue. The construction team will install lagging as needed along the perimeter as the excavation proceeds.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
											25	Appr. 625
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	193	Appr. 4,825	18	Appr. 450	22	Appr. 550	88	Appr. 2200

Site Grid Map

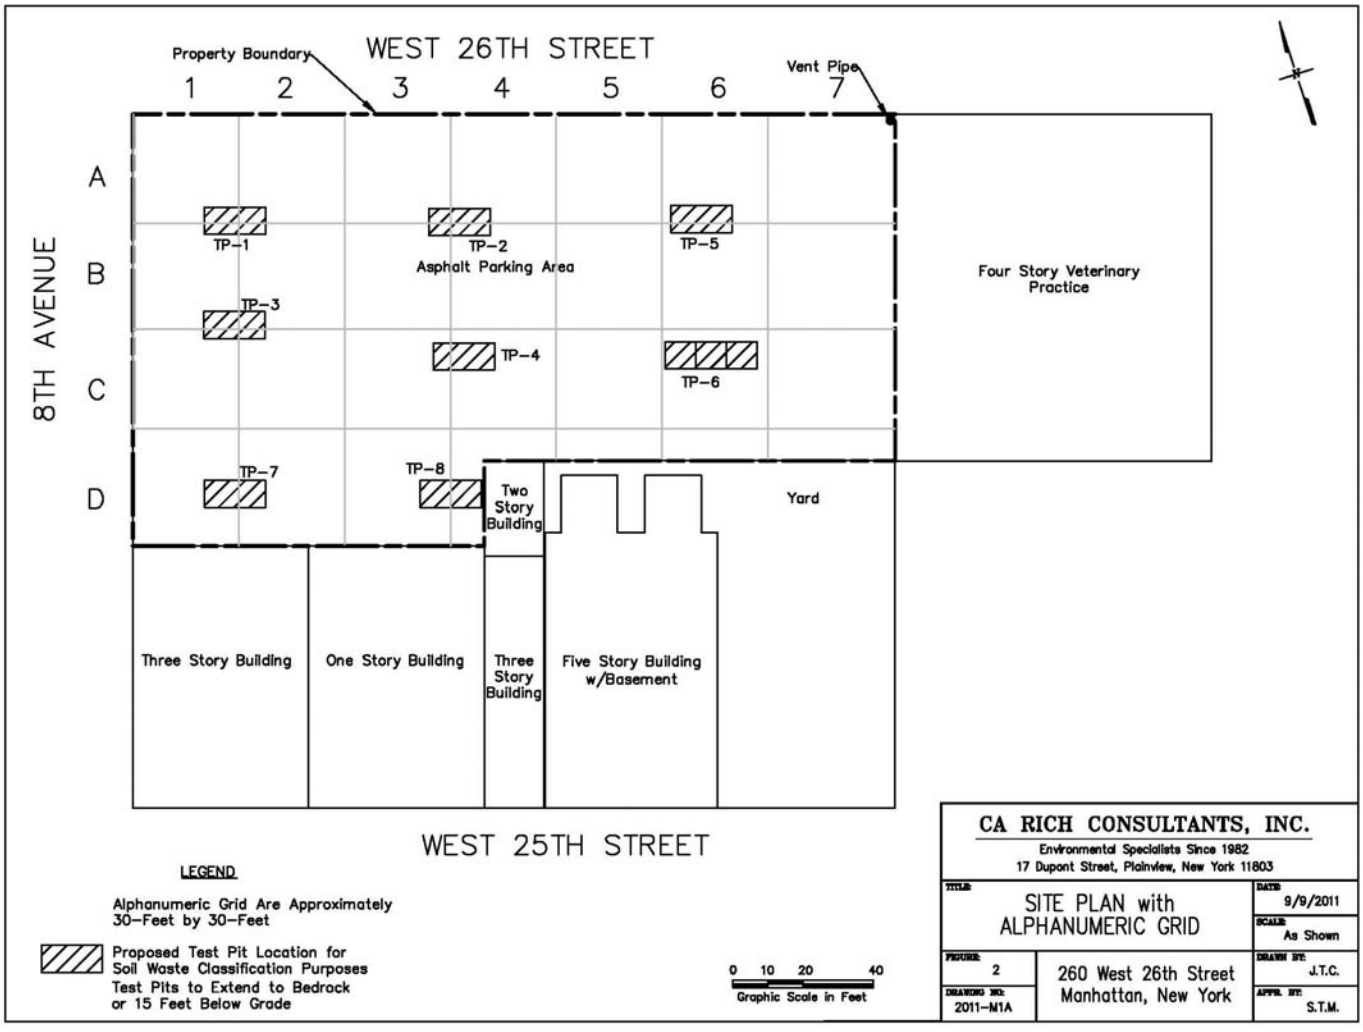

 File Name: _____

Photo Log

Photo 1 – Additional lagging was installed along 26th Street.	
Photo 2 – Additional Lagging boards were delivered to the site.	
Photo 3 – (25) Trucks of Bedrock were transported to Red Roc Facility.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Steve Malinowski of CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	11-7-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Two truckloads of soil were excavated from grids A7 and B7 and transported to the Soil Safe Facility in Logan, New Jersey for disposal as non-hazardous. Three truckloads of bedrock were transported to the Red Roc Materials Facility in Lyndhurst, NJ.

Welder was on site today to begin extending HP Piles along 26th Ave. in preparation to install waler and rakers.

Working In Grids #: A5, A6, A7, B5, B6, B7, C5, C6, C7, D5, D3, D5, D6, D7

Air Monitoring (Since Last Report):

Air Monitoring was not performed today. Very minor excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

DEP was on site today in response to a noise complaint due to the rock chopping. No tickets were issued.

Planned Activities for Next Week:

We plan to continue soil excavation and disposal activities to Soil Safe in Logan Township, New Jersey. Chipping and removal of bedrock throughout the week. The construction team will install lagging as needed along the perimeter as the excavation proceeds.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
					2	Appr. 50					3	Appr. 75
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	195	Appr. 4,875	18	Appr. 450	22	Appr. 550	91	Appr. 2275

Site Grid Map

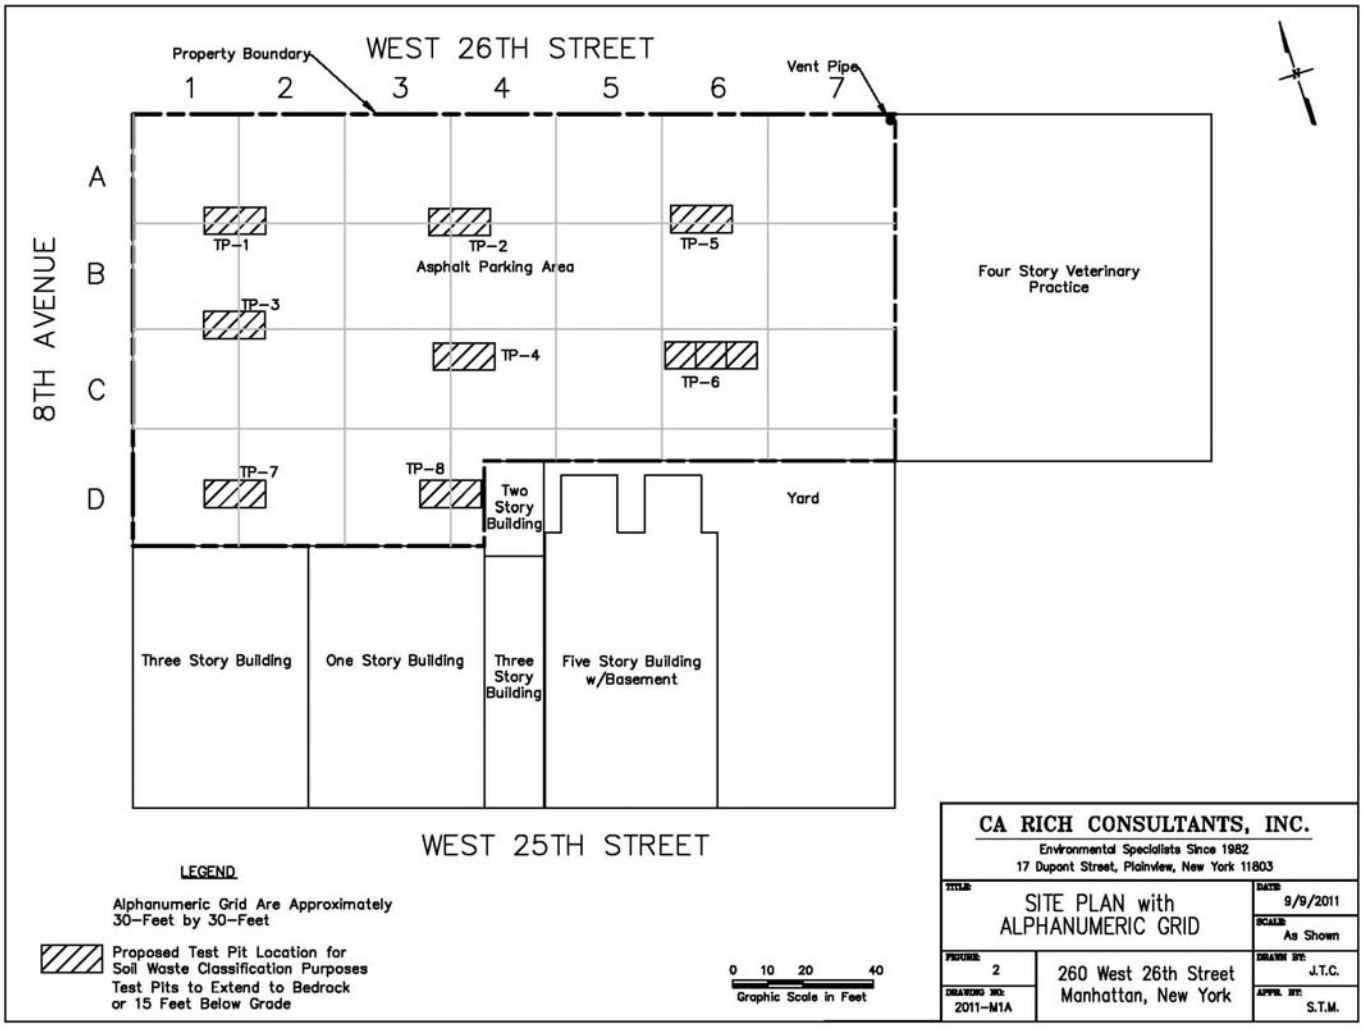

 File Name: _____

Photo Log

Photo 1 – Line Drill was delivered on site to break rock next to neighboring buildings.	
Photo 2 – Existing Foundation Wall was taken down by hand.	
Photo 3 – Welder on site today to extend the height of some HP Piles to prepare for installation of waler and rakers.	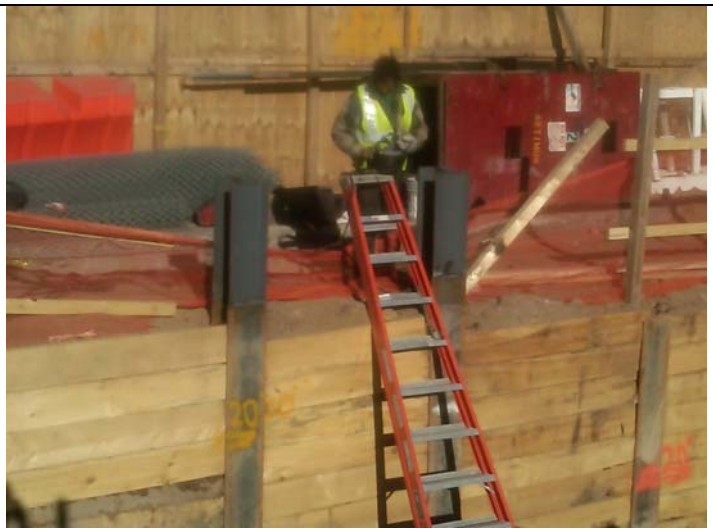

 File Name: _____

DAILY STATUS REPORT

Prepared By: Steve Malinowski of CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	11-8-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Twenty-two truckloads of bedrock were transported to the Red Roc Materials Facility in Lyndhurst, NJ.

Rock chopping continued and welder was on site today to install walers along 26th Street and 8th Ave.

Working In Grids #: A5, A6, A7, B5, B6, B7, C5, C6, C7, D5, D3, D5, D6, D7, A1

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

We plan to continue soil excavation and disposal activities to Soil Safe in Logan Township, New Jersey. Chipping and removal of bedrock throughout the week. The construction team will install lagging as needed along the perimeter as the excavation proceeds.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
											22	Appr. 550
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	195	Appr. 4,875	18	Appr. 450	24	Appr. 600	113	Appr. 2825

Site Grid Map

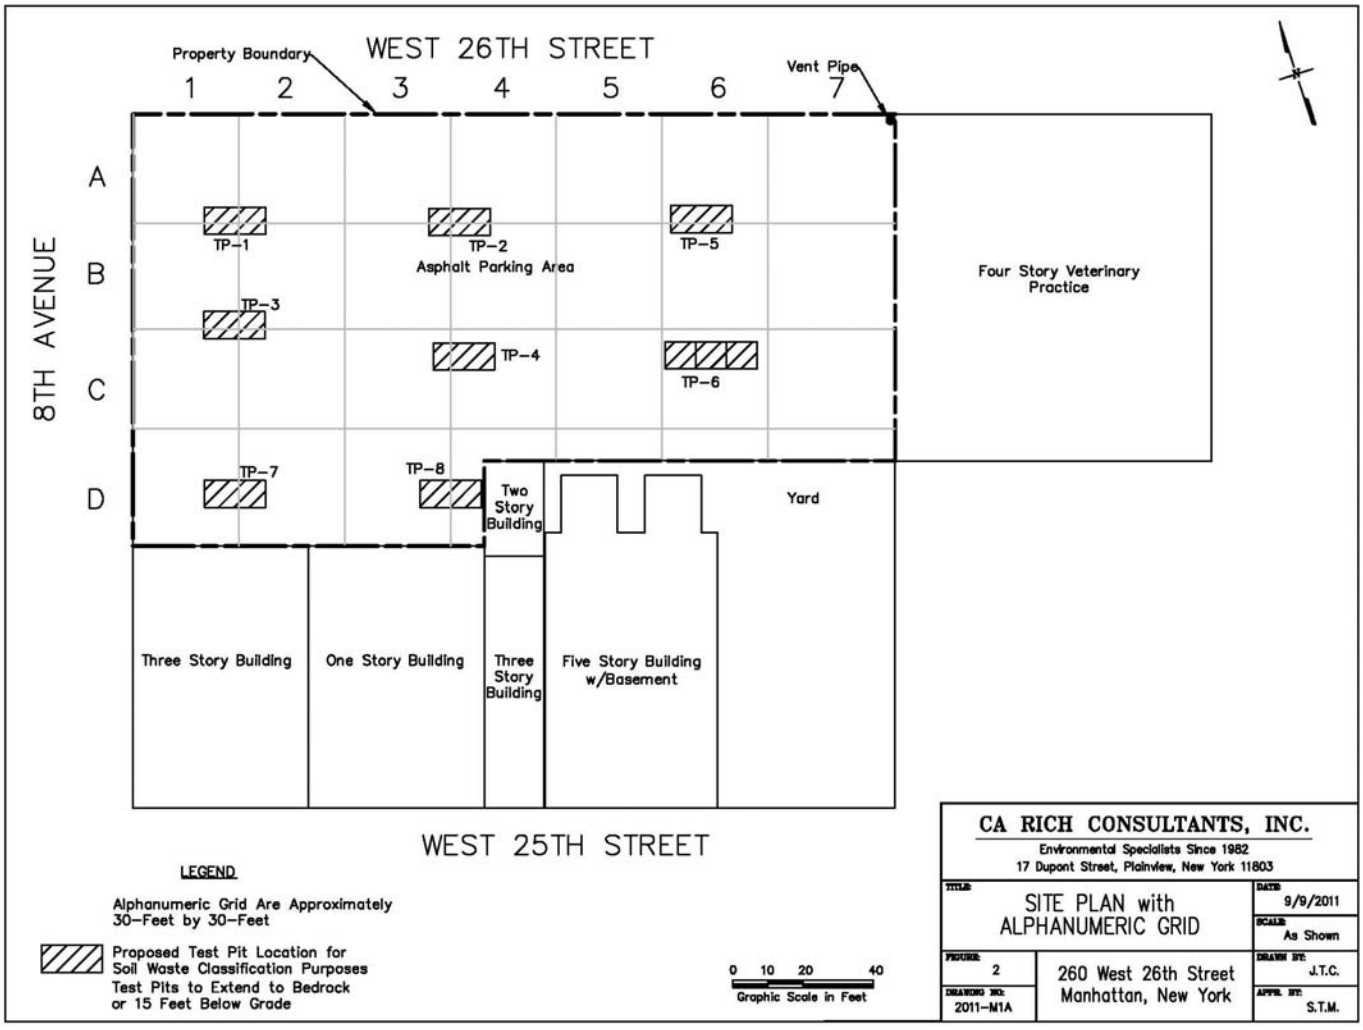

 File Name: _____

Photo Log

Photo 1 – Lagging continued to be installed around the perimeter of the site.	
Photo 2 – Waler beginning to be installed along 8th Ave.	
Photo 3 – Welder connecting waler along 26th Street and 8th Ave.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Steve Malinowski of CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	11-9-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

.

Excavation contractor continued rock chopping and stockpiled rock.

Welder's continued to install waler along 8th Ave. today.

Working In Grids #: A5, A6, B5, B6, C5, C6, D5, D3, D5, D6, A1, B1

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

We plan to continue soil excavation and disposal activities to Soil Safe in Logan Township, New Jersey. Chipping and removal of bedrock throughout the week. The construction team will install lagging as needed along the perimeter as the excavation proceeds.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	195	Appr. 4,875	18	Appr. 450	24	Appr. 600	113	Appr. 2825

Site Grid Map

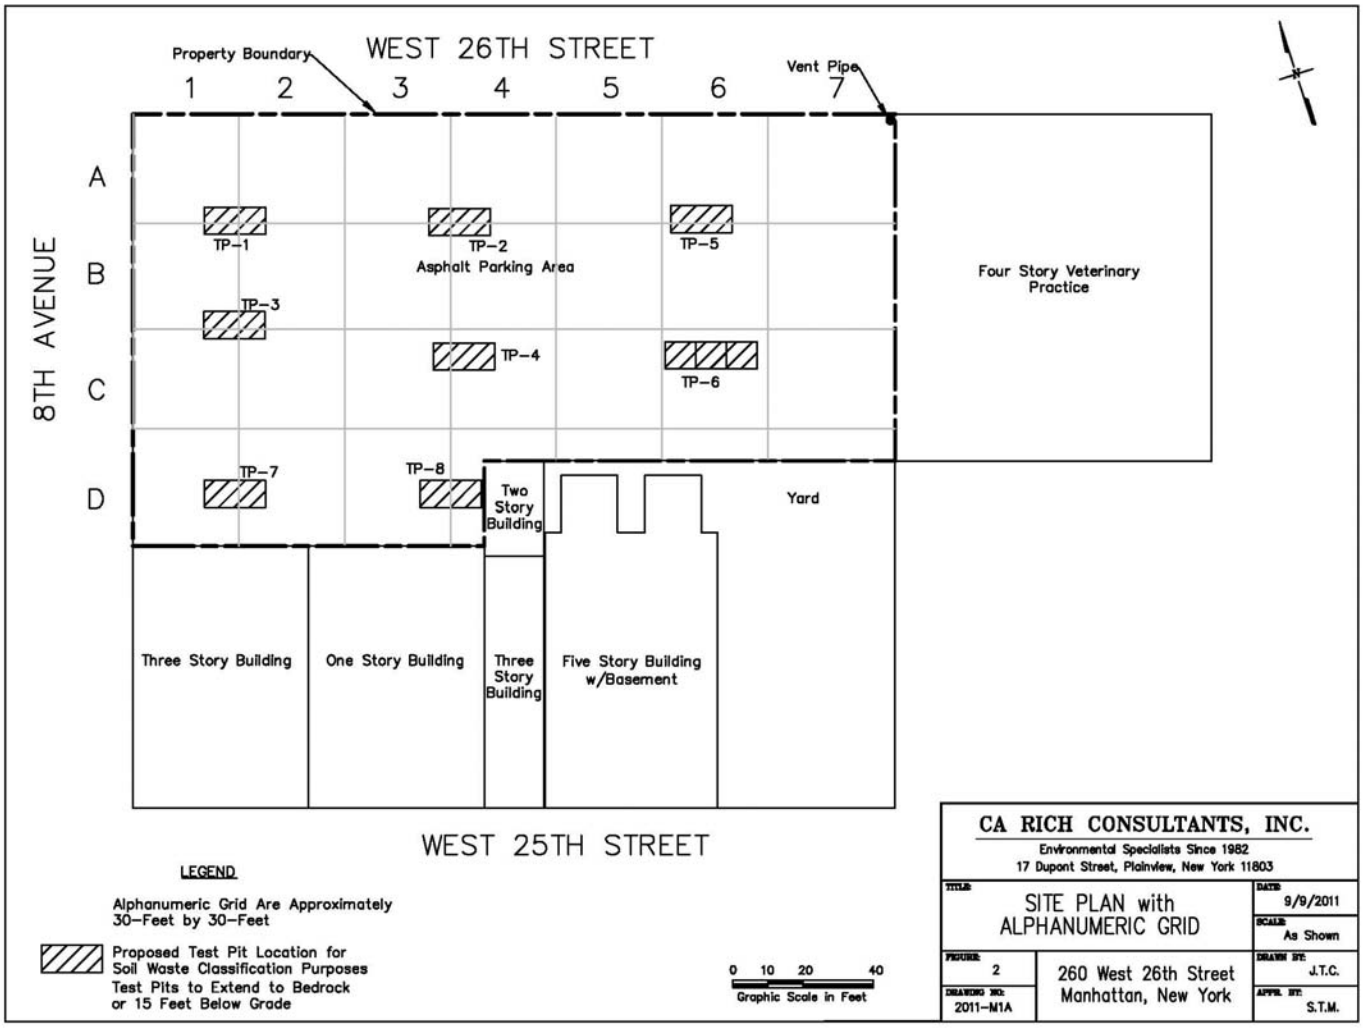

 File Name: _____

Photo Log

Photo 1 – Rock chopping and excavating beside lagging along 26th Street.	
Photo 2 – Rock chopping in Southeast corner of site. Rock was stockpiled and will be trucked to Red Roc Materials tomorrow.	
Photo 3 – Welder continuing to install waler along 8th Ave.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Steve Malinowski of CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	11-10-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

(12) Truckloads of Bedrock were transported to Red Roc Material Facility.

Excavation contractor continued rock chopping.

Welder's continued to install waler and rakers along 8th Ave. today.

Working In Grids #: A5, A6, B5, B6, C5, C6, D5, D3, D5, D6, A1, B1

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

We plan to continue soil excavation and disposal activities to Soil Safe in Logan Township, New Jersey. Chipping and removal of bedrock throughout the week. The construction team will install lagging as needed along the perimeter as the excavation proceeds.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
											12	Appr 300
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	195	Appr. 4,875	18	Appr. 450	24	Appr. 600	125	Appr. 3125

Site Grid Map

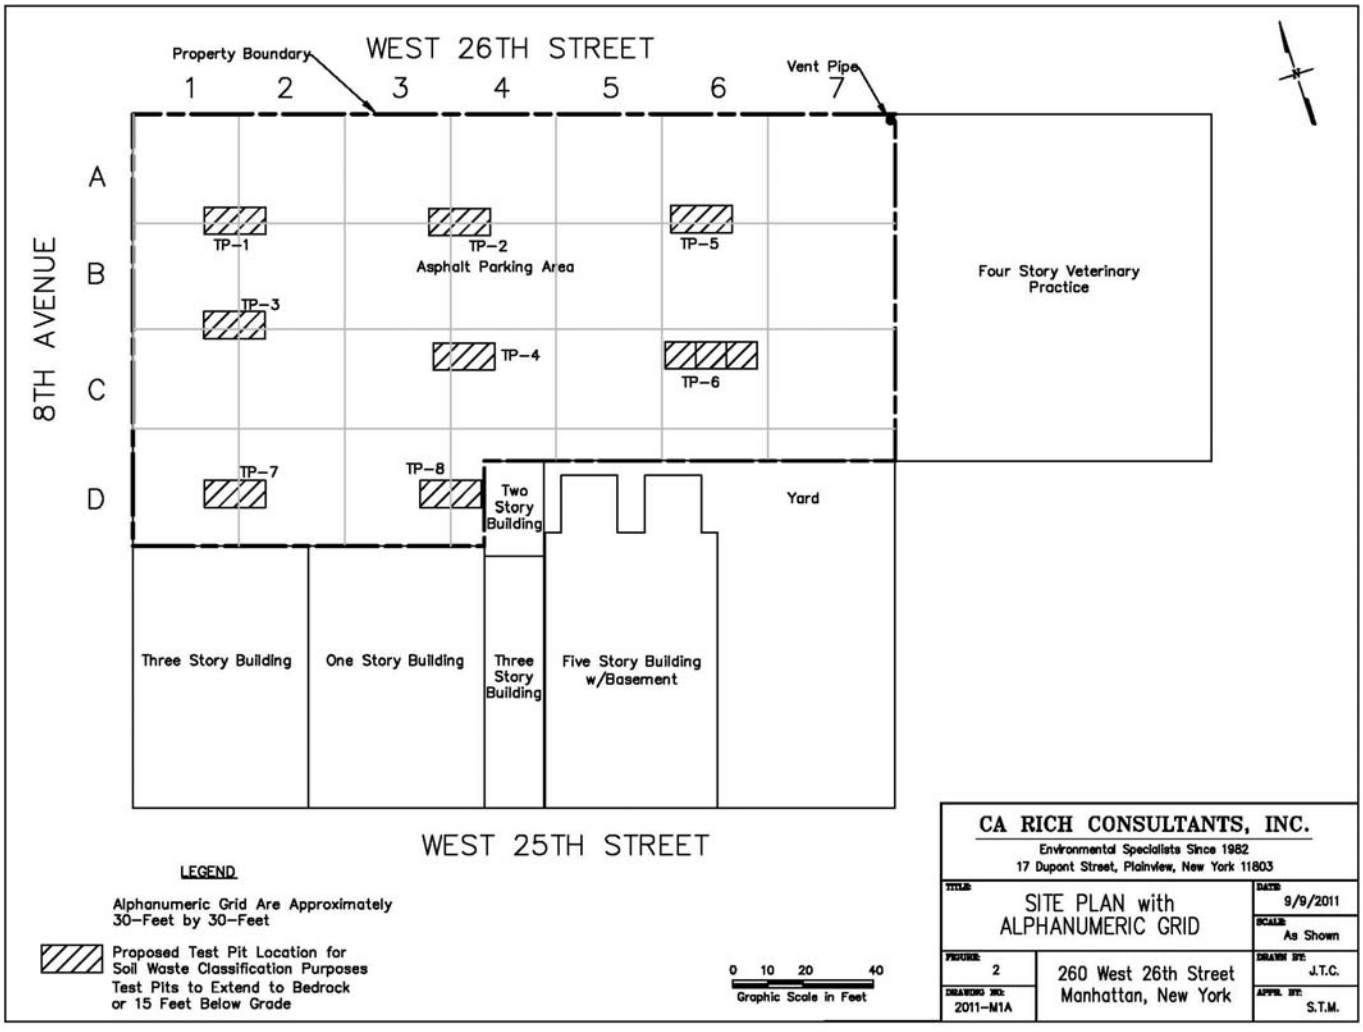

 File Name: _____

Photo Log

Photo 1 – Rock chopping and excavating beside lagging along 26th Street.	
Photo 2 – W10X49 Brace was installed in the corner of 26th Street and 8th Ave.	
Photo 3 – South Property wall was marked out to prepare for underpinning. Underpinning to begin next week.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Steve Malinowski of CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	11-11-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Excavation contractor continued rock chopping.

Welder's continued to install waler and rakers along 8th Ave. today.

Working In Grids #: A5, A6, B5, B6, C5, C6, D5, D3, D5, D6, A1, B1

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

We plan to continue soil excavation and disposal activities to Soil Safe in Logan Township, New Jersey. Chipping and removal of bedrock throughout the week. The construction team will install lagging as needed along the perimeter as the excavation proceeds. Underpinning neighboring buildings will begin next week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	195	Appr. 4,875	18	Appr. 450	24	Appr. 600	125	Appr. 3125

Site Grid Map

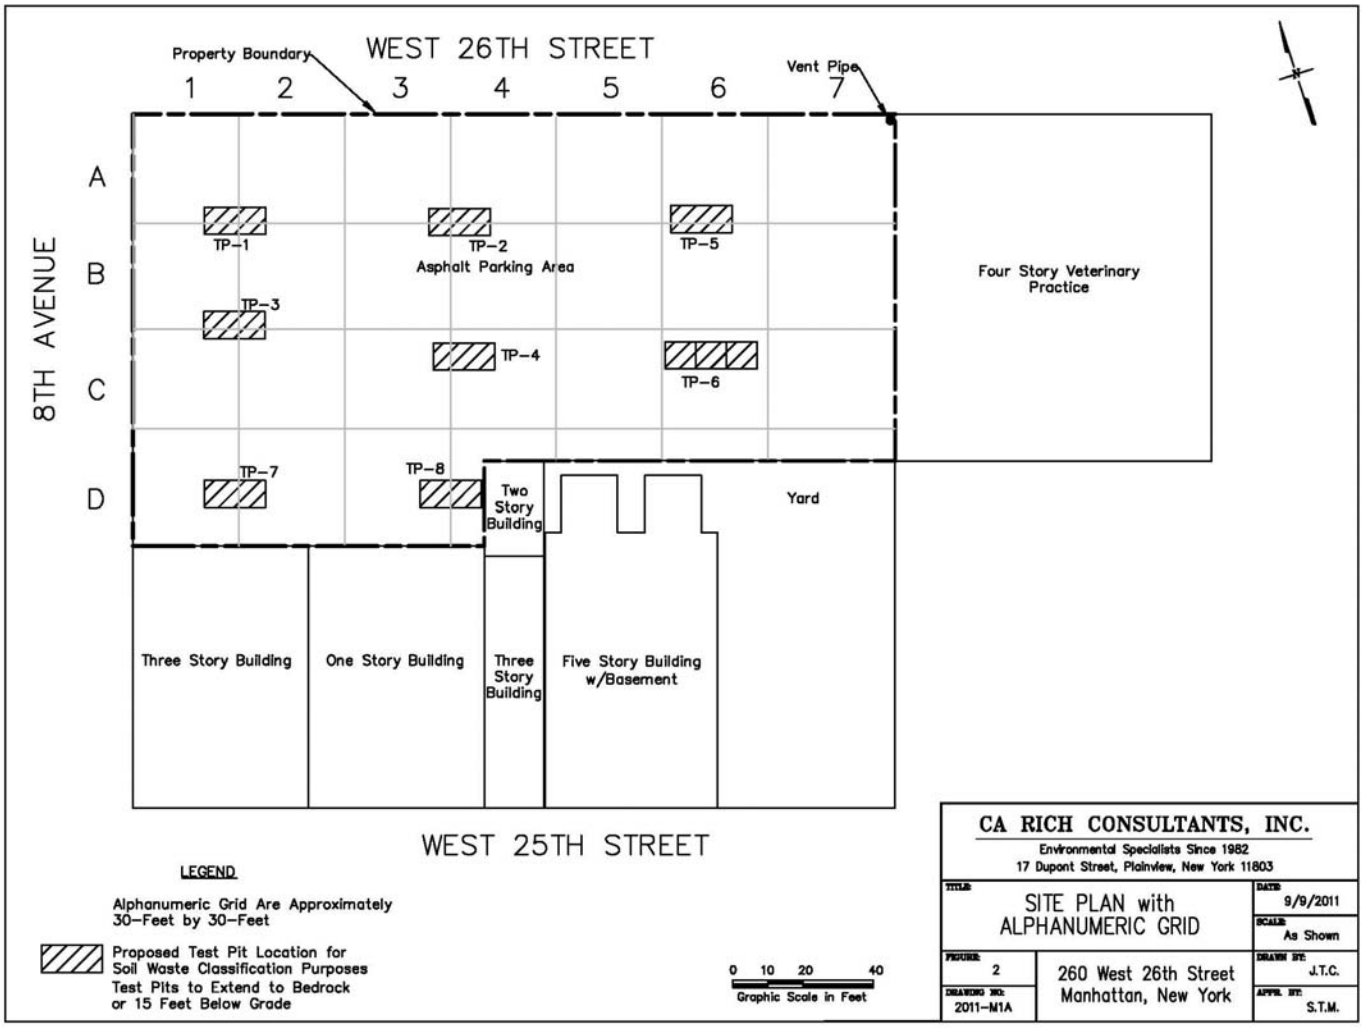

 File Name: _____

Photo Log

Photo 1 – Rock chopping and lagging being installed along South property line.	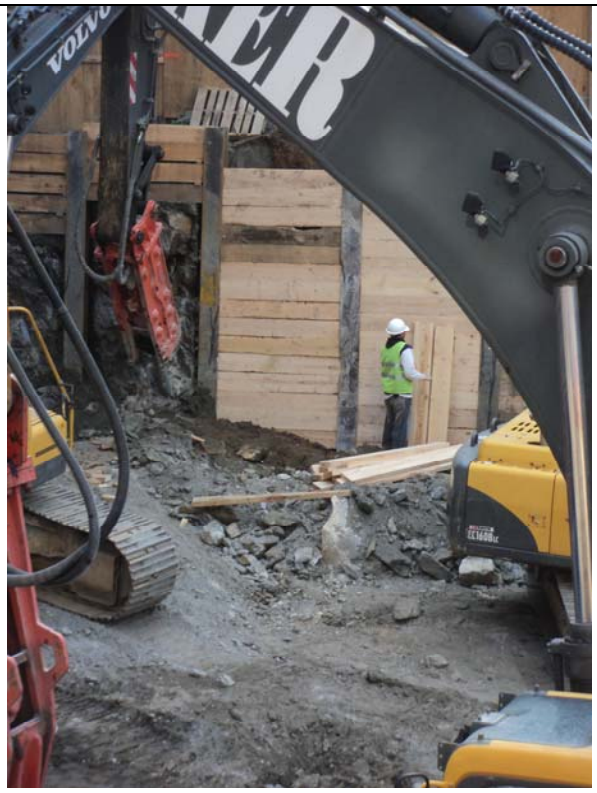
Photo 2 – Welder continued to install waler along 8th Ave.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Steve Malinowski of CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	11-12-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

(24) Trucks were filled with Bedrock and transported to Red Roc Facility in Lyndhurst, NJ.

Lagging continued to be installed along perimeter of site.

Working In Grids #: A5, A6, B5, B6, C5, C6, D5, D3, D5, D6,

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

We plan to continue soil excavation and disposal activities to Soil Safe in Logan Township, New Jersey. Chipping and removal of bedrock throughout the week. The construction team will install lagging as needed along the perimeter as the excavation proceeds. Underpinning neighboring buildings will begin next week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
											24	600
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	195	Appr. 4,875	18	Appr. 450	24	Appr. 600	149	Appr. 3725

Site Grid Map

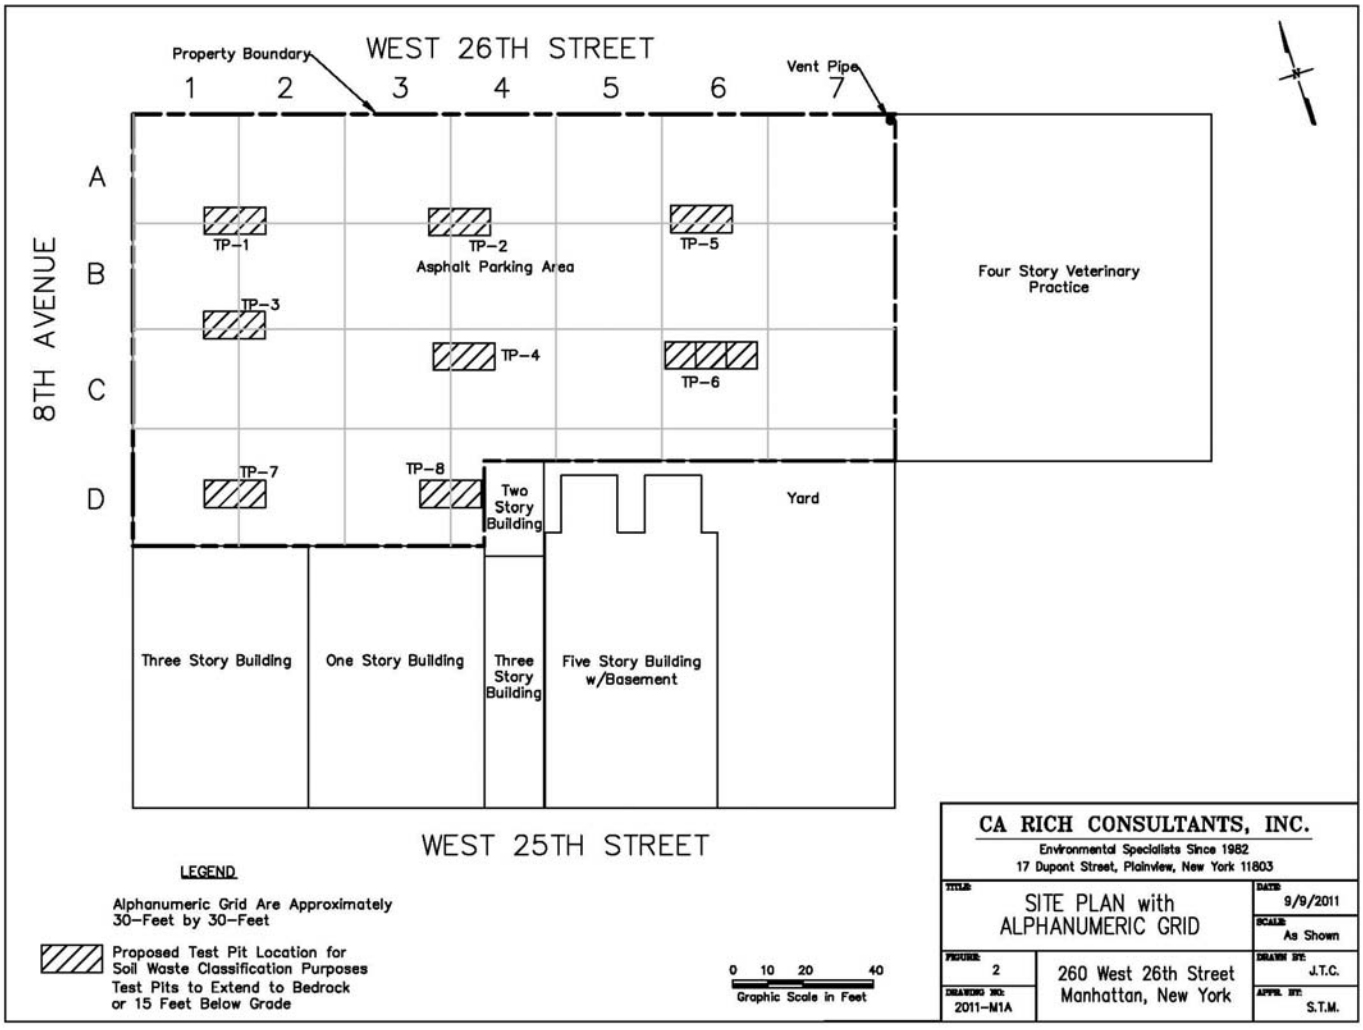

 File Name: _____

Photo Log

Photo 1 – (24) Trucks were filled with Bedrock and transported to Red Roc Facility.	
Photo 2 – Working on installing lagging in northeast corner of the site.	
Photo 3 – Drilling rock out to install lagging along 26th Street.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Steve Malinowski of CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	11-14-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Rock Chopping continued.

Waler was installed in Southwest corner of the site.

Lagging continued to be installed along perimeter of site.

Underpinning of the neighboring building at the south property line began.

Working In Grids #: A5, A6, B5, B6, C5, C6, D5, D3, D4, D5, D6,

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

We plan to continue soil excavation and disposal activities to Soil Safe in Logan Township, New Jersey. Bedrock will continued to be chopped and trucked off site throughout the week. The construction team will install lagging as needed along the perimeter as the excavation proceeds. Underpinning neighboring buildings will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	195	Appr. 4,875	18	Appr. 450	24	Appr. 600	149	Appr. 3725

Site Grid Map

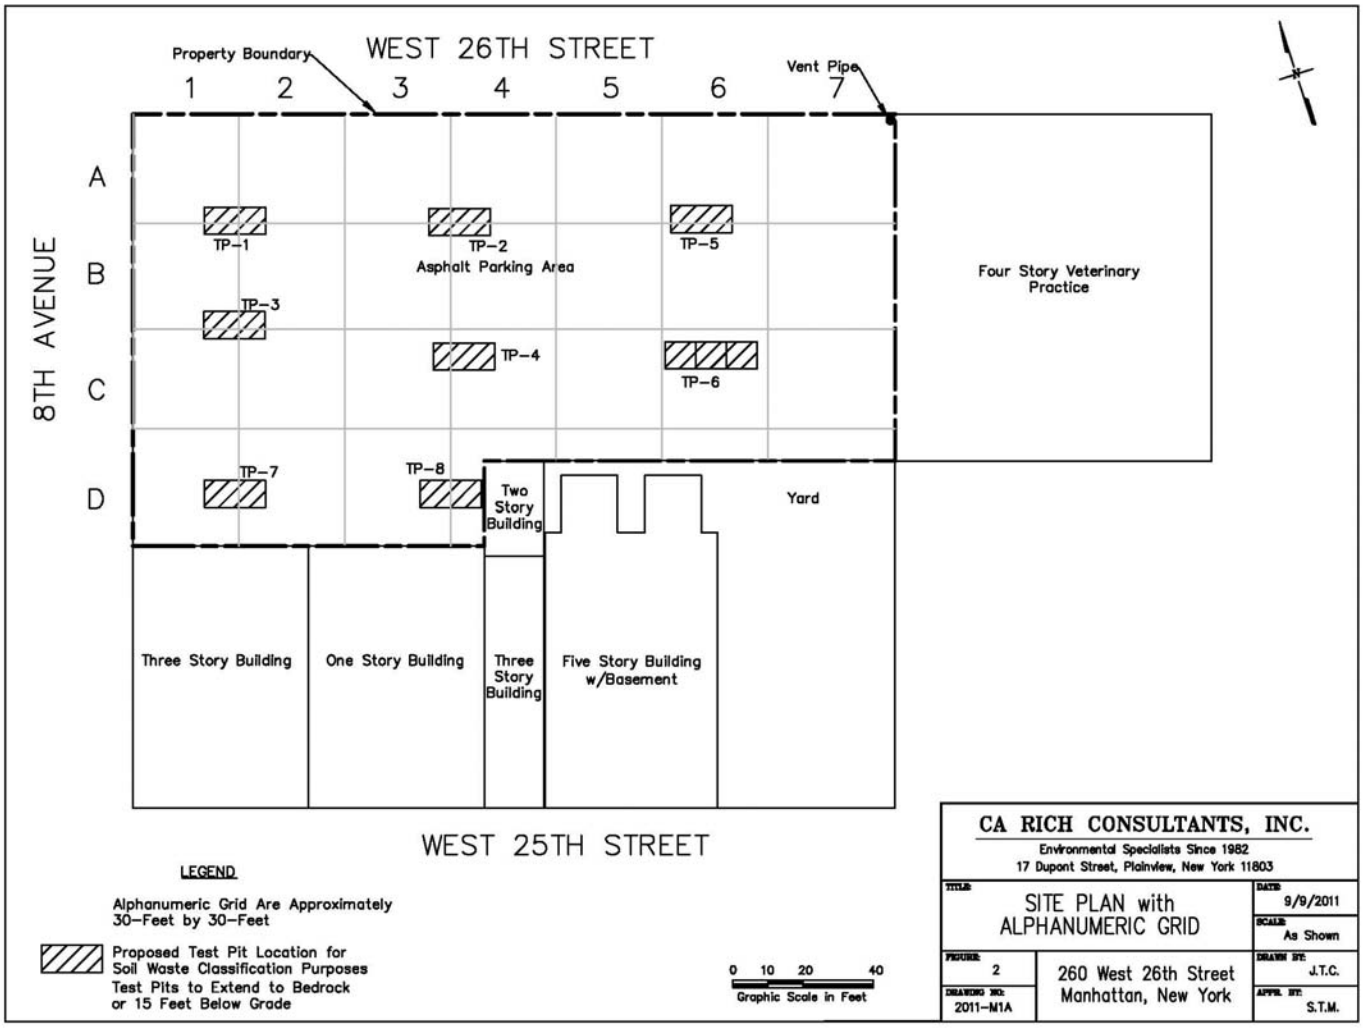

 File Name: _____

Photo Log

Photo 1 – Rock Chopping continued on East side of site.	
Photo 2 – Underpinning work began at neighboring building on the south property line. A structural engineer was on site to oversee all work.	
Photo 3 – Waler was installed in southwest corner of site.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Steve Malinowski of CA RICH

WEATHER	Snow		Rain		Overcast	X	Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	11-15-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Seven truckloads of soil were excavated and removed from grids B3, C4, and D4. The soil was transported to the Soil Safe Facility in Logan Township, New Jersey.

Rock Chopping continued. Lagging continued to be installed along perimeter of site.

Underpinning of the neighboring building at the south property was also conducted.

Working In Grids #: excavation in grids B3, C4 and D4

Air Monitoring (Since Last Report):

Air Monitoring was performed today and no problems were encountered.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Bedrock will continued to be chopped and trucked off site throughout the week. The construction team will install lagging as needed along the perimeter as the excavation proceeds. Underpinning neighboring buildings will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
					7	175						
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	202	Appr. 5,050	18	Appr. 450	24	Appr. 600	149	Appr. 3725

Site Grid Map

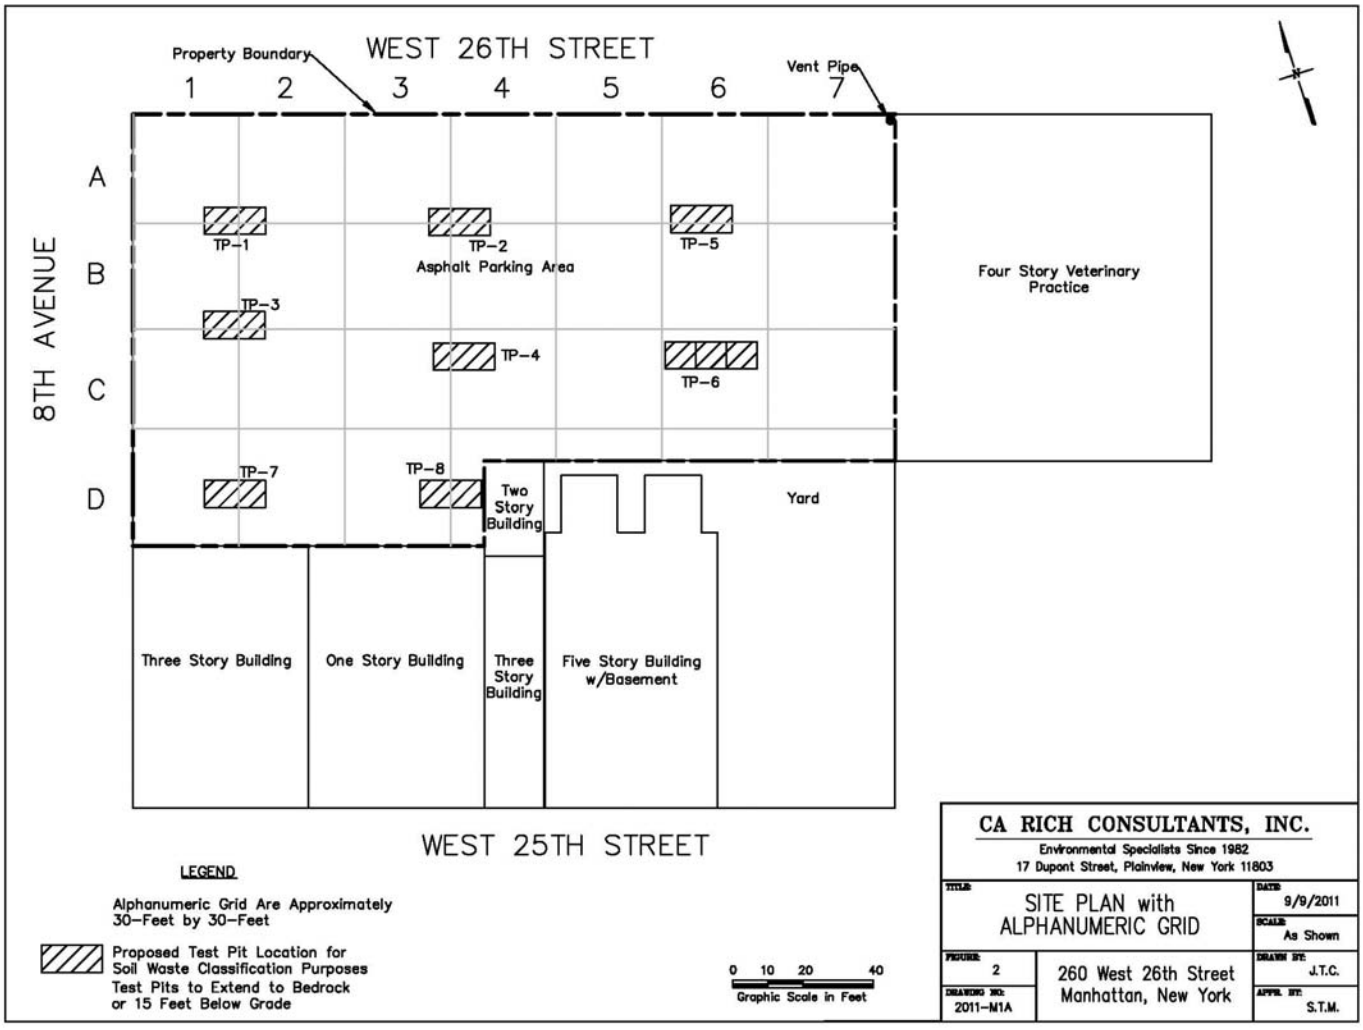

 File Name: _____

Photo Log

Photo 1 – Soil removal from former test pit TP-4 to Soil Safe Facility.	
Photo 2 – Approaching final depth of excavation on top of bedrock along east side of the Site.	
Photo 3 – Looking east across excavation area.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain	X	Overcast		Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	11-16-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Rock Chopping continued.

Lagging continued to be installed along perimeter of site.

Working In Grids #: A5, A6, B5, B6, C5, C6,

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Bedrock will continue to be chopped and trucked off site throughout the week. The construction team will install lagging as needed along the perimeter as the excavation proceeds. Underpinning neighboring buildings will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	202	Appr. 5,050	18	Appr. 450	24	Appr. 600	149	Appr. 3725

Site Grid Map

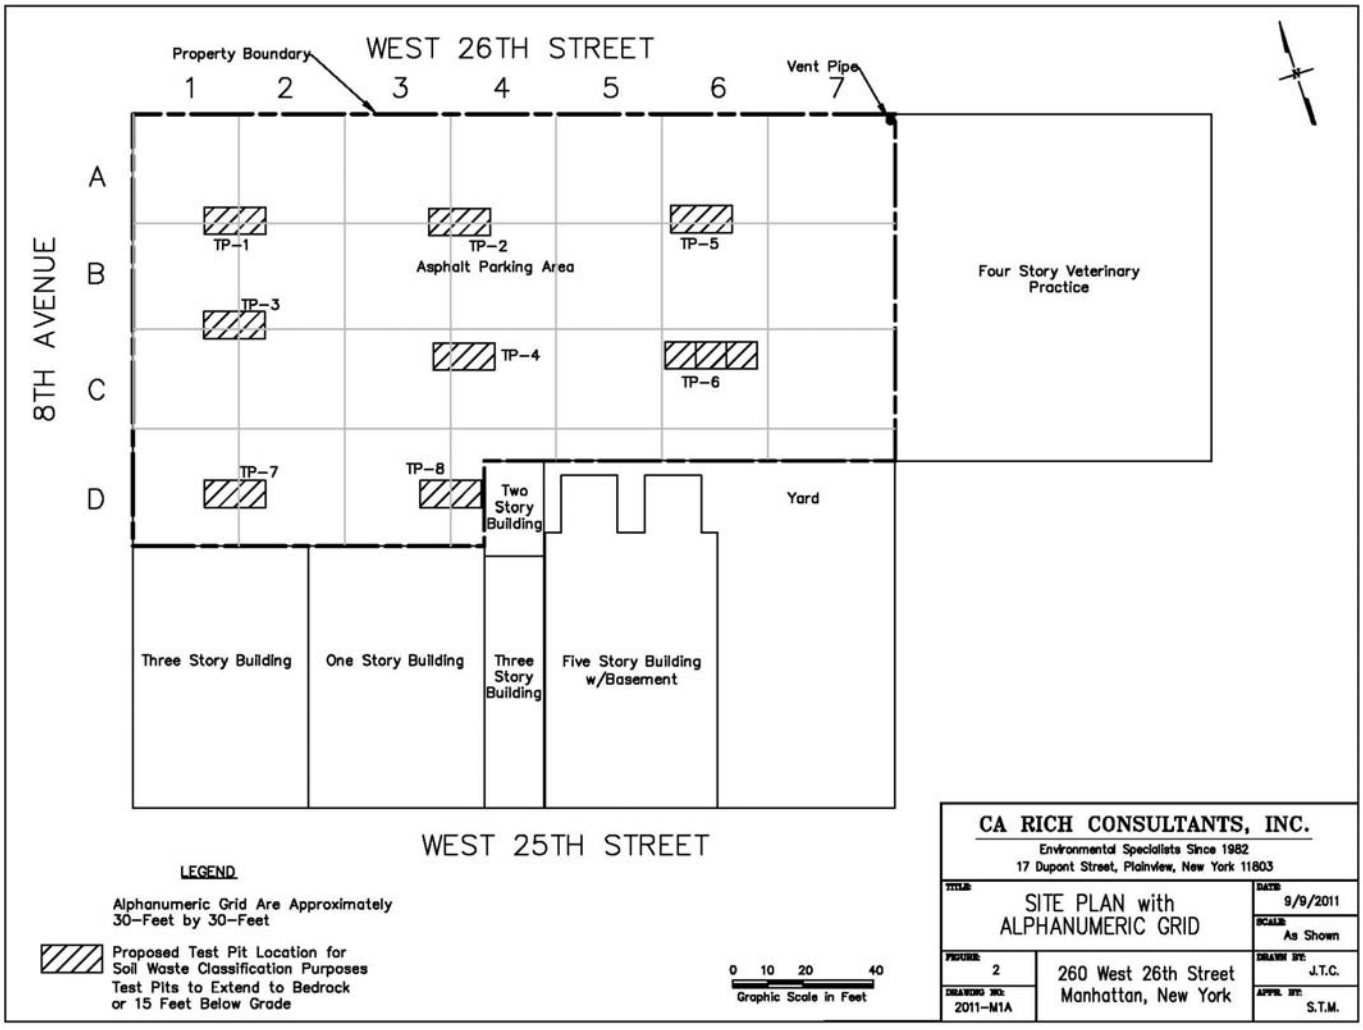

 File Name: _____

Photo Log

Photo 1 – Rock Chopping continued on South property line.	
Photo 2 – Rock chopping continued and bedrock was stockpiled.	
Photo 3 – Guardrail was installed along the west side of the excavation area.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Steve Malinowski of CA RICH

WEATHER	Snow		Rain	X	Overcast		Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	11-17-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Soil excavation and off-site disposal activities were conducted today. A total of six truckloads of soil were transported to the Soil Safe Facility in Logan Township, New Jersey.

Lagging continued to be installed along perimeter of site.

Working In Grids #: A1, B1, C4, and D4

Air Monitoring (Since Last Report):

Air Monitoring for VOCs and dust was performed during today's soil excavation activities.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Bedrock will continue to be chopped and trucked off site throughout the week. The construction team will install lagging as needed along the perimeter as the excavation proceeds. Underpinning neighboring buildings will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
					6	150						
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	208	Appr. 5,200	18	Appr. 450	24	Appr. 600	149	Appr. 3,725

Site Grid Map

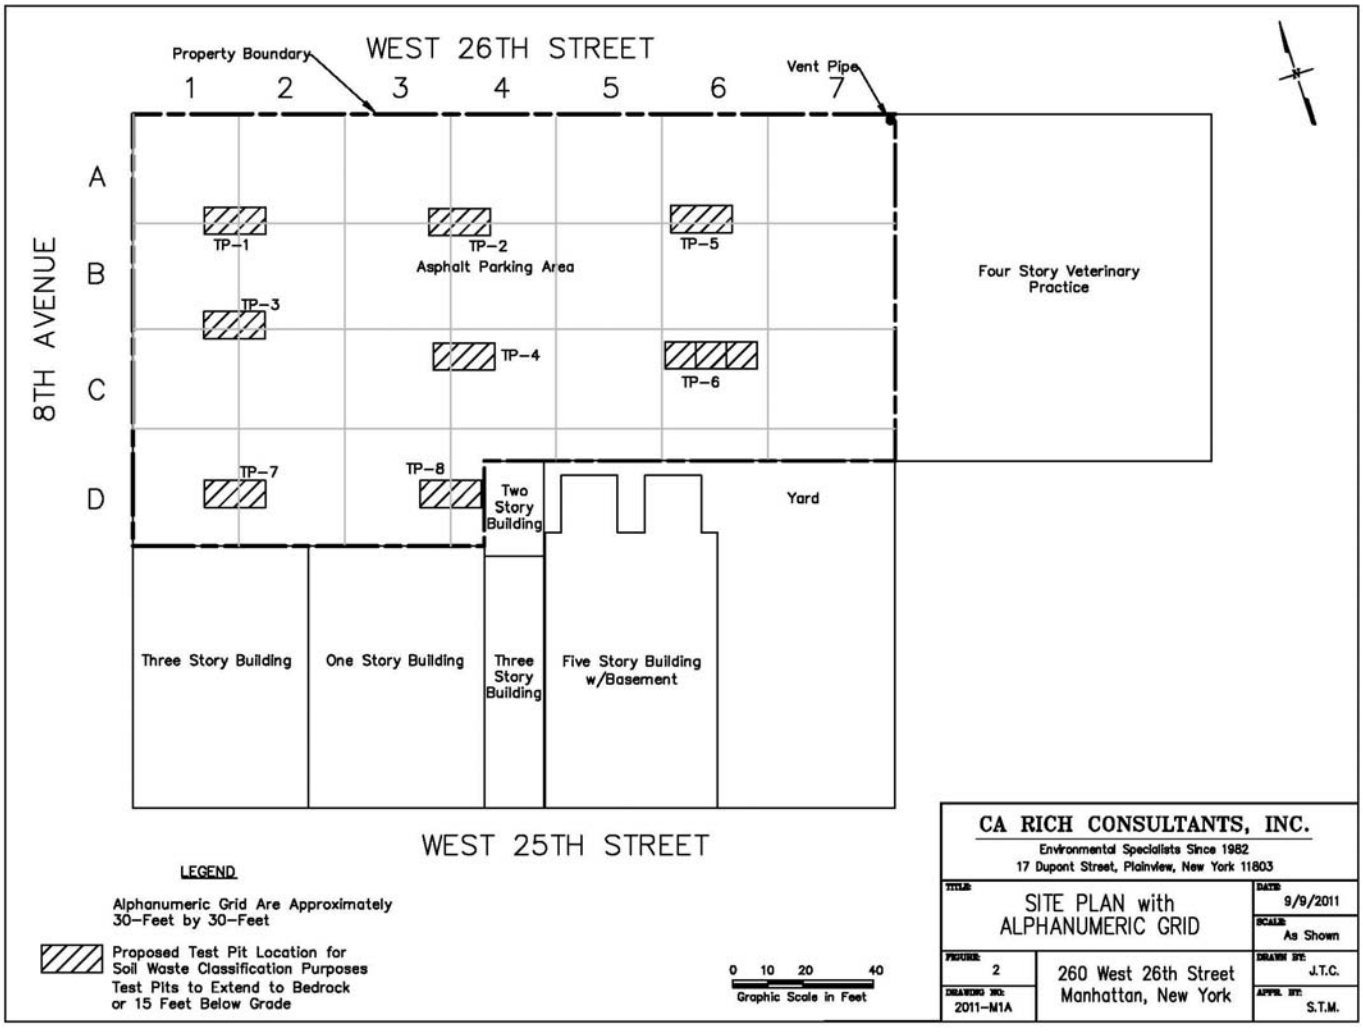

 File Name: _____

Photo Log

Photo 1 – Excavation of soil in grids D3 and D4.	
Photo 2 – Excavation of soil in grids B1 and C1.	
Photo 3 – Looking east across site.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Steve Malinowski of CA RICH

WEATHER	Snow		Rain		Overcast	x	Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50	x	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	11-18-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Site Safety Officer: Steve Malinowski
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Soil excavation and off-site disposal activities were conducted today. A total of six truckloads of soil were transported to the Soil Safe Facility in Logan Township, New Jersey.

Lagging continued to be installed along perimeter of site.

Working In Grids: Excavation in grids B1, B2 & C2; underpinning and rock chipping grids C4, D4 & D3

Air Monitoring (Since Last Report):

Air Monitoring for VOCs and dust was performed during today's soil excavation activities.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Bedrock will continue to be chopped and trucked off site throughout the week. The construction team will install lagging as needed along the perimeter as the excavation proceeds. Underpinning neighboring buildings will continue throughout the week. Excavation in select areas will continue on an as-needed basis.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
					6	150					10	250
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	214	Appr. 5,350	18	Appr. 450	24	Appr. 600	159	Appr. 3,975

Site Grid Map

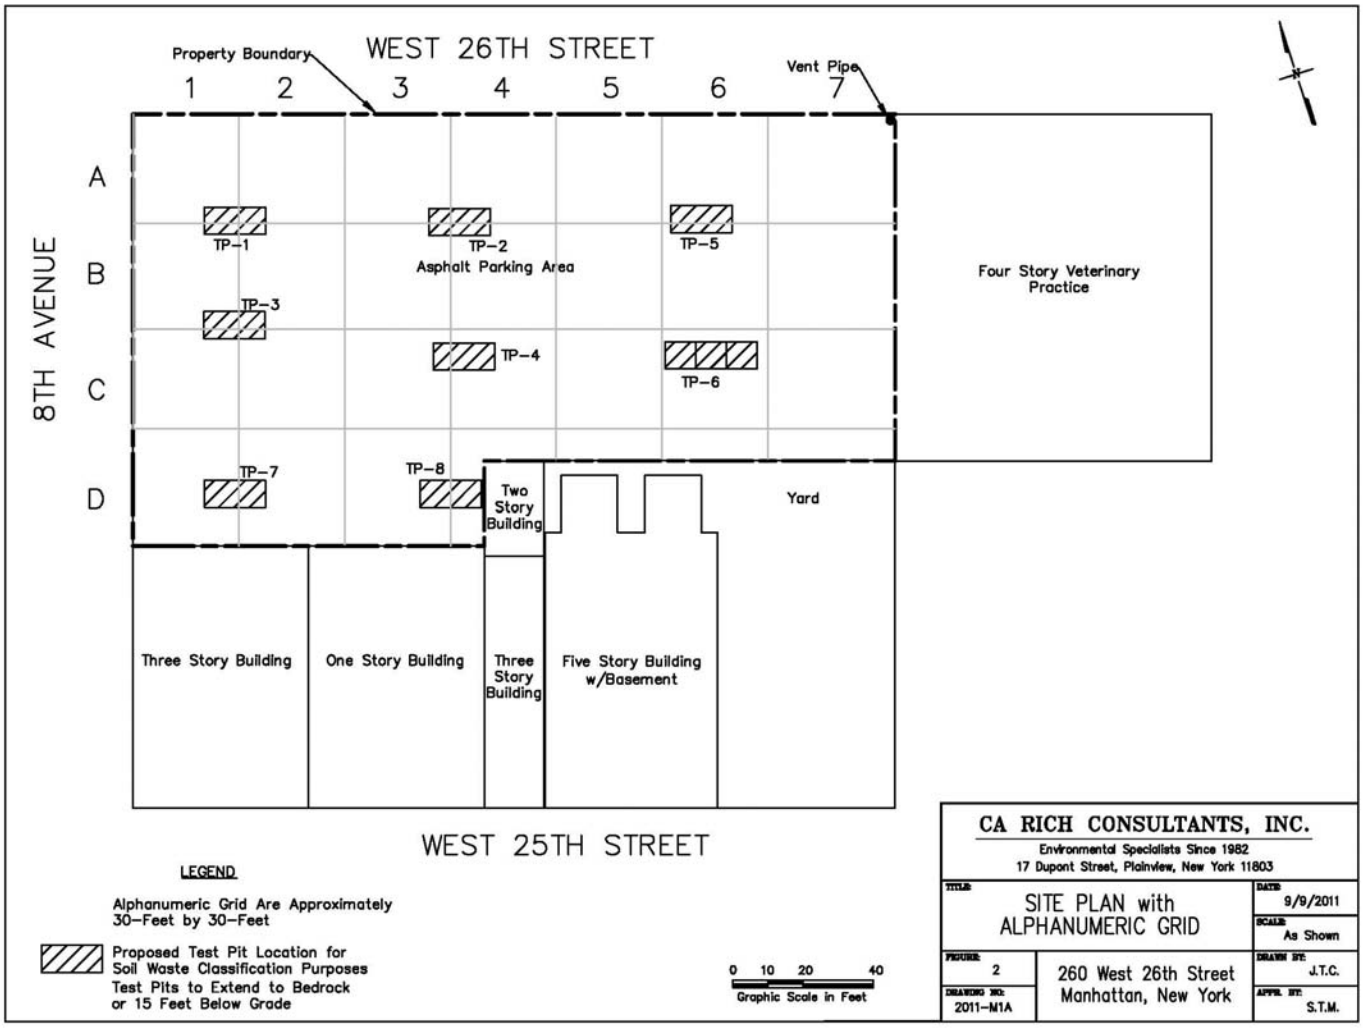

 File Name: _____

Photo Log

Photo 1 – Installation of additional gravel for truck wash pad.	
Photo 2 – Excavation of soil in grid B1.	
Photo 3 – Looking west towards site entrance.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Jessica Proscia of CA RICH

WEATHER	Snow		Rain	X	Overcast		Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	11-21-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc. Contractor: Chelsea W26 LLC	Safety Officer: Jessica Proscia Alternate Site Safety Officer: Steve Malinowski

Work Activities Performed (Since Last Report):

Soil excavation and off-site disposal activities were conducted today. A total of six truckloads of soil were transported to the Soil Safe Facility in Logan Township, New Jersey.

Lagging continued to be installed along perimeter of site.

Working In Grids: Excavation in grids B2, B4 & D4

Air Monitoring (Since Last Report):

Air Monitoring for VOCs was performed during today's soil excavation activities.
Air Monitoring for dust was not performed due to the rain.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Underpinning neighboring buildings will continue throughout the week. Excavation in select areas will continue on an as-needed basis.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
					6	150					10	250
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	220	Appr. 5,500	18	Appr. 450	24	Appr. 600	159	Appr. 3,975

Site Grid Map

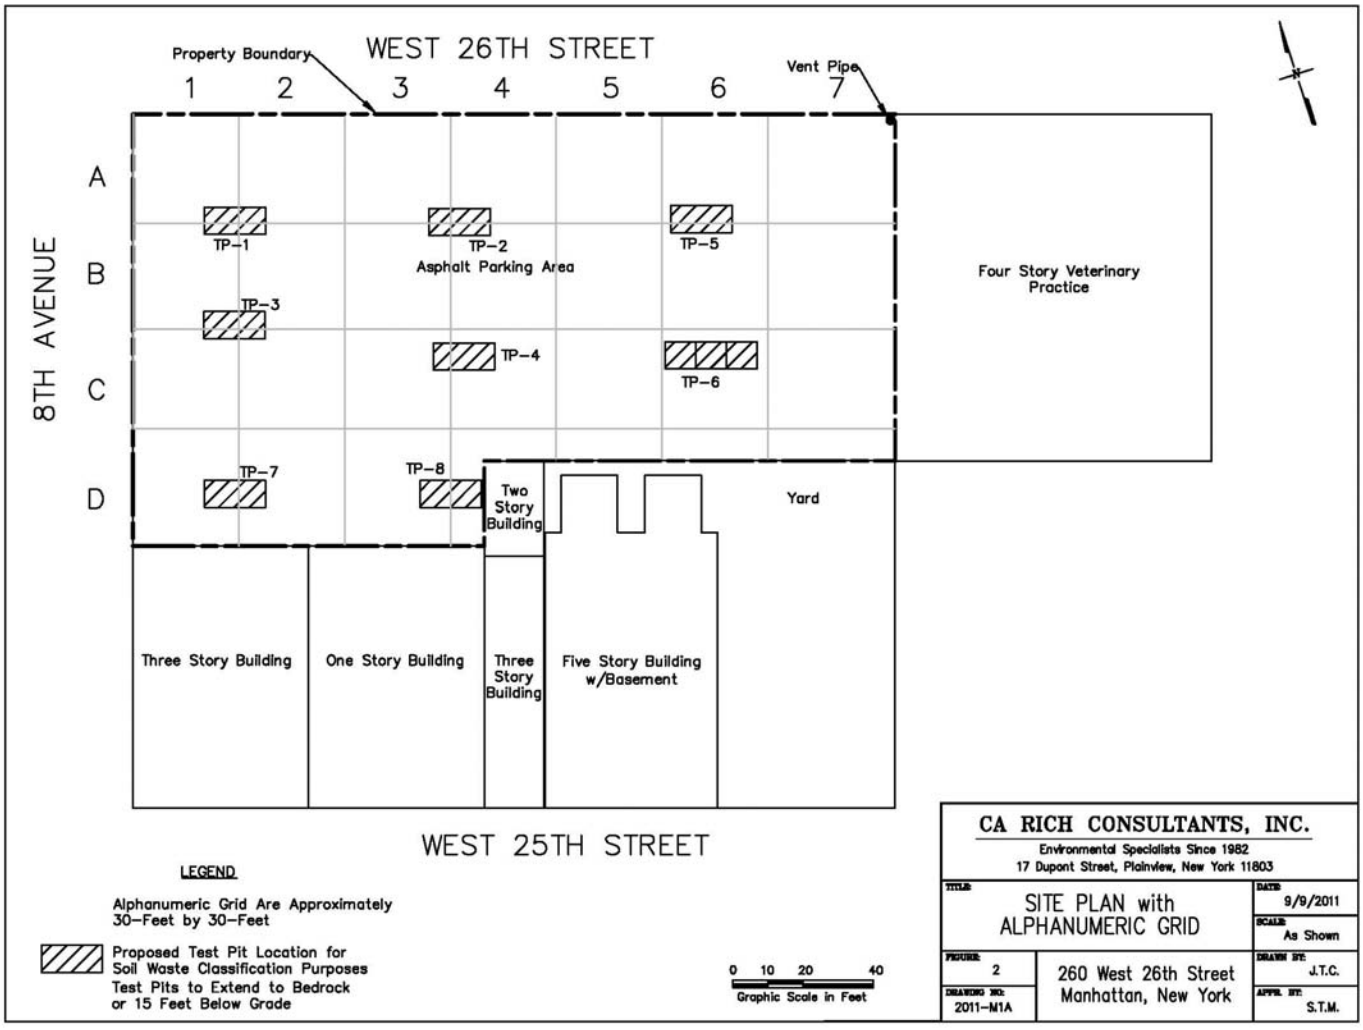

 File Name: _____

Photo Log

Photo 1 – Excavation of soil in grid B4.	
Photo 2 – Excavation of soil in grid D4.	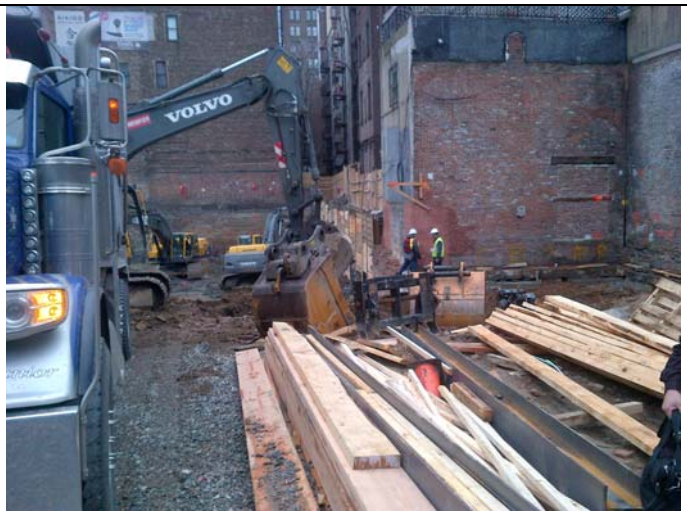
Photo 3 – Looking west towards site entrance.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain	X	Overcast		Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	11-22-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Concrete footing in the northeast corner of the site was formed and poured.

Rock Chopping and lagging continued along the perimeter of the site. Bedrock was stockpiled on site.

Rakers and Walers were installed along 8th Ave. Steel "WT" sections were welded to the HP piles.

Working In Grids #: A2, A3, A4, C5, C6,

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Bedrock will continue to be chopped and trucked off site throughout the week. The construction team will install lagging as needed along the perimeter as the excavation proceeds. Underpinning neighboring buildings will continue throughout the week. Excavation in select areas will continue on an as-needed basis.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	214	Appr. 5,350	18	Appr. 450	24	Appr. 600	159	Appr. 3975

Site Grid Map

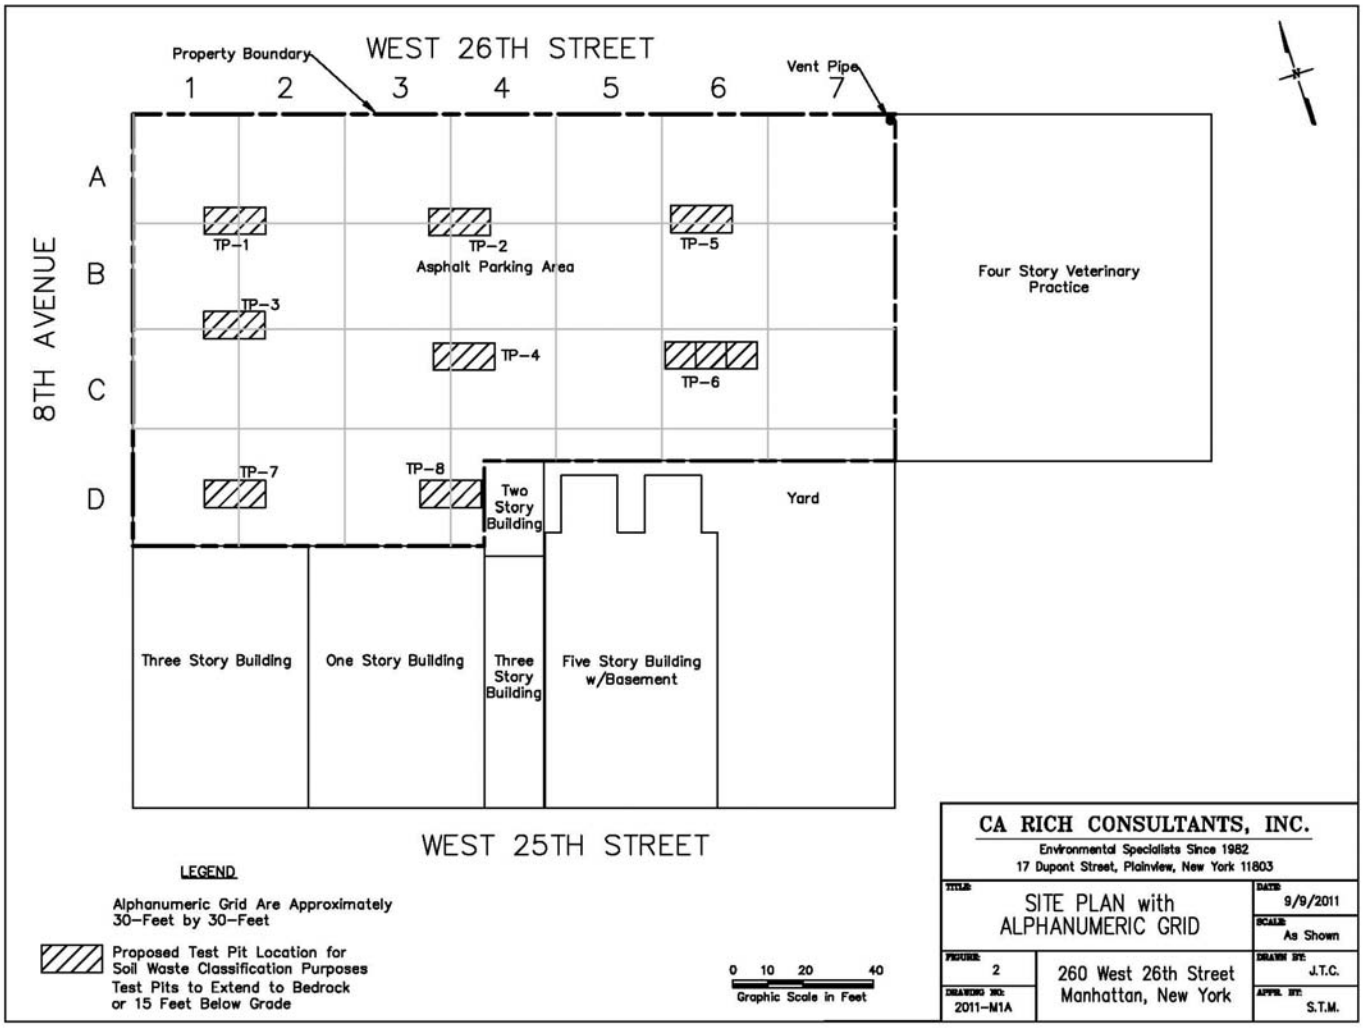

 File Name: _____

Photo Log

Photo 1 – Rock Chopping continued on South property line and additional lagging was installed.	
Photo 2 – Welding “WT” Steel sections to Soldier Beams.	
Photo 3 – Additional lagging installed along the North Property line.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain	X	Overcast		Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	11-23-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Footing Formwork continued to be built, and rebar and waterproofing for wall section along 26th Street was installed.

Rock Chopping and lagging continued along the perimeter of the site. Bedrock was stockpiled on site.

Steel "WT" sections were welded to the HP piles along 8th Ave.

Working In Grids #: A1, A2, A3, A4, A5, A6, A7

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Bedrock will continue to be chopped and trucked off site throughout the week. The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings will continue to be installed throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	214	Appr. 5,350	18	Appr. 450	24	Appr. 600	159	Appr. 3975

Site Grid Map

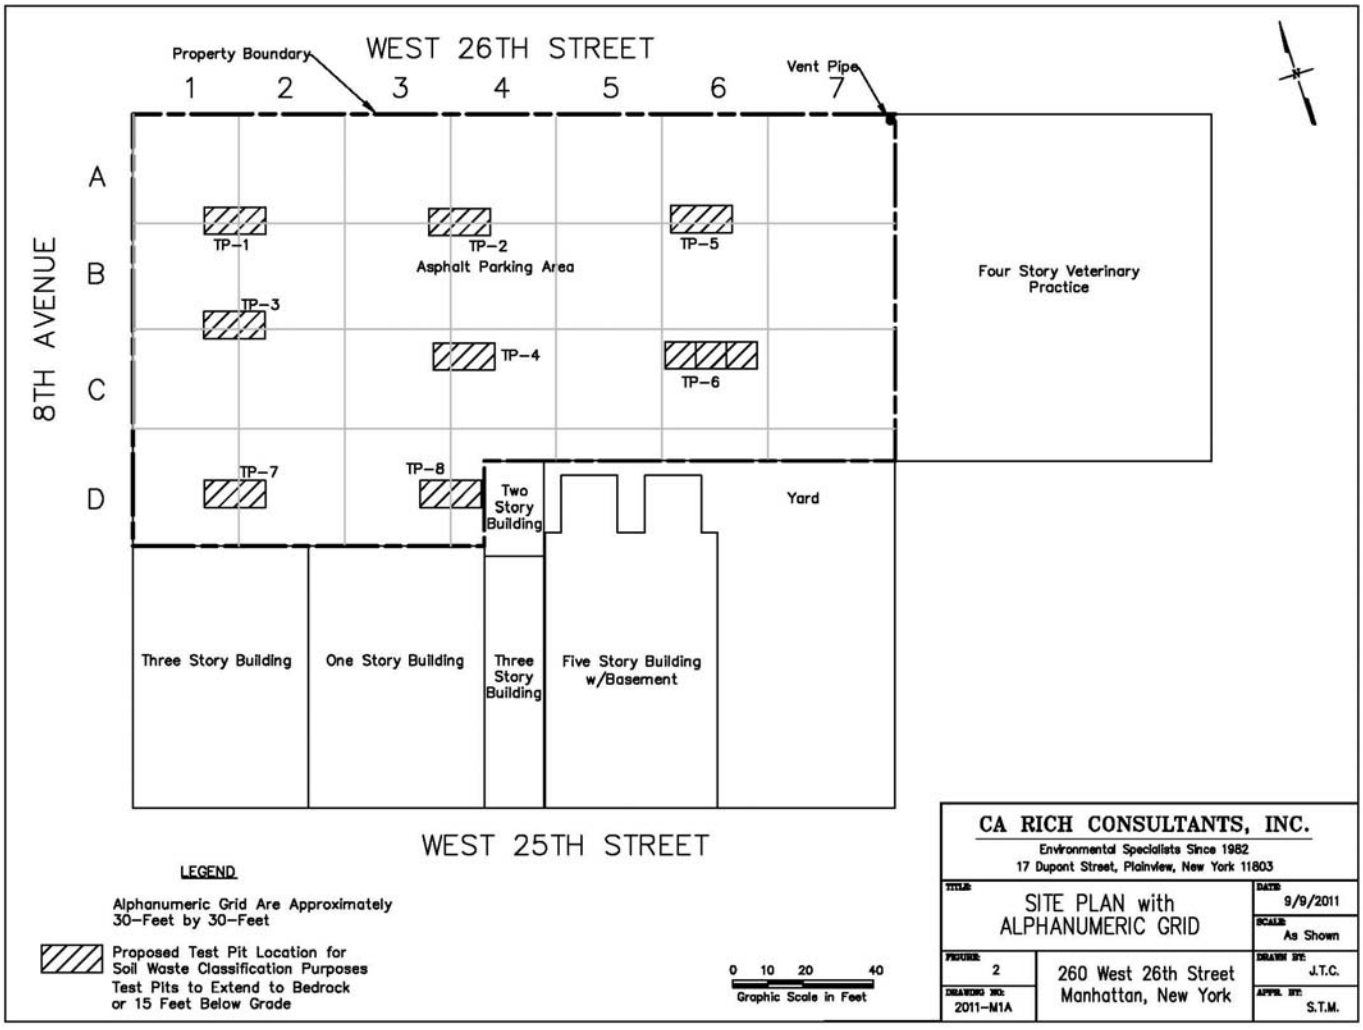

 File Name: _____

Photo Log

Photo 1 – Waterproofing was installed along 26th Street.	
Photo 2 – Stockpile of Rebar ready to be installed at foundation wall along 26th Street.	
Photo 3 – Rock Chopping continued as needed.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	11-25-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Footing Formwork was built at South Property Line and a mud slab was poured so waterproofing could be installed.

The last section of underpinning was poured along the south property line.

The DEP Dewatering Permit was obtained on Wednesday, November 23rd. Dewatering occurred intermittingly throughout the day as needed. Water was pumped off site through a 10 micron bag filtration system and into the existing city catch basin.

Working In Grids #: D2, D3, D5, D6, D7

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Bedrock will continue to be chopped and trucked off site throughout the week. The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings will continue to be installed throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	214	Appr. 5,350	18	Appr. 450	24	Appr. 600	159	Appr. 3975

Site Grid Map

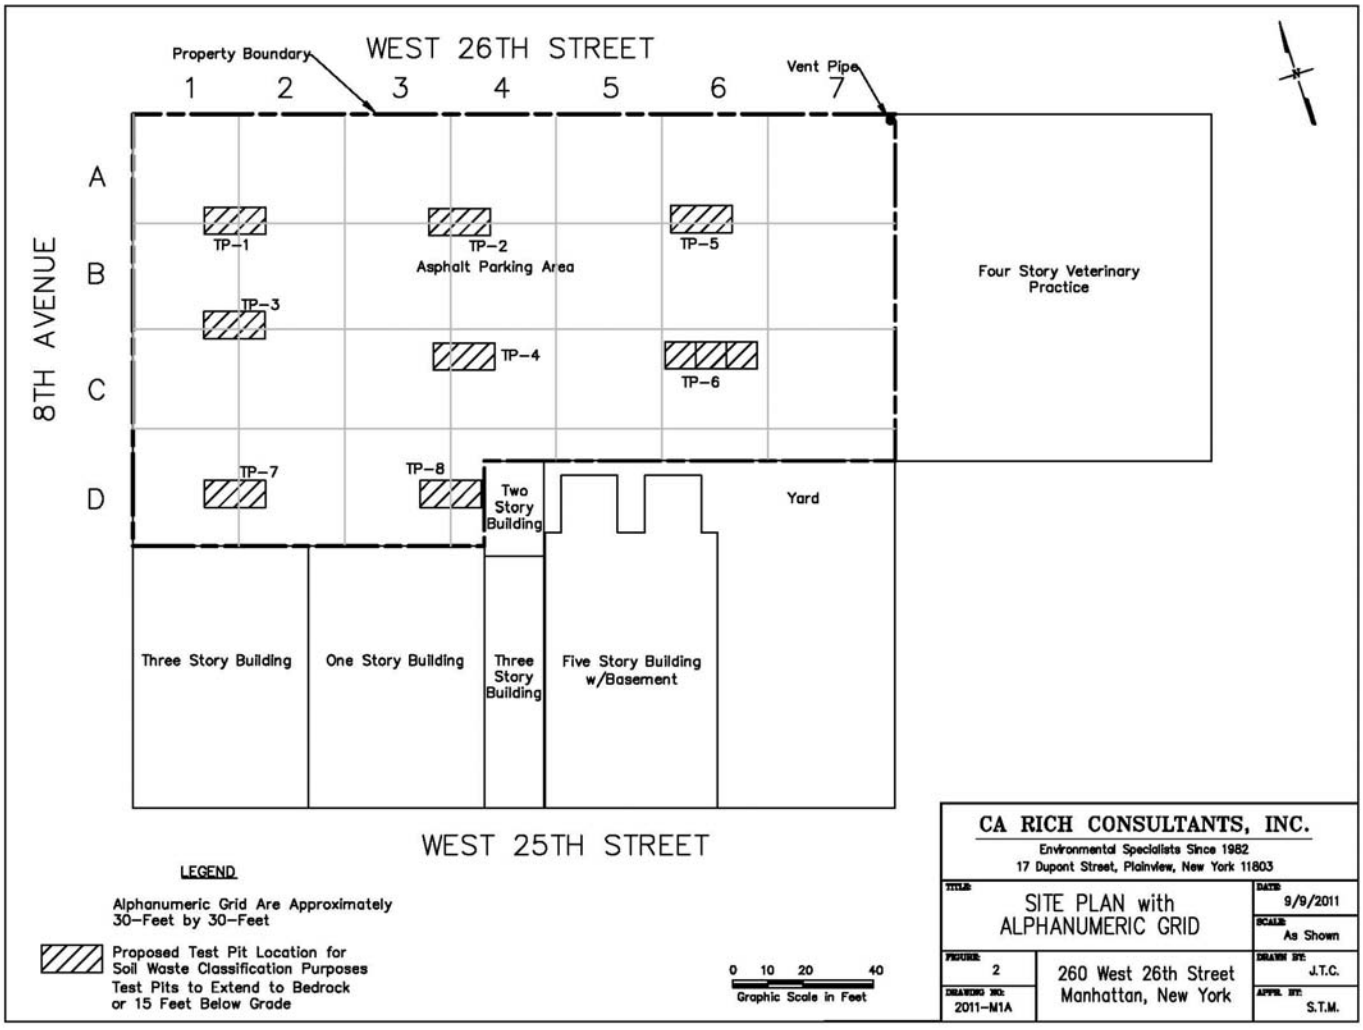

 File Name: _____

Photo Log

Photo 1 – Footing Formwork along the South Property line. A mud slab is currently being poured so waterproofing can begin to be installed.	
Photo 2 – The last section of underpinning was poured today along the south property line.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	11-26-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Rebar was installed for the Foundation Wall along the North Property line.

Lagging was installed along the North Property Line

Waterproofing was installed along the South Property Line on the mud slab.

Working In Grids #: A3, A5, A6, A7, D5, D6, D7

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Bedrock will continue to be chopped and trucked off site throughout the week. The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings will continue to be installed throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	214	Appr. 5,350	18	Appr. 450	24	Appr. 600	159	Appr. 3975

Site Grid Map

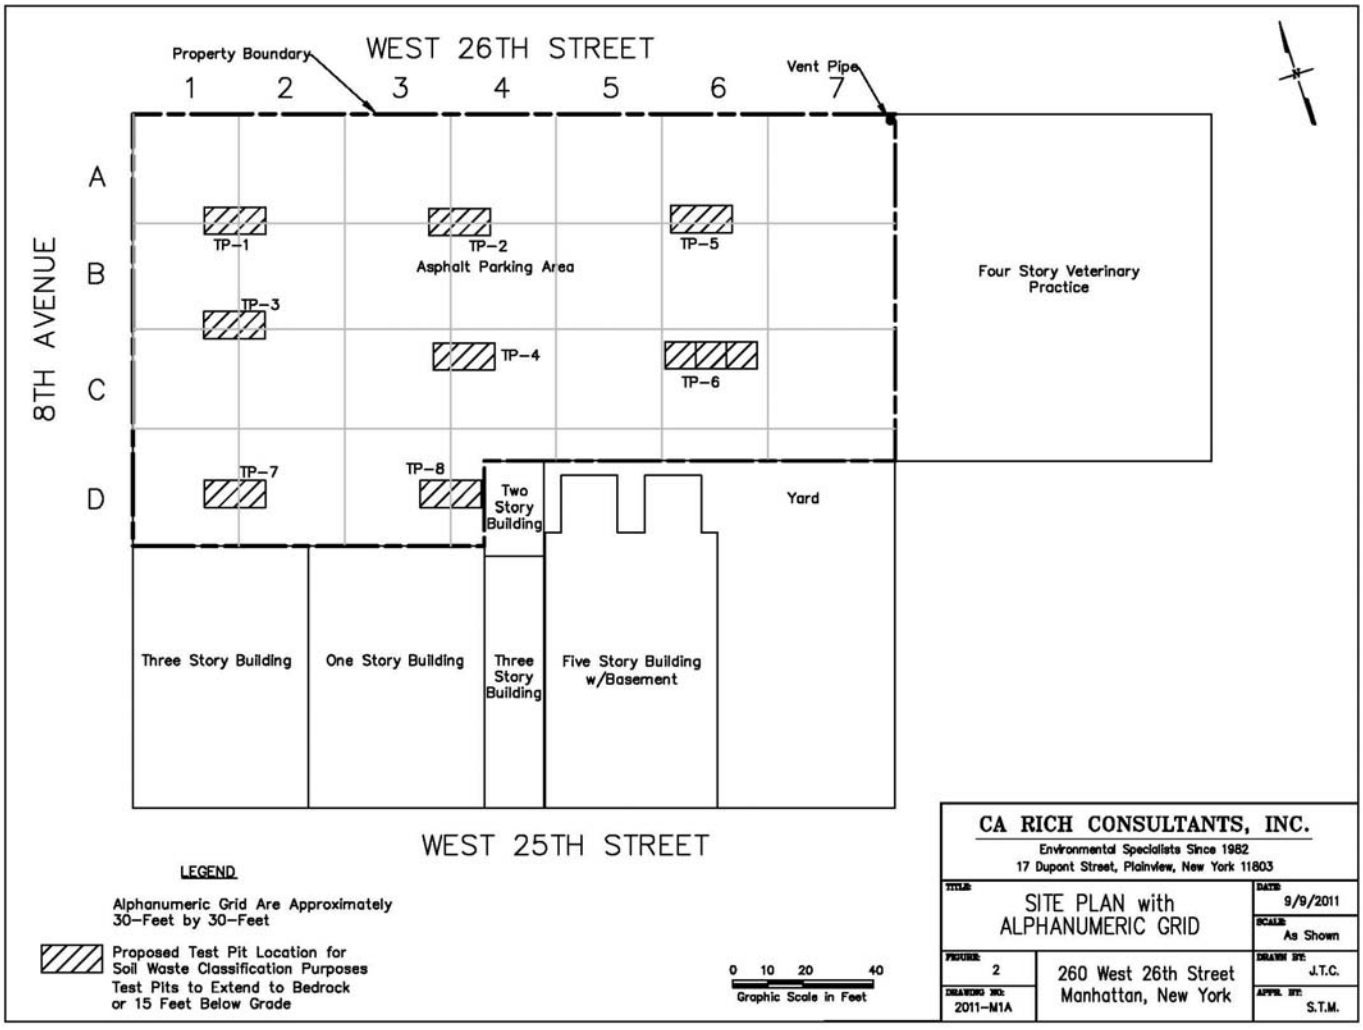

 File Name: _____

Photo Log

Photo 1 – Workers installing Foundation wall rebar on North wall.	
Photo 2 – Working on Lagging along North Wall.	
Photo 3: Workers installing waterproofing along South Property Line.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	11-28-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Rock Chopping continued on Northeast half of site.

Formwork for footings was installed along the East Property line of the site.

Waterproofing was installed along the South Property Line on the mud slab.

Working In Grids #: A3, A5, A6, A7, D5, D6, D7

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Bedrock will continue to be chopped and trucked off site throughout the week. The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings will continue to be installed throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	214	Appr. 5,350	18	Appr. 450	24	Appr. 600	159	Appr. 3975

Site Grid Map

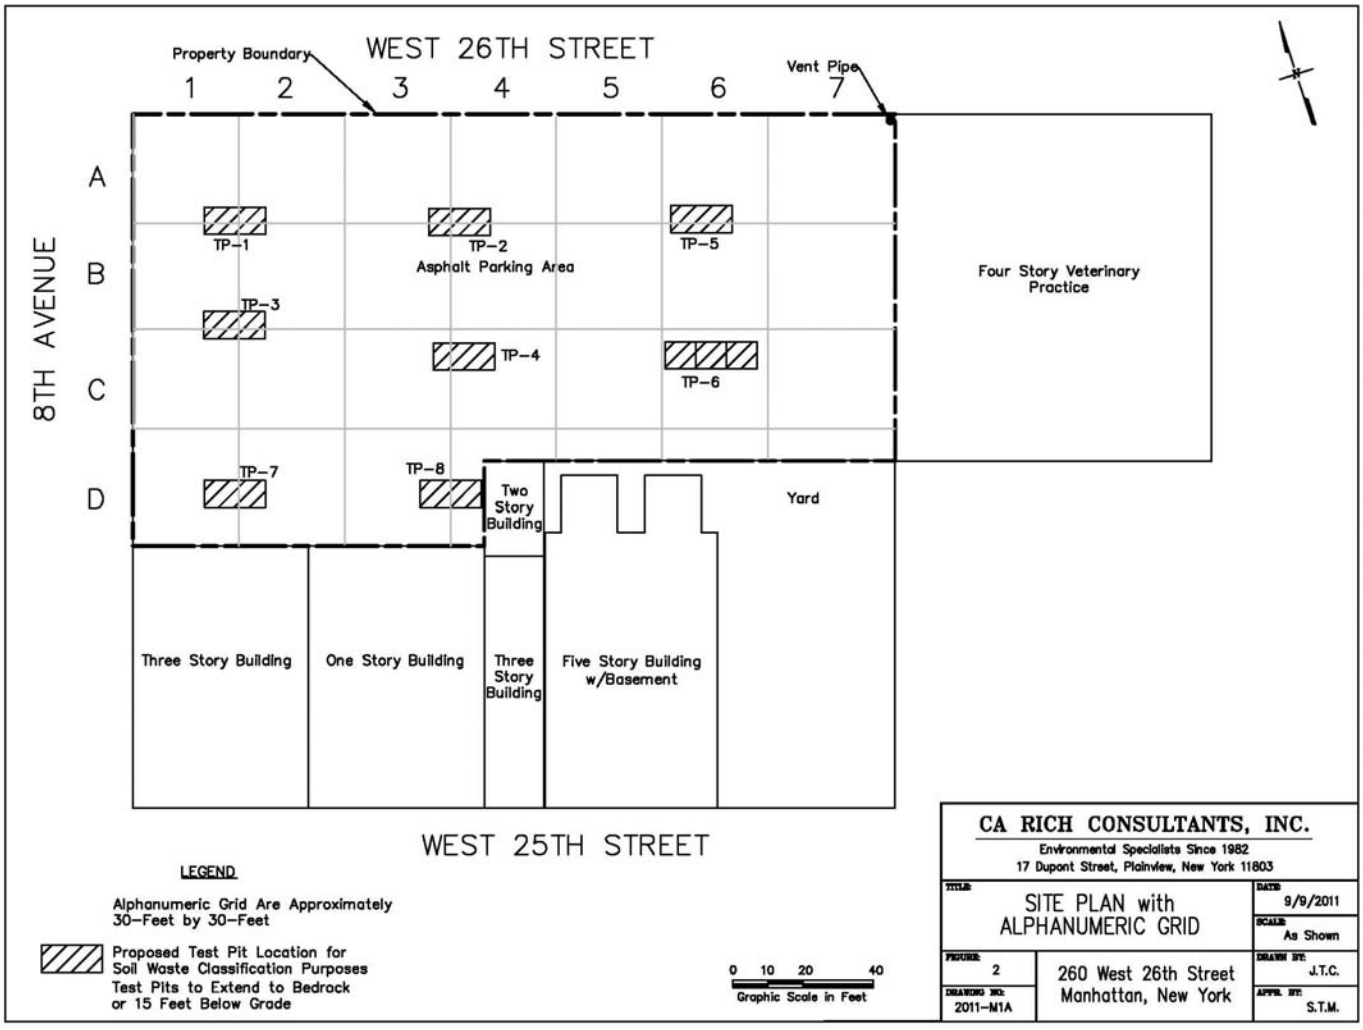

 File Name: _____

Photo Log

Photo 1 – Rock Chopping in East half of Site.	
Photo 2 – Workers welding WT-section stiffeners to the HP Piles along 8th Ave and 26th Street.	
Photo 3: Workers continuing to install waterproofing along South Property Line.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain	X	Overcast		Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	11-29-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Rock Chopping continued on Northeast half of site.

Mud Slab was poured along the East Foundation Wall and rebar began to be installed for the footing.

Formwork for the North Foundation wall was erected on site.

Working In Grids #: A5, A6, A7, B5, C7, D7

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Bedrock will continue to be chopped and trucked off site throughout the week. The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings will continue to be installed throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	214	Appr. 5,350	18	Appr. 450	24	Appr. 600	159	Appr. 3975

Site Grid Map

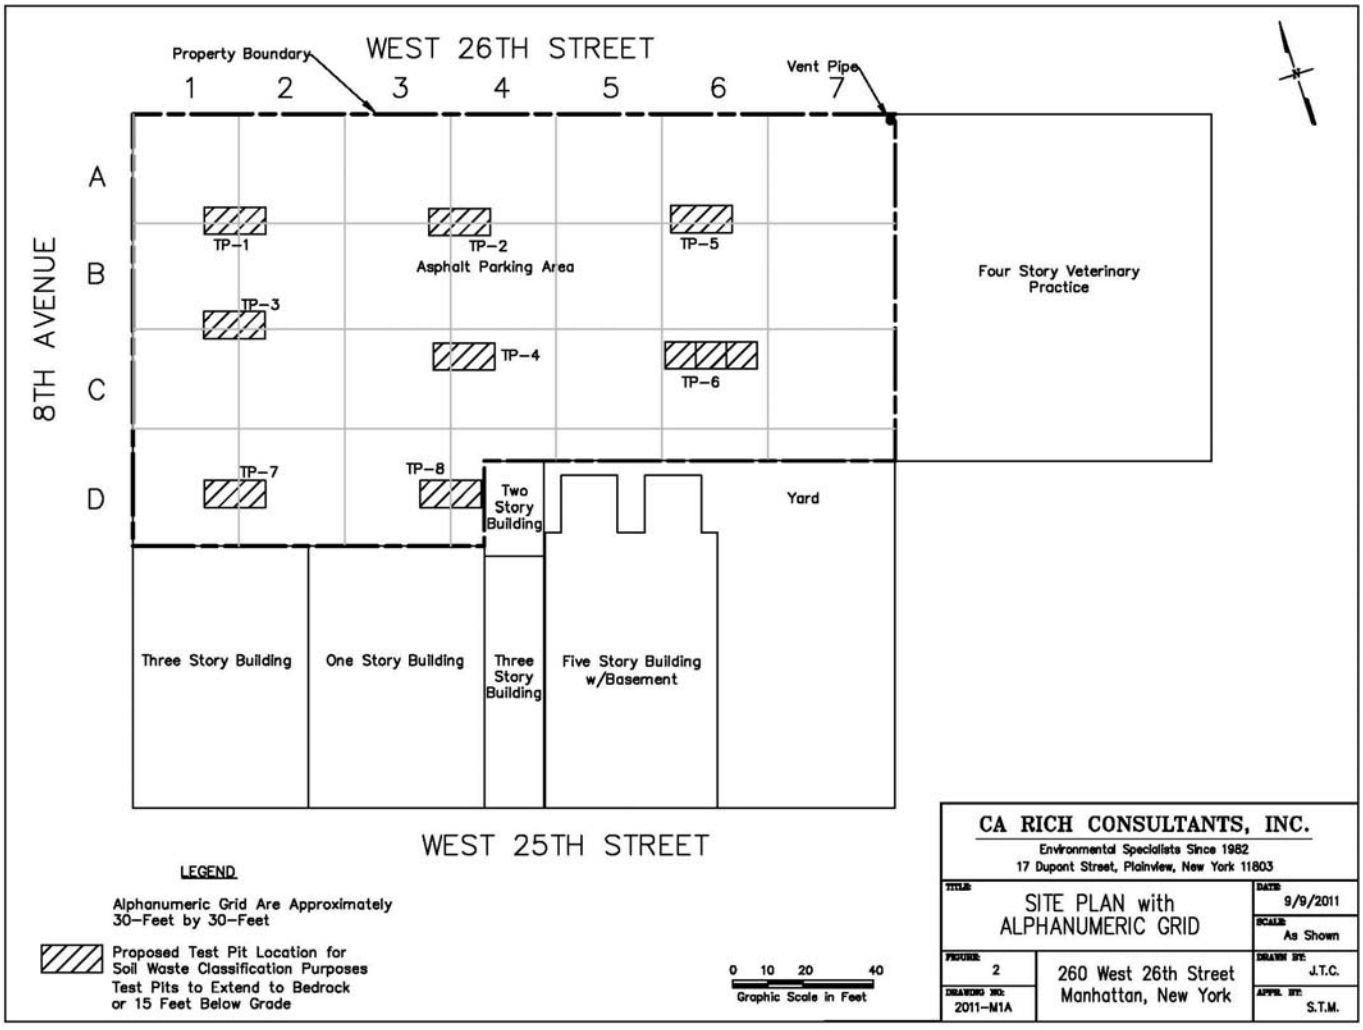

 File Name: _____

Photo Log

Photo 1 – Rain water being pumped off site through a 10 micron bag filtration system.	
Photo 2 – Workers building the foundation footings along the East property line.	
Photo 3: Formwork for the North Foundation wall was erected.	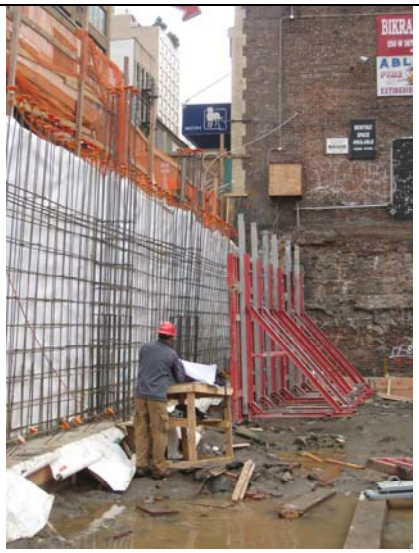

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	11-30-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Rock Chopping continued on Northeast half of site.

Mud Slab was poured along the East Foundation Wall and rebar began to be installed for the footing.

Formwork for the North Foundation wall was erected on site.

Working In Grids #: A5, A6, A7, B7, C7, D7

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Bedrock will continue to be chopped and trucked off site throughout the week. The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings and foundation walls will continue to be installed throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
											5	Appr. 125
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	214	Appr. 5,350	18	Appr. 450	24	Appr. 600	164	Appr. 4100

Site Grid Map

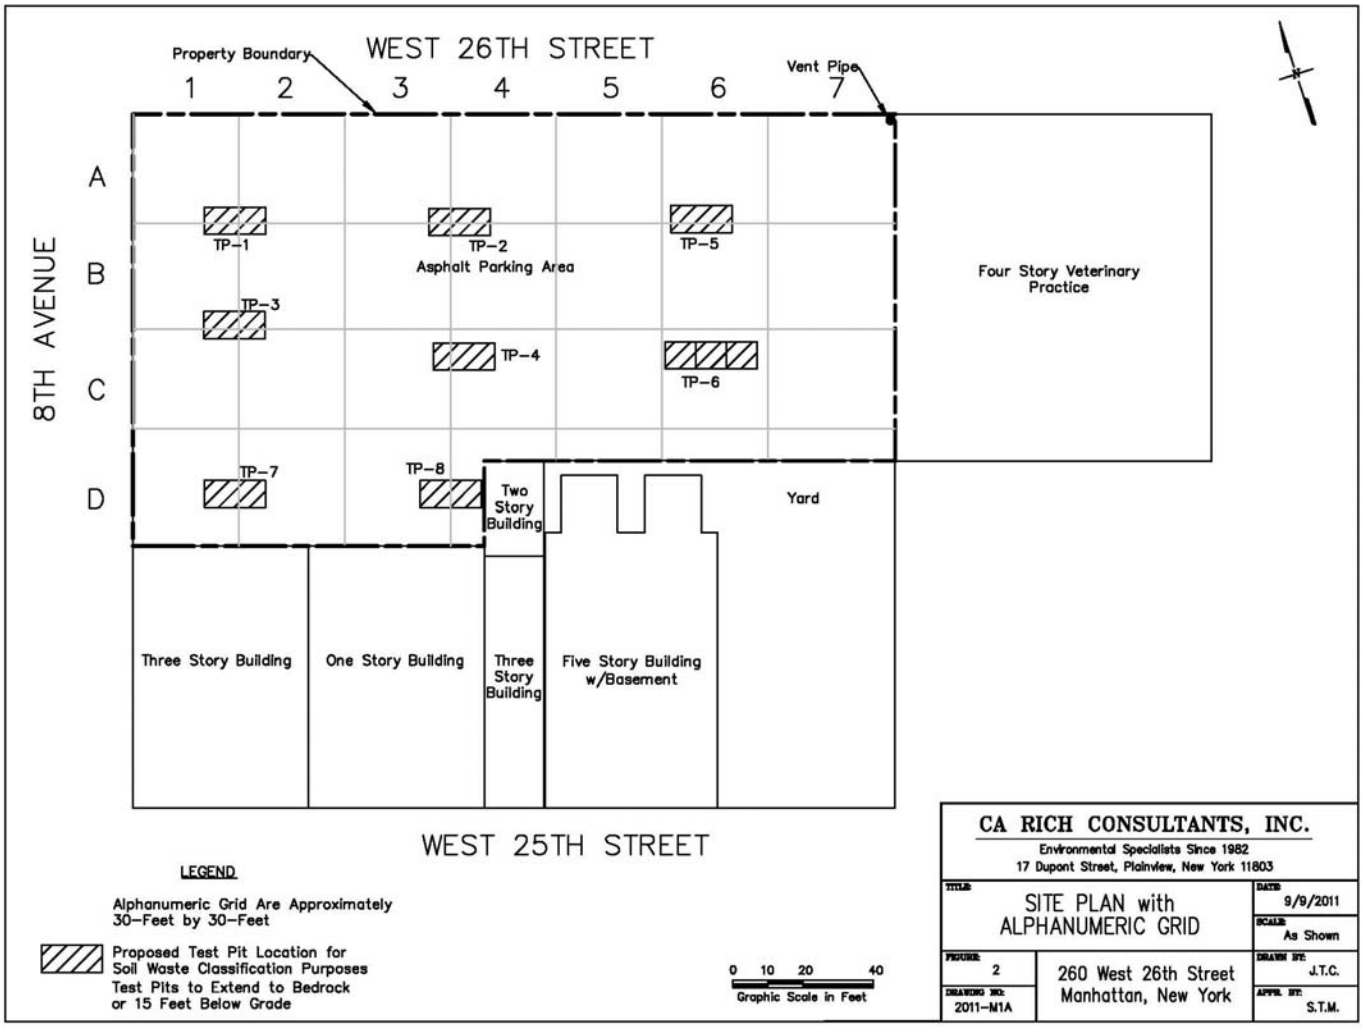

 File Name: _____

Photo Log

Photo 1 – Foundation Wall Formwork System being set up along the North wall.	
Photo 2 – Formwork and Waterproofing being installed on the South wall.	
Photo 3: The stockpile of Bedrock was trucked to a recycling facility.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	12-01-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Rebar for Footing on the South Property line was installed.

Waterproofing was installed along the East wall.

Final Formwork was set in place along the North Foundation Wall. This wall will be poured tomorrow afternoon.

Working In Grids #: A5, A6, A7, B7, C7, D7

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Bedrock will continue to be chopped and trucked off site throughout the week. The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings and foundation walls will continue to be installed throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	214	Appr. 5,350	18	Appr. 450	24	Appr. 600	164	Appr. 4100

Site Grid Map

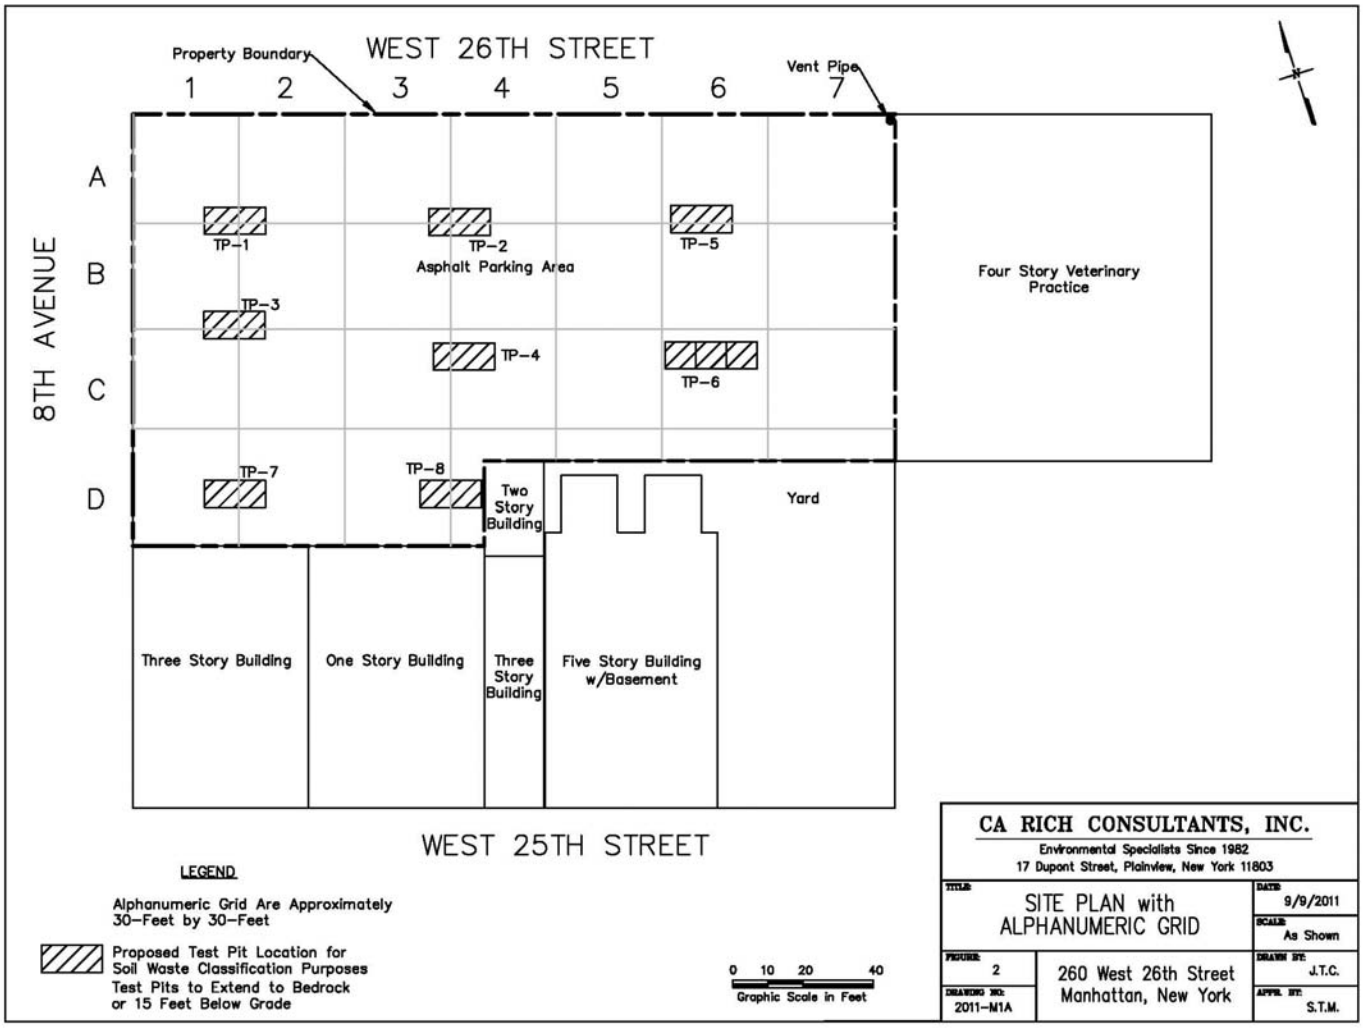

 File Name: _____

Photo Log

Photo 1 – Foundation Wall Formwork System completed along North Wall. Ready for Pour tomorrow.	
Photo 2 – Waterproofing installed at footing along South Wall.	
Photo 3: Footing rebar beginning to be installed along South wall.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	12-02-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc. Contractor: Chelsea W26 LLC	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Work Activities Performed (Since Last Report): Poured North Foundation Wall and South Wall Footing.	
Working In Grids #: A5, A6, A7, D5, D6, D7, C7	
Air Monitoring (Since Last Report): Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.	
Problems Encountered: No problems to report.	
Planned Activities for Next Week: Bedrock will continue to be chopped and trucked off site throughout the week. The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings and foundation walls will continue to be installed throughout the week.	

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	214	Appr. 5,350	18	Appr. 450	24	Appr. 600	164	Appr. 4100

Site Grid Map

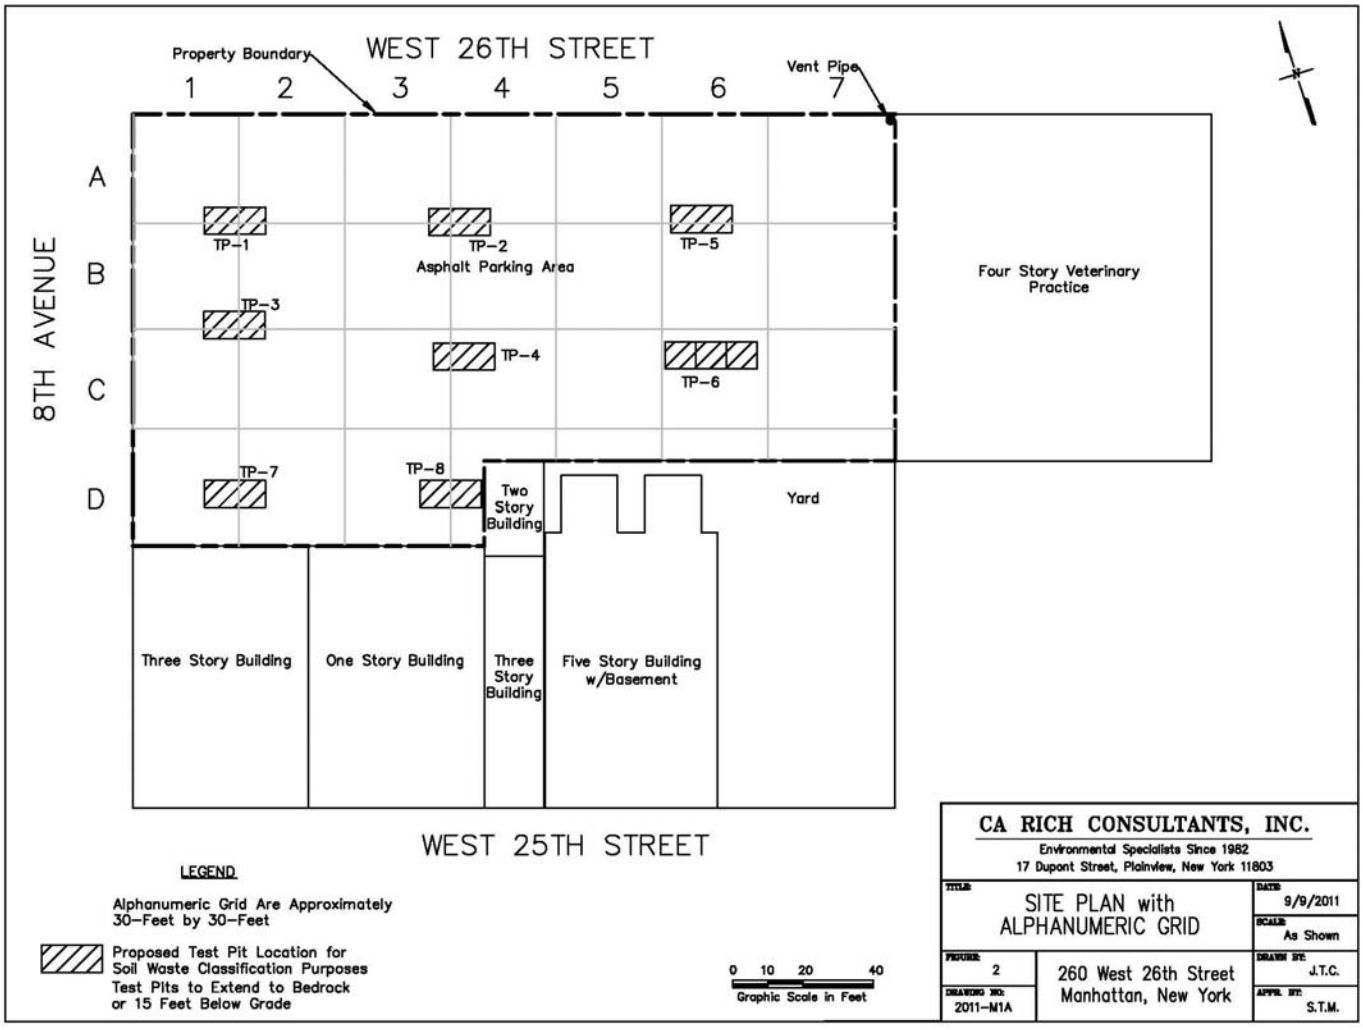

 File Name: _____

Photo Log

Photo 1 – Pouring North Foundation Wall on East Half of Site.	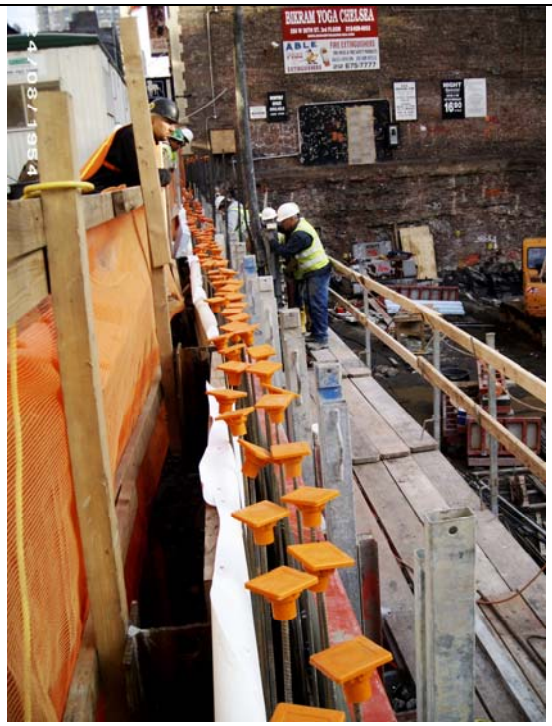
Photo 2 – Pouring Footing on the South Property Line.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	12-03-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Installed Rebar for South Foundation Wall.

8 Trucks of Bedrock were taken to Red Roc Facility.

Working In Grids #: A5, A6, A7, D5, D6, D7, C7

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings and foundation walls will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
											8	Appr. 200
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	214	Appr. 5,350	18	Appr. 450	24	Appr. 600	172	Appr. 4300

Site Grid Map

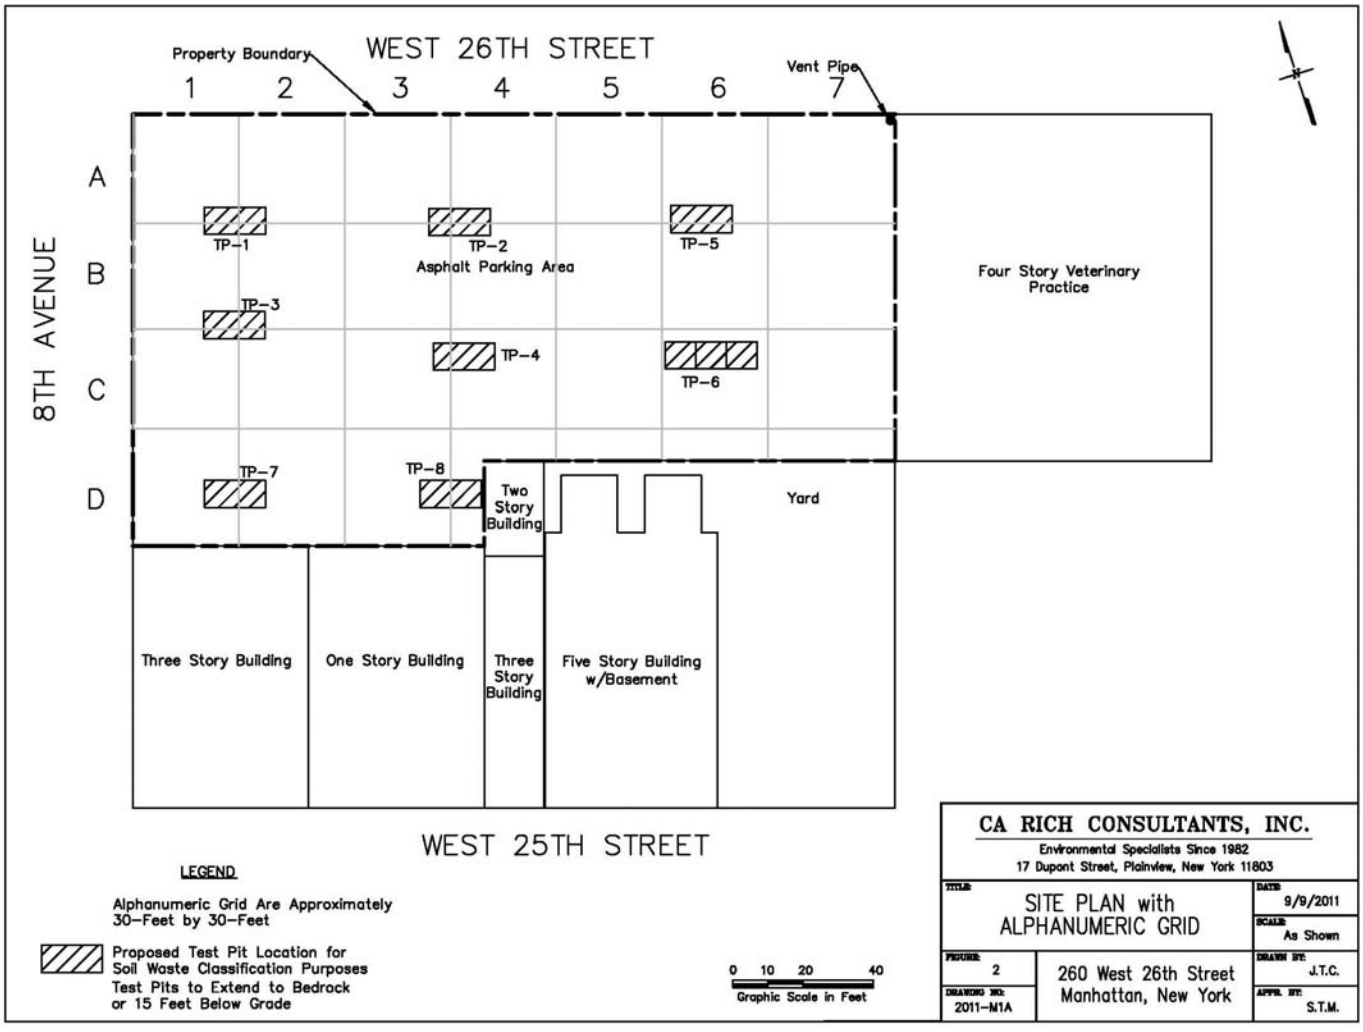

 File Name: _____

Photo Log

Photo 1 – Continued installing Rebar for East and South Foundation Wall.	
Photo 2 – Continued installing rebar for footings along the East property line.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	12-05-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Installed the remaining rebar along the South Foundation Wall.

Stripped the formwork from the North Foundation wall and reinstalled it along the South Property

Working In Grids #: A5, A6, A7, D5, D6, D7, C7

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings and foundation walls will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	214	Appr. 5,350	18	Appr. 450	24	Appr. 600	172	Appr. 4300

Site Grid Map

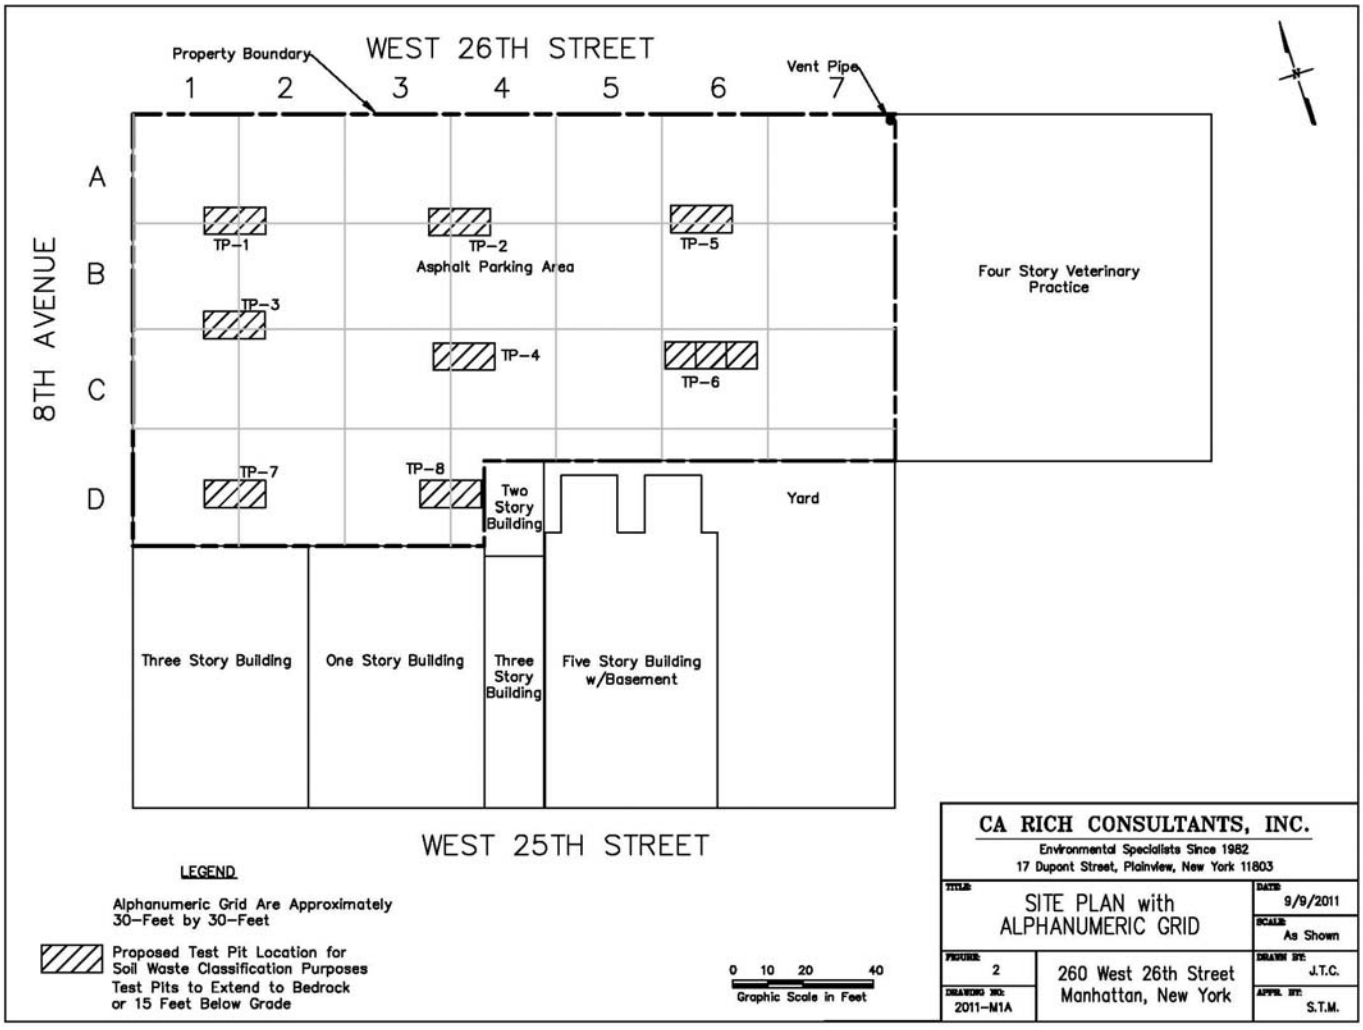

 File Name: _____

Photo Log

Photo 1 – North Wall after forms were stripped.	
Photo 2 – Continued installing rebar South Foundation Wall.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain	x	Overcast		Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	12-06-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Thirteen truckloads of soil were transported for disposal at the Soil Safe Facility in Logan, New Jersey as non-hazardous waste.

Waterproofing membrane was added along the northern and western perimeter wall.

Working In Grids #: A2, B2, and B3

Air Monitoring (Since Last Report):

Air Monitoring was not performed today due to the rain.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings and foundation walls will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
					13	325						
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	227	Appr. 5,675	18	Appr. 450	24	Appr. 600	172	Appr. 4300

Site Grid Map

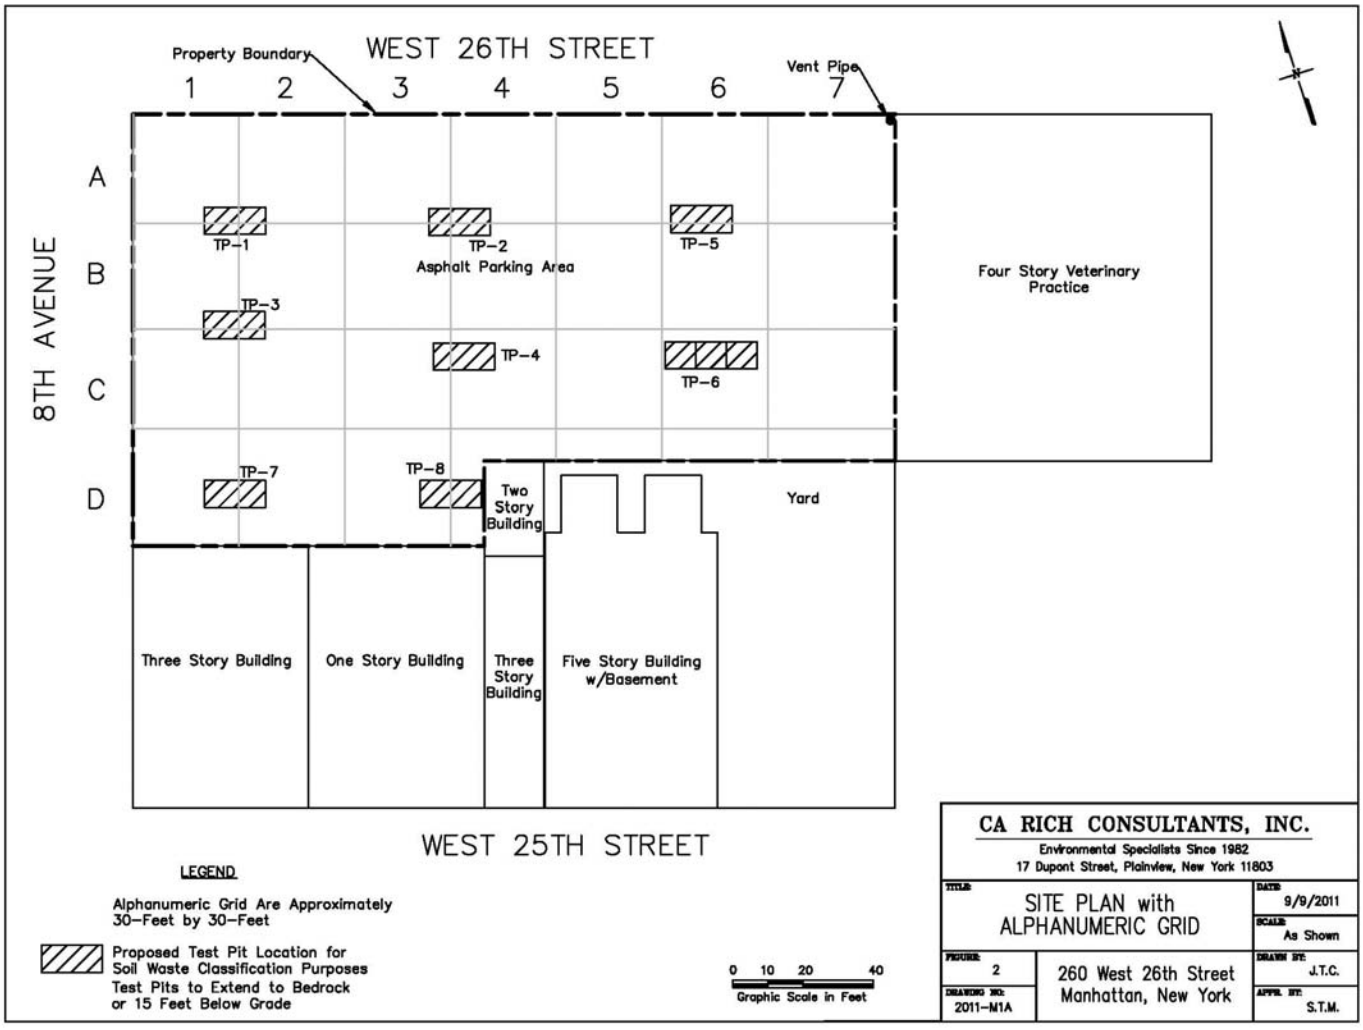

 File Name: _____

Photo Log

Photo 1 – Soil being removed from grid B3.	
Photo 2 – Continued installing waterproof membrane along northern perimeter wall.	

 File Name: _____

. Photo 3 – View of the eastern portion of the Site.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain	X	Overcast	X	Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	12-07-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Installed Rebar along the east wall and finalized Formwork along the South property line so the South Foundation Wall can be poured tomorrow.

Working In Grids #: C5,C6,A7,B7,C7,D7

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings and foundation walls will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	227	Appr. 5,675	18	Appr. 450	24	Appr. 600	172	Appr. 4300

Site Grid Map

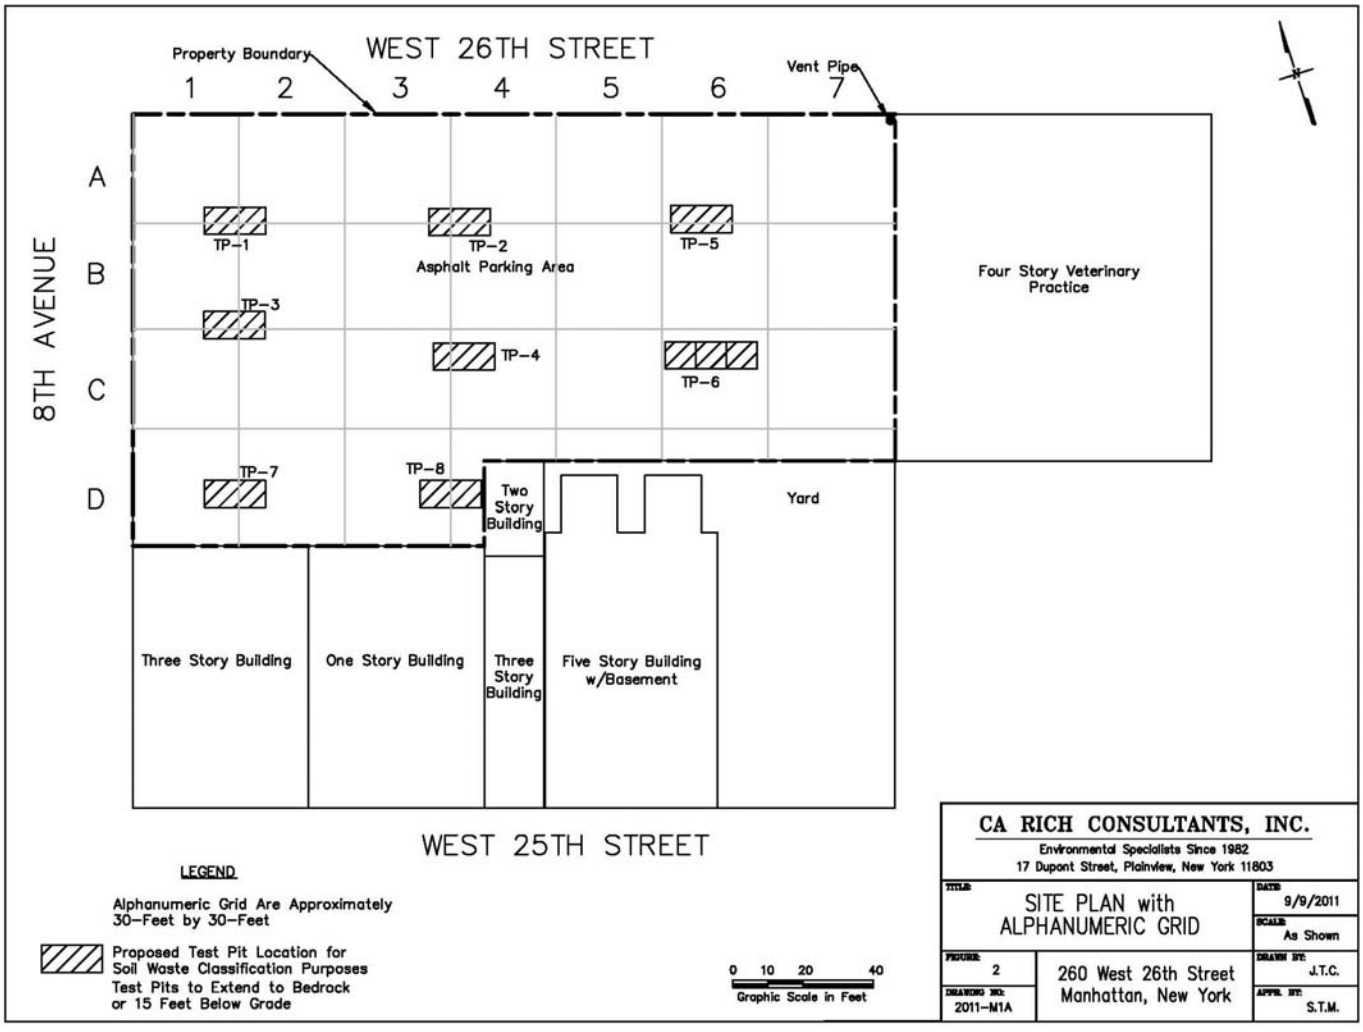

 File Name: _____

Photo Log

Photo 1 – Rebar and Waterproofing were installed for the East Foundation Wall Footing.	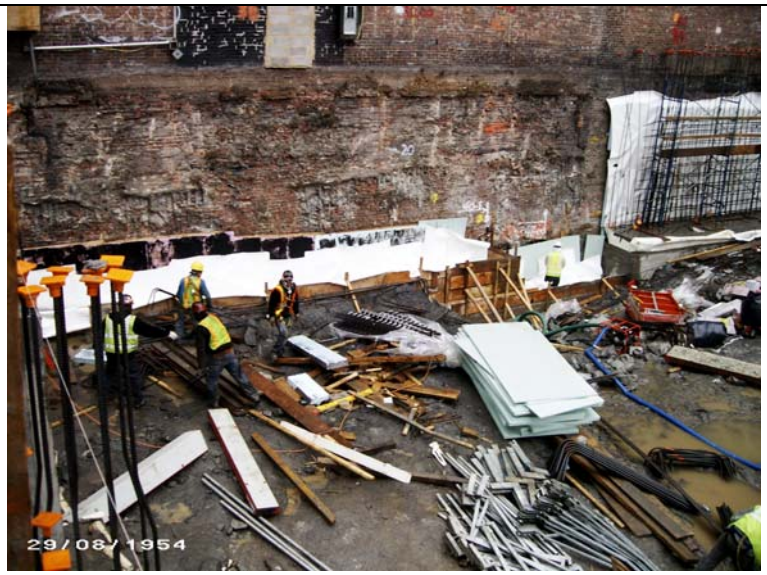
Photo 2 – Rebar continued to be installed for the East Foundation Wall.	
.Photo 3 – Formwork for the South Foundation Wall was completed today in preparation to be poured tomorrow.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	12-08-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Rebar for the East and South foundation walls and footings was installed.

Poured South Foundation Wall and a portion of the wall footings along the East and South property lines.

Working In Grids #: C5,C6,A7,B7,C7,D7

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings and foundation walls will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	220	Appr. 5500	18	Appr. 450	24	Appr. 600	186	Appr. 4650

Site Grid Map

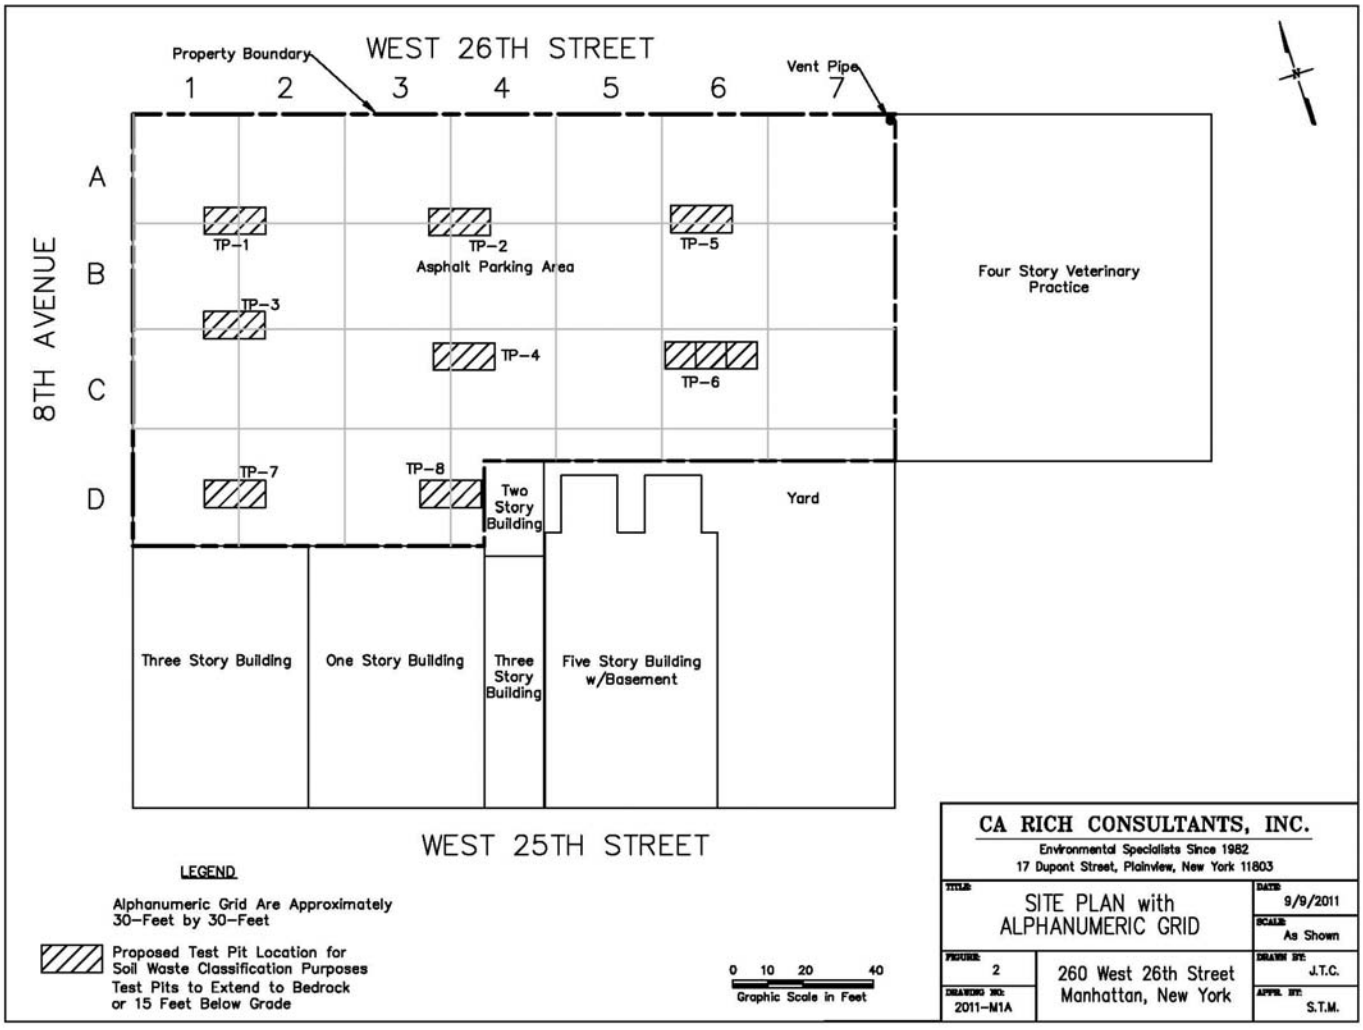

 File Name: _____

Photo Log

Photo 1 – Rebar continued to be installed for the East Wall Foundation Footing.	
Photo 2 – Rebar continued to be installed for the East Foundation Wall. Scaffolding was installed along the South Foundation wall in preparation for the wall to be poured.	
.Photo 3 – South Foundation Wall was poured today.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	12-09-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Poured the remaining section of the East Wall Footing.

Continued to install rebar for the East Foundation Wall and a portion of the South Foundation Wall.

Continued to install lagging along the West Foundation Wall.

Working In Grids #: C5,C6,A7,B7,C7,D7, A1, B1

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings and foundation walls will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	220	Appr. 5500	18	Appr. 450	24	Appr. 600	186	Appr. 4650

Site Grid Map

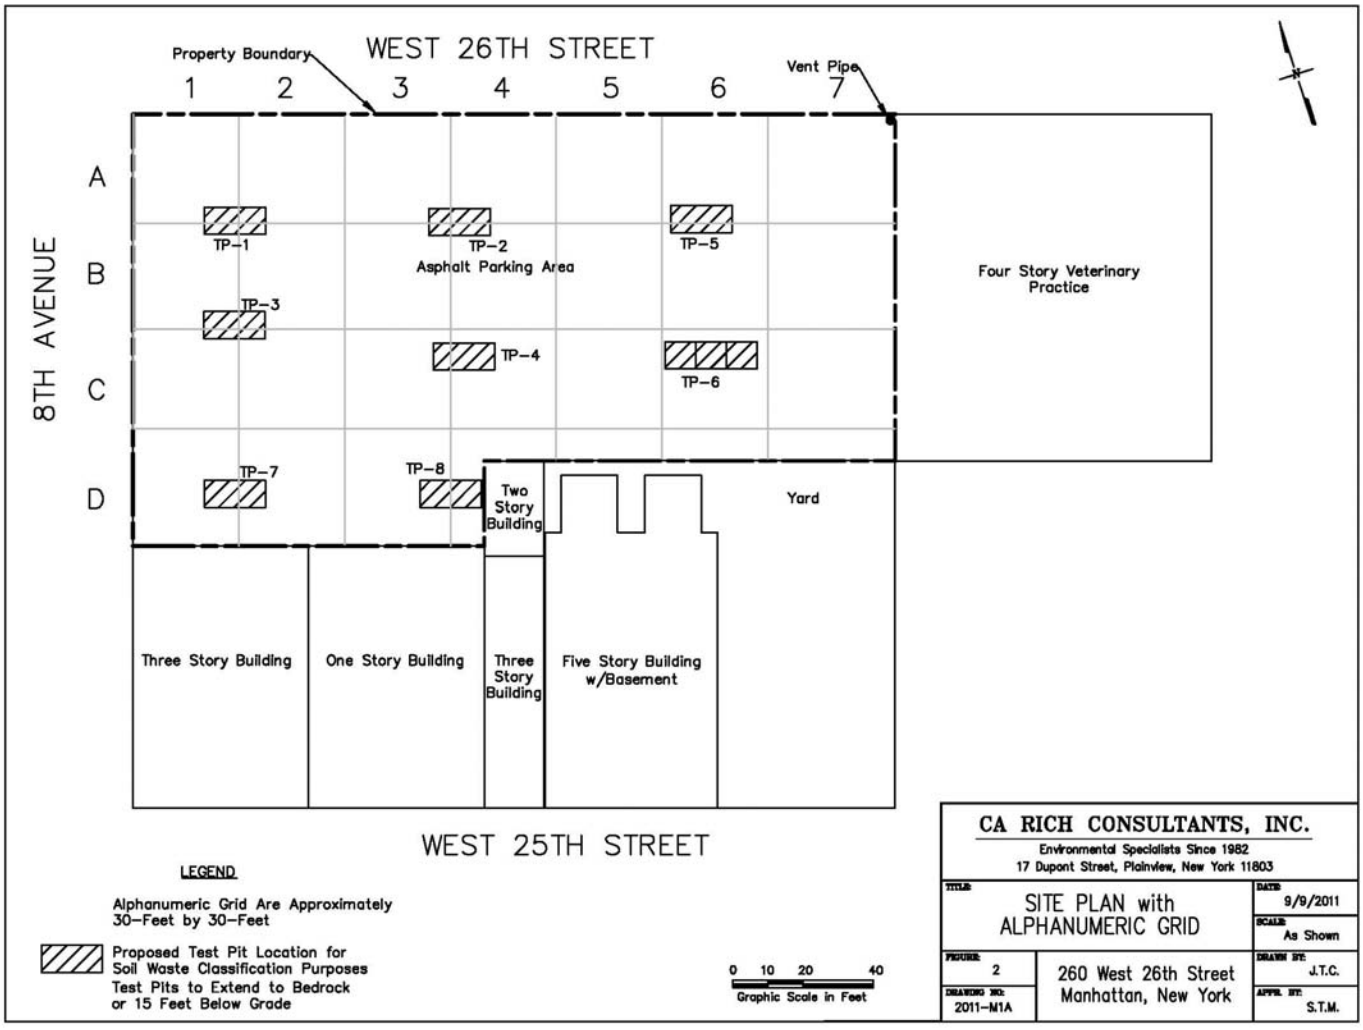

 File Name: _____

Photo Log

Photo 1 – East Wall Footing being poured.	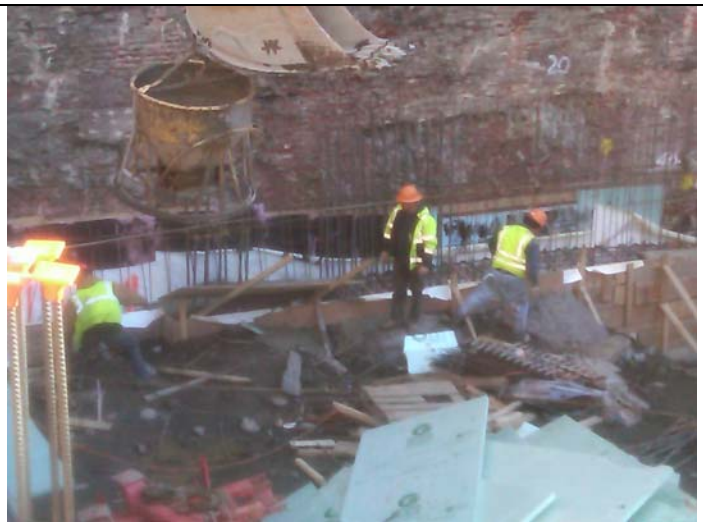
Photo 2 – East Wall Footing was poured.	
.Photo 3 – Continued lagging along the west foundation wall.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	12-10-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Installed waterproofing along the neighboring building on the East property line.

Continued to install rebar for the East Foundation Wall.

(8) Trucks of Rock were disposed of at Red Rock Materials Facility.

Working In Grids #: A7,B7,C7,D7

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings and foundation walls will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
											8	Appr. 200
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	220	Appr. 5500	18	Appr. 450	24	Appr. 600	194	Appr. 4850

Site Grid Map

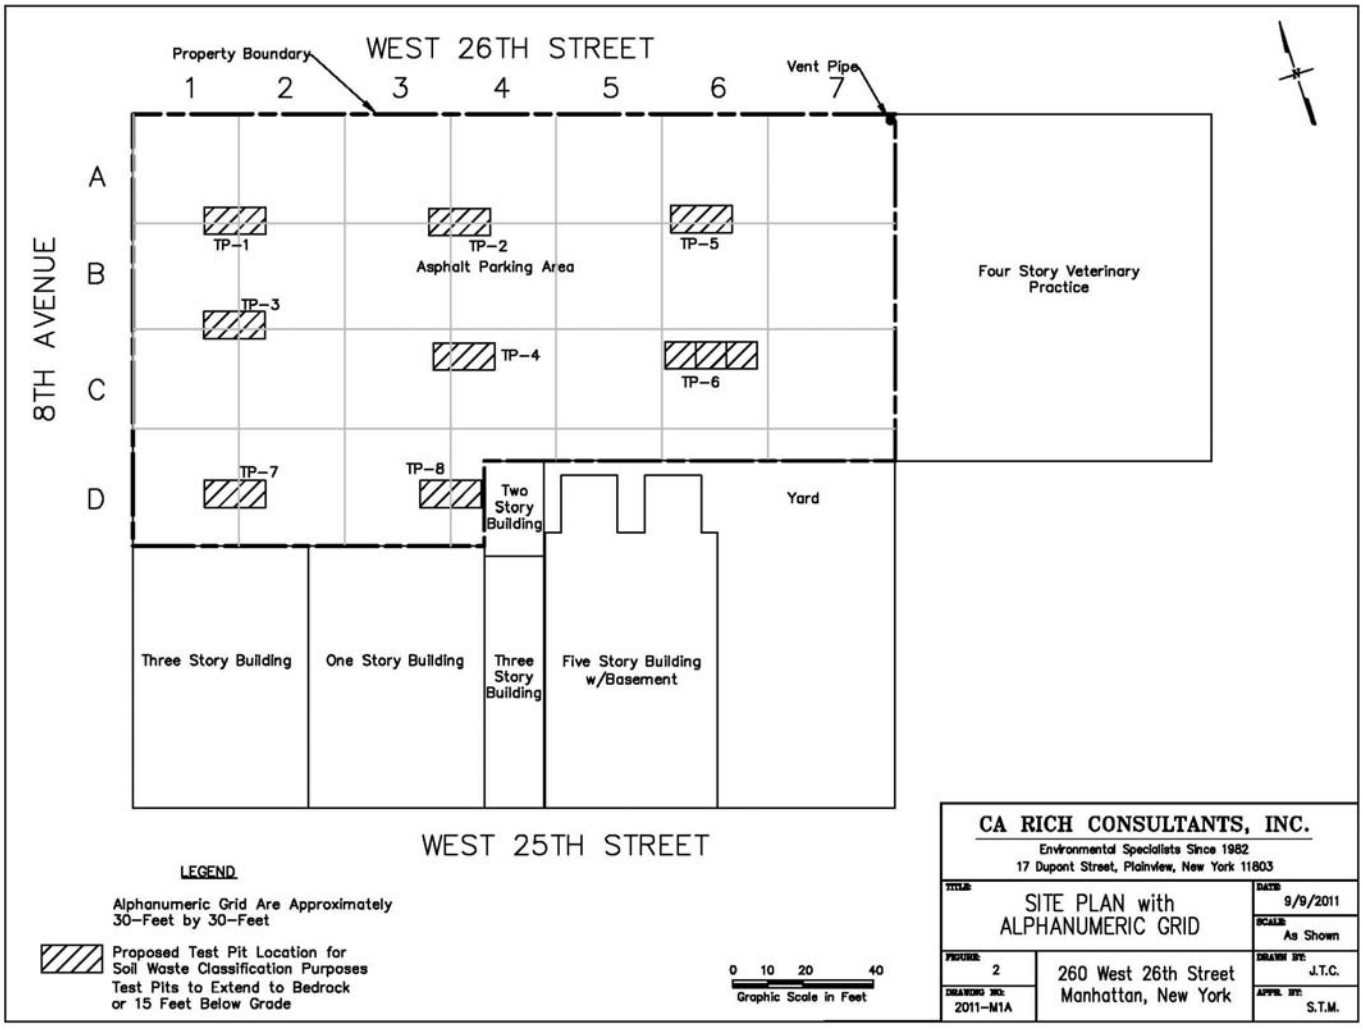

 File Name: _____

Photo Log

Photo 1 – Installing rebar and waterproofing along the East Foundation Wall.	
Photo 2 – Installing Rebar for the East Property line Shear wall.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	12-12-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Rock chopping continued along the South Property Line.

Workers continued to install rebar for the East Foundation Wall.

(2) Trucks of Rock were disposed of at Red Rock Materials Facility.

Working In Grids #: A7,B7,C7,D7, A1, A2, A3, D3, D4

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings and foundation walls will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
											2	Appr. 50
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	220	Appr. 5500	18	Appr. 450	24	Appr. 600	196	Appr. 4900

Site Grid Map

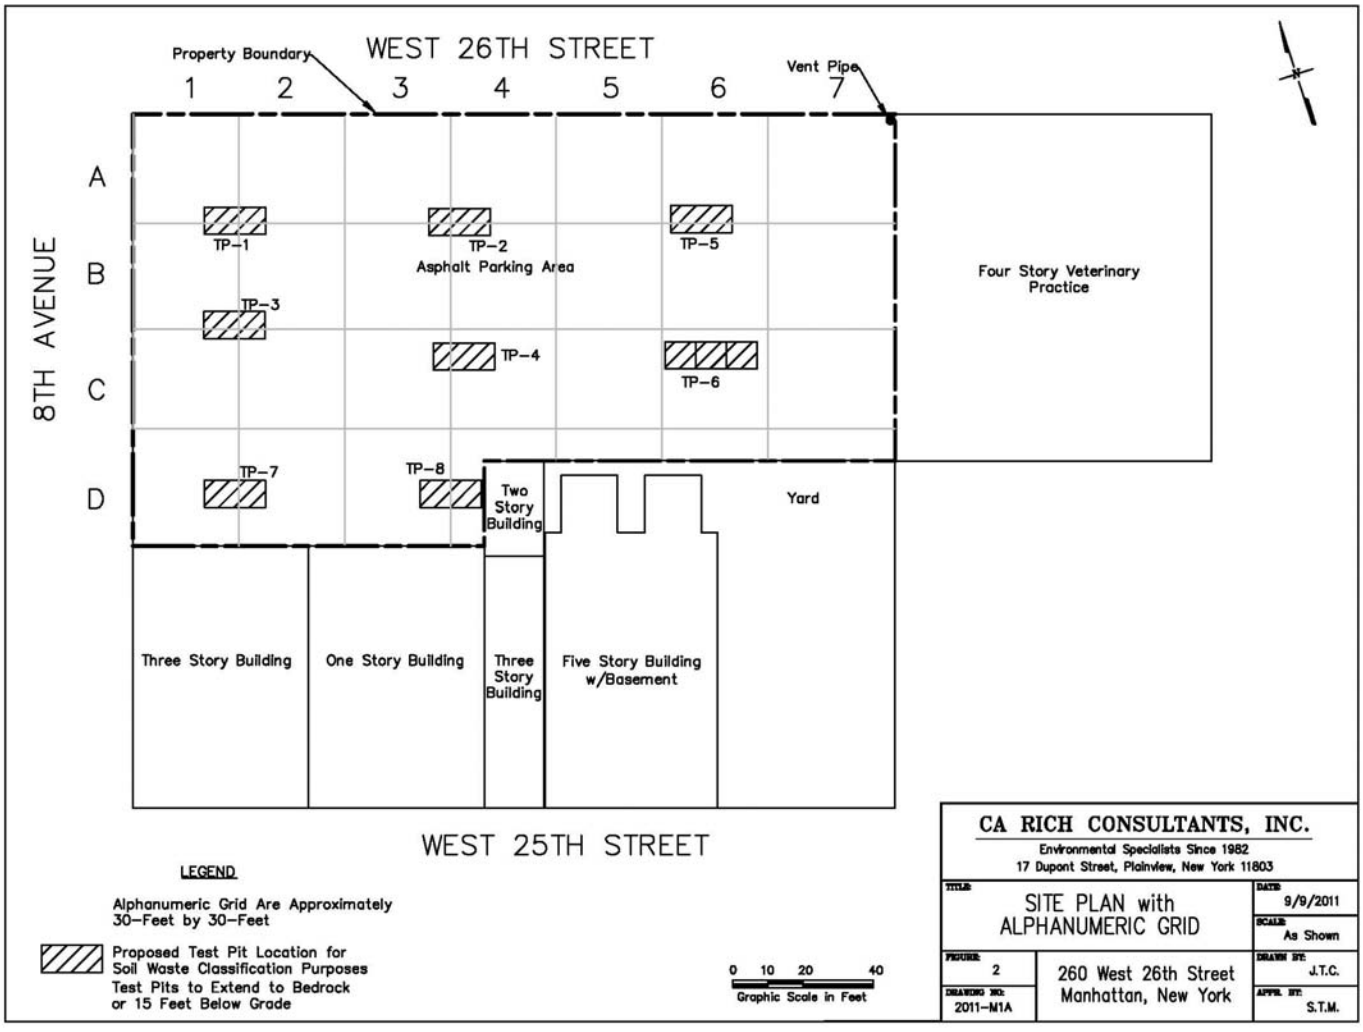

 File Name: _____

Photo Log

Photo 1 – Rock chopping continued along the South Property line.	
Photo 2 – Continuing the install lagging along the northwest corner of the site.	
Photo 3 – Workers continuing to install rebar along the East Foundation Wall.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Steve Malinowski of CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	12-13-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Rock chopping was conducted in grids D1, D2 and D3.

Workers continued to install rebar for the East Foundation Wall.

(2) Trucks of Rock were disposed of at Red Rock Materials Facility.

Working In Grids #: A7,B7,C7,D7, A1, A2, A3, D3, D4

Air Monitoring (Since Last Report):

Air Monitoring was conducted today by Jessica Proscia of CA RICH performed during today's soil excavation and loading activities. No problems were encountered.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings and foundation walls will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
					12	300					6	Appr. 150
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	232	Appr. 5,800	18	Appr. 450	24	Appr. 600	202	Appr. 5,050

Site Grid Map

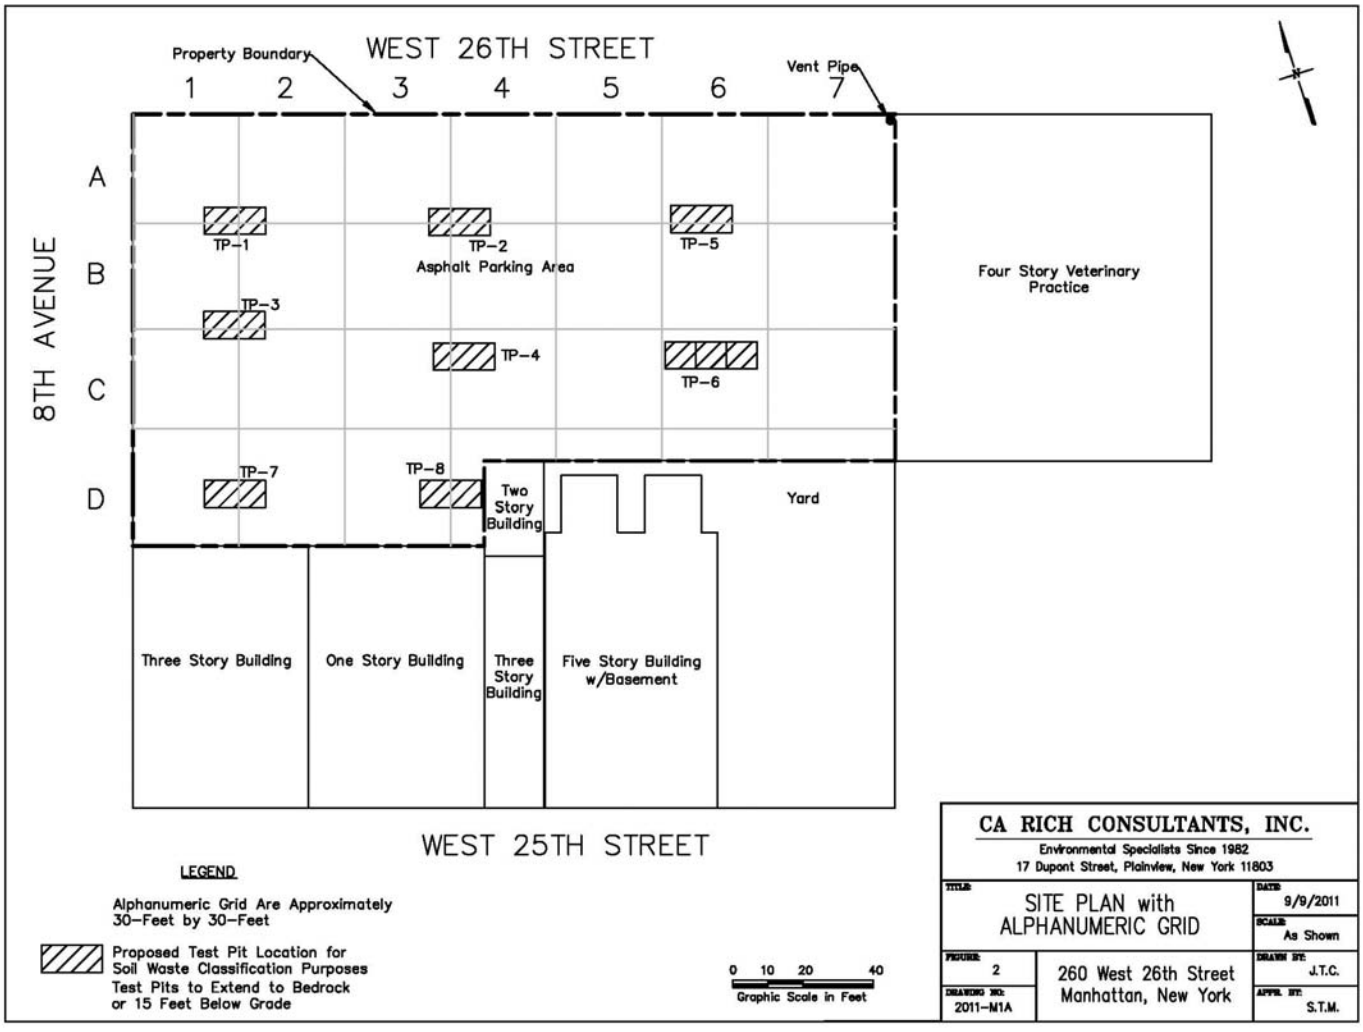

 File Name: _____

Photo Log

Photo 1 – Soil loading for off-site disposal at Soil Safe.	
Photo 2 – Excavation of bedrock in grids D3 and D4.	
Photo 3 – Rebar and waterproofing membrane installed along the eastern foundation Wall.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Steve Malinowski of CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	12-14-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Soil excavation and off-site disposal from grids C4 and C5 was conducted today. A total of eight truckloads were sent to the Soil Safe Facility in Logan Township, NJ.

Rock chopping continued in grids D3 and D4 with seven truckloads of rock being shipped off-site for disposal at Red Roc Materials in Lyndhurst, NJ

Working In Grids #: C4 and C5

Air Monitoring (Since Last Report):

Air Monitoring was conducted today by Jessica Proscia of CA RICH performed during today's soil excavation and loading activities. No problems were encountered.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings and foundation walls will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
					8	200					7	Appr. 175
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	232	Appr. 6,000	18	Appr. 450	24	Appr. 600	202	Appr. 5,225

Site Grid Map

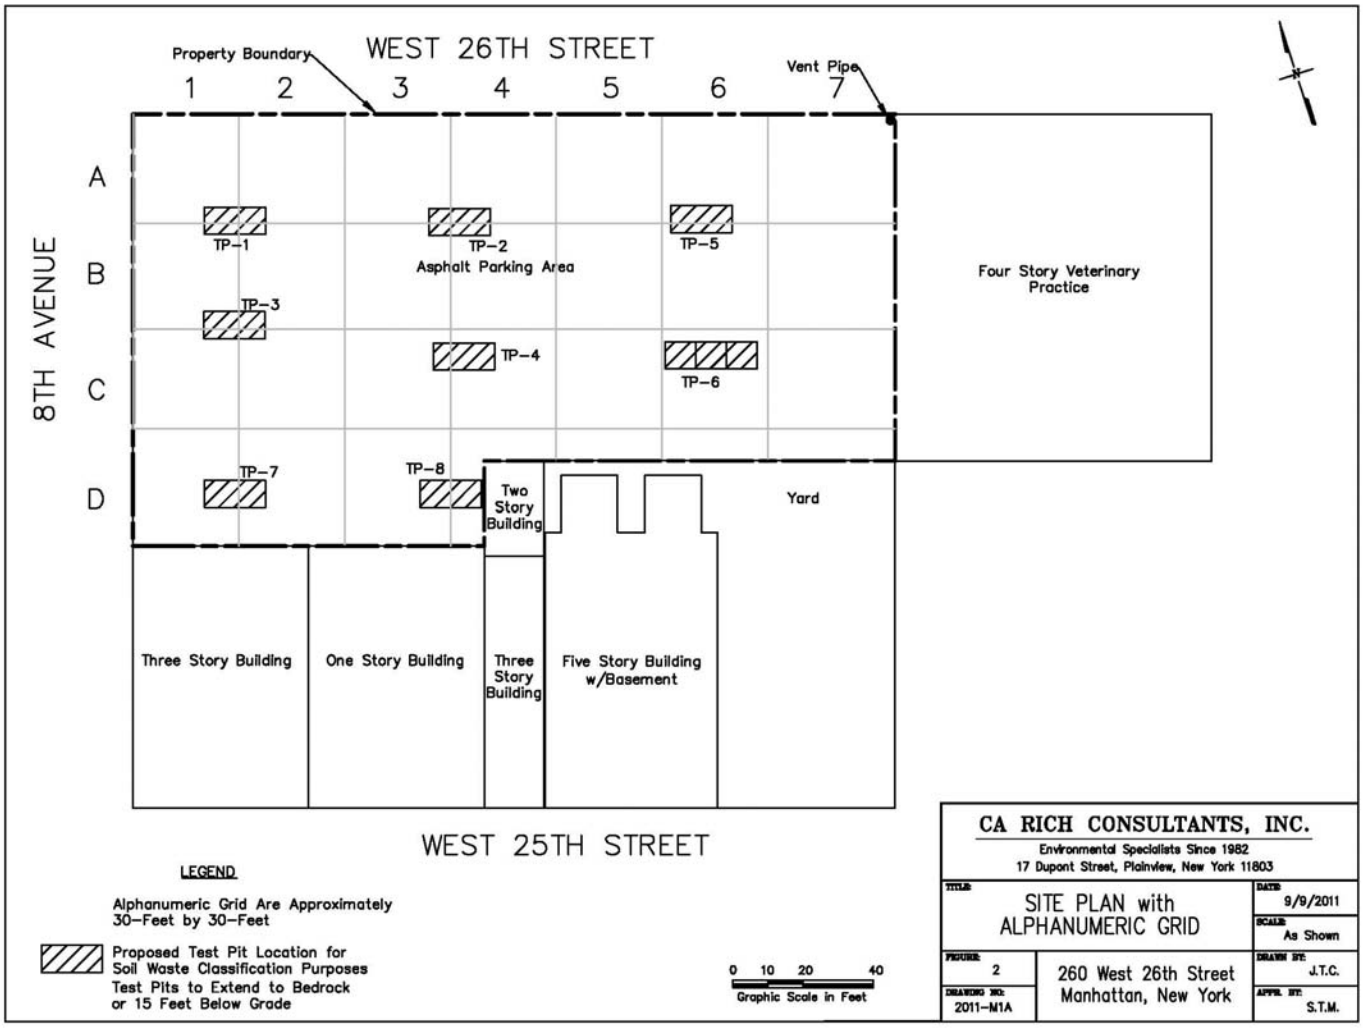

 File Name: _____

Photo Log

Photo 1 – Soil loading for off-site disposal at Soil Safe from grids C4 and 5.	
Photo 2 – Soil loading for off-site disposal at Soil Safe from grids C4 and 5.	
Photo 3 – Soil loading for off-site disposal at Soil Safe from grids C4 and 5.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Steve Malinowski of CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy	x	Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	12-15-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Soil excavation and off-site disposal from grids C3 and C4 was conducted today. A total of seventeen truckloads of soil were transported to the Soil Safe Facility in Logan Township, NJ.

Rock chopping continued in grids D3 and D4 with four truckloads of rock being shipped off-site for disposal at Red Roc Materials in Lyndhurst, NJ

Working In Grids #: C3, C4, D3 and D4

Air Monitoring (Since Last Report):

Air Monitoring was conducted today by Jessica Proscia of CA RICH performed during today's soil excavation and loading activities. No problems were encountered.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings and foundation walls will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
					17	425					4	Appr. 100
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	232	Appr. 6,425	18	Appr. 450	24	Appr. 600	206	Appr. 5,325

Site Grid Map

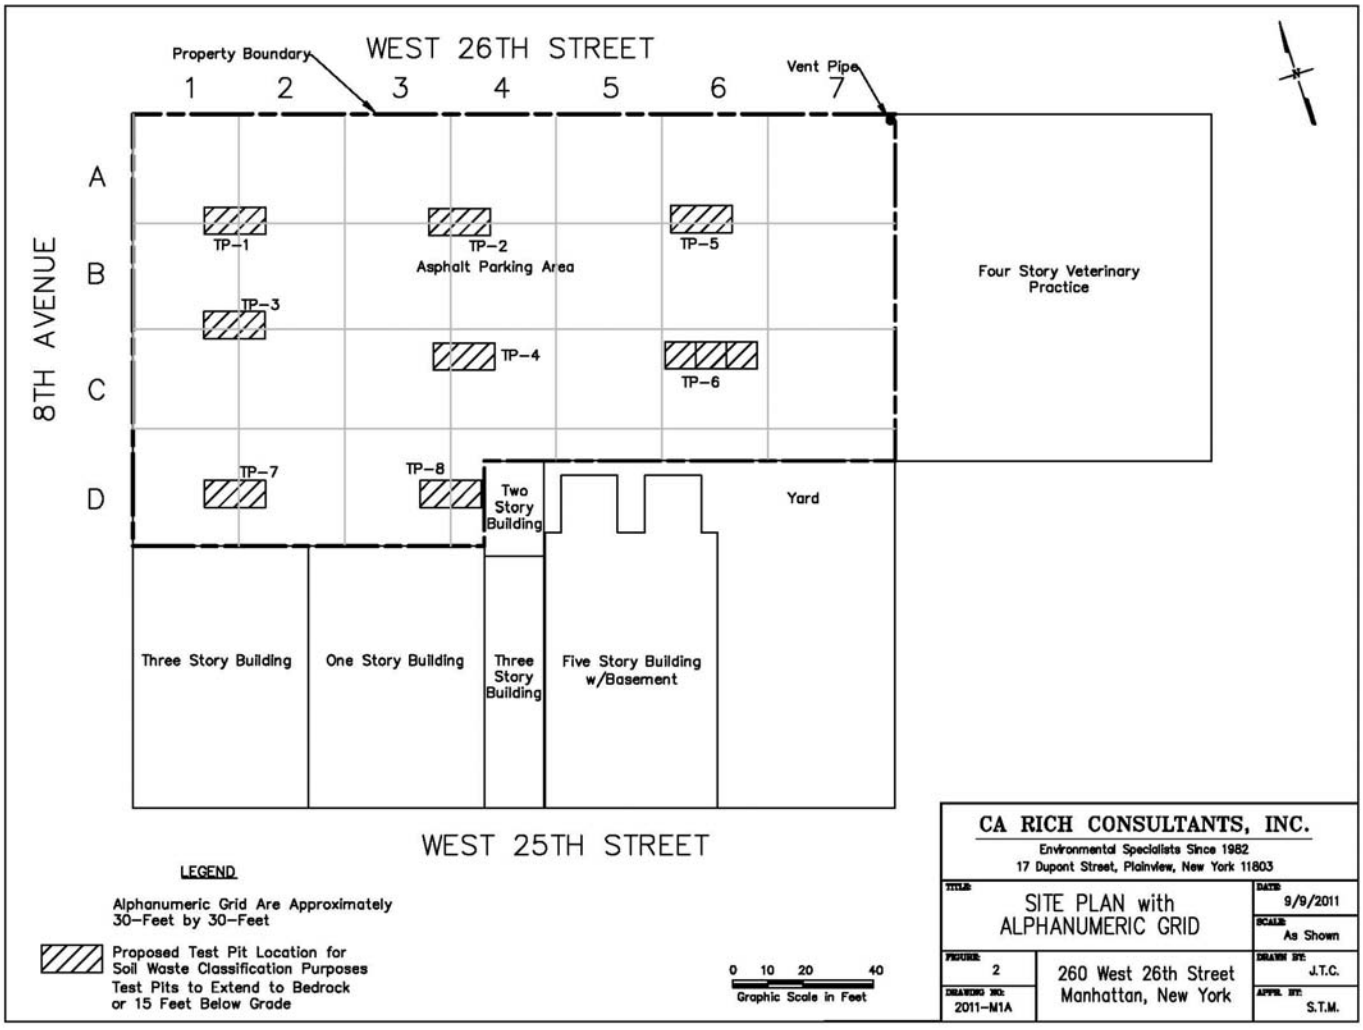

 File Name: _____

Photo Log

Photo 1 – Looking west across site at remaining soil excavation. Note: the bottom of the eastern portion is bedrock with building materials stored on top of it.	
Photo 2 – Looking south across center of the site .	
Photo 3 – Looking west across site at remaining soil excavation. Note: the bottom of the eastern portion is bedrock with building materials stored on top of it.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	12-16-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Rock chopping continued along the South Property Line.

Poured the East Foundation Wall.

Working In Grids #: A7, B7, C7, D7, D1, D2, D3, D4

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings and foundation walls will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	232	Appr. 6425	18	Appr. 450	24	Appr. 600	206	Appr. 5325

Site Grid Map

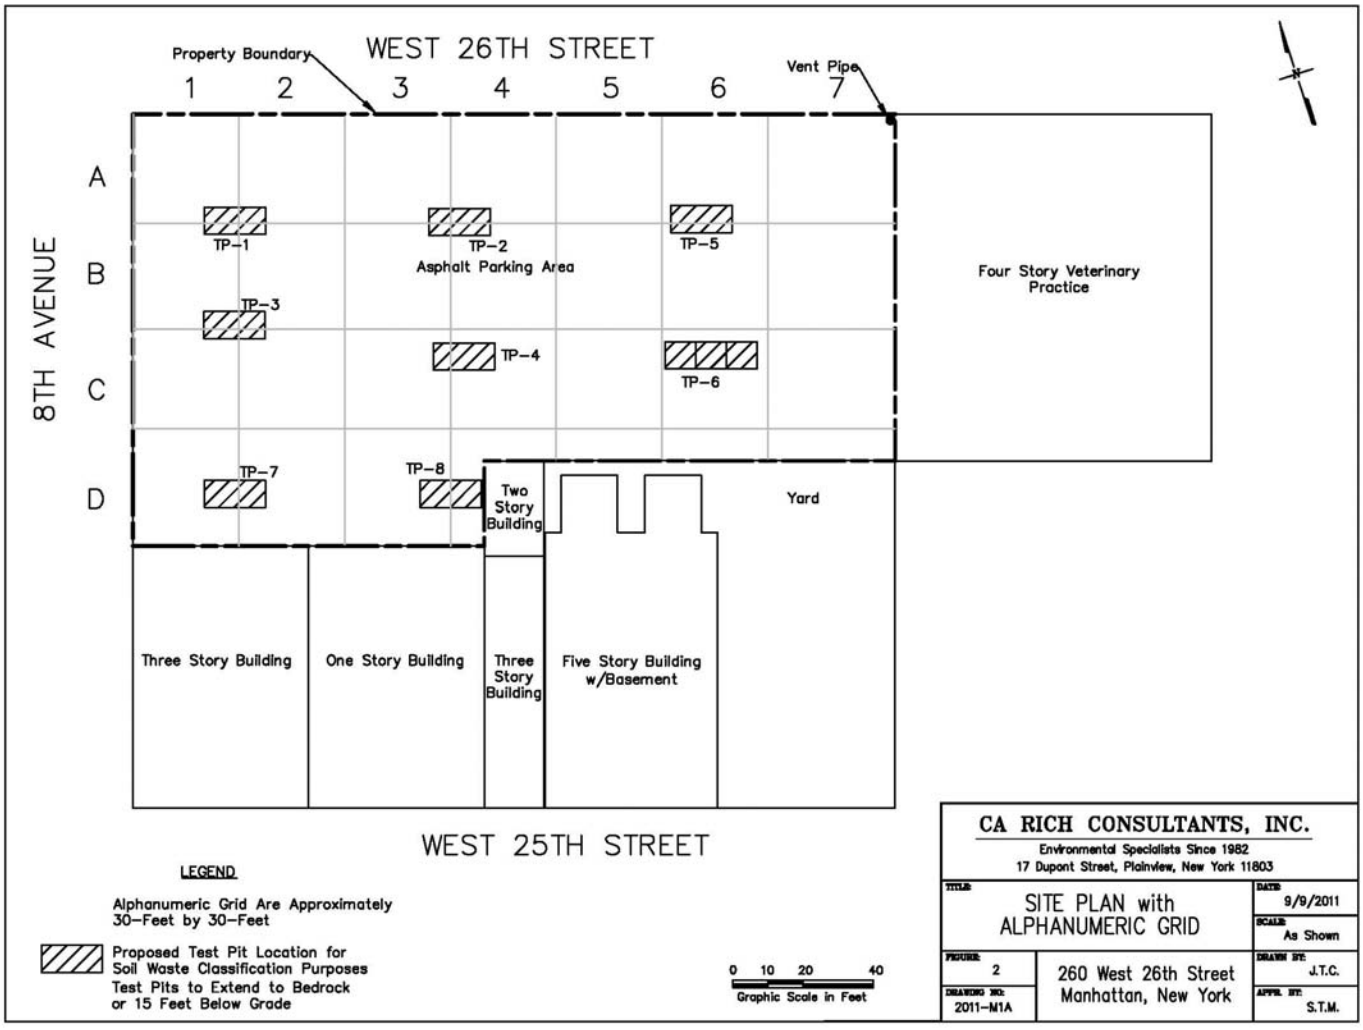

 File Name: _____

Photo Log

Photo 1 – Formwork along East Foundation Wall.	
Photo 2 – Meva Formwork set in place for East Foundation Wall pour.	
Photo 3 – Rock Chopping along South Property Line.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	12-17-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

11 Trucks of Bedrock were taken to Red Roc Materials.

Cleaned up site. Workers reorganized and staged material, equipment, etc. in preparation for work next week.

Working In Grids #: All

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings and foundation walls will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
											11	275
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	232	Appr. 6425	18	Appr. 450	24	Appr. 600	217	Appr. 5425

Site Grid Map

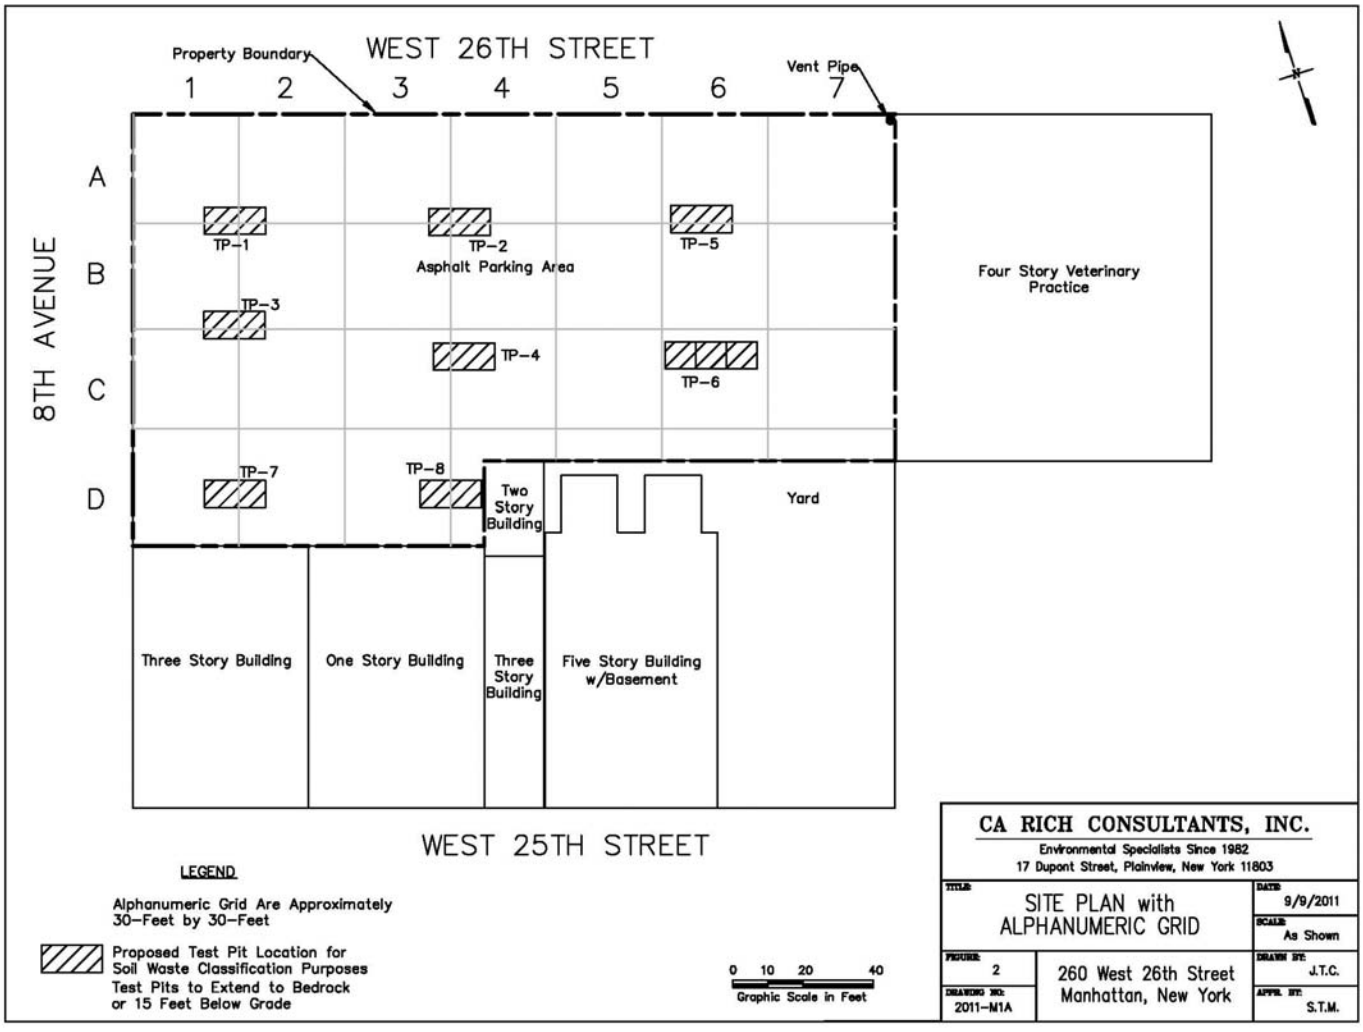

 File Name: _____

Photo Log

Photo 1 – Stockpile of Rock removed from the site. Material and equipment was stockpiled and reorganized throughout the site.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	12-19-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Interior Footings for Foundation Walls and Columns began to be formed.

Rock Chopping continued along the South Property line.

HP Piles were extended along the North Foundation Wall to provide additional bracing.

Working In Grids #: A2, A3, D1, D2, D3, C5, C6, C7

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings and foundation walls will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	232	Appr. 6425	18	Appr. 450	24	Appr. 600	217	Appr. 5425

Site Grid Map

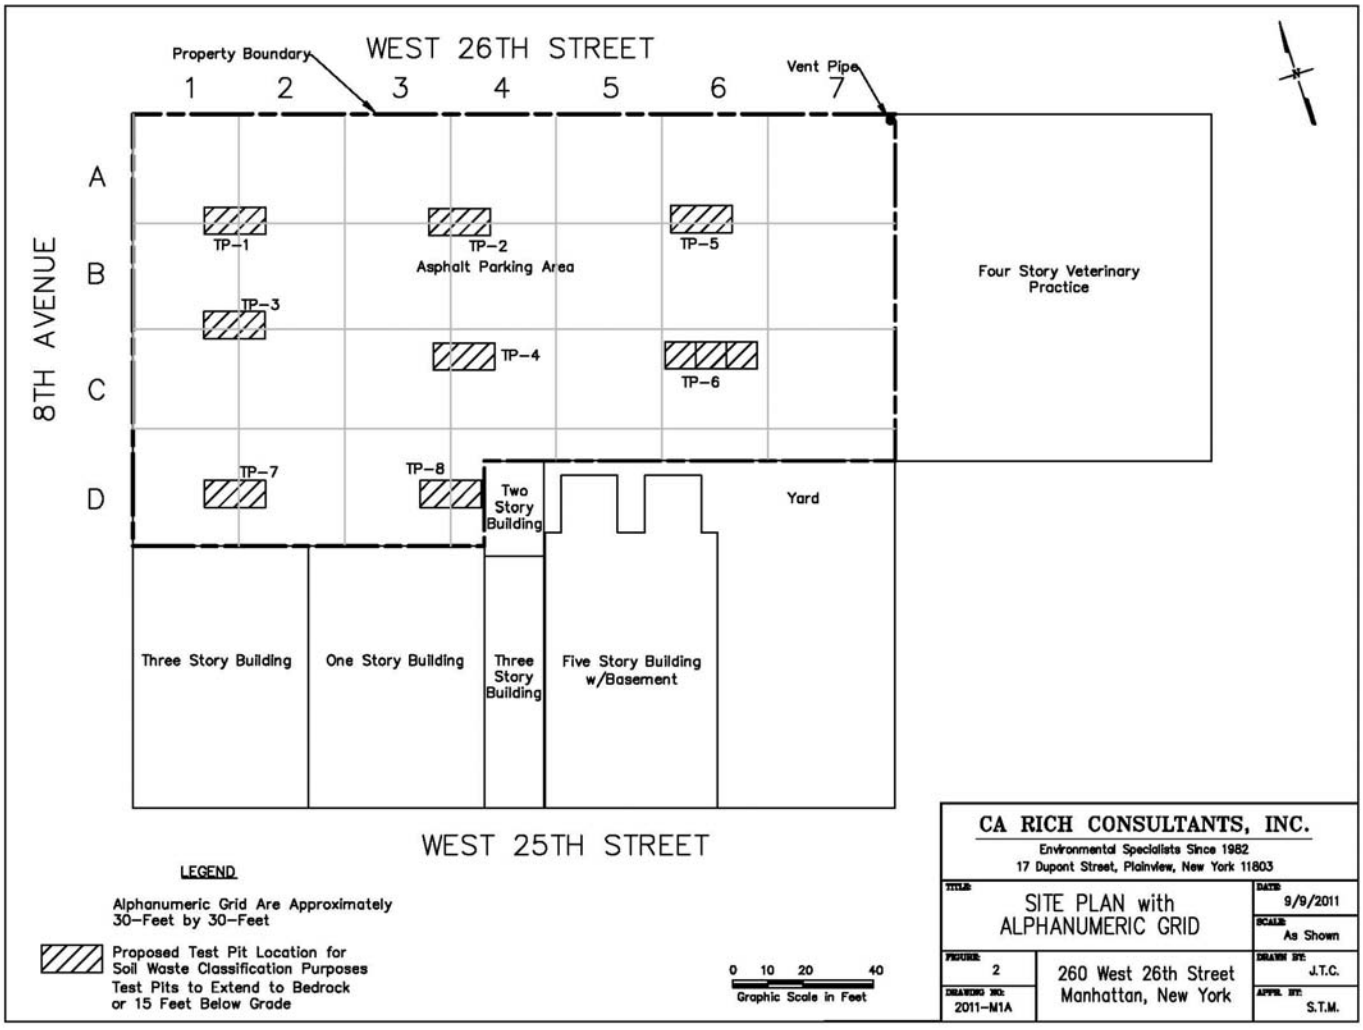

 File Name: _____

Photo Log

Photo 1 – Interior Footings for Columns and Foundation Walls began today.	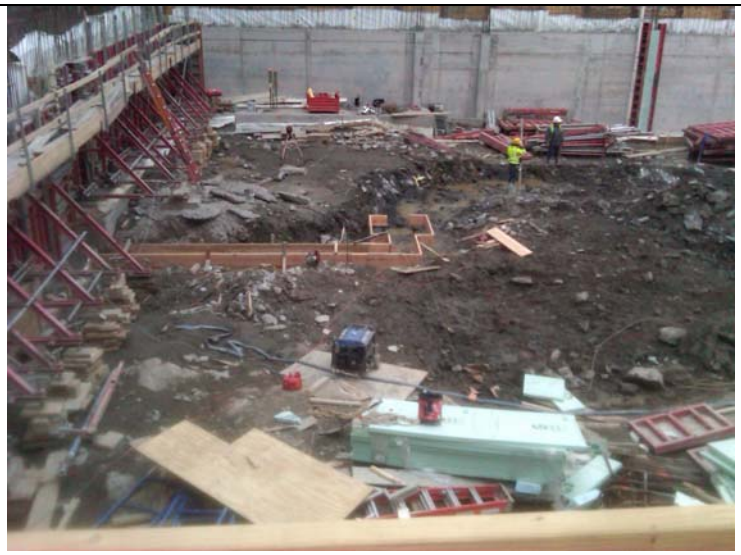
Photo 2 – Welders extended HP Piles to provide additional bracing for lagging.	
Photo 3 – Rock chopping continued along the South Property Line.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	12-20-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Interior Footings for Foundation Walls and Columns continued to be formed and a rat slab was poured in preparation for the waterproofing and rebar to be installed tomorrow.

Rock Chopping continued along the South Property line. 5 Truck loads of Rock were taken to Red Roc Materials Facility in Lyndhurst, NJ.

HP Piles were extended along the North Foundation Wall to provide additional bracing.

Working In Grids #: B5, B6, C5, C6, D1, D2, D3

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings and foundation walls will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
											5	
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	232	Appr. 6425	18	Appr. 450	24	Appr. 600	222	Appr. 5550

Site Grid Map

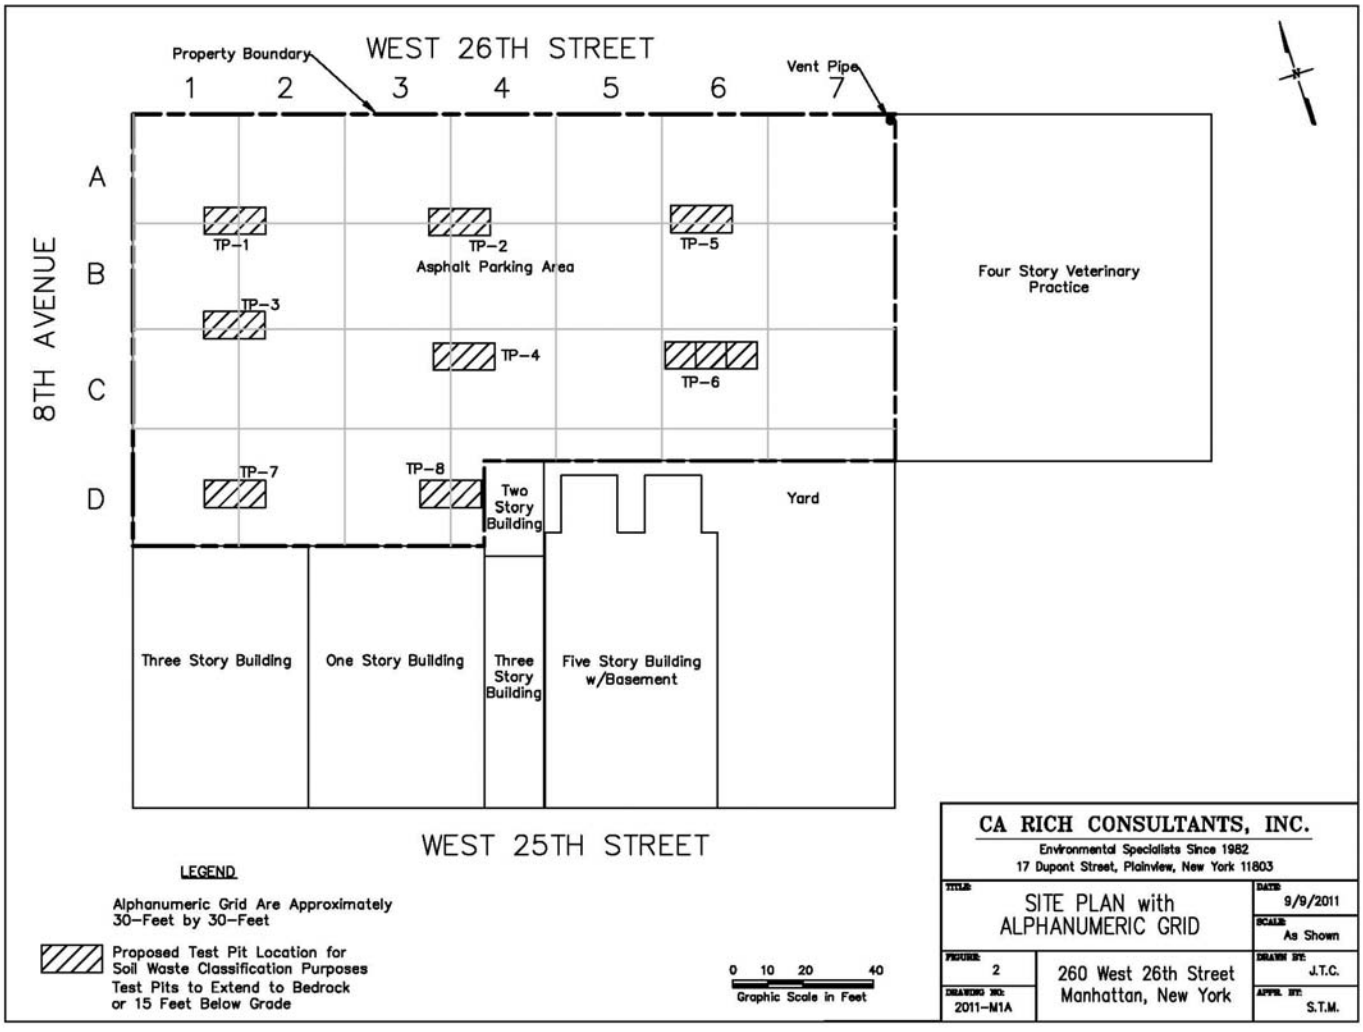

 File Name: _____

Photo Log

Photo 1 – Workers preparing elevator pit.	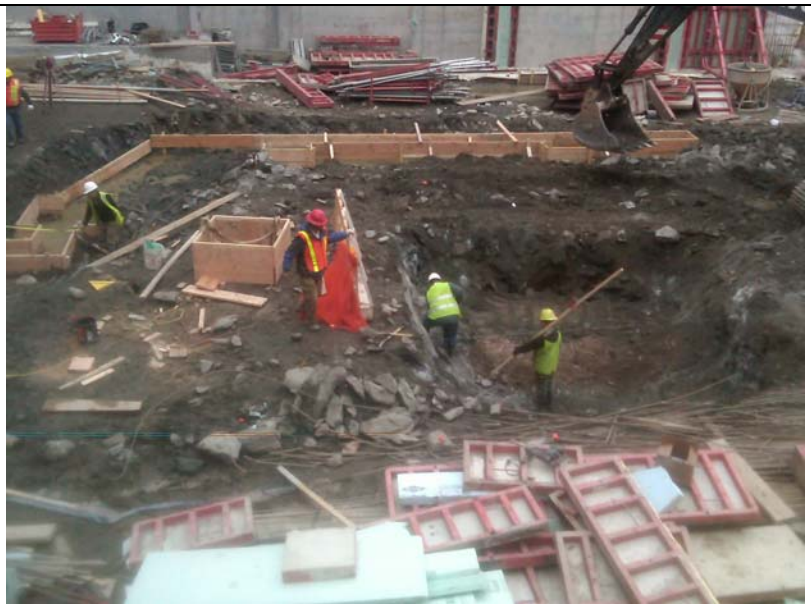
Photo 2 – Rat slab being poured in bottom of elevator pit.	
Photo 3 – Rat slab was poured for an interior foundation wall on the east half of the site.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain	X	Overcast		Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	12-21-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Interior Footings for Foundation Walls and Columns continued to be formed. Waterproofing and rebar were installed for the interior foundation wall footings. Footings are to be poured tomorrow.

Rock Chopping continued along the South Property line. 5 Truck loads of Rock were taken to Red Roc Materials Facility in Lyndhurst, NJ.

Working In Grids #: B5, B6, C5, C6, D1, D2, D3

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings and foundation walls will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
											5	
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	232	Appr. 6425	18	Appr. 450	24	Appr. 600	227	Appr. 5675

Site Grid Map

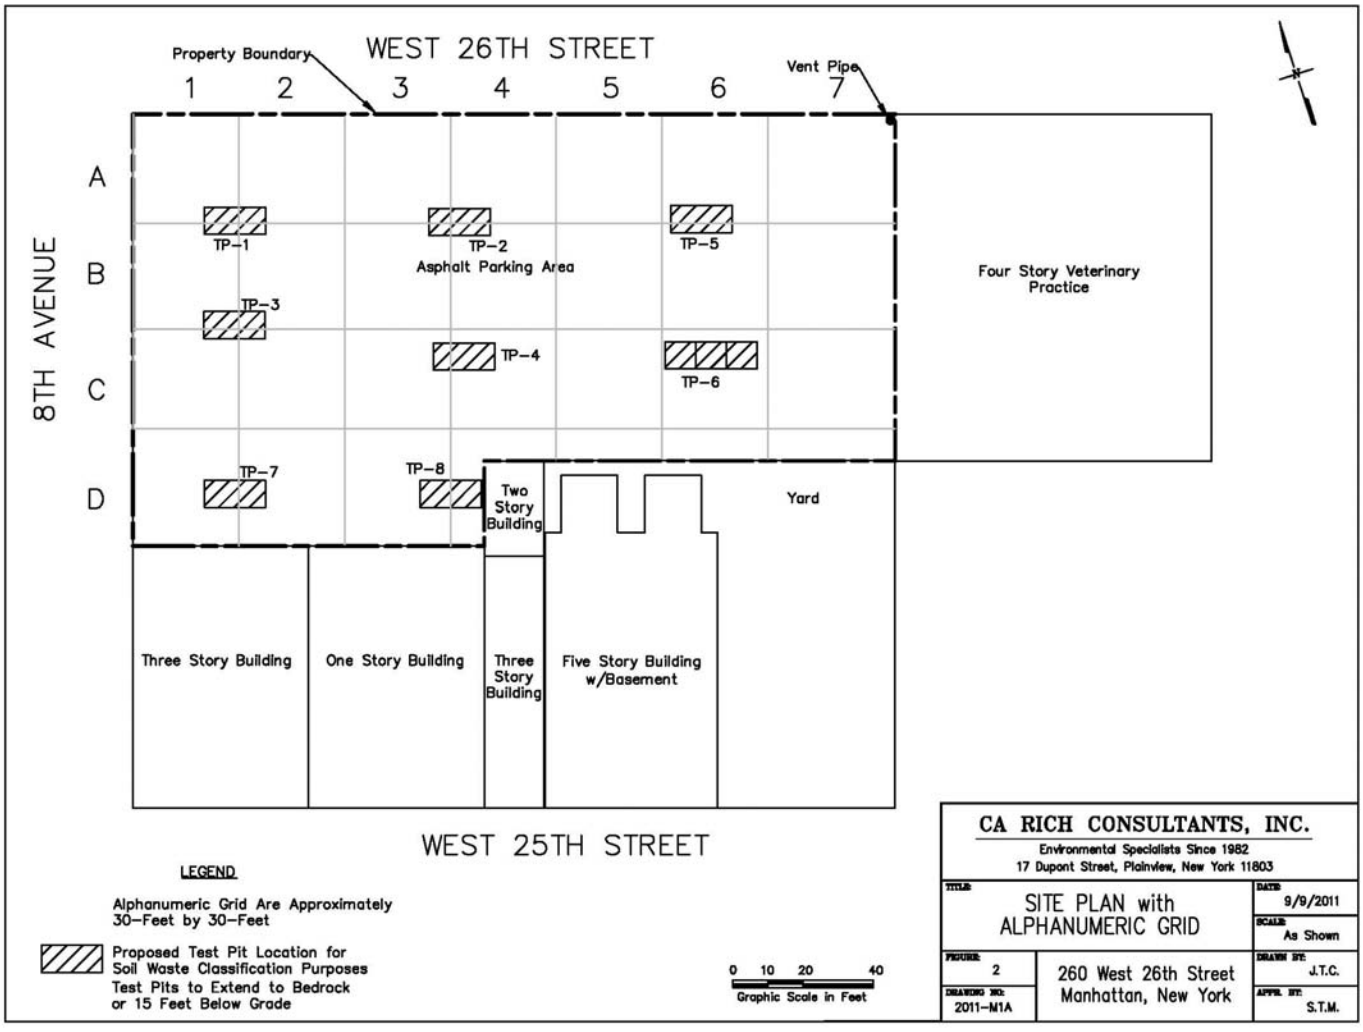

 File Name: _____

Photo Log

Photo 1 – Waterproofing installed on interior foundation wall footing.	
Photo 2 – Rebar beginning to be installed on interior foundation wall footing.	
Photo 3 – Workers marking out location of footing for elevator pits.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	12-22-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Footings for an elevator pit and an interior foundation wall were poured

Rock Chopping continued along the South Property line. 13 Truck loads of Rock were taken to Red Roc Materials Facility in Lyndhurst, NJ.

Working In Grids #: B5, B6, C5, C6, D1, D2, D3

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings and foundation walls will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
											13	
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	232	Appr. 6425	18	Appr. 450	24	Appr. 600	240	Appr. 6000

Site Grid Map

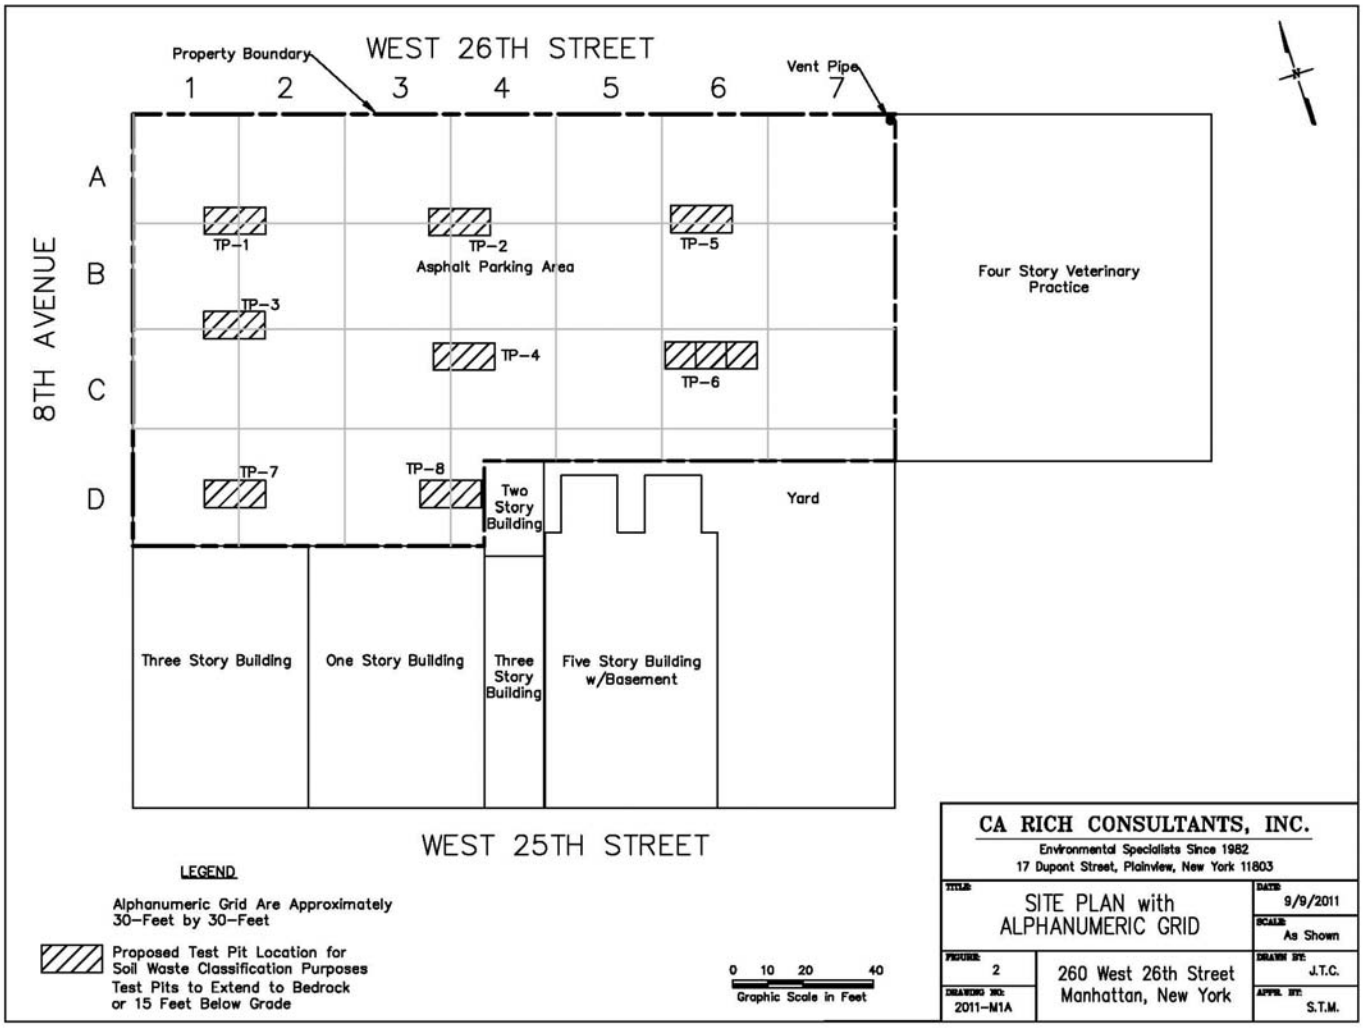

 File Name: _____

Photo Log

Photo 1 – Workers vibrating the concrete for the Elevator #4 Footing.	
Photo 2 – Rock chopping continued to prep for Elevator #1 Slab.	
Photo 3 – Concrete Footing being poured for interior foundation wall on the east half of the site.	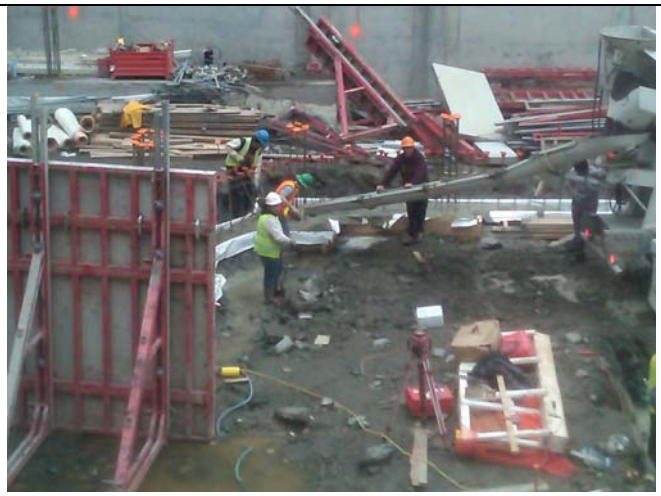

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	12-23-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

The Forms were moved away from the East Foundation Wall.

Contractor marked out where future excavation of columns and elevator pits will be rock chopped next week. Rock Chopping began on Residential Elevator Pit.

Rock Chopping continued along the South Property line. 6 Truck loads of Rock were taken to Red Roc Materials Facility in Lyndhurst, NJ.

Working In Grids #: B5, B6, C5, C6, D1, D2, D3

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings and foundation walls will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
											6	
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	232	Appr. 6425	18	Appr. 450	24	Appr. 600	246	Appr. 6150

Site Grid Map

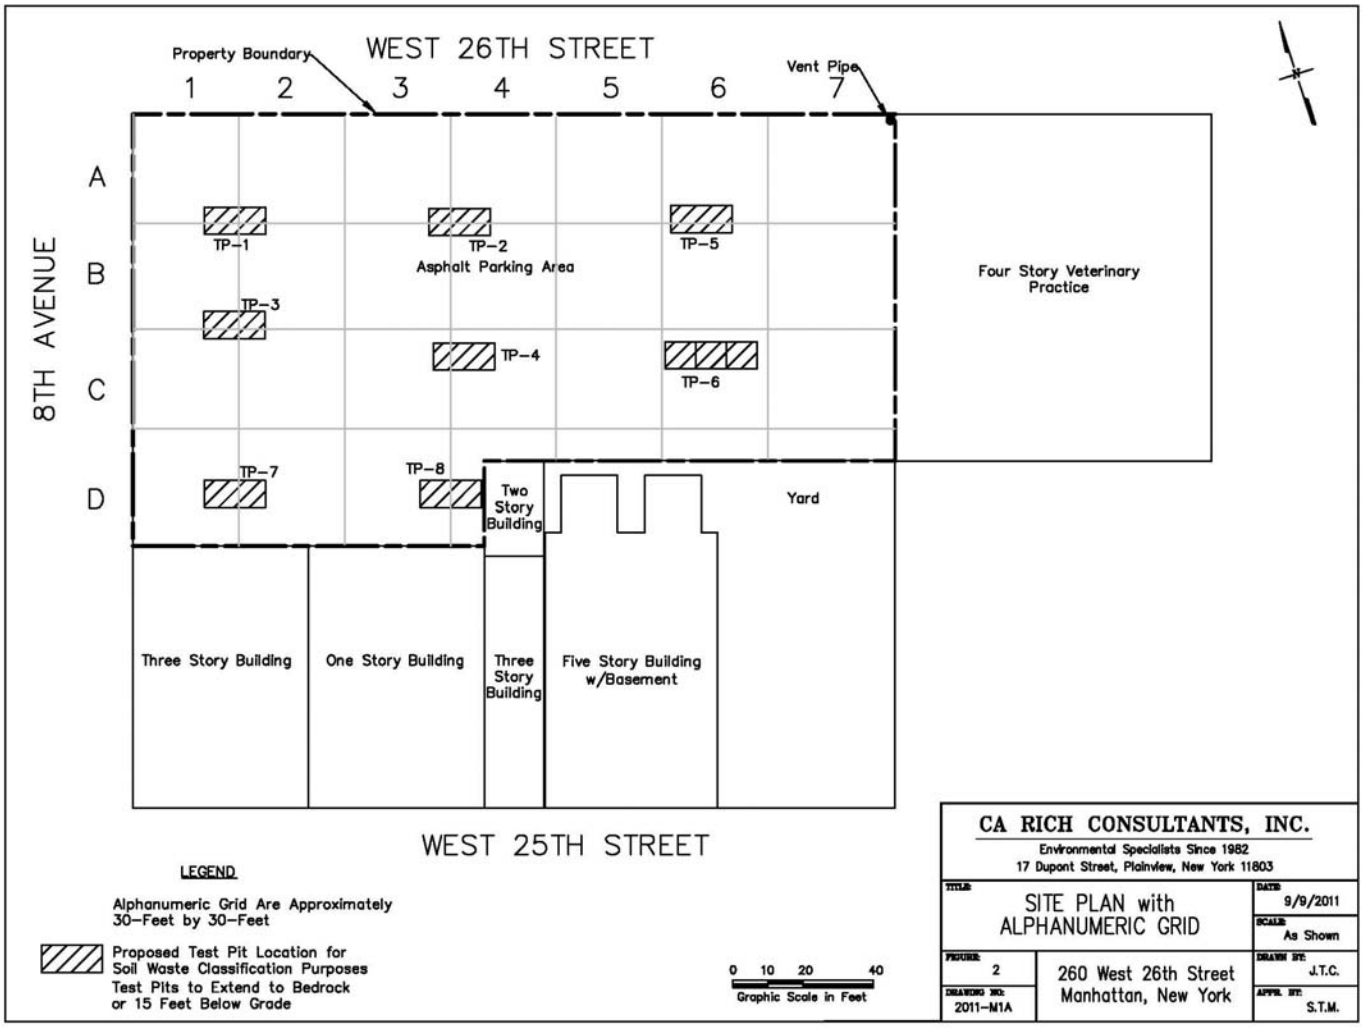

 File Name: _____

Photo Log

Photo 1 – Additional lagging boards were delivered to site to complete the lagging on the North and East Foundation Walls.	
Photo 2 – Rock Chopping for the residential elevator pit.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Steve Malinowski of CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy	x	Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	12-27-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Soil excavation and off-site disposal from grids C3 and C4 was conducted today. A total of nine truckloads of soil were transported to the Soil Safe Facility in Logan Township, NJ.

Rock chopping continued in grids D2, D3, and D4 with twelve truckloads of rock being shipped off-site for disposal at Red Roc Materials in Lyndhurst, NJ.

Working In Grids #: C3, C4, D2, D3, and D4

Air Monitoring (Since Last Report):

Air Monitoring was conducted today by Jessica Proscia of CA RICH performed during today's soil excavation and loading activities. No problems were encountered.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings and foundation walls will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
					9	180					12	Appr. 300
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	241	Appr. 6,605	18	Appr. 450	24	Appr. 600	218	Appr. 5,625

Site Grid Map

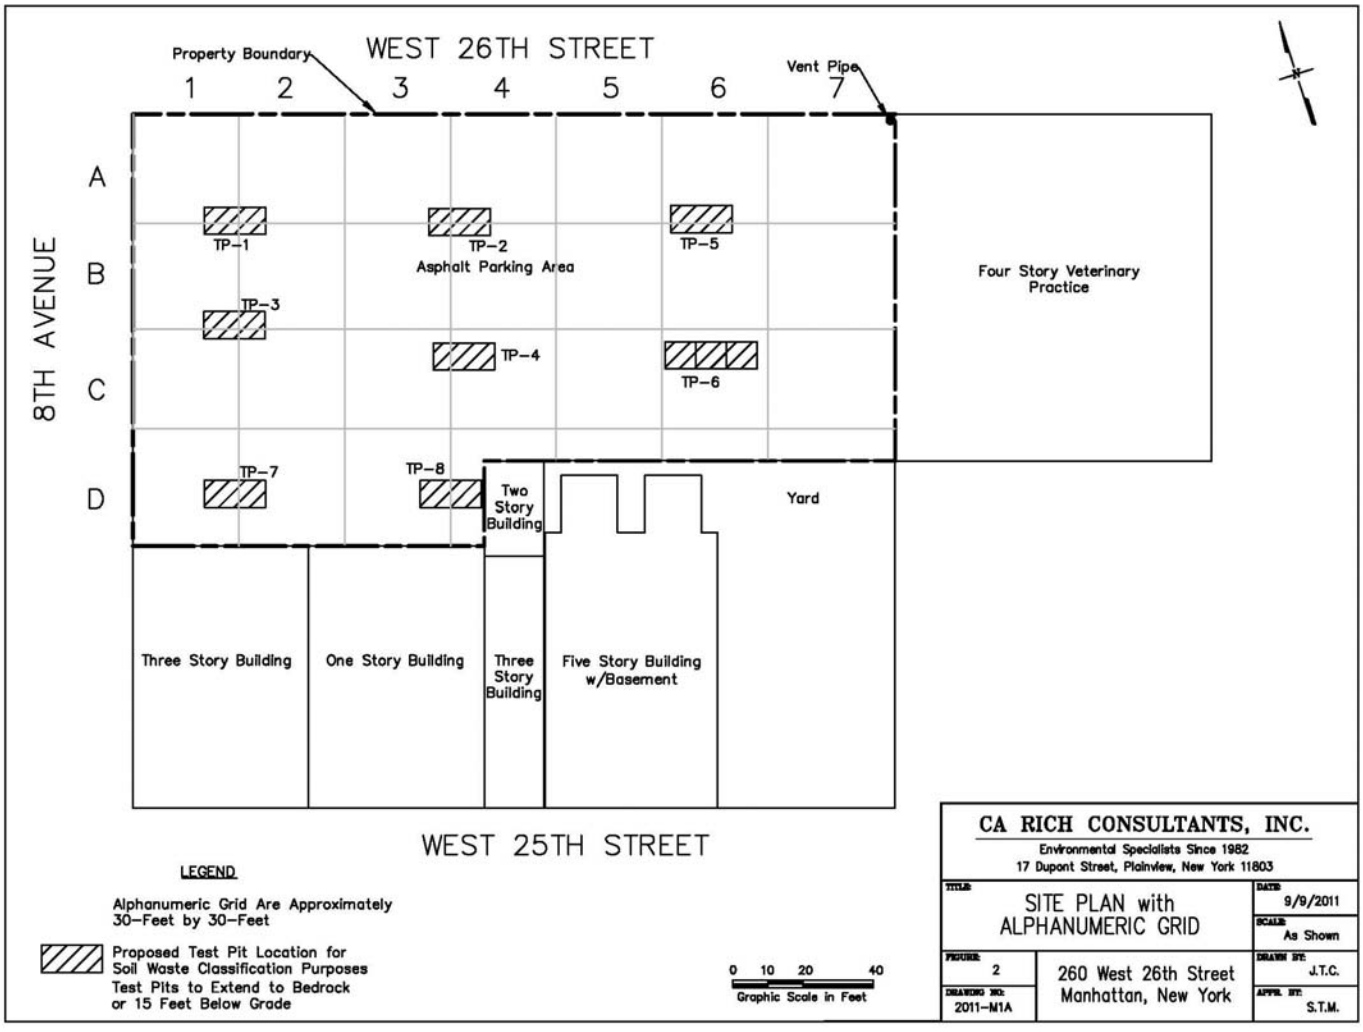

 File Name: _____

Photo Log

Photo 1 – Soil being excavated from grid C3.	
Photo 2 – Looking east across center of the site.	
Photo 3 – Looking west across site at remaining soil excavation. Note: the bottom of the eastern portion is bedrock with building materials stored on top of it.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Jessica Proscia of CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy	x	Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	12-28-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Soil excavation and off-site disposal from grids C3 and C4 was conducted today. A total of fourteen truckloads of soil were transported to the Soil Safe Facility in Logan Township, NJ.

Working In Grids #: C3, C4

Air Monitoring (Since Last Report):

Air Monitoring was conducted today by Jessica Proscia of CA RICH performed during today's soil excavation and loading activities. No problems were encountered.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings and foundation walls will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
					14	280						
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	255	Appr. 6,885	18	Appr. 450	24	Appr. 600	218	Appr. 5,625

Site Grid Map

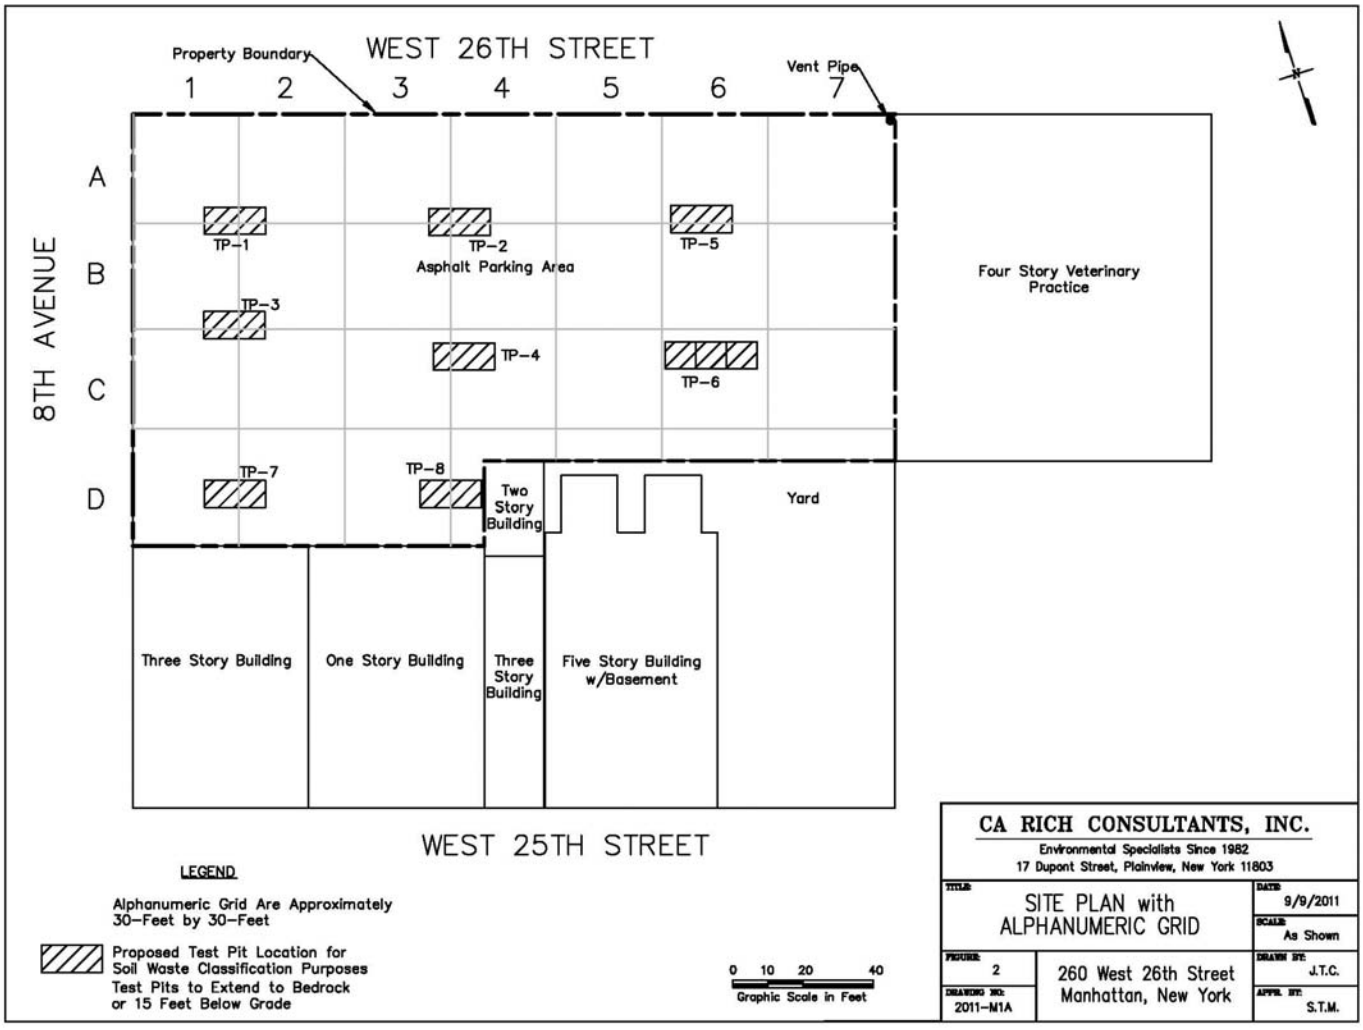

 File Name: _____

Photo Log

Photo 1 – Soil being excavated from grid C3.	
Photo 2 – View of the eastern portion of the Site.	
Photo 3 – View of southern wall at grid D3 and D4.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Jessica Proscia of CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy	x	Bright Sun	
TEMP.	TO 32	X	32-50		50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	12-29-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Soil excavation and off-site disposal from grids C3, C4, D1, and D2 was conducted today. A total of eight truckloads of soil were transported to the Soil Safe Facility in Logan Township, NJ.

Working In Grids #: C3, C4, D1, and D2

Air Monitoring (Since Last Report):

Air Monitoring was conducted today by Jessica Proscia of CA RICH performed during today's soil excavation and loading activities. No problems were encountered.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings and foundation walls will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
					8	160						
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	263	Appr. 7,045	18	Appr. 450	24	Appr. 600	218	Appr. 5,625

Site Grid Map

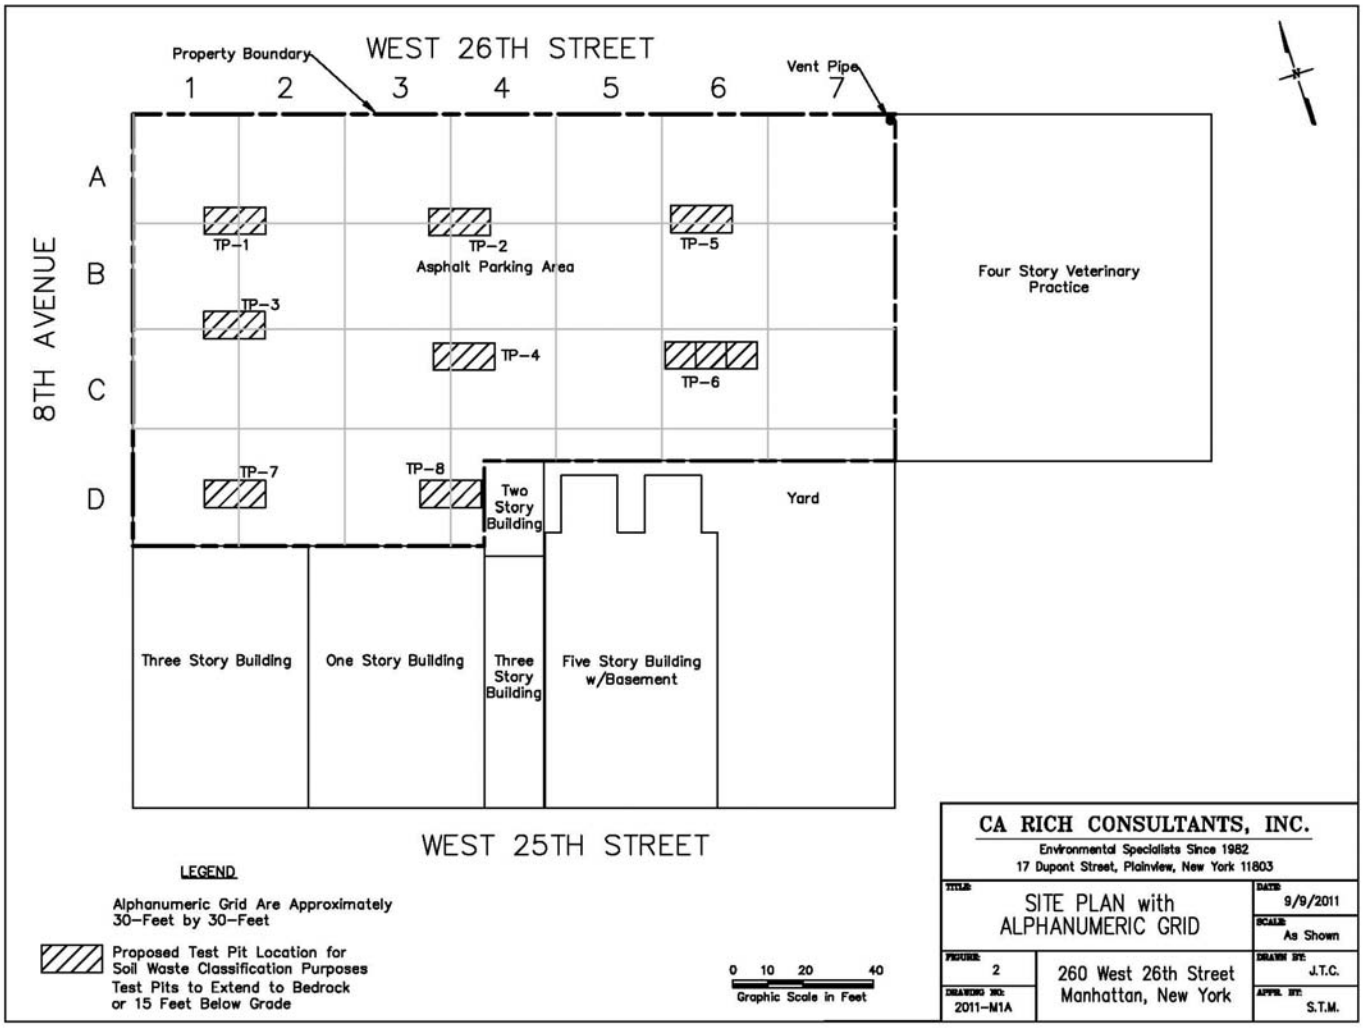

 File Name: _____

Photo Log

Photo 1 – Soil being excavated from grid C3.	
Photo 2 – View of the eastern portion of the Site.	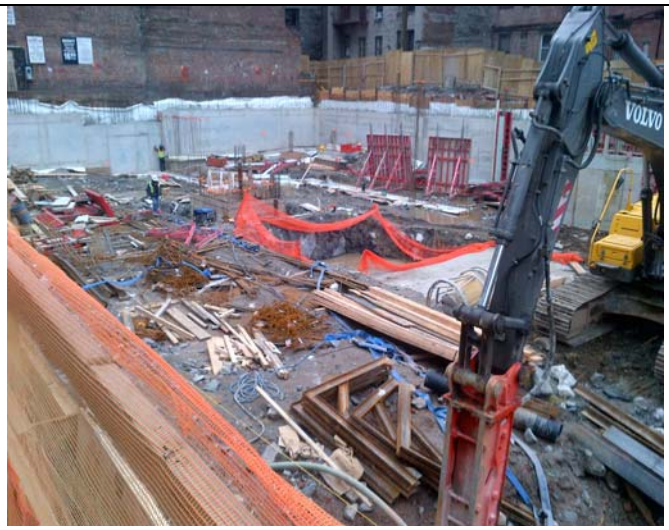
Photo 3 – View of southern wall at grids D1, D2, D3 and D4.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	12-30-11
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Additional Rebar was delivered to the site.

A raker was installed along the north foundation wall.

Rock Chopping continued along the South Property line and where future elevator pits will be installed.

Working In Grids #: B5, B6, C5, C6, D1, D2, D3

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings and foundation walls will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	263	Appr. 7045	18	Appr. 450	24	Appr. 600	246	Appr. 6150

Site Grid Map

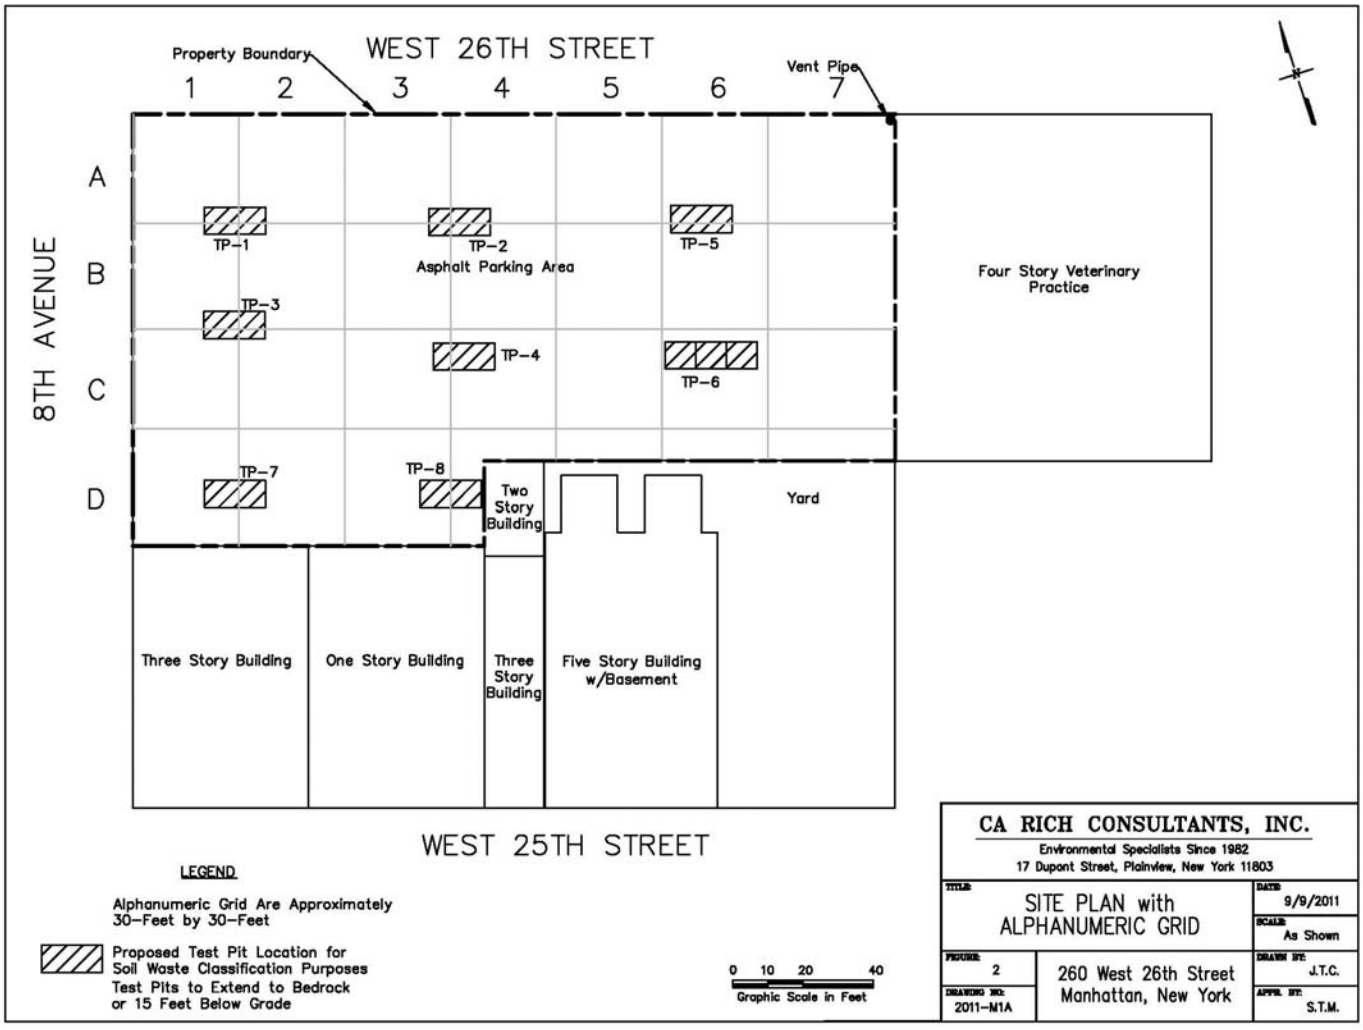

 File Name: _____

Photo Log

Photo 1 – Raker was installed along the North Foundation wall.	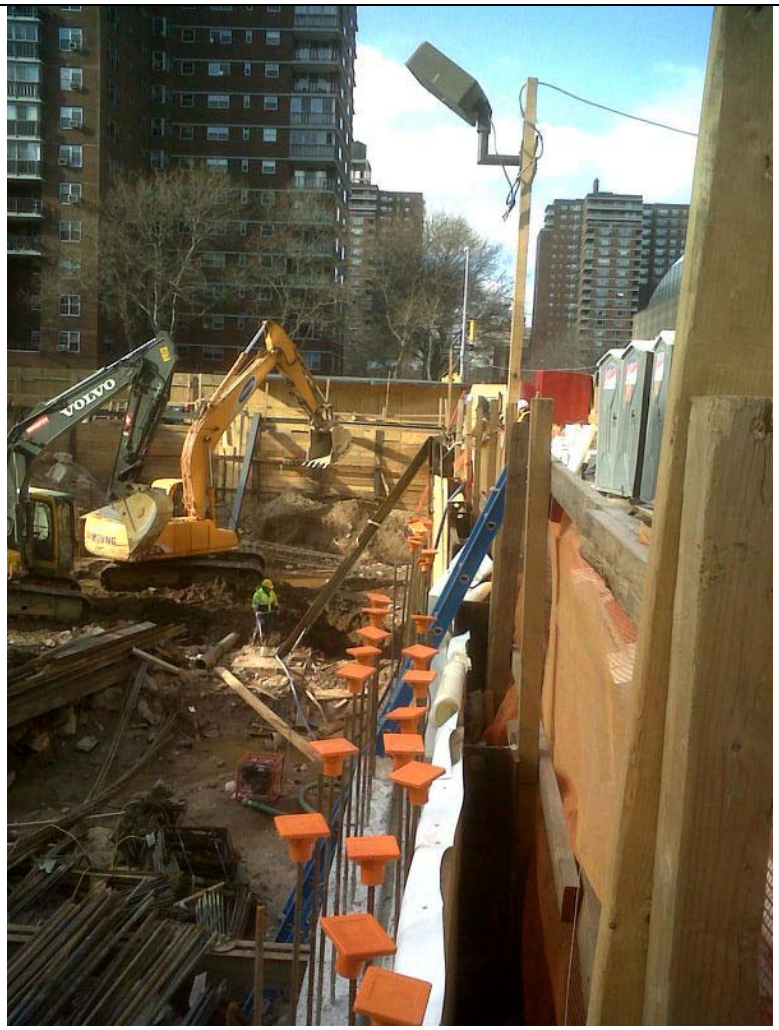

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32	X	32-50		50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	01-03-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Rebar was installed for Elevator 1 Pit.

Area was prepared along the South Property line for the wall footing to be installed tomorrow.

Rock Chopping continued along the South Property line and where the future ejector pit will be installed.

Working In Grids #: B5, B6, C5, D3, D4

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator and ejector pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	263	Appr. 7045	18	Appr. 450	24	Appr. 600	246	Appr. 6150

Site Grid Map

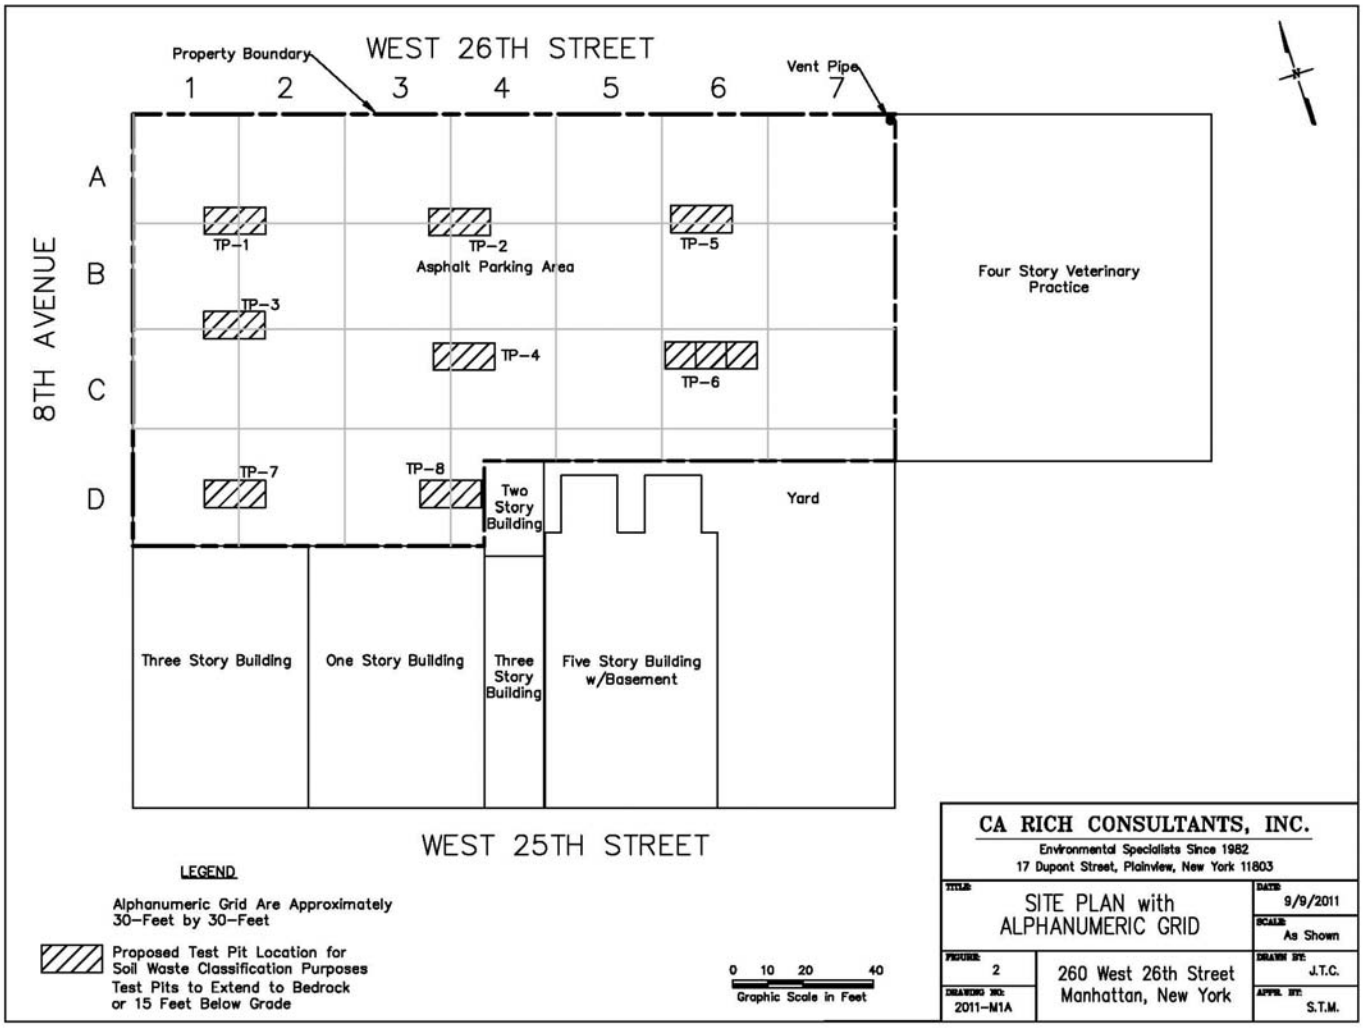

 File Name: _____

Photo Log

Photo 1 – Rebar was installed at the residential elevator pit. Contractor continued to chop rock for the future ejector pit to be installed.	
Photo 2 – Area along the south property line was prepared for the foundation wall footing to be installed tomorrow.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32	X	32-50		50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	01-04-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Lagging continued to be installed along the North wall.

Rock Chopping continued along the South Property line and where the future ejector pit will be installed.

Working In Grids #: A1, A2, A3, D3, D4

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator and ejector pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	263	Appr. 7045	18	Appr. 450	24	Appr. 600	246	Appr. 6150

Site Grid Map

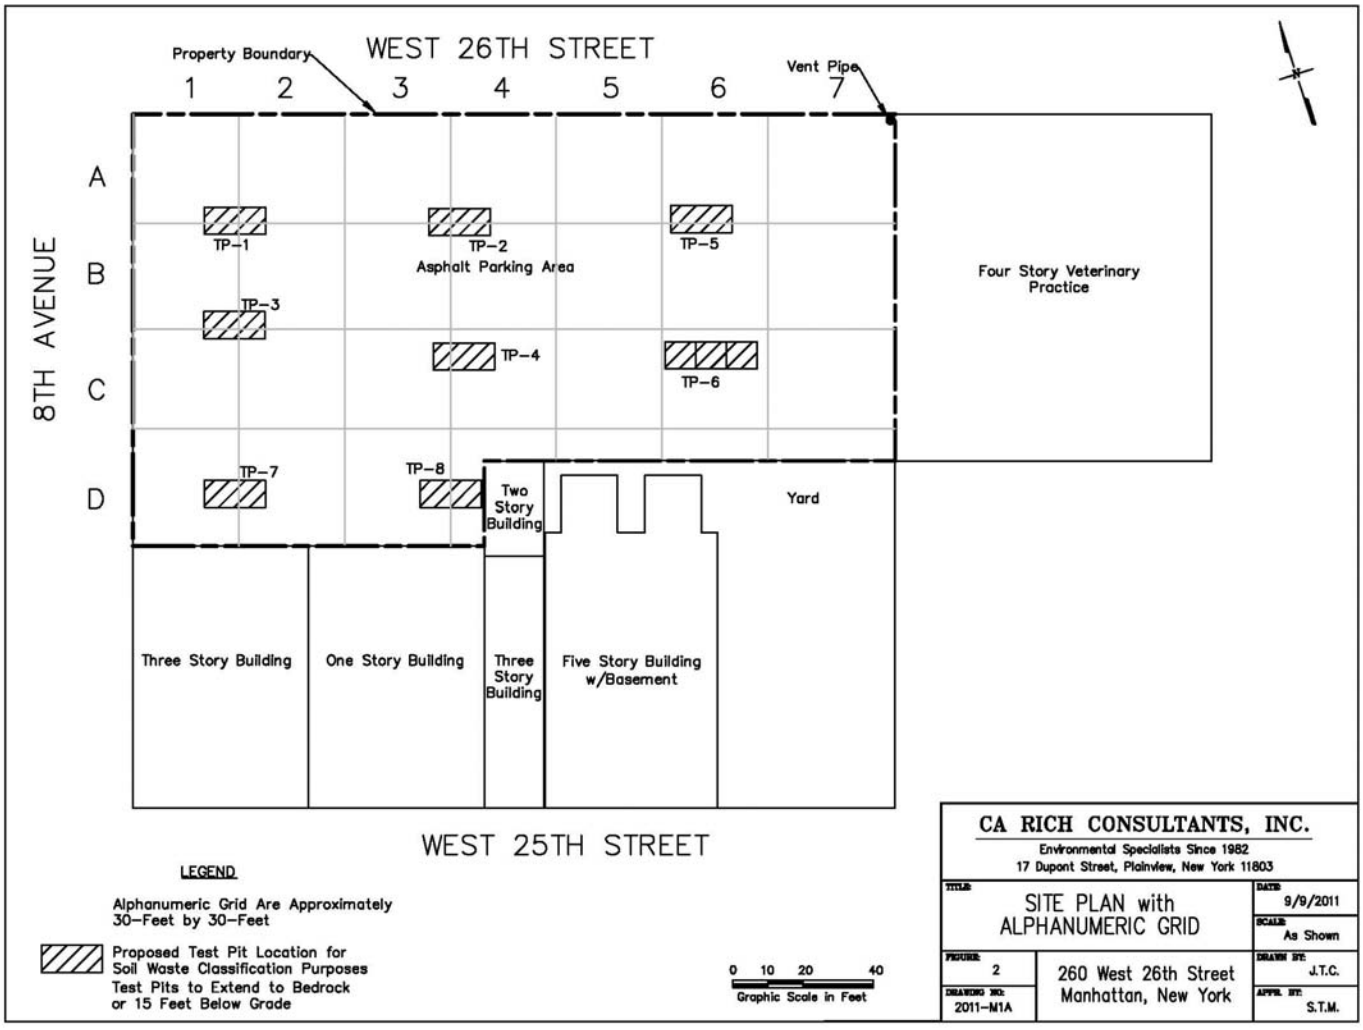

 File Name: _____

Photo Log

Photo 1 – Lagging continued along the North Foundation Wall.	
Photo 2 – The ejector pit continued to be rock chopped.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32	X	32-50		50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	01-05-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Lagging continued to be installed along the North wall.

Rock Chopping continued along the South Property line and where the future ejector pit will be installed.

Footings along the North Wall and the South Wall started to be formed.

Working In Grids #: A1, A2, A3, D3, D4

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator and ejector pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
											6	Appr. 150
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	263	Appr. 7045	18	Appr. 450	24	Appr. 600	252	Appr. 6300

Site Grid Map

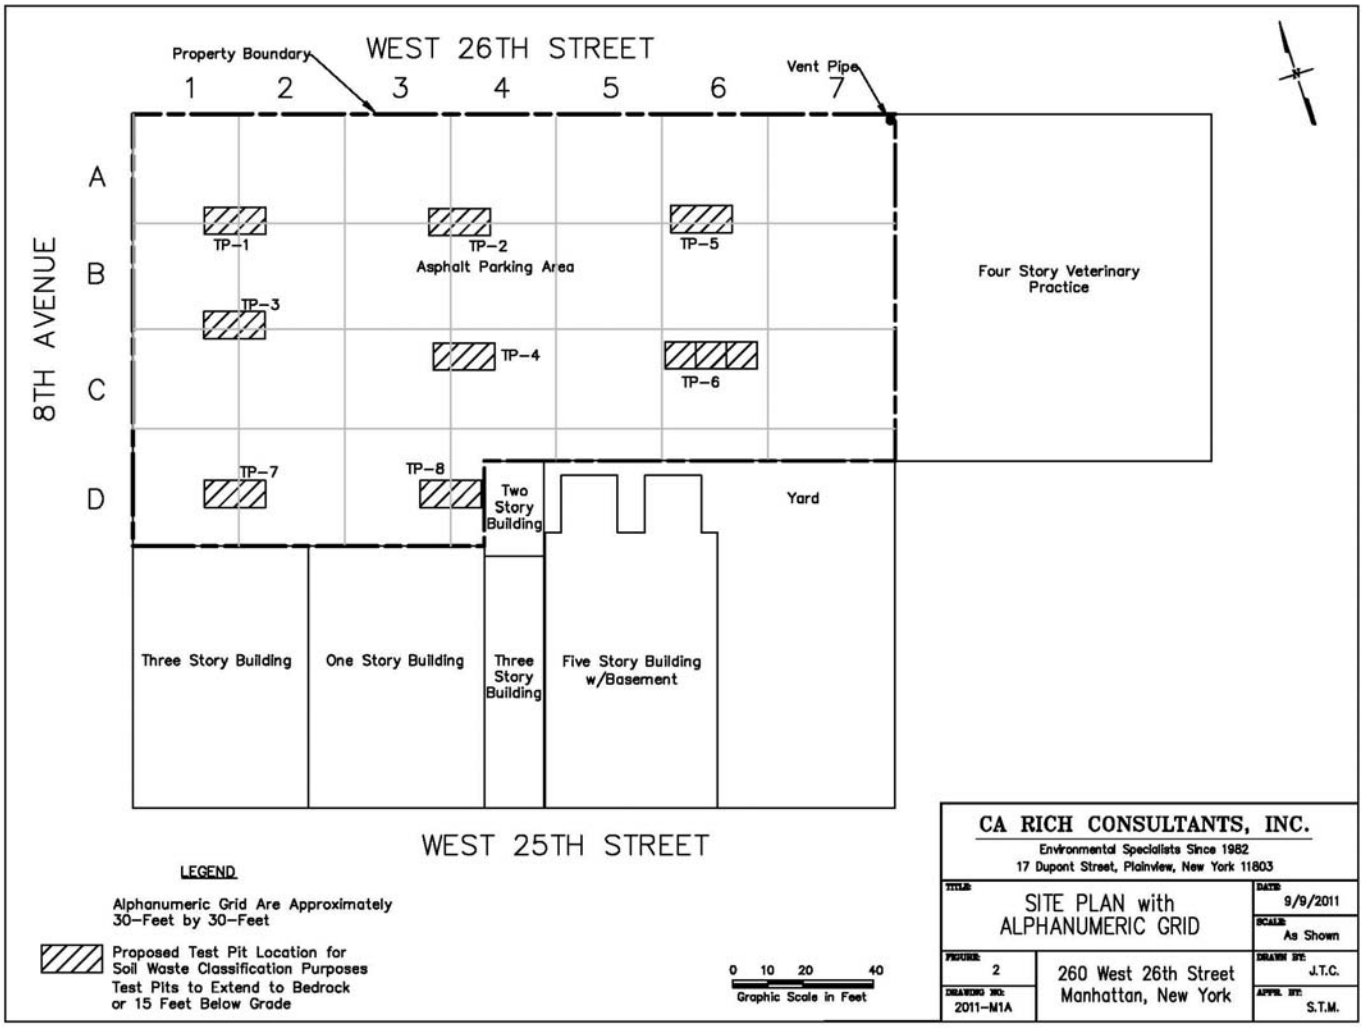

 File Name: _____

Photo Log

Photo 1 – Footings along the North Foundation wall beginning to be formed.	
Photo 2 – Workers finishing up rebar on Elevator Pit #1 Footing.	
Photo 3 – Workers installing lagging and forming concrete piers along the North Property Line.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	01-06-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Poured Elevator 4 Walls, Residential Elevators 1,2,3 Slab and Pier #8, 15, and 21 along the North Foundation Wall.

Working In Grids #: A4, A5, A6, B4, B5, B6

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator and ejector pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	263	Appr. 7045	18	Appr. 450	24	Appr. 600	252	Appr. 6300

Site Grid Map

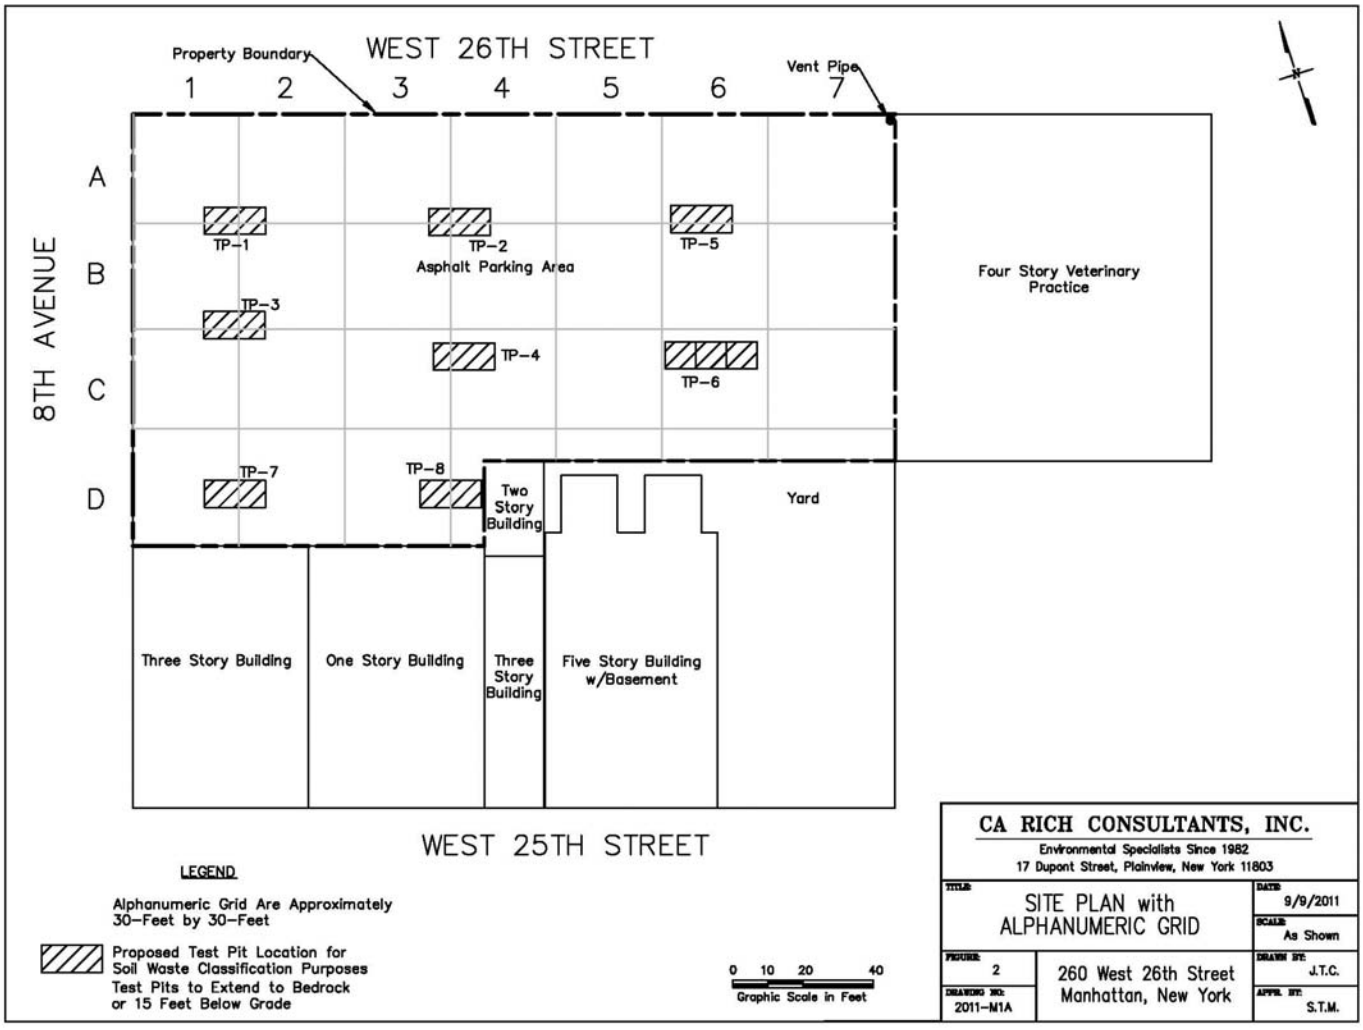

 File Name: _____

Photo Log

Photo 1 – Waterproofing and Rebar complete and ready for pour.	
Photo 2 – Elevator 1,2,3 Slab and Elevator 4 Walls ready for Pour.	
Photo 3 – Elevator 4 Walls being poured.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	01-07-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Danny Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Waterproofing was installed along the North Wall and North Wall footings.

Site was graded out in preparation for wall footings and column footings to be formed.

Concrete was poured along the rock of the south foundation wall to make a smooth surface so waterproofing could be installed properly.

Working In Grids #: A1, A2, A3, D2, D3, D4

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator and ejector pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	263	Appr. 7045	18	Appr. 450	24	Appr. 600	252	Appr. 6300

Site Grid Map

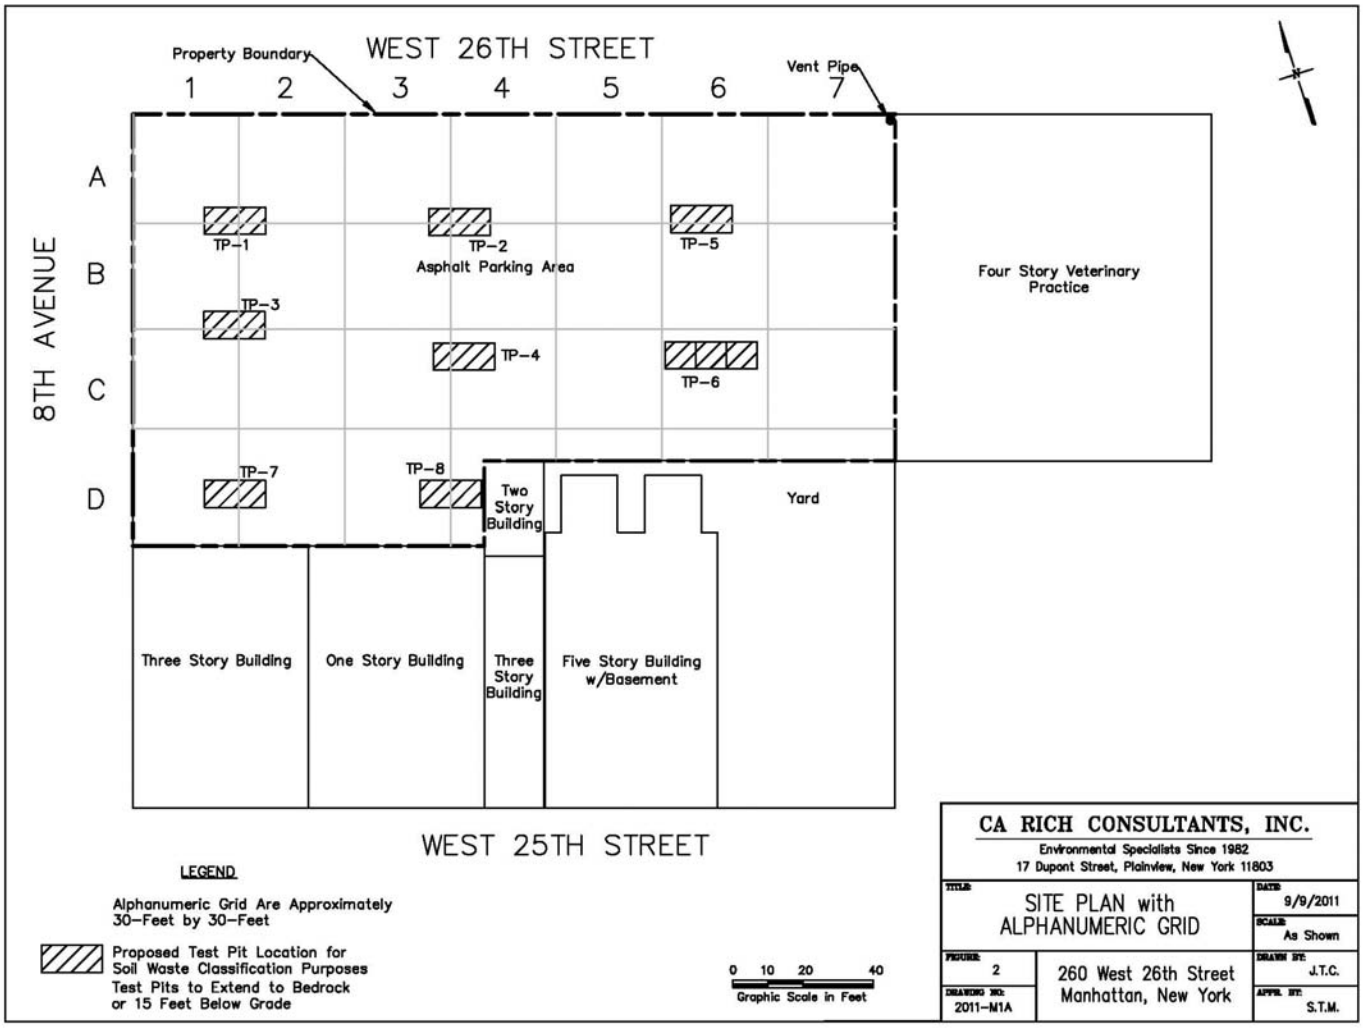

 File Name: _____

Photo Log

Photo 1- Area along south elevation was prepped and lean concrete was poured along jagged rock to make a smooth surface for waterproofing to be properly installed.	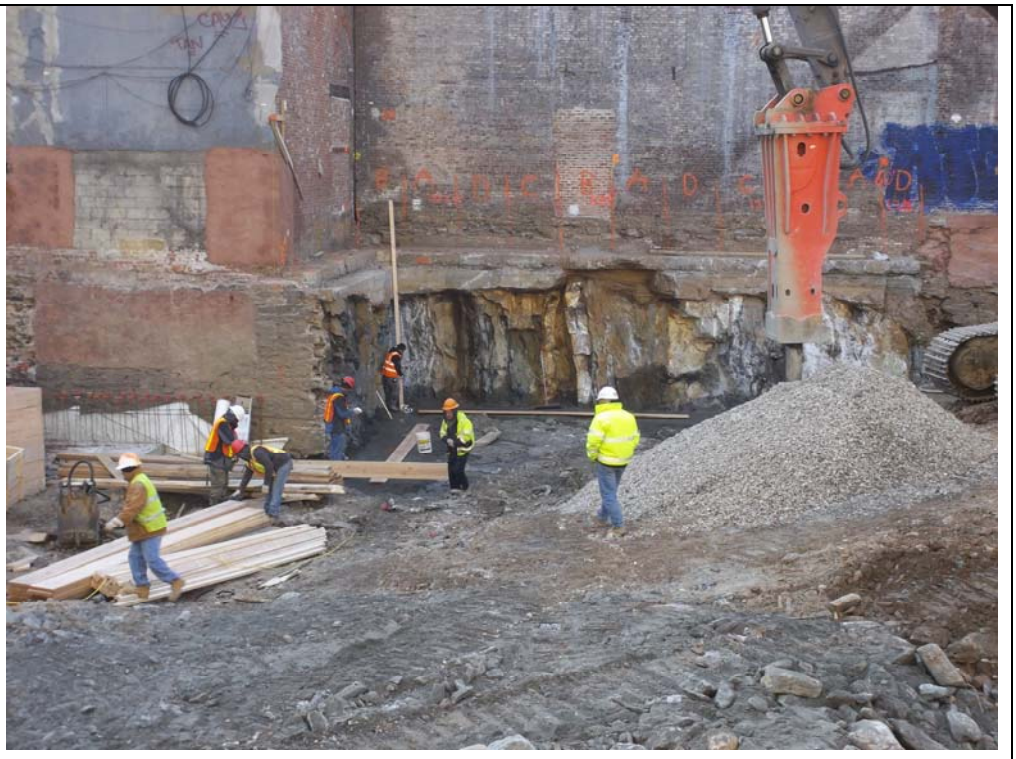

 File Name: _____

DAILY STATUS REPORT

Prepared By: Stephen Malinowski of

CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50		50-70	X	70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	01-09-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Soil excavation and off-site disposal from B1, B2, and C3 was conducted today. A total of nine truckloads of soil were transported to the Soil Safe Facility in Logan Township, NJ.

Working In Grids #: B1, B2, and C3

Air Monitoring (Since Last Report):

Air Monitoring was conducted today by Jessica Proscia of CA RICH performed during today's soil excavation and loading activities. No problems were encountered.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator and ejector pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
					9	225						
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	309	Appr. 7725	18	Appr. 450	24	Appr. 600	252	Appr. 6300

Site Grid Map

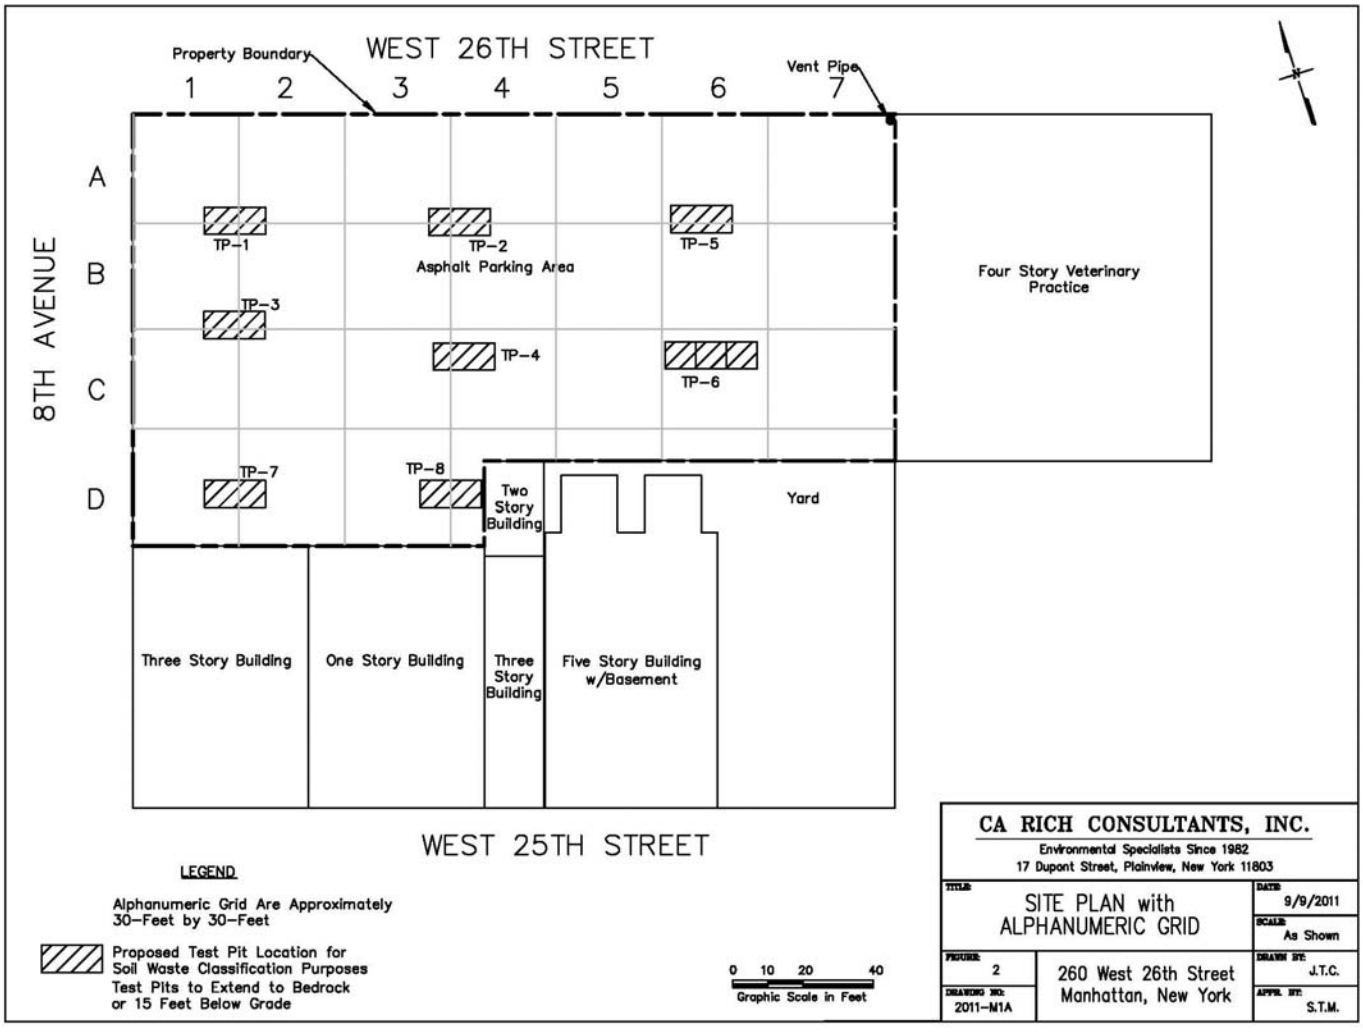

 File Name: _____

Photo Log

Photo 1- Soil Excavation in grid B-1.	
Looking southeast across site.	
Looking west-southwest across site. Construction ramp being removed.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Stephen Malinowski of

CA RICH

WEATHER	Snow		Rain		Overcast	X	Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	01-10-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Soil excavation and off-site disposal from grids B1 and B2 was conducted today. A total of twelve truckloads of soil were transported to the Soil Safe Facility in Logan Township, NJ.

The waterproofing membrane was installed around an elevator pit and along the northern site wall.

A soil sample for volatile organic compounds was collected to provide required analytical data for ongoing shipments to the Soil Safe Facility.

Working In Grids #: B1 and B2

Air Monitoring (Since Last Report):

Air Monitoring was conducted today by Jessica Proscia of CA RICH performed during today's soil excavation and loading activities. No problems were encountered.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator and ejector pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
					12	300					3	75
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	321	Appr. 7725	18	Appr. 450	24	Appr. 600	255	Appr. 6375

Site Grid Map

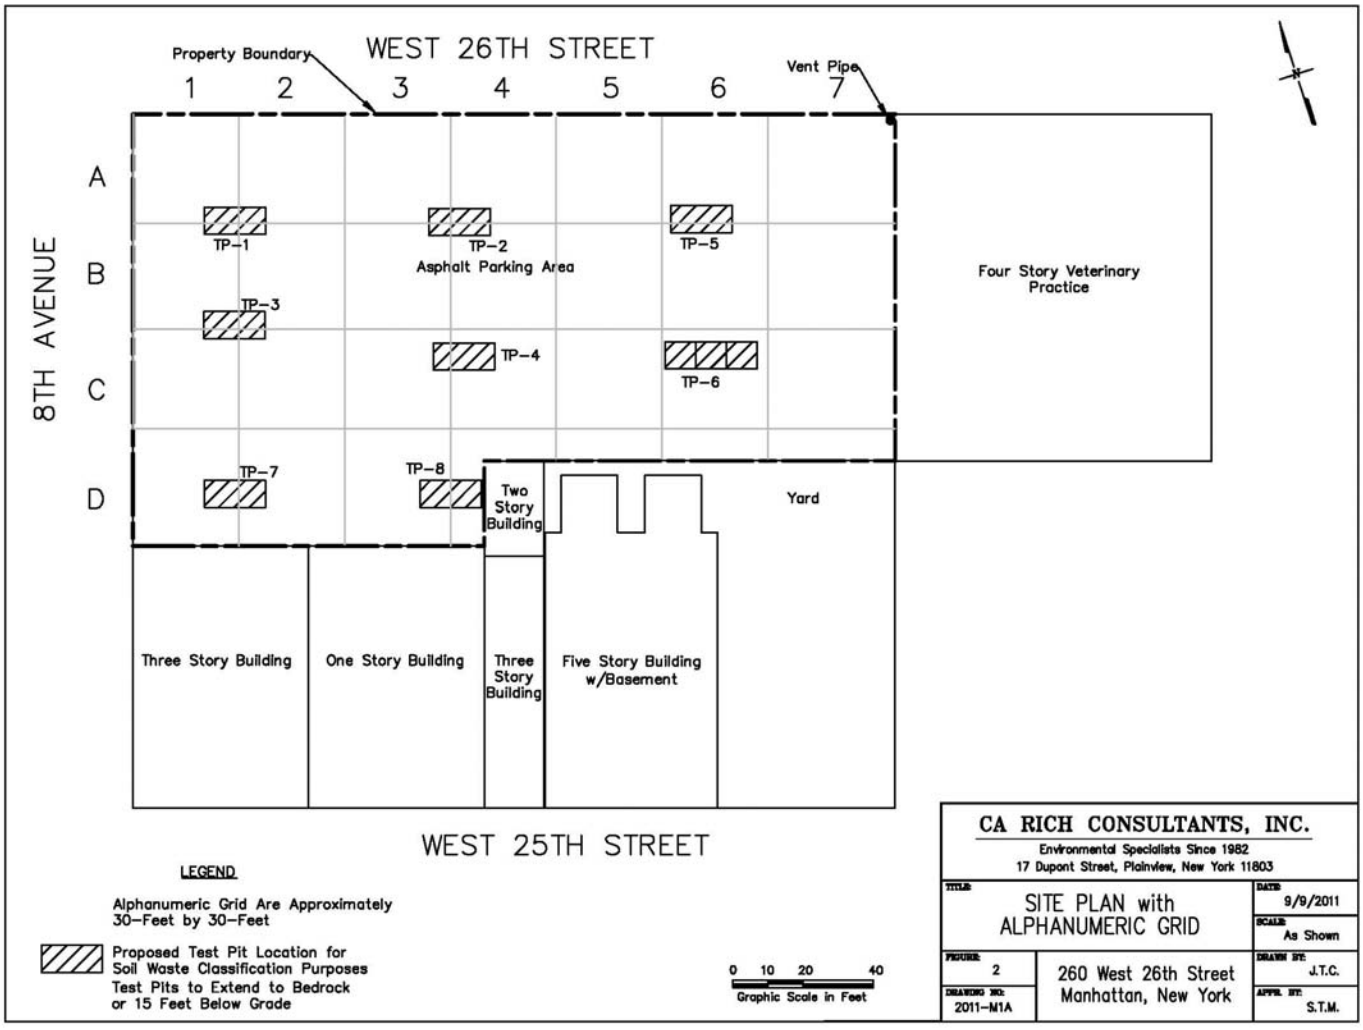

 File Name: _____

Photo Log

Photo 1- Looking east across site.	
Waterproofing membrane along northern wall.	
Elevator pit with Grace Bituthene waterproofing membrane and protection board.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Stephen Malinowski of

CA RICH

WEATHER	Snow		Rain		Overcast	X	Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	01-11-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Soil excavation and off-site disposal from grids C2 and C3 was conducted today. A total of seven truckloads of soil were transported to the Soil Safe Facility in Logan Township, NJ.

The waterproofing membrane was installed along portions of the southern and northern walls of the property.

Four loads of bedrock were removed from grids D1 and D2 and transported to the Red Rock Facility.

Working In Grids #: C2, C3 and D1 and D2

Air Monitoring (Since Last Report):

Air Monitoring was conducted today by Jessica Proscia of CA RICH performed during today's soil excavation and loading activities. No problems were encountered.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator and ejector pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
					7	175					4	100
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	321	Appr. 7900	18	Appr. 450	24	Appr. 600	259	Appr. 6475

Site Grid Map

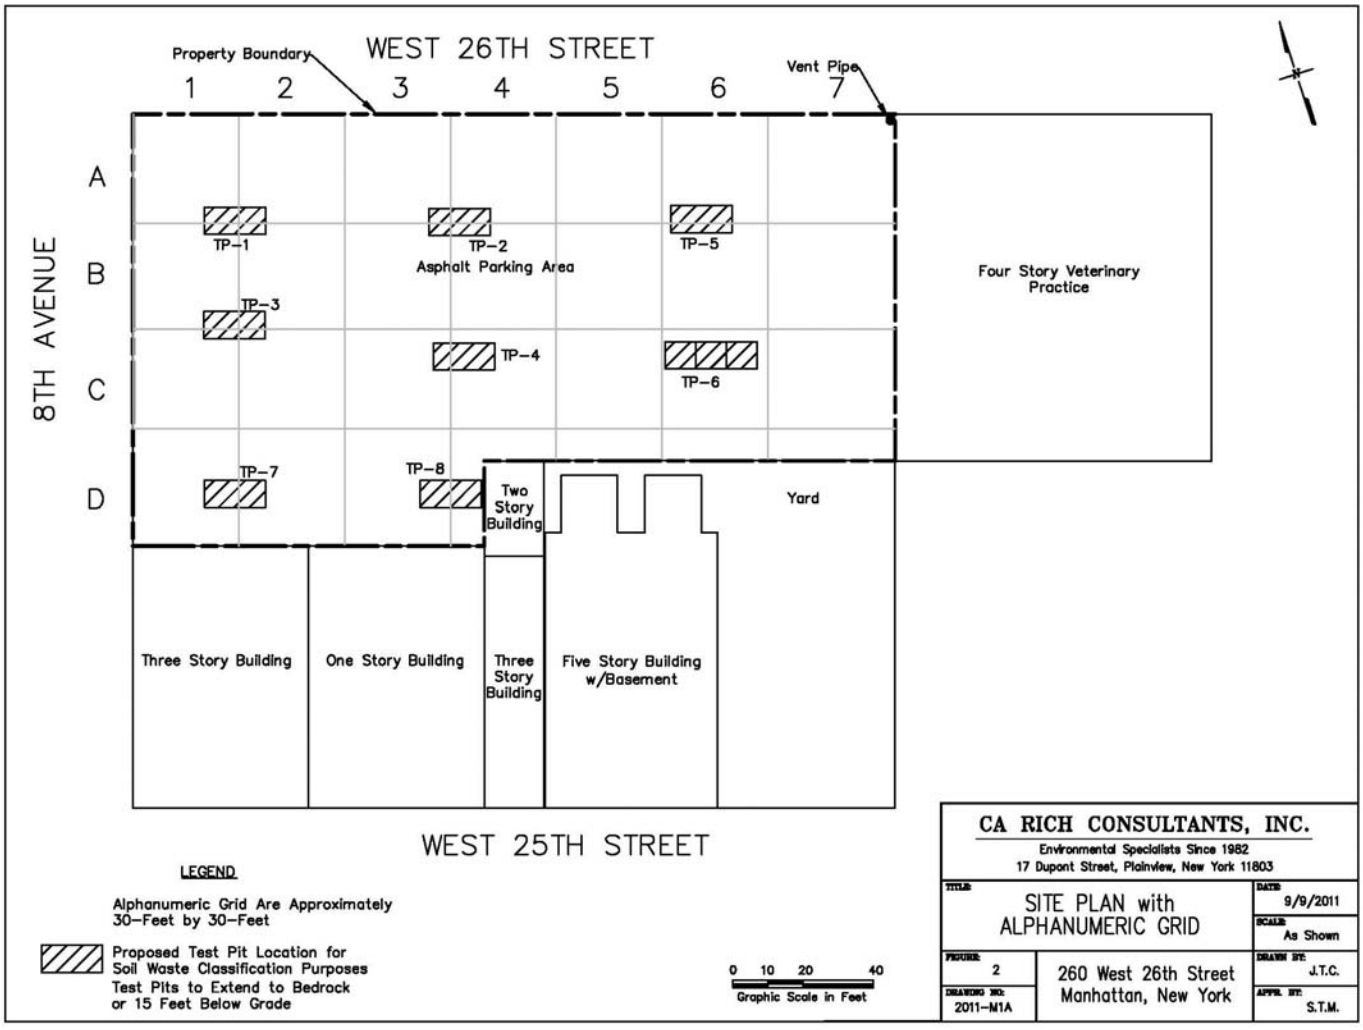

 File Name: _____

Photo Log

Photo 1- Soil excavation of construction ramp.	
Soil excavation of construction ramp.	
Water-proofing membrane along southern property boundary.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Stephen Malinowski of

CA RICH

WEATHER	Snow		Rain	X	Overcast		Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	01-12-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Soil excavation and off-site disposal from grids C2 and C3 was conducted today. A total of eight truckloads of soil were transported to the Soil Safe Facility in Logan Township, NJ.

Endpoint sampling in the northwestern portion of the site is scheduled for tomorrow.

Working In Grids #: C2 and C3

Air Monitoring (Since Last Report):

Air Monitoring was conducted today by Jessica Proscia of CA RICH performed during today's soil excavation and loading activities. No problems were encountered. It was not necessary to take dust readings due to rain. There were no complaints or elevated PID readings.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator and ejector pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
					8	200						
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	329	Appr. 8100	18	Appr. 450	24	Appr. 600	259	Appr. 6475

Site Grid Map

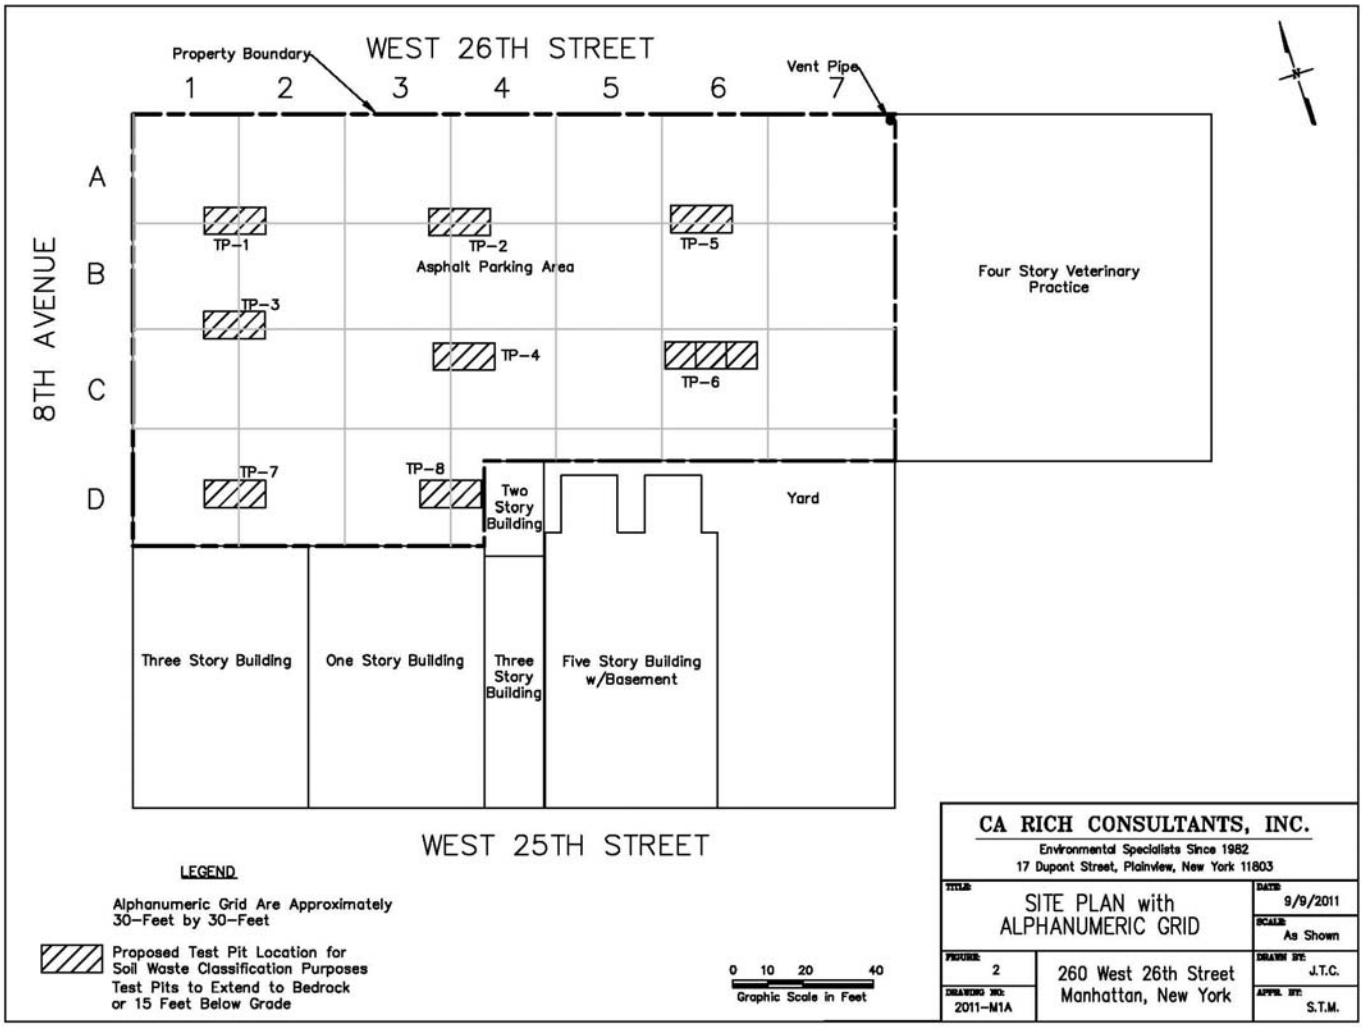

 File Name: _____

Photo Log

Photo 1- Looking east across site.	
Soil excavation of construction ramp.	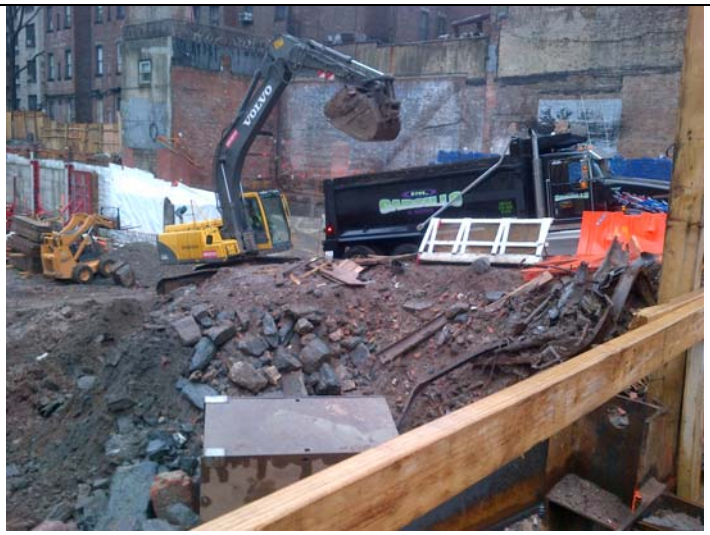
Looking west across site.	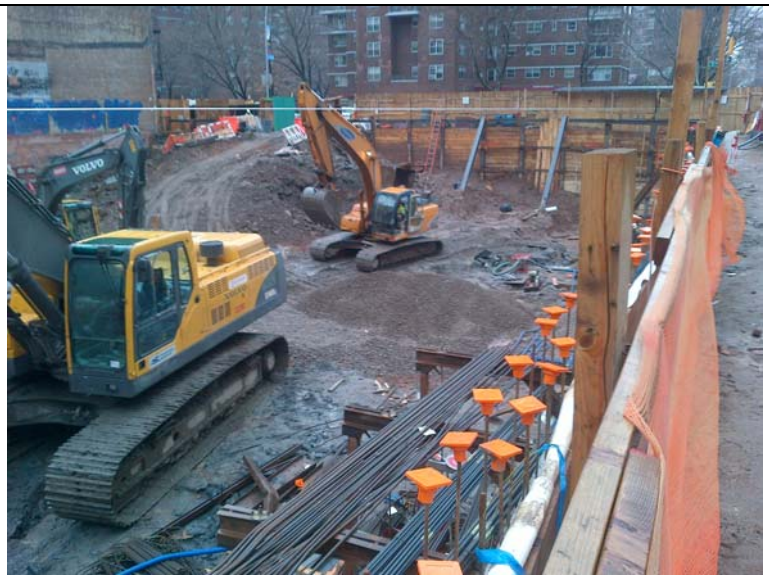

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	01-13-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

In accordance with the approved endpoint sampling plan, CA RICH Consultants collected soil endpoints samples from portions of the foundation excavation where the final depth has been achieved and is not composed of bedrock. Specifically, the samples were collected from grid A-1, A-3 and B-2 to document the residual concentration of SVOCs, metals and pesticides at the base of the excavation in that area of the site. An additional grab sample was collected from grid B-2 for the CP-51 list of volatile organic compounds to provide analytical data to allow OER/DEC to close out the spill. The samples are being shipped to Accutest Laboratories for 48 hour rush results analysis. Upon receipt of the results (hopefully late next Wednesday) a comparison to unrestricted standards (Track 1) will be performed to determine if the excavation in that portion of the site can be deemed complete.

Waterproofing was installed along the North and South Foundation Walls. Two footblocks were poured so two diagonal rakers could be installed along 8th Ave. on Monday. A 2" thick lean concrete slab approx. 5'-0"x5'-0" was poured at the location of the ejector pit so waterproofing could be installed. Rebar was completed and MEVA forms were set into place along the North Wall in preparation for them to be poured on Monday.

Working In Grids #: A1, A2, A3, B1, C1, D3, D4, B2

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:
Construction team will continue to install waterproofing, rebar, formwork, and pour footings, foundation walls, and elevator and ejector pits. The last area of the site requiring excavation is the construction ramp. We anticipate additional endpoint sampling in grids C-1 and C3 after the ramp has been removed in approximately 2-weeks.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	329	Appr. 8100	18	Appr. 450	24	Appr. 600	259	Appr. 6475

Site Grid Map

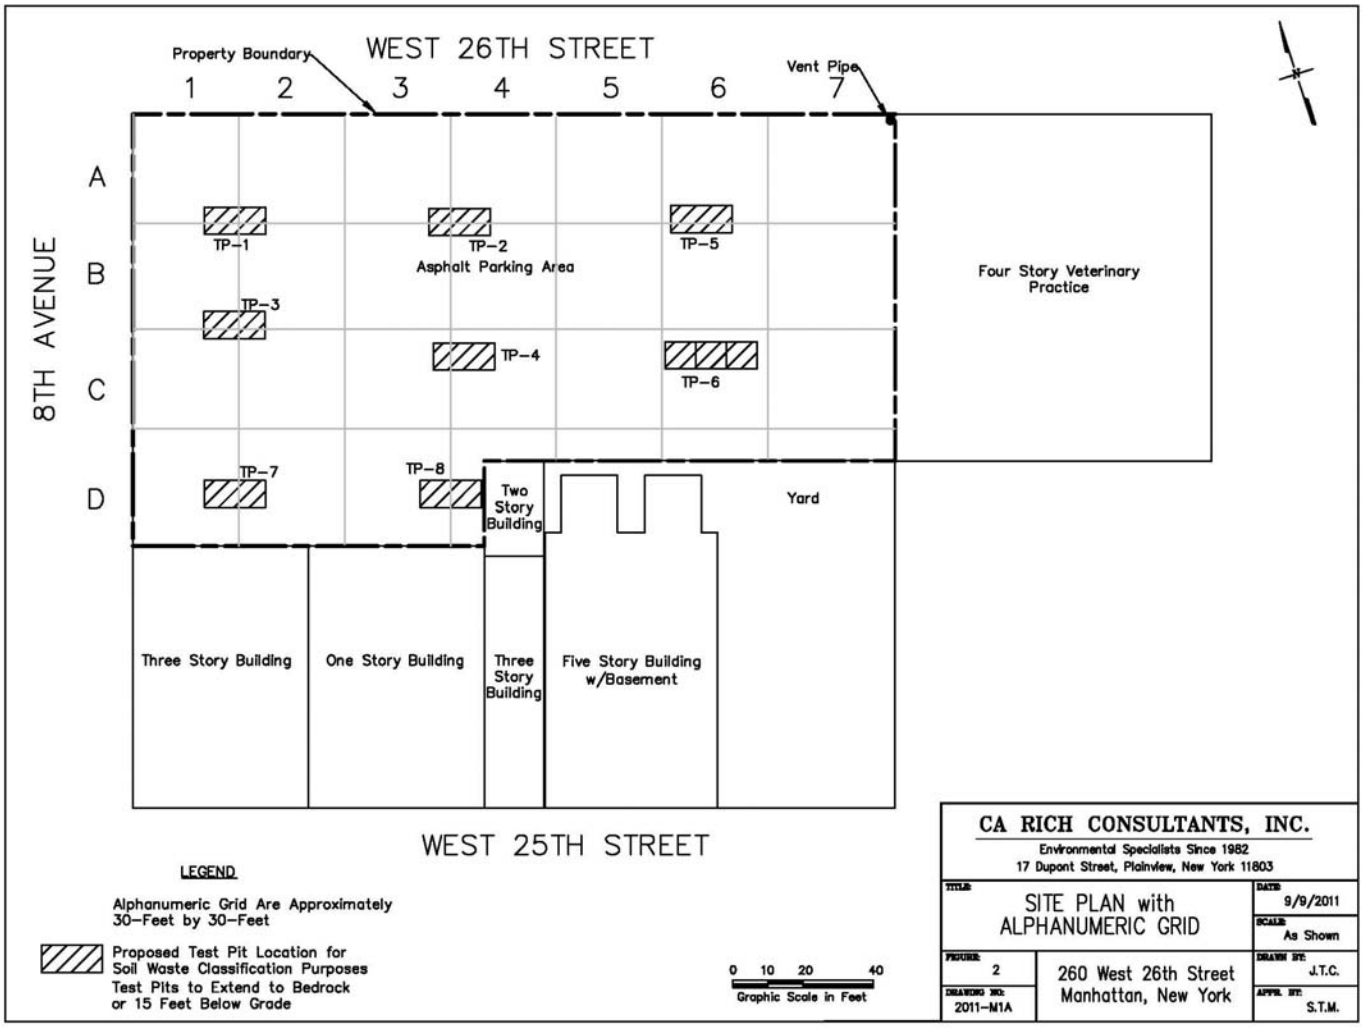

 File Name: _____

Photo Log

Photo 1- Waterproofing was installed along the South Foundation Wall.	
Photo 2- Waterproofing and rebar was installed along the North wall and Formwork was set in place in preparation for Monday's pour..	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	01-14-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

An additional steel raker was installed along the West Foundation Wall.

Rebar continued to be installed along the North Foundation Wall and Forms were set in place in preparation for the remaining section of the North Wall to be poured next week.

Working In Grids #: A1, A2, A3, D1

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:
Construction team will continue to install waterproofing, rebar, formwork, and pour footings, foundation walls, and elevator and ejector pits. The last area of the site requiring excavation is the construction ramp. We anticipate additional endpoint sampling in grids C-1 and C3 after the ramp has been removed in approximately 2-weeks.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	329	Appr. 8100	18	Appr. 450	24	Appr. 600	259	Appr. 6475

Site Grid Map

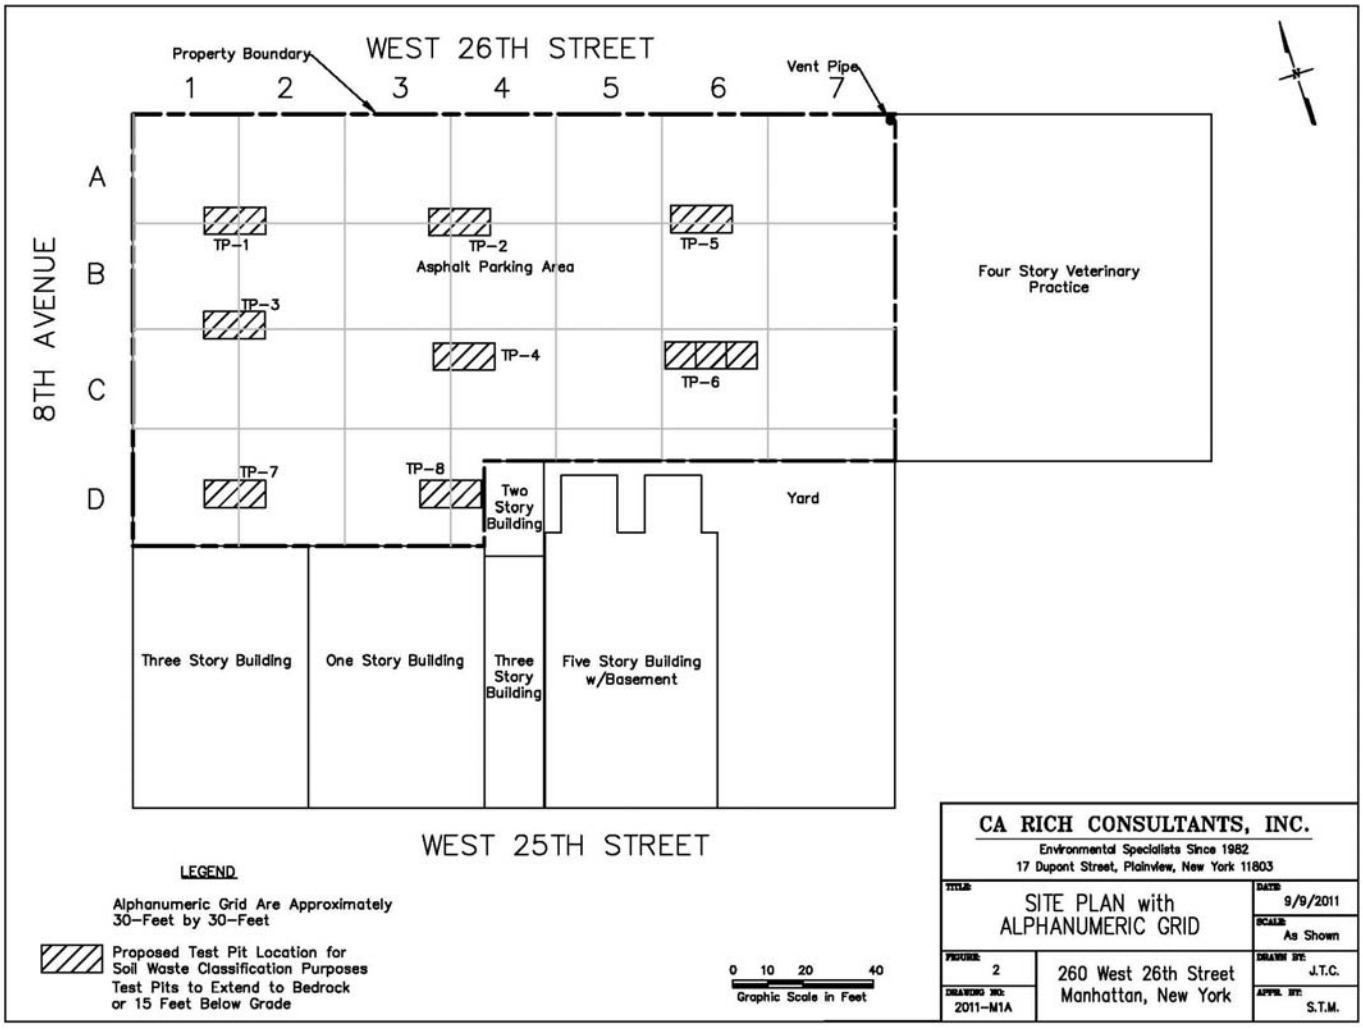

 File Name: _____

Photo Log

Photo 1- Rebar continued to be installed along the North Foundation wall.	
Photo 2- A third raker was installed along the west property line.	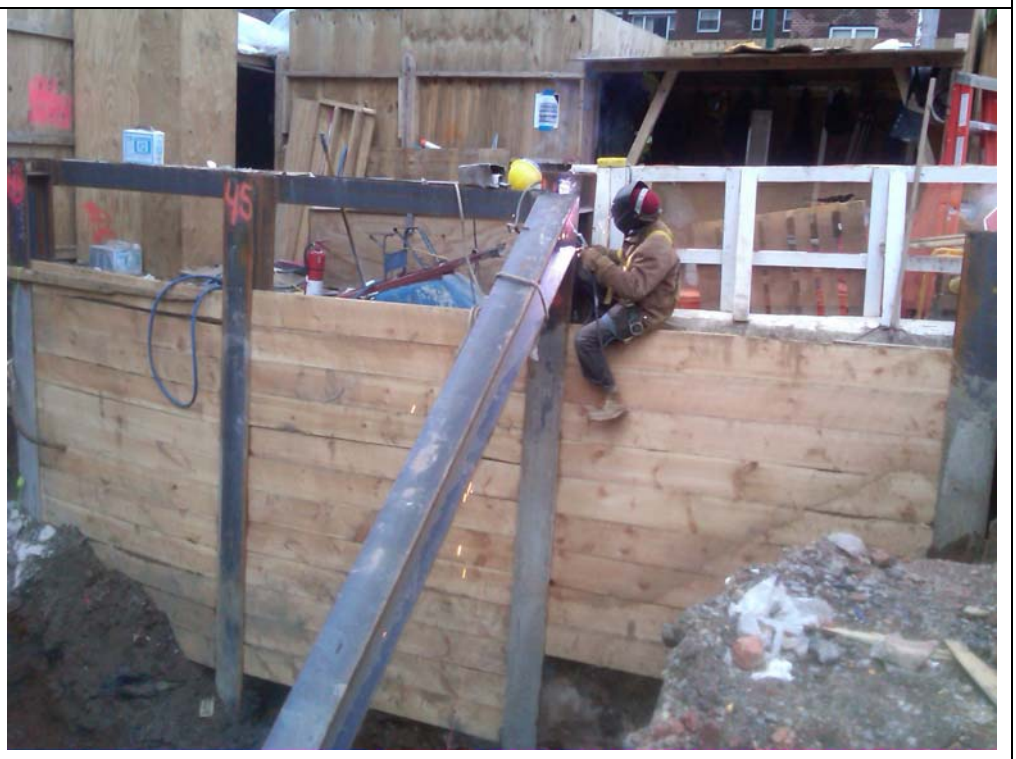

 File Name: _____

DAILY STATUS REPORT

Prepared By: Jessica Proscia of

CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32	X	32-50		50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	01-16-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Soil excavation and off-site disposal from grids C2 and C3 was conducted today. A total of five truckloads of soil were transported to the Soil Safe Facility in Logan Township, NJ.

The waterproofing membrane was installed along portions of the southern wall of the property.

Rock chopping continued in grids D1, and D2 with two truckloads of rock being shipped off-site for disposal at Red Roc Materials in Lyndhurst, NJ.

Working In Grids #: C2 and C3

Air Monitoring (Since Last Report):

Air Monitoring was conducted today by Jessica Proscia of CA RICH performed during today's soil excavation and loading activities. No problems were encountered. There were no complaints or elevated PID readings.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator and ejector pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.
					5	125					2	50
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	334	Appr. 8225	18	Appr. 450	24	Appr. 600	261	Appr. 6525

Site Grid Map

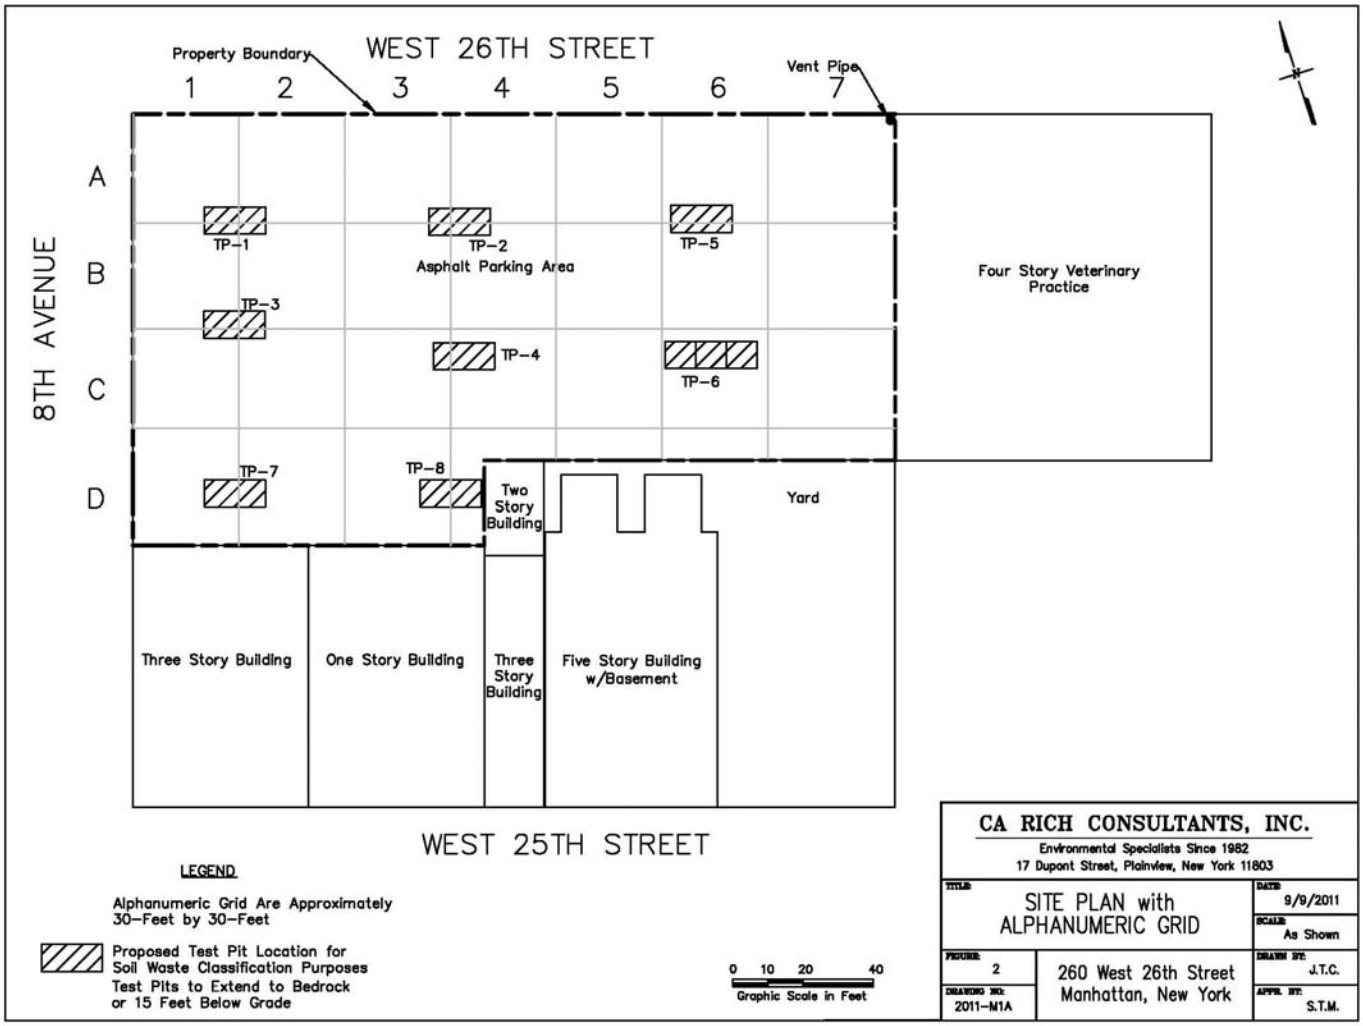

 File Name: _____

Photo Log

Photo 1- Water-proofing membrane along southern property boundary.	
Soil excavation of construction ramp.	
Looking west across site.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast	X	Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	01-17-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc. Contractor: Chelsea W26 LLC	Safety Officer: Jessica Proscia Alternate Safety Officer: Dan Manore

Work Activities Performed (Since Last Report):

Rebar and Formwork were completed along the North wall and the contractor poured 115'-0" of the North Foundation Wall, 2 Piers along the West Elevation, the ejector pit slab, a column footing, and a 25'-0" long interior foundation wall.

Working In Grids #: A1, A2, A3, C6, C7, A5

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	334	Appr. 8225	18	Appr. 450	24	Appr. 600	259	Appr. 6525

Site Grid Map

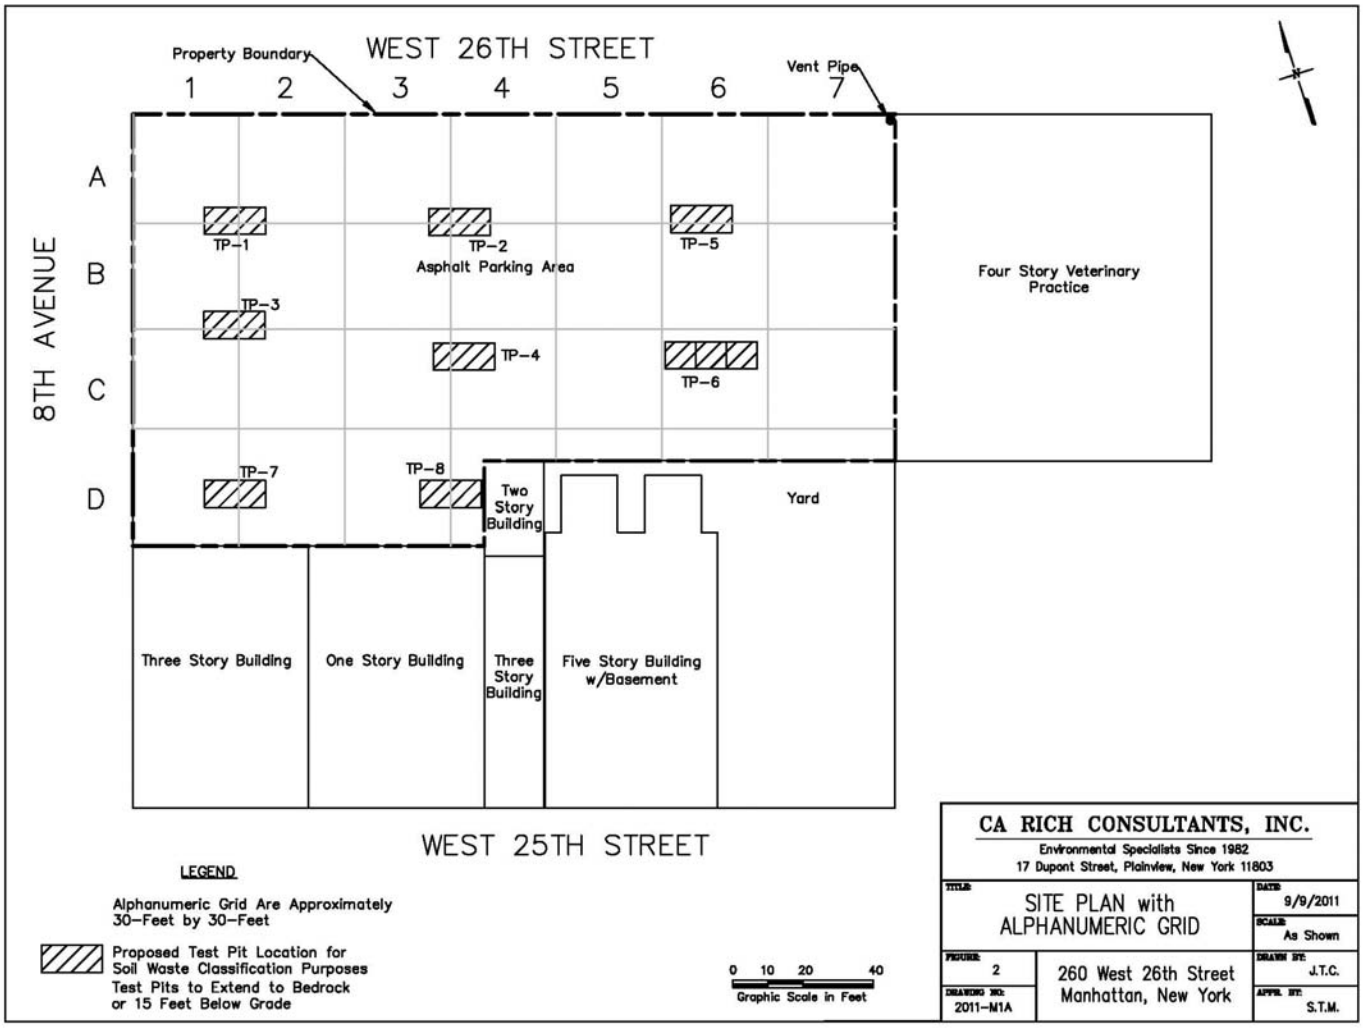

 File Name: _____

Photo Log

Photo 1- Workers installing scaffolding at North Wall in preparation for wall to be poured.	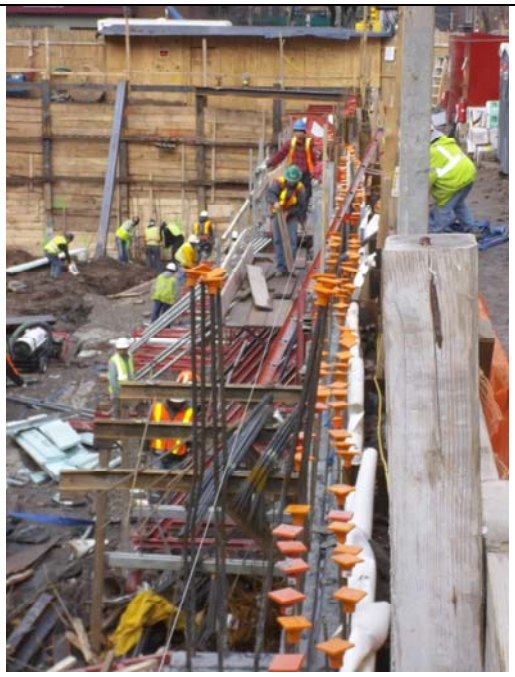
Photo 2- Formwork and Scaffolding completed for interior wall at the future ramp location to be poured.	
Photo 3 – Column Footing in Southeast corner of the site was properly installed and inspected and is ready for concrete pour.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	01-18-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Formwork was installed for column footings in the northwest corner of the site, the west wall footings, and Stair A Footing. Rebar was installed along the south wall and the ejector pit walls. Formwork was stripped from the interior ramp wall and waterproofing was installed along the west wall footing.

Working In Grids #: A1, B1, D3, D4, A6, A7, B6, B7

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	334	Appr. 8225	18	Appr. 450	24	Appr. 600	259	Appr. 6525

Site Grid Map

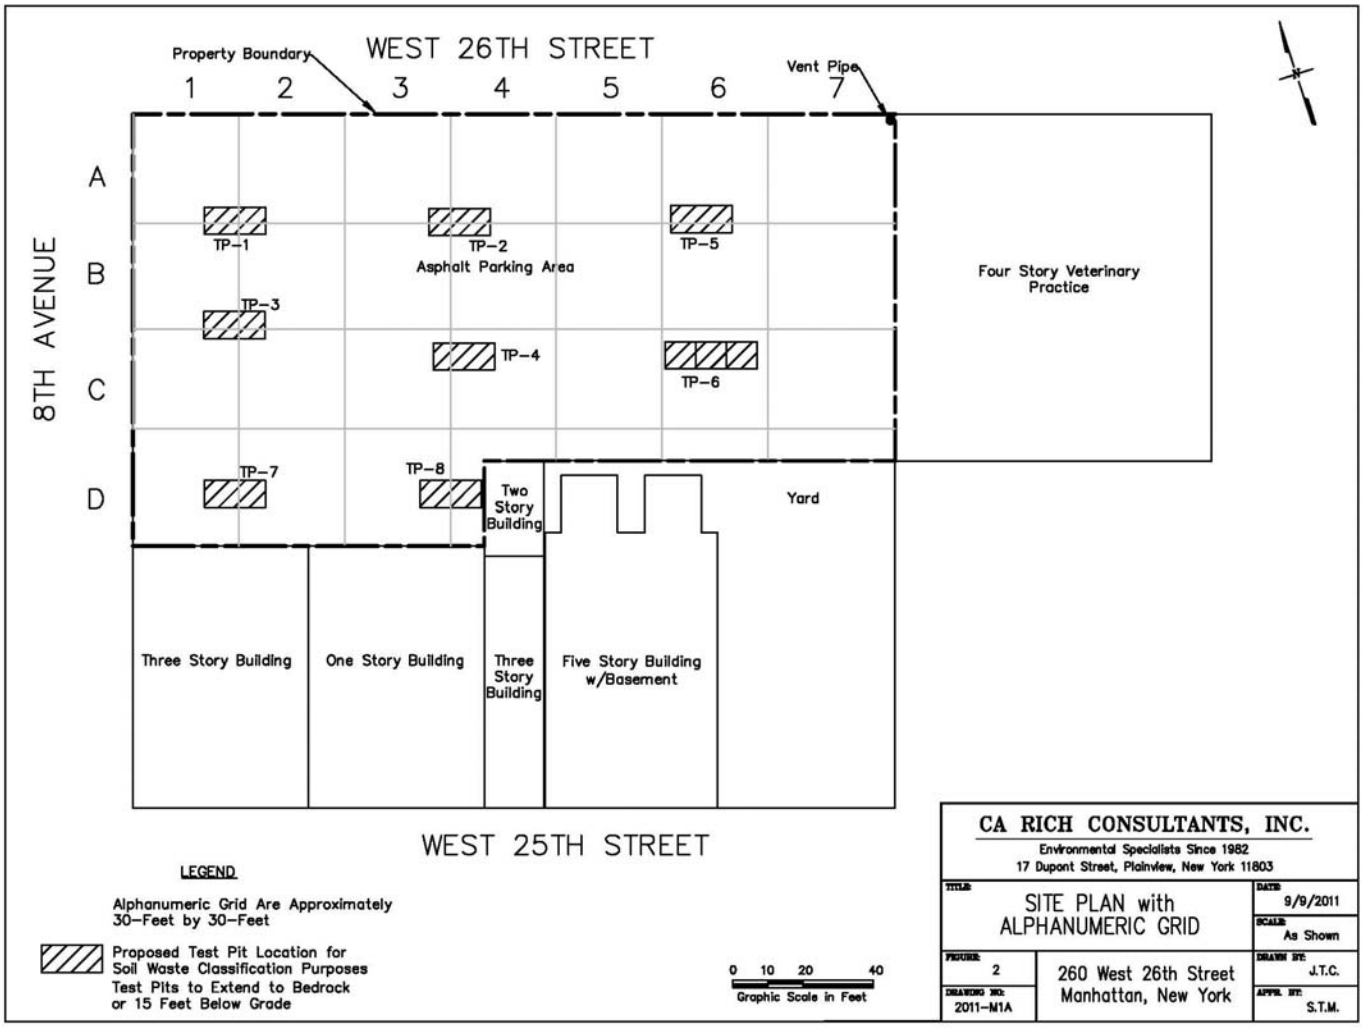

 File Name: _____

Photo Log

Photo 1- Rebar installed for Ejector Pit.	
Photo 2- Formwork installed for Stair A Footing	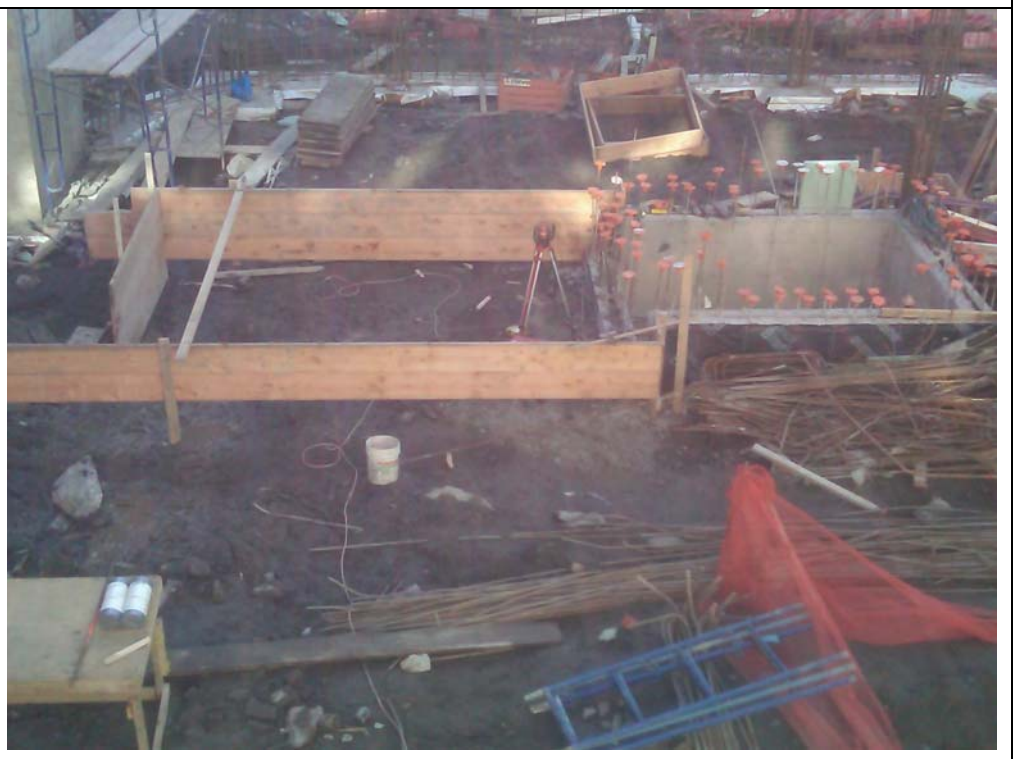

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32	X	32-50		50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	01-19-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Formwork was installed for 5 column footings on the Northeast half of the site and for the ejector pit. Rebar was installed along the South Wall and in the Stair A Footing. Waterproofing was installed along the West foundation wall footing.

Working In Grids #: A1, B1, D3, D4, A6, A7, B6, B7

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	334	Appr. 8225	18	Appr. 450	24	Appr. 600	259	Appr. 6525

Site Grid Map

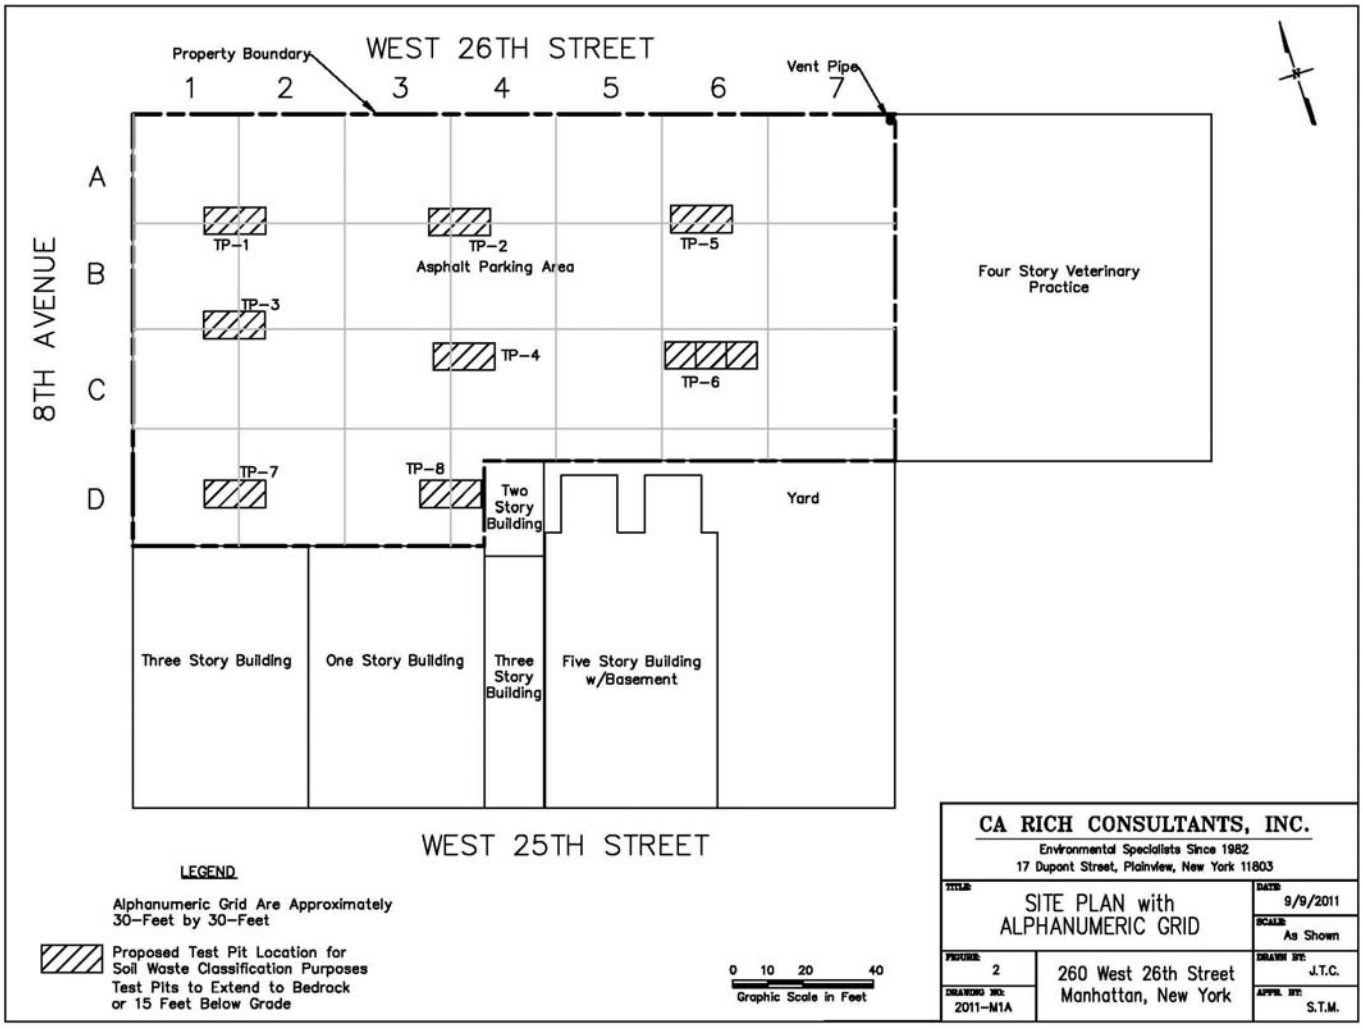

 File Name: _____

Photo Log

Photo 1- Waterproofing was installed along the west foundation wall.	
Photo 2- Formwork was installed for the Ejector Pit Walls	
Photo 3- South foundation wall rebar was installed.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32	X	32-50		50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	01-20-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

The following concrete was poured today: West Wall Footing, Ejector Pit Walls, Stair A Footing, a small section of the ramp wall, and Column Footings #54 and #90.

Rebar was completed along the south wall.

Working In Grids #: A1, B1, D3, D4, A6, A7, B6, B7

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	334	Appr. 8225	18	Appr. 450	24	Appr. 600	259	Appr. 6525

Site Grid Map

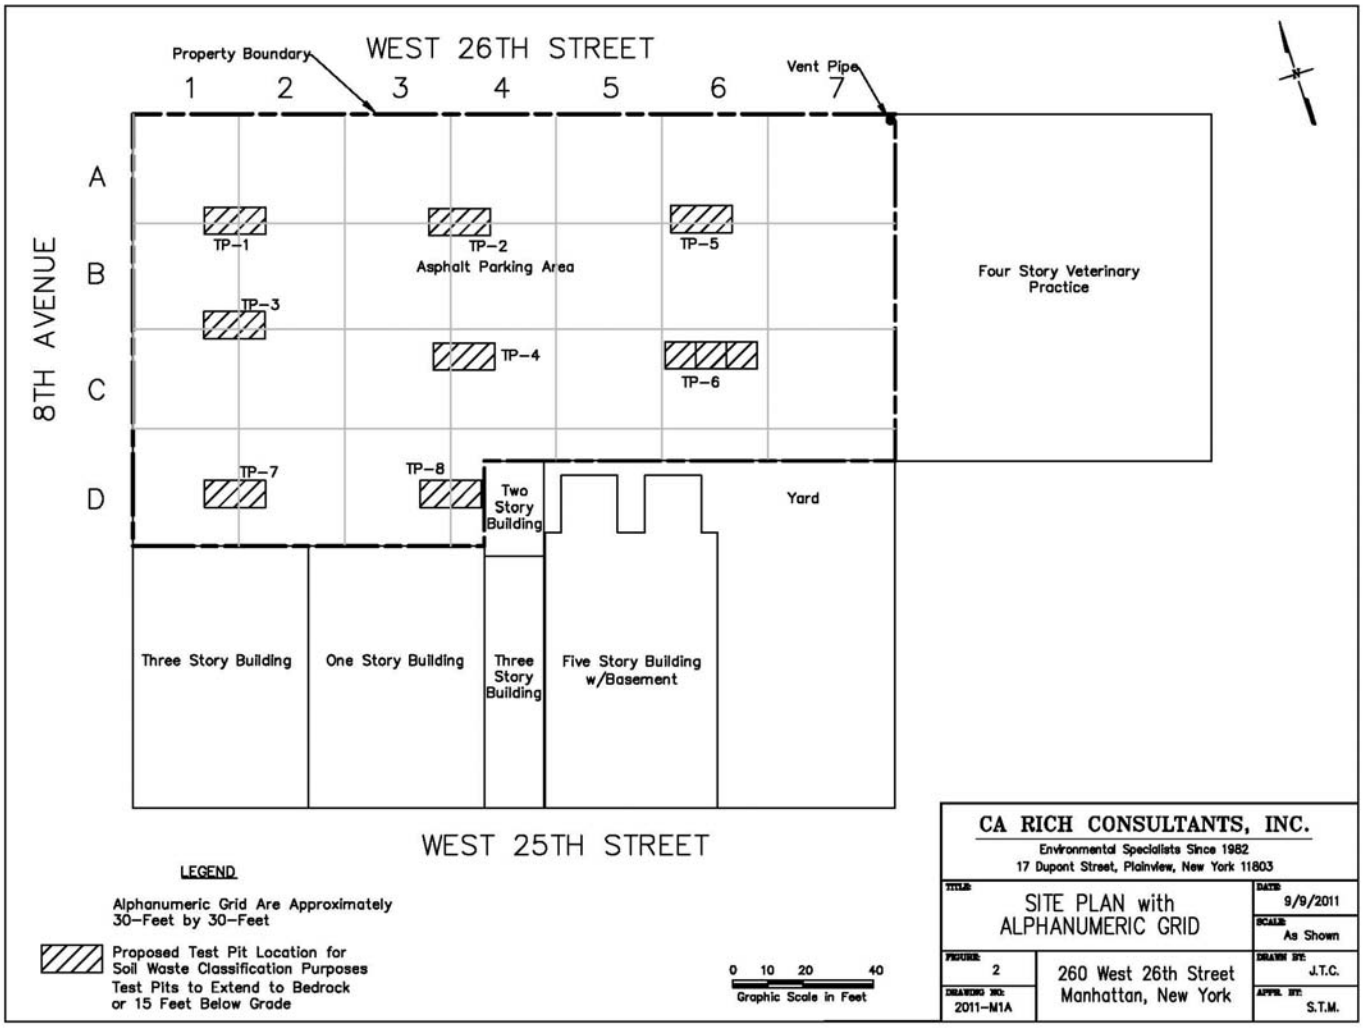

 File Name: _____

Photo Log

Photo 1- Ejector Pit walls were poured.	
Photo 2- Lower portion of the interior ramp wall was poure.	
Photo 3- West Footing was poured.	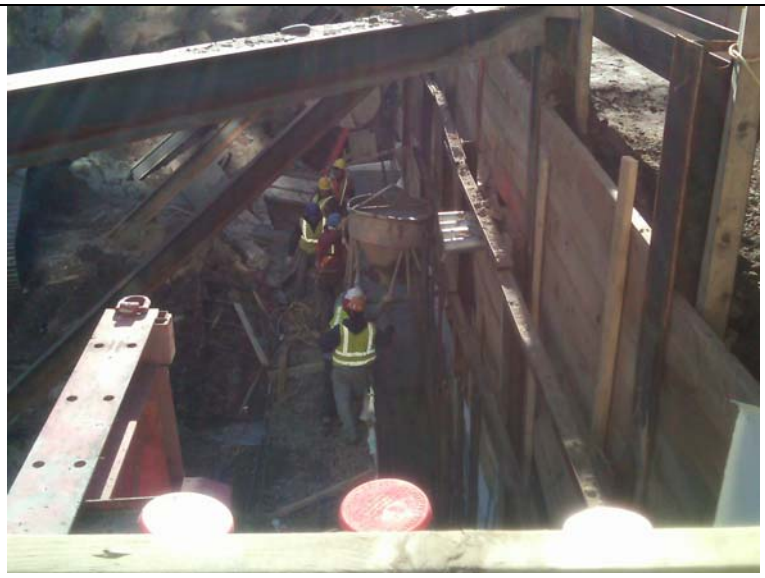

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow	X	Rain		Overcast		Partly Cloudy		Bright Sun	
TEMP.	TO 32	X	32-50		50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	01-21-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Meva Formwork was installed along the South Property Line in preparation to be poured on Monday. Waterproofing was installed along the West Property Line.

Working In Grids #: D4, A1, B1

Air Monitoring (Since Last Report):

Air Monitoring was not performed today, no excavation occurred. Monitoring will resume when soil excavation activities resume.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	334	Appr. 8225	18	Appr. 450	24	Appr. 600	259	Appr. 6525

Site Grid Map

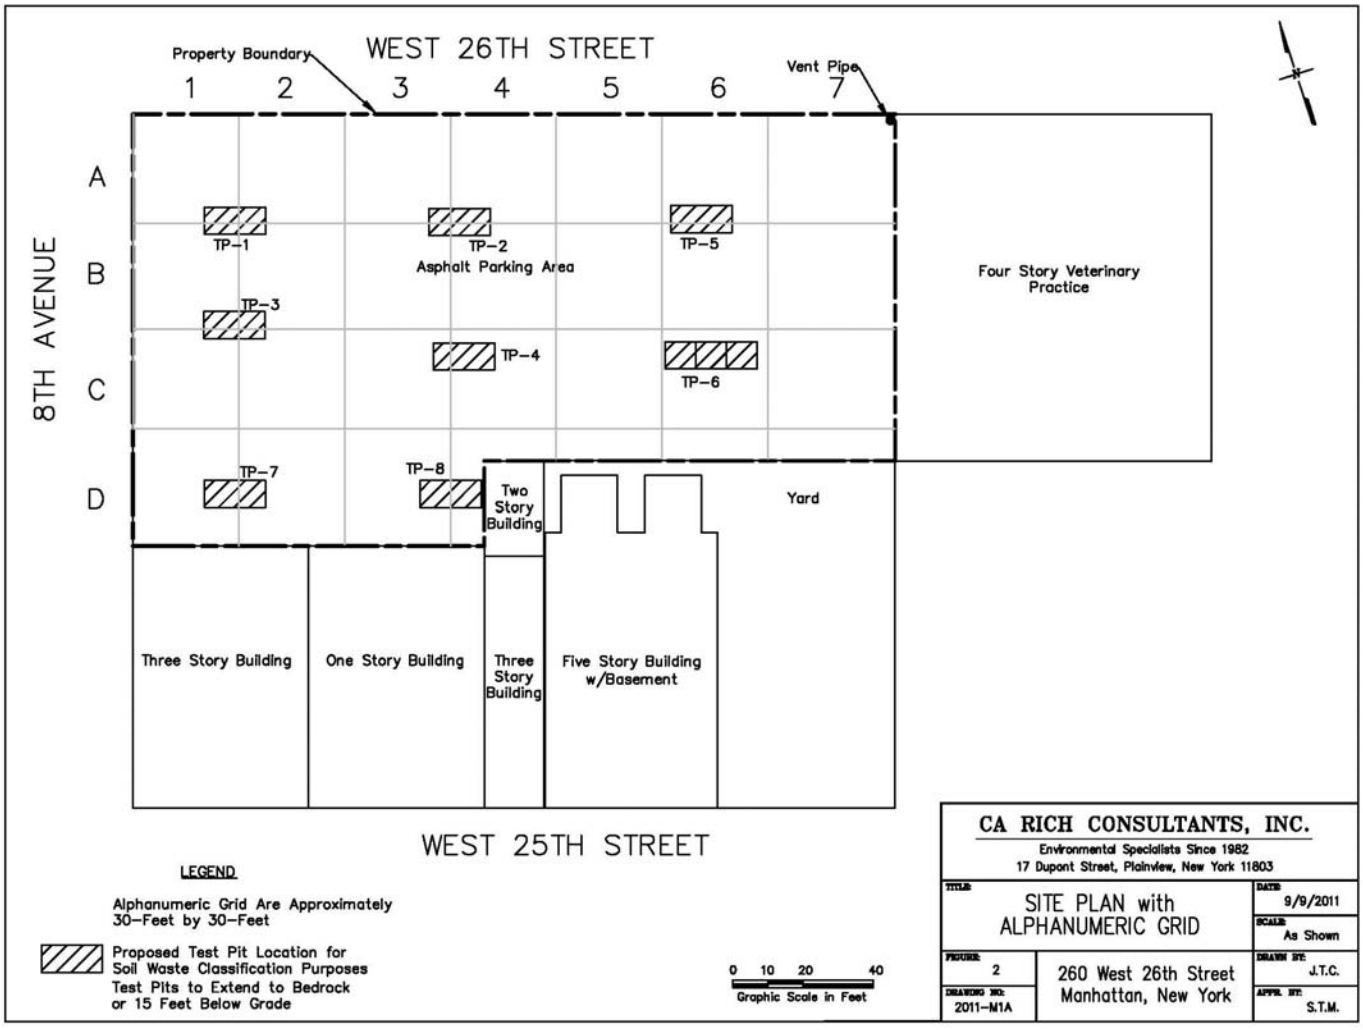

 File Name: _____

Photo Log

Photo 1- Waterproofing was installed along the west foundation wall.	
Photo 2- Meva Formwork was installed along the South Property Line.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast	X	Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	01-23-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Rebar was installed for the west foundation wall and footing along the South Property Line. A portion of the South Property Foundation Wall was poured. Waterproofing was installed on the ejector pit walls after the formwork was removed.

Jessica from CA Rich was on site to perform a limited 2 foot excavation in Grid A1 today. The soil was resampled for pesticides and submitted to the laboratory.

Working In Grids #: D4, A1, B1, D1, D2, D3

Air Monitoring (Since Last Report):

Air Monitoring was performed during the minor excavation today. No problems to report.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	334	Appr. 8225	18	Appr. 450	24	Appr. 600	259	Appr. 6525

Site Grid Map

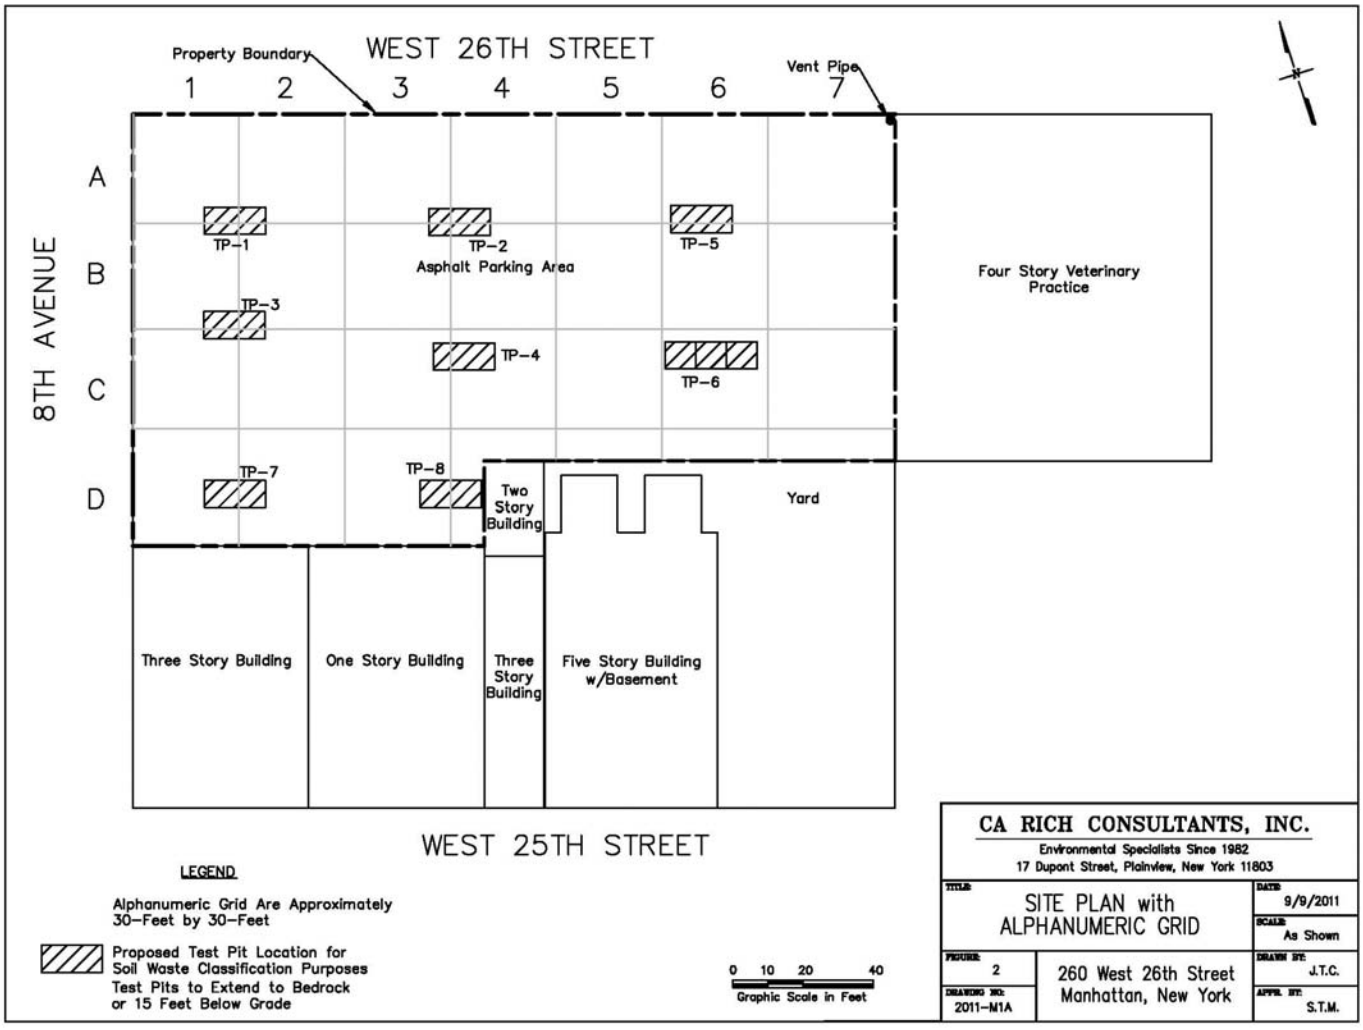

 File Name: _____

Photo Log

Photo 1- Waterproofing was installed on the ejector pit walls after the forms were stripped.	
Photo 2- Rebar was installed for the West Foundation wall.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	01-24-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

(4) Column Footings were poured today in the North east corner of the Site. Waterproofing was installed along the South Wall. Formwork was removed from the portion of the South Wall that was poured yesterday.

The curved wall at the ramp was formed today in preparation to be poured on Thursday.

Working In Grids #: 5A, 5B, 6A, 6B, D1, D2, D3, D4

Air Monitoring (Since Last Report):

No Air Monitoring was conducted. Air Monitoring will continue when excavation continues.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	334	Appr. 8225	18	Appr. 450	24	Appr. 600	259	Appr. 6525

Site Grid Map

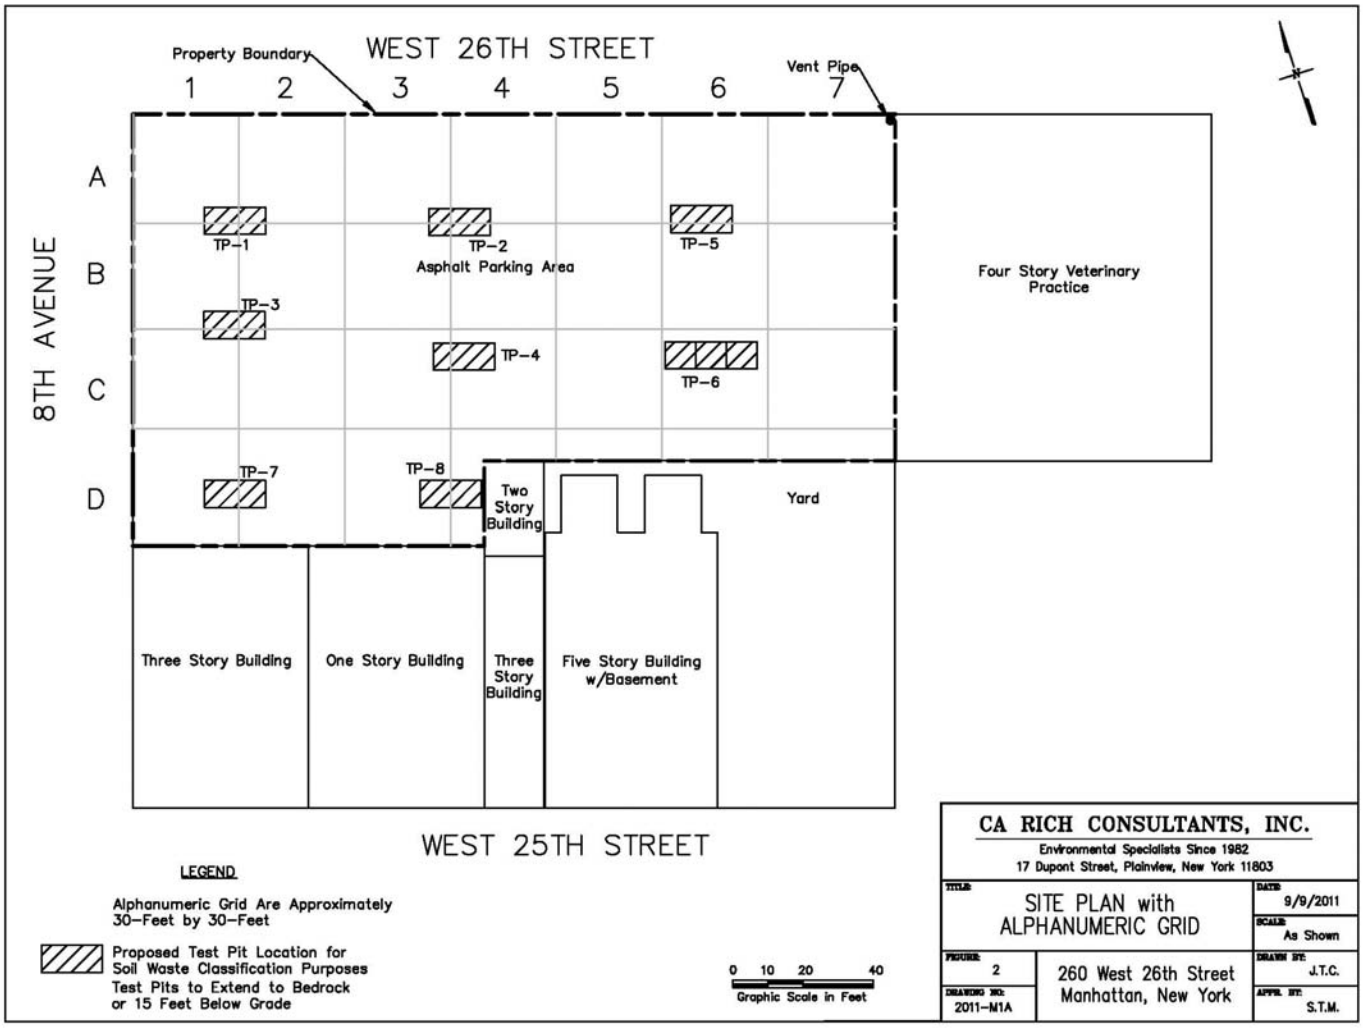

 File Name: _____

Photo Log

Photo 1- Curved section of Ramp wall was formed today.	
Photo 2- Rebar was delivered for the South and West wall today.	
Photo 3- (4) Columns were poured in the northeast corner of the site.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	01-25-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Curved portion of the ramp wall is being formed. Waterproofing was applied to the South side of the ramp wall. Rebar and waterproofing for the Footing is being installed along the South property line. Meva Formwork is being installed along the West Foundation wall. Trenching for underground plumbing has began.

Working In Grids #: A1, B1, D1, D2, D3, D4, A5, B5, A6, B6

Air Monitoring (Since Last Report):

No Air Monitoring was conducted. Air Monitoring will continue when excavation continues.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	334	Appr. 8225	18	Appr. 450	24	Appr. 600	259	Appr. 6525

Site Grid Map

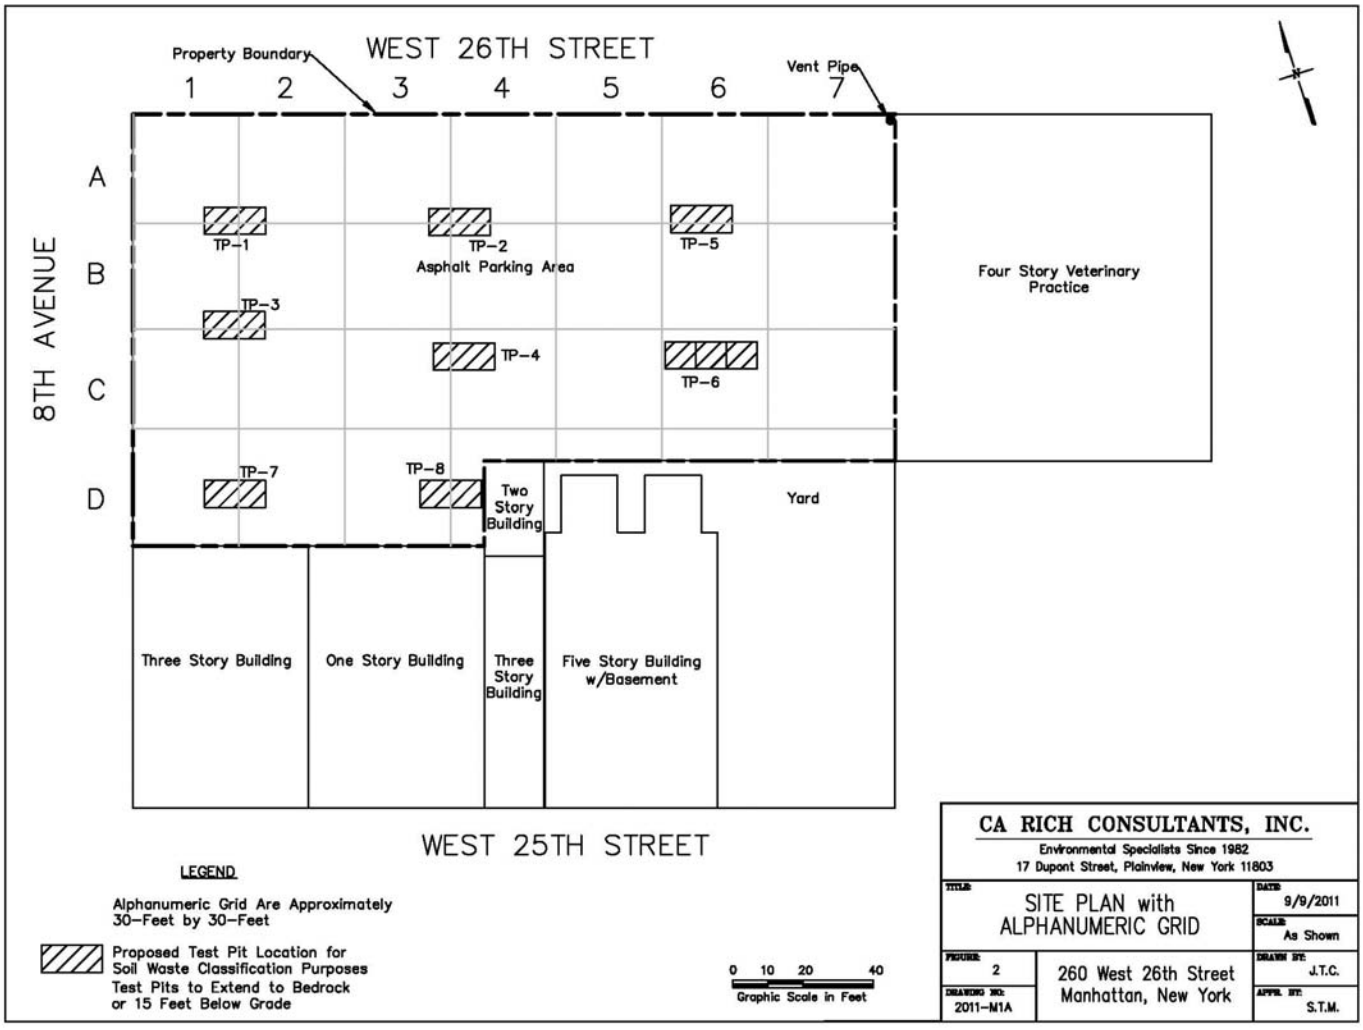

 File Name: _____

Photo Log

Photo 1- Waterproofing being installed along the south side of the ramp wall.	
Photo 2- Curved section of the Ramp wall being formed.	
Photo 3- Waterproofing and Rebar being installed along the South Wall Footing.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	01-26-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

The forms for the curved portion of the ramp wall were completed. Waterproofing and rebar was installed for the escalator slab and south wall footing. Concrete was poured for the South Wall footing, Elevator #1 Walls, and the Curved Ramp Wall. Also, plumbers began installing the underground plumbing on site.

Working In Grids #: B2, D1, D2, D3, D4, B4, B5

Air Monitoring (Since Last Report):

No Air Monitoring was conducted. Air Monitoring will continue when excavation continues.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	334	Appr. 8225	18	Appr. 450	24	Appr. 600	259	Appr. 6525

Site Grid Map

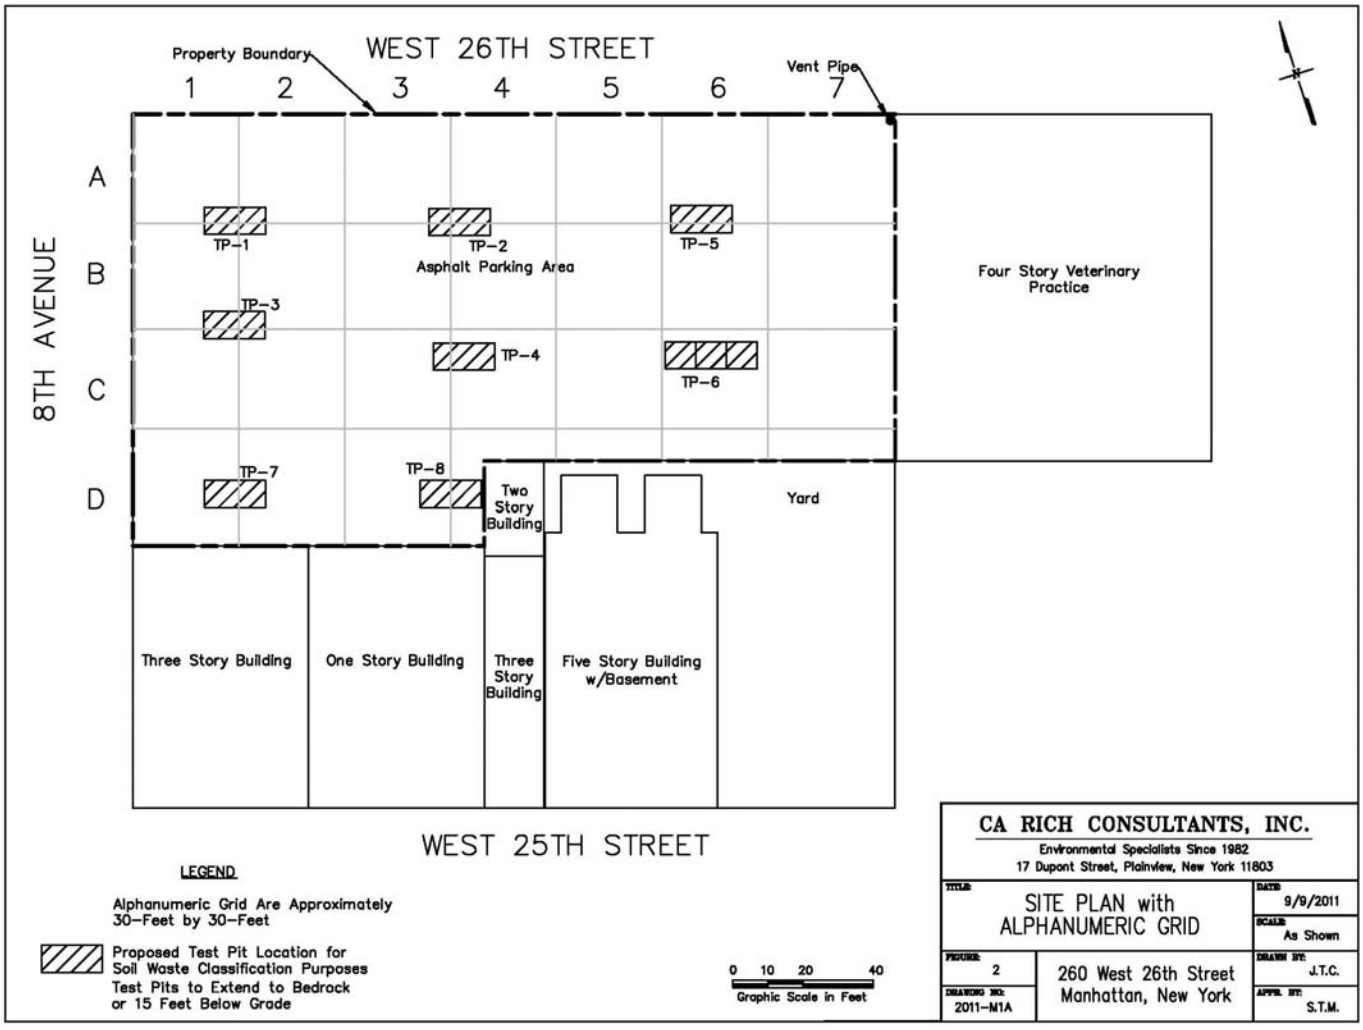

 File Name: _____

Photo Log

Photo 1- Footing along the South Wall was poured.	
Photo 2- Elev. #1 Walls were poured	
Photo 3- Rebar and Waterproofing for Escalator was completed and the Escalator Slab was poured.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	01-27-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

North Half of West Foundation Wall was poured. Forms were stripped from the curve wall and it was patched. Forms were removed from Elevator 1 walls. Underground plumbing began to be installed. (9) 20 yard Trucks of approved backfill were brought into the site as backfill from NYC Concrete Materials.

Working In Grids #: A6, B6, C6, A7, B7, C7, B5, A1, B1

Air Monitoring (Since Last Report):

No Air Monitoring was conducted. Air Monitoring will continue when excavation continues.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	334	Appr. 8225	18	Appr. 450	24	Appr. 600	259	Appr. 6525

Site Grid Map

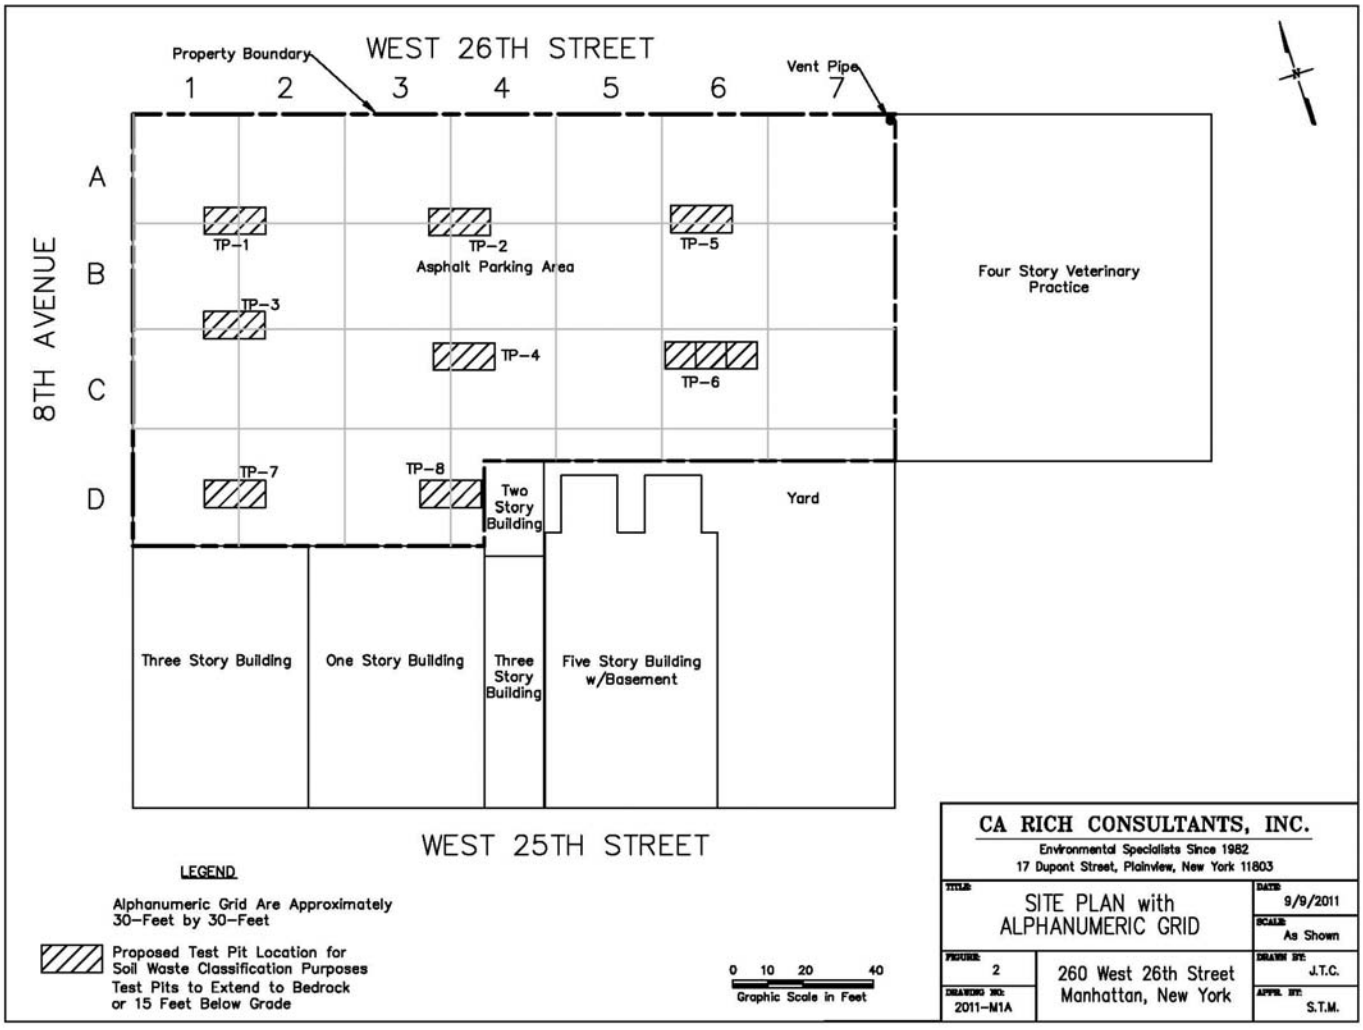

 File Name: _____

Photo Log

Photo 1- Workers beginning to pour West Foundation Wall.	
Photo 2- Rebar and Waterproofing was completed for the escalator pit.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	01-28-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Rebar and Waterproofing was installed for the South Foundation wall. Forms were removed from the West Foundation Wall.
(24) 20 yard Trucks of approved backfill were brought into the site as backfill for the ramp area from NYC Concrete Materials.

Working In Grids #: D1, D2, D3, D4, C5, C6, C7

Air Monitoring (Since Last Report):

No Air Monitoring was conducted. Air Monitoring will continue when excavation continues.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	334	Appr. 8225	18	Appr. 450	24	Appr. 600	259	Appr. 6525

Site Grid Map

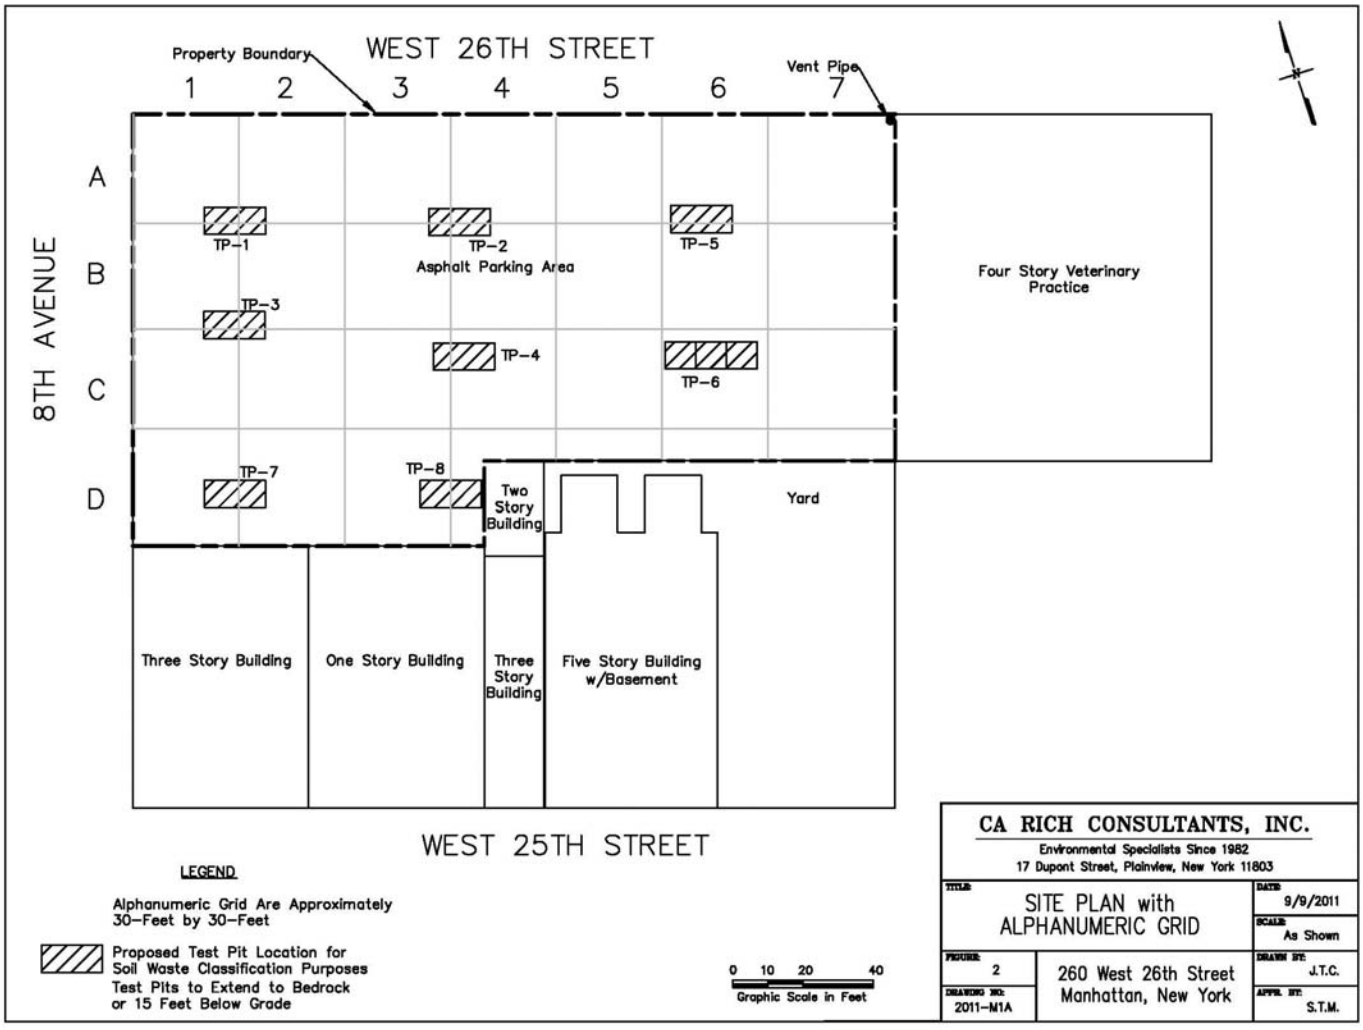

 File Name: _____

Photo Log

Photo 1- Workers installed waterproofing and rebar along the South Wall.	
Photo 2- Ramp Area was backfilled.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	01-30-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Officer: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Rebar was completed along the South Wall and forms started being installed. Rebar and waterproofing for escalator slab was completed and the slab was poured. Underground plumbing continued to be installed. 3 Trucks of Rock were removed from the site and sent to Red Roc Materials.

Working In Grids #: D1, D2, D3, D4, B2

Air Monitoring (Since Last Report):

No Air Monitoring was conducted. Air Monitoring will continue when excavation continues.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Clean Earth of North Jersey Mountainside, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Cu. Yds.	Trucks	Cu. Yds	Trucks	Cu. Yds.	Cu. Yds.
											3	Appr. 75
Totals (trucks, cu.yds.)	84	2,100	5	Appr. 125	334	Appr. 8225	18	Appr. 450	24	Appr. 600	262	Appr. 6550

Site Grid Map

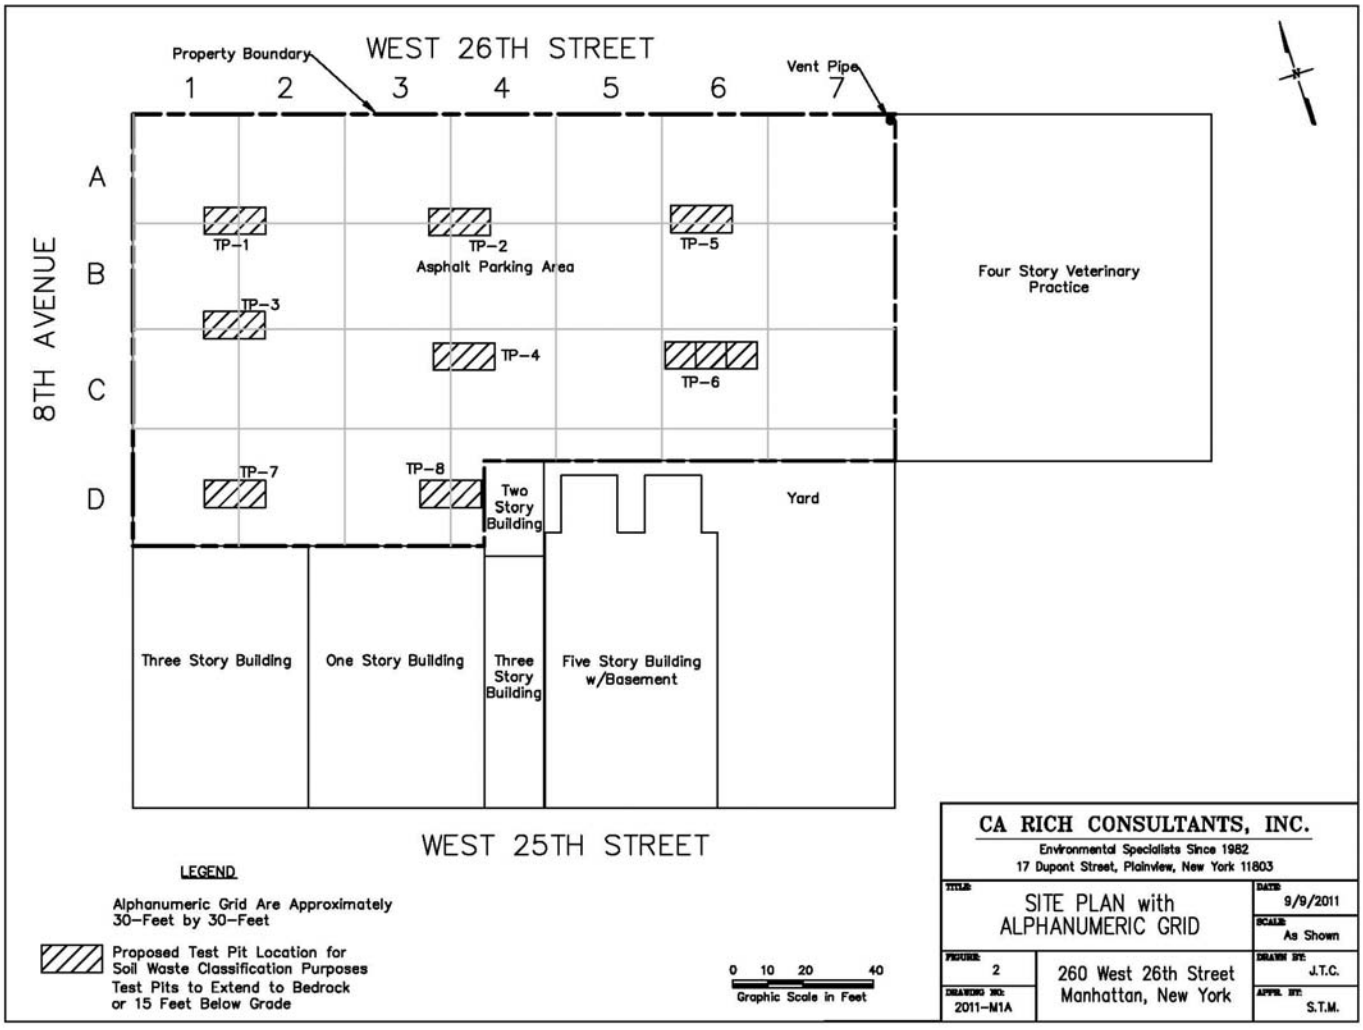

 File Name: _____

Photo Log

Photo 1- Meva Forms were placed along the South Foundation Wall.	
Photo 2- Escalator Slab was poured	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Steve Malinowski of CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	01-31-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Six truckloads of soil were removed from grid B1 to the Pure Soil Technologies Facility in Jackson Township, NJ. Five trucks of crushed rock were removed from the site and sent to Red Roc Materials. Exploratory excavation was conduct in grids A1, A2, A3, B1, B2, and B3 to determine the depth to bedrock.

Working In Grids #: A1, A2, A3, B1, B2, B3

Air Monitoring (Since Last Report):

Air Monitoring was performed today and no problems were encountered.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Pure Soil Technologies Jackson Township, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	trucks	Cu yds.	trucks	Cu. Yds.
											5	Appr. 75
Totals (trucks, cu.yds.)	84	2,100	6	Appr 150	334	Appr. 8,225	18	Appr. 450	24	Appr. 600	267	Appr. 6,675

A total of 5 truckloads of soil were disposed of at the Clean Earth of North Jersey Facility in Mountainside, NJ as hazardous solid due to elevated levels of lead.

Site Grid Map

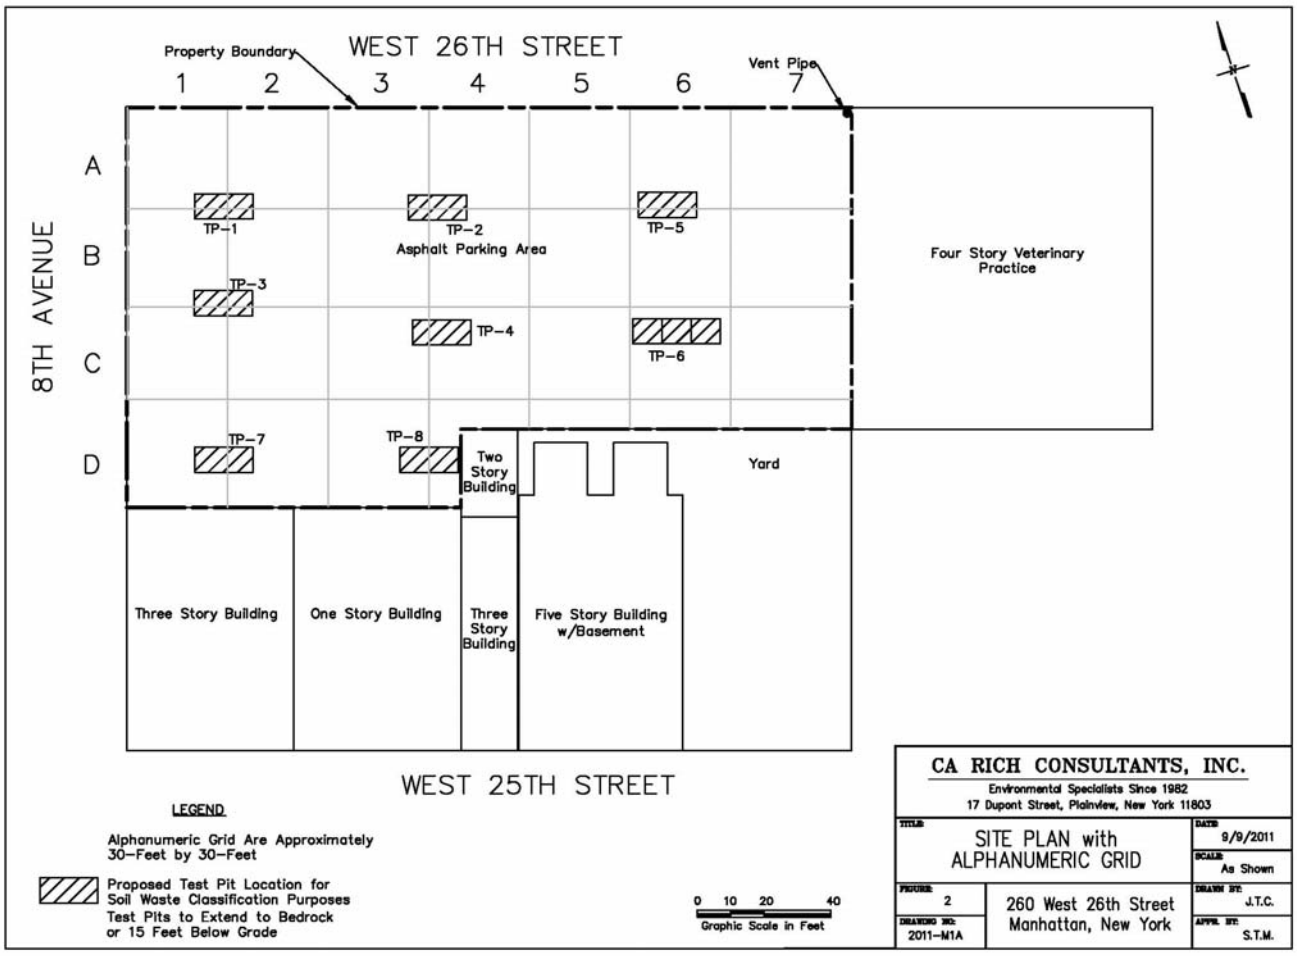

 File Name: _____

Photo Log

Southern wall rebar and waterproofing. Base of excavation to bedrock in grids D1, D2, D3 and D4.	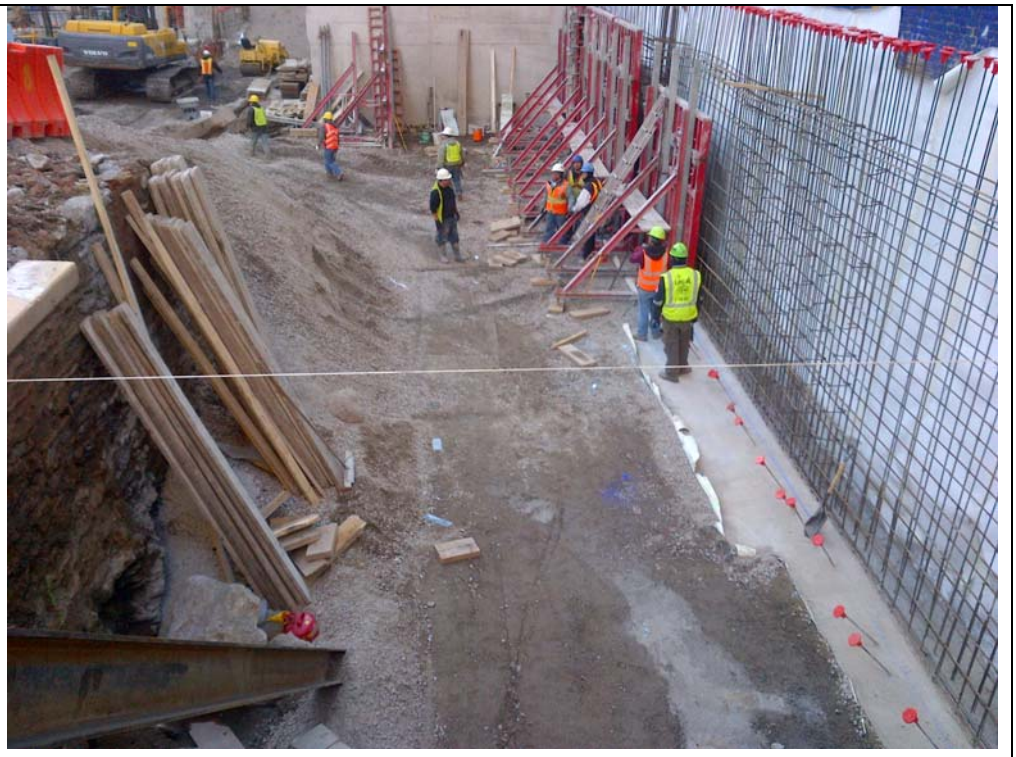
Photo 2- Bedrock excavation for elevator pit in western portion of site near grid B3.	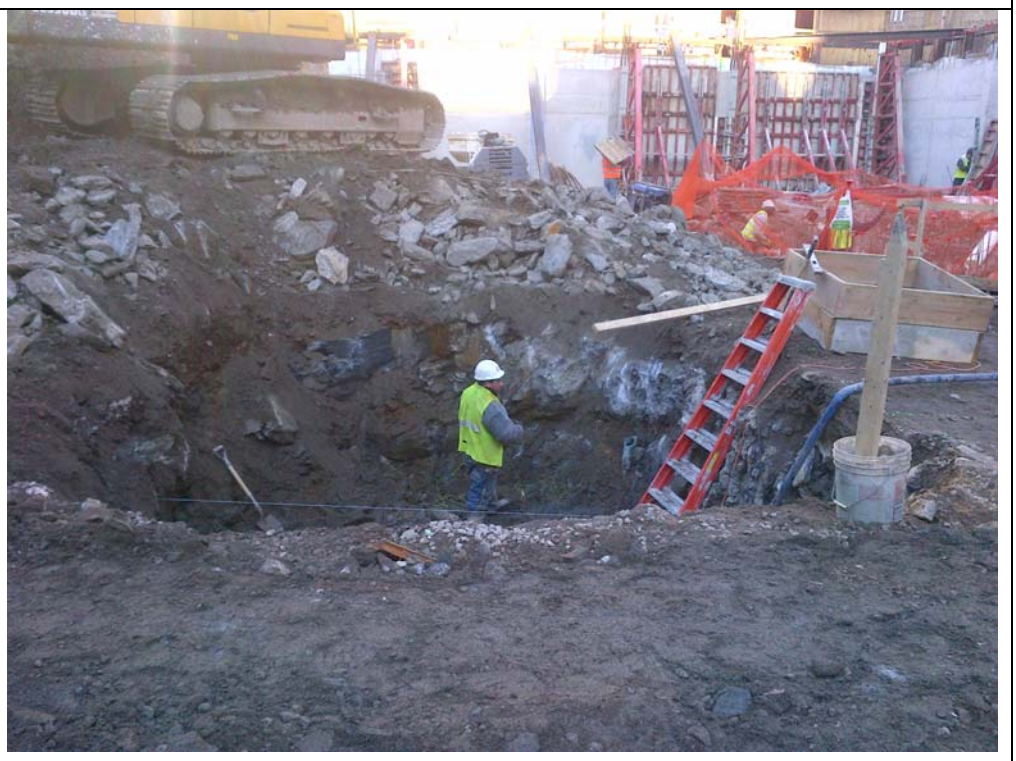

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	02-01-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Office: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Meva forms were completed along the South Wall. Waterproofing and Rebar was installed in Elevator 5 Pit. Forms were installed for escalator walls. (5) Trucks of Rock were hauled to Red Roc Materials. (8) Trucks of approved DOT back fill were trucked into the site for the Ramp area.

Electrical underground piping started to be installed. Contractor passed the first of three underground plumbing inspections with DOB.

Working In Grids #: A1, A2, A3, B1, B2, B3, B6, B7, C6, C7

Air Monitoring (Since Last Report):

Air Monitoring was not performed today and no problems were encountered. Monitoring will resume when excavation resumes.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Pure Soil Technologies Jackson Township, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	trucks	Cu yds.	trucks	Cu. Yds.
											5	Appr. 125
Totals (trucks, cu.yds.)	84	2,100	6	Appr 150	334	Appr. 8,225	18	Appr. 450	24	Appr. 600	272	Appr. 6,800

A total of 5 truckloads of soil were disposed of at the Clean Earth of North Jersey Facility in Mountainside, NJ as hazardous solid due to elevated levels of lead.

Site Grid Map

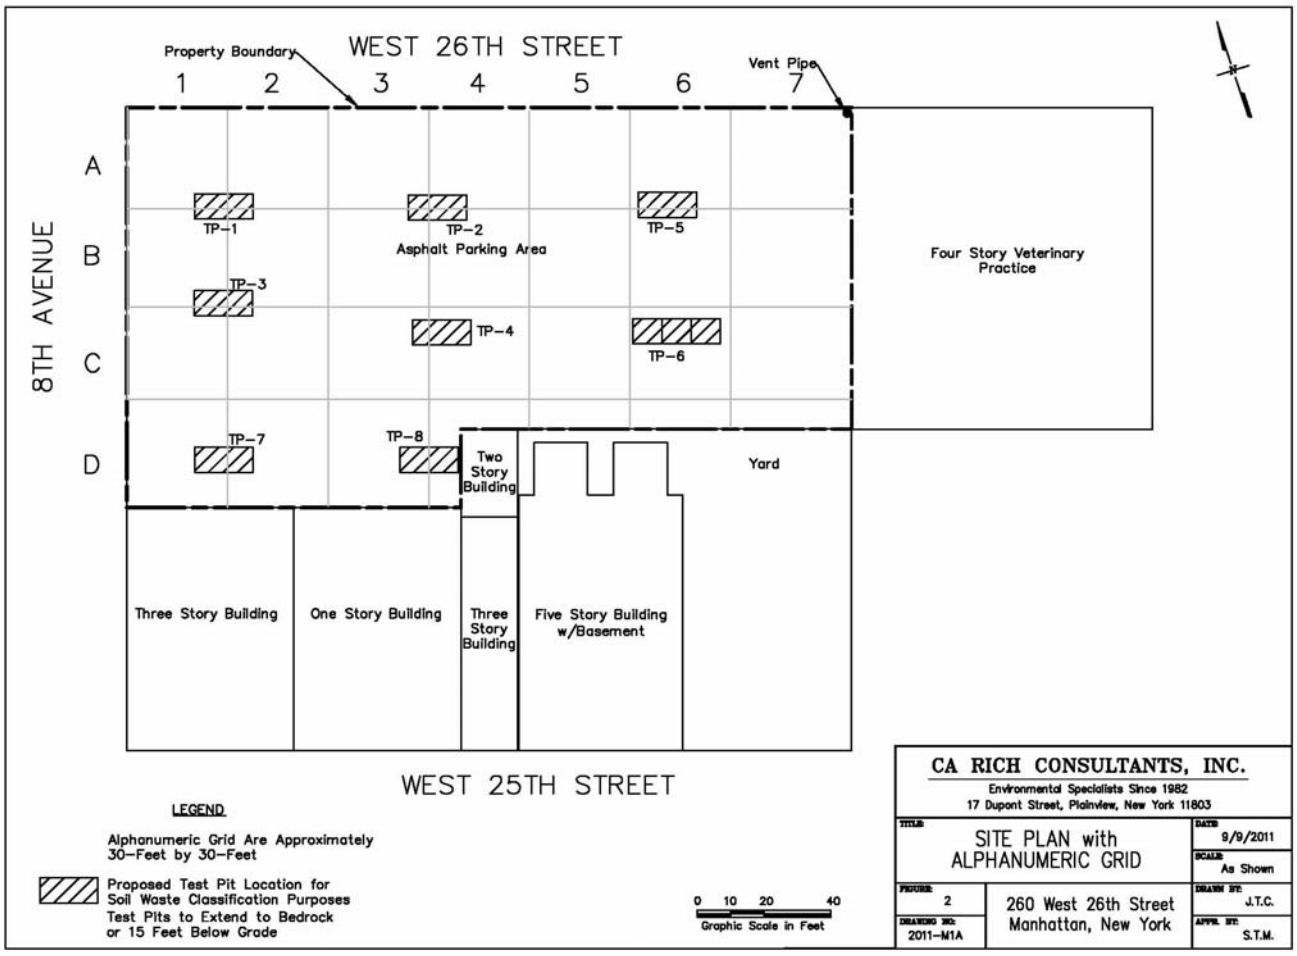

 File Name: _____

Photo Log

Photo 1- Meva forms were completed along the South Foundation wall in preparation for pour tomorrow.	
Photo 2- Ramp Area was backfilled with approved DOB Backfill Material.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	02-02-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Office: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

South Foundation Wall was poured. (3) Column Footings in the Northeast corner were poured. Underground Electrical conduit was laid out. Rebar and waterproofing for Elevator 5 was installed.

(3) Truckloads of DOB approved Backfill were brought into the site for the ramp area.

Working In Grids #: C5, C6, C7, D5, D6, D7, D1, D2, D3, C3

Air Monitoring (Since Last Report):

Air Monitoring was not performed today and no problems were encountered. Monitoring will resume when excavation resumes.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Pure Soil Technologies Jackson Township, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	trucks	Cu yds.	trucks	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	6	Appr 150	334	Appr. 8,225	18	Appr. 450	24	Appr. 600	272	Appr. 6,800

A total of 5 truckloads of soil were disposed of at the Clean Earth of North Jersey Facility in Mountainside, NJ as hazardous solid due to elevated levels of lead.

Site Grid Map

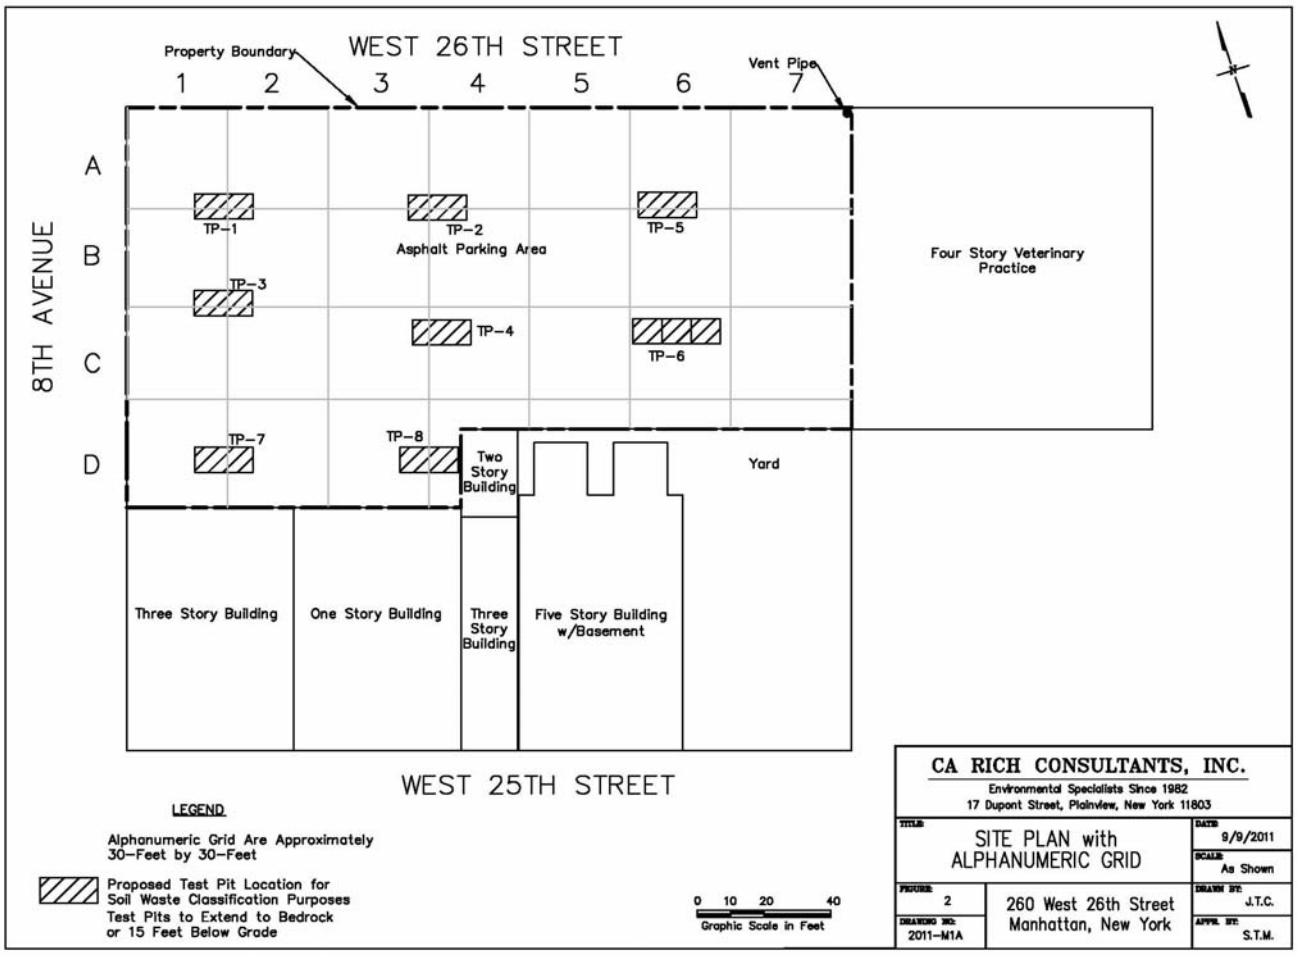

 File Name: _____

Photo Log

Photo 1 – The South Foundation Wall was poured.	
Photo 2- Rebar and Waterproofing for Elevator 5 Pit was installed.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Jessica Proscia of CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	x
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	02-3-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Eight truckloads of soil were removed from grid B2 and a portion of the ramp to the Pure Soil Technologies Facility in Jackson Township, NJ. Three trucks of crushed rock were removed from the site and sent to Red Roc Materials. Additional waste characterization samples were obtained from grids A1, and B1 to keep up with facility requirements.

Working In Grids #: A1, B1, B2

Air Monitoring (Since Last Report):

Air Monitoring was performed today and no problems were encountered.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

The construction team will install lagging as needed along the perimeter as the excavation proceeds. Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Pure Soil Technologies Jackson Township, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	trucks	Cu yds.	trucks	Cu. Yds.
			8								3	Appr. 75
Totals (trucks, cu.yds.)	84	2,100	14	Appr 350	334	Appr. 8,225	18	Appr. 450	24	Appr. 600	270	Appr. 6,750

A total of 5 truckloads of soil were disposed of at the Clean Earth of North Jersey Facility in Mountainside, NJ as hazardous solid due to elevated levels of lead.

Site Grid Map

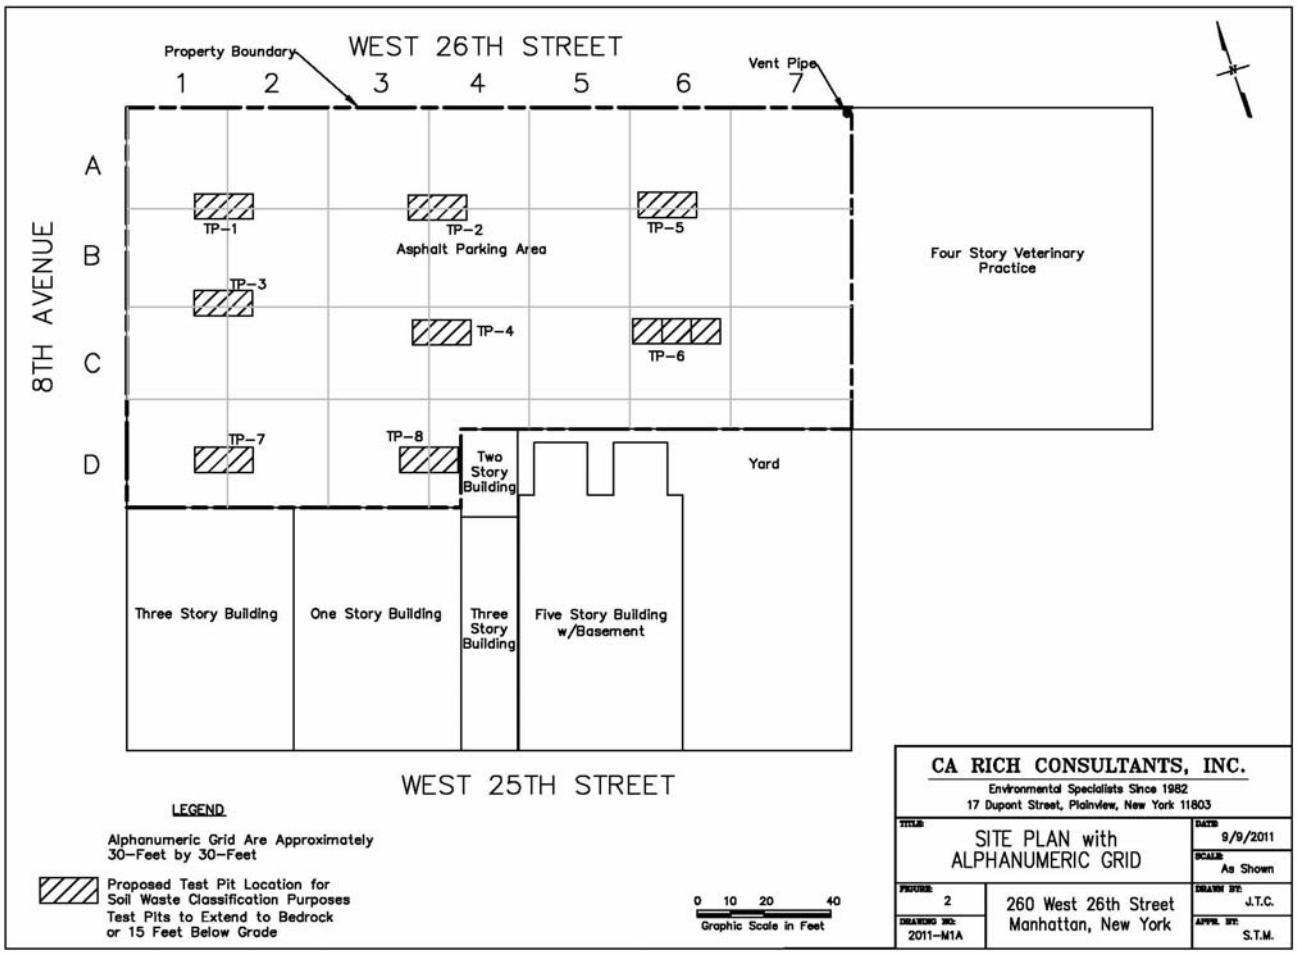

 File Name: _____

Photo Log

Photo 1- Eastern portion of the site.	
Photo 2- Soil being excavated from grid B2.	
Photo 3- Additional waste characterization samples being obtained.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	02-04-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Office: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Waterproofing, wire mesh, formwork, and rebar was installed in the North east corner of the site in preparation for the slab to be poured on Monday.

Working In Grids #: A6, A7, B6, B7

Air Monitoring (Since Last Report):

Air Monitoring was not performed today and no problems were encountered. Monitoring will resume when excavation resumes.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Pure Soil Technologies Jackson Township, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	trucks	Cu yds.	trucks	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	14	Appr 350	334	Appr. 8,225	18	Appr. 450	24	Appr. 600	272	Appr. 6,800

A total of 5 truckloads of soil were disposed of at the Clean Earth of North Jersey Facility in Mountainside, NJ as hazardous solid due to elevated levels of lead.

Site Grid Map

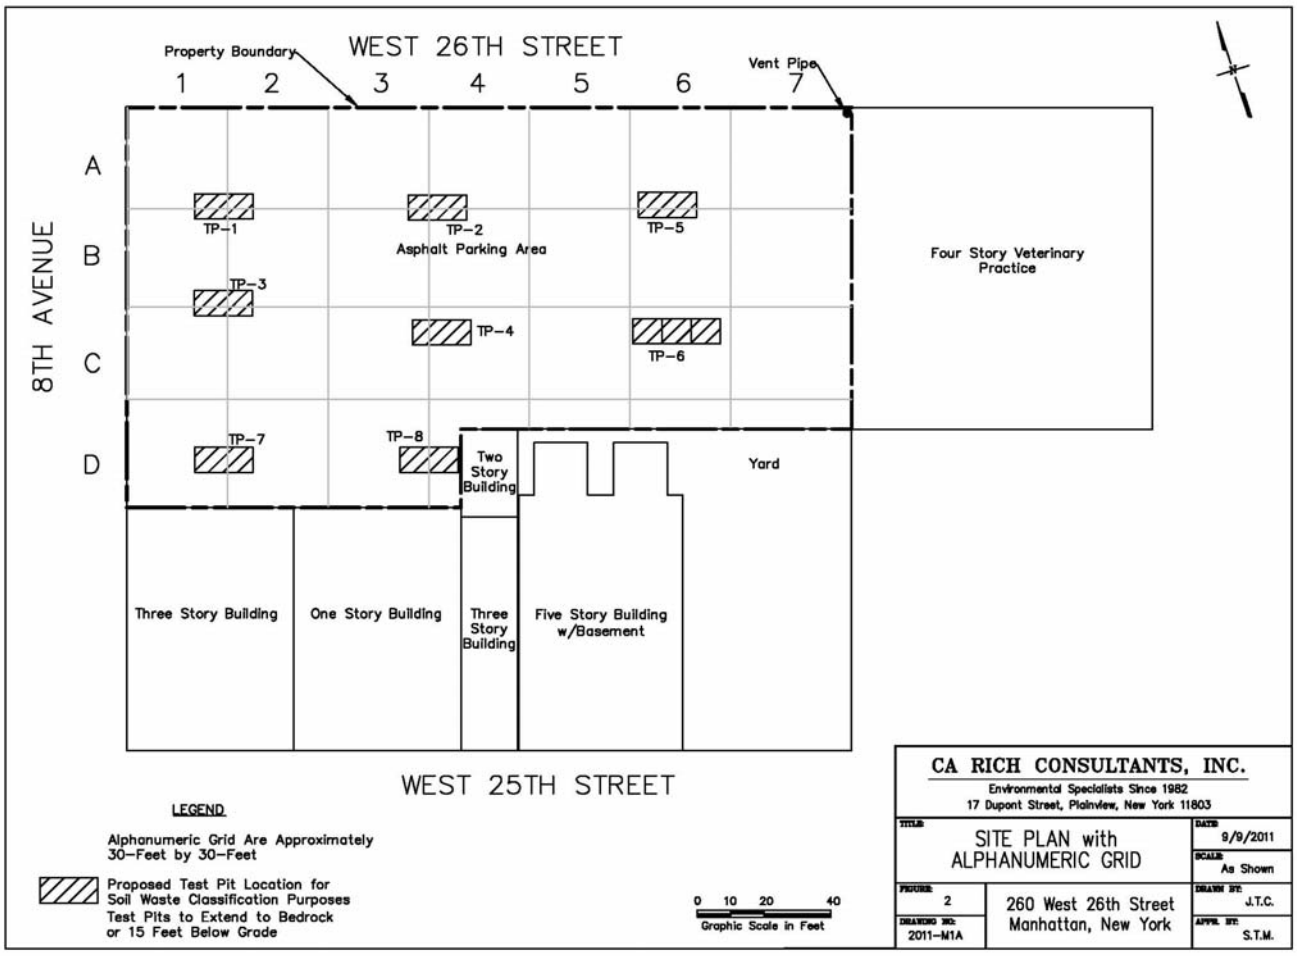

 File Name: _____

Photo Log

Photo 1 – Underground electrical piping was completed.	
Photo 2 – Waterproofing and Wire Mesh was installed for the 4” slab in the Northeast Corner of the site.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	02-06-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Office: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Waterproofing was inspected and Slab was poured in the Northeast corner of the site. Escalator Walls were poured. Underground plumbing was completed for Phase #2 DOB Inspection tomorrow morning.

Working In Grids #: A6, A7, B6, B7, B2, C3, C4

Air Monitoring (Since Last Report):

Air Monitoring was not performed today and no problems were encountered. Monitoring will resume when excavation resumes.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Pure Soil Technologies Jackson Township, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	trucks	Cu yds.	trucks	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	14	Appr 350	334	Appr. 8,225	18	Appr. 450	24	Appr. 600	272	Appr. 6,800

A total of 5 truckloads of soil were disposed of at the Clean Earth of North Jersey Facility in Mountainside, NJ as hazardous solid due to elevated levels of lead.

Site Grid Map

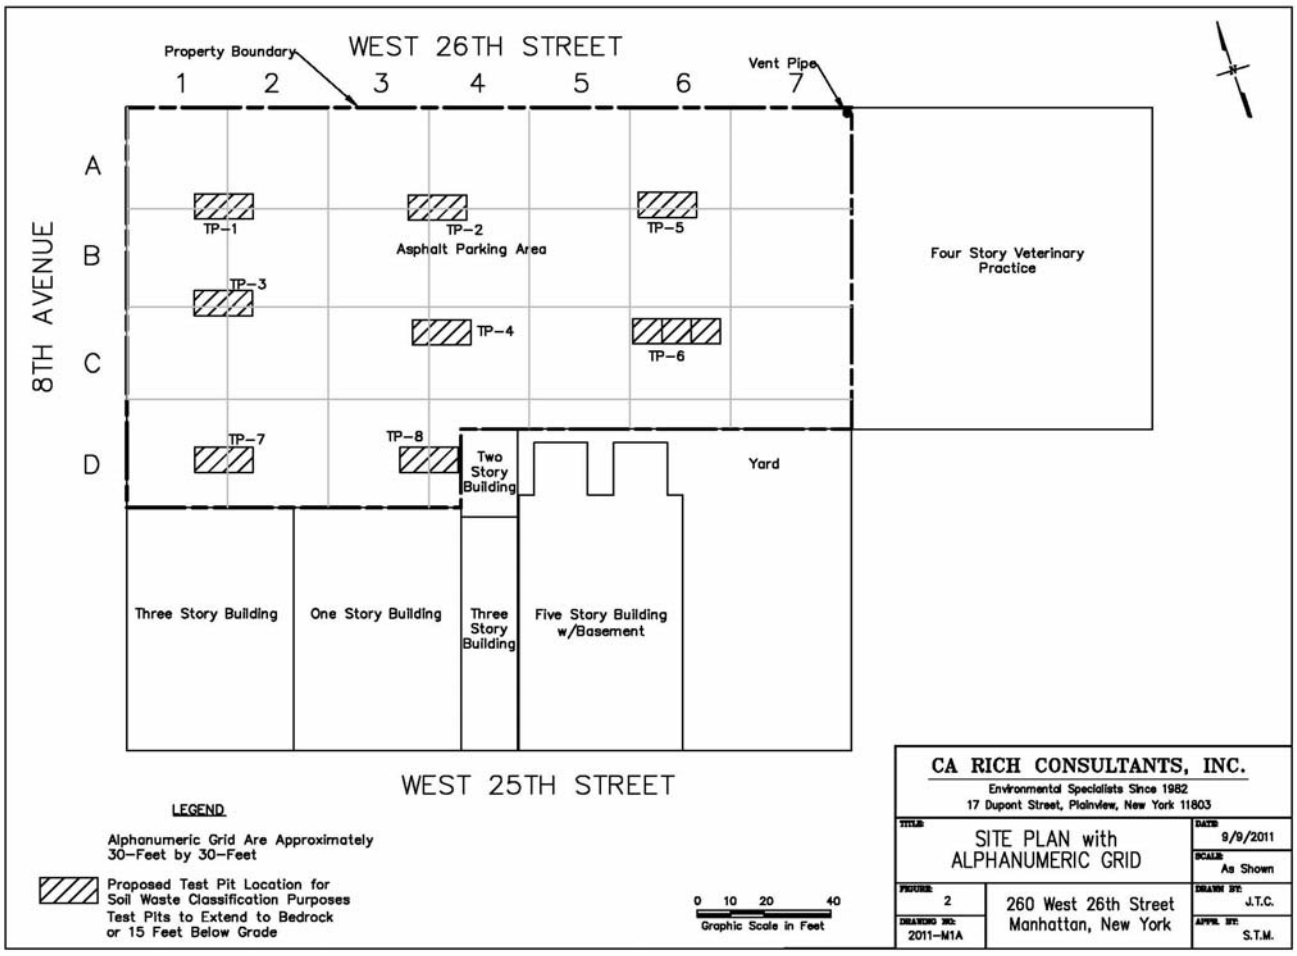

 File Name: _____

Photo Log

Photo 1 – Slab being poured in Northeast corner of the site.	
Photo 2 – Finished 4” Thick Slab in Northeast Corner of the Site	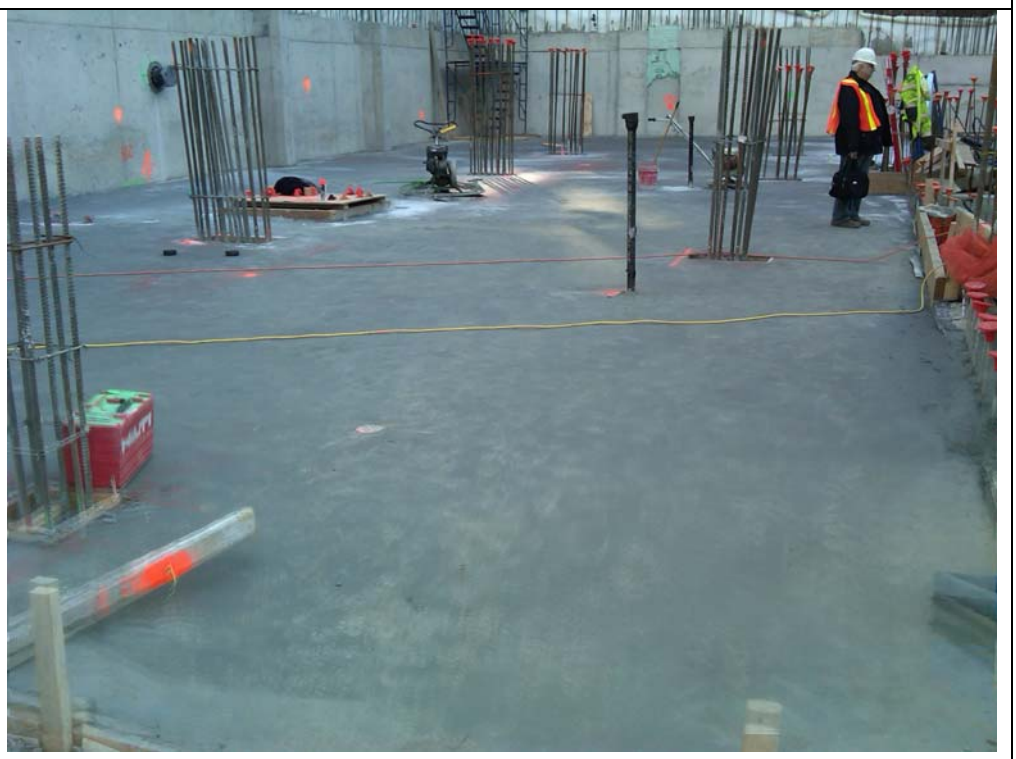

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	02-07-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Office: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Elevator #5 Walls were poured today. Escalator walls were waterproofed. (6) Column Footings were poured today. Meva formwork was stripped from the South Wall today. Ramp was graded out and will be ready for pour on Thursday.

(3) Trucks of rock were taken to Red Roc Materials Facility.

Working In Grids #: C5, C6,C7, D1, D2, D3, B2, B3

Air Monitoring (Since Last Report):

Air Monitoring was not performed today and no problems were encountered. Monitoring will resume when excavation resumes.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Pure Soil Technologies Jackson Township, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	trucks	Cu yds.	trucks	Cu. Yds.
											3	Appr. 75
Totals (trucks, cu.yds.)	84	2,100	14	Appr 350	334	Appr. 8,225	18	Appr. 450	24	Appr. 600	275	Appr. 6,875

A total of 5 truckloads of soil were disposed of at the Clean Earth of North Jersey Facility in Mountainside, NJ as hazardous solid due to elevated levels of lead.

Site Grid Map

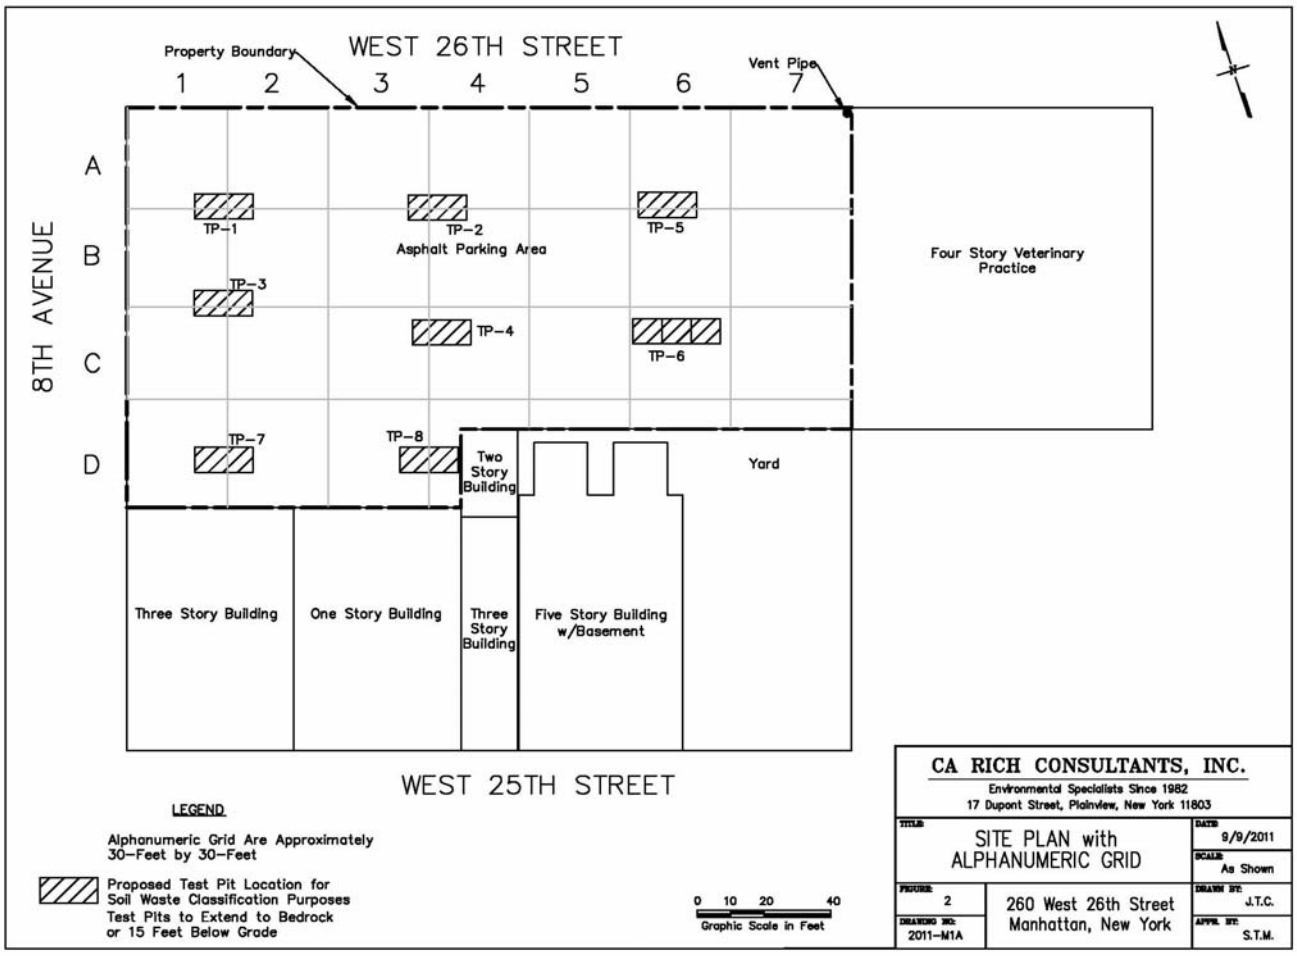

 File Name: _____

Photo Log

Photo 1 – Waterproofing was installed on the Escalator walls.	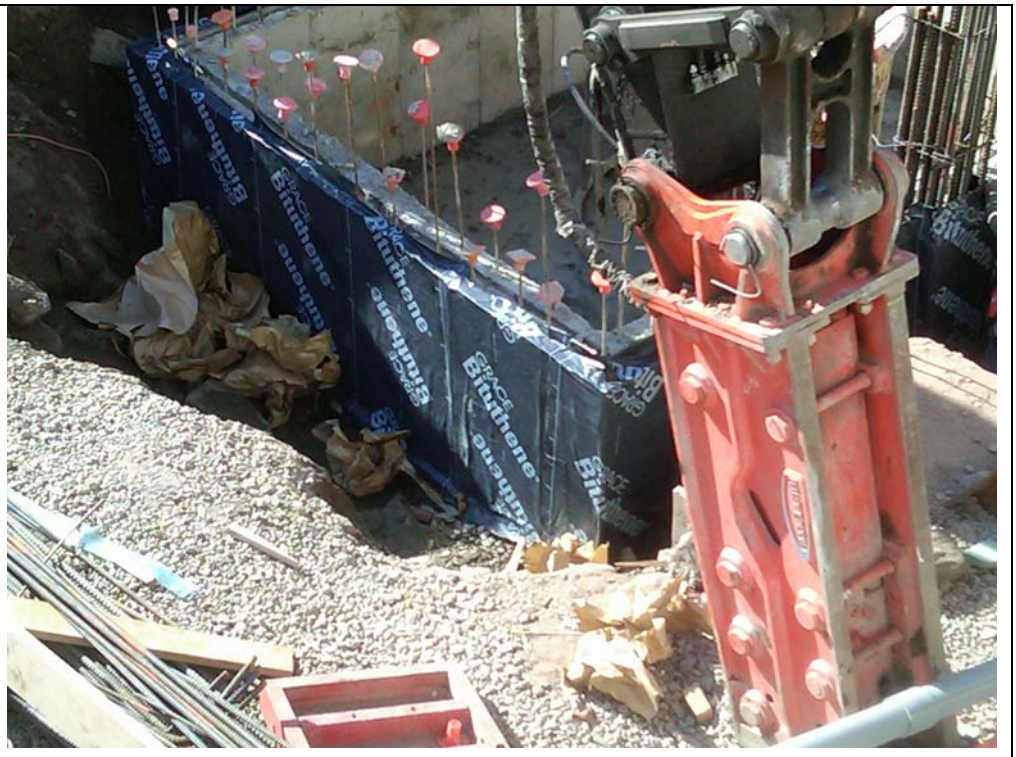
Photo 2 – (6) Column Footings were poured today in the southeast corner of the site.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain	X	Overcast		Partly Cloudy		Bright Sun	
TEMP.	TO 32	X	32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	02-08-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Office: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Workers continued to backfill the ramp area. Steve O. from CA Rich was on site to do a waterproofing inspection on the east half of the lower slab. After Steve approved the waterproofing, the slab was poured. Phase 2 of the underground plumbing was approved by DOB.

(7) Trucks of DOB approved RCA Backfill were delivered to the site today.

Working In Grids #: C5, C6, D6, D7

Air Monitoring (Since Last Report):

Air Monitoring was not performed today and no problems were encountered. Monitoring will resume when excavation resumes.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Pure Soil Technologies Jackson Township, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	trucks	Cu yds.	trucks	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	14	Appr 350	334	Appr. 8,225	18	Appr. 450	24	Appr. 600	275	Appr. 6,875

A total of 5 truckloads of soil were disposed of at the Clean Earth of North Jersey Facility in Mountainside, NJ as hazardous solid due to elevated levels of lead.

Site Grid Map

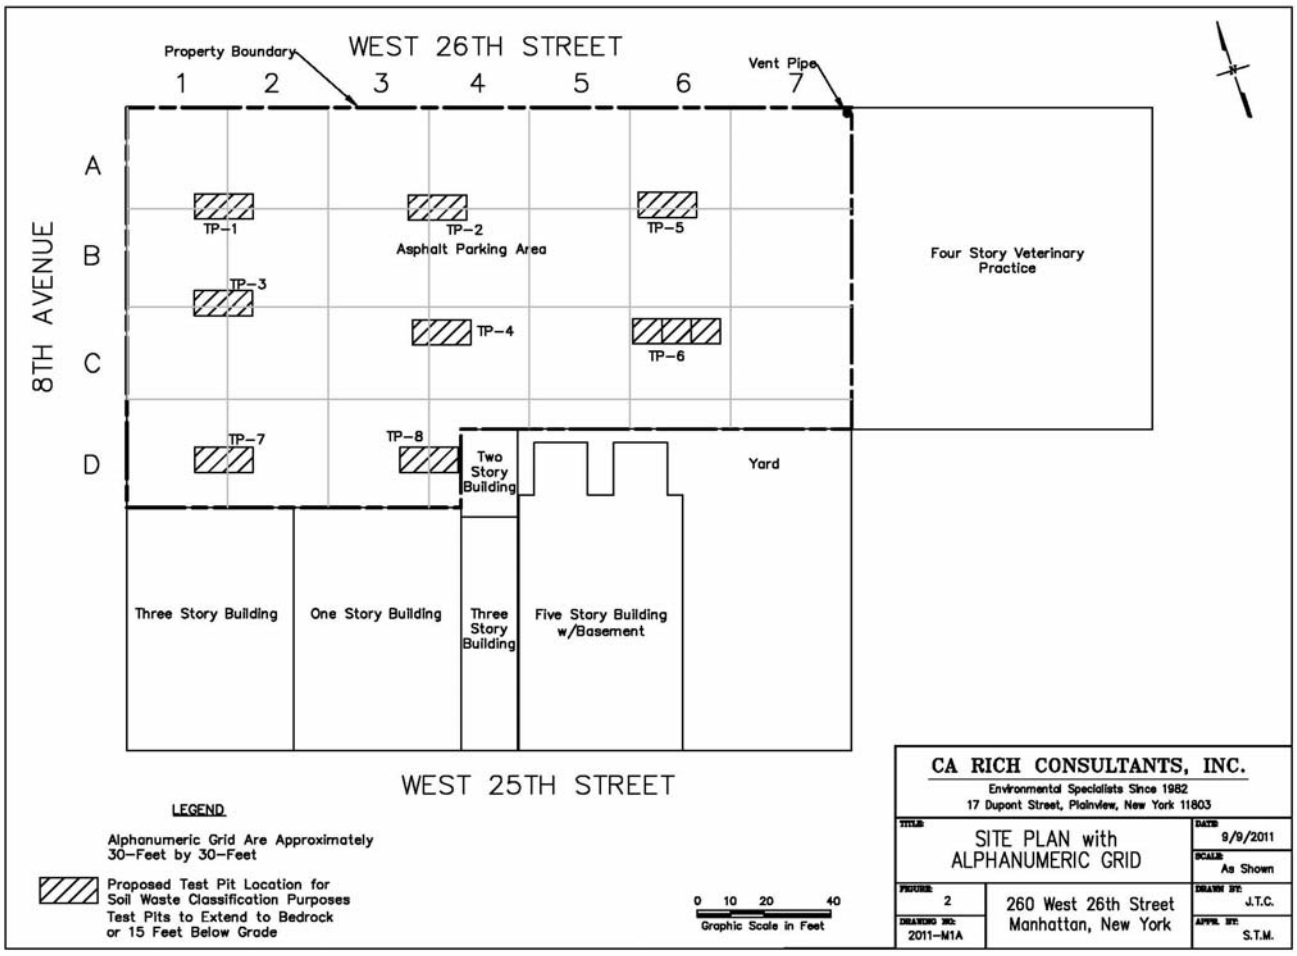

 File Name: _____

Photo Log

Photo 1 – Lower portion of the slab was poured after the waterproofing was installed.	
Photo 2 – Workers installing waterproofing in preparation for the slab to be poured.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	02-09-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Office: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Rebar and waterproofing was installed for Shear Wall #6 Footing. Waterproofing was installed on the South Wall. Workers finished grading the ramp and the ramp was poured.

Working In Grids #: C5, C6, C7, D5, D6, D7, B2

Air Monitoring (Since Last Report):

Air Monitoring was not performed today and no problems were encountered. Monitoring will resume when excavation resumes.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Pure Soil Technologies Jackson Township, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	trucks	Cu yds.	trucks	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	14	Appr 350	334	Appr. 8,225	18	Appr. 450	24	Appr. 600	275	Appr. 6,875

A total of 5 truckloads of soil were disposed of at the Clean Earth of North Jersey Facility in Mountainside, NJ as hazardous solid due to elevated levels of lead.

Site Grid Map

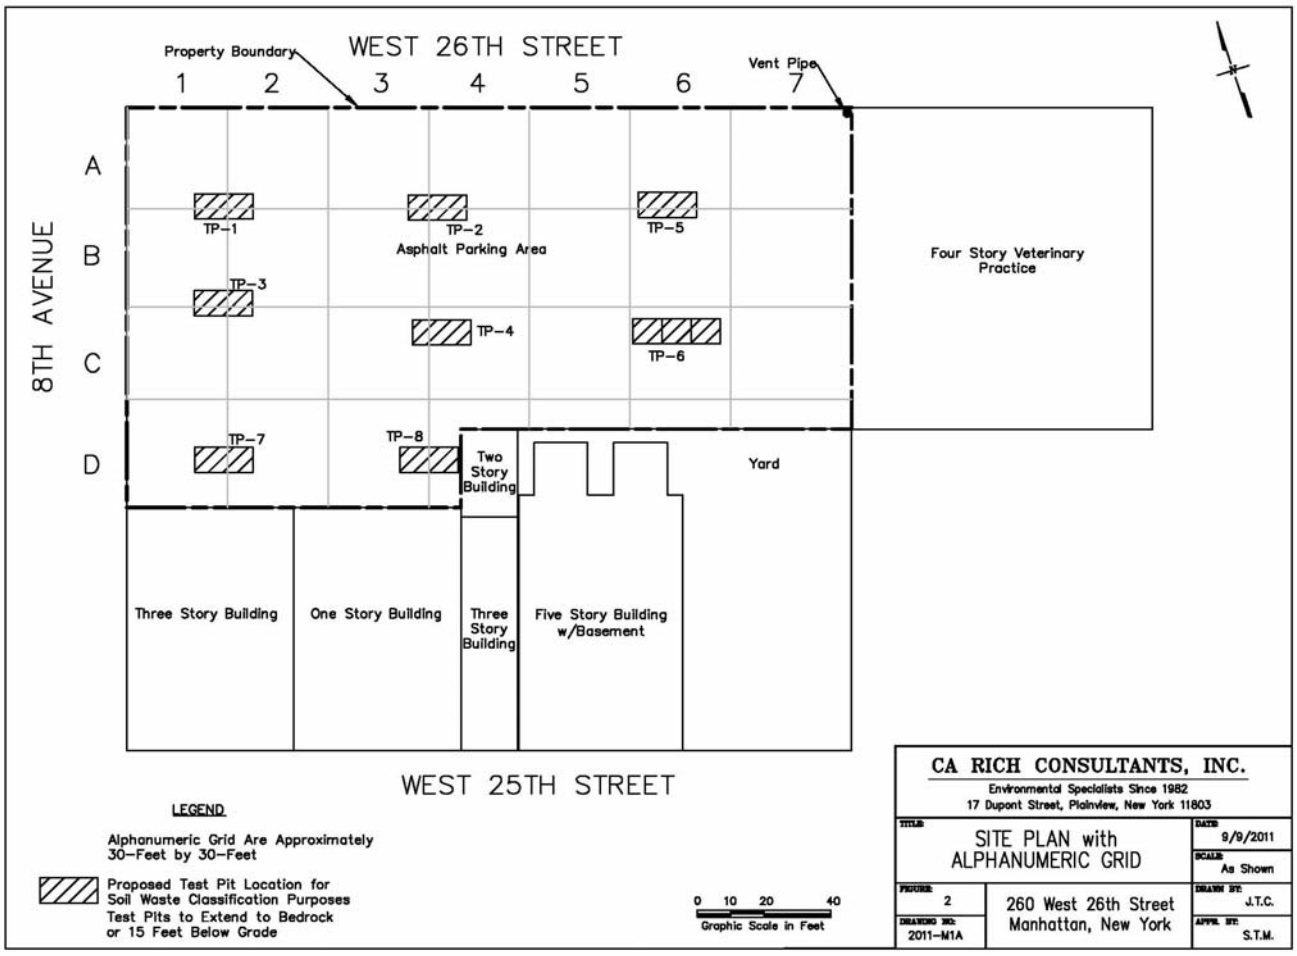

 File Name: _____

Photo Log

Photo 1 – Waterproofing and Rebar installed for Shear Wall #6 Footing.	
Photo 2 – Workers pouring concrete at ramp.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	02-10-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Office: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Rebar was completed on Shear Wall #6 Footing and then concrete was poured. Rock was chipped for the hoist pad to be installed. (2) Truck loads of rock were removed and sent to Red Rock Materials facility.

Working In Grids #: C5, C6, C7, D5, D6, D7, B2

Air Monitoring (Since Last Report):

Air Monitoring was not performed today and no problems were encountered. Monitoring will resume when excavation resumes.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Excavation in select areas will continue on an as-needed basis. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Pure Soil Technologies Jackson Township, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	trucks	Cu yds.	trucks	Cu. Yds.
											2	Appr. 50
Totals (trucks, cu.yds.)	84	2,100	14	Appr 350	334	Appr. 8,225	18	Appr. 450	24	Appr. 600	277	Appr. 6,925

A total of 5 truckloads of soil were disposed of at the Clean Earth of North Jersey Facility in Mountainside, NJ as hazardous solid due to elevated levels of lead.

Site Grid Map

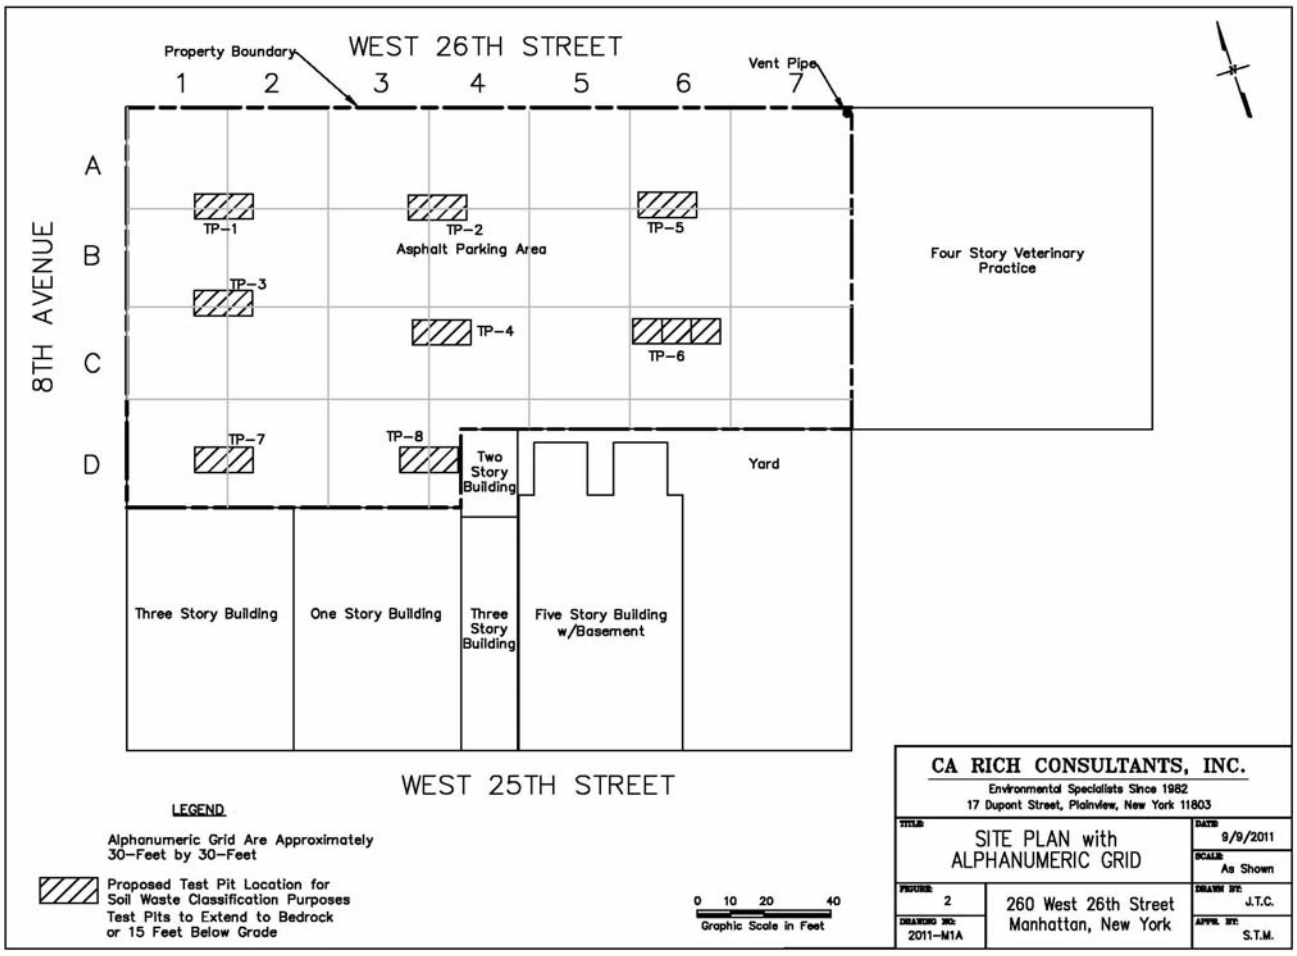

 File Name: _____

Photo Log

Photo 1 – Waterproofing and Rebar was installed in the column footing and concrete was poured.	
Photo 2 – Workers pouring concrete at the Shear Wall #6 Footing.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Jessica Proscia of CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	x
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	02-13-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Sixteen truckloads of soil were removed from grid C2 to the Pure Soil Technologies Facility in Jackson Township, NJ. The Grace waterproofing membrane was installed in grids A4, B4, B5, C4 and C5.

Working In Grids #: A1, B1, B2 A4, B4, B5, C2, C4 and C5.

Air Monitoring (Since Last Report):

Air Monitoring was performed today and no problems were encountered.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Excavation activities will continue until bedrock is reached is Grids A1, A2, A3, B1, B2, B3, C1, C2, and C3. The excavation will be done simultaneously with the installation of the water-proofing barrier and select concrete pours of the foundation. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Pure Soil Technologies Jackson Township, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	trucks	Cu yds.	trucks	Cu. Yds.
			16	400								
Totals (trucks, cu.yds.)	84	2,100	30	Appr 750	334	Appr. 8,225	18	Appr. 450	24	Appr. 600	270	Appr. 6,750

A total of 5 truckloads of soil were disposed of at the Clean Earth of North Jersey Facility in Mountainside, NJ as hazardous solid due to elevated levels of lead.

Site Grid Map

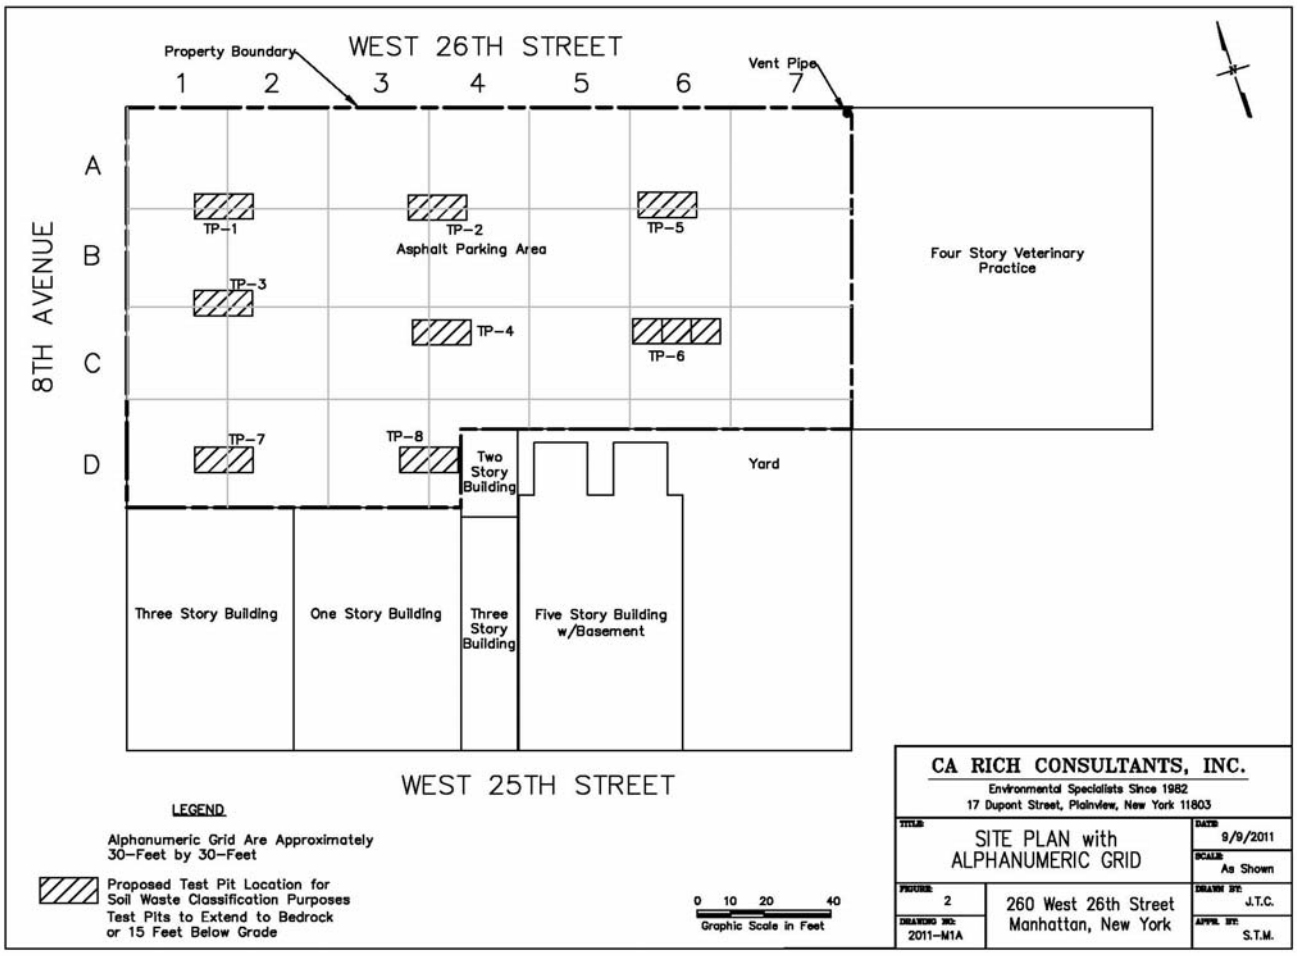

 File Name: _____

Photo Log

Photo 1- Excavation of ramp in grid C2 with off-site shipping to Pure Soil Technologies.	
Photo 2- Water-proofing membrane installation near bottom of new garage access ramp.	
Photo 3- Close up of water-proofing membrane and wire mesh in preparation of concrete upcoming pouring.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Jessica Proscia of CA RICH

WEATHER	Snow		Rain		Overcast	X	Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	02-14-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Fifteen truckloads of soil were removed from grids C1 and C2 for off-site disposal at the Pure Soil Technologies Facility in Jackson Township, NJ. The construction ramp is almost completely removed as well as the last remaining soil from grids A3 and B3. Grids A3 and B3 have now been fully excavated until bedrock.

Working In Grids #: A3, B3, C1, C2, and C3.

Air Monitoring (Since Last Report):

Air Monitoring was performed today and no problems were encountered.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Excavation activities will continue until bedrock is reached is Grids A1, A2, B1, B2, C1, C2, and C3. Excavation will be performed simultaneously with the installation of the water-proofing barrier and select concrete pours of the foundation. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Pure Soil Technologies Jackson Township, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	trucks	Cu yds.	trucks	Cu. Yds.
			15	375								
Totals (trucks, cu.yds.)	84	2,100	30	Appr 1125	334	Appr. 8,225	18	Appr. 450	24	Appr. 600	270	Appr. 6,750

A total of 5 truckloads of soil were disposed of at the Clean Earth of North Jersey Facility in Mountainside, NJ as hazardous solid due to elevated levels of lead.

Site Grid Map

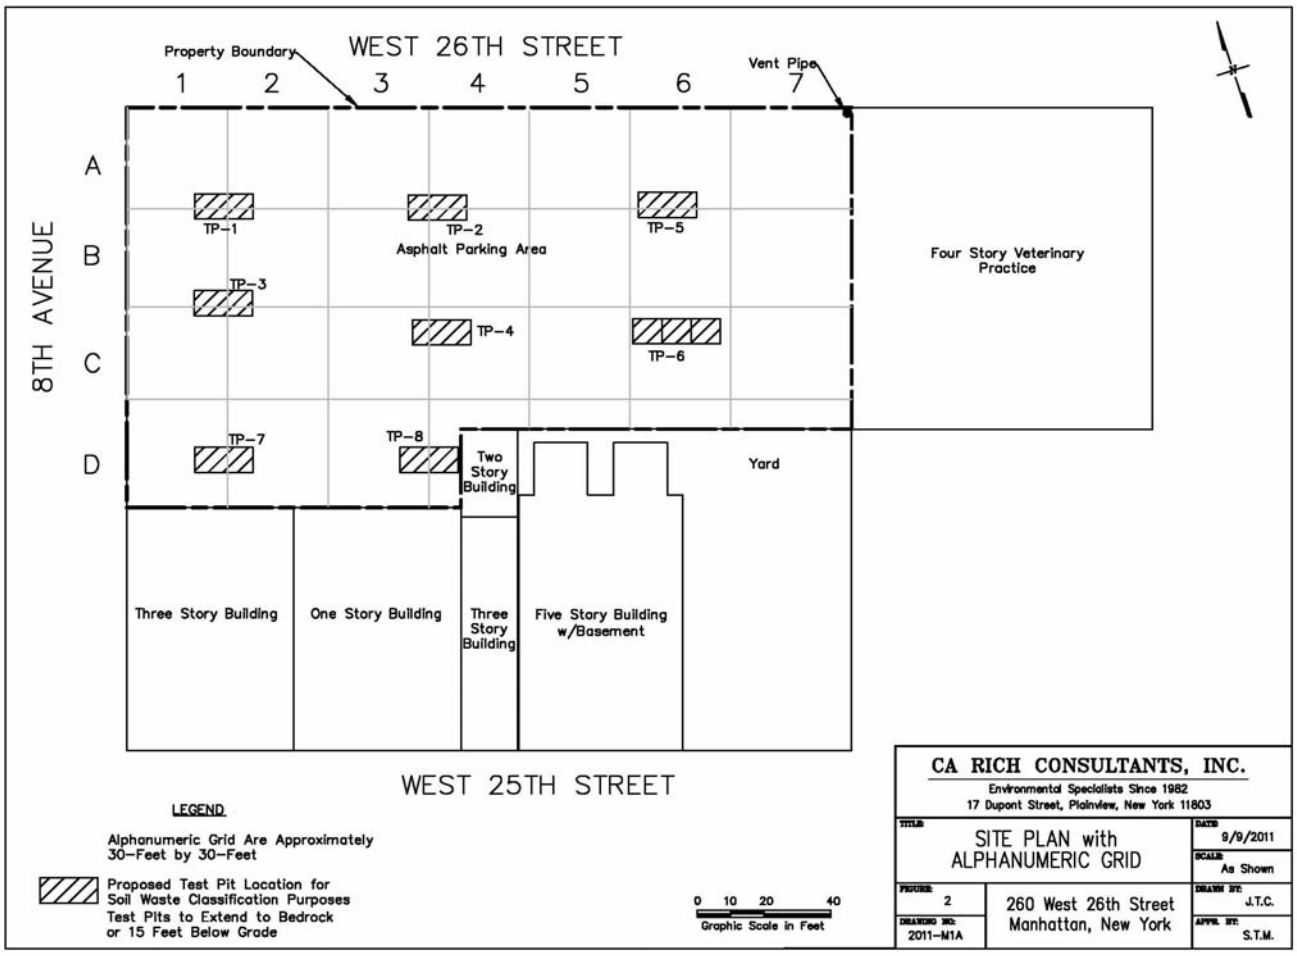

 File Name: _____

Photo Log

Photo 1- Excavation of ramp in grids C1 and C2 with off-site shipping to Pure Soil Technologies.	
Photo 2- Bedrock at final depth of excavation in grids A3 and B3. Note: the bedrock is wet because it was washed with a hose while being swept by laborers.	
Photo 3- Bedrock at final depth of excavation in grid B3. Note: the bedrock is wet because it was washed with a hose while being swept by laborers.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain	X	Overcast	X	Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	02-15-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Office: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Steve O. from CA Rich was on site and oversaw the excavation to bedrock in grids A3 and B3. After excavation occurred, the contractor graded out approve RCA material across those grids. Workers also installed waterproofing and rebar in footings on the west side of the site.

Working In Grids #: A1, A2, B1, B2,

Air Monitoring (Since Last Report):

Air Monitoring was not performed today and no problems were encountered. Monitoring will resume when excavation resumes.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Excavation activities will continue until bedrock is reached in Grids A1, A2, B1, B2, C1, C2, and C3. Excavation will be performed simultaneously with the installation of the water-proofing barrier and select concrete pours of the foundation. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Pure Soil Technologies Jackson Township, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	trucks	Cu yds.	trucks	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	30	Appr 1125	334	Appr. 8,225	18	Appr. 450	24	Appr. 600	277	Appr. 6,925

A total of 5 truckloads of soil were disposed of at the Clean Earth of North Jersey Facility in Mountainside, NJ as hazardous solid due to elevated levels of lead.

Site Grid Map

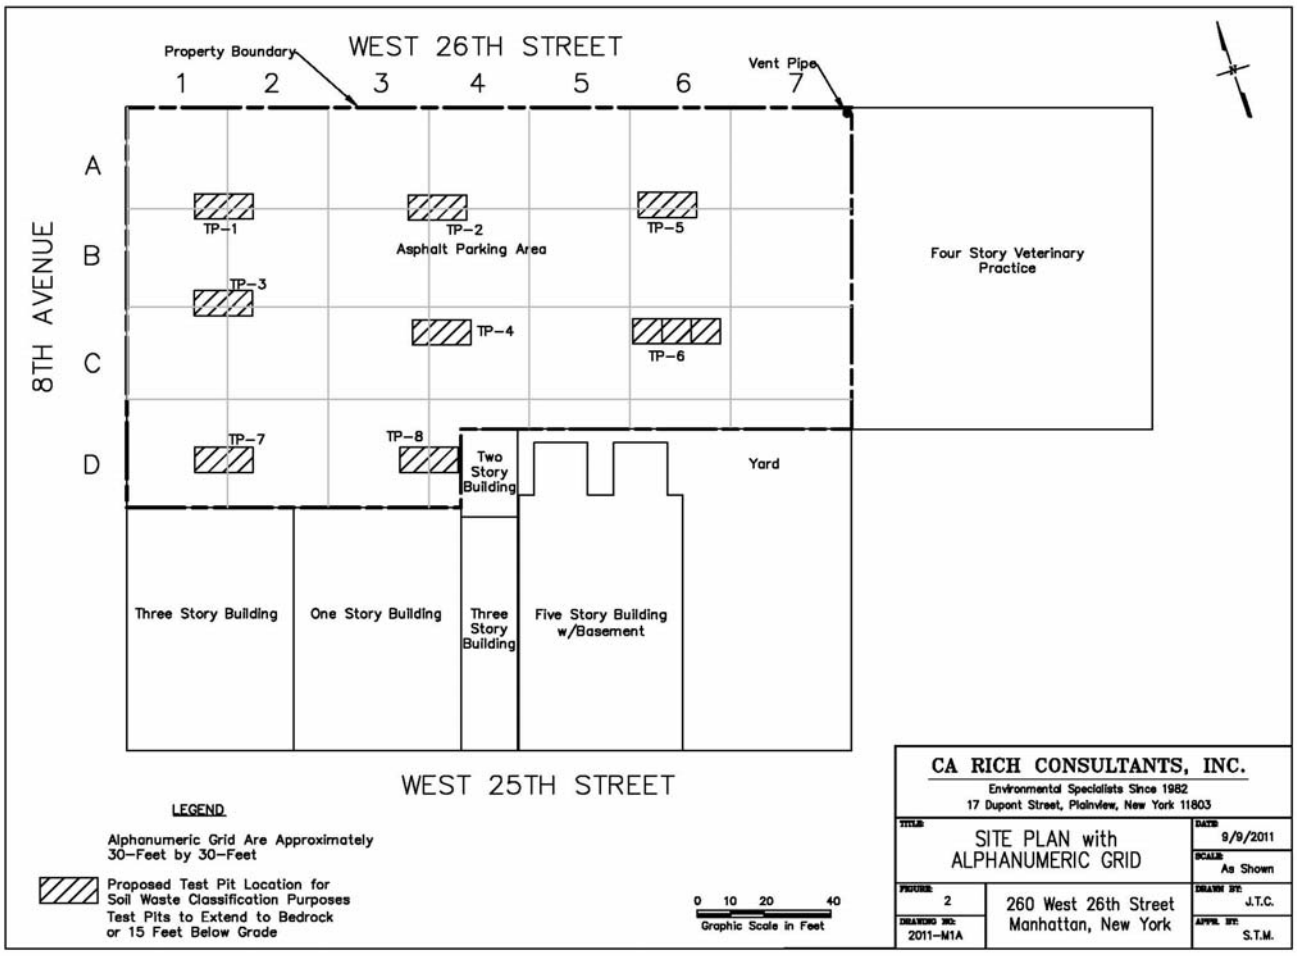

 File Name: _____

Photo Log

Photo 1 – Waterproofing and Rebar was installed in the column footing and concrete was poured.	
Photo 2 – Workers pouring concrete at the Shear Wall #6 Footing.	
Photo 3 – Workers grading out approved RCA bedrock on the west side of the site.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Jessica Proscia of CA RICH

WEATHER	Snow		Rain	X	Overcast		Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	02-16-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Grids A1, B1, A2, and B2 were dug to bedrock to achieve Track 1 Cleanup Criteria. Only Grids C1, C2 and C3 now remain where excavation to bedrock has not been completed. The plan is to finalize the excavation by digging these areas to bedrock in the next two weeks.

Working In Grids #: A1, B1, A2, and B2

Air Monitoring (Since Last Report):

Dust monitoring was not necessary today due to rain.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Excavation activities will continue until bedrock is reached is Grids C1, C2, and C3. Excavation will be performed simultaneously with the installation of the water-proofing barrier and select concrete pours of the foundation. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Pure Soil Technologies Jackson Township, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	trucks	Cu yds.	trucks	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	30	Appr 1125	334	Appr. 8,225	18	Appr. 450	24	Appr. 600	270	Appr. 6,750

A total of 5 truckloads of soil were disposed of at the Clean Earth of North Jersey Facility in Mountainside, NJ as hazardous solid due to elevated levels of lead.

Site Grid Map

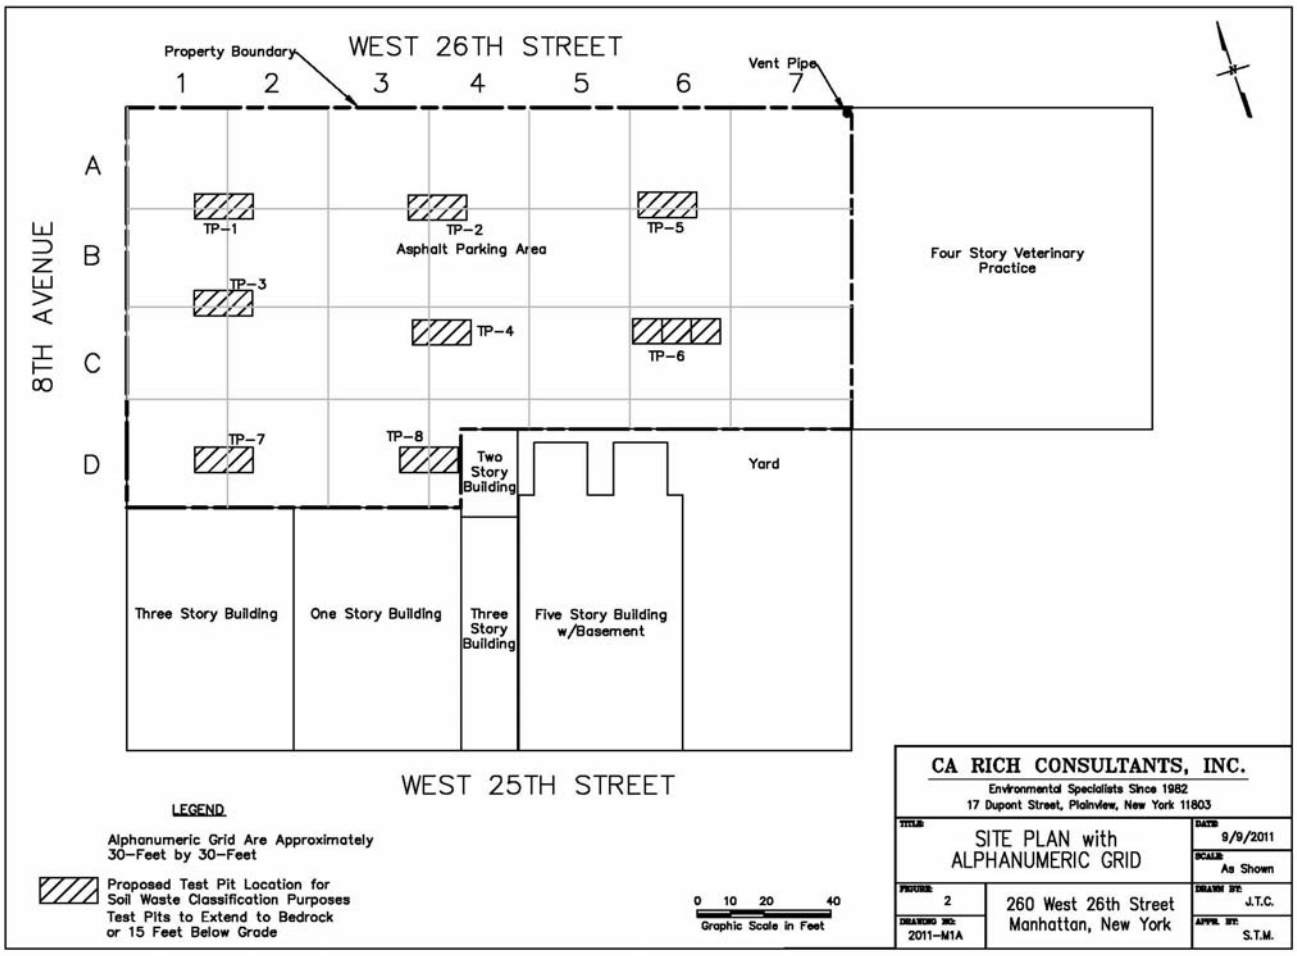

 File Name: _____

Photo Log

Photo 1- Bedrock exposed at the base of excavation in grids A2 and B2.	
Photo 2- Bedrock exposed in base of excavation in grid A1.	
Photo 3- Bedrock exposed in base of excavation in grid A1.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	02-16-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Office: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Workers formed, waterproofed, and installed Rebar on Footings 27, 23, 24, 37, and 60. Workers also installed waterproofing on the west foundation wall.

Working In Grids #: B3, B4, B5, C3, C4, C5, C1, D1

Air Monitoring (Since Last Report):

Air Monitoring was not performed today and no problems were encountered. Monitoring will resume when excavation resumes.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Excavation activities will continue until bedrock is reached in Grids A1, A2, B1, B2, C1, C2, and C3. Excavation will be performed simultaneously with the installation of the water-proofing barrier and select concrete pours of the foundation. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Pure Soil Technologies Jackson Township, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	trucks	Cu yds.	trucks	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	30	Appr 1125	334	Appr. 8,225	18	Appr. 450	24	Appr. 600	277	Appr. 6,925

A total of 5 truckloads of soil were disposed of at the Clean Earth of North Jersey Facility in Mountainside, NJ as hazardous solid due to elevated levels of lead.

Site Grid Map

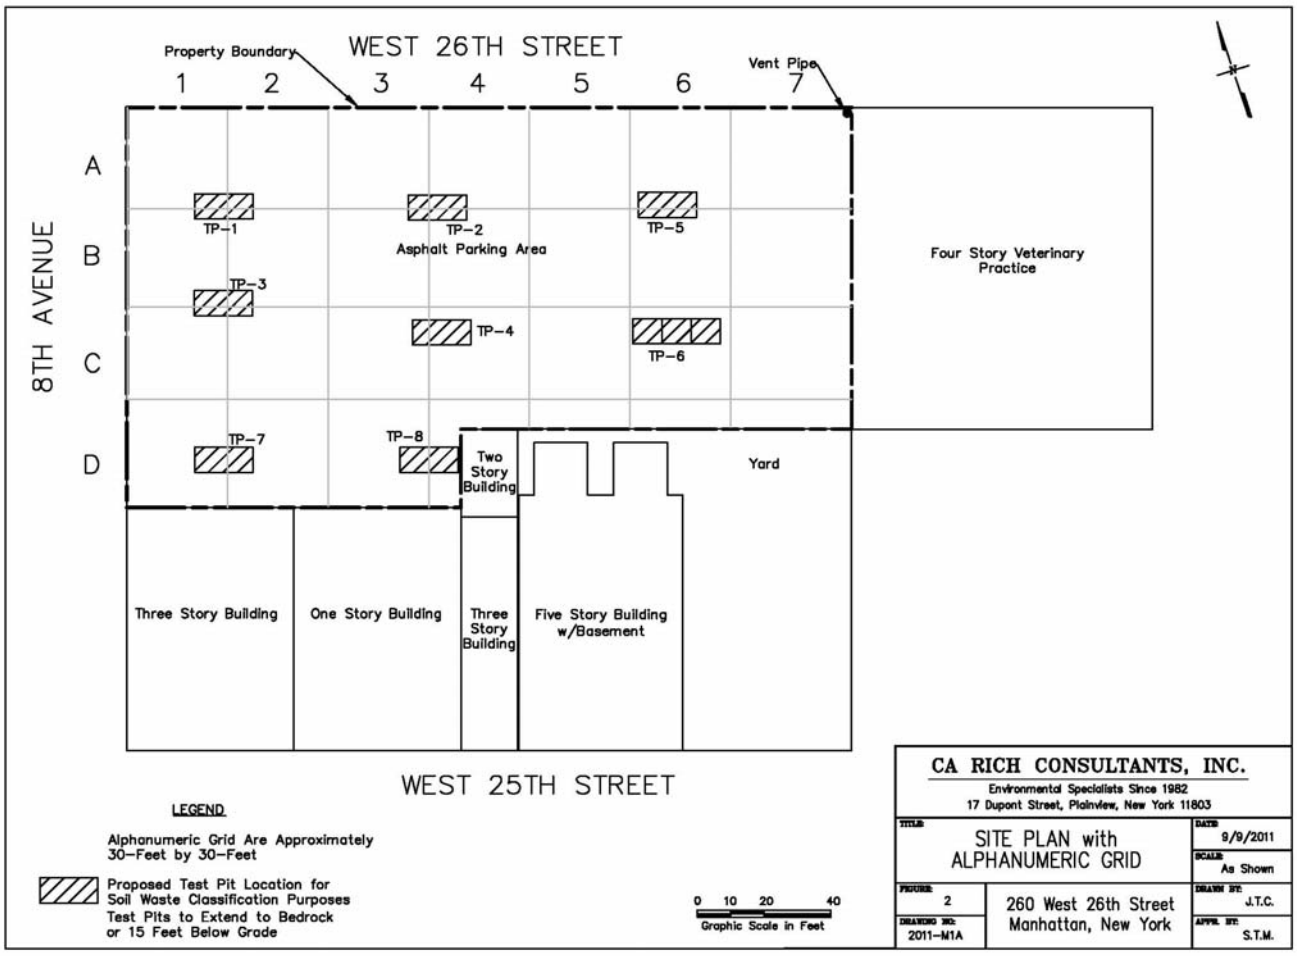

 File Name: _____

Photo Log

Photo 1 – Waterproofing installed on the west foundation wall.	
Photo 2 – Waterproofing and Rebar were installed on numerous footings throughout the site.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain	X	Overcast	X	Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	02-17-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Office: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

(1) Steel Diagonal Raker was installed along the west foundation wall. Rebar started to be installed along the west foundation wall. (15) trucks of DOB approved RCA backfill were delivered to the site and the west half of the slab was graded out. A small section of the slab was poured on the east half of the site after the waterproofing was inspected and appoved.

Working In Grids #: B5, B6, C1, D1, A1, A2, B1, B2

Air Monitoring (Since Last Report):

Air Monitoring was not performed today and no problems were encountered. Monitoring will resume when excavation resumes.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Excavation activities will continue until bedrock is reached in Grids A1, A2, B1, B2, C1, C2, and C3. Excavation will be performed simultaneously with the installation of the water-proofing barrier and select concrete pours of the foundation. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Pure Soil Technologies Jackson Township, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	trucks	Cu yds.	trucks	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	30	Appr 1125	334	Appr. 8,225	18	Appr. 450	24	Appr. 600	277	Appr. 6,925

A total of 5 truckloads of soil were disposed of at the Clean Earth of North Jersey Facility in Mountainside, NJ as hazardous solid due to elevated levels of lead.

Site Grid Map

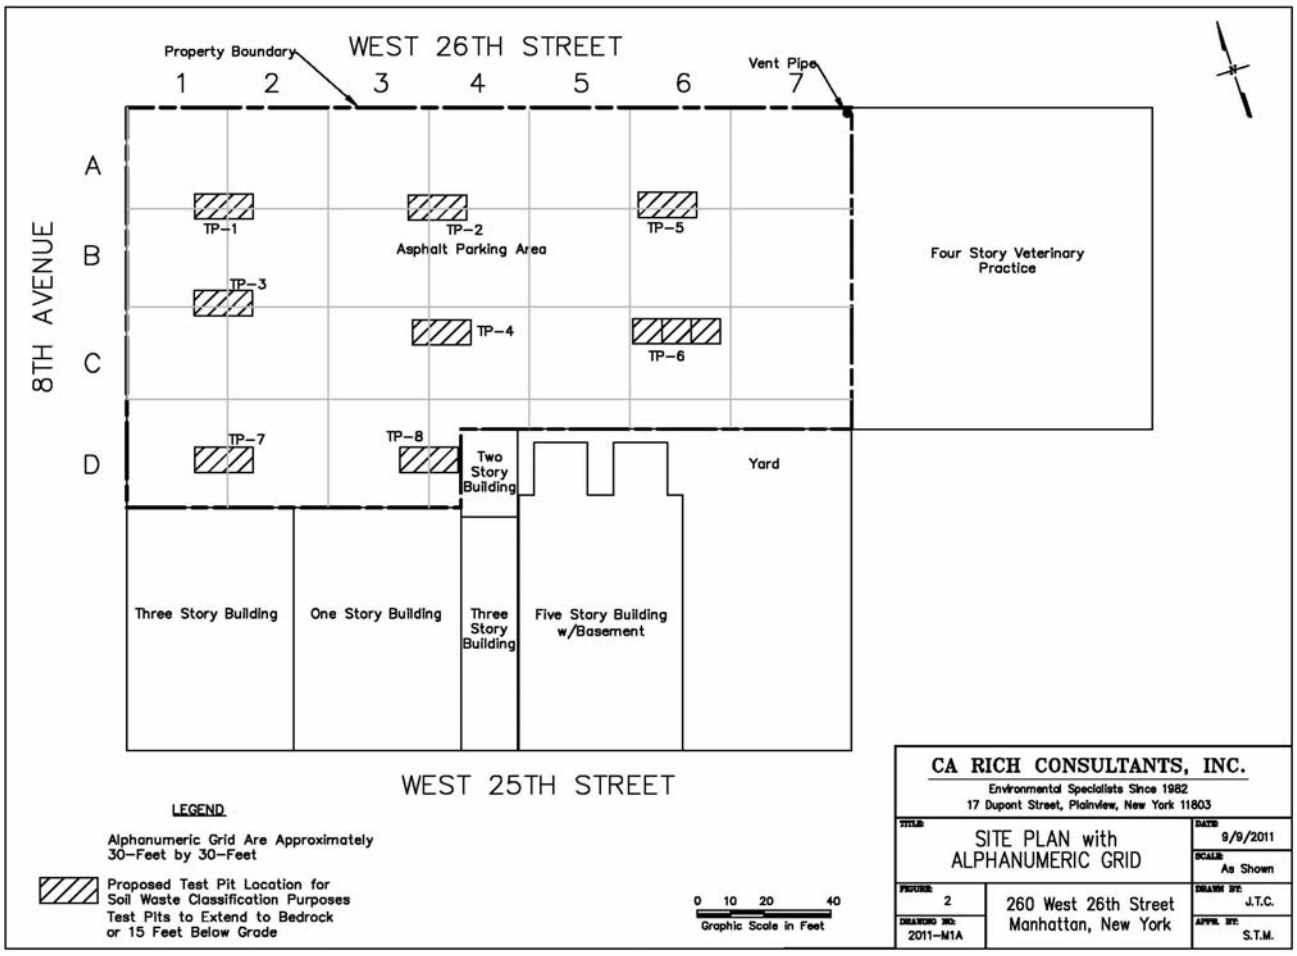

 File Name: _____

Photo Log

Photo 1 – Rebar started to be installed for the west foundation wall.	
Photo 2 – Raker was installed along west foundation wall.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	02-18-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Office: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Rebar was completed along the west foundation wall.

Working In Grids #: C1, D1

Air Monitoring (Since Last Report):

Air Monitoring was not performed today and no problems were encountered. Monitoring will resume when excavation resumes.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Excavation activities will continue until bedrock is reached in Grids A1, A2, B1, B2, C1, C2, and C3. Excavation will be performed simultaneously with the installation of the water-proofing barrier and select concrete pours of the foundation. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Pure Soil Technologies Jackson Township, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	trucks	Cu yds.	trucks	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	30	Appr 1125	334	Appr. 8,225	18	Appr. 450	24	Appr. 600	277	Appr. 6,925

A total of 5 truckloads of soil were disposed of at the Clean Earth of North Jersey Facility in Mountainside, NJ as hazardous solid due to elevated levels of lead.

Site Grid Map

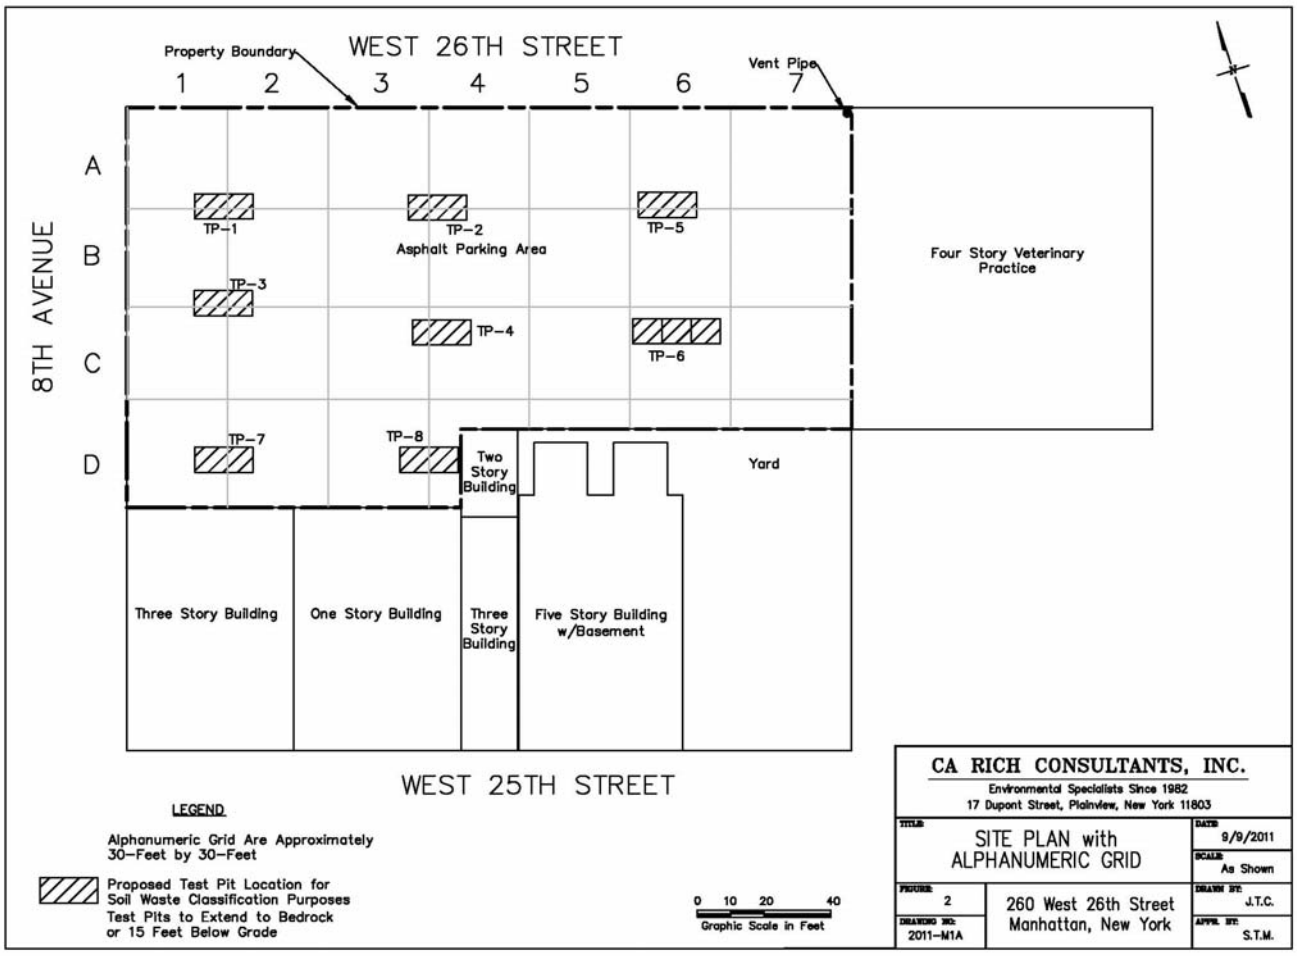

 File Name: _____

Photo Log

Photo 1 – Rebar was completed along the west foundation wall.	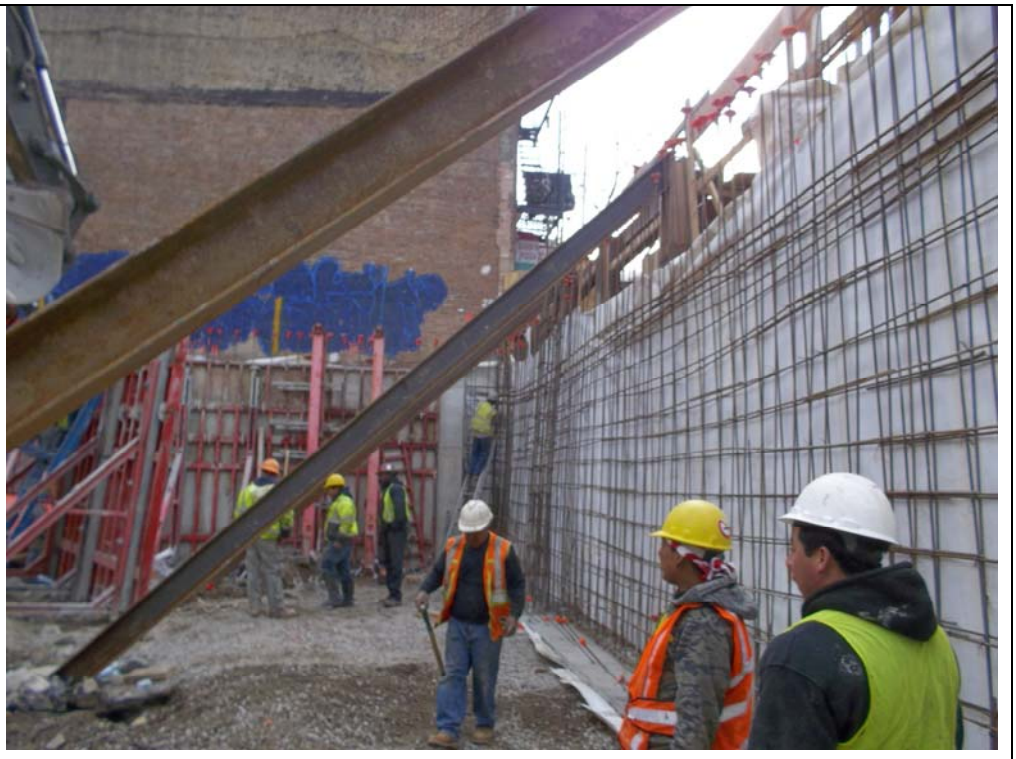

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	02-19-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Office: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Meva Formwork was relocated from the South Wall to the West Wall. Formwork was locked into place and the west wall is ready to be poured tomorrow.

Working In Grids #: C1, D1

Air Monitoring (Since Last Report):

Air Monitoring was not performed today and no problems were encountered. Monitoring will resume when excavation resumes.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Excavation activities will continue until bedrock is reached in Grids A1, A2, B1, B2, C1, C2, and C3. Excavation will be performed simultaneously with the installation of the water-proofing barrier and select concrete pours of the foundation. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Pure Soil Technologies Jackson Township, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	trucks	Cu yds.	trucks	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	30	Appr 1125	334	Appr. 8,225	18	Appr. 450	24	Appr. 600	277	Appr. 6,925

A total of 5 truckloads of soil were disposed of at the Clean Earth of North Jersey Facility in Mountainside, NJ as hazardous solid due to elevated levels of lead.

Site Grid Map

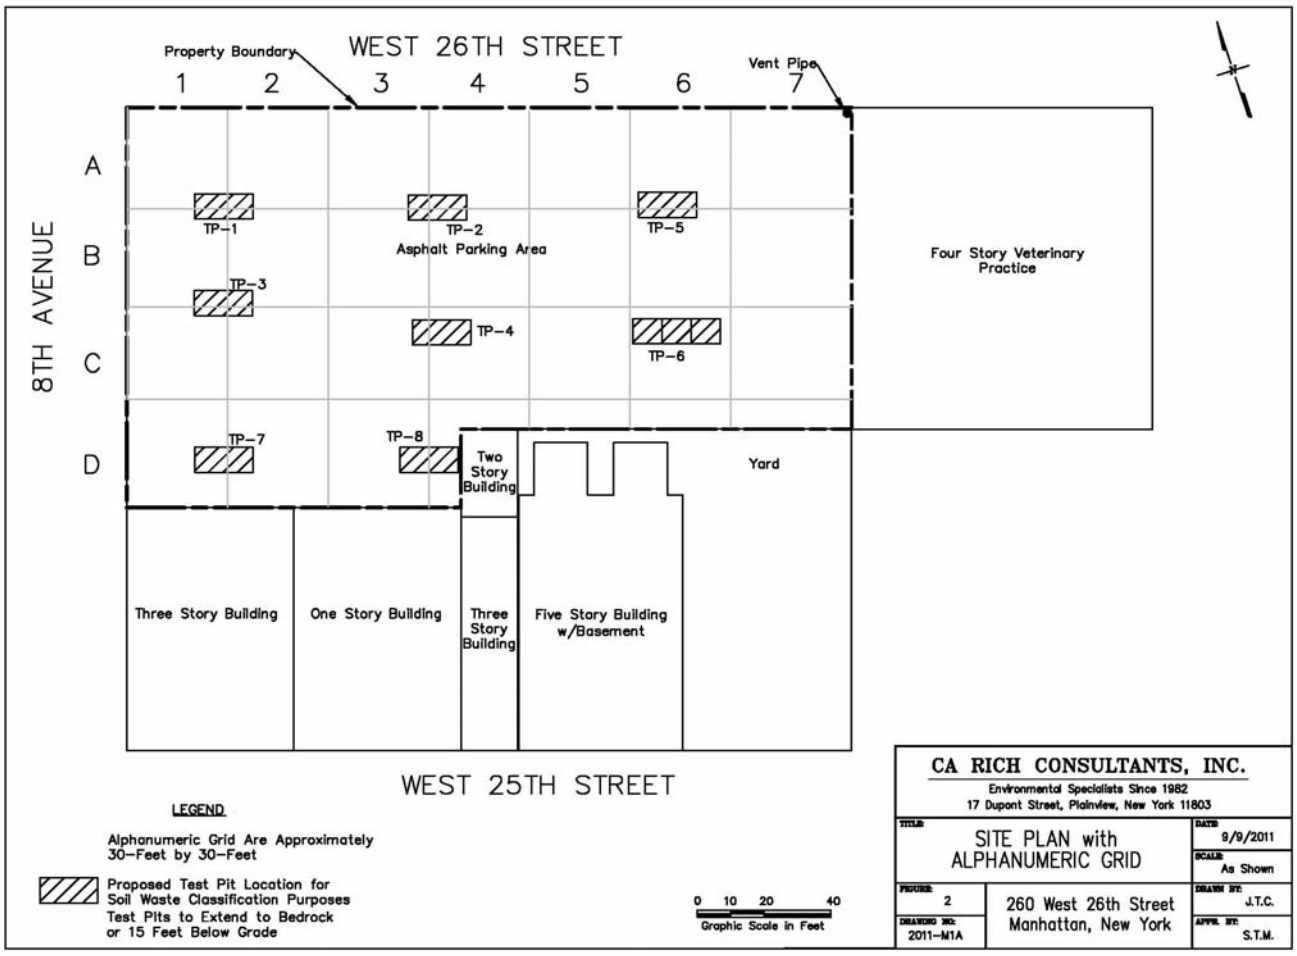

 File Name: _____

Photo Log

Photo 1 – Workers setting Meva Formwork into place along the west foundation wall in preparation for concrete pour tomorrow.	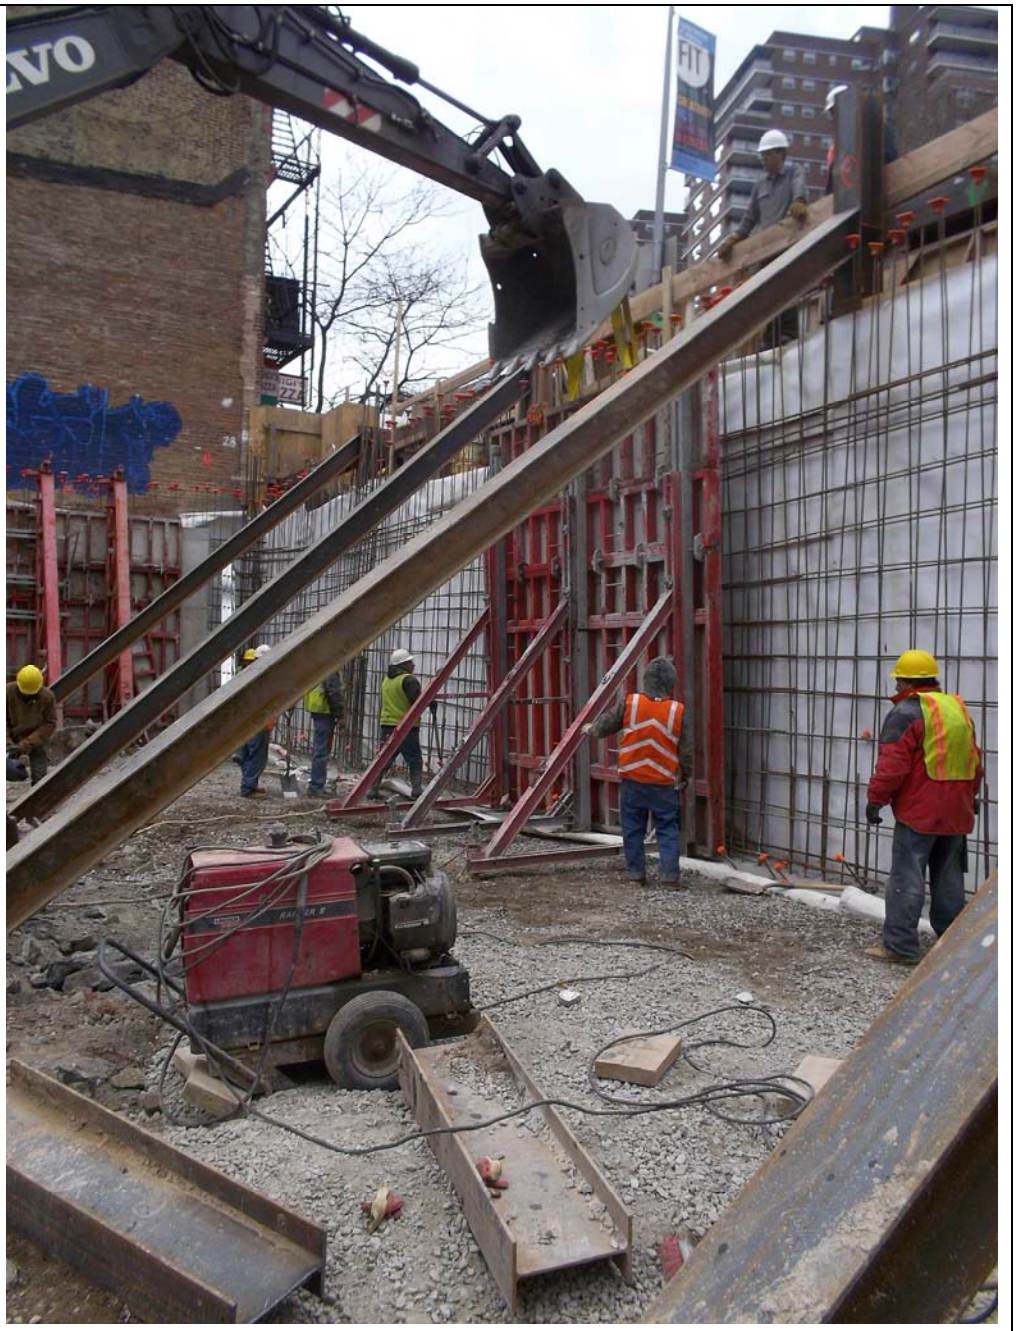

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	02-20-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Office: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Meva Formwork and Scaffolding was completed along the west wall and the West Foundation Wall was poured. As a result, all foundation walls have been completed. Also, a portion of lower slab along the north foundation wall was poured after the waterproofing was inspected carefully.

Working In Grids #: C1, D1, A2, A3, B2, B3

Air Monitoring (Since Last Report):

Air Monitoring was not performed today and no problems were encountered. Monitoring will resume when excavation resumes.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Excavation activities will continue until bedrock is reached in Grids A1, A2, B1, B2, C1, C2, and C3. Excavation will be performed simultaneously with the installation of the water-proofing barrier and select concrete pours of the foundation. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Pure Soil Technologies Jackson Township, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	trucks	Cu yds.	trucks	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	30	Appr 1125	334	Appr. 8,225	18	Appr. 450	24	Appr. 600	277	Appr. 6,925

A total of 5 truckloads of soil were disposed of at the Clean Earth of North Jersey Facility in Mountainside, NJ as hazardous solid due to elevated levels of lead.

Site Grid Map

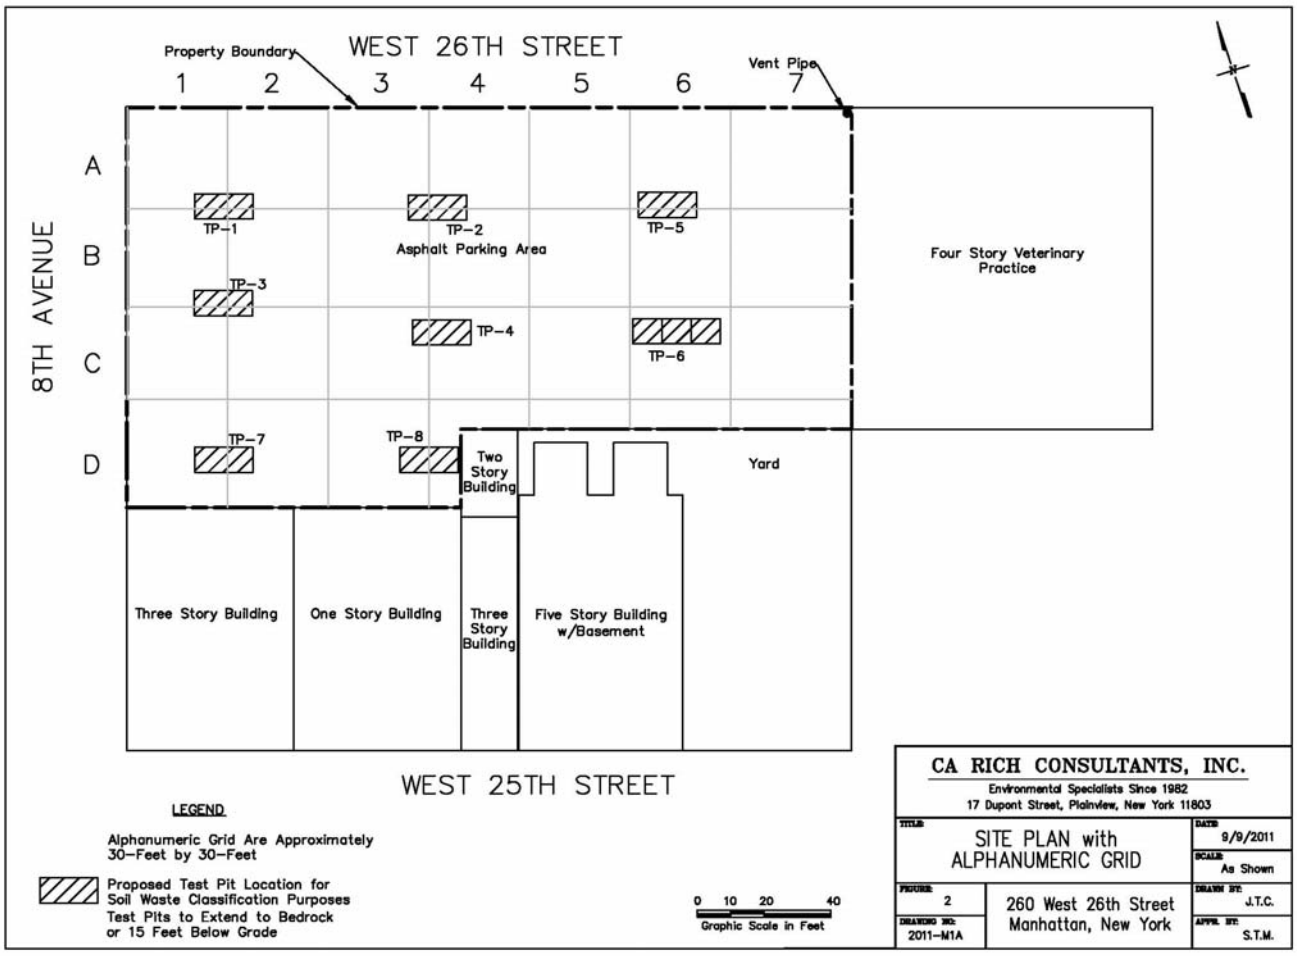

 File Name: _____

Photo Log

Photo 1 – Workers pouring west foundation wall.	
Photo 2 – Workers finalizing layout of rebar and wire mesh in preparation for the slab to be poured.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	02-21-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Office: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

The last waler was installed along the west foundation wall. Formwork and waterproofing were installed for the 3'-0" slab drop on the east half of the site. The 3'-0" slab drop was poured this afternoon. Formwork was stripped from the West Foundation wall.

Working In Grids #: C1, D1, A4, B4, B5, B6, B7,

Air Monitoring (Since Last Report):

Air Monitoring was not performed today and no problems were encountered. Monitoring will resume when excavation resumes.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Excavation activities will continue until bedrock is reached in Grids A1, A2, B1, B2, C1, C2, and C3. Excavation will be performed simultaneously with the installation of the water-proofing barrier and select concrete pours of the foundation. Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Pure Soil Technologies Jackson Township, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	trucks	Cu yds.	trucks	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	30	Appr 1125	334	Appr. 8,225	18	Appr. 450	24	Appr. 600	277	Appr. 6,925

A total of 5 truckloads of soil were disposed of at the Clean Earth of North Jersey Facility in Mountainside, NJ as hazardous solid due to elevated levels of lead.

Site Grid Map

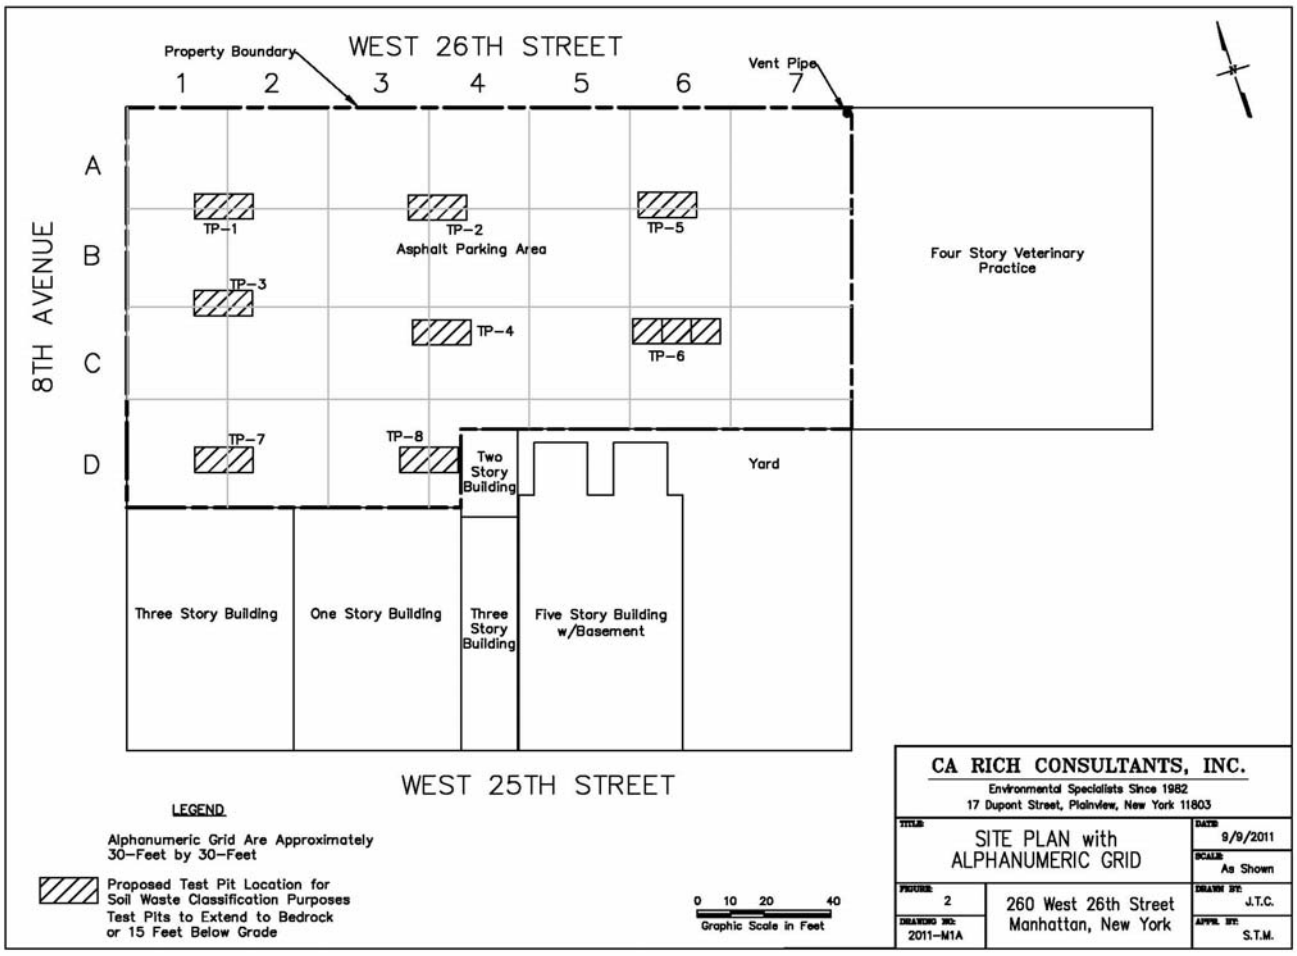

 File Name: _____

Photo Log

Photo 1 – Workers pouring 3’-0” slab drop.	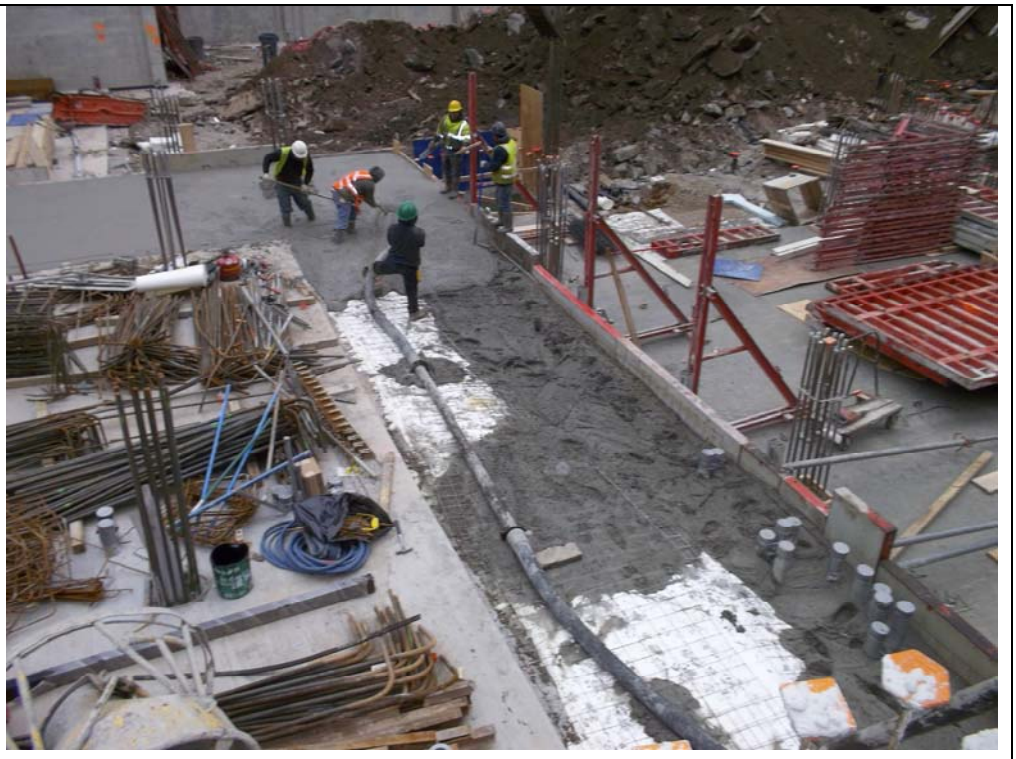
Photo 2 – Workers installing waterproofing at 3’-0” slab drop.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Jessica Proscia of CA RICH

WEATHER	Snow		Rain		Overcast	X	Partly Cloudy		Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	02-22-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Twenty five truckloads of soil were removed from grids C1, C2, and C3 for off-site disposal at the Pure Soil Technologies Facility in Jackson Township, NJ. Grids C2 and C3 have now been fully excavated until bedrock.

Approximately three gallons of engine oil leaked from an on-site excavator in grid C3 resulting in elevated PID readings. The contaminated soil got approved to be disposed of at Pure Soil Technologies and was completely removed. As we discussed, since all of the contaminated soil was properly removed and the grid was dug to bedrock, no further action is required.

Working In Grids #: C1, C2, and C3.

Air Monitoring (Since Last Report):

Air Monitoring was performed today and no problems were encountered.

Problems Encountered:

Approximately three gallons of engine oil leaked from an on-site excavator in grid C3 resulting in elevated PID readings. The contaminated soil got approved to be disposed of at Pure Soil Technologies and was completely removed. As we discussed, since all of the contaminated soil was properly removed and the grid was dug to bedrock, no further action is required.

Planned Activities for Next Week:

Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Pure Soil Technologies Jackson Township, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	trucks	Cu yds.	trucks	Cu. Yds.
			25	625								
Totals (trucks, cu.yds.)	84	2,100	55	Appr 1750	334	Appr. 8,225	18	Appr. 450	24	Appr. 600	270	Appr. 6,750

A total of 5 truckloads of soil were disposed of at the Clean Earth of North Jersey Facility in Mountainside, NJ as hazardous solid due to elevated levels of lead.

Site Grid Map

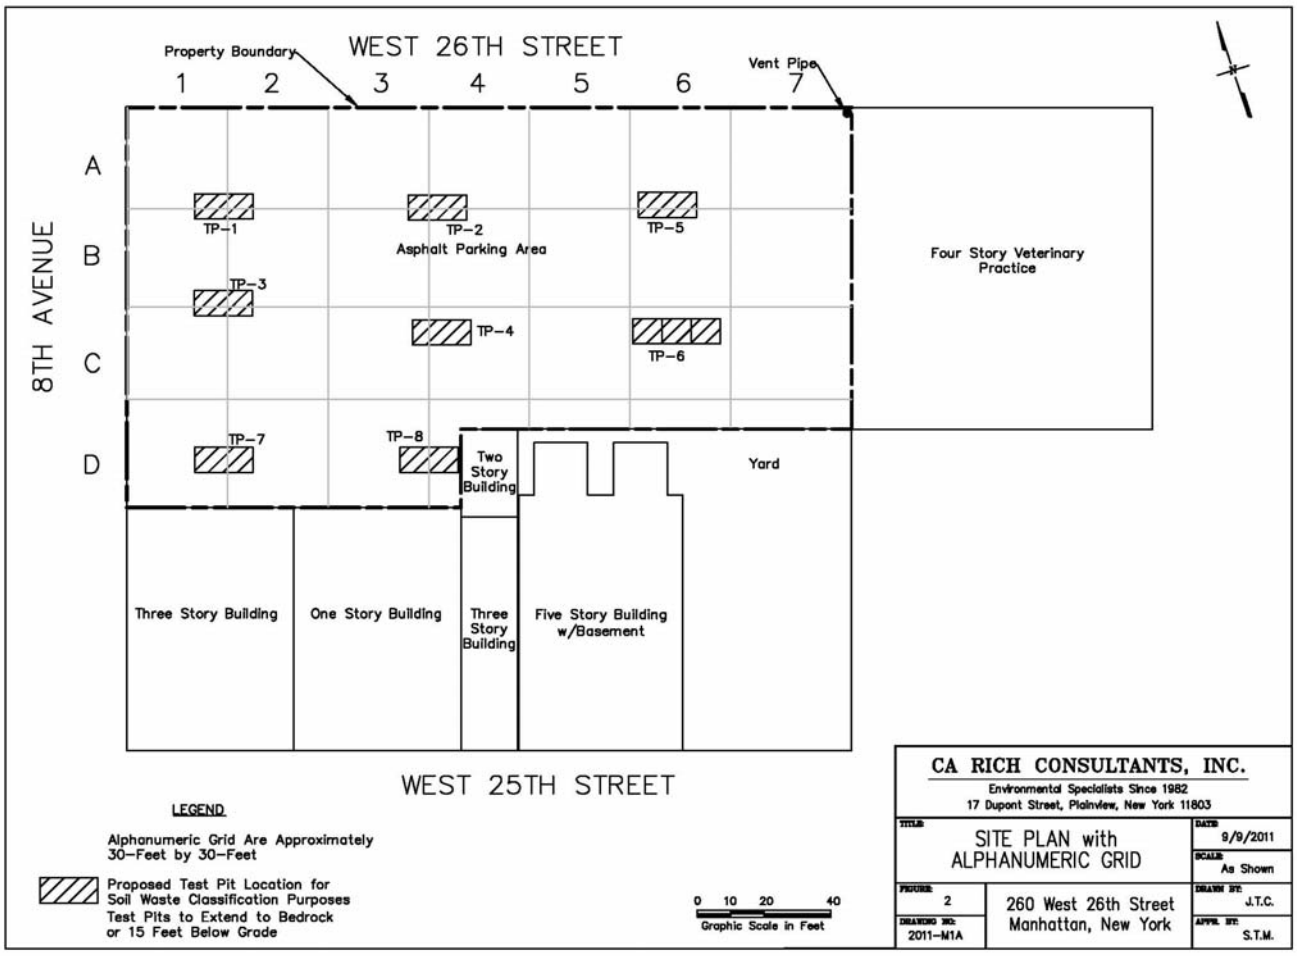

 File Name: _____

Photo Log

Photo 1- Excavation of ramp in grids C1, C2, and C3 with off-site shipping to Pure Soil Technologies.	
Photo 2- Bedrock at final depth of excavation in grids C2 and C3.	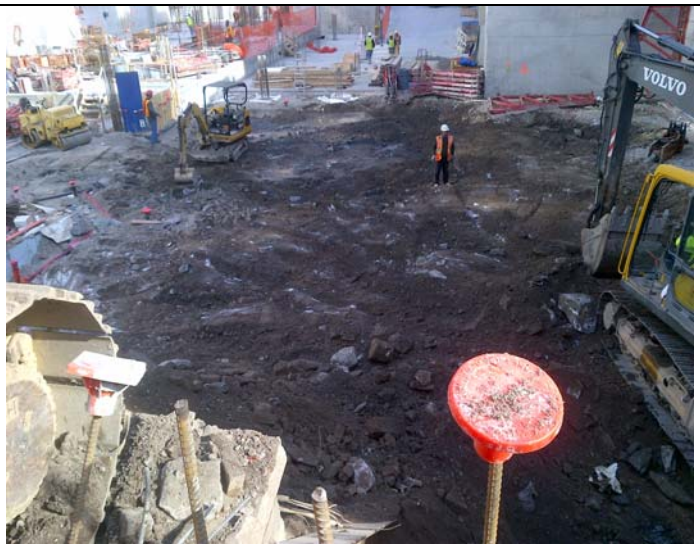
Photo 3- View of contaminated soil (before removal) in grid C3.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Jessica Proscia of CA RICH

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	02-23-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Five truckloads of soil were removed from grid C1 for off-site disposal at the Pure Soil Technologies Facility in Jackson Township, NJ. Grid C1 has now been fully excavated until bedrock.

All grids have now been dug to bedrock to achieve Track 1 Cleanup Criteria.

Working In Grids #: C1

Air Monitoring (Since Last Report):

Air Monitoring was performed today and no problems were encountered.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Pure Soil Technologies Jackson Township, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	trucks	Cu yds.	trucks	Cu. Yds.
			5	125								
Totals (trucks, cu.yds.)	84	2,100	60	Appr 1875	334	Appr. 8,225	18	Appr. 450	24	Appr. 600	270	Appr. 6,750

A total of 5 truckloads of soil were disposed of at the Clean Earth of North Jersey Facility in Mountainside, NJ as hazardous solid due to elevated levels of lead.

Site Grid Map

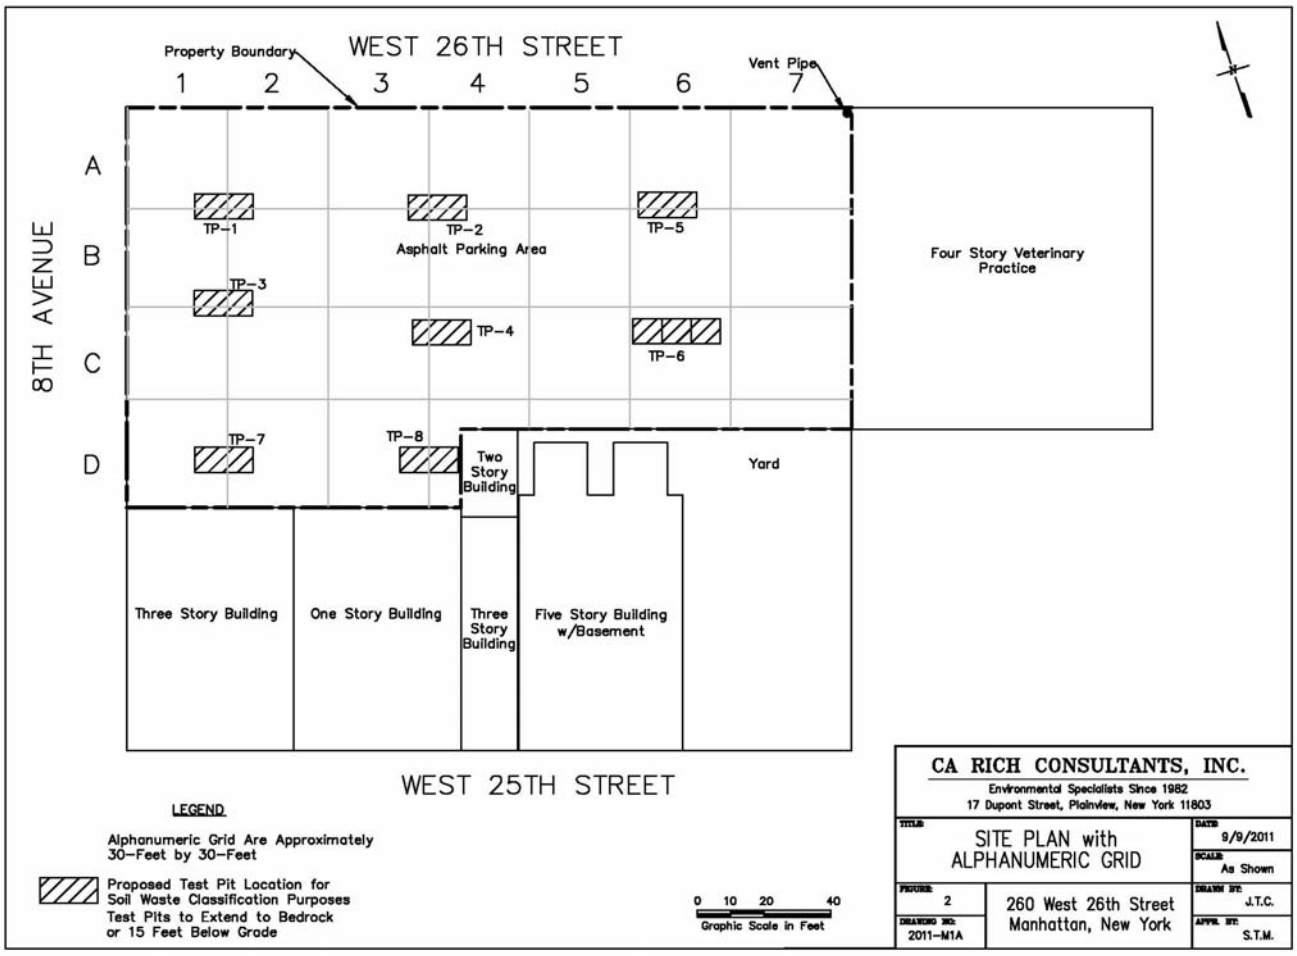

 File Name: _____

Photo Log

Photo 1- Excavation of ramp in grid C1 with off-site shipping to Pure Soil Technologies.	
Photo 2- Bedrock at final depth of excavation in grid C1.	
Photo 3- View of southwestern portion of the Site.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	02-24-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Office: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

All formwork was removed from the site. A large section of the west slab was prepped and waterproofed including the location of the hoist pad and column footings. After waterproofing was inspected, wire mesh was installed in preparation for pour tomorrow.

Working In Grids #: C1, D1, A4, B4, B5, B6, B7,

Air Monitoring (Since Last Report):

Air Monitoring was not performed today and no problems were encountered. Monitoring will resume when excavation resumes.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Formwork and Rebar for footings, foundation walls, and elevator pits will continue to be installed throughout the week. Concrete for Footings and Walls will continue throughout the week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Pure Soil Technologies Jackson Township, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	trucks	Cu yds.	trucks	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	60	Appr 1875	334	Appr. 8,225	18	Appr. 450	24	Appr. 600	277	Appr. 6,925

A total of 5 truckloads of soil were disposed of at the Clean Earth of North Jersey Facility in Mountainside, NJ as hazardous solid due to elevated levels of lead.

Site Grid Map

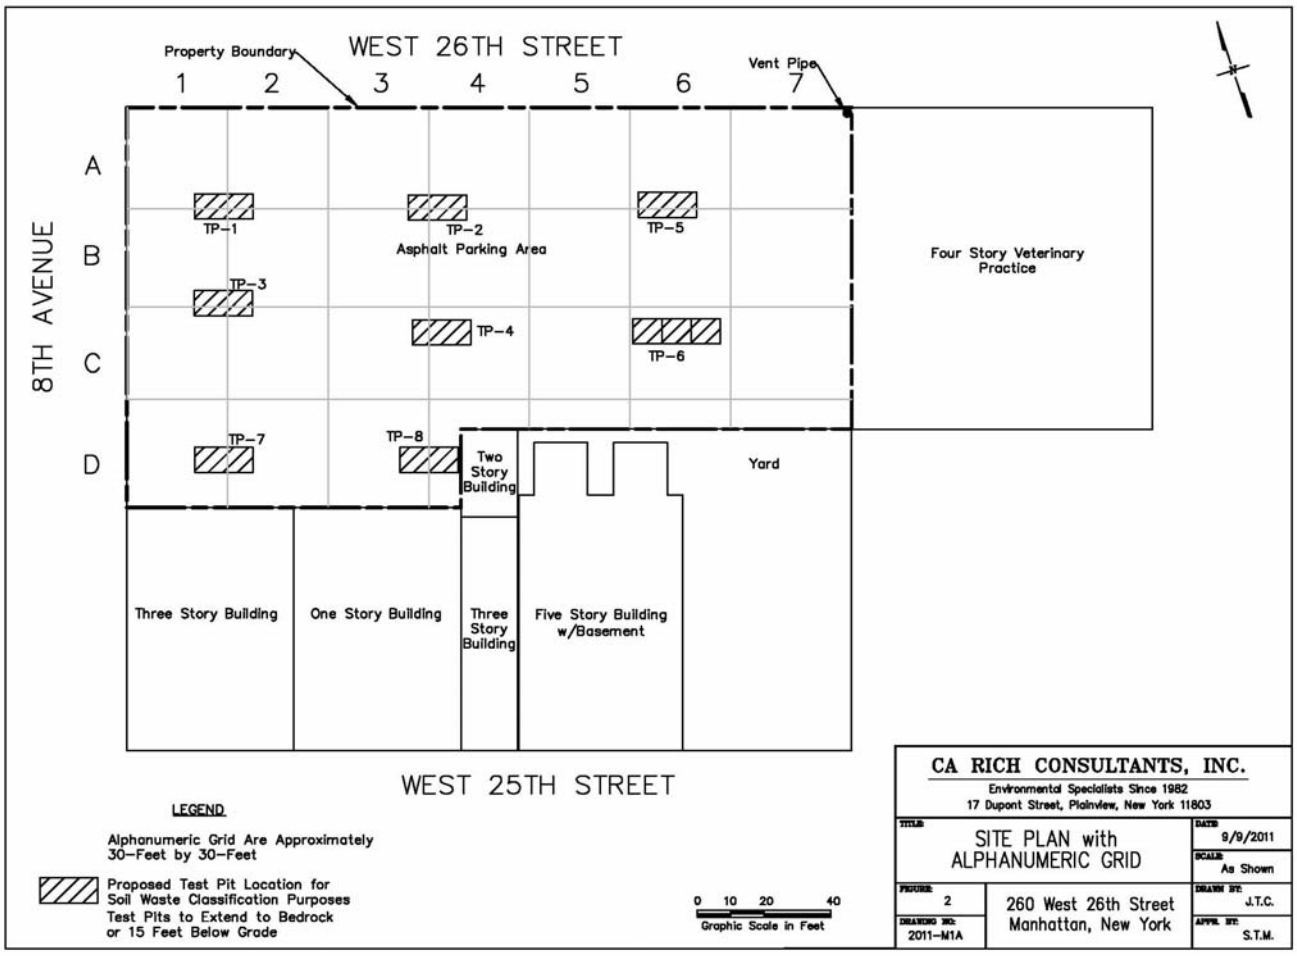

 File Name: _____

Photo Log

Photo 1 – Formwork being removed from the site.	
Photo 2 – Workers forming for hoist pad installation.	
Photo 3 – Waterproofing and Rebar was installed for columns in the southwest corner of the site.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	02-25-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Office: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Workers installed waterproofing throughout the west half of the slab and after waterproofing passed inspection, the slab was poured.

Working In Grids #: A1, A2, B1, B2, C1, C2

Air Monitoring (Since Last Report):

Air Monitoring was not performed today and no problems were encountered. Monitoring will resume when excavation resumes.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

All foundation walls and pits are complete. The west half of the cellar slab will be completed this coming week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Pure Soil Technologies Jackson Township, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	trucks	Cu yds.	trucks	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	60	Appr 1875	334	Appr. 8,225	18	Appr. 450	24	Appr. 600	277	Appr. 6,925

A total of 5 truckloads of soil were disposed of at the Clean Earth of North Jersey Facility in Mountainside, NJ as hazardous solid due to elevated levels of lead.

Site Grid Map

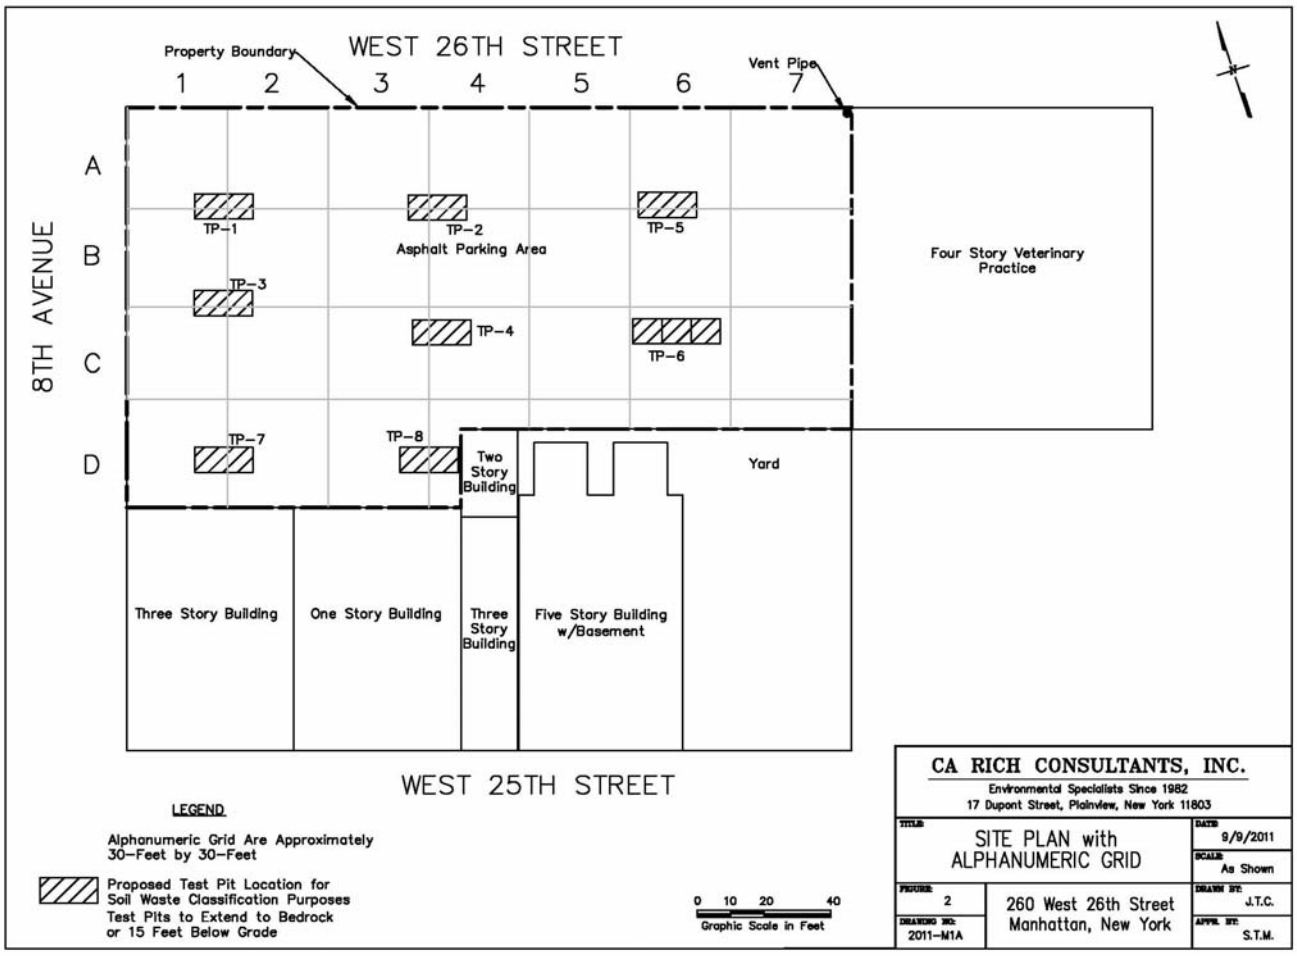

 File Name: _____

Photo Log

Photo 1 – Workers installing waterproofing on the west half of the site in preparation for the pour today.	
Photo 2 – Corner of formed completely sealed with the waterproofing.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	02-27-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Office: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

Workers installed the remaining waterproofing in the southwest corner of the site.

Working In Grids #: C1, C2, D1, D2

Air Monitoring (Since Last Report):

Air Monitoring was not performed today and no problems were encountered. Monitoring will resume when excavation resumes.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

All foundation walls and pits are complete. The west half of the cellar slab will be completed this coming week.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Pure Soil Technologies Jackson Township, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	trucks	Cu yds.	trucks	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	60	Appr 1875	334	Appr. 8,225	18	Appr. 450	24	Appr. 600	277	Appr. 6,925

A total of 5 truckloads of soil were disposed of at the Clean Earth of North Jersey Facility in Mountainside, NJ as hazardous solid due to elevated levels of lead.

Site Grid Map

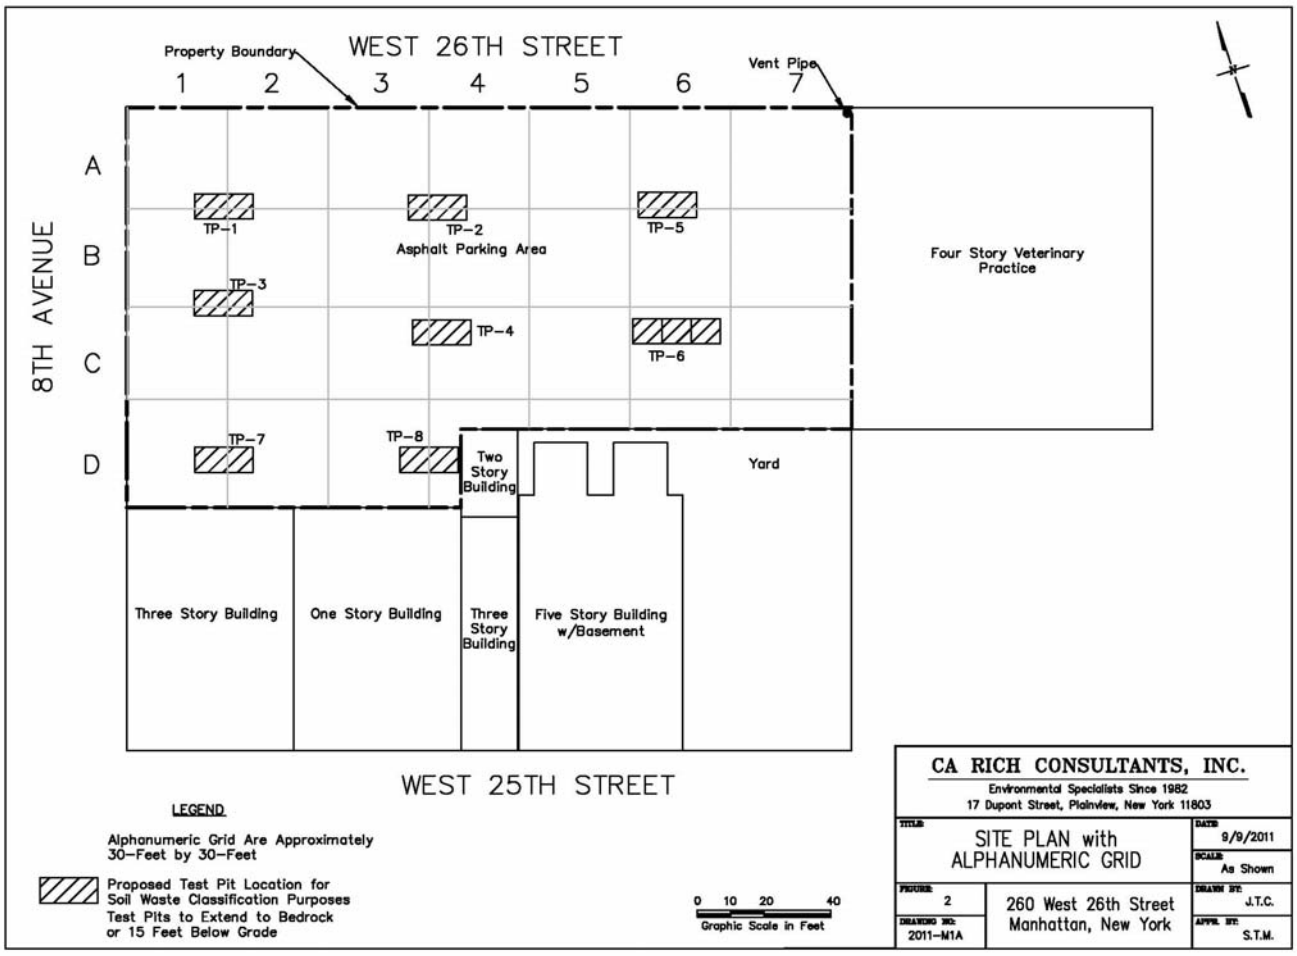

 File Name: _____

Photo Log

Photo 1 – Workers installing waterproofing and wire mesh in preparation for the pour tomorrow.	

 File Name: _____

DAILY STATUS REPORT

Prepared By: Dan Manore of Artimus

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	TO 32		32-50	X	50-70		70-85		>85	

BCP Project No:	11CBCP011M	E-Number:	11EHAZ246M	Date:	02-28-12
Project Name:	260 West 26th Street				

Consultant: CA RICH Consultants, Inc.	Safety Officer: Jessica Proscia Alternate Safety Office: Dan Manore
Contractor: Chelsea W26 LLC	

Work Activities Performed (Since Last Report):

The final waterproofing/vapor barrier inspection was today and the final portion of the cellar slab was poured. Foundation is complete.

Working In Grids #: C1, C2, D1, D2

Air Monitoring (Since Last Report):

Air Monitoring was not performed today and no problems were encountered. Monitoring will resume when excavation resumes.

Problems Encountered:

No problems to report.

Planned Activities for Next Week:

Foundation is complete. This will be the last Daily Report.

 File Name: _____

Facility # Name/ location type of waste	Bayshore Recycling Woodbridge, NJ Solid		Pure Soil Technologies Jackson Township, NJ Solid		Soil Safe Logan Township, NJ Solid		Bellmarw Waterfront Redevelopment Site Bellmarw, NJ Solid		Pave Co. Medford, NY Solid/Rock		Red Roc Materials Lyndhurst, NJ 07071 Solid/Rock	
Today (trucks, cu.yds.)	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	trucks	Cu yds.	trucks	Cu. Yds.
Totals (trucks, cu.yds.)	84	2,100	60	Appr 1875	334	Appr. 8,225	18	Appr. 450	24	Appr. 600	322	Appr. 8050

A total of 5 truckloads of soil were disposed of at the Clean Earth of North Jersey Facility in Mountainside, NJ as hazardous solid due to elevated levels of lead.

Site Grid Map

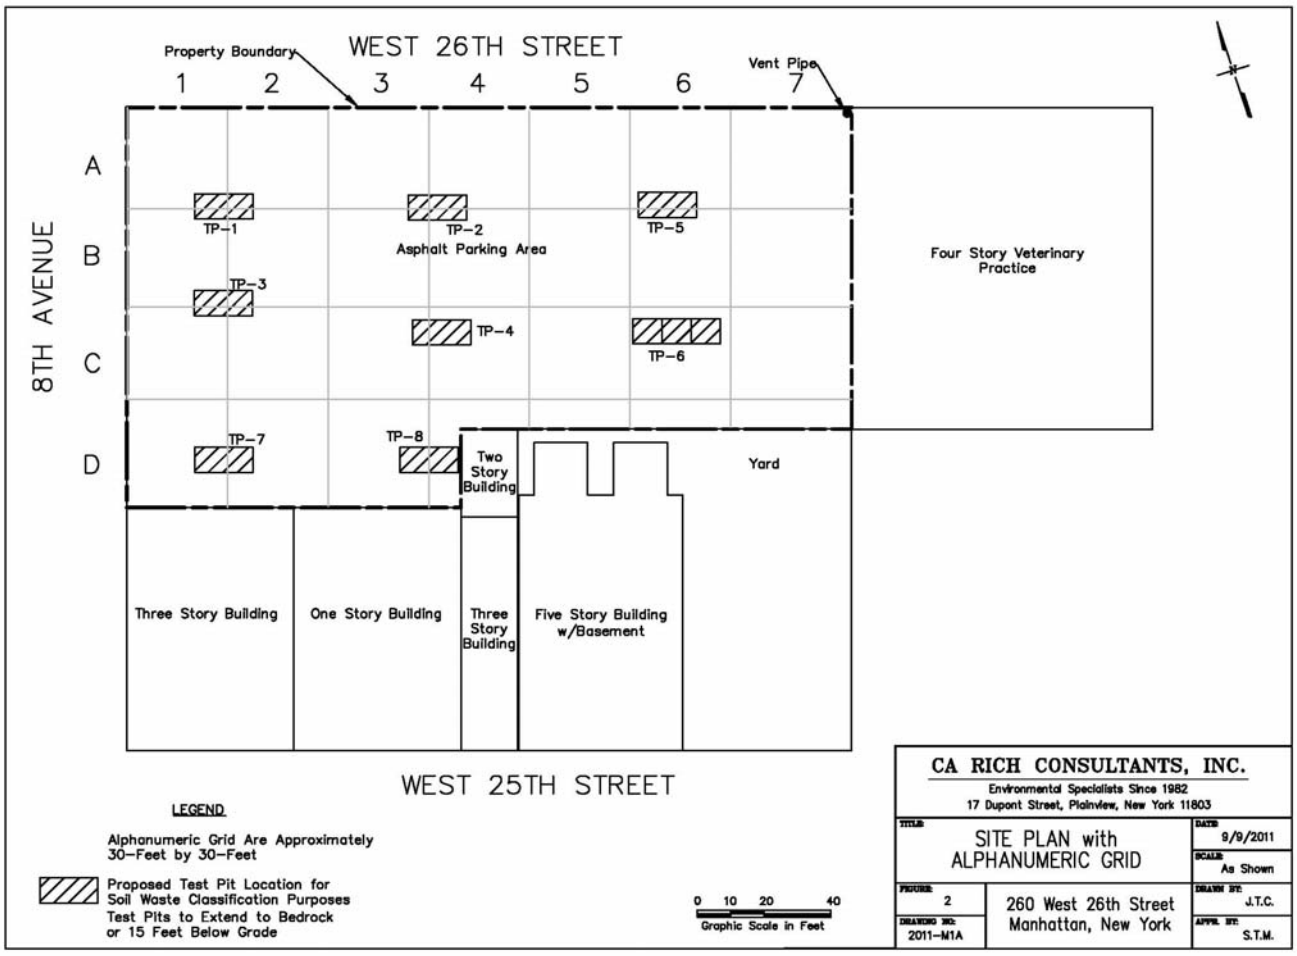

 File Name: _____

Photo Log

Photo 1 – Workers installed wire mesh after final waterproofing inspection was approved.	
Photo 2 – The final portion of the slab was poured. Foundation is complete.	

 File Name: _____

APPENDIX G

Soil Profile Report with Waste Classification Data

September 29, 2011

Soil Safe Solutions Group
2545 Hempstead Turnpike,Ste201
East Meadow, NY 11554

Attention: Stephen Shapiro

Re: Waste Classification Sampling Report
260 West 26th Street
New York, NY
NYCBCP Site # 11CBCP011M

Dear Mr. Shapiro:

CA Rich Consultants, Inc. (CA RICH) is pleased to provide Soil Safe Solutions Group with this Waste Classification Sampling Report for the above-referenced location (the Site). This report has been prepared for use as supplemental information to support soil disposal activities necessary to install a new approximately 15-foot deep building foundation at the Site. CA RICH is assisting the Site Owner in redeveloping the property under the New York City Brownfield Cleanup Program. The construction is being conducted in accordance with a Remedial Action Work Plan (RAWP) (Ref.1) approved by the New York City Office of Environmental Remediation. The RAWP requires that all soil removed during the installation of the new foundation undergo testing and be properly disposed of in accordance with all Federal, State and local regulations.

Site Location and Description

The Site is located at 260 West 26th Street in the Chelsea section of New York, New York and is identified as Block: 775; Lots: 4, 69, 77, 78, 79, and 80 on the New York City Tax Map. Figure 1 shows the Site location. The Site area is 26,000 square feet and is bounded by West 26th Street to the north, residential and commercial buildings to the south, a four-story veterinary practice to the east, and Eighth Avenue to the west. Until recently, the Site consisted of a two-story building and an asphalt-covered automotive parking lot. The building which was last used as a video store and art gallery was demolished in August 2011. The Site is currently a fenced-off construction site preparing for a site-wide excavation to approximately 15-feet deep. As the foundation excavation proceeds, it is estimated that approximately 9,000 tons of soil may require off-site disposal. The construction team plans to mechanically screen brick, concrete and debris from the material prior disposal. The final volume of soil will be dependent upon the depth to bedrock and amount of brick concrete and debris screened-out prior to loading for disposal.

Description of Soil Sampling Procedures

On August 30, 2011, a track-mounted excavator was utilized to install eight test pits identified as TP-1 through TP-8 in a uniform pattern across the Site. Each test pit was extended from grade to approximately 15 feet deep or bedrock (whichever was shallower). During the excavation activities, CA RICH personnel continuously screened the subsurface soil for Volatile Organic Compounds (VOCs) with a Photo-Ionization Detector (PID) for evidence of volatile organic contamination. There were no PID readings observed during the sampling event. Soil samples were collected from the test pits in accordance with the frequency criteria required by the proposed disposal facilities and the approved-RAWP for the Site.

The sampling included the collection of a discrete grab sample from middle sidewall of each test pit for VOCs using the En Core sampling method. An additional discrete sample for VOCS was collected with an En Core sample from the lower middle sidewall of test pits TP-1, TP-2, TP-3 and TP-4 for a total of 12 VOC samples. A five-point composite sample was collected from the sidewalls and bottom of test pits TP-5, TP-6, TP-7 and TP-8 for an expanded list of chemical parameters in order to meet the acceptance criteria of multiple beneficial reuse facilities. For test pits TP-1, TP-2, TP-3 and TP-4, one five-point composite sample was collected from 0-7 feet and a second from 7 - 14 feet for the expanded list of chemical parameters. In addition, 12 additional five-point composite samples were collected for Total Petroleum Hydrocarbons.

Gloves worn for sample handling were discarded between sample collections. All soil samples were placed in lab-supplied containers, stored in an ice-filled cooler and submitted to American Analytical Laboratories (a State-certified laboratory located in Farmingdale, NY) for analysis. Copies of the soil test results are attached to this report. A Site plan depicting test pit locations is included as Figure 2.

The Chain-of-Custody program allows for the tracing of possession and handling of the sample from its time of collection through its chemical analysis in the laboratory. The chain-of-custody program at this Site included:

- Sample labels
- Chain-of-Custody records
- Field records

To prevent misidentification of samples, a label was affixed to the sample container and contained the following information:

- Site Name
- Sample identification number
- Date and time of collection
- Name of Sampler
- Preservation (if any)
- Type of analysis to be conducted

To establish the documentation necessary to trace sample possession from the time of collection, a chain-of-custody record was filled out and accompanied samples at all times. The record contained the following information:

- Project name
- Printed name and signature of samplers
- Sample number
- Date and time of collection
- Sampling location
- Number of containers for each sample
- Signature of individuals involved in sample transfer (when relinquishing and accepting samples)
- Inclusive dates and times of possession

Field records were maintained during each sampling effort in a logbook and on field sampling forms. All aspects of sample collection, handling and visual observations were recorded. All sample collection equipment, field analytical equipment and equipment utilized to make physical measurements were identified in the field logbook. Entries were made in ink, dated and initialed.

The fundamental Quality Assurance objective with respect to accuracy, precision, and sensitivity of analysis for laboratory analytical data is to achieve the QC acceptance of the analytical protocol. The accuracy, precision and completeness requirements were addressed by the laboratory for all data generated.

Collected samples were appropriately packaged, placed in coolers and shipped or delivered directly to the analytical laboratory by field personnel. Samples were containerized in appropriate laboratory

provided glassware and shipped in plastic coolers. Samples were preserved to maintain a temperature of 4°C.

Grab samples were collected using a clean stainless steel trowel and placed into jars using clean dedicated tongue depressors. Samples were composited using a clean stainless steel bowl and trowel. Decontamination of non-dedicated sampling equipment consisted of the following:

- Gently tap or scrape to remove adhered soil;
- Rinse with tap water;
- Wash with alconox® detergent solution and scrub;
- Rinse with tap water;
- Rinse with distilled or de-ionized water;

Conclusion

A total of 12 grab samples for VOCs, 12 five-point composite samples for TPH, and 12 five-point composite samples for an expanded list of testing parameters were collected to profile the soil for disposal prior to the start of excavation activities. Based on our review of the test results and preliminary discussions with Soil Safe, test pits TP-5 and TP-7 must be disposed of as lead contaminated hazardous soil while the remainder of the soil would qualify for disposal at Soil Safe's facility in Logan, New Jersey or for beneficial reuse at the Bellmarw Redevelopment site. The construction plan is to first remove the hazardous soil identified in test pits TP-5 and TP-7 and conduct additional sampling for total and TCLP lead to confirm all soil with hazardous levels of lead was removed. Upon completion of your review, kindly provide us with an acceptance letter from the facility(s) indicating that they will accept this material from the 260 West 26th Street job Site.

If you have any questions regarding the information presented in this report, please feel free to call our office.

Sincerely,

CA RICH CONSULTANTS, INC.

Stephen T. Malinowski

Stephen T. Malinowski
Associate

cc: Amnon Solomon, Artimus Contrsuction

REFERENCE

1) CA RICH Consultants, Inc. April 2011. Remedial Action Work Plan, 260 West 26th Street, New York, New York

September 20, 2011

Nipam Shah
Senior Environmental Project Manager
Clean Earth Inc.
115 Jacobus Avenue
Kearny, NJ 07032

Re: Waste Classification Sampling Report
260 West 26th Street
New York, NY
NYCBCP Site # 11CBCP011M

Dear Mr. Shah:

CA Rich Consultants, Inc. (CA RICH) is pleased to provide Clean Earth Inc. with this Waste Classification Sampling Report for the above-referenced location (the Site). This report has been prepared for use as supplemental information to support soil disposal activities necessary to install a new approximately 15-foot deep building foundation at the Site. CA RICH is assisting the Site Owner in redeveloping the property under the New York City Brownfield Cleanup Program. The construction is being conducted in accordance with a Remedial Action Work Plan (RAWP) (Ref.1) approved by the New York City Office of Environmental Remediation. The RAWP requires that all soil removed during the installation of the new foundation undergo testing and be properly disposed of in accordance with all Federal, State and local regulations.

Site Location and Description

The Site is located at 260 West 26th Street in the Chelsea section of New York, New York and is identified as Block: 775; Lots: 4, 69, 77, 78, 79, and 80 on the New York City Tax Map. Figure 1 shows the Site location. The Site area is 26,000 square feet and is bounded by West 26th Street to the north, residential and commercial buildings to the south, a four-story veterinary practice to the east, and Eighth Avenue to the west. Until recently, the Site consisted of a two-story building and an asphalt-covered automotive parking lot. The building which was last used as a video store and art gallery was demolished in August 2011. The Site is currently a fenced-off construction site preparing for a site-wide excavation to approximately 15-feet deep. As the foundation excavation proceeds, it is estimated that approximately 9,000 tons of soil may require off-site disposal. The construction team plans to mechanically screen brick, concrete and debris from the material prior disposal. The final volume of soil will be dependent upon the depth to bedrock and amount of brick concrete and debris screened-out prior to loading for disposal.

Description of Soil Sampling Procedures

On August 30, 2011, a track-mounted excavator was utilized to install eight test pits identified as TP-1 through TP-8 in a uniform pattern across the Site. Each test pit was extended from grade to approximately 15 feet deep or bedrock (whichever was shallower). During the excavation activities, CA RICH personnel continuously screened the subsurface soil for Volatile Organic Compounds (VOCs) with a Photo-Ionization Detector (PID) for evidence of volatile organic contamination. There were no PID readings observed during the sampling event. Soil samples were collected from the test pits in accordance with the frequency criteria required by the proposed disposal facilities and the approved-RAWP for the Site.

The sampling included the collection of a discrete grab sample from middle sidewall of each test pit for VOCs using the En Core sampling method. An additional discrete sample for VOCS was collected with an En Core sample from the lower middle sidewall of test pits TP-1, TP-2, TP-3 and TP-4 for a total of 12 VOC samples. A five-point composite sample was collected from the sidewalls and bottom of test pits TP-5, TP-6, TP-7 and TP-8 for an expanded list of chemical parameters in order to meet the acceptance criteria of multiple beneficial reuse facilities. For test pits TP-1, TP-2, TP-3 and TP-4, one five-point composite sample was collected from 0-7 feet and a second from 7 - 14 feet for the expanded list of chemical parameters. In addition, 12 additional five-point composite samples were collected for Total Petroleum Hydrocarbons.

Gloves worn for sample handling were discarded between sample collections. All soil samples were placed in lab-supplied containers, stored in an ice-filled cooler and submitted to American Analytical Laboratories (a State-certified laboratory located in Farmingdale, NY) for analysis. Copies of the soil test results are attached to this report. A Site plan depicting test pit locations is included as Figure 2.

The Chain-of-Custody program allows for the tracing of possession and handling of the sample from its time of collection through its chemical analysis in the laboratory. The chain-of-custody program at this Site included:

- Sample labels
- Chain-of-Custody records
- Field records

To prevent misidentification of samples, a label was affixed to the sample container and contained the following information:

- Site Name
- Sample identification number
- Date and time of collection
- Name of Sampler
- Preservation (if any)
- Type of analysis to be conducted

To establish the documentation necessary to trace sample possession from the time of collection, a chain-of-custody record was filled out and accompanied samples at all times. The record contained the following information:

- Project name
- Printed name and signature of samplers
- Sample number
- Date and time of collection
- Sampling location
- Number of containers for each sample
- Signature of individuals involved in sample transfer (when relinquishing and accepting samples)
- Inclusive dates and times of possession

Field records were maintained during each sampling effort in a logbook and on field sampling forms. All aspects of sample collection, handling and visual observations were recorded. All sample collection equipment, field analytical equipment and equipment utilized to make physical measurements were identified in the field logbook. Entries were made in ink, dated and initialed.

The fundamental Quality Assurance objective with respect to accuracy, precision, and sensitivity of analysis for laboratory analytical data is to achieve the QC acceptance of the analytical protocol. The accuracy, precision and completeness requirements were addressed by the laboratory for all data generated.

Collected samples were appropriately packaged, placed in coolers and shipped or delivered directly to the analytical laboratory by field personnel. Samples were containerized in appropriate laboratory

provided glassware and shipped in plastic coolers. Samples were preserved to maintain a temperature of 4°C.

Grab samples were collected using a clean stainless steel trowel and placed into jars using clean dedicated tongue depressors. Samples were composited using a clean stainless steel bowl and trowel. Decontamination of non-dedicated sampling equipment consisted of the following:

- Gently tap or scrape to remove adhered soil;
- Rinse with tap water;
- Wash with alconox® detergent solution and scrub;
- Rinse with tap water;
- Rinse with distilled or de-ionized water;

Conclusion

A total of 12 grab samples for VOCs, 12 five-point composite samples for TPH, and 12 five-point composite samples for an expanded list of testing parameters were collected to profile the soil for disposal prior to the start of excavation activities. Based on our review of the test results and preliminary discussions with Richard Crawford of Clean Earth Inc., test pits TP-5 and TP-7 must be disposed of as lead contaminated hazardous soil while the remainder of the soil would qualify for disposal at one of Clean Earth's beneficial reuse facilities (ILR, Teterboro or Dupont). The construction plan is to first remove the hazardous soil identified in test pits TP-5 and TP-7, then conduct additional sampling for total and TCLP lead to confirm all soil with hazardous levels of lead was removed prior to initiating a site-wide excavation to one of the beneficial reuse facilities. Upon completion of your review, kindly provide us with an acceptance letter from the facility indicating that they will accept material from the 260 West 26th Street job Site.

If you have any questions regarding the information presented in this report, please feel free to call our office.

Sincerely,

CA RICH CONSULTANTS, INC.

Stephen T. Malinowski
Associate

cc: Richard Crawford, Clean Earth

REFERENCE

1) CA RICH Consultants, Inc. April 2011. Remedial Action Work Plan, 260 West 26th Street, New York, New York

FIGURES

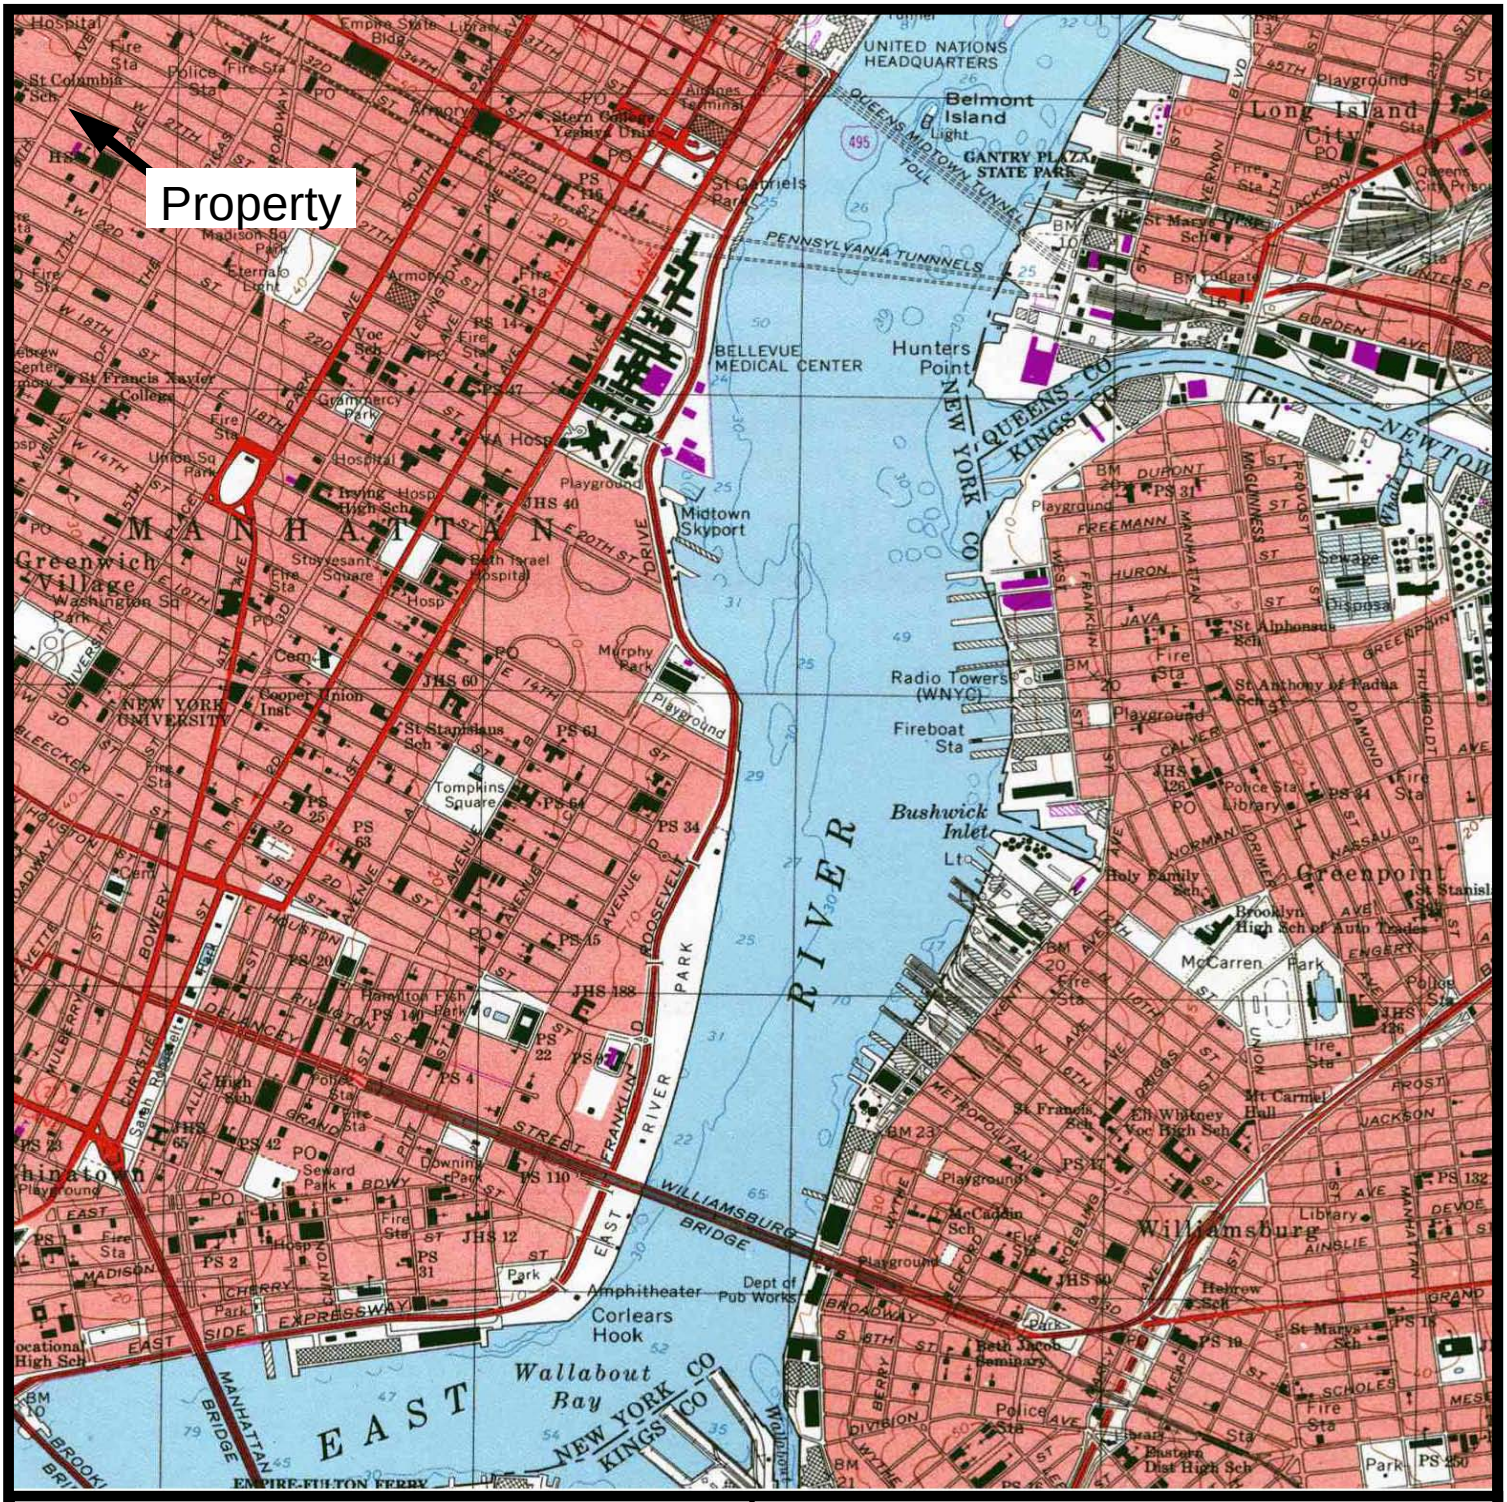

APPROX. SCALE (ft.)

0 *1,200* *2,400* *N*

Adapted from USGS 1995 Brooklyn Quadrangle Map.

CA RICH CONSULTANTS, INC.

Certified Ground Water and Environmental Specialists
17 Dupont Street, Plainview, NY 11803

TITLE: **PROPERTY LOCATION MAP**	*DATE:* **2/25/11**
	SCALE: **AS SHOWN**
FIGURE: **1**	*DRAWN BY:* **JEP**
DRAWING:	**260 West 26th Street Manhattan, New York**
	APPR. BY: **DS**

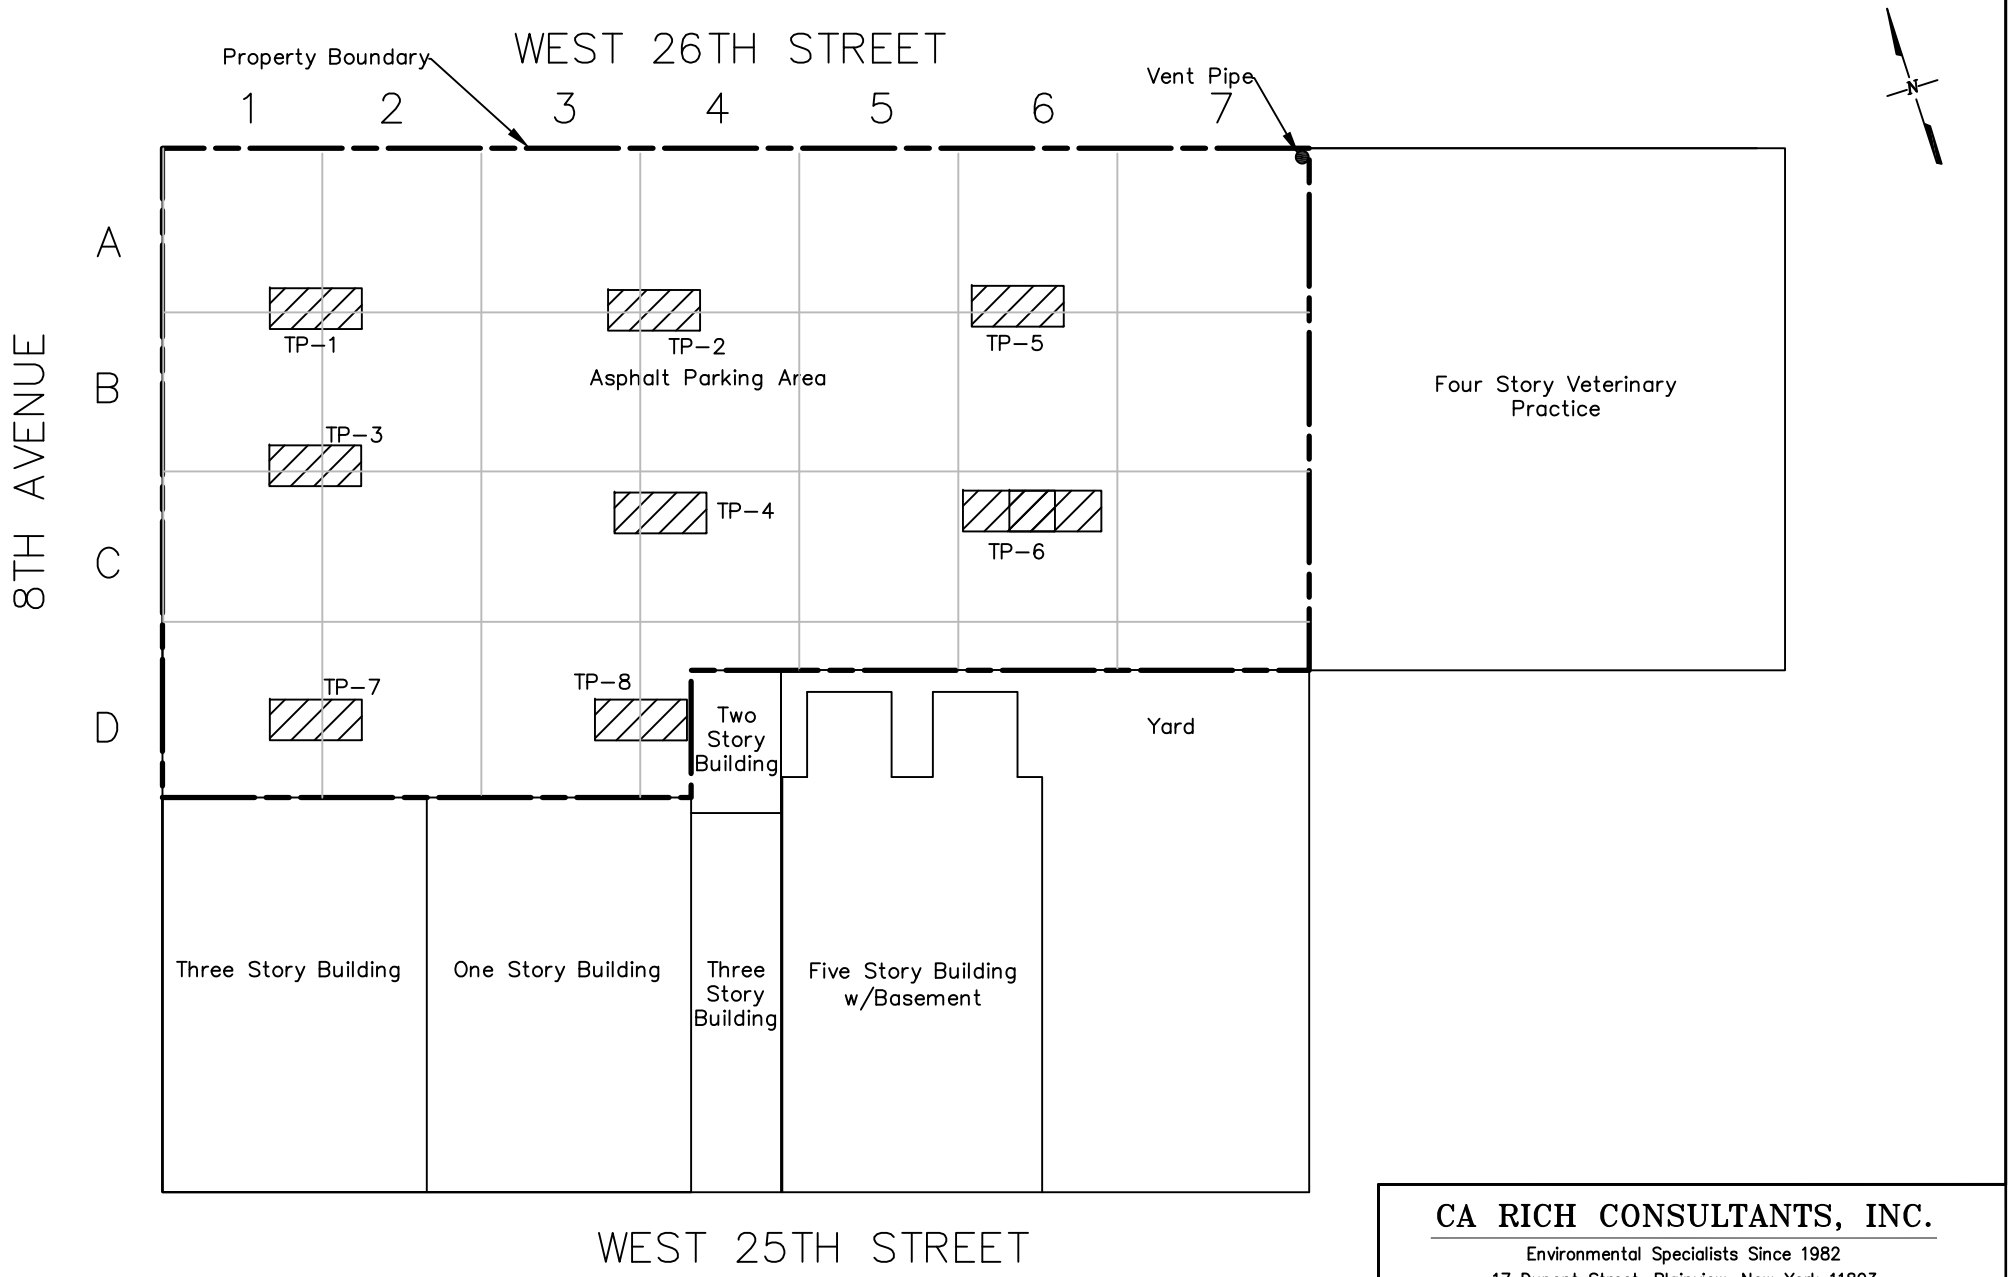

LEGEND

Alphanumeric Grid Are Approximately 30-Feet by 30-Feet

Proposed Test Pit Location for Soil Waste Classification Purposes
Test Pits to Extend to Bedrock or 15 Feet Below Grade

0 10 20 40
Graphic Scale in Feet

CA RICH CONSULTANTS, INC.

Environmental Specialists Since 1982
17 Dupont Street, Plainview, New York 11803

TITLE: SITE PLAN with ALPHANUMERIC GRID	DATE: 9/9/2011
	SCALE: As Shown
FIGURE: 2	DRAWN BY: J.T.C.
DRAWING NO: 2011-M1A	260 West 26th Street Manhattan, New York
	APPR. BY: S.T.M.

Attachment A

Laboratory Analytical Results

AMERICAN ANALYTICAL LABORATORIES

NYSDOH 11418
NJDEP NY050
CTDOH PH-0205
PADEP 68-00573

Friday, September 09, 2011

Steve Malinowski
CA Rich Consultants Inc.
17 Dupont Street
Plainview, NY 11803

TEL: (516) 576-8844
FAX (516) 576-0093

RE: 260 West 26th Street, NY, NY

Order No.: 1108200

Dear Steve Malinowski:

American Analytical Laboratories, LLC. received 36 sample(s) on 8/31/2011 for the analyses presented in the following report.

Samples were analyzed in accordance with the test procedures documented on the chain of custody and detailed throughout the text of this report.

The results reported herein relate only to the items tested or to the samples as received by the laboratory. This report may not be reproduced, except in full, without the approval of American Analytical Laboratories, LLC and is not considered complete without a cover page and chain of custody documentation. The limits (LOQ) provided in the data package are analytical reporting limits and not Federal or Local mandated values to which the sample results should be compared.

There were no problems with the analyses and all data for associated QC met laboratory specifications. If there are any exceptions a Case Narrative is provided in the report or the data is qualified. This package has been reviewed by American Analytical Laboratories' QA Department/Laboratory Director to comply with NELAC standards prior to report submittal. This report consists of 213 pages.

If you have any questions regarding these tests results, please do not hesitate to call (631) 454-6100 or email me directly at lbeyer@american-analytical.com.

Sincerely,

Lori Beyer
Lab Director

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

CLIENT: CA Rich Consultants Inc.
Project: 260 West 26th Street, NY, NY
Lab Order: 1108200

Work Order Sample Summary

Lab Sample ID	Client Sample ID	Date Collected	Date Received
1108200-01A	TP-1G (4 ft.)	8/30/2011 11:05:00 AM	8/31/2011
1108200-02A	TP-1C (0-7 ft.)	8/30/2011 11:00:00 AM	8/31/2011
1108200-02B	TP-1C (0-7 ft.)	8/30/2011 11:00:00 AM	8/31/2011
1108200-03A	TP-1Ca (0-7 ft.)	8/30/2011 11:02:00 AM	8/31/2011
1108200-04A	TP-1G (12 ft.)	8/30/2011 11:25:00 AM	8/31/2011
1108200-05A	TP-1C (7-14 ft.)	8/30/2011 11:20:00 AM	8/31/2011
1108200-05B	TP-1C (7-14 ft.)	8/30/2011 11:20:00 AM	8/31/2011
1108200-06A	TP-1Ca (7-14 ft.)	8/30/2011 11:22:00 AM	8/31/2011
1108200-07A	TP-2G (4 ft.)	8/30/2011 10:25:00 AM	8/31/2011
1108200-08A	TP-2C (0-7 ft.)	8/30/2011 10:15:00 AM	8/31/2011
1108200-08B	TP-2C (0-7 ft.)	8/30/2011 10:15:00 AM	8/31/2011
1108200-09A	TP-2Ca (0-7 ft.)	8/30/2011 10:17:00 AM	8/31/2011
1108200-10A	TP-2G (12 ft.)	8/30/2011 10:45:00 AM	8/31/2011
1108200-11A	TP-2C (7-14 ft.)	8/30/2011 10:40:00 AM	8/31/2011
1108200-11B	TP-2C (7-14 ft.)	8/30/2011 10:40:00 AM	8/31/2011
1108200-12A	TP-2Ca (7-14 ft.)	8/30/2011 10:44:00 AM	8/31/2011
1108200-13A	TP-3G (4 ft.)	8/30/2011 11:45:00 AM	8/31/2011
1108200-14A	TP-3C (0-7 ft.)	8/30/2011 11:40:00 AM	8/31/2011
1108200-14B	TP-3C (0-7 ft.)	8/30/2011 11:40:00 AM	8/31/2011
1108200-15A	TP-3Ca (0-7 ft.)	8/30/2011 11:42:00 AM	8/31/2011
1108200-16A	TP-3G (12 ft.)	8/30/2011 12:00:00 PM	8/31/2011
1108200-17A	TP-3C (7-14 ft.)	8/30/2011 11:50:00 AM	8/31/2011
1108200-17B	TP-3C (7-14 ft.)	8/30/2011 11:50:00 AM	8/31/2011
1108200-18A	TP-3Ca (7-14 ft.)	8/30/2011 11:55:00 AM	8/31/2011
1108200-19A	TP-4G (4 ft.)	8/30/2011 12:15:00 PM	8/31/2011
1108200-20A	TP-4C (0-7 ft.)	8/30/2011 12:10:00 PM	8/31/2011
1108200-20B	TP-4C (0-7 ft.)	8/30/2011 12:10:00 PM	8/31/2011
1108200-21A	TP-4Ca (0-7 ft.)	8/30/2011 12:11:00 PM	8/31/2011
1108200-22A	TP-4G (12 ft.)	8/30/2011 12:30:00 PM	8/31/2011
1108200-23A	TP-4C (7-14 ft.)	8/30/2011 12:25:00 PM	8/31/2011
1108200-23B	TP-4C (7-14 ft.)	8/30/2011 12:25:00 PM	8/31/2011
1108200-24A	TP-4Ca (7-14 ft.)	8/30/2011 12:20:00 PM	8/31/2011
1108200-25A	TP-5G (11 ft.)	8/30/2011 9:40:00 AM	8/31/2011
1108200-26A	TP-5C (0-11 ft.)	8/30/2011 9:35:00 AM	8/31/2011
1108200-26B	TP-5C (0-11 ft.)	8/30/2011 9:35:00 AM	8/31/2011
1108200-27A	TP-5Ca (0-11 ft.)	8/30/2011 9:37:00 AM	8/31/2011

CLIENT:	CA Rich Consultants Inc.
Project:	260 West 26th Street, NY, NY
Lab Order:	1108200

Work Order Sample Summary

Lab Sample ID	Client Sample ID	Date Collected	Date Received
1108200-28A	TP-6G (4 ft.)	8/30/2011 10:07:00 AM	8/31/2011
1108200-29A	TP-6C (0-8 ft.)	8/30/2011 10:02:00 AM	8/31/2011
1108200-29B	TP-6C (0-8 ft.)	8/30/2011 10:02:00 AM	8/31/2011
1108200-30A	TP-6Ca (0-8 ft.)	8/30/2011 10:04:00 AM	8/31/2011
1108200-31A	TP-7G (5 ft.)	8/30/2011 2:10:00 PM	8/31/2011
1108200-32A	TP-7C (0-7 ft.)	8/30/2011 2:00:00 PM	8/31/2011
1108200-32B	TP-7C (0-7 ft.)	8/30/2011 2:00:00 PM	8/31/2011
1108200-33A	TP-7Ca (0-7 ft.)	8/30/2011 2:02:00 PM	8/31/2011
1108200-34A	TP-8G (2 ft.)	8/30/2011 1:45:00 PM	8/31/2011
1108200-35A	TP-8C (0-4 ft.)	8/30/2011 1:40:00 PM	8/31/2011
1108200-35B	TP-8C (0-4 ft.)	8/30/2011 1:40:00 PM	8/31/2011
1108200-36A	TP-8Ca (0-4 ft.)	8/30/2011 1:30:00 PM	8/31/2011

AMERICAN ANALYTICAL LABORATORIES
56 TOLEDO STREET • FARMINGDALE, NEW YORK 11735
(631) 454-6100 • FAX (631) 454-8027

TAG # / COC 08675

NYSDOH 11418
CTDOH PH-0205
NJDEP NY050
PADEP 68-573

CHAIN OF CUSTODY / REQUEST FOR ANALYSIS DOCUMENT

CLIENT NAME/ADDRESS
Ca Rich Consultants, Inc
17 DuPont Street
Plainview, NY

CONTACT: Steve Malinowski

SAMPLER (SIGNATURE)

SAMPLER NAME (PRINT): Jessica Prascia

SAMPLE(S) SEALED (YES / NO): YES

CORRECT CONTAINER(S) (YES / NO): YES

PROJECT LOCATION: 260 West 26th Street NY, NY

LABORATORY ID #	MATRIX	# CONTAINERS	SAMPLING DATE/ TIME	SAMPLE # - LOCATION	ANALYSIS REQUIRED: VOC 8260	TPHC 8015	SVOC MS SCL	TAL metals + Cyanide + Hexavalent Chromium	PCB's	Herbs / Pests	Full TCLP VOCs	Full TCLP Metals	Herb / Pest	RCRA Charact.	Paint Filter	FOR METHANOL PRESERVED SAMPLES [VOLATILE VIAL #]
1108200-01A	S/C	2	8/30/11 11:05	TP-1G (4ft)	X											
1108200-02AB	S/C	3	8/30/11 11am	TP-1C (0-7ft)		X	X	X	X	X	X	X	X	X	X	
1108200-03A	S/C	1	8/30/11 11:02	TP-1Ca (0-7ft)		X										
1108200-4A	S/G	2	8/30/11 11:25	TP-1G (12ft)	X											
1108200-05AB	S/C	3	8/30/11 11:20	TP-1G (7-14ft)		X	X	X	X	X	X	X	X	X	X	
1108200-06A	S/C	1	8/30/11 11:22	TP-1Ca (7-14ft)		X										
1108200-07A	S/G	2	8/30/11 10:25	TP-2G (4ft)	X											
1108200-08AB	S/C	3	8/30/11 10:15	TP-2C (0-7ft)		X	X	X	X	X	X	X	X	X	X	
1108200 09A	S/C	1	8/30/11 10:17	TP-2Ca (0-7ft)		X										
1108200 10A	S/G	2	8/30/11 10:45	TP-2G (12ft)	X											
1108200 11AB	S/C	3	8/30/11 10:40	TP-2C (7-14ft)		X	X	X	X	X	X	X	X	X	X	
1108200-12A	S/C	1	8/30/11 10:44	TP-2Ca (7-14ft)		X										

1 of 3

COOLER TEMPERATURE: 0.5°C

MATRIX S=SOIL; L=LIQUID; SL=SLUDGE; A-AIR; W=WIPE; P=PAINT CHIPS; B=BULK MATERIAL
TYPE G=GRAB; C=COMPOSITE, SS=SPLIT SPOON

TURNAROUND REQUIRED: NORMAL ☒ STAT ☐ BY / /

COMMENTS / INSTRUCTIONS

RELINQUISHED BY (SIGNATURE)	DATE / TIME	PRINTED NAME	RECEIVED BY LAB (SIGNATURE)	DATE / TIME	PRINTED NAME
	8/31/11 10:40	Jessica Prascia	C Dunn	8/31/11 10:40	C Dunn
C Dunn	8/31/11 11:05	C Dunn	Lori Beyer	8/31/11 11:05	Lori Beyer

WHITE-OFFICE / CANARY-LAB / PINK-SAMPLE CUSTODIAN / GOLDENROD-CLIENT

AMERICAN ANALYTICAL LABORATORIES
56 TOLEDO STREET • FARMINGDALE, NEW YORK 11735
(631) 454-6100 • FAX (631) 454-8027
www.american-analytical.com

NYSDOH	11418
CTDOH	PH-0205
NJDEP	NY050
PADEP	68-573

CHAIN OF CUSTODY / REQUEST FOR ANALYSIS DOCUMENT

CLIENT NAME/ADDRESS: Ca Rich

CONTACT: Steve Malinowski

SAMPLER (SIGNATURE):

SAMPLER NAME (PRINT): Jessica Prosci

SAMPLE(S) SEALED: YES / NO

CORRECT CONTAINER(S): YES / NO

TEMPERATURE (° C): 0.5°C

PROJECT LOCATION: 260 West 26th Street NY, NY

ANALYSIS REQUIRED: VOCs 8260; TPH GC/FIDS; SVOC MS scn; TAL metals +cyanide; Hexavalent Chromium; PCBs; Herbs/Pests; TCLP VOCs; SVOCs; Metals; Herb/Pest; RCRA Characteristics

LABORATORY ID# LAB USE ONLY	MATRIX/ TYPE	NO. OF CONTAINERS	SAMPLING DATE	SAMPLING TIME	SAMPLE # - LOCATION
1108200-13A	S/G	2	8/30/11	11:45	TP-3G (4ft)
14AB	S/C	3	8/30/11	11:40	TP-3C (0-7ft)
15A	S/C	1	8/30/11	11:42	TP-3Ca (0-7ft)
16A	S/G	2	8/30/11	12:00	TP-3G (12ft)
17AB	S/C	3	8/30/11	11:50	TP-3C (7-14ft)
18A	S/C	1	8/30/11	11:55	TP-3Ca (7-14ft)
19A	S/G	2	8/30/11	12:15	TP-4G (4ft)
20AB	S/C	3	8/30/11	12:10	TP-4C (0-7ft)
21A	S/C	1	8/30/11	12:11	TP-4Ca (0-7ft)
22A	S/G	2	8/30/11	12:30	TP-4G (12ft)
23AB	S/C	3	8/30/11	12:25	TP-4C (7-14ft)
24A	S/C	1	8/30/11	12:20	TP-4Ca (7-14ft)

COMMENTS / INSTRUCTIONS

Samples must be on ICE (<6° C)

2083

MATRIX S=SOIL; W=WATER; SL=SLUDGE; A=AIR; M=MISCELLANEOUS

TYPE G=GRAB; C=COMPOSITE

TURNAROUND REQUIRED: STANDARD ☒ STAT ☐ BY / /
(7-10 business days)

E-MAIL ADDRESS FOR RESULTS:

RELINQUISHED BY (SIGNATURE)	DATE / TIME	PRINTED NAME	RECEIVED BY LAB (SIGNATURE)	DATE / TIME	PRINTED NAME
	8/31/11 10:42	Jessica Prosci		8/31/11 10:42	C Dunn
	8/31/11	C Dunn		8/31/11 1110	Tom Beyer

WHITE-OFFICE / CANARY-LAB / PINK-SAMPLE CUSTODIAN / GOLDENROD-CLIENT

AMERICAN ANALYTICAL LABORATORIES
56 TOLEDO STREET • FARMINGDALE, NEW YORK 11735
(631) 454-6100 • FAX (631) 454-8027
www.american-analytical.com

NYSDOH	11418
CTDOH	PH-0205
NJDEP	NY050
PADEP	68-573

CHAIN OF CUSTODY / REQUEST FOR ANALYSIS DOCUMENT

CLIENT NAME/ADDRESS: Ca Rich

CONTACT:

SAMPLER (SIGNATURE):

SAMPLER NAME (PRINT): Jessica Placia

SAMPLE(S) SEALED: YES / NO

CORRECT CONTAINER(S): YES / NO

TEMPERATURE (° C): 0.5°C

PROJECT LOCATION: 260 west 26th Street NY, NY

LABORATORY ID# LAB USE ONLY	MATRIX/ TYPE	NO. OF CONTAINERS	SAMPLING DATE	SAMPLING TIME	SAMPLE # - LOCATION	ANALYSIS REQUIRED: VOC 8260	TPH 8015	SVOC NO 5 CL	TAL Metals + Cyanide	Hexavalent Chromium	PCB's	Herbicides	Full Tal + VOCs	SVOCs, metals, Mers + Pest	RCRA Chromium
1108200-25A	S/G	2	8/30/11	9:40	TP-5G (11FT)	X									
26AB	S/C	3	8/30/11	9:25	TP-5C (0-11FT)		X	X	X	X	X	X	X	X	X
27A	S/C	1	8/30/11	9:37	TP-5Ca (0-11FT)		X								
28A	S/G	2	8/30/11	10:07	TP-6G (4FT)	X									
29AB	S/C	3	8/30/11	10:02	TP-6C (0-8FT)		X	X	X	X	X	X	X	X	X
30A	S/C	1	8/30/11	10:04	TP-6Ca (0-8FT)		X								
31A	S/G	2	8/30/11	2:10PM	TP-7G (5FT)	X									
32AB	S/C	3	8/30/11	2PM	TP-7C (0-7FT)		X	X	X	X	X	X	X	X	X
33A	S/C	1	8/30/11	2:02PM	TP-7Ca (0-7FT)		X								
34A	S/G	2	8/30/11	1:45	TP-8G (2FT)	X									
35AB	S/C	3	8/30/11	1:40	TP-8C (0-4FT)		X	X	X	X	X	X	X	X	X
36A	S/C	1	8/30/11	1:30	TP-8Ca (0-4FT)		X								

COMMENTS / INSTRUCTIONS

Samples must be on ICE (<6° C)

3 of 3

MATRIX S=SOIL; W=WATER; SL=SLUDGE; A=AIR; M=MISCELLANEOUS
TYPE G=GRAB; C=COMPOSITE

TURNAROUND REQUIRED
STANDARD ☑ STAT ☐ BY / /
(7-10 business days)

E-MAIL ADDRESS FOR RESULTS:

RELINQUISHED BY (SIGNATURE)	DATE / TIME	PRINTED NAME	RECEIVED BY LAB (SIGNATURE)	DATE / TIME	PRINTED NAME
	8/31/11 10:45	Jessica Placia		8/31/11 10:45	C Lunn
C Lunn	8/31/11 11:05	C Lunn		8/31/11	Lori Beyer

WHITE-OFFICE / CANARY-LAB / PINK-SAMPLE CUSTODIAN / GOLDENROD-CLIENT

(07)

American Analytical Laboratories, LLC.

Sample Receipt Checklist

Client Name CA RICH | Date and Time Receive 8/31/2011 1:10:41 PM

Work Order Numbe 1108200 | RcptNo: 1 | Received by LB

COC_ID: | CoolerID:

Checklist completed b [Signature] [Date] 8/31/11 | Reviewed by [Initials] [Date] 8/31/11

Matrix | Carrier name Lab Courier

Shipping container/cooler in good condition?	Yes ☑	No ☐	Not Presen ☐
Custody seals intact on shippping container/cooler?	Yes ☐	No ☐	Not Presen ☑
Custody seals intact on sample bottles?	Yes ☐	No ☐	Not Presen ☑
Chain of custody present?	Yes ☑	No ☐	
Chain of custody signed when relinquished and received?	Yes ☑	No ☐	
Chain of custody agrees with sample labels?	Yes ☑	No ☐	
Samples in proper container/bottle?	Yes ☑	No ☐	
Sample containers intact?	Yes ☑	No ☐	
Sufficient sample volume for indicated test?	Yes ☑	No ☐	
All samples received within holding time?	Yes ☐	No ☑	
Container/Temp Blank temperature in compliance?	Yes ☑	No ☐	
Water - VOA vials have zero headspace?	No VOA vials submitted ☑	Yes ☐	No ☐
Water - pH acceptable upon receipt?	Yes ☐	No ☐	N/A ☐

Adjusted _____ Checked b _____

Any No and/or NA (not applicable) response must be detailed in the comments section b

Client contacted _____ Date contacted: _____ Person contacted _____

Contacted by: _____ Regarding _____

Comments: pH is an analyze immediately parameter and will be performed as quickly as possible after receipt at the laboratory.

Corrective Action _____

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-1G (4 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:05:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-01A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	15.9	0	0		wt%	1	9/1/2011
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: **LA**
1,1,1,2-Tetrachloroethane	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
1,1,1-Trichloroethane	U	0.65	6.5	C	µg/Kg-dry	1	8/31/2011 2:46:00 PM
1,1,2,2-Tetrachloroethane	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
1,1,2-Trichloro-1,2,2-trifluoroethan	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
1,1,2-Trichloroethane	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
1,1-Dichloroethane	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
1,1-Dichloroethene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
1,1-Dichloropropene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
1,2,3-Trichlorobenzene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
1,2,3-Trichloropropane	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
1,2,4,5-Tetramethylbenzene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
1,2,4-Trichlorobenzene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
1,2,4-Trimethylbenzene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
1,2-Dibromo-3-chloropropane	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
1,2-Dibromoethane	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
1,2-Dichlorobenzene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
1,2-Dichloroethane	U	0.65	6.5	C	µg/Kg-dry	1	8/31/2011 2:46:00 PM
1,2-Dichloropropane	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
1,3,5-Trimethylbenzene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
1,3-Dichlorobenzene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
1,3-dichloropropane	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
1,4-Dichlorobenzene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
1,4-Dioxane	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
2,2-Dichloropropane	U	0.65	6.5	C	µg/Kg-dry	1	8/31/2011 2:46:00 PM
2-Butanone	U	2	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
2-Chloroethyl vinyl ether	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
2-Chlorotoluene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
2-Hexanone	U	2	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
2-Propanol	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
4-Chlorotoluene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-1G (4 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:05:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-01A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: **LA**
4-Isopropyltoluene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
4-Methyl-2-pentanone	U	2	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Acetone	U	2	6.5	C	µg/Kg-dry	1	8/31/2011 2:46:00 PM
Acrolein	U	3.3	13	C	µg/Kg-dry	1	8/31/2011 2:46:00 PM
Acrylonitrile	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Benzene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Bromobenzene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Bromochloromethane	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Bromodichloromethane	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Bromoform	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Bromomethane	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Carbon disulfide	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Carbon tetrachloride	U	0.65	6.5	C	µg/Kg-dry	1	8/31/2011 2:46:00 PM
Chlorobenzene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Chlorodifluoromethane	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Chloroethane	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Chloroform	U	0.65	6.5	C	µg/Kg-dry	1	8/31/2011 2:46:00 PM
Chloromethane	U	0.65	6.5	C	µg/Kg-dry	1	8/31/2011 2:46:00 PM
cis-1,2-Dichloroethene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
cis-1,3-Dichloropropene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Dibromochloromethane	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Dibromomethane	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Dichlorodifluoromethane	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Diisopropyl ether	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Ethanol	U	3.3	13		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Ethyl acetate	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Ethylbenzene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Freon-114	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Hexachlorobutadiene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Isopropyl acetate	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Isopropylbenzene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
m,p-Xylene	U	1.3	13		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Methyl Acetate	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-1G (4 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:05:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-01A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: **LA**
Methyl tert-butyl ether	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Methylene chloride	12	0.65	6.5	B	µg/Kg-dry	1	8/31/2011 2:46:00 PM
n-Amyl acetate	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Naphthalene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
n-Butyl acetate	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
n-Butylbenzene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
n-Propyl acetate	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
n-Propylbenzene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
o-Xylene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
p-Diethylbenzene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
p-Ethyltoluene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
sec-Butylbenzene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Styrene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
t-Butyl alcohol	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
tert-Butylbenzene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Tetrachloroethene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Toluene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
trans-1,2-Dichloroethene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
trans-1,3-Dichloropropene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Trichloroethene	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Trichlorofluoromethane	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Vinyl acetate	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Vinyl chloride	U	0.65	6.5		µg/Kg-dry	1	8/31/2011 2:46:00 PM
Surr: 4-Bromofluorobenzene	92.0	0	42-133		%REC	1	8/31/2011 2:46:00 PM
Surr: Dibromofluoromethane	97.4	0	50-133		%REC	1	8/31/2011 2:46:00 PM
Surr: Toluene-d8	96.9	0	53-130		%REC	1	8/31/2011 2:46:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-1C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:00:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-02A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
MERCURY			**SW7471B**		**SW7471B**		Analyst: **AB**
Mercury	3.36	0.05	0.0993		mg/Kg-dry	10	9/2/2011 12:17:20 PM
TOTAL DRO AS #2 FUEL (C8-C40)			**SW8015C**		**SW3550C**		Analyst: **LDS**
Total DRO TPH	260	2.86	11		mg/Kg-dry	1	9/1/2011 1:33:00 PM
Surr: o-Terphenyl	35.5	0	31-137		%REC	1	9/1/2011 1:33:00 PM
HERBICIDES SW-846 8151			**SW8151A**		**SW8151**		Analyst: **SB**
2,4,5-T	U	1.14	11		µg/Kg-dry	1	9/8/2011 1:33:00 AM
2,4,5-TP	U	1.14	11		µg/Kg-dry	1	9/8/2011 1:33:00 AM
2,4-D	U	1.14	11		µg/Kg-dry	1	9/8/2011 1:33:00 AM
Surr: 2,4-DCAA	124	0	14-148		%REC	1	9/8/2011 1:33:00 AM
PCB'S AS AROCLORS SW-846 METHOD 8082			**SW8082A**		**SW3550C**		Analyst: **SB**
Aroclor 1016	U	1.14	46		µg/Kg-dry	1	9/1/2011 6:27:00 PM
Aroclor 1221	U	1.14	46		µg/Kg-dry	1	9/1/2011 6:27:00 PM
Aroclor 1232	U	1.14	46		µg/Kg-dry	1	9/1/2011 6:27:00 PM
Aroclor 1242	U	1.14	46		µg/Kg-dry	1	9/1/2011 6:27:00 PM
Aroclor 1248	U	1.14	46		µg/Kg-dry	1	9/1/2011 6:27:00 PM
Aroclor 1254	U	1.14	46		µg/Kg-dry	1	9/1/2011 6:27:00 PM
Aroclor 1260	U	1.14	46		µg/Kg-dry	1	9/1/2011 6:27:00 PM
Aroclor 1262	U	1.14	46		µg/Kg-dry	1	9/1/2011 6:27:00 PM
Aroclor 1268	U	1.14	46		µg/Kg-dry	1	9/1/2011 6:27:00 PM
Surr: TCX	57.2	0	17-151		%REC	1	9/1/2011 6:27:00 PM
Surr: DCB	72.4	0	16-152		%REC	1	9/1/2011 6:27:00 PM
PESTICIDES SW-846 METHOD 8081			**SW8081B**		**SW3550C**		Analyst: **SB**
4,4´-DDD	110	0.23	2.3		µg/Kg-dry	1	9/2/2011 12:13:00 PM
4,4´-DDE	380	2.29	23		µg/Kg-dry	10	9/2/2011 6:23:00 PM
4,4´-DDT	1300	2.29	23		µg/Kg-dry	10	9/2/2011 6:23:00 PM
Aldrin	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 12:13:00 PM
alpha-BHC	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 12:13:00 PM
beta-BHC	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 12:13:00 PM
Chlordane	970	11.4	23		µg/Kg-dry	10	9/2/2011 6:23:00 PM
Chlorobenzilate	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 12:13:00 PM
DBCP	19	0.23	2.3	P	µg/Kg-dry	1	9/2/2011 12:13:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-1C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:00:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-02A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PESTICIDES SW-846 METHOD 8081			**SW8081B**		**SW3550C**		Analyst: **SB**
delta-BHC	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 12:13:00 PM
Dieldrin	52	0.23	2.3		µg/Kg-dry	1	9/2/2011 12:13:00 PM
Endosulfan I	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 12:13:00 PM
Endosulfan II	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 12:13:00 PM
Endosulfan sulfate	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 12:13:00 PM
Endrin	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 12:13:00 PM
Endrin aldehyde	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 12:13:00 PM
Endrin ketone	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 12:13:00 PM
gamma-BHC	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 12:13:00 PM
Heptachlor	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 12:13:00 PM
Heptachlor epoxide	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 12:13:00 PM
Hexachlorobenzene	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 12:13:00 PM
Hexachlorocyclopentadiene	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 12:13:00 PM
Methoxychlor	29	0.23	2.3		µg/Kg-dry	1	9/2/2011 12:13:00 PM
Toxaphene	U	5.72	11		µg/Kg-dry	1	9/2/2011 12:13:00 PM
Surr: DCB	56.9	0	23-157		%REC	1	9/2/2011 12:13:00 PM
Surr: DCB	104	0	23-157		%REC	10	9/2/2011 6:23:00 PM
Surr: TCX	71.6	0	21-151		%REC	10	9/2/2011 6:23:00 PM
Surr: TCX	42.4	0	21-151		%REC	1	9/2/2011 12:13:00 PM
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	13.2	0	0		wt%	1	9/1/2011
TARGET ANALYTE LIST METALS			**SW6010C**		**SW3050B**		Analyst: **JP**
Aluminum	4410	0.11	0.435		mg/Kg-dry	1	9/2/2011 9:48:48 AM
Antimony	U	0.22	0.543		mg/Kg-dry	1	9/2/2011 9:48:48 AM
Arsenic	7.39	0.22	0.543		mg/Kg-dry	1	9/2/2011 9:48:48 AM
Barium	270	0.22	0.435		mg/Kg-dry	1	9/2/2011 9:48:48 AM
Beryllium	U	0.11	0.435		mg/Kg-dry	1	9/2/2011 9:48:48 AM
Cadmium	0.674	0.11	0.435		mg/Kg-dry	1	9/2/2011 9:48:48 AM
Calcium	25900	2.17	5.43		mg/Kg-dry	10	9/2/2011 12:27:03 PM
Chromium	13.2	0.11	0.435		mg/Kg-dry	1	9/2/2011 9:48:48 AM
Cobalt	U	0.11	0.435		mg/Kg-dry	1	9/2/2011 9:48:48 AM
Copper	75.4	0.11	0.435		mg/Kg-dry	1	9/2/2011 9:48:48 AM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-1C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:00:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-02A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TARGET ANALYTE LIST METALS			**SW6010C**		**SW3050B**		Analyst: **JP**
Iron	10200	2.17	4.35		mg/Kg-dry	10	9/2/2011 12:27:03 PM
Lead	904	0.22	0.435		mg/Kg-dry	1	9/2/2011 9:48:48 AM
Magnesium	2900	0.11	0.435		mg/Kg-dry	1	9/2/2011 9:48:48 AM
Manganese	179	0.11	0.435		mg/Kg-dry	1	9/2/2011 9:48:48 AM
Nickel	11.7	0.11	0.435		mg/Kg-dry	1	9/2/2011 9:48:48 AM
Potassium	1730	0.22	0.543		mg/Kg-dry	1	9/2/2011 9:48:48 AM
Selenium	0.369	0.22	0.543	J	mg/Kg-dry	1	9/2/2011 9:48:48 AM
Silver	2.09	0.11	0.435		mg/Kg-dry	1	9/2/2011 9:48:48 AM
Sodium	270	0.22	0.543		mg/Kg-dry	1	9/2/2011 9:48:48 AM
Thallium	U	0.33	0.543		mg/Kg-dry	1	9/2/2011 9:48:48 AM
Vanadium	13.8	0.11	0.435		mg/Kg-dry	1	9/2/2011 9:48:48 AM
Zinc	321	0.11	0.435		mg/Kg-dry	1	9/2/2011 9:48:48 AM
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
1,2,4-Trichlorobenzene	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
1,2-Dichlorobenzene	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
1,3-Dichlorobenzene	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
1,4-Dichlorobenzene	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
2,4,5-Trichlorophenol	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
2,4,6-Trichlorophenol	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
2,4-Dichlorophenol	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
2,4-Dimethylphenol	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
2,4-Dinitrophenol	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
2,4-Dinitrotoluene	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
2,6-Dinitrotoluene	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
2-Chloronaphthalene	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
2-Chlorophenol	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
2-Methylnaphthalene	330	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
2-Methylphenol	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
2-Nitroaniline	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
2-Nitrophenol	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
3,3'-Dichlorobenzidine	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
3+4-Methylphenol	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.	

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-1C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:00:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-02A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
3-Nitroaniline	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
4,6-Dinitro-2-methylphenol	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
4-Bromophenyl phenyl ether	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
4-Chloro-3-methylphenol	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
4-Chloroaniline	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
4-Chlorophenyl phenyl ether	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
4-Nitroaniline	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
4-Nitrophenol	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Acenaphthene	890	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Acenaphthylene	430	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Acetophenone	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Aniline	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Anthracene	13000	286	2900		µg/Kg-dry	10	9/2/2011 1:08:00 PM
Atrazine	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Azobenzene	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Benzaldehyde	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Benzidine	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Benzo(a)anthracene	8600	286	2900		µg/Kg-dry	10	9/2/2011 1:08:00 PM
Benzo(a)pyrene	6600	286	2900		µg/Kg-dry	10	9/2/2011 1:08:00 PM
Benzo(b)fluoranthene	6700	286	2900		µg/Kg-dry	10	9/2/2011 1:08:00 PM
Benzo(g,h,i)perylene	4100	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Benzo(k)fluoranthene	6700	286	2900		µg/Kg-dry	10	9/2/2011 1:08:00 PM
Benzoic acid	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Benzyl alcohol	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Biphenyl	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Bis(2-chloroethoxy)methane	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Bis(2-chloroethyl)ether	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Bis(2-chloroisopropyl)ether	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Bis(2-ethylhexyl)phthalate	890	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Butyl benzyl phthalate	640	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Caprolactam	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Carbazole	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Chrysene	8300	286	2900		µg/Kg-dry	10	9/2/2011 1:08:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-1C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:00:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-02A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
Dibenzo(a,h)anthracene	340	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Dibenzofuran	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Diethyl phthalate	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Dimethyl phthalate	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Di-n-butyl phthalate	410	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Di-n-octyl phthalate	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Fluoranthene	19000	286	2900		µg/Kg-dry	10	9/2/2011 1:08:00 PM
Fluorene	720	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Hexachlorobenzene	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Hexachlorobutadiene	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Hexachlorocyclopentadiene	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Hexachloroethane	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Indeno(1,2,3-c,d)pyrene	4100	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Isophorone	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Naphthalene	350	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Nitrobenzene	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
N-Nitrosodimethylamine	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
N-Nitrosodi-n-propylamine	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
N-Nitrosodiphenylamine	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Parathion	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Pentachlorophenol	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Phenanthrene	13000	286	2900		µg/Kg-dry	10	9/2/2011 1:08:00 PM
Phenol	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Pyrene	17000	286	2900		µg/Kg-dry	10	9/2/2011 1:08:00 PM
Pyridine	U	28.6	290		µg/Kg-dry	1	9/1/2011 2:01:00 PM
Surr: 2,4,6-Tribromophenol	48.4	0	21-119		%REC	1	9/1/2011 2:01:00 PM
Surr: 2,4,6-Tribromophenol	51.2	0	21-119		%REC	10	9/2/2011 1:08:00 PM
Surr: 2-Fluorobiphenyl	79.1	0	21-117		%REC	1	9/1/2011 2:01:00 PM
Surr: 2-Fluorobiphenyl	73.4	0	21-117		%REC	10	9/2/2011 1:08:00 PM
Surr: 2-Fluorophenol	39.3	0	11-105		%REC	10	9/2/2011 1:08:00 PM
Surr: 2-Fluorophenol	41.6	0	11-105		%REC	1	9/1/2011 2:01:00 PM
Surr: 4-Terphenyl-d14	80.2	0	21-132		%REC	10	9/2/2011 1:08:00 PM
Surr: 4-Terphenyl-d14	85.1	0	21-132		%REC	1	9/1/2011 2:01:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

ACCREDITED IN ACCORDANCE WITH nelac

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-1C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:00:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-02A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
Surr: Nitrobenzene-d5	54.3	0	18-116		%REC	10	9/2/2011 1:08:00 PM
Surr: Nitrobenzene-d5	56.7	0	18-116		%REC	1	9/1/2011 2:01:00 PM
Surr: Phenol-d6	41.3	0	12-110		%REC	10	9/2/2011 1:08:00 PM
Surr: Phenol-d6	30.1	0	12-110		%REC	1	9/1/2011 2:01:00 PM
CYANIDE, TOTAL			**SW9012A**		**SW9012A**		Analyst: **STP**
Cyanide, Total & Amenable: Auto Colorimetric	U	0.06	0.115		mg/Kg-dry	1	9/6/2011
HEXAVALENT CHROMIUM			**SW7196A**				Analyst: **AB**
Chromium, Hexavalent	0.430	0.23	0.461	J	mg/Kg-dry	1	9/6/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-1C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:00:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-02B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP MERCURY			**SW1311/7471B**		**SW1311**		Analyst: **AB**
Mercury	U	0.0005	0.0200		mg/L	1	9/2/2011 10:16:10 AM
TCLP HERBICIDES SW-846 8151			**SW8151A**		**SW3510C**		Analyst: **SB**
2,4,5-TP	U	0.0002	0.0050		mg/L	1	9/7/2011 6:53:00 PM
2,4-D	U	0.0002	0.0050		mg/L	1	9/7/2011 6:53:00 PM
Surr: 2,4-DCAA	68.8	0	21-144		%REC	1	9/7/2011 6:53:00 PM
TCLP PESTICIDES SW-846 8081			**SW8081B**		**SW3510C**		Analyst: **SB**
Chlordane	0.0010	0.0005	0.0010		mg/L	1	9/7/2011 2:22:00 PM
Endrin	U	0.0002	0.0010		mg/L	1	9/7/2011 2:22:00 PM
gamma-BHC	U	0.0002	0.0010		mg/L	1	9/7/2011 2:22:00 PM
Heptachlor	U	0.0002	0.0010		mg/L	1	9/7/2011 2:22:00 PM
Heptachlor epoxide	U	0.0002	0.0010		mg/L	1	9/7/2011 2:22:00 PM
Methoxychlor	U	0.0002	0.0010		mg/L	1	9/7/2011 2:22:00 PM
Toxaphene	U	0.002	0.010		mg/L	1	9/7/2011 2:22:00 PM
Surr: DCB	85.7	0	28-146		%REC	1	9/7/2011 2:22:00 PM
Surr: TCX	85.2	0	25-147		%REC	1	9/7/2011 2:22:00 PM
TCLP METALS			**SW1311/6010C**		**SW1311**		Analyst: **JP**
Arsenic	0.0220	0.01	0.0500	J	mg/L	1	9/1/2011 3:04:48 PM
Barium	U	1	5.00		mg/L	1	9/1/2011 3:04:48 PM
Cadmium	U	0.005	0.0500		mg/L	1	9/1/2011 3:04:48 PM
Chromium	0.0490	0.005	0.0500	J	mg/L	1	9/1/2011 3:04:48 PM
Lead	0.0430	0.005	0.0500	J	mg/L	1	9/1/2011 3:04:48 PM
Selenium	U	0.01	0.0500		mg/L	1	9/1/2011 3:04:48 PM
Silver	U	0.005	0.0500		mg/L	1	9/1/2011 3:04:48 PM
TCLP SEMIVOLATILES SW-846 8270			**SW8270D**		**SW3510C**		Analyst: **LDS**
2,4,5-Trichlorophenol	U	0.005	0.050		mg/L	1	9/6/2011 6:48:00 PM
2,4,6-Trichlorophenol	U	0.005	0.085		mg/L	1	9/6/2011 6:48:00 PM
2,4-Dinitrotoluene	U	0.005	0.045		mg/L	1	9/6/2011 6:48:00 PM
2-Methylphenol	U	0.005	0.035		mg/L	1	9/6/2011 6:48:00 PM
3+4-Methylphenol	U	0.005	0.040		mg/L	1	9/6/2011 6:48:00 PM
Hexachlorobenzene	U	0.005	0.090		mg/L	1	9/6/2011 6:48:00 PM
Hexachlorobutadiene	U	0.005	0.15		mg/L	1	9/6/2011 6:48:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

ACCREDITED IN ACCORDANCE WITH nelac

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-1C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:00:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-02B		

Certificate of Results

Analyses	Sample Result		LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP SEMIVOLATILES SW-846 8270				**SW8270D**		**SW3510C**		Analyst: **LDS**
Hexachloroethane	U		0.005	0.040		mg/L	1	9/6/2011 6:48:00 PM
Nitrobenzene	U		0.005	0.035		mg/L	1	9/6/2011 6:48:00 PM
Pentachlorophenol	U		0.05	0.17		mg/L	1	9/6/2011 6:48:00 PM
Pyridine	U		0.05	0.12		mg/L	1	9/6/2011 6:48:00 PM
Surr: 2,4,6-Tribromophenol	71.6		0	36-133		%REC	1	9/6/2011 6:48:00 PM
Surr: 2-Fluorobiphenyl	90.7		0	20-131		%REC	1	9/6/2011 6:48:00 PM
Surr: 2-Fluorophenol	70.8		0	22-128		%REC	1	9/6/2011 6:48:00 PM
Surr: 4-Terphenyl-d14	91.5		0	22-132		%REC	1	9/6/2011 6:48:00 PM
Surr: Nitrobenzene-d5	78.6		0	19-133		%REC	1	9/6/2011 6:48:00 PM
Surr: Phenol-d6	49.7		0	18-128		%REC	1	9/6/2011 6:48:00 PM
TCLP VOLATILES				**SW8260C**				Analyst: **LA**
1,1-Dichloroethene	U		0.01	0.020		mg/L	20	9/1/2011 11:41:00 AM
1,2-Dichloroethane	U		0.01	0.020		mg/L	20	9/1/2011 11:41:00 AM
1,4-Dichlorobenzene	U		0.01	0.020		mg/L	20	9/1/2011 11:41:00 AM
2-Butanone	U		0.02	0.040		mg/L	20	9/1/2011 11:41:00 AM
Benzene	U		0.01	0.020		mg/L	20	9/1/2011 11:41:00 AM
Carbon tetrachloride	U		0.01	0.020		mg/L	20	9/1/2011 11:41:00 AM
Chlorobenzene	U		0.01	0.020		mg/L	20	9/1/2011 11:41:00 AM
Chloroform	U		0.01	0.020		mg/L	20	9/1/2011 11:41:00 AM
Tetrachloroethene	U		0.01	0.020		mg/L	20	9/1/2011 11:41:00 AM
Trichloroethene	U		0.01	0.020		mg/L	20	9/1/2011 11:41:00 AM
Vinyl chloride	U		0.01	0.020		mg/L	20	9/1/2011 11:41:00 AM
Surr: 4-Bromofluorobenzene	100		0	63-123		%REC	20	9/1/2011 11:41:00 AM
Surr: Dibromofluoromethane	107		0	68-124		%REC	20	9/1/2011 11:41:00 AM
Surr: Toluene-d8	98.7		0	67-125		%REC	20	9/1/2011 11:41:00 AM
TRIVALENT CHROMIUM				**SW6010C**				Analyst: **JP**
Chromium, Trivalent	12.7		0.11	0.435		mg/Kg-dry	1	9/2/2011
IGNITABILITY/FLASHPOINT SW-846 1020				**SW1020B**				Analyst: **STP**
Ignitability	>		0	140		°F	1	9/1/2011
PAINT FILTER				**SW9095A**				Analyst: **AB**
Free Liquids	ND		0	0		Negative	1	9/1/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-1C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:00:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-02B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SOIL PH MEASURED IN WATER			**SW9045C**				Analyst: **AB**
pH	7.60	0	1.00	H	pH Units	1	9/1/2011 1:30:00 PM
TEMPERATURE			**M2550 B**				Analyst: **AB**
Temp at which pH was measured	21.5	0	0		°C	1	9/1/2011 1:30:00 PM
REACTIVE CYANIDE			**SW7.3.3.2**				Analyst: **STP**
Reactive Cyanide	U	0.06	0.115		mg/Kg-dry	1	9/8/2011
REACTIVE SULFIDE			**SW7.3.4.2**				Analyst: **STP**
Reactive Sulfide	U	1.15	2.30		mg/Kg-dry	1	9/8/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-1Ca (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:02:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-03A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TOTAL DRO AS #2 FUEL (C8-C40)			**SW8015C**		**SW3550C**		Analyst: **LDS**
Total DRO TPH	410	2.81	11		mg/Kg-dry	1	9/2/2011 2:12:00 PM
Surr: o-Terphenyl	55.6	0	31-137		%REC	1	9/2/2011 2:12:00 PM
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	13.0	0	0		wt%	1	9/1/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-1G (12 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:25:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-04A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	13.2	0	0		wt%	1	9/1/2011
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: **LA**
1,1,1,2-Tetrachloroethane	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
1,1,1-Trichloroethane	U	0.59	5.9	C	µg/Kg-dry	1	8/31/2011 3:11:00 PM
1,1,2,2-Tetrachloroethane	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
1,1,2-Trichloro-1,2,2-trifluoroethan	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
1,1,2-Trichloroethane	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
1,1-Dichloroethane	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
1,1-Dichloroethene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
1,1-Dichloropropene	U	0.59	5.9	C	µg/Kg-dry	1	8/31/2011 3:11:00 PM
1,2,3-Trichlorobenzene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
1,2,3-Trichloropropane	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
1,2,4,5-Tetramethylbenzene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
1,2,4-Trichlorobenzene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
1,2,4-Trimethylbenzene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
1,2-Dibromo-3-chloropropane	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
1,2-Dibromoethane	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
1,2-Dichlorobenzene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
1,2-Dichloroethane	U	0.59	5.9	C	µg/Kg-dry	1	8/31/2011 3:11:00 PM
1,2-Dichloropropane	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
1,3,5-Trimethylbenzene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
1,3-Dichlorobenzene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
1,3-dichloropropane	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
1,4-Dichlorobenzene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
1,4-Dioxane	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
2,2-Dichloropropane	U	0.59	5.9	C	µg/Kg-dry	1	8/31/2011 3:11:00 PM
2-Butanone	U	1.8	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
2-Chloroethyl vinyl ether	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
2-Chlorotoluene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
2-Hexanone	U	1.8	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
2-Propanol	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
4-Chlorotoluene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-1G (12 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:25:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-04A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: LA
4-Isopropyltoluene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
4-Methyl-2-pentanone	U	1.8	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Acetone	U	1.8	5.9	C	µg/Kg-dry	1	8/31/2011 3:11:00 PM
Acrolein	U	2.9	12	C	µg/Kg-dry	1	8/31/2011 3:11:00 PM
Acrylonitrile	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Benzene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Bromobenzene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Bromochloromethane	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Bromodichloromethane	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Bromoform	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Bromomethane	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Carbon disulfide	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Carbon tetrachloride	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Chlorobenzene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Chlorodifluoromethane	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Chloroethane	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Chloroform	U	0.59	5.9	C	µg/Kg-dry	1	8/31/2011 3:11:00 PM
Chloromethane	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
cis-1,2-Dichloroethene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
cis-1,3-Dichloropropene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Dibromochloromethane	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Dibromomethane	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Dichlorodifluoromethane	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Diisopropyl ether	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Ethanol	U	2.9	12		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Ethyl acetate	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Ethylbenzene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Freon-114	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Hexachlorobutadiene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Isopropyl acetate	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Isopropylbenzene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
m,p-Xylene	U	1.2	12		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Methyl Acetate	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-1G (12 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:25:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-04A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: **LA**
Methyl tert-butyl ether	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Methylene chloride	13	0.59	5.9	B	µg/Kg-dry	1	8/31/2011 3:11:00 PM
n-Amyl acetate	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Naphthalene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
n-Butyl acetate	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
n-Butylbenzene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
n-Propyl acetate	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
n-Propylbenzene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
o-Xylene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
p-Diethylbenzene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
p-Ethyltoluene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
sec-Butylbenzene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Styrene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
t-Butyl alcohol	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
tert-Butylbenzene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Tetrachloroethene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Toluene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
trans-1,2-Dichloroethene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
trans-1,3-Dichloropropene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Trichloroethene	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Trichlorofluoromethane	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Vinyl acetate	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Vinyl chloride	U	0.59	5.9		µg/Kg-dry	1	8/31/2011 3:11:00 PM
Surr: 4-Bromofluorobenzene	93.2	0	42-133		%REC	1	8/31/2011 3:11:00 PM
Surr: Dibromofluoromethane	97.5	0	50-133		%REC	1	8/31/2011 3:11:00 PM
Surr: Toluene-d8	98.9	0	53-130		%REC	1	8/31/2011 3:11:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-1C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:20:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-05A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
MERCURY			**SW7471B**		**SW7471B**		Analyst: **AB**
Mercury	3.50	0.06	0.116		mg/Kg-dry	10	9/2/2011 12:19:29 PM
TOTAL DRO AS #2 FUEL (C8-C40)			**SW8015C**		**SW3550C**		Analyst: **LDS**
Total DRO TPH	180	2.96	12		mg/Kg-dry	1	9/1/2011 1:59:00 PM
Surr: o-Terphenyl	32.6	0	31-137		%REC	1	9/1/2011 1:59:00 PM
HERBICIDES SW-846 8151			**SW8151A**		**SW8151**		Analyst: **SB**
2,4,5-T	U	1.16	12		µg/Kg-dry	1	9/8/2011 1:47:00 AM
2,4,5-TP	U	1.16	12		µg/Kg-dry	1	9/8/2011 1:47:00 AM
2,4-D	U	1.16	12		µg/Kg-dry	1	9/8/2011 1:47:00 AM
Surr: 2,4-DCAA	127	0	14-148		%REC	1	9/8/2011 1:47:00 AM
PCB'S AS AROCLORS SW-846 METHOD 8082			**SW8082A**		**SW3550C**		Analyst: **SB**
Aroclor 1016	U	1.18	47		µg/Kg-dry	1	9/1/2011 6:51:00 PM
Aroclor 1221	U	1.18	47		µg/Kg-dry	1	9/1/2011 6:51:00 PM
Aroclor 1232	U	1.18	47		µg/Kg-dry	1	9/1/2011 6:51:00 PM
Aroclor 1242	U	1.18	47		µg/Kg-dry	1	9/1/2011 6:51:00 PM
Aroclor 1248	U	1.18	47		µg/Kg-dry	1	9/1/2011 6:51:00 PM
Aroclor 1254	U	1.18	47		µg/Kg-dry	1	9/1/2011 6:51:00 PM
Aroclor 1260	U	1.18	47		µg/Kg-dry	1	9/1/2011 6:51:00 PM
Aroclor 1262	U	1.18	47		µg/Kg-dry	1	9/1/2011 6:51:00 PM
Aroclor 1268	U	1.18	47		µg/Kg-dry	1	9/1/2011 6:51:00 PM
Surr: TCX	33.2	0	17-151		%REC	1	9/1/2011 6:51:00 PM
Surr: DCB	54.8	0	16-152		%REC	1	9/1/2011 6:51:00 PM
PESTICIDES SW-846 METHOD 8081			**SW8081B**		**SW3550C**		Analyst: **SB**
4,4´-DDD	69	0.24	2.4		µg/Kg-dry	1	9/2/2011 12:55:00 PM
4,4´-DDE	400	4.74	47		µg/Kg-dry	20	9/2/2011 6:37:00 PM
4,4´-DDT	1800	4.74	47		µg/Kg-dry	20	9/2/2011 6:37:00 PM
Aldrin	U	0.24	2.4		µg/Kg-dry	1	9/2/2011 12:55:00 PM
alpha-BHC	U	0.24	2.4		µg/Kg-dry	1	9/2/2011 12:55:00 PM
beta-BHC	U	0.24	2.4		µg/Kg-dry	1	9/2/2011 12:55:00 PM
Chlordane	800	23.7	47		µg/Kg-dry	20	9/2/2011 6:37:00 PM
Chlorobenzilate	U	0.24	2.4		µg/Kg-dry	1	9/2/2011 12:55:00 PM
DBCP	9.8	0.24	2.4	P	µg/Kg-dry	1	9/2/2011 12:55:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-1C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:20:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-05A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PESTICIDES SW-846 METHOD 8081			**SW8081B**		**SW3550C**		Analyst: **SB**
delta-BHC	U	0.24	2.4		µg/Kg-dry	1	9/2/2011 12:55:00 PM
Dieldrin	31	0.24	2.4	P	µg/Kg-dry	1	9/2/2011 12:55:00 PM
Endosulfan I	U	0.24	2.4		µg/Kg-dry	1	9/2/2011 12:55:00 PM
Endosulfan II	U	0.24	2.4		µg/Kg-dry	1	9/2/2011 12:55:00 PM
Endosulfan sulfate	U	0.24	2.4		µg/Kg-dry	1	9/2/2011 12:55:00 PM
Endrin	U	0.24	2.4		µg/Kg-dry	1	9/2/2011 12:55:00 PM
Endrin aldehyde	U	0.24	2.4		µg/Kg-dry	1	9/2/2011 12:55:00 PM
Endrin ketone	U	0.24	2.4		µg/Kg-dry	1	9/2/2011 12:55:00 PM
gamma-BHC	U	0.24	2.4		µg/Kg-dry	1	9/2/2011 12:55:00 PM
Heptachlor	1.8	0.24	2.4	JP	µg/Kg-dry	1	9/2/2011 12:55:00 PM
Heptachlor epoxide	U	0.24	2.4		µg/Kg-dry	1	9/2/2011 12:55:00 PM
Hexachlorobenzene	U	0.24	2.4		µg/Kg-dry	1	9/2/2011 12:55:00 PM
Hexachlorocyclopentadiene	U	0.24	2.4		µg/Kg-dry	1	9/2/2011 12:55:00 PM
Methoxychlor	U	0.24	2.4		µg/Kg-dry	1	9/2/2011 12:55:00 PM
Toxaphene	U	5.92	12		µg/Kg-dry	1	9/2/2011 12:55:00 PM
Surr: DCB	62.8	0	23-157		%REC	1	9/2/2011 12:55:00 PM
Surr: DCB	155	0	23-157		%REC	20	9/2/2011 6:37:00 PM
Surr: TCX	82.4	0	21-151		%REC	20	9/2/2011 6:37:00 PM
Surr: TCX	30.5	0	21-151		%REC	1	9/2/2011 12:55:00 PM
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	15.8	0	0		wt%	1	9/1/2011
TARGET ANALYTE LIST METALS			**SW6010C**		**SW3050B**		Analyst: **JP**
Aluminum	4870	0.11	0.446		mg/Kg-dry	1	9/2/2011 9:50:51 AM
Antimony	0.357	0.22	0.558	J	mg/Kg-dry	1	9/2/2011 9:50:51 AM
Arsenic	8.75	0.22	0.558		mg/Kg-dry	1	9/2/2011 9:50:51 AM
Barium	317	0.22	0.446		mg/Kg-dry	1	9/2/2011 9:50:51 AM
Beryllium	U	0.11	0.446		mg/Kg-dry	1	9/2/2011 9:50:51 AM
Cadmium	0.402	0.11	0.446	J	mg/Kg-dry	1	9/2/2011 9:50:51 AM
Calcium	30800	2.23	5.58		mg/Kg-dry	10	9/2/2011 12:29:06 PM
Chromium	13.3	0.11	0.446		mg/Kg-dry	1	9/2/2011 9:50:51 AM
Cobalt	U	0.11	0.446		mg/Kg-dry	1	9/2/2011 9:50:51 AM
Copper	33.2	0.11	0.446		mg/Kg-dry	1	9/2/2011 9:50:51 AM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

ACCREDITED IN ACCORDANCE WITH nelac

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-1C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:20:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-05A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TARGET ANALYTE LIST METALS			**SW6010C**		**SW3050B**		Analyst: **JP**
Iron	27200	2.23	4.46		mg/Kg-dry	10	9/2/2011 12:29:06 PM
Lead	562	0.22	0.446		mg/Kg-dry	1	9/2/2011 9:50:51 AM
Magnesium	2950	0.11	0.446		mg/Kg-dry	1	9/2/2011 9:50:51 AM
Manganese	198	0.11	0.446		mg/Kg-dry	1	9/2/2011 9:50:51 AM
Nickel	12.1	0.11	0.446		mg/Kg-dry	1	9/2/2011 9:50:51 AM
Potassium	1610	0.22	0.558		mg/Kg-dry	1	9/2/2011 9:50:51 AM
Selenium	U	0.22	0.558		mg/Kg-dry	1	9/2/2011 9:50:51 AM
Silver	0.379	0.11	0.446	J	mg/Kg-dry	1	9/2/2011 9:50:51 AM
Sodium	289	0.22	0.558		mg/Kg-dry	1	9/2/2011 9:50:51 AM
Thallium	U	0.33	0.558		mg/Kg-dry	1	9/2/2011 9:50:51 AM
Vanadium	14.9	0.11	0.446		mg/Kg-dry	1	9/2/2011 9:50:51 AM
Zinc	320	0.11	0.446		mg/Kg-dry	1	9/2/2011 9:50:51 AM
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
1,2,4-Trichlorobenzene	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
1,2-Dichlorobenzene	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
1,3-Dichlorobenzene	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
1,4-Dichlorobenzene	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
2,4,5-Trichlorophenol	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
2,4,6-Trichlorophenol	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
2,4-Dichlorophenol	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
2,4-Dimethylphenol	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
2,4-Dinitrophenol	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
2,4-Dinitrotoluene	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
2,6-Dinitrotoluene	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
2-Chloronaphthalene	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
2-Chlorophenol	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
2-Methylnaphthalene	340	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
2-Methylphenol	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
2-Nitroaniline	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
2-Nitrophenol	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
3,3'-Dichlorobenzidine	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
3+4-Methylphenol	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-1C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:20:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-05A		

Certificate of Results

Analyses	Sample Result		LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270				**SW8270D**		**SW3550C**		Analyst: **LDS**
3-Nitroaniline	U		29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
4,6-Dinitro-2-methylphenol	U		29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
4-Bromophenyl phenyl ether	U		29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
4-Chloro-3-methylphenol	U		29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
4-Chloroaniline	U		29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
4-Chlorophenyl phenyl ether	U		29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
4-Nitroaniline	U		29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
4-Nitrophenol	U		29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Acenaphthene	1400		29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Acenaphthylene	370		29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Acetophenone	U		29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Aniline	U		29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Anthracene	14000		296	3000		µg/Kg-dry	10	9/2/2011 1:33:00 PM
Atrazine	U		29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Azobenzene	U		29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Benzaldehyde	U		29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Benzidine	U		29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Benzo(a)anthracene	6900		296	3000		µg/Kg-dry	10	9/2/2011 1:33:00 PM
Benzo(a)pyrene	5000		296	3000		µg/Kg-dry	10	9/2/2011 1:33:00 PM
Benzo(b)fluoranthene	5300		296	3000		µg/Kg-dry	10	9/2/2011 1:33:00 PM
Benzo(g,h,i)perylene	3300		29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Benzo(k)fluoranthene	5300		296	3000		µg/Kg-dry	10	9/2/2011 1:33:00 PM
Benzoic acid	U		29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Benzyl alcohol	U		29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Biphenyl	U		29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Bis(2-chloroethoxy)methane	U		29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Bis(2-chloroethyl)ether	U		29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Bis(2-chloroisopropyl)ether	U		29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Bis(2-ethylhexyl)phthalate	810		29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Butyl benzyl phthalate	540		29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Caprolactam	U		29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Carbazole	1100		29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Chrysene	7100		296	3000		µg/Kg-dry	10	9/2/2011 1:33:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-1C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:20:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-05A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
Dibenzo(a,h)anthracene	1200	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Dibenzofuran	940	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Diethyl phthalate	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Dimethyl phthalate	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Di-n-butyl phthalate	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Di-n-octyl phthalate	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Fluoranthene	17000	296	3000		µg/Kg-dry	10	9/2/2011 1:33:00 PM
Fluorene	1200	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Hexachlorobenzene	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Hexachlorobutadiene	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Hexachlorocyclopentadiene	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Hexachloroethane	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Indeno(1,2,3-c,d)pyrene	3200	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Isophorone	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Naphthalene	750	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Nitrobenzene	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
N-Nitrosodimethylamine	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
N-Nitrosodi-n-propylamine	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
N-Nitrosodiphenylamine	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Parathion	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Pentachlorophenol	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Phenanthrene	15000	296	3000		µg/Kg-dry	10	9/2/2011 1:33:00 PM
Phenol	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Pyrene	13000	296	3000		µg/Kg-dry	10	9/2/2011 1:33:00 PM
Pyridine	U	29.6	300		µg/Kg-dry	1	9/1/2011 2:26:00 PM
Surr: 2,4,6-Tribromophenol	50.4	0	21-119		%REC	1	9/1/2011 2:26:00 PM
Surr: 2,4,6-Tribromophenol	39.1	0	21-119		%REC	10	9/2/2011 1:33:00 PM
Surr: 2-Fluorobiphenyl	68.4	0	21-117		%REC	1	9/1/2011 2:26:00 PM
Surr: 2-Fluorobiphenyl	56.8	0	21-117		%REC	10	9/2/2011 1:33:00 PM
Surr: 2-Fluorophenol	23.3	0	11-105		%REC	10	9/2/2011 1:33:00 PM
Surr: 2-Fluorophenol	26.9	0	11-105		%REC	1	9/1/2011 2:26:00 PM
Surr: 4-Terphenyl-d14	58.9	0	21-132		%REC	10	9/2/2011 1:33:00 PM
Surr: 4-Terphenyl-d14	67.1	0	21-132		%REC	1	9/1/2011 2:26:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-1C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:20:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-05A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
Surr: Nitrobenzene-d5	27.1	0	18-116		%REC	10	9/2/2011 1:33:00 PM
Surr: Nitrobenzene-d5	45.1	0	18-116		%REC	1	9/1/2011 2:26:00 PM
Surr: Phenol-d6	21.7	0	12-110		%REC	10	9/2/2011 1:33:00 PM
Surr: Phenol-d6	23.6	0	12-110		%REC	1	9/1/2011 2:26:00 PM
CYANIDE, TOTAL			**SW9012A**		**SW9012A**		Analyst: **STP**
Cyanide, Total & Amenable: Auto Colorimetric	0.452	0.06	0.119		mg/Kg-dry	1	9/6/2011
HEXAVALENT CHROMIUM			**SW7196A**				Analyst: **AB**
Chromium, Hexavalent	1.77	0.24	0.475		mg/Kg-dry	1	9/6/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-1C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:20:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-05B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP MERCURY			**SW1311/7471B**		**SW1311**		Analyst: **AB**
Mercury	U	0.0005	0.0200		mg/L	1	9/2/2011 10:18:18 AM
TCLP HERBICIDES SW-846 8151			**SW8151A**		**SW3510C**		Analyst: **SB**
2,4,5-TP	U	0.0002	0.0050		mg/L	1	9/7/2011 7:08:00 PM
2,4-D	U	0.0002	0.0050		mg/L	1	9/7/2011 7:08:00 PM
Surr: 2,4-DCAA	108	0	21-144		%REC	1	9/7/2011 7:08:00 PM
TCLP PESTICIDES SW-846 8081			**SW8081B**		**SW3510C**		Analyst: **SB**
Chlordane	0.00099	0.0005	0.0010	J	mg/L	1	9/7/2011 2:37:00 PM
Endrin	U	0.0002	0.0010		mg/L	1	9/7/2011 2:37:00 PM
gamma-BHC	U	0.0002	0.0010		mg/L	1	9/7/2011 2:37:00 PM
Heptachlor	U	0.0002	0.0010		mg/L	1	9/7/2011 2:37:00 PM
Heptachlor epoxide	U	0.0002	0.0010		mg/L	1	9/7/2011 2:37:00 PM
Methoxychlor	U	0.0002	0.0010		mg/L	1	9/7/2011 2:37:00 PM
Toxaphene	U	0.002	0.010		mg/L	1	9/7/2011 2:37:00 PM
Surr: DCB	95.3	0	28-146		%REC	1	9/7/2011 2:37:00 PM
Surr: TCX	96.2	0	25-147		%REC	1	9/7/2011 2:37:00 PM
TCLP METALS			**SW1311/6010C**		**SW1311**		Analyst: **JP**
Arsenic	0.0160	0.01	0.0500	J	mg/L	1	9/1/2011 3:06:52 PM
Barium	U	1	5.00		mg/L	1	9/1/2011 3:06:52 PM
Cadmium	U	0.005	0.0500		mg/L	1	9/1/2011 3:06:52 PM
Chromium	0.00900	0.005	0.0500	J	mg/L	1	9/1/2011 3:06:52 PM
Lead	0.0130	0.005	0.0500	J	mg/L	1	9/1/2011 3:06:52 PM
Selenium	U	0.01	0.0500		mg/L	1	9/1/2011 3:06:52 PM
Silver	U	0.005	0.0500		mg/L	1	9/1/2011 3:06:52 PM
TCLP SEMIVOLATILES SW-846 8270			**SW8270D**		**SW3510C**		Analyst: **LDS**
2,4,5-Trichlorophenol	U	0.005	0.050		mg/L	1	9/6/2011 7:13:00 PM
2,4,6-Trichlorophenol	U	0.005	0.085		mg/L	1	9/6/2011 7:13:00 PM
2,4-Dinitrotoluene	U	0.005	0.045		mg/L	1	9/6/2011 7:13:00 PM
2-Methylphenol	U	0.005	0.035		mg/L	1	9/6/2011 7:13:00 PM
3+4-Methylphenol	U	0.005	0.040		mg/L	1	9/6/2011 7:13:00 PM
Hexachlorobenzene	U	0.005	0.090		mg/L	1	9/6/2011 7:13:00 PM
Hexachlorobutadiene	U	0.005	0.15		mg/L	1	9/6/2011 7:13:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.	

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-1C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:20:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-05B		

Certificate of Results

Analyses	Sample Result		LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP SEMIVOLATILES SW-846 8270				**SW8270D**		**SW3510C**		Analyst: **LDS**
Hexachloroethane	U		0.005	0.040		mg/L	1	9/6/2011 7:13:00 PM
Nitrobenzene	U		0.005	0.035		mg/L	1	9/6/2011 7:13:00 PM
Pentachlorophenol	U		0.05	0.17		mg/L	1	9/6/2011 7:13:00 PM
Pyridine	U		0.05	0.12		mg/L	1	9/6/2011 7:13:00 PM
Surr: 2,4,6-Tribromophenol	70.4		0	36-133		%REC	1	9/6/2011 7:13:00 PM
Surr: 2-Fluorobiphenyl	87.7		0	20-131		%REC	1	9/6/2011 7:13:00 PM
Surr: 2-Fluorophenol	72.2		0	22-128		%REC	1	9/6/2011 7:13:00 PM
Surr: 4-Terphenyl-d14	95.2		0	22-132		%REC	1	9/6/2011 7:13:00 PM
Surr: Nitrobenzene-d5	80.4		0	19-133		%REC	1	9/6/2011 7:13:00 PM
Surr: Phenol-d6	52.2		0	18-128		%REC	1	9/6/2011 7:13:00 PM
TCLP VOLATILES				**SW8260C**				Analyst: **LA**
1,1-Dichloroethene	U		0.01	0.020		mg/L	20	9/1/2011 12:05:00 PM
1,2-Dichloroethane	U		0.01	0.020		mg/L	20	9/1/2011 12:05:00 PM
1,4-Dichlorobenzene	U		0.01	0.020		mg/L	20	9/1/2011 12:05:00 PM
2-Butanone	U		0.02	0.040		mg/L	20	9/1/2011 12:05:00 PM
Benzene	U		0.01	0.020		mg/L	20	9/1/2011 12:05:00 PM
Carbon tetrachloride	U		0.01	0.020		mg/L	20	9/1/2011 12:05:00 PM
Chlorobenzene	U		0.01	0.020		mg/L	20	9/1/2011 12:05:00 PM
Chloroform	U		0.01	0.020		mg/L	20	9/1/2011 12:05:00 PM
Tetrachloroethene	U		0.01	0.020		mg/L	20	9/1/2011 12:05:00 PM
Trichloroethene	U		0.01	0.020		mg/L	20	9/1/2011 12:05:00 PM
Vinyl chloride	U		0.01	0.020		mg/L	20	9/1/2011 12:05:00 PM
Surr: 4-Bromofluorobenzene	97.4		0	63-123		%REC	20	9/1/2011 12:05:00 PM
Surr: Dibromofluoromethane	101		0	68-124		%REC	20	9/1/2011 12:05:00 PM
Surr: Toluene-d8	98.0		0	67-125		%REC	20	9/1/2011 12:05:00 PM
TRIVALENT CHROMIUM				**SW6010C**				Analyst: **JP**
Chromium, Trivalent	11.6		0.11	0.446		mg/Kg-dry	1	9/2/2011
IGNITABILITY/FLASHPOINT SW-846 1020				**SW1020B**				Analyst: **STP**
Ignitability	>		0	140		°F	1	9/1/2011
SOIL PH MEASURED IN WATER				**SW9045C**				Analyst: **AB**
pH	7.40		0	1.00	H	pH Units	1	9/1/2011 1:32:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-1C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:20:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-05B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TEMPERATURE			**M2550 B**				Analyst: **AB**
Temp at which pH was measured	21.0	0	0		°C	1	9/1/2011 1:32:00 PM
REACTIVE CYANIDE			**SW7.3.3.2**				Analyst: **STP**
Reactive Cyanide	U	0.06	0.119		mg/Kg-dry	1	9/8/2011
REACTIVE SULFIDE			**SW7.3.4.2**				Analyst: **STP**
Reactive Sulfide	U	1.19	2.37		mg/Kg-dry	1	9/8/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-1Ca (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:22:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-06A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TOTAL DRO AS #2 FUEL (C8-C40)			**SW8015C**		**SW3550C**		Analyst: **LDS**
Total DRO TPH	110	2.92	12		mg/Kg-dry	1	9/2/2011 2:37:00 PM
Surr: o-Terphenyl	35.3	0	31-137		%REC	1	9/2/2011 2:37:00 PM
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	14.6	0	0		wt%	1	9/1/2011

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-2G (4 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:25:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-07A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PERCENT MOISTURE			D2216				Analyst: KK
Percent Moisture	11.7	0	0		wt%	1	9/1/2011
VOLATILE SW-846 METHOD 8260			SW8260C				Analyst: LA
1,1,1,2-Tetrachloroethane	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
1,1,1-Trichloroethane	U	0.58	5.8	C	µg/Kg-dry	1	8/31/2011 3:36:00 PM
1,1,2,2-Tetrachloroethane	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
1,1,2-Trichloro-1,2,2-trifluoroethan	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
1,1,2-Trichloroethane	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
1,1-Dichloroethane	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
1,1-Dichloroethene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
1,1-Dichloropropene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
1,2,3-Trichlorobenzene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
1,2,3-Trichloropropane	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
1,2,4,5-Tetramethylbenzene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
1,2,4-Trichlorobenzene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
1,2,4-Trimethylbenzene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
1,2-Dibromo-3-chloropropane	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
1,2-Dibromoethane	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
1,2-Dichlorobenzene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
1,2-Dichloroethane	U	0.58	5.8	C	µg/Kg-dry	1	8/31/2011 3:36:00 PM
1,2-Dichloropropane	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
1,3,5-Trimethylbenzene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
1,3-Dichlorobenzene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
1,3-dichloropropane	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
1,4-Dichlorobenzene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
1,4-Dioxane	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
2,2-Dichloropropane	U	0.58	5.8	C	µg/Kg-dry	1	8/31/2011 3:36:00 PM
2-Butanone	U	1.7	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
2-Chloroethyl vinyl ether	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
2-Chlorotoluene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
2-Hexanone	U	1.7	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
2-Propanol	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
4-Chlorotoluene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

ACCREDITED IN ACCORDANCE WITH nelac

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-2G (4 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:25:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-07A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: **LA**
4-Isopropyltoluene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
4-Methyl-2-pentanone	U	1.7	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Acetone	U	1.7	5.8	C	µg/Kg-dry	1	8/31/2011 3:36:00 PM
Acrolein	U	2.9	12	C	µg/Kg-dry	1	8/31/2011 3:36:00 PM
Acrylonitrile	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Benzene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Bromobenzene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Bromochloromethane	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Bromodichloromethane	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Bromoform	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Bromomethane	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Carbon disulfide	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Carbon tetrachloride	U	0.58	5.8	C	µg/Kg-dry	1	8/31/2011 3:36:00 PM
Chlorobenzene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Chlorodifluoromethane	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Chloroethane	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Chloroform	U	0.58	5.8	C	µg/Kg-dry	1	8/31/2011 3:36:00 PM
Chloromethane	U	0.58	5.8	C	µg/Kg-dry	1	8/31/2011 3:36:00 PM
cis-1,2-Dichloroethene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
cis-1,3-Dichloropropene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Dibromochloromethane	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Dibromomethane	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Dichlorodifluoromethane	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Diisopropyl ether	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Ethanol	U	2.9	12		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Ethyl acetate	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Ethylbenzene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Freon-114	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Hexachlorobutadiene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Isopropyl acetate	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Isopropylbenzene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
m,p-Xylene	U	1.2	12		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Methyl Acetate	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-2G (4 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:25:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-07A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: **LA**
Methyl tert-butyl ether	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Methylene chloride	11	0.58	5.8	B	µg/Kg-dry	1	8/31/2011 3:36:00 PM
n-Amyl acetate	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Naphthalene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
n-Butyl acetate	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
n-Butylbenzene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
n-Propyl acetate	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
n-Propylbenzene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
o-Xylene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
p-Diethylbenzene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
p-Ethyltoluene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
sec-Butylbenzene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Styrene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
t-Butyl alcohol	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
tert-Butylbenzene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Tetrachloroethene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Toluene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
trans-1,2-Dichloroethene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
trans-1,3-Dichloropropene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Trichloroethene	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Trichlorofluoromethane	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Vinyl acetate	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Vinyl chloride	U	0.58	5.8		µg/Kg-dry	1	8/31/2011 3:36:00 PM
Surr: 4-Bromofluorobenzene	94.4	0	42-133		%REC	1	8/31/2011 3:36:00 PM
Surr: Dibromofluoromethane	98.5	0	50-133		%REC	1	8/31/2011 3:36:00 PM
Surr: Toluene-d8	99.2	0	53-130		%REC	1	8/31/2011 3:36:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-2C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:15:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-08A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
MERCURY			**SW7471B**		**SW7471B**		Analyst: **AB**
Mercury	1.66	0.03	0.0531		mg/Kg-dry	5	9/2/2011 12:21:38 PM
TOTAL DRO AS #2 FUEL (C8-C40)			**SW8015C**		**SW3550C**		Analyst: **LDS**
Total DRO TPH	220	2.87	11		mg/Kg-dry	1	9/1/2011 2:24:00 PM
Surr: o-Terphenyl	44.0	0	31-137		%REC	1	9/1/2011 2:24:00 PM
HERBICIDES SW-846 8151			**SW8151A**		**SW8151**		Analyst: **SB**
2,4,5-T	U	1.16	12		µg/Kg-dry	1	9/8/2011 2:01:00 AM
2,4,5-TP	U	1.16	12		µg/Kg-dry	1	9/8/2011 2:01:00 AM
2,4-D	U	1.16	12		µg/Kg-dry	1	9/8/2011 2:01:00 AM
Surr: 2,4-DCAA	89.1	0	14-148		%REC	1	9/8/2011 2:01:00 AM
PCB'S AS AROCLORS SW-846 METHOD 8082			**SW8082A**		**SW3550C**		Analyst: **SB**
Aroclor 1016	U	1.15	46		µg/Kg-dry	1	9/1/2011 7:15:00 PM
Aroclor 1221	U	1.15	46		µg/Kg-dry	1	9/1/2011 7:15:00 PM
Aroclor 1232	U	1.15	46		µg/Kg-dry	1	9/1/2011 7:15:00 PM
Aroclor 1242	U	1.15	46		µg/Kg-dry	1	9/1/2011 7:15:00 PM
Aroclor 1248	U	1.15	46		µg/Kg-dry	1	9/1/2011 7:15:00 PM
Aroclor 1254	U	1.15	46		µg/Kg-dry	1	9/1/2011 7:15:00 PM
Aroclor 1260	U	1.15	46		µg/Kg-dry	1	9/1/2011 7:15:00 PM
Aroclor 1262	U	1.15	46		µg/Kg-dry	1	9/1/2011 7:15:00 PM
Aroclor 1268	U	1.15	46		µg/Kg-dry	1	9/1/2011 7:15:00 PM
Surr: TCX	45.0	0	17-151		%REC	1	9/1/2011 7:15:00 PM
Surr: DCB	57.7	0	16-152		%REC	1	9/1/2011 7:15:00 PM
PESTICIDES SW-846 METHOD 8081			**SW8081B**		**SW3550C**		Analyst: **SB**
4,4´-DDD	1.2	0.23	2.3	JP	µg/Kg-dry	1	9/2/2011 1:38:00 PM
4,4´-DDE	3.5	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:38:00 PM
4,4´-DDT	15	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:38:00 PM
Aldrin	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:38:00 PM
alpha-BHC	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:38:00 PM
beta-BHC	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:38:00 PM
Chlordane	34	1.15	2.3		µg/Kg-dry	1	9/2/2011 1:38:00 PM
Chlorobenzilate	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:38:00 PM
DBCP	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:38:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.	

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-2C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:15:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-08A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PESTICIDES SW-846 METHOD 8081			**SW8081B**		**SW3550C**		Analyst: **SB**
delta-BHC	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:38:00 PM
Dieldrin	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:38:00 PM
Endosulfan I	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:38:00 PM
Endosulfan II	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:38:00 PM
Endosulfan sulfate	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:38:00 PM
Endrin	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:38:00 PM
Endrin aldehyde	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:38:00 PM
Endrin ketone	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:38:00 PM
gamma-BHC	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:38:00 PM
Heptachlor	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:38:00 PM
Heptachlor epoxide	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:38:00 PM
Hexachlorobenzene	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:38:00 PM
Hexachlorocyclopentadiene	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:38:00 PM
Methoxychlor	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:38:00 PM
Toxaphene	U	5.74	11		µg/Kg-dry	1	9/2/2011 1:38:00 PM
Surr: DCB	55.3	0	23-157		%REC	1	9/2/2011 1:38:00 PM
Surr: TCX	38.4	0	21-151		%REC	1	9/2/2011 1:38:00 PM
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	13.6	0	0		wt%	1	9/1/2011
TARGET ANALYTE LIST METALS			**SW6010C**		**SW3050B**		Analyst: **JP**
Aluminum	4180	0.11	0.443		mg/Kg-dry	1	9/2/2011 9:52:54 AM
Antimony	0.266	0.22	0.554	J	mg/Kg-dry	1	9/2/2011 9:52:54 AM
Arsenic	12.7	0.22	0.554		mg/Kg-dry	1	9/2/2011 9:52:54 AM
Barium	264	0.22	0.443		mg/Kg-dry	1	9/2/2011 9:52:54 AM
Beryllium	U	0.11	0.443		mg/Kg-dry	1	9/2/2011 9:52:54 AM
Cadmium	0.842	0.11	0.443		mg/Kg-dry	1	9/2/2011 9:52:54 AM
Calcium	18800	2.22	5.54		mg/Kg-dry	10	9/2/2011 12:31:10 PM
Chromium	17.9	0.11	0.443		mg/Kg-dry	1	9/2/2011 9:52:54 AM
Cobalt	U	0.11	0.443		mg/Kg-dry	1	9/2/2011 9:52:54 AM
Copper	50.1	0.11	0.443		mg/Kg-dry	1	9/2/2011 9:52:54 AM
Iron	13400	2.22	4.43		mg/Kg-dry	10	9/2/2011 12:31:10 PM
Lead	1180	0.22	0.443		mg/Kg-dry	1	9/2/2011 9:52:54 AM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.	

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-2C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:15:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-08A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TARGET ANALYTE LIST METALS			**SW6010C**		**SW3050B**		Analyst: **JP**
Magnesium	2940	0.11	0.443		mg/Kg-dry	1	9/2/2011 9:52:54 AM
Manganese	158	0.11	0.443		mg/Kg-dry	1	9/2/2011 9:52:54 AM
Nickel	13.9	0.11	0.443		mg/Kg-dry	1	9/2/2011 9:52:54 AM
Potassium	1240	0.22	0.554		mg/Kg-dry	1	9/2/2011 9:52:54 AM
Selenium	1.35	0.22	0.554		mg/Kg-dry	1	9/2/2011 9:52:54 AM
Silver	0.355	0.11	0.443	J	mg/Kg-dry	1	9/2/2011 9:52:54 AM
Sodium	257	0.22	0.554		mg/Kg-dry	1	9/2/2011 9:52:54 AM
Thallium	U	0.33	0.554		mg/Kg-dry	1	9/2/2011 9:52:54 AM
Vanadium	18.4	0.11	0.443		mg/Kg-dry	1	9/2/2011 9:52:54 AM
Zinc	372	0.11	0.443		mg/Kg-dry	1	9/2/2011 9:52:54 AM
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
1,2,4-Trichlorobenzene	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
1,2-Dichlorobenzene	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
1,3-Dichlorobenzene	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
1,4-Dichlorobenzene	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
2,4,5-Trichlorophenol	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
2,4,6-Trichlorophenol	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
2,4-Dichlorophenol	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
2,4-Dimethylphenol	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
2,4-Dinitrophenol	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
2,4-Dinitrotoluene	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
2,6-Dinitrotoluene	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
2-Chloronaphthalene	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
2-Chlorophenol	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
2-Methylnaphthalene	750	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
2-Methylphenol	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
2-Nitroaniline	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
2-Nitrophenol	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
3,3´-Dichlorobenzidine	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
3+4-Methylphenol	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
3-Nitroaniline	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
4,6-Dinitro-2-methylphenol	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

ACCREDITED IN ACCORDANCE WITH nelac

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-2C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:15:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-08A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
4-Bromophenyl phenyl ether	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
4-Chloro-3-methylphenol	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
4-Chloroaniline	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
4-Chlorophenyl phenyl ether	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
4-Nitroaniline	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
4-Nitrophenol	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Acenaphthene	2400	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Acenaphthylene	260	28.7	290	J	µg/Kg-dry	1	9/1/2011 2:51:00 PM
Acetophenone	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Aniline	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Anthracene	26000	287	2900		µg/Kg-dry	10	9/2/2011 1:58:00 PM
Atrazine	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Azobenzene	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Benzaldehyde	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Benzidine	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Benzo(a)anthracene	9000	287	2900		µg/Kg-dry	10	9/2/2011 1:58:00 PM
Benzo(a)pyrene	6400	287	2900		µg/Kg-dry	10	9/2/2011 1:58:00 PM
Benzo(b)fluoranthene	5300	287	2900		µg/Kg-dry	10	9/2/2011 1:58:00 PM
Benzo(g,h,i)perylene	3400	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Benzo(k)fluoranthene	5400	287	2900		µg/Kg-dry	10	9/2/2011 1:58:00 PM
Benzoic acid	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Benzyl alcohol	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Biphenyl	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Bis(2-chloroethoxy)methane	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Bis(2-chloroethyl)ether	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Bis(2-chloroisopropyl)ether	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Bis(2-ethylhexyl)phthalate	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Butyl benzyl phthalate	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Caprolactam	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Carbazole	1200	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Chrysene	9100	287	2900		µg/Kg-dry	10	9/2/2011 1:58:00 PM
Dibenzo(a,h)anthracene	1200	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Dibenzofuran	1500	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-2C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:15:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-08A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
Diethyl phthalate	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Dimethyl phthalate	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Di-n-butyl phthalate	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Di-n-octyl phthalate	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Fluoranthene	21000	287	2900		µg/Kg-dry	10	9/2/2011 1:58:00 PM
Fluorene	2300	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Hexachlorobenzene	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Hexachlorobutadiene	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Hexachlorocyclopentadiene	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Hexachloroethane	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Indeno(1,2,3-c,d)pyrene	3200	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Isophorone	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Naphthalene	1100	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Nitrobenzene	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
N-Nitrosodimethylamine	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
N-Nitrosodi-n-propylamine	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
N-Nitrosodiphenylamine	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Parathion	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Pentachlorophenol	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Phenanthrene	26000	287	2900		µg/Kg-dry	10	9/2/2011 1:58:00 PM
Phenol	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Pyrene	21000	287	2900		µg/Kg-dry	10	9/2/2011 1:58:00 PM
Pyridine	U	28.7	290		µg/Kg-dry	1	9/1/2011 2:51:00 PM
Surr: 2,4,6-Tribromophenol	56.7	0	21-119		%REC	1	9/1/2011 2:51:00 PM
Surr: 2,4,6-Tribromophenol	25.6	0	21-119		%REC	10	9/2/2011 1:58:00 PM
Surr: 2-Fluorobiphenyl	71.1	0	21-117		%REC	1	9/1/2011 2:51:00 PM
Surr: 2-Fluorobiphenyl	72.9	0	21-117		%REC	10	9/2/2011 1:58:00 PM
Surr: 2-Fluorophenol	32.0	0	11-105		%REC	10	9/2/2011 1:58:00 PM
Surr: 2-Fluorophenol	42.3	0	11-105		%REC	1	9/1/2011 2:51:00 PM
Surr: 4-Terphenyl-d14	66.2	0	21-132		%REC	10	9/2/2011 1:58:00 PM
Surr: 4-Terphenyl-d14	73.7	0	21-132		%REC	1	9/1/2011 2:51:00 PM
Surr: Nitrobenzene-d5	46.8	0	18-116		%REC	10	9/2/2011 1:58:00 PM
Surr: Nitrobenzene-d5	52.5	0	18-116		%REC	1	9/1/2011 2:51:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-2C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:15:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-08A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
Surr: Phenol-d6	38.6	0	12-110		%REC	10	9/2/2011 1:58:00 PM
Surr: Phenol-d6	39.5	0	12-110		%REC	1	9/1/2011 2:51:00 PM
CYANIDE, TOTAL			**SW9012A**		**SW9012A**		Analyst: **STP**
Cyanide, Total & Amenable: Auto Colorimetric	0.526	0.06	0.116		mg/Kg-dry	1	9/6/2011
HEXAVALENT CHROMIUM			**SW7196A**				Analyst: **AB**
Chromium, Hexavalent	U	0.23	0.463		mg/Kg-dry	1	9/6/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-2C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:15:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-08B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP MERCURY			**SW1311/7471B**		**SW1311**		Analyst: **AB**
Mercury	U	0.0005	0.0200		mg/L	1	9/2/2011 10:20:25 AM
TCLP HERBICIDES SW-846 8151			**SW8151A**		**SW3510C**		Analyst: **SB**
2,4,5-TP	U	0.0002	0.0050		mg/L	1	9/7/2011 7:22:00 PM
2,4-D	U	0.0002	0.0050		mg/L	1	9/7/2011 7:22:00 PM
Surr: 2,4-DCAA	68.3	0	21-144		%REC	1	9/7/2011 7:22:00 PM
TCLP PESTICIDES SW-846 8081			**SW8081B**		**SW3510C**		Analyst: **SB**
Chlordane	0.00059	0.0005	0.0010	J	mg/L	1	9/7/2011 2:51:00 PM
Endrin	U	0.0002	0.0010		mg/L	1	9/7/2011 2:51:00 PM
gamma-BHC	U	0.0002	0.0010		mg/L	1	9/7/2011 2:51:00 PM
Heptachlor	U	0.0002	0.0010		mg/L	1	9/7/2011 2:51:00 PM
Heptachlor epoxide	U	0.0002	0.0010		mg/L	1	9/7/2011 2:51:00 PM
Methoxychlor	U	0.0002	0.0010		mg/L	1	9/7/2011 2:51:00 PM
Toxaphene	U	0.002	0.010		mg/L	1	9/7/2011 2:51:00 PM
Surr: DCB	109	0	28-146		%REC	1	9/7/2011 2:51:00 PM
Surr: TCX	106	0	25-147		%REC	1	9/7/2011 2:51:00 PM
TCLP METALS			**SW1311/6010C**		**SW1311**		Analyst: **JP**
Arsenic	0.0360	0.01	0.0500	J	mg/L	1	9/1/2011 3:08:56 PM
Barium	U	1	5.00		mg/L	1	9/1/2011 3:08:56 PM
Cadmium	U	0.005	0.0500		mg/L	1	9/1/2011 3:08:56 PM
Chromium	0.0100	0.005	0.0500	J	mg/L	1	9/1/2011 3:08:56 PM
Lead	0.0370	0.005	0.0500	J	mg/L	1	9/1/2011 3:08:56 PM
Selenium	U	0.01	0.0500		mg/L	1	9/1/2011 3:08:56 PM
Silver	U	0.005	0.0500		mg/L	1	9/1/2011 3:08:56 PM
TCLP SEMIVOLATILES SW-846 8270			**SW8270D**		**SW3510C**		Analyst: **LDS**
2,4,5-Trichlorophenol	U	0.005	0.050		mg/L	1	9/6/2011 7:38:00 PM
2,4,6-Trichlorophenol	U	0.005	0.085		mg/L	1	9/6/2011 7:38:00 PM
2,4-Dinitrotoluene	U	0.005	0.045		mg/L	1	9/6/2011 7:38:00 PM
2-Methylphenol	U	0.005	0.035		mg/L	1	9/6/2011 7:38:00 PM
3+4-Methylphenol	U	0.005	0.040		mg/L	1	9/6/2011 7:38:00 PM
Hexachlorobenzene	U	0.005	0.090		mg/L	1	9/6/2011 7:38:00 PM
Hexachlorobutadiene	U	0.005	0.15		mg/L	1	9/6/2011 7:38:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

ACCREDITED IN ACCORDANCE WITH nelac

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-2C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:15:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-08B		

Certificate of Results

Analyses	Sample Result		LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP SEMIVOLATILES SW-846 8270				**SW8270D**		**SW3510C**		Analyst: **LDS**
Hexachloroethane	U		0.005	0.040		mg/L	1	9/6/2011 7:38:00 PM
Nitrobenzene	U		0.005	0.035		mg/L	1	9/6/2011 7:38:00 PM
Pentachlorophenol	U		0.05	0.17		mg/L	1	9/6/2011 7:38:00 PM
Pyridine	U		0.05	0.12		mg/L	1	9/6/2011 7:38:00 PM
Surr: 2,4,6-Tribromophenol	58.7		0	36-133		%REC	1	9/6/2011 7:38:00 PM
Surr: 2-Fluorobiphenyl	87.9		0	20-131		%REC	1	9/6/2011 7:38:00 PM
Surr: 2-Fluorophenol	79.1		0	22-128		%REC	1	9/6/2011 7:38:00 PM
Surr: 4-Terphenyl-d14	96.9		0	22-132		%REC	1	9/6/2011 7:38:00 PM
Surr: Nitrobenzene-d5	75.8		0	19-133		%REC	1	9/6/2011 7:38:00 PM
Surr: Phenol-d6	57.7		0	18-128		%REC	1	9/6/2011 7:38:00 PM
TCLP VOLATILES				**SW8260C**				Analyst: **LA**
1,1-Dichloroethene	U		0.01	0.020		mg/L	20	9/1/2011 12:28:00 PM
1,2-Dichloroethane	U		0.01	0.020		mg/L	20	9/1/2011 12:28:00 PM
1,4-Dichlorobenzene	U		0.01	0.020		mg/L	20	9/1/2011 12:28:00 PM
2-Butanone	U		0.02	0.040		mg/L	20	9/1/2011 12:28:00 PM
Benzene	U		0.01	0.020		mg/L	20	9/1/2011 12:28:00 PM
Carbon tetrachloride	U		0.01	0.020		mg/L	20	9/1/2011 12:28:00 PM
Chlorobenzene	U		0.01	0.020		mg/L	20	9/1/2011 12:28:00 PM
Chloroform	U		0.01	0.020		mg/L	20	9/1/2011 12:28:00 PM
Tetrachloroethene	U		0.01	0.020		mg/L	20	9/1/2011 12:28:00 PM
Trichloroethene	U		0.01	0.020		mg/L	20	9/1/2011 12:28:00 PM
Vinyl chloride	U		0.01	0.020		mg/L	20	9/1/2011 12:28:00 PM
Surr: 4-Bromofluorobenzene	98.3		0	63-123		%REC	20	9/1/2011 12:28:00 PM
Surr: Dibromofluoromethane	104		0	68-124		%REC	20	9/1/2011 12:28:00 PM
Surr: Toluene-d8	96.1		0	67-125		%REC	20	9/1/2011 12:28:00 PM
TRIVALENT CHROMIUM				**SW6010C**				Analyst: **JP**
Chromium, Trivalent	17.9		0.11	0.443		mg/Kg-dry	1	9/2/2011
IGNITABILITY/FLASHPOINT SW-846 1020				**SW1020B**				Analyst: **STP**
Ignitability	>		0	140		°F	1	9/1/2011
SOIL PH MEASURED IN WATER				**SW9045C**				Analyst: **AB**
pH	7.80		0	1.00	H	pH Units	1	9/1/2011 1:34:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-2C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:15:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-08B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TEMPERATURE			**M2550 B**				Analyst: **AB**
Temp at which pH was measured	21.5	0	0		°C	1	9/1/2011 1:34:00 PM
REACTIVE CYANIDE			**SW7.3.3.2**				Analyst: **STP**
Reactive Cyanide	U	0.06	0.116		mg/Kg-dry	1	9/8/2011
REACTIVE SULFIDE			**SW7.3.4.2**				Analyst: **STP**
Reactive Sulfide	U	1.16	2.31		mg/Kg-dry	1	9/8/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-2Ca (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:17:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-09A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TOTAL DRO AS #2 FUEL (C8-C40)			**SW8015C**		**SW3550C**		Analyst: **LDS**
Total DRO TPH	160	2.94	12		mg/Kg-dry	1	9/2/2011 3:02:00 PM
Surr: o-Terphenyl	39.7	0	31-137		%REC	1	9/2/2011 3:02:00 PM
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	16.1	0	0		wt%	1	9/1/2011

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-2G (12 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:45:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-10A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PERCENT MOISTURE			D2216				Analyst: KK
Percent Moisture	17.2	0	0		wt%	1	9/1/2011
VOLATILE SW-846 METHOD 8260			SW8260C				Analyst: LA
1,1,1,2-Tetrachloroethane	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
1,1,1-Trichloroethane	U	0.53	5.3	C	µg/Kg-dry	1	8/31/2011 4:00:00 PM
1,1,2,2-Tetrachloroethane	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
1,1,2-Trichloro-1,2,2-trifluoroethan	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
1,1,2-Trichloroethane	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
1,1-Dichloroethane	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
1,1-Dichloroethene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
1,1-Dichloropropene	U	0.53	5.3	C	µg/Kg-dry	1	8/31/2011 4:00:00 PM
1,2,3-Trichlorobenzene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
1,2,3-Trichloropropane	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
1,2,4,5-Tetramethylbenzene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
1,2,4-Trichlorobenzene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
1,2,4-Trimethylbenzene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
1,2-Dibromo-3-chloropropane	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
1,2-Dibromoethane	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
1,2-Dichlorobenzene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
1,2-Dichloroethane	U	0.53	5.3	C	µg/Kg-dry	1	8/31/2011 4:00:00 PM
1,2-Dichloropropane	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
1,3,5-Trimethylbenzene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
1,3-Dichlorobenzene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
1,3-dichloropropane	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
1,4-Dichlorobenzene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
1,4-Dioxane	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
2,2-Dichloropropane	U	0.53	5.3	C	µg/Kg-dry	1	8/31/2011 4:00:00 PM
2-Butanone	U	1.6	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
2-Chloroethyl vinyl ether	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
2-Chlorotoluene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
2-Hexanone	U	1.6	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
2-Propanol	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
4-Chlorotoluene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-2G (12 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:45:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-10A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: **LA**
4-Isopropyltoluene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
4-Methyl-2-pentanone	U	1.6	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Acetone	U	1.6	5.3	C	µg/Kg-dry	1	8/31/2011 4:00:00 PM
Acrolein	U	2.6	11	C	µg/Kg-dry	1	8/31/2011 4:00:00 PM
Acrylonitrile	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Benzene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Bromobenzene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Bromochloromethane	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Bromodichloromethane	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Bromoform	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Bromomethane	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Carbon disulfide	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Carbon tetrachloride	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Chlorobenzene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Chlorodifluoromethane	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Chloroethane	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Chloroform	U	0.53	5.3	C	µg/Kg-dry	1	8/31/2011 4:00:00 PM
Chloromethane	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
cis-1,2-Dichloroethene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
cis-1,3-Dichloropropene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Dibromochloromethane	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Dibromomethane	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Dichlorodifluoromethane	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Diisopropyl ether	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Ethanol	U	2.6	11		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Ethyl acetate	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Ethylbenzene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Freon-114	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Hexachlorobutadiene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Isopropyl acetate	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Isopropylbenzene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
m,p-Xylene	U	1.1	11		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Methyl Acetate	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-2G (12 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:45:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-10A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: **LA**
Methyl tert-butyl ether	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Methylene chloride	10	0.53	5.3	B	µg/Kg-dry	1	8/31/2011 4:00:00 PM
n-Amyl acetate	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Naphthalene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
n-Butyl acetate	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
n-Butylbenzene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
n-Propyl acetate	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
n-Propylbenzene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
o-Xylene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
p-Diethylbenzene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
p-Ethyltoluene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
sec-Butylbenzene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Styrene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
t-Butyl alcohol	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
tert-Butylbenzene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Tetrachloroethene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Toluene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
trans-1,2-Dichloroethene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
trans-1,3-Dichloropropene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Trichloroethene	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Trichlorofluoromethane	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Vinyl acetate	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Vinyl chloride	U	0.53	5.3		µg/Kg-dry	1	8/31/2011 4:00:00 PM
Surr: 4-Bromofluorobenzene	91.4	0	42-133		%REC	1	8/31/2011 4:00:00 PM
Surr: Dibromofluoromethane	96.3	0	50-133		%REC	1	8/31/2011 4:00:00 PM
Surr: Toluene-d8	98.1	0	53-130		%REC	1	8/31/2011 4:00:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-2C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:40:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-11A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
MERCURY			**SW7471B**		**SW7471B**		Analyst: **AB**
Mercury	0.457	0.005	0.0102		mg/Kg-dry	1	9/2/2011 11:08:53 AM
TOTAL DRO AS #2 FUEL (C8-C40)			**SW8015C**		**SW3550C**		Analyst: **LDS**
Total DRO TPH	52	2.90	12		mg/Kg-dry	1	9/1/2011 2:49:00 PM
Surr: o-Terphenyl	28.5	0	31-137	S	%REC	1	9/1/2011 2:49:00 PM
HERBICIDES SW-846 8151			**SW8151A**		**SW8151**		Analyst: **SB**
2,4,5-T	U	1.16	12		µg/Kg-dry	1	9/8/2011 2:16:00 AM
2,4,5-TP	U	1.16	12		µg/Kg-dry	1	9/8/2011 2:16:00 AM
2,4-D	U	1.16	12		µg/Kg-dry	1	9/8/2011 2:16:00 AM
Surr: 2,4-DCAA	80.9	0	14-148		%REC	1	9/8/2011 2:16:00 AM
PCB'S AS AROCLORS SW-846 METHOD 8082			**SW8082A**		**SW3550C**		Analyst: **SB**
Aroclor 1016	U	1.16	46		µg/Kg-dry	1	9/1/2011 7:39:00 PM
Aroclor 1221	U	1.16	46		µg/Kg-dry	1	9/1/2011 7:39:00 PM
Aroclor 1232	U	1.16	46		µg/Kg-dry	1	9/1/2011 7:39:00 PM
Aroclor 1242	U	1.16	46		µg/Kg-dry	1	9/1/2011 7:39:00 PM
Aroclor 1248	U	1.16	46		µg/Kg-dry	1	9/1/2011 7:39:00 PM
Aroclor 1254	U	1.16	46		µg/Kg-dry	1	9/1/2011 7:39:00 PM
Aroclor 1260	U	1.16	46		µg/Kg-dry	1	9/1/2011 7:39:00 PM
Aroclor 1262	U	1.16	46		µg/Kg-dry	1	9/1/2011 7:39:00 PM
Aroclor 1268	U	1.16	46		µg/Kg-dry	1	9/1/2011 7:39:00 PM
Surr: TCX	41.9	0	17-151		%REC	1	9/1/2011 7:39:00 PM
Surr: DCB	61.9	0	16-152		%REC	1	9/1/2011 7:39:00 PM
PESTICIDES SW-846 METHOD 8081			**SW8081B**		**SW3550C**		Analyst: **SB**
4,4'-DDD	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:52:00 PM
4,4'-DDE	0.62	0.23	2.3	JP	µg/Kg-dry	1	9/2/2011 1:52:00 PM
4,4'-DDT	1.3	0.23	2.3	J	µg/Kg-dry	1	9/2/2011 1:52:00 PM
Aldrin	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:52:00 PM
alpha-BHC	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:52:00 PM
beta-BHC	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:52:00 PM
Chlordane	3.5	1.16	2.3		µg/Kg-dry	1	9/2/2011 1:52:00 PM
Chlorobenzilate	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:52:00 PM
DBCP	12	0.23	2.3	P	µg/Kg-dry	1	9/2/2011 1:52:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-2C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:40:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-11A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PESTICIDES SW-846 METHOD 8081			**SW8081B**		**SW3550C**		Analyst: **SB**
delta-BHC	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:52:00 PM
Dieldrin	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:52:00 PM
Endosulfan I	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:52:00 PM
Endosulfan II	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:52:00 PM
Endosulfan sulfate	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:52:00 PM
Endrin	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:52:00 PM
Endrin aldehyde	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:52:00 PM
Endrin ketone	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:52:00 PM
gamma-BHC	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:52:00 PM
Heptachlor	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:52:00 PM
Heptachlor epoxide	0.31	0.23	2.3	JP	µg/Kg-dry	1	9/2/2011 1:52:00 PM
Hexachlorobenzene	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:52:00 PM
Hexachlorocyclopentadiene	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:52:00 PM
Methoxychlor	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 1:52:00 PM
Toxaphene	U	5.81	12		µg/Kg-dry	1	9/2/2011 1:52:00 PM
Surr: DCB	68.9	0	23-157		%REC	1	9/2/2011 1:52:00 PM
Surr: TCX	39.8	0	21-151		%REC	1	9/2/2011 1:52:00 PM
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	14.3	0	0		wt%	1	9/1/2011
TARGET ANALYTE LIST METALS			**SW6010C**		**SW3050B**		Analyst: **JP**
Aluminum	4240	0.11	0.454		mg/Kg-dry	1	9/2/2011 9:54:57 AM
Antimony	U	0.23	0.567		mg/Kg-dry	1	9/2/2011 9:54:57 AM
Arsenic	17.1	0.23	0.567		mg/Kg-dry	1	9/2/2011 9:54:57 AM
Barium	63.8	0.23	0.454		mg/Kg-dry	1	9/2/2011 9:54:57 AM
Beryllium	U	0.11	0.454		mg/Kg-dry	1	9/2/2011 9:54:57 AM
Cadmium	0.545	0.11	0.454		mg/Kg-dry	1	9/2/2011 9:54:57 AM
Calcium	6280	0.23	0.567		mg/Kg-dry	1	9/2/2011 9:54:57 AM
Chromium	12.8	0.11	0.454		mg/Kg-dry	1	9/2/2011 9:54:57 AM
Cobalt	U	0.11	0.454		mg/Kg-dry	1	9/2/2011 9:54:57 AM
Copper	20.5	0.11	0.454		mg/Kg-dry	1	9/2/2011 9:54:57 AM
Iron	9990	2.27	4.54		mg/Kg-dry	10	9/2/2011 12:33:13 PM
Lead	129	0.23	0.454		mg/Kg-dry	1	9/2/2011 9:54:57 AM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-2C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:40:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-11A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TARGET ANALYTE LIST METALS			**SW6010C**		**SW3050B**		Analyst: **JP**
Magnesium	1680	0.11	0.454		mg/Kg-dry	1	9/2/2011 9:54:57 AM
Manganese	213	0.11	0.454		mg/Kg-dry	1	9/2/2011 9:54:57 AM
Nickel	14.0	0.11	0.454		mg/Kg-dry	1	9/2/2011 9:54:57 AM
Potassium	1420	0.23	0.567		mg/Kg-dry	1	9/2/2011 9:54:57 AM
Selenium	1.57	0.23	0.567		mg/Kg-dry	1	9/2/2011 9:54:57 AM
Silver	0.113	0.11	0.454	J	mg/Kg-dry	1	9/2/2011 9:54:57 AM
Sodium	129	0.23	0.567		mg/Kg-dry	1	9/2/2011 9:54:57 AM
Thallium	U	0.34	0.567		mg/Kg-dry	1	9/2/2011 9:54:57 AM
Vanadium	15.4	0.11	0.454		mg/Kg-dry	1	9/2/2011 9:54:57 AM
Zinc	123	0.11	0.454		mg/Kg-dry	1	9/2/2011 9:54:57 AM
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
1,2,4-Trichlorobenzene	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
1,2-Dichlorobenzene	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
1,3-Dichlorobenzene	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
1,4-Dichlorobenzene	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
2,4,5-Trichlorophenol	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
2,4,6-Trichlorophenol	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
2,4-Dichlorophenol	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
2,4-Dimethylphenol	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
2,4-Dinitrophenol	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
2,4-Dinitrotoluene	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
2,6-Dinitrotoluene	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
2-Chloronaphthalene	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
2-Chlorophenol	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
2-Methylnaphthalene	38	29.0	290	J	µg/Kg-dry	1	9/1/2011 3:16:00 PM
2-Methylphenol	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
2-Nitroaniline	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
2-Nitrophenol	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
3,3´-Dichlorobenzidine	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
3+4-Methylphenol	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
3-Nitroaniline	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
4,6-Dinitro-2-methylphenol	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-2C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:40:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-11A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
4-Bromophenyl phenyl ether	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
4-Chloro-3-methylphenol	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
4-Chloroaniline	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
4-Chlorophenyl phenyl ether	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
4-Nitroaniline	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
4-Nitrophenol	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Acenaphthene	210	29.0	290	J	µg/Kg-dry	1	9/1/2011 3:16:00 PM
Acenaphthylene	69	29.0	290	J	µg/Kg-dry	1	9/1/2011 3:16:00 PM
Acetophenone	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Aniline	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Anthracene	520	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Atrazine	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Azobenzene	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Benzaldehyde	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Benzidine	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Benzo(a)anthracene	1400	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Benzo(a)pyrene	1000	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Benzo(b)fluoranthene	880	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Benzo(g,h,i)perylene	640	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Benzo(k)fluoranthene	870	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Benzoic acid	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Benzyl alcohol	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Biphenyl	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Bis(2-chloroethoxy)methane	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Bis(2-chloroethyl)ether	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Bis(2-chloroisopropyl)ether	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Bis(2-ethylhexyl)phthalate	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Butyl benzyl phthalate	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Caprolactam	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Carbazole	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Chrysene	1300	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Dibenzo(a,h)anthracene	190	29.0	290	J	µg/Kg-dry	1	9/1/2011 3:16:00 PM
Dibenzofuran	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-2C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:40:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-11A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
Diethyl phthalate	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Dimethyl phthalate	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Di-n-butyl phthalate	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Di-n-octyl phthalate	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Fluoranthene	2300	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Fluorene	180	29.0	290	J	µg/Kg-dry	1	9/1/2011 3:16:00 PM
Hexachlorobenzene	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Hexachlorobutadiene	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Hexachlorocyclopentadiene	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Hexachloroethane	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Indeno(1,2,3-c,d)pyrene	570	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Isophorone	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Naphthalene	69	29.0	290	J	µg/Kg-dry	1	9/1/2011 3:16:00 PM
Nitrobenzene	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
N-Nitrosodimethylamine	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
N-Nitrosodi-n-propylamine	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
N-Nitrosodiphenylamine	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Parathion	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Pentachlorophenol	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Phenanthrene	2700	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Phenol	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Pyrene	2900	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Pyridine	U	29.0	290		µg/Kg-dry	1	9/1/2011 3:16:00 PM
Surr: 2,4,6-Tribromophenol	53.2	0	21-119		%REC	1	9/1/2011 3:16:00 PM
Surr: 2-Fluorobiphenyl	73.5	0	21-117		%REC	1	9/1/2011 3:16:00 PM
Surr: 2-Fluorophenol	31.3	0	11-105		%REC	1	9/1/2011 3:16:00 PM
Surr: 4-Terphenyl-d14	84.9	0	21-132		%REC	1	9/1/2011 3:16:00 PM
Surr: Nitrobenzene-d5	56.4	0	18-116		%REC	1	9/1/2011 3:16:00 PM
Surr: Phenol-d6	27.6	0	12-110		%REC	1	9/1/2011 3:16:00 PM
CYANIDE, TOTAL			**SW9012A**		**SW9012A**		Analyst: **STP**
Cyanide, Total & Amenable: Auto Colorimetric	U	0.06	0.117		mg/Kg-dry	1	9/6/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-2C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:40:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-11A		

Certificate of Results

Analyses	Sample Result		LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
HEXAVALENT CHROMIUM				**SW7196A**				Analyst: **AB**
Chromium, Hexavalent		U	0.23	0.467		mg/Kg-dry	1	9/6/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-2C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:40:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-11B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP MERCURY			**SW1311/7471B**		**SW1311**		Analyst: **AB**
Mercury	U	0.0005	0.0200		mg/L	1	9/2/2011 10:22:33 AM
TCLP HERBICIDES SW-846 8151			**SW8151A**		**SW3510C**		Analyst: **SB**
2,4,5-TP	U	0.0002	0.0050		mg/L	1	9/7/2011 7:36:00 PM
2,4-D	U	0.0002	0.0050		mg/L	1	9/7/2011 7:36:00 PM
Surr: 2,4-DCAA	98.6	0	21-144		%REC	1	9/7/2011 7:36:00 PM
TCLP PESTICIDES SW-846 8081			**SW8081B**		**SW3510C**		Analyst: **SB**
Chlordane	0.00099	0.0005	0.0010	J	mg/L	1	9/7/2011 3:05:00 PM
Endrin	U	0.0002	0.0010		mg/L	1	9/7/2011 3:05:00 PM
gamma-BHC	U	0.0002	0.0010		mg/L	1	9/7/2011 3:05:00 PM
Heptachlor	U	0.0002	0.0010		mg/L	1	9/7/2011 3:05:00 PM
Heptachlor epoxide	U	0.0002	0.0010		mg/L	1	9/7/2011 3:05:00 PM
Methoxychlor	U	0.0002	0.0010		mg/L	1	9/7/2011 3:05:00 PM
Toxaphene	U	0.002	0.010		mg/L	1	9/7/2011 3:05:00 PM
Surr: DCB	93.0	0	28-146		%REC	1	9/7/2011 3:05:00 PM
Surr: TCX	91.6	0	25-147		%REC	1	9/7/2011 3:05:00 PM
TCLP METALS			**SW1311/6010C**		**SW1311**		Analyst: **JP**
Arsenic	0.0200	0.01	0.0500	J	mg/L	1	9/1/2011 3:26:20 PM
Barium	U	1	5.00		mg/L	1	9/1/2011 3:26:20 PM
Cadmium	U	0.005	0.0500		mg/L	1	9/1/2011 3:26:20 PM
Chromium	U	0.005	0.0500		mg/L	1	9/1/2011 3:26:20 PM
Lead	0.0220	0.005	0.0500	J	mg/L	1	9/1/2011 3:26:20 PM
Selenium	U	0.01	0.0500		mg/L	1	9/1/2011 3:26:20 PM
Silver	U	0.005	0.0500		mg/L	1	9/1/2011 3:26:20 PM
TCLP SEMIVOLATILES SW-846 8270			**SW8270D**		**SW3510C**		Analyst: **LDS**
2,4,5-Trichlorophenol	U	0.005	0.050		mg/L	1	9/6/2011 8:03:00 PM
2,4,6-Trichlorophenol	U	0.005	0.085		mg/L	1	9/6/2011 8:03:00 PM
2,4-Dinitrotoluene	U	0.005	0.045		mg/L	1	9/6/2011 8:03:00 PM
2-Methylphenol	U	0.005	0.035		mg/L	1	9/6/2011 8:03:00 PM
3+4-Methylphenol	U	0.005	0.040		mg/L	1	9/6/2011 8:03:00 PM
Hexachlorobenzene	U	0.005	0.090		mg/L	1	9/6/2011 8:03:00 PM
Hexachlorobutadiene	U	0.005	0.15		mg/L	1	9/6/2011 8:03:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.	

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-2C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:40:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-11B		

Certificate of Results

Analyses	Sample Result		LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP SEMIVOLATILES SW-846 8270				**SW8270D**		**SW3510C**		Analyst: **LDS**
Hexachloroethane	U		0.005	0.040		mg/L	1	9/6/2011 8:03:00 PM
Nitrobenzene	U		0.005	0.035		mg/L	1	9/6/2011 8:03:00 PM
Pentachlorophenol	U		0.05	0.17		mg/L	1	9/6/2011 8:03:00 PM
Pyridine	U		0.05	0.12		mg/L	1	9/6/2011 8:03:00 PM
Surr: 2,4,6-Tribromophenol	77.8		0	36-133		%REC	1	9/6/2011 8:03:00 PM
Surr: 2-Fluorobiphenyl	88.8		0	20-131		%REC	1	9/6/2011 8:03:00 PM
Surr: 2-Fluorophenol	80.4		0	22-128		%REC	1	9/6/2011 8:03:00 PM
Surr: 4-Terphenyl-d14	97.2		0	22-132		%REC	1	9/6/2011 8:03:00 PM
Surr: Nitrobenzene-d5	80.8		0	19-133		%REC	1	9/6/2011 8:03:00 PM
Surr: Phenol-d6	55.5		0	18-128		%REC	1	9/6/2011 8:03:00 PM
TCLP VOLATILES				**SW8260C**				Analyst: **LA**
1,1-Dichloroethene	U		0.01	0.020		mg/L	20	9/1/2011 12:52:00 PM
1,2-Dichloroethane	U		0.01	0.020		mg/L	20	9/1/2011 12:52:00 PM
1,4-Dichlorobenzene	U		0.01	0.020		mg/L	20	9/1/2011 12:52:00 PM
2-Butanone	U		0.02	0.040		mg/L	20	9/1/2011 12:52:00 PM
Benzene	U		0.01	0.020		mg/L	20	9/1/2011 12:52:00 PM
Carbon tetrachloride	U		0.01	0.020		mg/L	20	9/1/2011 12:52:00 PM
Chlorobenzene	U		0.01	0.020		mg/L	20	9/1/2011 12:52:00 PM
Chloroform	U		0.01	0.020		mg/L	20	9/1/2011 12:52:00 PM
Tetrachloroethene	U		0.01	0.020		mg/L	20	9/1/2011 12:52:00 PM
Trichloroethene	U		0.01	0.020		mg/L	20	9/1/2011 12:52:00 PM
Vinyl chloride	U		0.01	0.020		mg/L	20	9/1/2011 12:52:00 PM
Surr: 4-Bromofluorobenzene	106		0	63-123		%REC	20	9/1/2011 12:52:00 PM
Surr: Dibromofluoromethane	109		0	68-124		%REC	20	9/1/2011 12:52:00 PM
Surr: Toluene-d8	97.0		0	67-125		%REC	20	9/1/2011 12:52:00 PM
TRIVALENT CHROMIUM				**SW6010C**				Analyst: **JP**
Chromium, Trivalent	12.8		0.11	0.454		mg/Kg-dry	1	9/2/2011
IGNITABILITY/FLASHPOINT SW-846 1020				**SW1020B**				Analyst: **STP**
Ignitability	>		0	140		°F	1	9/1/2011
SOIL PH MEASURED IN WATER				**SW9045C**				Analyst: **AB**
pH	7.60		0	1.00	H	pH Units	1	9/1/2011 1:35:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-2C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:40:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-11B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TEMPERATURE			**M2550 B**				Analyst: **AB**
Temp at which pH was measured	21.0	0	0		°C	1	9/1/2011 1:35:00 PM
REACTIVE CYANIDE			**SW7.3.3.2**				Analyst: **STP**
Reactive Cyanide	U	0.06	0.117		mg/Kg-dry	1	9/8/2011
REACTIVE SULFIDE			**SW7.3.4.2**				Analyst: **STP**
Reactive Sulfide	U	1.17	2.33		mg/Kg-dry	1	9/8/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-2Ca (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:44:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-12A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TOTAL DRO AS #2 FUEL (C8-C40)			**SW8015C**		**SW3550C**		Analyst: **LDS**
Total DRO TPH	19	2.89	12		mg/Kg-dry	1	9/2/2011 3:28:00 PM
Surr: o-Terphenyl	37.7	0	31-137		%REC	1	9/2/2011 3:28:00 PM
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	15.7	0	0		wt%	1	9/1/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-3G (4 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:45:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-13A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PERCENT MOISTURE			D2216				Analyst: KK
Percent Moisture	12.7	0	0		wt%	1	9/1/2011
VOLATILE SW-846 METHOD 8260			SW8260C				Analyst: LA
1,1,1,2-Tetrachloroethane	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
1,1,1-Trichloroethane	U	0.72	7.2	C	µg/Kg-dry	1	8/31/2011 4:24:00 PM
1,1,2,2-Tetrachloroethane	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
1,1,2-Trichloro-1,2,2-trifluoroethan	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
1,1,2-Trichloroethane	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
1,1-Dichloroethane	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
1,1-Dichloroethene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
1,1-Dichloropropene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
1,2,3-Trichlorobenzene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
1,2,3-Trichloropropane	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
1,2,4,5-Tetramethylbenzene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
1,2,4-Trichlorobenzene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
1,2,4-Trimethylbenzene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
1,2-Dibromo-3-chloropropane	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
1,2-Dibromoethane	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
1,2-Dichlorobenzene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
1,2-Dichloroethane	U	0.72	7.2	C	µg/Kg-dry	1	8/31/2011 4:24:00 PM
1,2-Dichloropropane	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
1,3,5-Trimethylbenzene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
1,3-Dichlorobenzene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
1,3-dichloropropane	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
1,4-Dichlorobenzene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
1,4-Dioxane	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
2,2-Dichloropropane	U	0.72	7.2	C	µg/Kg-dry	1	8/31/2011 4:24:00 PM
2-Butanone	U	2.2	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
2-Chloroethyl vinyl ether	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
2-Chlorotoluene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
2-Hexanone	U	2.2	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
2-Propanol	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
4-Chlorotoluene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-3G (4 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:45:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-13A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: **LA**
4-Isopropyltoluene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
4-Methyl-2-pentanone	U	2.2	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Acetone	U	2.2	7.2	C	µg/Kg-dry	1	8/31/2011 4:24:00 PM
Acrolein	U	3.6	14	C	µg/Kg-dry	1	8/31/2011 4:24:00 PM
Acrylonitrile	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Benzene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Bromobenzene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Bromochloromethane	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Bromodichloromethane	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Bromoform	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Bromomethane	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Carbon disulfide	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Carbon tetrachloride	U	0.72	7.2	C	µg/Kg-dry	1	8/31/2011 4:24:00 PM
Chlorobenzene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Chlorodifluoromethane	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Chloroethane	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Chloroform	U	0.72	7.2	C	µg/Kg-dry	1	8/31/2011 4:24:00 PM
Chloromethane	U	0.72	7.2	C	µg/Kg-dry	1	8/31/2011 4:24:00 PM
cis-1,2-Dichloroethene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
cis-1,3-Dichloropropene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Dibromochloromethane	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Dibromomethane	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Dichlorodifluoromethane	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Diisopropyl ether	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Ethanol	U	3.6	14		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Ethyl acetate	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Ethylbenzene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Freon-114	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Hexachlorobutadiene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Isopropyl acetate	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Isopropylbenzene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
m,p-Xylene	U	1.4	14		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Methyl Acetate	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-3G (4 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:45:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-13A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: **LA**
Methyl tert-butyl ether	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Methylene chloride	15	0.72	7.2	B	µg/Kg-dry	1	8/31/2011 4:24:00 PM
n-Amyl acetate	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Naphthalene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
n-Butyl acetate	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
n-Butylbenzene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
n-Propyl acetate	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
n-Propylbenzene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
o-Xylene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
p-Diethylbenzene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
p-Ethyltoluene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
sec-Butylbenzene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Styrene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
t-Butyl alcohol	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
tert-Butylbenzene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Tetrachloroethene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Toluene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
trans-1,2-Dichloroethene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
trans-1,3-Dichloropropene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Trichloroethene	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Trichlorofluoromethane	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Vinyl acetate	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Vinyl chloride	U	0.72	7.2		µg/Kg-dry	1	8/31/2011 4:24:00 PM
Surr: 4-Bromofluorobenzene	92.0	0	42-133		%REC	1	8/31/2011 4:24:00 PM
Surr: Dibromofluoromethane	96.1	0	50-133		%REC	1	8/31/2011 4:24:00 PM
Surr: Toluene-d8	83.0	0	53-130		%REC	1	8/31/2011 4:24:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.	

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-3C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:40:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-14A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
MERCURY			**SW7471B**		**SW7471B**		Analyst: **AB**
Mercury	0.937	0.01	0.0231		mg/Kg-dry	2	9/2/2011 12:23:48 PM
TOTAL DRO AS #2 FUEL (C8-C40)			**SW8015C**		**SW3550C**		Analyst: **LDS**
Total DRO TPH	90	2.92	12		mg/Kg-dry	1	9/1/2011 3:14:00 PM
Surr: o-Terphenyl	32.7	0	31-137		%REC	1	9/1/2011 3:14:00 PM
HERBICIDES SW-846 8151			**SW8151A**		**SW8151**		Analyst: **SB**
2,4,5-T	3.8	1.17	12	J	µg/Kg-dry	1	9/8/2011 12:12:00 PM
2,4,5-TP	1.9	1.17	12	J	µg/Kg-dry	1	9/8/2011 12:12:00 PM
2,4-D	U	1.17	12		µg/Kg-dry	1	9/8/2011 12:12:00 PM
Surr: 2,4-DCAA	114	0	14-148		%REC	1	9/8/2011 12:12:00 PM
PCB'S AS AROCLORS SW-846 METHOD 8082			**SW8082A**		**SW3550C**		Analyst: **SB**
Aroclor 1016	U	1.17	47		µg/Kg-dry	1	9/1/2011 8:03:00 PM
Aroclor 1221	U	1.17	47		µg/Kg-dry	1	9/1/2011 8:03:00 PM
Aroclor 1232	U	1.17	47		µg/Kg-dry	1	9/1/2011 8:03:00 PM
Aroclor 1242	U	1.17	47		µg/Kg-dry	1	9/1/2011 8:03:00 PM
Aroclor 1248	U	1.17	47		µg/Kg-dry	1	9/1/2011 8:03:00 PM
Aroclor 1254	U	1.17	47		µg/Kg-dry	1	9/1/2011 8:03:00 PM
Aroclor 1260	U	1.17	47		µg/Kg-dry	1	9/1/2011 8:03:00 PM
Aroclor 1262	U	1.17	47		µg/Kg-dry	1	9/1/2011 8:03:00 PM
Aroclor 1268	U	1.17	47		µg/Kg-dry	1	9/1/2011 8:03:00 PM
Surr: TCX	36.3	0	17-151		%REC	1	9/1/2011 8:03:00 PM
Surr: DCB	55.5	0	16-152		%REC	1	9/1/2011 8:03:00 PM
PESTICIDES SW-846 METHOD 8081			**SW8081B**		**SW3550C**		Analyst: **SB**
4,4'-DDD	10	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:06:00 PM
4,4'-DDE	72	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:06:00 PM
4,4'-DDT	120	0.47	4.7		µg/Kg-dry	2	9/2/2011 6:51:00 PM
Aldrin	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:06:00 PM
alpha-BHC	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:06:00 PM
beta-BHC	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:06:00 PM
Chlordane	51	1.17	2.3		µg/Kg-dry	1	9/2/2011 2:06:00 PM
Chlorobenzilate	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:06:00 PM
DBCP	11	0.23	2.3	P	µg/Kg-dry	1	9/2/2011 2:06:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

ACCREDITED IN ACCORDANCE WITH nelac

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-3C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:40:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-14A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PESTICIDES SW-846 METHOD 8081			**SW8081B**		**SW3550C**		Analyst: **SB**
delta-BHC	3.2	0.23	2.3	P	µg/Kg-dry	1	9/2/2011 2:06:00 PM
Dieldrin	7.2	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:06:00 PM
Endosulfan I	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:06:00 PM
Endosulfan II	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:06:00 PM
Endosulfan sulfate	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:06:00 PM
Endrin	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:06:00 PM
Endrin aldehyde	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:06:00 PM
Endrin ketone	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:06:00 PM
gamma-BHC	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:06:00 PM
Heptachlor	0.68	0.23	2.3	JP	µg/Kg-dry	1	9/2/2011 2:06:00 PM
Heptachlor epoxide	1.7	0.23	2.3	J	µg/Kg-dry	1	9/2/2011 2:06:00 PM
Hexachlorobenzene	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:06:00 PM
Hexachlorocyclopentadiene	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:06:00 PM
Methoxychlor	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:06:00 PM
Toxaphene	U	5.84	12		µg/Kg-dry	1	9/2/2011 2:06:00 PM
Surr: DCB	56.9	0	23-157		%REC	2	9/2/2011 6:51:00 PM
Surr: DCB	61.0	0	23-157		%REC	1	9/2/2011 2:06:00 PM
Surr: TCX	35.9	0	21-151		%REC	2	9/2/2011 6:51:00 PM
Surr: TCX	36.7	0	21-151		%REC	1	9/2/2011 2:06:00 PM
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	15.1	0	0		wt%	1	9/1/2011
TARGET ANALYTE LIST METALS			**SW6010C**		**SW3050B**		Analyst: **JP**
Aluminum	3000	0.11	0.428		mg/Kg-dry	1	9/2/2011 9:57:01 AM
Antimony	U	0.21	0.536		mg/Kg-dry	1	9/2/2011 9:57:01 AM
Arsenic	7.52	0.21	0.536		mg/Kg-dry	1	9/2/2011 9:57:01 AM
Barium	393	0.21	0.428		mg/Kg-dry	1	9/2/2011 9:57:01 AM
Beryllium	U	0.11	0.428		mg/Kg-dry	1	9/2/2011 9:57:01 AM
Cadmium	0.857	0.11	0.428		mg/Kg-dry	1	9/2/2011 9:57:01 AM
Calcium	35200	2.14	5.36		mg/Kg-dry	10	9/2/2011 12:35:17 PM
Chromium	10.7	0.11	0.428		mg/Kg-dry	1	9/2/2011 9:57:01 AM
Cobalt	U	0.11	0.428		mg/Kg-dry	1	9/2/2011 9:57:01 AM
Copper	88.9	0.11	0.428		mg/Kg-dry	1	9/2/2011 9:57:01 AM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

ACCREDITED IN ACCORDANCE WITH nelac

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-3C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:40:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-14A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TARGET ANALYTE LIST METALS			**SW6010C**		**SW3050B**		Analyst: **JP**
Iron	22300	2.14	4.28		mg/Kg-dry	10	9/2/2011 12:35:17 PM
Lead	723	0.21	0.428		mg/Kg-dry	1	9/2/2011 9:57:01 AM
Magnesium	3010	0.11	0.428		mg/Kg-dry	1	9/2/2011 9:57:01 AM
Manganese	229	0.11	0.428		mg/Kg-dry	1	9/2/2011 9:57:01 AM
Nickel	9.00	0.11	0.428		mg/Kg-dry	1	9/2/2011 9:57:01 AM
Potassium	1310	0.21	0.536		mg/Kg-dry	1	9/2/2011 9:57:01 AM
Selenium	0.279	0.21	0.536	J	mg/Kg-dry	1	9/2/2011 9:57:01 AM
Silver	0.578	0.11	0.428		mg/Kg-dry	1	9/2/2011 9:57:01 AM
Sodium	647	0.21	0.536		mg/Kg-dry	1	9/2/2011 9:57:01 AM
Thallium	U	0.32	0.536		mg/Kg-dry	1	9/2/2011 9:57:01 AM
Vanadium	11.7	0.11	0.428		mg/Kg-dry	1	9/2/2011 9:57:01 AM
Zinc	395	0.11	0.428		mg/Kg-dry	1	9/2/2011 9:57:01 AM
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
1,2,4-Trichlorobenzene	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
1,2-Dichlorobenzene	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
1,3-Dichlorobenzene	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
1,4-Dichlorobenzene	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
2,4,5-Trichlorophenol	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
2,4,6-Trichlorophenol	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
2,4-Dichlorophenol	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
2,4-Dimethylphenol	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
2,4-Dinitrophenol	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
2,4-Dinitrotoluene	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
2,6-Dinitrotoluene	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
2-Chloronaphthalene	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
2-Chlorophenol	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
2-Methylnaphthalene	160	29.2	290	J	µg/Kg-dry	1	9/1/2011 3:41:00 PM
2-Methylphenol	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
2-Nitroaniline	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
2-Nitrophenol	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
3,3'-Dichlorobenzidine	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
3+4-Methylphenol	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.	

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-3C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:40:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-14A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
3-Nitroaniline	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
4,6-Dinitro-2-methylphenol	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
4-Bromophenyl phenyl ether	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
4-Chloro-3-methylphenol	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
4-Chloroaniline	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
4-Chlorophenyl phenyl ether	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
4-Nitroaniline	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
4-Nitrophenol	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Acenaphthene	440	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Acenaphthylene	210	29.2	290	J	µg/Kg-dry	1	9/1/2011 3:41:00 PM
Acetophenone	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Aniline	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Anthracene	9000	292	2900		µg/Kg-dry	10	9/2/2011 2:23:00 PM
Atrazine	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Azobenzene	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Benzaldehyde	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Benzidine	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Benzo(a)anthracene	4500	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Benzo(a)pyrene	3400	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Benzo(b)fluoranthene	3300	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Benzo(g,h,i)perylene	2300	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Benzo(k)fluoranthene	3100	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Benzoic acid	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Benzyl alcohol	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Biphenyl	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Bis(2-chloroethoxy)methane	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Bis(2-chloroethyl)ether	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Bis(2-chloroisopropyl)ether	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Bis(2-ethylhexyl)phthalate	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Butyl benzyl phthalate	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Caprolactam	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Carbazole	630	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Chrysene	4400	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-3C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:40:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-14A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
Dibenzo(a,h)anthracene	640	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Dibenzofuran	510	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Diethyl phthalate	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Dimethyl phthalate	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Di-n-butyl phthalate	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Di-n-octyl phthalate	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Fluoranthene	11000	292	2900		µg/Kg-dry	10	9/2/2011 2:23:00 PM
Fluorene	380	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Hexachlorobenzene	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Hexachlorobutadiene	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Hexachlorocyclopentadiene	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Hexachloroethane	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Indeno(1,2,3-c,d)pyrene	2100	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Isophorone	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Naphthalene	280	29.2	290	J	µg/Kg-dry	1	9/1/2011 3:41:00 PM
Nitrobenzene	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
N-Nitrosodimethylamine	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
N-Nitrosodi-n-propylamine	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
N-Nitrosodiphenylamine	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Parathion	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Pentachlorophenol	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Phenanthrene	9200	292	2900		µg/Kg-dry	10	9/2/2011 2:23:00 PM
Phenol	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Pyrene	9600	292	2900		µg/Kg-dry	10	9/2/2011 2:23:00 PM
Pyridine	U	29.2	290		µg/Kg-dry	1	9/1/2011 3:41:00 PM
Surr: 2,4,6-Tribromophenol	36.8	0	21-119		%REC	10	9/2/2011 2:23:00 PM
Surr: 2,4,6-Tribromophenol	42.2	0	21-119		%REC	1	9/1/2011 3:41:00 PM
Surr: 2-Fluorobiphenyl	56.5	0	21-117		%REC	10	9/2/2011 2:23:00 PM
Surr: 2-Fluorobiphenyl	55.0	0	21-117		%REC	1	9/1/2011 3:41:00 PM
Surr: 2-Fluorophenol	19.6	0	11-105		%REC	1	9/1/2011 3:41:00 PM
Surr: 2-Fluorophenol	16.6	0	11-105		%REC	10	9/2/2011 2:23:00 PM
Surr: 4-Terphenyl-d14	63.0	0	21-132		%REC	1	9/1/2011 3:41:00 PM
Surr: 4-Terphenyl-d14	61.7	0	21-132		%REC	10	9/2/2011 2:23:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-3C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:40:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-14A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
Surr: Nitrobenzene-d5	31.2	0	18-116		%REC	1	9/1/2011 3:41:00 PM
Surr: Nitrobenzene-d5	29.9	0	18-116		%REC	10	9/2/2011 2:23:00 PM
Surr: Phenol-d6	19.4	0	12-110		%REC	1	9/1/2011 3:41:00 PM
Surr: Phenol-d6	22.8	0	12-110		%REC	10	9/2/2011 2:23:00 PM
CYANIDE, TOTAL			**SW9012A**		**SW9012A**		Analyst: **STP**
Cyanide, Total & Amenable: Auto Colorimetric	0.973	0.06	0.118		mg/Kg-dry	1	9/6/2011
HEXAVALENT CHROMIUM			**SW7196A**				Analyst: **AB**
Chromium, Hexavalent	1.12	0.24	0.471		mg/Kg-dry	1	9/6/2011

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-3C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:40:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-14B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP MERCURY			**SW1311/7471B**		**SW1311**		Analyst: **AB**
Mercury	U	0.0005	0.0200		mg/L	1	9/2/2011 10:24:40 AM
TCLP HERBICIDES SW-846 8151			**SW8151A**		**SW3510C**		Analyst: **SB**
2,4,5-TP	U	0.0002	0.0050		mg/L	1	9/7/2011 7:50:00 PM
2,4-D	U	0.0002	0.0050		mg/L	1	9/7/2011 7:50:00 PM
Surr: 2,4-DCAA	114	0	21-144		%REC	1	9/7/2011 7:50:00 PM
TCLP PESTICIDES SW-846 8081			**SW8081B**		**SW3510C**		Analyst: **SB**
Chlordane	0.00074	0.0005	0.0010	J	mg/L	1	9/7/2011 3:19:00 PM
Endrin	U	0.0002	0.0010		mg/L	1	9/7/2011 3:19:00 PM
gamma-BHC	U	0.0002	0.0010		mg/L	1	9/7/2011 3:19:00 PM
Heptachlor	U	0.0002	0.0010		mg/L	1	9/7/2011 3:19:00 PM
Heptachlor epoxide	U	0.0002	0.0010		mg/L	1	9/7/2011 3:19:00 PM
Methoxychlor	U	0.0002	0.0010		mg/L	1	9/7/2011 3:19:00 PM
Toxaphene	U	0.002	0.010		mg/L	1	9/7/2011 3:19:00 PM
Surr: DCB	90.5	0	28-146		%REC	1	9/7/2011 3:19:00 PM
Surr: TCX	88.2	0	25-147		%REC	1	9/7/2011 3:19:00 PM
TCLP METALS			**SW1311/6010C**		**SW1311**		Analyst: **JP**
Arsenic	U	0.01	0.0500		mg/L	1	9/1/2011 3:28:23 PM
Barium	U	1	5.00		mg/L	1	9/1/2011 3:28:23 PM
Cadmium	U	0.005	0.0500		mg/L	1	9/1/2011 3:28:23 PM
Chromium	U	0.005	0.0500		mg/L	1	9/1/2011 3:28:23 PM
Lead	0.131	0.005	0.0500		mg/L	1	9/1/2011 3:28:23 PM
Selenium	U	0.01	0.0500		mg/L	1	9/1/2011 3:28:23 PM
Silver	U	0.005	0.0500		mg/L	1	9/1/2011 3:28:23 PM
TCLP SEMIVOLATILES SW-846 8270			**SW8270D**		**SW3510C**		Analyst: **LDS**
2,4,5-Trichlorophenol	U	0.005	0.050		mg/L	1	9/6/2011 8:28:00 PM
2,4,6-Trichlorophenol	U	0.005	0.085		mg/L	1	9/6/2011 8:28:00 PM
2,4-Dinitrotoluene	U	0.005	0.045		mg/L	1	9/6/2011 8:28:00 PM
2-Methylphenol	U	0.005	0.035		mg/L	1	9/6/2011 8:28:00 PM
3+4-Methylphenol	U	0.005	0.040		mg/L	1	9/6/2011 8:28:00 PM
Hexachlorobenzene	U	0.005	0.090		mg/L	1	9/6/2011 8:28:00 PM
Hexachlorobutadiene	U	0.005	0.15		mg/L	1	9/6/2011 8:28:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.	

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-3C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:40:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-14B		

Certificate of Results

Analyses	Sample Result		LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP SEMIVOLATILES SW-846 8270				**SW8270D**		**SW3510C**		Analyst: **LDS**
Hexachloroethane	U		0.005	0.040		mg/L	1	9/6/2011 8:28:00 PM
Nitrobenzene	U		0.005	0.035		mg/L	1	9/6/2011 8:28:00 PM
Pentachlorophenol	U		0.05	0.17		mg/L	1	9/6/2011 8:28:00 PM
Pyridine	U		0.05	0.12		mg/L	1	9/6/2011 8:28:00 PM
Surr: 2,4,6-Tribromophenol	72.5		0	36-133		%REC	1	9/6/2011 8:28:00 PM
Surr: 2-Fluorobiphenyl	92.3		0	20-131		%REC	1	9/6/2011 8:28:00 PM
Surr: 2-Fluorophenol	74.0		0	22-128		%REC	1	9/6/2011 8:28:00 PM
Surr: 4-Terphenyl-d14	93.6		0	22-132		%REC	1	9/6/2011 8:28:00 PM
Surr: Nitrobenzene-d5	82.0		0	19-133		%REC	1	9/6/2011 8:28:00 PM
Surr: Phenol-d6	55.2		0	18-128		%REC	1	9/6/2011 8:28:00 PM
TCLP VOLATILES				**SW8260C**				Analyst: **LA**
1,1-Dichloroethene	U		0.01	0.020		mg/L	20	9/1/2011 1:16:00 PM
1,2-Dichloroethane	U		0.01	0.020		mg/L	20	9/1/2011 1:16:00 PM
1,4-Dichlorobenzene	U		0.01	0.020		mg/L	20	9/1/2011 1:16:00 PM
2-Butanone	U		0.02	0.040		mg/L	20	9/1/2011 1:16:00 PM
Benzene	U		0.01	0.020		mg/L	20	9/1/2011 1:16:00 PM
Carbon tetrachloride	U		0.01	0.020		mg/L	20	9/1/2011 1:16:00 PM
Chlorobenzene	U		0.01	0.020		mg/L	20	9/1/2011 1:16:00 PM
Chloroform	U		0.01	0.020		mg/L	20	9/1/2011 1:16:00 PM
Tetrachloroethene	U		0.01	0.020		mg/L	20	9/1/2011 1:16:00 PM
Trichloroethene	U		0.01	0.020		mg/L	20	9/1/2011 1:16:00 PM
Vinyl chloride	U		0.01	0.020		mg/L	20	9/1/2011 1:16:00 PM
Surr: 4-Bromofluorobenzene	97.4		0	63-123		%REC	20	9/1/2011 1:16:00 PM
Surr: Dibromofluoromethane	105		0	68-124		%REC	20	9/1/2011 1:16:00 PM
Surr: Toluene-d8	96.2		0	67-125		%REC	20	9/1/2011 1:16:00 PM
TRIVALENT CHROMIUM				**SW6010C**				Analyst: **JP**
Chromium, Trivalent	9.61		0.11	0.428		mg/Kg-dry	1	9/2/2011
IGNITABILITY/FLASHPOINT SW-846 1020				**SW1020B**				Analyst: **STP**
Ignitability	>		0	140		°F	1	9/1/2011
SOIL PH MEASURED IN WATER				**SW9045C**				Analyst: **AB**
pH	7.80		0	1.00	H	pH Units	1	9/1/2011 1:37:00 AM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-3C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:40:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-14B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TEMPERATURE			**M2550 B**				Analyst: **AB**
Temp at which pH was measured	21.0	0	0		°C	1	9/1/2011 1:37:00 AM
REACTIVE CYANIDE			**SW7.3.3.2**				Analyst: **STP**
Reactive Cyanide	U	0.06	0.118		mg/Kg-dry	1	9/8/2011
REACTIVE SULFIDE			**SW7.3.4.2**				Analyst: **STP**
Reactive Sulfide	U	1.18	2.36		mg/Kg-dry	1	9/8/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-3Ca (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:42:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-15A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TOTAL DRO AS #2 FUEL (C8-C40)			**SW8015C**	**SW3550C**			Analyst: **LDS**
Total DRO TPH	55	2.81	11		mg/Kg-dry	1	9/2/2011 3:53:00 PM
Surr: o-Terphenyl	37.6	0	31-137		%REC	1	9/2/2011 3:53:00 PM
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	14.4	0	0		wt%	1	9/1/2011

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-3G (12 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 12:00:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-16A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PERCENT MOISTURE			D2216				Analyst: KK
Percent Moisture	14.6	0	0		wt%	1	9/1/2011
VOLATILE SW-846 METHOD 8260			SW8260C				Analyst: LA
1,1,1,2-Tetrachloroethane	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
1,1,1-Trichloroethane	U	0.68	6.8	C	µg/Kg-dry	1	8/31/2011 4:47:00 PM
1,1,2,2-Tetrachloroethane	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
1,1,2-Trichloro-1,2,2-trifluoroethan	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
1,1,2-Trichloroethane	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
1,1-Dichloroethane	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
1,1-Dichloroethene	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
1,1-Dichloropropene	U	0.68	6.8	C	µg/Kg-dry	1	8/31/2011 4:47:00 PM
1,2,3-Trichlorobenzene	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
1,2,3-Trichloropropane	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
1,2,4,5-Tetramethylbenzene	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
1,2,4-Trichlorobenzene	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
1,2,4-Trimethylbenzene	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
1,2-Dibromo-3-chloropropane	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
1,2-Dibromoethane	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
1,2-Dichlorobenzene	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
1,2-Dichloroethane	U	0.68	6.8	C	µg/Kg-dry	1	8/31/2011 4:47:00 PM
1,2-Dichloropropane	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
1,3,5-Trimethylbenzene	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
1,3-Dichlorobenzene	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
1,3-dichloropropane	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
1,4-Dichlorobenzene	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
1,4-Dioxane	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
2,2-Dichloropropane	U	0.68	6.8	C	µg/Kg-dry	1	8/31/2011 4:47:00 PM
2-Butanone	U	2	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
2-Chloroethyl vinyl ether	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
2-Chlorotoluene	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
2-Hexanone	U	2	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
2-Propanol	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
4-Chlorotoluene	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-3G (12 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 12:00:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-16A		

Certificate of Results

Analyses	Sample Result		LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
VOLATILE SW-846 METHOD 8260				**SW8260C**				Analyst: **LA**
4-Isopropyltoluene	U		0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
4-Methyl-2-pentanone	U		2	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Acetone	U		2	6.8	C	µg/Kg-dry	1	8/31/2011 4:47:00 PM
Acrolein	U		3.4	14	C	µg/Kg-dry	1	8/31/2011 4:47:00 PM
Acrylonitrile	U		0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Benzene	U		0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Bromobenzene	U		0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Bromochloromethane	U		0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Bromodichloromethane	U		0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Bromoform	U		0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Bromomethane	U		0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Carbon disulfide	U		0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Carbon tetrachloride	U		0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Chlorobenzene	U		0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Chlorodifluoromethane	U		0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Chloroethane	U		0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Chloroform	U		0.68	6.8	C	µg/Kg-dry	1	8/31/2011 4:47:00 PM
Chloromethane	U		0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
cis-1,2-Dichloroethene	U		0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
cis-1,3-Dichloropropene	U		0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Dibromochloromethane	U		0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Dibromomethane	U		0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Dichlorodifluoromethane	U		0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Diisopropyl ether	U		0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Ethanol	U		3.4	14		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Ethyl acetate	U		0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Ethylbenzene	U		0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Freon-114	U		0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Hexachlorobutadiene	U		0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Isopropyl acetate	U		0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Isopropylbenzene	U		0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
m,p-Xylene	U		1.4	14		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Methyl Acetate	U		0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.	

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-3G (12 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 12:00:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-16A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: **LA**
Methyl tert-butyl ether	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Methylene chloride	14	0.68	6.8	B	µg/Kg-dry	1	8/31/2011 4:47:00 PM
n-Amyl acetate	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Naphthalene	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
n-Butyl acetate	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
n-Butylbenzene	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
n-Propyl acetate	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
n-Propylbenzene	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
o-Xylene	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
p-Diethylbenzene	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
p-Ethyltoluene	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
sec-Butylbenzene	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Styrene	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
t-Butyl alcohol	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
tert-Butylbenzene	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Tetrachloroethene	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Toluene	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
trans-1,2-Dichloroethene	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
trans-1,3-Dichloropropene	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Trichloroethene	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Trichlorofluoromethane	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Vinyl acetate	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Vinyl chloride	U	0.68	6.8		µg/Kg-dry	1	8/31/2011 4:47:00 PM
Surr: 4-Bromofluorobenzene	92.7	0	42-133		%REC	1	8/31/2011 4:47:00 PM
Surr: Dibromofluoromethane	97.8	0	50-133		%REC	1	8/31/2011 4:47:00 PM
Surr: Toluene-d8	101	0	53-130		%REC	1	8/31/2011 4:47:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-3C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:50:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-17A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
MERCURY			**SW7471B**		**SW7471B**		Analyst: **AB**
Mercury	0.216	0.005	0.00967		mg/Kg-dry	1	9/2/2011 11:14:17 AM
TOTAL DRO AS #2 FUEL (C8-C40)			**SW8015C**		**SW3550C**		Analyst: **LDS**
Total DRO TPH	42	2.84	11		mg/Kg-dry	1	9/1/2011 3:39:00 PM
Surr: o-Terphenyl	32.3	0	31-137		%REC	1	9/1/2011 3:39:00 PM
HERBICIDES SW-846 8151			**SW8151A**		**SW8151**		Analyst: **SB**
2,4,5-T	U	1.12	11		µg/Kg-dry	1	9/8/2011 12:26:00 PM
2,4,5-TP	U	1.12	11		µg/Kg-dry	1	9/8/2011 12:26:00 PM
2,4-D	U	1.12	11		µg/Kg-dry	1	9/8/2011 12:26:00 PM
Surr: 2,4-DCAA	54.8	0	14-148		%REC	1	9/8/2011 12:26:00 PM
PCB'S AS AROCLORS SW-846 METHOD 8082			**SW8082A**		**SW3550C**		Analyst: **SB**
Aroclor 1016	U	1.13	45		µg/Kg-dry	1	9/1/2011 8:27:00 PM
Aroclor 1221	U	1.13	45		µg/Kg-dry	1	9/1/2011 8:27:00 PM
Aroclor 1232	U	1.13	45		µg/Kg-dry	1	9/1/2011 8:27:00 PM
Aroclor 1242	U	1.13	45		µg/Kg-dry	1	9/1/2011 8:27:00 PM
Aroclor 1248	U	1.13	45		µg/Kg-dry	1	9/1/2011 8:27:00 PM
Aroclor 1254	U	1.13	45		µg/Kg-dry	1	9/1/2011 8:27:00 PM
Aroclor 1260	U	1.13	45		µg/Kg-dry	1	9/1/2011 8:27:00 PM
Aroclor 1262	U	1.13	45		µg/Kg-dry	1	9/1/2011 8:27:00 PM
Aroclor 1268	U	1.13	45		µg/Kg-dry	1	9/1/2011 8:27:00 PM
Surr: TCX	53.6	0	17-151		%REC	1	9/1/2011 8:27:00 PM
Surr: DCB	68.1	0	16-152		%REC	1	9/1/2011 8:27:00 PM
PESTICIDES SW-846 METHOD 8081			**SW8081B**		**SW3550C**		Analyst: **SB**
4,4'-DDD	1.5	0.23	2.3	J	µg/Kg-dry	1	9/2/2011 2:20:00 PM
4,4'-DDE	10	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:20:00 PM
4,4'-DDT	17	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:20:00 PM
Aldrin	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:20:00 PM
alpha-BHC	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:20:00 PM
beta-BHC	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:20:00 PM
Chlordane	11	1.13	2.3		µg/Kg-dry	1	9/2/2011 2:20:00 PM
Chlorobenzilate	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:20:00 PM
DBCP	22	0.23	2.3	P	µg/Kg-dry	1	9/2/2011 2:20:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.	

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-3C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:50:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-17A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PESTICIDES SW-846 METHOD 8081			**SW8081B**		**SW3550C**		Analyst: **SB**
delta-BHC	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:20:00 PM
Dieldrin	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:20:00 PM
Endosulfan I	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:20:00 PM
Endosulfan II	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:20:00 PM
Endosulfan sulfate	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:20:00 PM
Endrin	0.25	0.23	2.3	JP	µg/Kg-dry	1	9/2/2011 2:20:00 PM
Endrin aldehyde	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:20:00 PM
Endrin ketone	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:20:00 PM
gamma-BHC	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:20:00 PM
Heptachlor	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:20:00 PM
Heptachlor epoxide	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:20:00 PM
Hexachlorobenzene	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:20:00 PM
Hexachlorocyclopentadiene	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:20:00 PM
Methoxychlor	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:20:00 PM
Toxaphene	U	5.67	11		µg/Kg-dry	1	9/2/2011 2:20:00 PM
Surr: DCB	71.0	0	23-157		%REC	1	9/2/2011 2:20:00 PM
Surr: TCX	47.4	0	21-151		%REC	1	9/2/2011 2:20:00 PM
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	12.4	0	0		wt%	1	9/1/2011
TARGET ANALYTE LIST METALS			**SW6010C**		**SW3050B**		Analyst: **JP**
Aluminum	3930	0.10	0.406		mg/Kg-dry	1	9/2/2011 9:59:05 AM
Antimony	U	0.20	0.508		mg/Kg-dry	1	9/2/2011 9:59:05 AM
Arsenic	3.59	0.20	0.508		mg/Kg-dry	1	9/2/2011 9:59:05 AM
Barium	212	0.20	0.406		mg/Kg-dry	1	9/2/2011 9:59:05 AM
Beryllium	U	0.10	0.406		mg/Kg-dry	1	9/2/2011 9:59:05 AM
Cadmium	0.183	0.10	0.406	J	mg/Kg-dry	1	9/2/2011 9:59:05 AM
Calcium	28600	2.03	5.08		mg/Kg-dry	10	9/2/2011 12:37:20 PM
Chromium	12.9	0.10	0.406		mg/Kg-dry	1	9/2/2011 9:59:05 AM
Cobalt	U	0.10	0.406		mg/Kg-dry	1	9/2/2011 9:59:05 AM
Copper	24.6	0.10	0.406		mg/Kg-dry	1	9/2/2011 9:59:05 AM
Iron	12400	2.03	4.06		mg/Kg-dry	10	9/2/2011 12:37:20 PM
Lead	332	0.20	0.406		mg/Kg-dry	1	9/2/2011 9:59:05 AM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-3C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:50:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-17A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TARGET ANALYTE LIST METALS			**SW6010C**		**SW3050B**		Analyst: **JP**
Magnesium	2320	0.10	0.406		mg/Kg-dry	1	9/2/2011 9:59:05 AM
Manganese	206	0.10	0.406		mg/Kg-dry	1	9/2/2011 9:59:05 AM
Nickel	10.2	0.10	0.406		mg/Kg-dry	1	9/2/2011 9:59:05 AM
Potassium	1240	0.20	0.508		mg/Kg-dry	1	9/2/2011 9:59:05 AM
Selenium	U	0.20	0.508		mg/Kg-dry	1	9/2/2011 9:59:05 AM
Silver	0.122	0.10	0.406	J	mg/Kg-dry	1	9/2/2011 9:59:05 AM
Sodium	311	0.20	0.508		mg/Kg-dry	1	9/2/2011 9:59:05 AM
Thallium	U	0.30	0.508		mg/Kg-dry	1	9/2/2011 9:59:05 AM
Vanadium	13.2	0.10	0.406		mg/Kg-dry	1	9/2/2011 9:59:05 AM
Zinc	127	0.10	0.406		mg/Kg-dry	1	9/2/2011 9:59:05 AM
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
1,2,4-Trichlorobenzene	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
1,2-Dichlorobenzene	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
1,3-Dichlorobenzene	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
1,4-Dichlorobenzene	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
2,4,5-Trichlorophenol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
2,4,6-Trichlorophenol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
2,4-Dichlorophenol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
2,4-Dimethylphenol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
2,4-Dinitrophenol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
2,4-Dinitrotoluene	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
2,6-Dinitrotoluene	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
2-Chloronaphthalene	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
2-Chlorophenol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
2-Methylnaphthalene	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
2-Methylphenol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
2-Nitroaniline	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
2-Nitrophenol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
3,3´-Dichlorobenzidine	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
3+4-Methylphenol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
3-Nitroaniline	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
4,6-Dinitro-2-methylphenol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-3C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:50:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-17A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
4-Bromophenyl phenyl ether	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
4-Chloro-3-methylphenol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
4-Chloroaniline	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
4-Chlorophenyl phenyl ether	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
4-Nitroaniline	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
4-Nitrophenol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Acenaphthene	45	28.4	280	J	µg/Kg-dry	1	9/1/2011 4:07:00 PM
Acenaphthylene	72	28.4	280	J	µg/Kg-dry	1	9/1/2011 4:07:00 PM
Acetophenone	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Aniline	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Anthracene	1500	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Atrazine	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Azobenzene	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Benzaldehyde	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Benzidine	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Benzo(a)anthracene	1100	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Benzo(a)pyrene	890	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Benzo(b)fluoranthene	910	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Benzo(g,h,i)perylene	640	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Benzo(k)fluoranthene	860	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Benzoic acid	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Benzyl alcohol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Biphenyl	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Bis(2-chloroethoxy)methane	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Bis(2-chloroethyl)ether	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Bis(2-chloroisopropyl)ether	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Bis(2-ethylhexyl)phthalate	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Butyl benzyl phthalate	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Caprolactam	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Carbazole	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Chrysene	1100	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Dibenzo(a,h)anthracene	190	28.4	280	J	µg/Kg-dry	1	9/1/2011 4:07:00 PM
Dibenzofuran	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-3C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:50:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-17A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
Diethyl phthalate	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Dimethyl phthalate	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Di-n-butyl phthalate	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Di-n-octyl phthalate	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Fluoranthene	2100	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Fluorene	40	28.4	280	J	µg/Kg-dry	1	9/1/2011 4:07:00 PM
Hexachlorobenzene	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Hexachlorobutadiene	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Hexachlorocyclopentadiene	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Hexachloroethane	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Indeno(1,2,3-c,d)pyrene	580	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Isophorone	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Naphthalene	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Nitrobenzene	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
N-Nitrosodimethylamine	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
N-Nitrosodi-n-propylamine	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
N-Nitrosodiphenylamine	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Parathion	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Pentachlorophenol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Phenanthrene	1500	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Phenol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Pyrene	2200	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Pyridine	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:07:00 PM
Surr: 2,4,6-Tribromophenol	57.7	0	21-119		%REC	1	9/1/2011 4:07:00 PM
Surr: 2-Fluorobiphenyl	81.9	0	21-117		%REC	1	9/1/2011 4:07:00 PM
Surr: 2-Fluorophenol	32.0	0	11-105		%REC	1	9/1/2011 4:07:00 PM
Surr: 4-Terphenyl-d14	86.3	0	21-132		%REC	1	9/1/2011 4:07:00 PM
Surr: Nitrobenzene-d5	56.6	0	18-116		%REC	1	9/1/2011 4:07:00 PM
Surr: Phenol-d6	31.8	0	12-110		%REC	1	9/1/2011 4:07:00 PM
CYANIDE, TOTAL			**SW9012A**		**SW9012A**		Analyst: **STP**
Cyanide, Total & Amenable: Auto Colorimetric	0.280	0.06	0.114		mg/Kg-dry	1	9/6/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-3C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:50:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-17A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
HEXAVALENT CHROMIUM			**SW7196A**				Analyst: **AB**
Chromium, Hexavalent	U	0.23	0.457		mg/Kg-dry	1	9/6/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-3C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:50:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-17B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP MERCURY			**SW1311/7471B**		**SW1311**		Analyst: **AB**
Mercury	U	0.0005	0.0200		mg/L	1	9/2/2011 10:26:47 AM
TCLP HERBICIDES SW-846 8151			**SW8151A**		**SW3510C**		Analyst: **SB**
2,4,5-TP	U	0.0002	0.0050		mg/L	1	9/7/2011 8:05:00 PM
2,4-D	U	0.0002	0.0050		mg/L	1	9/7/2011 8:05:00 PM
Surr: 2,4-DCAA	110	0	21-144		%REC	1	9/7/2011 8:05:00 PM
TCLP PESTICIDES SW-846 8081			**SW8081B**		**SW3510C**		Analyst: **SB**
Chlordane	0.0032	0.0005	0.0010	P	mg/L	1	9/7/2011 3:34:00 PM
Endrin	U	0.0002	0.0010		mg/L	1	9/7/2011 3:34:00 PM
gamma-BHC	U	0.0002	0.0010		mg/L	1	9/7/2011 3:34:00 PM
Heptachlor	U	0.0002	0.0010		mg/L	1	9/7/2011 3:34:00 PM
Heptachlor epoxide	U	0.0002	0.0010		mg/L	1	9/7/2011 3:34:00 PM
Methoxychlor	U	0.0002	0.0010		mg/L	1	9/7/2011 3:34:00 PM
Toxaphene	U	0.002	0.010		mg/L	1	9/7/2011 3:34:00 PM
Surr: DCB	92.3	0	28-146		%REC	1	9/7/2011 3:34:00 PM
Surr: TCX	92.2	0	25-147		%REC	1	9/7/2011 3:34:00 PM
TCLP METALS			**SW1311/6010C**		**SW1311**		Analyst: **JP**
Arsenic	U	0.01	0.0500		mg/L	1	9/1/2011 3:30:27 PM
Barium	U	1	5.00		mg/L	1	9/1/2011 3:30:27 PM
Cadmium	U	0.005	0.0500		mg/L	1	9/1/2011 3:30:27 PM
Chromium	0.00500	0.005	0.0500	J	mg/L	1	9/1/2011 3:30:27 PM
Lead	0.0870	0.005	0.0500		mg/L	1	9/1/2011 3:30:27 PM
Selenium	U	0.01	0.0500		mg/L	1	9/1/2011 3:30:27 PM
Silver	U	0.005	0.0500		mg/L	1	9/1/2011 3:30:27 PM
TCLP SEMIVOLATILES SW-846 8270			**SW8270D**		**SW3510C**		Analyst: **LDS**
2,4,5-Trichlorophenol	U	0.005	0.050		mg/L	1	9/6/2011 8:53:00 PM
2,4,6-Trichlorophenol	U	0.005	0.085		mg/L	1	9/6/2011 8:53:00 PM
2,4-Dinitrotoluene	U	0.005	0.045		mg/L	1	9/6/2011 8:53:00 PM
2-Methylphenol	U	0.005	0.035		mg/L	1	9/6/2011 8:53:00 PM
3+4-Methylphenol	U	0.005	0.040		mg/L	1	9/6/2011 8:53:00 PM
Hexachlorobenzene	U	0.005	0.090		mg/L	1	9/6/2011 8:53:00 PM
Hexachlorobutadiene	U	0.005	0.15		mg/L	1	9/6/2011 8:53:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.	

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-3C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:50:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-17B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP SEMIVOLATILES SW-846 8270			**SW8270D**		**SW3510C**		Analyst: **LDS**
Hexachloroethane	U	0.005	0.040		mg/L	1	9/6/2011 8:53:00 PM
Nitrobenzene	U	0.005	0.035		mg/L	1	9/6/2011 8:53:00 PM
Pentachlorophenol	U	0.05	0.17		mg/L	1	9/6/2011 8:53:00 PM
Pyridine	U	0.05	0.12		mg/L	1	9/6/2011 8:53:00 PM
Surr: 2,4,6-Tribromophenol	68.3	0	36-133		%REC	1	9/6/2011 8:53:00 PM
Surr: 2-Fluorobiphenyl	93.1	0	20-131		%REC	1	9/6/2011 8:53:00 PM
Surr: 2-Fluorophenol	86.3	0	22-128		%REC	1	9/6/2011 8:53:00 PM
Surr: 4-Terphenyl-d14	101	0	22-132		%REC	1	9/6/2011 8:53:00 PM
Surr: Nitrobenzene-d5	78.5	0	19-133		%REC	1	9/6/2011 8:53:00 PM
Surr: Phenol-d6	60.5	0	18-128		%REC	1	9/6/2011 8:53:00 PM
TCLP VOLATILES			**SW8260C**				Analyst: **LA**
1,1-Dichloroethene	U	0.01	0.020		mg/L	20	9/1/2011 1:39:00 PM
1,2-Dichloroethane	U	0.01	0.020		mg/L	20	9/1/2011 1:39:00 PM
1,4-Dichlorobenzene	U	0.01	0.020		mg/L	20	9/1/2011 1:39:00 PM
2-Butanone	U	0.02	0.040		mg/L	20	9/1/2011 1:39:00 PM
Benzene	U	0.01	0.020		mg/L	20	9/1/2011 1:39:00 PM
Carbon tetrachloride	U	0.01	0.020		mg/L	20	9/1/2011 1:39:00 PM
Chlorobenzene	U	0.01	0.020		mg/L	20	9/1/2011 1:39:00 PM
Chloroform	U	0.01	0.020		mg/L	20	9/1/2011 1:39:00 PM
Tetrachloroethene	U	0.01	0.020		mg/L	20	9/1/2011 1:39:00 PM
Trichloroethene	U	0.01	0.020		mg/L	20	9/1/2011 1:39:00 PM
Vinyl chloride	U	0.01	0.020		mg/L	20	9/1/2011 1:39:00 PM
Surr: 4-Bromofluorobenzene	97.1	0	63-123		%REC	20	9/1/2011 1:39:00 PM
Surr: Dibromofluoromethane	108	0	68-124		%REC	20	9/1/2011 1:39:00 PM
Surr: Toluene-d8	97.5	0	67-125		%REC	20	9/1/2011 1:39:00 PM
TRIVALENT CHROMIUM			**SW6010C**				Analyst: **JP**
Chromium, Trivalent	12.9	0.10	0.406		mg/Kg-dry	1	9/2/2011
IGNITABILITY/FLASHPOINT SW-846 1020			**SW1020B**				Analyst: **STP**
Ignitability	>	0	140		°F	1	9/1/2011
SOIL PH MEASURED IN WATER			**SW9045C**				Analyst: **AB**
pH	8.00	0	1.00	H	pH Units	1	9/1/2011 1:39:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-3C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:50:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-17B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TEMPERATURE			**M2550 B**				Analyst: **AB**
Temp at which pH was measured	21.0	0	0		°C	1	9/1/2011 1:39:00 PM
REACTIVE CYANIDE			**SW7.3.3.2**				Analyst: **STP**
Reactive Cyanide	U	0.06	0.114		mg/Kg-dry	1	9/8/2011
REACTIVE SULFIDE			**SW7.3.4.2**				Analyst: **STP**
Reactive Sulfide	U	1.14	2.28		mg/Kg-dry	1	9/8/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-3Ca (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 11:55:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-18A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TOTAL DRO AS #2 FUEL (C8-C40)			**SW8015C**		**SW3550C**		Analyst: **LDS**
Total DRO TPH	48	2.81	11		mg/Kg-dry	1	9/2/2011 4:19:00 PM
Surr: o-Terphenyl	36.2	0	31-137		%REC	1	9/2/2011 4:19:00 PM
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	12.8	0	0		wt%	1	9/1/2011

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-4G (4 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 12:15:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-19A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	12.6	0	0		wt%	1	9/1/2011
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: **LA**
1,1,1,2-Tetrachloroethane	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
1,1,1-Trichloroethane	U	0.6	6.0	C	µg/Kg-dry	1	8/31/2011 5:12:00 PM
1,1,2,2-Tetrachloroethane	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
1,1,2-Trichloro-1,2,2-trifluoroethan	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
1,1,2-Trichloroethane	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
1,1-Dichloroethane	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
1,1-Dichloroethene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
1,1-Dichloropropene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
1,2,3-Trichlorobenzene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
1,2,3-Trichloropropane	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
1,2,4,5-Tetramethylbenzene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
1,2,4-Trichlorobenzene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
1,2,4-Trimethylbenzene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
1,2-Dibromo-3-chloropropane	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
1,2-Dibromoethane	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
1,2-Dichlorobenzene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
1,2-Dichloroethane	U	0.6	6.0	C	µg/Kg-dry	1	8/31/2011 5:12:00 PM
1,2-Dichloropropane	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
1,3,5-Trimethylbenzene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
1,3-Dichlorobenzene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
1,3-dichloropropane	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
1,4-Dichlorobenzene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
1,4-Dioxane	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
2,2-Dichloropropane	U	0.6	6.0	C	µg/Kg-dry	1	8/31/2011 5:12:00 PM
2-Butanone	U	1.8	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
2-Chloroethyl vinyl ether	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
2-Chlorotoluene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
2-Hexanone	U	1.8	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
2-Propanol	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
4-Chlorotoluene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-4G (4 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 12:15:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-19A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: **LA**
4-Isopropyltoluene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
4-Methyl-2-pentanone	U	1.8	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Acetone	U	1.8	6.0	C	µg/Kg-dry	1	8/31/2011 5:12:00 PM
Acrolein	U	3	12	C	µg/Kg-dry	1	8/31/2011 5:12:00 PM
Acrylonitrile	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Benzene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Bromobenzene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Bromochloromethane	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Bromodichloromethane	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Bromoform	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Bromomethane	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Carbon disulfide	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Carbon tetrachloride	U	0.6	6.0	C	µg/Kg-dry	1	8/31/2011 5:12:00 PM
Chlorobenzene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Chlorodifluoromethane	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Chloroethane	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Chloroform	U	0.6	6.0	C	µg/Kg-dry	1	8/31/2011 5:12:00 PM
Chloromethane	U	0.6	6.0	C	µg/Kg-dry	1	8/31/2011 5:12:00 PM
cis-1,2-Dichloroethene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
cis-1,3-Dichloropropene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Dibromochloromethane	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Dibromomethane	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Dichlorodifluoromethane	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Diisopropyl ether	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Ethanol	U	3	12		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Ethyl acetate	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Ethylbenzene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Freon-114	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Hexachlorobutadiene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Isopropyl acetate	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Isopropylbenzene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
m,p-Xylene	U	1.2	12		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Methyl Acetate	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

ACCREDITED IN ACCORDANCE WITH nelac

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-4G (4 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 12:15:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-19A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: LA
Methyl tert-butyl ether	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Methylene chloride	13	0.6	6.0	B	µg/Kg-dry	1	8/31/2011 5:12:00 PM
n-Amyl acetate	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Naphthalene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
n-Butyl acetate	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
n-Butylbenzene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
n-Propyl acetate	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
n-Propylbenzene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
o-Xylene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
p-Diethylbenzene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
p-Ethyltoluene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
sec-Butylbenzene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Styrene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
t-Butyl alcohol	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
tert-Butylbenzene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Tetrachloroethene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Toluene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
trans-1,2-Dichloroethene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
trans-1,3-Dichloropropene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Trichloroethene	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Trichlorofluoromethane	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Vinyl acetate	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Vinyl chloride	U	0.6	6.0		µg/Kg-dry	1	8/31/2011 5:12:00 PM
Surr: 4-Bromofluorobenzene	93.7	0	42-133		%REC	1	8/31/2011 5:12:00 PM
Surr: Dibromofluoromethane	100	0	50-133		%REC	1	8/31/2011 5:12:00 PM
Surr: Toluene-d8	99.2	0	53-130		%REC	1	8/31/2011 5:12:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-4C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 12:10:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-20A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
MERCURY			**SW7471B**		**SW7471B**		Analyst: **AB**
Mercury	1.19	0.03	0.0501		mg/Kg-dry	5	9/2/2011 12:25:58 PM
TOTAL DRO AS #2 FUEL (C8-C40)			**SW8015C**		**SW3550C**		Analyst: **LDS**
Total DRO TPH	49	2.81	11		mg/Kg-dry	1	9/1/2011 4:05:00 PM
Surr: o-Terphenyl	29.0	0	31-137	S	%REC	1	9/1/2011 4:05:00 PM
HERBICIDES SW-846 8151			**SW8151A**		**SW8151**		Analyst: **SB**
2,4,5-T	1.8	1.12	11	J	µg/Kg-dry	1	9/8/2011 12:40:00 PM
2,4,5-TP	U	1.12	11		µg/Kg-dry	1	9/8/2011 12:40:00 PM
2,4-D	U	1.12	11		µg/Kg-dry	1	9/8/2011 12:40:00 PM
Surr: 2,4-DCAA	79.6	0	14-148		%REC	1	9/8/2011 12:40:00 PM
PCB'S AS AROCLORS SW-846 METHOD 8082			**SW8082A**		**SW3550C**		Analyst: **SB**
Aroclor 1016	U	1.12	45		µg/Kg-dry	1	9/1/2011 8:51:00 PM
Aroclor 1221	U	1.12	45		µg/Kg-dry	1	9/1/2011 8:51:00 PM
Aroclor 1232	U	1.12	45		µg/Kg-dry	1	9/1/2011 8:51:00 PM
Aroclor 1242	U	1.12	45		µg/Kg-dry	1	9/1/2011 8:51:00 PM
Aroclor 1248	U	1.12	45		µg/Kg-dry	1	9/1/2011 8:51:00 PM
Aroclor 1254	U	1.12	45		µg/Kg-dry	1	9/1/2011 8:51:00 PM
Aroclor 1260	U	1.12	45		µg/Kg-dry	1	9/1/2011 8:51:00 PM
Aroclor 1262	U	1.12	45		µg/Kg-dry	1	9/1/2011 8:51:00 PM
Aroclor 1268	U	1.12	45		µg/Kg-dry	1	9/1/2011 8:51:00 PM
Surr: TCX	53.6	0	17-151		%REC	1	9/1/2011 8:51:00 PM
Surr: DCB	93.2	0	16-152		%REC	1	9/1/2011 8:51:00 PM
PESTICIDES SW-846 METHOD 8081			**SW8081B**		**SW3550C**		Analyst: **SB**
4,4'-DDD	5.4	0.22	2.2		µg/Kg-dry	1	9/2/2011 2:34:00 PM
4,4'-DDE	40	0.22	2.2		µg/Kg-dry	1	9/2/2011 2:34:00 PM
4,4'-DDT	84	0.22	2.2		µg/Kg-dry	1	9/2/2011 2:34:00 PM
Aldrin	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 2:34:00 PM
alpha-BHC	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 2:34:00 PM
beta-BHC	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 2:34:00 PM
Chlordane	34	1.12	2.2		µg/Kg-dry	1	9/2/2011 2:34:00 PM
Chlorobenzilate	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 2:34:00 PM
DBCP	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 2:34:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.	

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-4C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 12:10:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-20A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PESTICIDES SW-846 METHOD 8081			**SW8081B**		**SW3550C**		Analyst: **SB**
delta-BHC	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 2:34:00 PM
Dieldrin	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 2:34:00 PM
Endosulfan I	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 2:34:00 PM
Endosulfan II	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 2:34:00 PM
Endosulfan sulfate	1.1	0.22	2.2	J	µg/Kg-dry	1	9/2/2011 2:34:00 PM
Endrin	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 2:34:00 PM
Endrin aldehyde	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 2:34:00 PM
Endrin ketone	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 2:34:00 PM
gamma-BHC	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 2:34:00 PM
Heptachlor	0.71	0.22	2.2	J	µg/Kg-dry	1	9/2/2011 2:34:00 PM
Heptachlor epoxide	0.94	0.22	2.2	J	µg/Kg-dry	1	9/2/2011 2:34:00 PM
Hexachlorobenzene	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 2:34:00 PM
Hexachlorocyclopentadiene	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 2:34:00 PM
Methoxychlor	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 2:34:00 PM
Toxaphene	U	5.61	11		µg/Kg-dry	1	9/2/2011 2:34:00 PM
Surr: DCB	71.7	0	23-157		%REC	1	9/2/2011 2:34:00 PM
Surr: TCX	44.1	0	21-151		%REC	1	9/2/2011 2:34:00 PM
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	11.6	0	0		wt%	1	9/1/2011
TARGET ANALYTE LIST METALS			**SW6010C**		**SW3050B**		Analyst: **JP**
Aluminum	6020	0.11	0.440		mg/Kg-dry	1	9/2/2011 10:01:08 AM
Antimony	U	0.22	0.550		mg/Kg-dry	1	9/2/2011 10:01:08 AM
Arsenic	7.99	0.22	0.550		mg/Kg-dry	1	9/2/2011 10:01:08 AM
Barium	320	0.22	0.440		mg/Kg-dry	1	9/2/2011 10:01:08 AM
Beryllium	U	0.11	0.440		mg/Kg-dry	1	9/2/2011 10:01:08 AM
Cadmium	0.506	0.11	0.440		mg/Kg-dry	1	9/2/2011 10:01:08 AM
Calcium	22800	2.20	5.50		mg/Kg-dry	10	9/2/2011 12:57:00 PM
Chromium	16.5	0.11	0.440		mg/Kg-dry	1	9/2/2011 10:01:08 AM
Cobalt	U	0.11	0.440		mg/Kg-dry	1	9/2/2011 10:01:08 AM
Copper	58.5	0.11	0.440		mg/Kg-dry	1	9/2/2011 10:01:08 AM
Iron	15700	2.20	4.40		mg/Kg-dry	10	9/2/2011 12:57:00 PM
Lead	530	0.22	0.440		mg/Kg-dry	1	9/2/2011 10:01:08 AM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.	

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-4C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 12:10:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-20A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TARGET ANALYTE LIST METALS			**SW6010C**		**SW3050B**		Analyst: **JP**
Magnesium	2380	0.11	0.440		mg/Kg-dry	1	9/2/2011 10:01:08 AM
Manganese	292	0.11	0.440		mg/Kg-dry	1	9/2/2011 10:01:08 AM
Nickel	14.0	0.11	0.440		mg/Kg-dry	1	9/2/2011 10:01:08 AM
Potassium	1460	0.22	0.550		mg/Kg-dry	1	9/2/2011 10:01:08 AM
Selenium	0.660	0.22	0.550		mg/Kg-dry	1	9/2/2011 10:01:08 AM
Silver	1.34	0.11	0.440		mg/Kg-dry	1	9/2/2011 10:01:08 AM
Sodium	334	0.22	0.550		mg/Kg-dry	1	9/2/2011 10:01:08 AM
Thallium	U	0.33	0.550		mg/Kg-dry	1	9/2/2011 10:01:08 AM
Vanadium	24.7	0.11	0.440		mg/Kg-dry	1	9/2/2011 10:01:08 AM
Zinc	305	0.11	0.440		mg/Kg-dry	1	9/2/2011 10:01:08 AM
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
1,2,4-Trichlorobenzene	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
1,2-Dichlorobenzene	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
1,3-Dichlorobenzene	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
1,4-Dichlorobenzene	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
2,4,5-Trichlorophenol	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
2,4,6-Trichlorophenol	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
2,4-Dichlorophenol	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
2,4-Dimethylphenol	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
2,4-Dinitrophenol	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
2,4-Dinitrotoluene	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
2,6-Dinitrotoluene	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
2-Chloronaphthalene	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
2-Chlorophenol	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
2-Methylnaphthalene	95	28.1	280	J	µg/Kg-dry	1	9/1/2011 4:32:00 PM
2-Methylphenol	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
2-Nitroaniline	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
2-Nitrophenol	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
3,3´-Dichlorobenzidine	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
3+4-Methylphenol	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
3-Nitroaniline	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
4,6-Dinitro-2-methylphenol	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-4C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 12:10:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-20A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
4-Bromophenyl phenyl ether	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
4-Chloro-3-methylphenol	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
4-Chloroaniline	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
4-Chlorophenyl phenyl ether	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
4-Nitroaniline	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
4-Nitrophenol	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Acenaphthene	300	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Acenaphthylene	140	28.1	280	J	µg/Kg-dry	1	9/1/2011 4:32:00 PM
Acetophenone	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Aniline	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Anthracene	4200	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Atrazine	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Azobenzene	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Benzaldehyde	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Benzidine	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Benzo(a)anthracene	2200	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Benzo(a)pyrene	1800	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Benzo(b)fluoranthene	1500	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Benzo(g,h,i)perylene	1100	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Benzo(k)fluoranthene	1200	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Benzoic acid	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Benzyl alcohol	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Biphenyl	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Bis(2-chloroethoxy)methane	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Bis(2-chloroethyl)ether	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Bis(2-chloroisopropyl)ether	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Bis(2-ethylhexyl)phthalate	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Butyl benzyl phthalate	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Caprolactam	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Carbazole	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Chrysene	2000	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Dibenzo(a,h)anthracene	350	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Dibenzofuran	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-4C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 12:10:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-20A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
Diethyl phthalate	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Dimethyl phthalate	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Di-n-butyl phthalate	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Di-n-octyl phthalate	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Fluoranthene	5900	281	2800		µg/Kg-dry	10	9/2/2011 2:48:00 PM
Fluorene	300	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Hexachlorobenzene	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Hexachlorobutadiene	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Hexachlorocyclopentadiene	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Hexachloroethane	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Indeno(1,2,3-c,d)pyrene	1000	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Isophorone	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Naphthalene	44	28.1	280	J	µg/Kg-dry	1	9/1/2011 4:32:00 PM
Nitrobenzene	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
N-Nitrosodimethylamine	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
N-Nitrosodi-n-propylamine	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
N-Nitrosodiphenylamine	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Parathion	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Pentachlorophenol	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Phenanthrene	4300	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Phenol	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Pyrene	4200	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Pyridine	U	28.1	280		µg/Kg-dry	1	9/1/2011 4:32:00 PM
Surr: 2,4,6-Tribromophenol	61.5	0	21-119		%REC	10	9/2/2011 2:48:00 PM
Surr: 2,4,6-Tribromophenol	48.1	0	21-119		%REC	1	9/1/2011 4:32:00 PM
Surr: 2-Fluorobiphenyl	66.5	0	21-117		%REC	1	9/1/2011 4:32:00 PM
Surr: 2-Fluorobiphenyl	70.6	0	21-117		%REC	10	9/2/2011 2:48:00 PM
Surr: 2-Fluorophenol	26.9	0	11-105		%REC	1	9/1/2011 4:32:00 PM
Surr: 2-Fluorophenol	32.8	0	11-105		%REC	10	9/2/2011 2:48:00 PM
Surr: 4-Terphenyl-d14	71.0	0	21-132		%REC	1	9/1/2011 4:32:00 PM
Surr: 4-Terphenyl-d14	81.9	0	21-132		%REC	10	9/2/2011 2:48:00 PM
Surr: Nitrobenzene-d5	48.9	0	18-116		%REC	1	9/1/2011 4:32:00 PM
Surr: Nitrobenzene-d5	41.7	0	18-116		%REC	10	9/2/2011 2:48:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-4C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 12:10:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-20A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
Surr: Phenol-d6	36.8	0	12-110		%REC	10	9/2/2011 2:48:00 PM
Surr: Phenol-d6	27.2	0	12-110		%REC	1	9/1/2011 4:32:00 PM
CYANIDE, TOTAL			**SW9012A**		**SW9012A**		Analyst: **STP**
Cyanide, Total & Amenable: Auto Colorimetric	0.458	0.06	0.113		mg/Kg-dry	1	9/6/2011
HEXAVALENT CHROMIUM			**SW7196A**				Analyst: **AB**
Chromium, Hexavalent	0.258	0.23	0.453	J	mg/Kg-dry	1	9/6/2011

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-4C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 12:10:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-20B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP MERCURY			**SW1311/7471B**		**SW1311**		Analyst: **AB**
Mercury	U	0.0005	0.0200		mg/L	1	9/2/2011 10:33:13 AM
TCLP HERBICIDES SW-846 8151			**SW8151A**		**SW3510C**		Analyst: **SB**
2,4,5-TP	U	0.0002	0.0050		mg/L	1	9/7/2011 8:19:00 PM
2,4-D	U	0.0002	0.0050		mg/L	1	9/7/2011 8:19:00 PM
Surr: 2,4-DCAA	77.6	0	21-144		%REC	1	9/7/2011 8:19:00 PM
TCLP PESTICIDES SW-846 8081			**SW8081B**		**SW3510C**		Analyst: **SB**
Chlordane	0.00068	0.0005	0.0010	J	mg/L	1	9/7/2011 3:48:00 PM
Endrin	U	0.0002	0.0010		mg/L	1	9/7/2011 3:48:00 PM
gamma-BHC	U	0.0002	0.0010		mg/L	1	9/7/2011 3:48:00 PM
Heptachlor	U	0.0002	0.0010		mg/L	1	9/7/2011 3:48:00 PM
Heptachlor epoxide	U	0.0002	0.0010		mg/L	1	9/7/2011 3:48:00 PM
Methoxychlor	U	0.0002	0.0010		mg/L	1	9/7/2011 3:48:00 PM
Toxaphene	U	0.002	0.010		mg/L	1	9/7/2011 3:48:00 PM
Surr: DCB	66.0	0	28-146		%REC	1	9/7/2011 3:48:00 PM
Surr: TCX	60.7	0	25-147		%REC	1	9/7/2011 3:48:00 PM
TCLP METALS			**SW1311/6010C**		**SW1311**		Analyst: **JP**
Arsenic	0.0100	0.01	0.0500	J	mg/L	1	9/1/2011 3:32:30 PM
Barium	U	1	5.00		mg/L	1	9/1/2011 3:32:30 PM
Cadmium	U	0.005	0.0500		mg/L	1	9/1/2011 3:32:30 PM
Chromium	0.00500	0.005	0.0500	J	mg/L	1	9/1/2011 3:32:30 PM
Lead	0.166	0.005	0.0500		mg/L	1	9/1/2011 3:32:30 PM
Selenium	U	0.01	0.0500		mg/L	1	9/1/2011 3:32:30 PM
Silver	U	0.005	0.0500		mg/L	1	9/1/2011 3:32:30 PM
TCLP SEMIVOLATILES SW-846 8270			**SW8270D**		**SW3510C**		Analyst: **LDS**
2,4,5-Trichlorophenol	U	0.005	0.050		mg/L	1	9/6/2011 9:18:00 PM
2,4,6-Trichlorophenol	U	0.005	0.085		mg/L	1	9/6/2011 9:18:00 PM
2,4-Dinitrotoluene	U	0.005	0.045		mg/L	1	9/6/2011 9:18:00 PM
2-Methylphenol	U	0.005	0.035		mg/L	1	9/6/2011 9:18:00 PM
3+4-Methylphenol	U	0.005	0.040		mg/L	1	9/6/2011 9:18:00 PM
Hexachlorobenzene	U	0.005	0.090		mg/L	1	9/6/2011 9:18:00 PM
Hexachlorobutadiene	U	0.005	0.15		mg/L	1	9/6/2011 9:18:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.	

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-4C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 12:10:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-20B		

Certificate of Results

Analyses	Sample Result		LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP SEMIVOLATILES SW-846 8270				**SW8270D**		**SW3510C**		Analyst: **LDS**
Hexachloroethane	U		0.005	0.040		mg/L	1	9/6/2011 9:18:00 PM
Nitrobenzene	U		0.005	0.035		mg/L	1	9/6/2011 9:18:00 PM
Pentachlorophenol	U		0.05	0.17		mg/L	1	9/6/2011 9:18:00 PM
Pyridine	U		0.05	0.12		mg/L	1	9/6/2011 9:18:00 PM
Surr: 2,4,6-Tribromophenol	75.9		0	36-133		%REC	1	9/6/2011 9:18:00 PM
Surr: 2-Fluorobiphenyl	97.1		0	20-131		%REC	1	9/6/2011 9:18:00 PM
Surr: 2-Fluorophenol	77.1		0	22-128		%REC	1	9/6/2011 9:18:00 PM
Surr: 4-Terphenyl-d14	109		0	22-132		%REC	1	9/6/2011 9:18:00 PM
Surr: Nitrobenzene-d5	78.4		0	19-133		%REC	1	9/6/2011 9:18:00 PM
Surr: Phenol-d6	54.9		0	18-128		%REC	1	9/6/2011 9:18:00 PM
TCLP VOLATILES				**SW8260C**				Analyst: **LA**
1,1-Dichloroethene	U		0.01	0.020		mg/L	20	9/1/2011 2:03:00 PM
1,2-Dichloroethane	U		0.01	0.020		mg/L	20	9/1/2011 2:03:00 PM
1,4-Dichlorobenzene	U		0.01	0.020		mg/L	20	9/1/2011 2:03:00 PM
2-Butanone	U		0.02	0.040		mg/L	20	9/1/2011 2:03:00 PM
Benzene	U		0.01	0.020		mg/L	20	9/1/2011 2:03:00 PM
Carbon tetrachloride	U		0.01	0.020		mg/L	20	9/1/2011 2:03:00 PM
Chlorobenzene	U		0.01	0.020		mg/L	20	9/1/2011 2:03:00 PM
Chloroform	U		0.01	0.020		mg/L	20	9/1/2011 2:03:00 PM
Tetrachloroethene	U		0.01	0.020		mg/L	20	9/1/2011 2:03:00 PM
Trichloroethene	U		0.01	0.020		mg/L	20	9/1/2011 2:03:00 PM
Vinyl chloride	U		0.01	0.020		mg/L	20	9/1/2011 2:03:00 PM
Surr: 4-Bromofluorobenzene	102		0	63-123		%REC	20	9/1/2011 2:03:00 PM
Surr: Dibromofluoromethane	109		0	68-124		%REC	20	9/1/2011 2:03:00 PM
Surr: Toluene-d8	98.1		0	67-125		%REC	20	9/1/2011 2:03:00 PM
TRIVALENT CHROMIUM				**SW6010C**				Analyst: **JP**
Chromium, Trivalent	16.3		0.11	0.440		mg/Kg-dry	1	9/2/2011
IGNITABILITY/FLASHPOINT SW-846 1020				**SW1020B**				Analyst: **STP**
Ignitability	>		0	140		°F	1	9/1/2011
SOIL PH MEASURED IN WATER				**SW9045C**				Analyst: **AB**
pH	7.80		0	1.00	H	pH Units	1	9/1/2011 1:41:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-4C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 12:10:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-20B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TEMPERATURE			**M2550 B**				Analyst: **AB**
Temp at which pH was measured	21.0	0	0		°C	1	9/1/2011 1:41:00 PM
REACTIVE CYANIDE			**SW7.3.3.2**				Analyst: **STP**
Reactive Cyanide	U	0.06	0.113		mg/Kg-dry	1	9/8/2011
REACTIVE SULFIDE			**SW7.3.4.2**				Analyst: **STP**
Reactive Sulfide	U	1.13	2.26		mg/Kg-dry	1	9/8/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-4Ca (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 12:11:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-21A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TOTAL DRO AS #2 FUEL (C8-C40)			**SW8015C**		**SW3550C**		Analyst: **LDS**
Total DRO TPH	33	2.81	11		mg/Kg-dry	1	9/2/2011 4:44:00 PM
Surr: o-Terphenyl	35.2	0	31-137		%REC	1	9/2/2011 4:44:00 PM
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	12.3	0	0		wt%	1	9/1/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-4G (12 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 12:30:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-22A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PERCENT MOISTURE			D2216				Analyst: KK
Percent Moisture	12.4	0	0		wt%	1	9/1/2011
VOLATILE SW-846 METHOD 8260			SW8260C				Analyst: LA
1,1,1,2-Tetrachloroethane	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
1,1,1-Trichloroethane	U	0.64	6.4	C	µg/Kg-dry	1	8/31/2011 5:35:00 PM
1,1,2,2-Tetrachloroethane	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
1,1,2-Trichloro-1,2,2-trifluoroethan	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
1,1,2-Trichloroethane	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
1,1-Dichloroethane	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
1,1-Dichloroethene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
1,1-Dichloropropene	U	0.64	6.4	C	µg/Kg-dry	1	8/31/2011 5:35:00 PM
1,2,3-Trichlorobenzene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
1,2,3-Trichloropropane	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
1,2,4,5-Tetramethylbenzene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
1,2,4-Trichlorobenzene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
1,2,4-Trimethylbenzene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
1,2-Dibromo-3-chloropropane	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
1,2-Dibromoethane	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
1,2-Dichlorobenzene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
1,2-Dichloroethane	U	0.64	6.4	C	µg/Kg-dry	1	8/31/2011 5:35:00 PM
1,2-Dichloropropane	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
1,3,5-Trimethylbenzene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
1,3-Dichlorobenzene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
1,3-dichloropropane	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
1,4-Dichlorobenzene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
1,4-Dioxane	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
2,2-Dichloropropane	U	0.64	6.4	C	µg/Kg-dry	1	8/31/2011 5:35:00 PM
2-Butanone	U	1.9	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
2-Chloroethyl vinyl ether	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
2-Chlorotoluene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
2-Hexanone	U	1.9	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
2-Propanol	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
4-Chlorotoluene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-4G (12 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 12:30:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-22A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: LA
4-Isopropyltoluene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
4-Methyl-2-pentanone	U	1.9	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Acetone	U	1.9	6.4	C	µg/Kg-dry	1	8/31/2011 5:35:00 PM
Acrolein	U	3.2	13	C	µg/Kg-dry	1	8/31/2011 5:35:00 PM
Acrylonitrile	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Benzene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Bromobenzene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Bromochloromethane	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Bromodichloromethane	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Bromoform	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Bromomethane	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Carbon disulfide	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Carbon tetrachloride	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Chlorobenzene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Chlorodifluoromethane	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Chloroethane	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Chloroform	U	0.64	6.4	C	µg/Kg-dry	1	8/31/2011 5:35:00 PM
Chloromethane	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
cis-1,2-Dichloroethene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
cis-1,3-Dichloropropene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Dibromochloromethane	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Dibromomethane	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Dichlorodifluoromethane	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Diisopropyl ether	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Ethanol	U	3.2	13		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Ethyl acetate	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Ethylbenzene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Freon-114	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Hexachlorobutadiene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Isopropyl acetate	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Isopropylbenzene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
m,p-Xylene	U	1.3	13		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Methyl Acetate	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-4G (12 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 12:30:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-22A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: **LA**
Methyl tert-butyl ether	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Methylene chloride	14	0.64	6.4	B	µg/Kg-dry	1	8/31/2011 5:35:00 PM
n-Amyl acetate	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Naphthalene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
n-Butyl acetate	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
n-Butylbenzene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
n-Propyl acetate	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
n-Propylbenzene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
o-Xylene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
p-Diethylbenzene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
p-Ethyltoluene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
sec-Butylbenzene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Styrene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
t-Butyl alcohol	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
tert-Butylbenzene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Tetrachloroethene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Toluene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
trans-1,2-Dichloroethene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
trans-1,3-Dichloropropene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Trichloroethene	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Trichlorofluoromethane	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Vinyl acetate	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Vinyl chloride	U	0.64	6.4		µg/Kg-dry	1	8/31/2011 5:35:00 PM
Surr: 4-Bromofluorobenzene	92.6	0	42-133		%REC	1	8/31/2011 5:35:00 PM
Surr: Dibromofluoromethane	103	0	50-133		%REC	1	8/31/2011 5:35:00 PM
Surr: Toluene-d8	99.3	0	53-130		%REC	1	8/31/2011 5:35:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-4C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 12:25:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-23A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
MERCURY			**SW7471B**		**SW7471B**		Analyst: **AB**
Mercury	1.60	0.03	0.0530		mg/Kg-dry	5	9/2/2011 12:28:08 PM
TOTAL DRO AS #2 FUEL (C8-C40)			**SW8015C**		**SW3550C**		Analyst: **LDS**
Total DRO TPH	170	2.84	11		mg/Kg-dry	1	9/1/2011 4:30:00 PM
Surr: o-Terphenyl	48.0	0	31-137		%REC	1	9/1/2011 4:30:00 PM
HERBICIDES SW-846 8151			**SW8151A**		**SW8151**		Analyst: **SB**
2,4,5-T	U	1.13	11		µg/Kg-dry	1	9/8/2011 3:42:00 PM
2,4,5-TP	U	1.13	11		µg/Kg-dry	1	9/8/2011 3:42:00 PM
2,4-D	U	1.13	11		µg/Kg-dry	1	9/8/2011 3:42:00 PM
Surr: 2,4-DCAA	100	0	14-148		%REC	1	9/8/2011 3:42:00 PM
PCB'S AS AROCLORS SW-846 METHOD 8082			**SW8082A**		**SW3550C**		Analyst: **SB**
Aroclor 1016	U	1.13	45		µg/Kg-dry	1	9/1/2011 9:14:00 PM
Aroclor 1221	U	1.13	45		µg/Kg-dry	1	9/1/2011 9:14:00 PM
Aroclor 1232	U	1.13	45		µg/Kg-dry	1	9/1/2011 9:14:00 PM
Aroclor 1242	U	1.13	45		µg/Kg-dry	1	9/1/2011 9:14:00 PM
Aroclor 1248	U	1.13	45		µg/Kg-dry	1	9/1/2011 9:14:00 PM
Aroclor 1254	U	1.13	45		µg/Kg-dry	1	9/1/2011 9:14:00 PM
Aroclor 1260	U	1.13	45		µg/Kg-dry	1	9/1/2011 9:14:00 PM
Aroclor 1262	U	1.13	45		µg/Kg-dry	1	9/1/2011 9:14:00 PM
Aroclor 1268	U	1.13	45		µg/Kg-dry	1	9/1/2011 9:14:00 PM
Surr: TCX	57.9	0	17-151		%REC	1	9/1/2011 9:14:00 PM
Surr: DCB	89.0	0	16-152		%REC	1	9/1/2011 9:14:00 PM
PESTICIDES SW-846 METHOD 8081			**SW8081B**		**SW3550C**		Analyst: **SB**
4,4'-DDD	1.2	0.23	2.3	J	µg/Kg-dry	1	9/2/2011 2:48:00 PM
4,4'-DDE	11	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:48:00 PM
4,4'-DDT	15	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:48:00 PM
Aldrin	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:48:00 PM
alpha-BHC	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:48:00 PM
beta-BHC	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:48:00 PM
Chlordane	20	1.13	2.3		µg/Kg-dry	1	9/2/2011 2:48:00 PM
Chlorobenzilate	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:48:00 PM
DBCP	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:48:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.	

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-4C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 12:25:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-23A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PESTICIDES SW-846 METHOD 8081			**SW8081B**		**SW3550C**		Analyst: **SB**
delta-BHC	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:48:00 PM
Dieldrin	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:48:00 PM
Endosulfan I	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:48:00 PM
Endosulfan II	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:48:00 PM
Endosulfan sulfate	2.1	0.23	2.3	JP	µg/Kg-dry	1	9/2/2011 2:48:00 PM
Endrin	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:48:00 PM
Endrin aldehyde	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:48:00 PM
Endrin ketone	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:48:00 PM
gamma-BHC	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:48:00 PM
Heptachlor	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:48:00 PM
Heptachlor epoxide	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:48:00 PM
Hexachlorobenzene	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:48:00 PM
Hexachlorocyclopentadiene	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:48:00 PM
Methoxychlor	U	0.23	2.3		µg/Kg-dry	1	9/2/2011 2:48:00 PM
Toxaphene	U	5.67	11		µg/Kg-dry	1	9/2/2011 2:48:00 PM
Surr: DCB	57.5	0	23-157		%REC	1	9/2/2011 2:48:00 PM
Surr: TCX	47.7	0	21-151		%REC	1	9/2/2011 2:48:00 PM
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	12.7	0	0		wt%	1	9/1/2011
TARGET ANALYTE LIST METALS			**SW6010C**		**SW3050B**		Analyst: **JP**
Aluminum	5140	0.10	0.417		mg/Kg-dry	1	9/2/2011 10:28:09 AM
Antimony	0.208	0.21	0.521	J	mg/Kg-dry	1	9/2/2011 10:28:09 AM
Arsenic	6.48	0.21	0.521		mg/Kg-dry	1	9/2/2011 10:28:09 AM
Barium	330	0.21	0.417		mg/Kg-dry	1	9/2/2011 10:28:09 AM
Beryllium	U	0.10	0.417		mg/Kg-dry	1	9/2/2011 10:28:09 AM
Cadmium	0.729	0.10	0.417		mg/Kg-dry	1	9/2/2011 10:28:09 AM
Calcium	23500	2.08	5.21		mg/Kg-dry	10	9/2/2011 12:59:04 PM
Chromium	14.5	0.10	0.417		mg/Kg-dry	1	9/2/2011 10:28:09 AM
Cobalt	U	0.10	0.417		mg/Kg-dry	1	9/2/2011 10:28:09 AM
Copper	73.0	0.10	0.417		mg/Kg-dry	1	9/2/2011 10:28:09 AM
Iron	13000	2.08	4.17		mg/Kg-dry	10	9/2/2011 12:59:04 PM
Lead	613	0.21	0.417		mg/Kg-dry	1	9/2/2011 10:28:09 AM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.	

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-4C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 12:25:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-23A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TARGET ANALYTE LIST METALS			**SW6010C**		**SW3050B**		Analyst: **JP**
Magnesium	2090	0.10	0.417		mg/Kg-dry	1	9/2/2011 10:28:09 AM
Manganese	238	0.10	0.417		mg/Kg-dry	1	9/2/2011 10:28:09 AM
Nickel	13.7	0.10	0.417		mg/Kg-dry	1	9/2/2011 10:28:09 AM
Potassium	1130	0.21	0.521		mg/Kg-dry	1	9/2/2011 10:28:09 AM
Selenium	0.479	0.21	0.521	J	mg/Kg-dry	1	9/2/2011 10:28:09 AM
Silver	1.21	0.10	0.417		mg/Kg-dry	1	9/2/2011 10:28:09 AM
Sodium	435	0.21	0.521		mg/Kg-dry	1	9/2/2011 10:28:09 AM
Thallium	U	0.31	0.521		mg/Kg-dry	1	9/2/2011 10:28:09 AM
Vanadium	18.9	0.10	0.417		mg/Kg-dry	1	9/2/2011 10:28:09 AM
Zinc	397	0.10	0.417		mg/Kg-dry	1	9/2/2011 10:28:09 AM
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
1,2,4-Trichlorobenzene	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
1,2-Dichlorobenzene	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
1,3-Dichlorobenzene	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
1,4-Dichlorobenzene	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
2,4,5-Trichlorophenol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
2,4,6-Trichlorophenol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
2,4-Dichlorophenol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
2,4-Dimethylphenol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
2,4-Dinitrophenol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
2,4-Dinitrotoluene	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
2,6-Dinitrotoluene	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
2-Chloronaphthalene	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
2-Chlorophenol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
2-Methylnaphthalene	650	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
2-Methylphenol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
2-Nitroaniline	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
2-Nitrophenol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
3,3´-Dichlorobenzidine	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
3+4-Methylphenol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
3-Nitroaniline	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
4,6-Dinitro-2-methylphenol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-4C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 12:25:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-23A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
4-Bromophenyl phenyl ether	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
4-Chloro-3-methylphenol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
4-Chloroaniline	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
4-Chlorophenyl phenyl ether	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
4-Nitroaniline	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
4-Nitrophenol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Acenaphthene	2000	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Acenaphthylene	150	28.4	280	J	µg/Kg-dry	1	9/1/2011 4:57:00 PM
Acetophenone	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Aniline	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Anthracene	5400	284	2800		µg/Kg-dry	10	9/2/2011 3:13:00 PM
Atrazine	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Azobenzene	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Benzaldehyde	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Benzidine	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Benzo(a)anthracene	9600	284	2800		µg/Kg-dry	10	9/2/2011 3:13:00 PM
Benzo(a)pyrene	6500	284	2800		µg/Kg-dry	10	9/2/2011 3:13:00 PM
Benzo(b)fluoranthene	4400	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Benzo(g,h,i)perylene	3400	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Benzo(k)fluoranthene	4400	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Benzoic acid	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Benzyl alcohol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Biphenyl	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Bis(2-chloroethoxy)methane	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Bis(2-chloroethyl)ether	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Bis(2-chloroisopropyl)ether	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Bis(2-ethylhexyl)phthalate	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Butyl benzyl phthalate	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Caprolactam	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Carbazole	810	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Chrysene	8700	284	2800		µg/Kg-dry	10	9/2/2011 3:13:00 PM
Dibenzo(a,h)anthracene	1000	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Dibenzofuran	870	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-4C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 12:25:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-23A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
Diethyl phthalate	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Dimethyl phthalate	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Di-n-butyl phthalate	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Di-n-octyl phthalate	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Fluoranthene	22000	284	2800		µg/Kg-dry	10	9/2/2011 3:13:00 PM
Fluorene	1800	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Hexachlorobenzene	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Hexachlorobutadiene	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Hexachlorocyclopentadiene	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Hexachloroethane	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Indeno(1,2,3-c,d)pyrene	3000	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Isophorone	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Naphthalene	620	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Nitrobenzene	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
N-Nitrosodimethylamine	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
N-Nitrosodi-n-propylamine	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
N-Nitrosodiphenylamine	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Parathion	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Pentachlorophenol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Phenanthrene	24000	284	2800		µg/Kg-dry	10	9/2/2011 3:13:00 PM
Phenol	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Pyrene	22000	284	2800		µg/Kg-dry	10	9/2/2011 3:13:00 PM
Pyridine	U	28.4	280		µg/Kg-dry	1	9/1/2011 4:57:00 PM
Surr: 2,4,6-Tribromophenol	59.8	0	21-119		%REC	1	9/1/2011 4:57:00 PM
Surr: 2,4,6-Tribromophenol	25.8	0	21-119		%REC	10	9/2/2011 3:13:00 PM
Surr: 2-Fluorobiphenyl	65.4	0	21-117		%REC	10	9/2/2011 3:13:00 PM
Surr: 2-Fluorobiphenyl	61.7	0	21-117		%REC	1	9/1/2011 4:57:00 PM
Surr: 2-Fluorophenol	24.8	0	11-105		%REC	1	9/1/2011 4:57:00 PM
Surr: 2-Fluorophenol	27.9	0	11-105		%REC	10	9/2/2011 3:13:00 PM
Surr: 4-Terphenyl-d14	72.2	0	21-132		%REC	10	9/2/2011 3:13:00 PM
Surr: 4-Terphenyl-d14	66.1	0	21-132		%REC	1	9/1/2011 4:57:00 PM
Surr: Nitrobenzene-d5	42.6	0	18-116		%REC	1	9/1/2011 4:57:00 PM
Surr: Nitrobenzene-d5	37.4	0	18-116		%REC	10	9/2/2011 3:13:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-4C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 12:25:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-23A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
Surr: Phenol-d6	31.2	0	12-110		%REC	10	9/2/2011 3:13:00 PM
Surr: Phenol-d6	26.3	0	12-110		%REC	1	9/1/2011 4:57:00 PM
CYANIDE, TOTAL			**SW9012A**		**SW9012A**		Analyst: **STP**
Cyanide, Total & Amenable: Auto Colorimetric	0.554	0.06	0.115		mg/Kg-dry	1	9/6/2011
HEXAVALENT CHROMIUM			**SW7196A**				Analyst: **AB**
Chromium, Hexavalent	0.511	0.23	0.458		mg/Kg-dry	1	9/6/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-4C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 12:25:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-23B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP MERCURY			**SW1311/7471B**		**SW1311**		Analyst: **AB**
Mercury	U	0.0005	0.0200		mg/L	1	9/2/2011 10:35:21 AM
TCLP HERBICIDES SW-846 8151			**SW8151A**		**SW3510C**		Analyst: **SB**
2,4,5-TP	U	0.0002	0.0050		mg/L	1	9/7/2011 8:33:00 PM
2,4-D	U	0.0002	0.0050		mg/L	1	9/7/2011 8:33:00 PM
Surr: 2,4-DCAA	85.0	0	21-144		%REC	1	9/7/2011 8:33:00 PM
TCLP PESTICIDES SW-846 8081			**SW8081B**		**SW3510C**		Analyst: **SB**
Chlordane	U	0.0005	0.0010		mg/L	1	9/7/2011 4:02:00 PM
Endrin	U	0.0002	0.0010		mg/L	1	9/7/2011 4:02:00 PM
gamma-BHC	U	0.0002	0.0010		mg/L	1	9/7/2011 4:02:00 PM
Heptachlor	U	0.0002	0.0010		mg/L	1	9/7/2011 4:02:00 PM
Heptachlor epoxide	U	0.0002	0.0010		mg/L	1	9/7/2011 4:02:00 PM
Methoxychlor	U	0.0002	0.0010		mg/L	1	9/7/2011 4:02:00 PM
Toxaphene	U	0.002	0.010		mg/L	1	9/7/2011 4:02:00 PM
Surr: DCB	84.0	0	28-146		%REC	1	9/7/2011 4:02:00 PM
Surr: TCX	82.2	0	25-147		%REC	1	9/7/2011 4:02:00 PM
TCLP METALS			**SW1311/6010C**		**SW1311**		Analyst: **JP**
Arsenic	U	0.01	0.0500		mg/L	1	9/1/2011 3:34:33 PM
Barium	U	1	5.00		mg/L	1	9/1/2011 3:34:33 PM
Cadmium	0.00600	0.005	0.0500	J	mg/L	1	9/1/2011 3:34:33 PM
Chromium	U	0.005	0.0500		mg/L	1	9/1/2011 3:34:33 PM
Lead	0.349	0.005	0.0500		mg/L	1	9/1/2011 3:34:33 PM
Selenium	U	0.01	0.0500		mg/L	1	9/1/2011 3:34:33 PM
Silver	U	0.005	0.0500		mg/L	1	9/1/2011 3:34:33 PM
TCLP SEMIVOLATILES SW-846 8270			**SW8270D**		**SW3510C**		Analyst: **LDS**
2,4,5-Trichlorophenol	U	0.005	0.050		mg/L	1	9/7/2011 9:46:00 AM
2,4,6-Trichlorophenol	U	0.005	0.085		mg/L	1	9/7/2011 9:46:00 AM
2,4-Dinitrotoluene	U	0.005	0.045		mg/L	1	9/7/2011 9:46:00 AM
2-Methylphenol	U	0.005	0.035		mg/L	1	9/7/2011 9:46:00 AM
3+4-Methylphenol	U	0.005	0.040		mg/L	1	9/7/2011 9:46:00 AM
Hexachlorobenzene	U	0.005	0.090		mg/L	1	9/7/2011 9:46:00 AM
Hexachlorobutadiene	U	0.005	0.15		mg/L	1	9/7/2011 9:46:00 AM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

ACCREDITED IN ACCORDANCE WITH nelac

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-4C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 12:25:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-23B		

Certificate of Results

Analyses	Sample Result		LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP SEMIVOLATILES SW-846 8270				**SW8270D**		**SW3510C**		Analyst: **LDS**
Hexachloroethane	U		0.005	0.040		mg/L	1	9/7/2011 9:46:00 AM
Nitrobenzene	U		0.005	0.035		mg/L	1	9/7/2011 9:46:00 AM
Pentachlorophenol	U		0.05	0.17		mg/L	1	9/7/2011 9:46:00 AM
Pyridine	U		0.05	0.12		mg/L	1	9/7/2011 9:46:00 AM
Surr: 2,4,6-Tribromophenol	78.9		0	36-133		%REC	1	9/7/2011 9:46:00 AM
Surr: 2-Fluorobiphenyl	93.3		0	20-131		%REC	1	9/7/2011 9:46:00 AM
Surr: 2-Fluorophenol	86.5		0	22-128		%REC	1	9/7/2011 9:46:00 AM
Surr: 4-Terphenyl-d14	107		0	22-132		%REC	1	9/7/2011 9:46:00 AM
Surr: Nitrobenzene-d5	86.9		0	19-133		%REC	1	9/7/2011 9:46:00 AM
Surr: Phenol-d6	54.9		0	18-128		%REC	1	9/7/2011 9:46:00 AM
TCLP VOLATILES				**SW8260C**				Analyst: **LA**
1,1-Dichloroethene	U		0.01	0.020		mg/L	20	9/1/2011 2:26:00 PM
1,2-Dichloroethane	U		0.01	0.020		mg/L	20	9/1/2011 2:26:00 PM
1,4-Dichlorobenzene	U		0.01	0.020		mg/L	20	9/1/2011 2:26:00 PM
2-Butanone	U		0.02	0.040		mg/L	20	9/1/2011 2:26:00 PM
Benzene	U		0.01	0.020		mg/L	20	9/1/2011 2:26:00 PM
Carbon tetrachloride	U		0.01	0.020		mg/L	20	9/1/2011 2:26:00 PM
Chlorobenzene	U		0.01	0.020		mg/L	20	9/1/2011 2:26:00 PM
Chloroform	U		0.01	0.020		mg/L	20	9/1/2011 2:26:00 PM
Tetrachloroethene	U		0.01	0.020		mg/L	20	9/1/2011 2:26:00 PM
Trichloroethene	U		0.01	0.020		mg/L	20	9/1/2011 2:26:00 PM
Vinyl chloride	U		0.01	0.020		mg/L	20	9/1/2011 2:26:00 PM
Surr: 4-Bromofluorobenzene	99.5		0	63-123		%REC	20	9/1/2011 2:26:00 PM
Surr: Dibromofluoromethane	108		0	68-124		%REC	20	9/1/2011 2:26:00 PM
Surr: Toluene-d8	96.8		0	67-125		%REC	20	9/1/2011 2:26:00 PM
TRIVALENT CHROMIUM				**SW6010C**				Analyst: **JP**
Chromium, Trivalent	13.9		0.10	0.417		mg/Kg-dry	1	9/2/2011
IGNITABILITY/FLASHPOINT SW-846 1020				**SW1020B**				Analyst: **STP**
Ignitability	>		0	140		°F	1	9/1/2011
SOIL PH MEASURED IN WATER				**SW9045C**				Analyst: **AB**
pH	7.80		0	1.00	H	pH Units	1	9/1/2011 1:43:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-4C (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 12:25:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-23B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TEMPERATURE			**M2550 B**				Analyst: **AB**
Temp at which pH was measured	21.0	0	0		°C	1	9/1/2011 1:43:00 PM
REACTIVE CYANIDE			**SW7.3.3.2**				Analyst: **STP**
Reactive Cyanide	U	0.06	0.115		mg/Kg-dry	1	9/8/2011
REACTIVE SULFIDE			**SW7.3.4.2**				Analyst: **STP**
Reactive Sulfide	U	1.15	2.29		mg/Kg-dry	1	9/8/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-4Ca (7-14 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 12:20:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-24A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TOTAL DRO AS #2 FUEL (C8-C40)			**SW8015C**	**SW3550C**			Analyst: **LDS**
Total DRO TPH	13	2.75	11		mg/Kg-dry	1	9/2/2011 5:10:00 PM
Surr: o-Terphenyl	33.8	0	31-137		%REC	1	9/2/2011 5:10:00 PM
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	13.0	0	0		wt%	1	9/1/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-5G (11 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 9:40:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-25A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PERCENT MOISTURE			D2216				Analyst: KK
Percent Moisture	21.2	0	0		wt%	1	9/1/2011
VOLATILE SW-846 METHOD 8260			SW8260C				Analyst: LA
1,1,1,2-Tetrachloroethane	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
1,1,1-Trichloroethane	U	1.7	17	C	µg/Kg-dry	1	8/31/2011 6:00:00 PM
1,1,2,2-Tetrachloroethane	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
1,1,2-Trichloro-1,2,2-trifluoroethan	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
1,1,2-Trichloroethane	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
1,1-Dichloroethane	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
1,1-Dichloroethene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
1,1-Dichloropropene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
1,2,3-Trichlorobenzene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
1,2,3-Trichloropropane	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
1,2,4,5-Tetramethylbenzene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
1,2,4-Trichlorobenzene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
1,2,4-Trimethylbenzene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
1,2-Dibromo-3-chloropropane	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
1,2-Dibromoethane	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
1,2-Dichlorobenzene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
1,2-Dichloroethane	U	1.7	17	C	µg/Kg-dry	1	8/31/2011 6:00:00 PM
1,2-Dichloropropane	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
1,3,5-Trimethylbenzene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
1,3-Dichlorobenzene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
1,3-dichloropropane	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
1,4-Dichlorobenzene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
1,4-Dioxane	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
2,2-Dichloropropane	U	1.7	17	C	µg/Kg-dry	1	8/31/2011 6:00:00 PM
2-Butanone	U	5	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
2-Chloroethyl vinyl ether	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
2-Chlorotoluene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
2-Hexanone	U	5	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
2-Propanol	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
4-Chlorotoluene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-5G (11 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 9:40:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-25A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: **LA**
4-Isopropyltoluene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
4-Methyl-2-pentanone	U	5	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Acetone	U	5	17	C	µg/Kg-dry	1	8/31/2011 6:00:00 PM
Acrolein	U	8.3	33	C	µg/Kg-dry	1	8/31/2011 6:00:00 PM
Acrylonitrile	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Benzene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Bromobenzene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Bromochloromethane	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Bromodichloromethane	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Bromoform	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Bromomethane	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Carbon disulfide	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Carbon tetrachloride	U	1.7	17	C	µg/Kg-dry	1	8/31/2011 6:00:00 PM
Chlorobenzene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Chlorodifluoromethane	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Chloroethane	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Chloroform	U	1.7	17	C	µg/Kg-dry	1	8/31/2011 6:00:00 PM
Chloromethane	U	1.7	17	C	µg/Kg-dry	1	8/31/2011 6:00:00 PM
cis-1,2-Dichloroethene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
cis-1,3-Dichloropropene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Dibromochloromethane	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Dibromomethane	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Dichlorodifluoromethane	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Diisopropyl ether	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Ethanol	U	8.3	33		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Ethyl acetate	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Ethylbenzene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Freon-114	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Hexachlorobutadiene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Isopropyl acetate	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Isopropylbenzene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
m,p-Xylene	U	3.3	33		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Methyl Acetate	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-5G (11 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 9:40:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-25A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: **LA**
Methyl tert-butyl ether	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Methylene chloride	31	1.7	17	B	µg/Kg-dry	1	8/31/2011 6:00:00 PM
n-Amyl acetate	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Naphthalene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
n-Butyl acetate	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
n-Butylbenzene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
n-Propyl acetate	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
n-Propylbenzene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
o-Xylene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
p-Diethylbenzene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
p-Ethyltoluene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
sec-Butylbenzene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Styrene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
t-Butyl alcohol	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
tert-Butylbenzene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Tetrachloroethene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Toluene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
trans-1,2-Dichloroethene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
trans-1,3-Dichloropropene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Trichloroethene	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Trichlorofluoromethane	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Vinyl acetate	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Vinyl chloride	U	1.7	17		µg/Kg-dry	1	8/31/2011 6:00:00 PM
Surr: 4-Bromofluorobenzene	89.9	0	42-133		%REC	1	8/31/2011 6:00:00 PM
Surr: Dibromofluoromethane	98.3	0	50-133		%REC	1	8/31/2011 6:00:00 PM
Surr: Toluene-d8	97.9	0	53-130		%REC	1	8/31/2011 6:00:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-5C (0-11 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 9:35:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-26A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
MERCURY			**SW7471B**		**SW7471B**		Analyst: **AB**
Mercury	0.543	0.009	0.0178		mg/Kg-dry	2	9/2/2011 12:34:30 PM
TOTAL DRO AS #2 FUEL (C8-C40)			**SW8015C**		**SW3550C**		Analyst: **LDS**
Total DRO TPH	49	2.75	11		mg/Kg-dry	1	9/1/2011 4:55:00 PM
Surr: o-Terphenyl	30.7	0	31-137	S	%REC	1	9/1/2011 4:55:00 PM
HERBICIDES SW-846 8151			**SW8151A**		**SW8151**		Analyst: **SB**
2,4,5-T	U	1.08	11		µg/Kg-dry	1	9/8/2011 3:56:00 PM
2,4,5-TP	U	1.08	11		µg/Kg-dry	1	9/8/2011 3:56:00 PM
2,4-D	U	1.08	11		µg/Kg-dry	1	9/8/2011 3:56:00 PM
Surr: 2,4-DCAA	80.5	0	14-148		%REC	1	9/8/2011 3:56:00 PM
PCB'S AS AROCLORS SW-846 METHOD 8082			**SW8082A**		**SW3550C**		Analyst: **SB**
Aroclor 1016	U	1.10	44		µg/Kg-dry	1	9/1/2011 9:38:00 PM
Aroclor 1221	U	1.10	44		µg/Kg-dry	1	9/1/2011 9:38:00 PM
Aroclor 1232	U	1.10	44		µg/Kg-dry	1	9/1/2011 9:38:00 PM
Aroclor 1242	U	1.10	44		µg/Kg-dry	1	9/1/2011 9:38:00 PM
Aroclor 1248	U	1.10	44		µg/Kg-dry	1	9/1/2011 9:38:00 PM
Aroclor 1254	U	1.10	44		µg/Kg-dry	1	9/1/2011 9:38:00 PM
Aroclor 1260	U	1.10	44		µg/Kg-dry	1	9/1/2011 9:38:00 PM
Aroclor 1262	76	1.10	44		µg/Kg-dry	1	9/1/2011 9:38:00 PM
Aroclor 1268	U	1.10	44		µg/Kg-dry	1	9/1/2011 9:38:00 PM
Surr: TCX	60.0	0	17-151		%REC	1	9/1/2011 9:38:00 PM
Surr: DCB	78.9	0	16-152		%REC	1	9/1/2011 9:38:00 PM
PESTICIDES SW-846 METHOD 8081			**SW8081B**		**SW3550C**		Analyst: **SB**
4,4'-DDD	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:02:00 PM
4,4'-DDE	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:02:00 PM
4,4'-DDT	4.1	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:02:00 PM
Aldrin	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:02:00 PM
alpha-BHC	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:02:00 PM
beta-BHC	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:02:00 PM
Chlordane	2.6	1.10	2.2		µg/Kg-dry	1	9/2/2011 3:02:00 PM
Chlorobenzilate	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:02:00 PM
DBCP	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:02:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.	

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-5C (0-11 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 9:35:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-26A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PESTICIDES SW-846 METHOD 8081			**SW8081B**		**SW3550C**		Analyst: **SB**
delta-BHC	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:02:00 PM
Dieldrin	2.5	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:02:00 PM
Endosulfan I	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:02:00 PM
Endosulfan II	1.7	0.22	2.2	J	µg/Kg-dry	1	9/2/2011 3:02:00 PM
Endosulfan sulfate	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:02:00 PM
Endrin	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:02:00 PM
Endrin aldehyde	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:02:00 PM
Endrin ketone	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:02:00 PM
gamma-BHC	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:02:00 PM
Heptachlor	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:02:00 PM
Heptachlor epoxide	0.66	0.22	2.2	J	µg/Kg-dry	1	9/2/2011 3:02:00 PM
Hexachlorobenzene	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:02:00 PM
Hexachlorocyclopentadiene	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:02:00 PM
Methoxychlor	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:02:00 PM
Toxaphene	U	5.51	11		µg/Kg-dry	1	9/2/2011 3:02:00 PM
Surr: DCB	64.6	0	23-157		%REC	1	9/2/2011 3:02:00 PM
Surr: TCX	47.5	0	21-151		%REC	1	9/2/2011 3:02:00 PM
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	9.97	0	0		wt%	1	9/1/2011
TARGET ANALYTE LIST METALS			**SW6010C**		**SW3050B**		Analyst: **JP**
Aluminum	4030	0.1	0.392		mg/Kg-dry	1	9/2/2011 10:03:28 AM
Antimony	U	0.2	0.491		mg/Kg-dry	1	9/2/2011 10:03:28 AM
Arsenic	9.14	0.2	0.491		mg/Kg-dry	1	9/2/2011 10:03:28 AM
Barium	216	0.2	0.392		mg/Kg-dry	1	9/2/2011 10:03:28 AM
Beryllium	U	0.1	0.392		mg/Kg-dry	1	9/2/2011 10:03:28 AM
Cadmium	0.589	0.1	0.392		mg/Kg-dry	1	9/2/2011 10:03:28 AM
Calcium	14200	1.96	4.91		mg/Kg-dry	10	9/2/2011 12:22:57 PM
Chromium	15.5	0.1	0.392		mg/Kg-dry	1	9/2/2011 10:03:28 AM
Cobalt	U	0.1	0.392		mg/Kg-dry	1	9/2/2011 10:03:28 AM
Copper	37.1	0.1	0.392		mg/Kg-dry	1	9/2/2011 10:03:28 AM
Iron	11500	1.96	3.92		mg/Kg-dry	10	9/2/2011 12:22:57 PM
Lead	882	0.2	0.392		mg/Kg-dry	1	9/2/2011 10:03:28 AM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-5C (0-11 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 9:35:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-26A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TARGET ANALYTE LIST METALS			**SW6010C**		**SW3050B**		Analyst: **JP**
Magnesium	2590	0.1	0.392		mg/Kg-dry	1	9/2/2011 10:03:28 AM
Manganese	168	0.1	0.392		mg/Kg-dry	1	9/2/2011 10:03:28 AM
Nickel	13.7	0.1	0.392		mg/Kg-dry	1	9/2/2011 10:03:28 AM
Potassium	1340	0.2	0.491		mg/Kg-dry	1	9/2/2011 10:03:28 AM
Selenium	1.00	0.2	0.491		mg/Kg-dry	1	9/2/2011 10:03:28 AM
Silver	0.255	0.1	0.392	J	mg/Kg-dry	1	9/2/2011 10:03:28 AM
Sodium	217	0.2	0.491		mg/Kg-dry	1	9/2/2011 10:03:28 AM
Thallium	U	0.29	0.491		mg/Kg-dry	1	9/2/2011 10:03:28 AM
Vanadium	17.3	0.1	0.392		mg/Kg-dry	1	9/2/2011 10:03:28 AM
Zinc	276	0.1	0.392		mg/Kg-dry	1	9/2/2011 10:03:28 AM
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
1,2,4-Trichlorobenzene	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
1,2-Dichlorobenzene	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
1,3-Dichlorobenzene	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
1,4-Dichlorobenzene	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
2,4,5-Trichlorophenol	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
2,4,6-Trichlorophenol	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
2,4-Dichlorophenol	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
2,4-Dimethylphenol	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
2,4-Dinitrophenol	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
2,4-Dinitrotoluene	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
2,6-Dinitrotoluene	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
2-Chloronaphthalene	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
2-Chlorophenol	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
2-Methylnaphthalene	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
2-Methylphenol	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
2-Nitroaniline	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
2-Nitrophenol	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
3,3'-Dichlorobenzidine	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
3+4-Methylphenol	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
3-Nitroaniline	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
4,6-Dinitro-2-methylphenol	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-5C (0-11 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 9:35:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-26A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
4-Bromophenyl phenyl ether	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
4-Chloro-3-methylphenol	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
4-Chloroaniline	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
4-Chlorophenyl phenyl ether	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
4-Nitroaniline	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
4-Nitrophenol	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Acenaphthene	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Acenaphthylene	29	27.5	280	J	µg/Kg-dry	1	9/1/2011 5:23:00 PM
Acetophenone	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Aniline	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Anthracene	75	27.5	280	J	µg/Kg-dry	1	9/1/2011 5:23:00 PM
Atrazine	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Azobenzene	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Benzaldehyde	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Benzidine	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Benzo(a)anthracene	200	27.5	280	J	µg/Kg-dry	1	9/1/2011 5:23:00 PM
Benzo(a)pyrene	230	27.5	280	J	µg/Kg-dry	1	9/1/2011 5:23:00 PM
Benzo(b)fluoranthene	220	27.5	280	J	µg/Kg-dry	1	9/1/2011 5:23:00 PM
Benzo(g,h,i)perylene	180	27.5	280	J	µg/Kg-dry	1	9/1/2011 5:23:00 PM
Benzo(k)fluoranthene	210	27.5	280	J	µg/Kg-dry	1	9/1/2011 5:23:00 PM
Benzoic acid	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Benzyl alcohol	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Biphenyl	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Bis(2-chloroethoxy)methane	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Bis(2-chloroethyl)ether	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Bis(2-chloroisopropyl)ether	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Bis(2-ethylhexyl)phthalate	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Butyl benzyl phthalate	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Caprolactam	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Carbazole	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Chrysene	260	27.5	280	J	µg/Kg-dry	1	9/1/2011 5:23:00 PM
Dibenzo(a,h)anthracene	66	27.5	280	J	µg/Kg-dry	1	9/1/2011 5:23:00 PM
Dibenzofuran	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-5C (0-11 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 9:35:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-26A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
Diethyl phthalate	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Dimethyl phthalate	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Di-n-butyl phthalate	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Di-n-octyl phthalate	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Fluoranthene	460	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Fluorene	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Hexachlorobenzene	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Hexachlorobutadiene	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Hexachlorocyclopentadiene	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Hexachloroethane	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Indeno(1,2,3-c,d)pyrene	160	27.5	280	J	µg/Kg-dry	1	9/1/2011 5:23:00 PM
Isophorone	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Naphthalene	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Nitrobenzene	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
N-Nitrosodimethylamine	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
N-Nitrosodi-n-propylamine	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
N-Nitrosodiphenylamine	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Parathion	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Pentachlorophenol	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Phenanthrene	340	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Phenol	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Pyrene	450	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Pyridine	U	27.5	280		µg/Kg-dry	1	9/1/2011 5:23:00 PM
Surr: 2,4,6-Tribromophenol	55.2	0	21-119		%REC	1	9/1/2011 5:23:00 PM
Surr: 2-Fluorobiphenyl	71.7	0	21-117		%REC	1	9/1/2011 5:23:00 PM
Surr: 2-Fluorophenol	31.3	0	11-105		%REC	1	9/1/2011 5:23:00 PM
Surr: 4-Terphenyl-d14	80.0	0	21-132		%REC	1	9/1/2011 5:23:00 PM
Surr: Nitrobenzene-d5	55.6	0	18-116		%REC	1	9/1/2011 5:23:00 PM
Surr: Phenol-d6	29.3	0	12-110		%REC	1	9/1/2011 5:23:00 PM
CYANIDE, TOTAL			**SW9012A**		**SW9012A**		Analyst: **STP**
Cyanide, Total & Amenable: Auto Colorimetric	0.215	0.06	0.111		mg/Kg-dry	1	9/6/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-5C (0-11 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 9:35:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-26A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
HEXAVALENT CHROMIUM			**SW7196A**				Analyst: **AB**
Chromium, Hexavalent	U	0.22	0.444		mg/Kg-dry	1	9/6/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-5C (0-11 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 9:35:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-26B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP MERCURY			**SW1311/7471B**		**SW1311**		Analyst: **AB**
Mercury	U	0.0005	0.0200		mg/L	1	9/2/2011 10:37:29 AM
TCLP HERBICIDES SW-846 8151			**SW8151A**		**SW3510C**		Analyst: **SB**
2,4,5-TP	U	0.0002	0.0050		mg/L	1	9/7/2011 8:47:00 PM
2,4-D	U	0.0002	0.0050		mg/L	1	9/7/2011 8:47:00 PM
Surr: 2,4-DCAA	81.9	0	21-144		%REC	1	9/7/2011 8:47:00 PM
TCLP PESTICIDES SW-846 8081			**SW8081B**		**SW3510C**		Analyst: **SB**
Chlordane	0.00053	0.0005	0.0010	J	mg/L	1	9/7/2011 4:16:00 PM
Endrin	U	0.0002	0.0010		mg/L	1	9/7/2011 4:16:00 PM
gamma-BHC	U	0.0002	0.0010		mg/L	1	9/7/2011 4:16:00 PM
Heptachlor	U	0.0002	0.0010		mg/L	1	9/7/2011 4:16:00 PM
Heptachlor epoxide	U	0.0002	0.0010		mg/L	1	9/7/2011 4:16:00 PM
Methoxychlor	U	0.0002	0.0010		mg/L	1	9/7/2011 4:16:00 PM
Toxaphene	U	0.002	0.010		mg/L	1	9/7/2011 4:16:00 PM
Surr: DCB	90.1	0	28-146		%REC	1	9/7/2011 4:16:00 PM
Surr: TCX	88.2	0	25-147		%REC	1	9/7/2011 4:16:00 PM
TCLP METALS			**SW1311/6010C**		**SW1311**		Analyst: **JP**
Arsenic	U	0.01	0.0500		mg/L	1	9/1/2011 3:36:36 PM
Barium	U	1	5.00		mg/L	1	9/1/2011 3:36:36 PM
Cadmium	0.0150	0.005	0.0500	J	mg/L	1	9/1/2011 3:36:36 PM
Chromium	U	0.005	0.0500		mg/L	1	9/1/2011 3:36:36 PM
Lead	5.21	0.005	0.0500	*	mg/L	1	9/1/2011 3:36:36 PM
Selenium	U	0.01	0.0500		mg/L	1	9/1/2011 3:36:36 PM
Silver	U	0.005	0.0500		mg/L	1	9/1/2011 3:36:36 PM
TCLP SEMIVOLATILES SW-846 8270			**SW8270D**		**SW3510C**		Analyst: **LDS**
2,4,5-Trichlorophenol	U	0.005	0.050		mg/L	1	9/7/2011 10:12:00 AM
2,4,6-Trichlorophenol	U	0.005	0.085		mg/L	1	9/7/2011 10:12:00 AM
2,4-Dinitrotoluene	U	0.005	0.045		mg/L	1	9/7/2011 10:12:00 AM
2-Methylphenol	U	0.005	0.035		mg/L	1	9/7/2011 10:12:00 AM
3+4-Methylphenol	U	0.005	0.040		mg/L	1	9/7/2011 10:12:00 AM
Hexachlorobenzene	U	0.005	0.090		mg/L	1	9/7/2011 10:12:00 AM
Hexachlorobutadiene	U	0.005	0.15		mg/L	1	9/7/2011 10:12:00 AM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-5C (0-11 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 9:35:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-26B		

Certificate of Results

Analyses	Sample Result		LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP SEMIVOLATILES SW-846 8270				**SW8270D**		**SW3510C**		Analyst: **LDS**
Hexachloroethane	U		0.005	0.040		mg/L	1	9/7/2011 10:12:00 AM
Nitrobenzene	U		0.005	0.035		mg/L	1	9/7/2011 10:12:00 AM
Pentachlorophenol	U		0.05	0.17		mg/L	1	9/7/2011 10:12:00 AM
Pyridine	U		0.05	0.12		mg/L	1	9/7/2011 10:12:00 AM
Surr: 2,4,6-Tribromophenol	71.8		0	36-133		%REC	1	9/7/2011 10:12:00 AM
Surr: 2-Fluorobiphenyl	104		0	20-131		%REC	1	9/7/2011 10:12:00 AM
Surr: 2-Fluorophenol	83.5		0	22-128		%REC	1	9/7/2011 10:12:00 AM
Surr: 4-Terphenyl-d14	104		0	22-132		%REC	1	9/7/2011 10:12:00 AM
Surr: Nitrobenzene-d5	78.5		0	19-133		%REC	1	9/7/2011 10:12:00 AM
Surr: Phenol-d6	56.0		0	18-128		%REC	1	9/7/2011 10:12:00 AM
TCLP VOLATILES				**SW8260C**				Analyst: **LA**
1,1-Dichloroethene	U		0.01	0.020		mg/L	20	9/1/2011 2:49:00 PM
1,2-Dichloroethane	U		0.01	0.020		mg/L	20	9/1/2011 2:49:00 PM
1,4-Dichlorobenzene	U		0.01	0.020		mg/L	20	9/1/2011 2:49:00 PM
2-Butanone	U		0.02	0.040		mg/L	20	9/1/2011 2:49:00 PM
Benzene	U		0.01	0.020		mg/L	20	9/1/2011 2:49:00 PM
Carbon tetrachloride	U		0.01	0.020		mg/L	20	9/1/2011 2:49:00 PM
Chlorobenzene	U		0.01	0.020		mg/L	20	9/1/2011 2:49:00 PM
Chloroform	U		0.01	0.020		mg/L	20	9/1/2011 2:49:00 PM
Tetrachloroethene	U		0.01	0.020		mg/L	20	9/1/2011 2:49:00 PM
Trichloroethene	U		0.01	0.020		mg/L	20	9/1/2011 2:49:00 PM
Vinyl chloride	U		0.01	0.020		mg/L	20	9/1/2011 2:49:00 PM
Surr: 4-Bromofluorobenzene	96.7		0	63-123		%REC	20	9/1/2011 2:49:00 PM
Surr: Dibromofluoromethane	104		0	68-124		%REC	20	9/1/2011 2:49:00 PM
Surr: Toluene-d8	98.2		0	67-125		%REC	20	9/1/2011 2:49:00 PM
TRIVALENT CHROMIUM				**SW6010C**				Analyst: **JP**
Chromium, Trivalent	15.5		0.1	0.392		mg/Kg-dry	1	9/2/2011
IGNITABILITY/FLASHPOINT SW-846 1020				**SW1020B**				Analyst: **STP**
Ignitability	>		0	140		°F	1	9/1/2011
SOIL PH MEASURED IN WATER				**SW9045C**				Analyst: **AB**
pH	7.80		0	1.00	H	pH Units	1	9/1/2011 1:44:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-5C (0-11 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 9:35:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-26B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TEMPERATURE			**M2550 B**				Analyst: **AB**
Temp at which pH was measured	21.0	0	0		°C	1	9/1/2011 1:44:00 PM
REACTIVE CYANIDE			**SW7.3.3.2**				Analyst: **STP**
Reactive Cyanide	U	0.06	0.111		mg/Kg-dry	1	9/8/2011
REACTIVE SULFIDE			**SW7.3.4.2**				Analyst: **STP**
Reactive Sulfide	U	1.11	2.22		mg/Kg-dry	1	9/8/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-5Ca (0-11 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 9:37:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-27A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TOTAL DRO AS #2 FUEL (C8-C40)			**SW8015C**	**SW3550C**			Analyst: **LDS**
Total DRO TPH	39	3.03	12		mg/Kg-dry	1	9/2/2011 5:35:00 PM
Surr: o-Terphenyl	33.8	0	31-137		%REC	1	9/2/2011 5:35:00 PM
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	20.2	0	0		wt%	1	9/1/2011

Qualifiers:	B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
	E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
	J	Analyte detected below quantitation limits	LOD	Limit of Detection
	LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
	PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
	U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-6G (4 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:07:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-28A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PERCENT MOISTURE			D2216				Analyst: KK
Percent Moisture	9.49	0	0		wt%	1	9/1/2011
VOLATILE SW-846 METHOD 8260			SW8260C				Analyst: LA
1,1,1,2-Tetrachloroethane	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
1,1,1-Trichloroethane	U	0.62	6.2	C	µg/Kg-dry	1	8/31/2011 10:25:00 PM
1,1,2,2-Tetrachloroethane	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
1,1,2-Trichloro-1,2,2-trifluoroethan	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
1,1,2-Trichloroethane	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
1,1-Dichloroethane	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
1,1-Dichloroethene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
1,1-Dichloropropene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
1,2,3-Trichlorobenzene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
1,2,3-Trichloropropane	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
1,2,4,5-Tetramethylbenzene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
1,2,4-Trichlorobenzene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
1,2,4-Trimethylbenzene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
1,2-Dibromo-3-chloropropane	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
1,2-Dibromoethane	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
1,2-Dichlorobenzene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
1,2-Dichloroethane	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
1,2-Dichloropropane	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
1,3,5-Trimethylbenzene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
1,3-Dichlorobenzene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
1,3-dichloropropane	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
1,4-Dichlorobenzene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
1,4-Dioxane	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
2,2-Dichloropropane	U	0.62	6.2	C	µg/Kg-dry	1	8/31/2011 10:25:00 PM
2-Butanone	U	1.9	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
2-Chloroethyl vinyl ether	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
2-Chlorotoluene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
2-Hexanone	U	1.9	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
2-Propanol	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
4-Chlorotoluene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-6G (4 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:07:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-28A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: **LA**
4-Isopropyltoluene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
4-Methyl-2-pentanone	U	1.9	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Acetone	U	1.9	6.2	C	µg/Kg-dry	1	8/31/2011 10:25:00 PM
Acrolein	U	3.1	12	C	µg/Kg-dry	1	8/31/2011 10:25:00 PM
Acrylonitrile	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Benzene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Bromobenzene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Bromochloromethane	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Bromodichloromethane	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Bromoform	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Bromomethane	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Carbon disulfide	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Carbon tetrachloride	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Chlorobenzene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Chlorodifluoromethane	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Chloroethane	U	0.62	6.2	C	µg/Kg-dry	1	8/31/2011 10:25:00 PM
Chloroform	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Chloromethane	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
cis-1,2-Dichloroethene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
cis-1,3-Dichloropropene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Dibromochloromethane	U	0.62	6.2	C	µg/Kg-dry	1	8/31/2011 10:25:00 PM
Dibromomethane	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Dichlorodifluoromethane	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Diisopropyl ether	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Ethanol	U	3.1	12		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Ethyl acetate	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Ethylbenzene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Freon-114	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Hexachlorobutadiene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Isopropyl acetate	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Isopropylbenzene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
m,p-Xylene	U	1.2	12		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Methyl Acetate	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-6G (4 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:07:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-28A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: **LA**
Methyl tert-butyl ether	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Methylene chloride	14	0.62	6.2	B	µg/Kg-dry	1	8/31/2011 10:25:00 PM
n-Amyl acetate	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Naphthalene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
n-Butyl acetate	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
n-Butylbenzene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
n-Propyl acetate	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
n-Propylbenzene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
o-Xylene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
p-Diethylbenzene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
p-Ethyltoluene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
sec-Butylbenzene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Styrene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
t-Butyl alcohol	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
tert-Butylbenzene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Tetrachloroethene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Toluene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
trans-1,2-Dichloroethene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
trans-1,3-Dichloropropene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Trichloroethene	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Trichlorofluoromethane	U	0.62	6.2	C	µg/Kg-dry	1	8/31/2011 10:25:00 PM
Vinyl acetate	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Vinyl chloride	U	0.62	6.2		µg/Kg-dry	1	8/31/2011 10:25:00 PM
Surr: 4-Bromofluorobenzene	93.5	0	42-133		%REC	1	8/31/2011 10:25:00 PM
Surr: Dibromofluoromethane	101	0	50-133		%REC	1	8/31/2011 10:25:00 PM
Surr: Toluene-d8	97.7	0	53-130		%REC	1	8/31/2011 10:25:00 PM

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-6C (0-8 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:02:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-29A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
MERCURY			**SW7471B**		**SW7471B**		Analyst: **AB**
Mercury	0.211	0.005	0.00929		mg/Kg-dry	1	9/2/2011 11:29:29 AM
TOTAL DRO AS #2 FUEL (C8-C40)			**SW8015C**		**SW3550C**		Analyst: **LDS**
Total DRO TPH	14	2.7	11		mg/Kg-dry	1	9/1/2011 5:20:00 PM
Surr: o-Terphenyl	30.3	0	31-137	S	%REC	1	9/1/2011 5:20:00 PM
HERBICIDES SW-846 8151			**SW8151A**		**SW8151**		Analyst: **SB**
2,4,5-T	U	1.08	11		µg/Kg-dry	1	9/8/2011 4:10:00 PM
2,4,5-TP	2.3	1.08	11	J	µg/Kg-dry	1	9/8/2011 4:10:00 PM
2,4-D	U	1.08	11		µg/Kg-dry	1	9/8/2011 4:10:00 PM
Surr: 2,4-DCAA	69.6	0	14-148		%REC	1	9/8/2011 4:10:00 PM
PCB'S AS AROCLORS SW-846 METHOD 8082			**SW8082A**		**SW3550C**		Analyst: **SB**
Aroclor 1016	U	1.08	43		µg/Kg-dry	1	9/1/2011 10:02:00 PM
Aroclor 1221	U	1.08	43		µg/Kg-dry	1	9/1/2011 10:02:00 PM
Aroclor 1232	U	1.08	43		µg/Kg-dry	1	9/1/2011 10:02:00 PM
Aroclor 1242	U	1.08	43		µg/Kg-dry	1	9/1/2011 10:02:00 PM
Aroclor 1248	U	1.08	43		µg/Kg-dry	1	9/1/2011 10:02:00 PM
Aroclor 1254	U	1.08	43		µg/Kg-dry	1	9/1/2011 10:02:00 PM
Aroclor 1260	U	1.08	43		µg/Kg-dry	1	9/1/2011 10:02:00 PM
Aroclor 1262	U	1.08	43		µg/Kg-dry	1	9/1/2011 10:02:00 PM
Aroclor 1268	U	1.08	43		µg/Kg-dry	1	9/1/2011 10:02:00 PM
Surr: TCX	51.1	0	17-151		%REC	1	9/1/2011 10:02:00 PM
Surr: DCB	63.6	0	16-152		%REC	1	9/1/2011 10:02:00 PM
PESTICIDES SW-846 METHOD 8081			**SW8081B**		**SW3550C**		Analyst: **SB**
4,4'-DDD	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:37:00 PM
4,4'-DDE	0.52	0.22	2.2	JP	µg/Kg-dry	1	9/2/2011 3:37:00 PM
4,4'-DDT	1.1	0.22	2.2	J	µg/Kg-dry	1	9/2/2011 3:37:00 PM
Aldrin	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:37:00 PM
alpha-BHC	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:37:00 PM
beta-BHC	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:37:00 PM
Chlordane	U	1.08	2.2		µg/Kg-dry	1	9/2/2011 3:37:00 PM
Chlorobenzilate	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:37:00 PM
DBCP	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:37:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.	

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-6C (0-8 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:02:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-29A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PESTICIDES SW-846 METHOD 8081			**SW8081B**		**SW3550C**		Analyst: **SB**
delta-BHC	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:37:00 PM
Dieldrin	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:37:00 PM
Endosulfan I	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:37:00 PM
Endosulfan II	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:37:00 PM
Endosulfan sulfate	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:37:00 PM
Endrin	0.39	0.22	2.2	J	µg/Kg-dry	1	9/2/2011 3:37:00 PM
Endrin aldehyde	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:37:00 PM
Endrin ketone	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:37:00 PM
gamma-BHC	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:37:00 PM
Heptachlor	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:37:00 PM
Heptachlor epoxide	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:37:00 PM
Hexachlorobenzene	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:37:00 PM
Hexachlorocyclopentadiene	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:37:00 PM
Methoxychlor	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:37:00 PM
Toxaphene	U	5.4	11		µg/Kg-dry	1	9/2/2011 3:37:00 PM
Surr: DCB	60.5	0	23-157		%REC	1	9/2/2011 3:37:00 PM
Surr: TCX	41.2	0	21-151		%REC	1	9/2/2011 3:37:00 PM
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	8.02	0	0		wt%	1	9/1/2011
TARGET ANALYTE LIST METALS			**SW6010C**		**SW3050B**		Analyst: **JP**
Aluminum	13500	1.05	4.21		mg/Kg-dry	10	9/2/2011 1:01:08 PM
Antimony	0.337	0.21	0.527	J	mg/Kg-dry	1	9/2/2011 10:30:13 AM
Arsenic	3.16	0.21	0.527		mg/Kg-dry	1	9/2/2011 10:30:13 AM
Barium	129	0.21	0.421		mg/Kg-dry	1	9/2/2011 10:30:13 AM
Beryllium	U	0.11	0.421		mg/Kg-dry	1	9/2/2011 10:30:13 AM
Cadmium	U	0.11	0.421		mg/Kg-dry	1	9/2/2011 10:30:13 AM
Calcium	2390	0.21	0.527		mg/Kg-dry	1	9/2/2011 10:30:13 AM
Chromium	26.9	0.11	0.421		mg/Kg-dry	1	9/2/2011 10:30:13 AM
Cobalt	U	0.11	0.421		mg/Kg-dry	1	9/2/2011 10:30:13 AM
Copper	49.3	0.11	0.421		mg/Kg-dry	1	9/2/2011 10:30:13 AM
Iron	19400	2.11	4.21		mg/Kg-dry	10	9/2/2011 1:01:08 PM
Lead	54.9	0.21	0.421		mg/Kg-dry	1	9/2/2011 10:30:13 AM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-6C (0-8 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:02:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-29A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TARGET ANALYTE LIST METALS			**SW6010C**		**SW3050B**		Analyst: **JP**
Magnesium	5410	0.11	0.421		mg/Kg-dry	1	9/2/2011 10:30:13 AM
Manganese	257	0.11	0.421		mg/Kg-dry	1	9/2/2011 10:30:13 AM
Nickel	20.1	0.11	0.421		mg/Kg-dry	1	9/2/2011 10:30:13 AM
Potassium	4160	0.21	0.527		mg/Kg-dry	1	9/2/2011 10:30:13 AM
Selenium	U	0.21	0.527		mg/Kg-dry	1	9/2/2011 10:30:13 AM
Silver	U	0.11	0.421		mg/Kg-dry	1	9/2/2011 10:30:13 AM
Sodium	182	0.21	0.527		mg/Kg-dry	1	9/2/2011 10:30:13 AM
Thallium	U	0.32	0.527		mg/Kg-dry	1	9/2/2011 10:30:13 AM
Vanadium	49.2	0.11	0.421		mg/Kg-dry	1	9/2/2011 10:30:13 AM
Zinc	122	0.11	0.421		mg/Kg-dry	1	9/2/2011 10:30:13 AM
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
1,2,4-Trichlorobenzene	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
1,2-Dichlorobenzene	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
1,3-Dichlorobenzene	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
1,4-Dichlorobenzene	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
2,4,5-Trichlorophenol	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
2,4,6-Trichlorophenol	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
2,4-Dichlorophenol	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
2,4-Dimethylphenol	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
2,4-Dinitrophenol	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
2,4-Dinitrotoluene	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
2,6-Dinitrotoluene	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
2-Chloronaphthalene	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
2-Chlorophenol	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
2-Methylnaphthalene	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
2-Methylphenol	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
2-Nitroaniline	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
2-Nitrophenol	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
3,3'-Dichlorobenzidine	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
3+4-Methylphenol	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
3-Nitroaniline	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
4,6-Dinitro-2-methylphenol	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-6C (0-8 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:02:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-29A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
4-Bromophenyl phenyl ether	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
4-Chloro-3-methylphenol	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
4-Chloroaniline	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
4-Chlorophenyl phenyl ether	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
4-Nitroaniline	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
4-Nitrophenol	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Acenaphthene	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Acenaphthylene	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Acetophenone	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Aniline	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Anthracene	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Atrazine	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Azobenzene	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Benzaldehyde	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Benzidine	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Benzo(a)anthracene	49	27	270	J	µg/Kg-dry	1	9/1/2011 5:48:00 PM
Benzo(a)pyrene	48	27	270	J	µg/Kg-dry	1	9/1/2011 5:48:00 PM
Benzo(b)fluoranthene	44	27	270	J	µg/Kg-dry	1	9/1/2011 5:48:00 PM
Benzo(g,h,i)perylene	27	27	270	J	µg/Kg-dry	1	9/1/2011 5:48:00 PM
Benzo(k)fluoranthene	33	27	270	J	µg/Kg-dry	1	9/1/2011 5:48:00 PM
Benzoic acid	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Benzyl alcohol	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Biphenyl	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Bis(2-chloroethoxy)methane	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Bis(2-chloroethyl)ether	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Bis(2-chloroisopropyl)ether	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Bis(2-ethylhexyl)phthalate	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Butyl benzyl phthalate	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Caprolactam	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Carbazole	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Chrysene	56	27	270	J	µg/Kg-dry	1	9/1/2011 5:48:00 PM
Dibenzo(a,h)anthracene	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Dibenzofuran	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-6C (0-8 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:02:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-29A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
Diethyl phthalate	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Dimethyl phthalate	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Di-n-butyl phthalate	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Di-n-octyl phthalate	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Fluoranthene	96	27	270	J	µg/Kg-dry	1	9/1/2011 5:48:00 PM
Fluorene	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Hexachlorobenzene	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Hexachlorobutadiene	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Hexachlorocyclopentadiene	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Hexachloroethane	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Indeno(1,2,3-c,d)pyrene	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Isophorone	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Naphthalene	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Nitrobenzene	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
N-Nitrosodimethylamine	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
N-Nitrosodi-n-propylamine	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
N-Nitrosodiphenylamine	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Parathion	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Pentachlorophenol	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Phenanthrene	76	27	270	J	µg/Kg-dry	1	9/1/2011 5:48:00 PM
Phenol	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Pyrene	94	27	270	J	µg/Kg-dry	1	9/1/2011 5:48:00 PM
Pyridine	U	27	270		µg/Kg-dry	1	9/1/2011 5:48:00 PM
Surr: 2,4,6-Tribromophenol	63.7	0	21-119		%REC	1	9/1/2011 5:48:00 PM
Surr: 2-Fluorobiphenyl	86.6	0	21-117		%REC	1	9/1/2011 5:48:00 PM
Surr: 2-Fluorophenol	37.4	0	11-105		%REC	1	9/1/2011 5:48:00 PM
Surr: 4-Terphenyl-d14	96.5	0	21-132		%REC	1	9/1/2011 5:48:00 PM
Surr: Nitrobenzene-d5	64.3	0	18-116		%REC	1	9/1/2011 5:48:00 PM
Surr: Phenol-d6	37.8	0	12-110		%REC	1	9/1/2011 5:48:00 PM
CYANIDE, TOTAL			**SW9012A**		**SW9012A**		Analyst: **STP**
Cyanide, Total & Amenable: Auto Colorimetric	0.244	0.05	0.109		mg/Kg-dry	1	9/6/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-6C (0-8 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:02:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-29A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
HEXAVALENT CHROMIUM			**SW7196A**				Analyst: **AB**
Chromium, Hexavalent	U	0.22	0.435		mg/Kg-dry	1	9/6/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-6C (0-8 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:02:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-29B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP MERCURY			**SW1311/7471B**		**SW1311**		Analyst: **AB**
Mercury	U	0.0005	0.0200		mg/L	1	9/2/2011 10:39:36 AM
TCLP HERBICIDES SW-846 8151			**SW8151A**		**SW3510C**		Analyst: **SB**
2,4,5-TP	U	0.0002	0.0050		mg/L	1	9/7/2011 9:02:00 PM
2,4-D	U	0.0002	0.0050		mg/L	1	9/7/2011 9:02:00 PM
Surr: 2,4-DCAA	104	0	21-144		%REC	1	9/7/2011 9:02:00 PM
TCLP PESTICIDES SW-846 8081			**SW8081B**		**SW3510C**		Analyst: **SB**
Chlordane	U	0.0005	0.0010		mg/L	1	9/7/2011 4:31:00 PM
Endrin	U	0.0002	0.0010		mg/L	1	9/7/2011 4:31:00 PM
gamma-BHC	U	0.0002	0.0010		mg/L	1	9/7/2011 4:31:00 PM
Heptachlor	U	0.0002	0.0010		mg/L	1	9/7/2011 4:31:00 PM
Heptachlor epoxide	U	0.0002	0.0010		mg/L	1	9/7/2011 4:31:00 PM
Methoxychlor	U	0.0002	0.0010		mg/L	1	9/7/2011 4:31:00 PM
Toxaphene	U	0.002	0.010		mg/L	1	9/7/2011 4:31:00 PM
Surr: DCB	90.6	0	28-146		%REC	1	9/7/2011 4:31:00 PM
Surr: TCX	89.7	0	25-147		%REC	1	9/7/2011 4:31:00 PM
TCLP METALS			**SW1311/6010C**		**SW1311**		Analyst: **JP**
Arsenic	U	0.01	0.0500		mg/L	1	9/1/2011 3:38:39 PM
Barium	1.50	1	5.00	J	mg/L	1	9/1/2011 3:38:39 PM
Cadmium	U	0.005	0.0500		mg/L	1	9/1/2011 3:38:39 PM
Chromium	U	0.005	0.0500		mg/L	1	9/1/2011 3:38:39 PM
Lead	0.0540	0.005	0.0500		mg/L	1	9/1/2011 3:38:39 PM
Selenium	U	0.01	0.0500		mg/L	1	9/1/2011 3:38:39 PM
Silver	U	0.005	0.0500		mg/L	1	9/1/2011 3:38:39 PM
TCLP SEMIVOLATILES SW-846 8270			**SW8270D**		**SW3510C**		Analyst: **LDS**
2,4,5-Trichlorophenol	U	0.005	0.050		mg/L	1	9/7/2011 10:37:00 AM
2,4,6-Trichlorophenol	U	0.005	0.085		mg/L	1	9/7/2011 10:37:00 AM
2,4-Dinitrotoluene	U	0.005	0.045		mg/L	1	9/7/2011 10:37:00 AM
2-Methylphenol	U	0.005	0.035		mg/L	1	9/7/2011 10:37:00 AM
3+4-Methylphenol	U	0.005	0.040		mg/L	1	9/7/2011 10:37:00 AM
Hexachlorobenzene	U	0.005	0.090		mg/L	1	9/7/2011 10:37:00 AM
Hexachlorobutadiene	U	0.005	0.15		mg/L	1	9/7/2011 10:37:00 AM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-6C (0-8 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:02:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-29B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP SEMIVOLATILES SW-846 8270			**SW8270D**		**SW3510C**		Analyst: **LDS**
Hexachloroethane	U	0.005	0.040		mg/L	1	9/7/2011 10:37:00 AM
Nitrobenzene	U	0.005	0.035		mg/L	1	9/7/2011 10:37:00 AM
Pentachlorophenol	U	0.05	0.17		mg/L	1	9/7/2011 10:37:00 AM
Pyridine	U	0.05	0.12		mg/L	1	9/7/2011 10:37:00 AM
Surr: 2,4,6-Tribromophenol	70.9	0	36-133		%REC	1	9/7/2011 10:37:00 AM
Surr: 2-Fluorobiphenyl	99.2	0	20-131		%REC	1	9/7/2011 10:37:00 AM
Surr: 2-Fluorophenol	81.0	0	22-128		%REC	1	9/7/2011 10:37:00 AM
Surr: 4-Terphenyl-d14	104	0	22-132		%REC	1	9/7/2011 10:37:00 AM
Surr: Nitrobenzene-d5	79.9	0	19-133		%REC	1	9/7/2011 10:37:00 AM
Surr: Phenol-d6	55.4	0	18-128		%REC	1	9/7/2011 10:37:00 AM
TCLP VOLATILES			**SW8260C**				Analyst: **LA**
1,1-Dichloroethene	U	0.01	0.020		mg/L	20	9/1/2011 3:13:00 PM
1,2-Dichloroethane	U	0.01	0.020		mg/L	20	9/1/2011 3:13:00 PM
1,4-Dichlorobenzene	U	0.01	0.020		mg/L	20	9/1/2011 3:13:00 PM
2-Butanone	U	0.02	0.040		mg/L	20	9/1/2011 3:13:00 PM
Benzene	U	0.01	0.020		mg/L	20	9/1/2011 3:13:00 PM
Carbon tetrachloride	U	0.01	0.020		mg/L	20	9/1/2011 3:13:00 PM
Chlorobenzene	U	0.01	0.020		mg/L	20	9/1/2011 3:13:00 PM
Chloroform	U	0.01	0.020		mg/L	20	9/1/2011 3:13:00 PM
Tetrachloroethene	U	0.01	0.020		mg/L	20	9/1/2011 3:13:00 PM
Trichloroethene	U	0.01	0.020		mg/L	20	9/1/2011 3:13:00 PM
Vinyl chloride	U	0.01	0.020		mg/L	20	9/1/2011 3:13:00 PM
Surr: 4-Bromofluorobenzene	97.2	0	63-123		%REC	20	9/1/2011 3:13:00 PM
Surr: Dibromofluoromethane	109	0	68-124		%REC	20	9/1/2011 3:13:00 PM
Surr: Toluene-d8	96.6	0	67-125		%REC	20	9/1/2011 3:13:00 PM
TRIVALENT CHROMIUM			**SW6010C**				Analyst: **JP**
Chromium, Trivalent	26.9	0.11	0.421		mg/Kg-dry	1	9/2/2011
IGNITABILITY/FLASHPOINT SW-846 1020			**SW1020B**				Analyst: **STP**
Ignitability	>	0	140		°F	1	9/1/2011
SOIL PH MEASURED IN WATER			**SW9045C**				Analyst: **AB**
pH	7.90	0	1.00	H	pH Units	1	9/1/2011 1:48:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-6C (0-8 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:02:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-29B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TEMPERATURE			**M2550 B**				Analyst: **AB**
Temp at which pH was measured	21.0	0	0		°C	1	9/1/2011 1:48:00 PM
REACTIVE CYANIDE			**SW7.3.3.2**				Analyst: **STP**
Reactive Cyanide	U	0.05	0.109		mg/Kg-dry	1	9/8/2011
REACTIVE SULFIDE			**SW7.3.4.2**				Analyst: **STP**
Reactive Sulfide	U	1.09	2.17		mg/Kg-dry	1	9/8/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-6Ca (0-8 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 10:04:00 AM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-30A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TOTAL DRO AS #2 FUEL (C8-C40)			**SW8015C**		**SW3550C**		Analyst: **LDS**
Total DRO TPH	3.7	3.06	12	J	mg/Kg-dry	1	9/2/2011 6:00:00 PM
Surr: o-Terphenyl	34.2	0	31-137		%REC	1	9/2/2011 6:00:00 PM
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	21.0	0	0		wt%	1	9/1/2011

Qualifiers:	B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
	E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
	J	Analyte detected below quantitation limits	LOD	Limit of Detection
	LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
	PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
	U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-7G (5 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 2:10:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-31A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PERCENT MOISTURE			D2216				Analyst: KK
Percent Moisture	11.0	0	0		wt%	1	9/1/2011
VOLATILE SW-846 METHOD 8260			SW8260C				Analyst: LA
1,1,1,2-Tetrachloroethane	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
1,1,1-Trichloroethane	U	0.55	5.5	C	µg/Kg-dry	1	8/31/2011 10:49:00 PM
1,1,2,2-Tetrachloroethane	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
1,1,2-Trichloro-1,2,2-trifluoroethan	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
1,1,2-Trichloroethane	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
1,1-Dichloroethane	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
1,1-Dichloroethene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
1,1-Dichloropropene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
1,2,3-Trichlorobenzene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
1,2,3-Trichloropropane	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
1,2,4,5-Tetramethylbenzene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
1,2,4-Trichlorobenzene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
1,2,4-Trimethylbenzene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
1,2-Dibromo-3-chloropropane	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
1,2-Dibromoethane	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
1,2-Dichlorobenzene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
1,2-Dichloroethane	U	0.55	5.5	C	µg/Kg-dry	1	8/31/2011 10:49:00 PM
1,2-Dichloropropane	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
1,3,5-Trimethylbenzene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
1,3-Dichlorobenzene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
1,3-dichloropropane	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
1,4-Dichlorobenzene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
1,4-Dioxane	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
2,2-Dichloropropane	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
2-Butanone	U	1.7	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
2-Chloroethyl vinyl ether	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
2-Chlorotoluene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
2-Hexanone	U	1.7	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
2-Propanol	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
4-Chlorotoluene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-7G (5 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 2:10:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-31A		

Certificate of Results

Analyses	Sample Result		LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
VOLATILE SW-846 METHOD 8260				**SW8260C**				Analyst: LA
4-Isopropyltoluene	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
4-Methyl-2-pentanone	U		1.7	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Acetone	U		1.7	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Acrolein	U		2.8	11		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Acrylonitrile	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Benzene	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Bromobenzene	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Bromochloromethane	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Bromodichloromethane	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Bromoform	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Bromomethane	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Carbon disulfide	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Carbon tetrachloride	U		0.55	5.5	C	µg/Kg-dry	1	8/31/2011 10:49:00 PM
Chlorobenzene	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Chlorodifluoromethane	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Chloroethane	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Chloroform	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Chloromethane	U		0.55	5.5	C	µg/Kg-dry	1	8/31/2011 10:49:00 PM
cis-1,2-Dichloroethene	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
cis-1,3-Dichloropropene	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Dibromochloromethane	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Dibromomethane	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Dichlorodifluoromethane	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Diisopropyl ether	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Ethanol	U		2.8	11		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Ethyl acetate	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Ethylbenzene	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Freon-114	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Hexachlorobutadiene	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Isopropyl acetate	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Isopropylbenzene	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
m,p-Xylene	U		1.1	11		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Methyl Acetate	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-7G (5 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 2:10:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-31A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: **LA**
Methyl tert-butyl ether	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Methylene chloride	11	0.55	5.5	B	µg/Kg-dry	1	8/31/2011 10:49:00 PM
n-Amyl acetate	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Naphthalene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
n-Butyl acetate	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
n-Butylbenzene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
n-Propyl acetate	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
n-Propylbenzene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
o-Xylene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
p-Diethylbenzene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
p-Ethyltoluene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
sec-Butylbenzene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Styrene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
t-Butyl alcohol	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
tert-Butylbenzene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Tetrachloroethene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Toluene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
trans-1,2-Dichloroethene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
trans-1,3-Dichloropropene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Trichloroethene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Trichlorofluoromethane	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Vinyl acetate	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Vinyl chloride	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 10:49:00 PM
Surr: 4-Bromofluorobenzene	92.0	0	42-133		%REC	1	8/31/2011 10:49:00 PM
Surr: Dibromofluoromethane	99.9	0	50-133		%REC	1	8/31/2011 10:49:00 PM
Surr: Toluene-d8	98.6	0	53-130		%REC	1	8/31/2011 10:49:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-7C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 2:00:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-32A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
MERCURY			**SW7471B**		**SW7471B**		Analyst: **AB**
Mercury	0.477	0.01	0.0194		mg/Kg-dry	2	9/2/2011 12:36:39 PM
TOTAL DRO AS #2 FUEL (C8-C40)			**SW8015C**		**SW3550C**		Analyst: **LDS**
Total DRO TPH	9.1	2.80	11	J	mg/Kg-dry	1	9/1/2011 5:46:00 PM
Surr: o-Terphenyl	31.1	0	31-137		%REC	1	9/1/2011 5:46:00 PM
HERBICIDES SW-846 8151			**SW8151A**		**SW8151**		Analyst: **SB**
2,4,5-T	1.4	1.11	11	J	µg/Kg-dry	1	9/8/2011 4:24:00 PM
2,4,5-TP	U	1.11	11		µg/Kg-dry	1	9/8/2011 4:24:00 PM
2,4-D	U	1.11	11		µg/Kg-dry	1	9/8/2011 4:24:00 PM
Surr: 2,4-DCAA	61.9	0	14-148		%REC	1	9/8/2011 4:24:00 PM
PCB'S AS AROCLORS SW-846 METHOD 8082			**SW8082A**		**SW3550C**		Analyst: **SB**
Aroclor 1016	U	1.12	45		µg/Kg-dry	1	9/1/2011 10:26:00 PM
Aroclor 1221	U	1.12	45		µg/Kg-dry	1	9/1/2011 10:26:00 PM
Aroclor 1232	U	1.12	45		µg/Kg-dry	1	9/1/2011 10:26:00 PM
Aroclor 1242	U	1.12	45		µg/Kg-dry	1	9/1/2011 10:26:00 PM
Aroclor 1248	U	1.12	45		µg/Kg-dry	1	9/1/2011 10:26:00 PM
Aroclor 1254	U	1.12	45		µg/Kg-dry	1	9/1/2011 10:26:00 PM
Aroclor 1260	U	1.12	45		µg/Kg-dry	1	9/1/2011 10:26:00 PM
Aroclor 1262	U	1.12	45		µg/Kg-dry	1	9/1/2011 10:26:00 PM
Aroclor 1268	U	1.12	45		µg/Kg-dry	1	9/1/2011 10:26:00 PM
Surr: TCX	53.1	0	17-151		%REC	1	9/1/2011 10:26:00 PM
Surr: DCB	71.4	0	16-152		%REC	1	9/1/2011 10:26:00 PM
PESTICIDES SW-846 METHOD 8081			**SW8081B**		**SW3550C**		Analyst: **SB**
4,4'-DDD	4.7	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:51:00 PM
4,4'-DDE	63	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:51:00 PM
4,4'-DDT	260	4.49	45		µg/Kg-dry	20	9/7/2011 10:27:00 PM
Aldrin	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:51:00 PM
alpha-BHC	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:51:00 PM
beta-BHC	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:51:00 PM
Chlordane	29	1.12	2.2		µg/Kg-dry	1	9/2/2011 3:51:00 PM
Chlorobenzilate	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:51:00 PM
DBCP	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:51:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.	

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-7C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 2:00:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-32A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PESTICIDES SW-846 METHOD 8081			**SW8081B**		**SW3550C**		Analyst: **SB**
delta-BHC	5.3	0.22	2.2	P	µg/Kg-dry	1	9/2/2011 3:51:00 PM
Dieldrin	1.9	0.22	2.2	J	µg/Kg-dry	1	9/2/2011 3:51:00 PM
Endosulfan I	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:51:00 PM
Endosulfan II	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:51:00 PM
Endosulfan sulfate	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:51:00 PM
Endrin	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:51:00 PM
Endrin aldehyde	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:51:00 PM
Endrin ketone	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:51:00 PM
gamma-BHC	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:51:00 PM
Heptachlor	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:51:00 PM
Heptachlor epoxide	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:51:00 PM
Hexachlorobenzene	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:51:00 PM
Hexachlorocyclopentadiene	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 3:51:00 PM
Methoxychlor	3.1	0.22	2.2	P	µg/Kg-dry	1	9/2/2011 3:51:00 PM
Toxaphene	U	5.61	11		µg/Kg-dry	1	9/2/2011 3:51:00 PM
Surr: DCB	97.2	0	23-157		%REC	20	9/7/2011 10:27:00 PM
Surr: DCB	62.6	0	23-157		%REC	1	9/2/2011 3:51:00 PM
Surr: TCX	56.4	0	21-151		%REC	20	9/7/2011 10:27:00 PM
Surr: TCX	45.5	0	21-151		%REC	1	9/2/2011 3:51:00 PM
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	11.2	0	0		wt%	1	9/1/2011
TARGET ANALYTE LIST METALS			**SW6010C**		**SW3050B**		Analyst: **JP**
Aluminum	4700	0.11	0.438		mg/Kg-dry	1	9/2/2011 10:05:31 AM
Antimony	0.241	0.22	0.547	J	mg/Kg-dry	1	9/2/2011 10:05:31 AM
Arsenic	6.33	0.22	0.547		mg/Kg-dry	1	9/2/2011 10:05:31 AM
Barium	125	0.22	0.438		mg/Kg-dry	1	9/2/2011 10:05:31 AM
Beryllium	U	0.11	0.438		mg/Kg-dry	1	9/2/2011 10:05:31 AM
Cadmium	0.350	0.11	0.438	J	mg/Kg-dry	1	9/2/2011 10:05:31 AM
Calcium	6280	0.22	0.547		mg/Kg-dry	1	9/2/2011 10:05:31 AM
Chromium	15.7	0.11	0.438		mg/Kg-dry	1	9/2/2011 10:05:31 AM
Cobalt	U	0.11	0.438		mg/Kg-dry	1	9/2/2011 10:05:31 AM
Copper	47.7	0.11	0.438		mg/Kg-dry	1	9/2/2011 10:05:31 AM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.	

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-7C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 2:00:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-32A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TARGET ANALYTE LIST METALS			**SW6010C**		**SW3050B**		Analyst: **JP**
Iron	16400	2.19	4.38		mg/Kg-dry	10	9/2/2011 12:25:00 PM
Lead	668	0.22	0.438		mg/Kg-dry	1	9/2/2011 10:05:31 AM
Magnesium	2090	0.11	0.438		mg/Kg-dry	1	9/2/2011 10:05:31 AM
Manganese	129	0.11	0.438		mg/Kg-dry	1	9/2/2011 10:05:31 AM
Nickel	12.2	0.11	0.438		mg/Kg-dry	1	9/2/2011 10:05:31 AM
Potassium	1100	0.22	0.547		mg/Kg-dry	1	9/2/2011 10:05:31 AM
Selenium	0.766	0.22	0.547		mg/Kg-dry	1	9/2/2011 10:05:31 AM
Silver	0.285	0.11	0.438	J	mg/Kg-dry	1	9/2/2011 10:05:31 AM
Sodium	140	0.22	0.547		mg/Kg-dry	1	9/2/2011 10:05:31 AM
Thallium	U	0.33	0.547		mg/Kg-dry	1	9/2/2011 10:05:31 AM
Vanadium	15.0	0.11	0.438		mg/Kg-dry	1	9/2/2011 10:05:31 AM
Zinc	185	0.11	0.438		mg/Kg-dry	1	9/2/2011 10:05:31 AM
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
1,2,4-Trichlorobenzene	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
1,2-Dichlorobenzene	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
1,3-Dichlorobenzene	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
1,4-Dichlorobenzene	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
2,4,5-Trichlorophenol	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
2,4,6-Trichlorophenol	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
2,4-Dichlorophenol	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
2,4-Dimethylphenol	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
2,4-Dinitrophenol	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
2,4-Dinitrotoluene	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
2,6-Dinitrotoluene	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
2-Chloronaphthalene	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
2-Chlorophenol	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
2-Methylnaphthalene	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
2-Methylphenol	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
2-Nitroaniline	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
2-Nitrophenol	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
3,3'-Dichlorobenzidine	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
3+4-Methylphenol	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-7C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 2:00:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-32A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
3-Nitroaniline	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
4,6-Dinitro-2-methylphenol	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
4-Bromophenyl phenyl ether	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
4-Chloro-3-methylphenol	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
4-Chloroaniline	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
4-Chlorophenyl phenyl ether	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
4-Nitroaniline	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
4-Nitrophenol	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Acenaphthene	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Acenaphthylene	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Acetophenone	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Aniline	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Anthracene	190	28.0	280	J	µg/Kg-dry	1	9/1/2011 6:13:00 PM
Atrazine	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Azobenzene	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Benzaldehyde	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Benzidine	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Benzo(a)anthracene	210	28.0	280	J	µg/Kg-dry	1	9/1/2011 6:13:00 PM
Benzo(a)pyrene	200	28.0	280	J	µg/Kg-dry	1	9/1/2011 6:13:00 PM
Benzo(b)fluoranthene	190	28.0	280	J	µg/Kg-dry	1	9/1/2011 6:13:00 PM
Benzo(g,h,i)perylene	140	28.0	280	J	µg/Kg-dry	1	9/1/2011 6:13:00 PM
Benzo(k)fluoranthene	190	28.0	280	J	µg/Kg-dry	1	9/1/2011 6:13:00 PM
Benzoic acid	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Benzyl alcohol	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Biphenyl	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Bis(2-chloroethoxy)methane	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Bis(2-chloroethyl)ether	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Bis(2-chloroisopropyl)ether	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Bis(2-ethylhexyl)phthalate	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Butyl benzyl phthalate	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Caprolactam	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Carbazole	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Chrysene	240	28.0	280	J	µg/Kg-dry	1	9/1/2011 6:13:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-7C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 2:00:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-32A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
Dibenzo(a,h)anthracene	50	28.0	280	J	µg/Kg-dry	1	9/1/2011 6:13:00 PM
Dibenzofuran	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Diethyl phthalate	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Dimethyl phthalate	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Di-n-butyl phthalate	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Di-n-octyl phthalate	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Fluoranthene	380	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Fluorene	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Hexachlorobenzene	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Hexachlorobutadiene	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Hexachlorocyclopentadiene	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Hexachloroethane	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Indeno(1,2,3-c,d)pyrene	140	28.0	280	J	µg/Kg-dry	1	9/1/2011 6:13:00 PM
Isophorone	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Naphthalene	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Nitrobenzene	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
N-Nitrosodimethylamine	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
N-Nitrosodi-n-propylamine	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
N-Nitrosodiphenylamine	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Parathion	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Pentachlorophenol	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Phenanthrene	200	28.0	280	J	µg/Kg-dry	1	9/1/2011 6:13:00 PM
Phenol	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Pyrene	360	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Pyridine	U	28.0	280		µg/Kg-dry	1	9/1/2011 6:13:00 PM
Surr: 2,4,6-Tribromophenol	62.4	0	21-119		%REC	1	9/1/2011 6:13:00 PM
Surr: 2-Fluorobiphenyl	78.6	0	21-117		%REC	1	9/1/2011 6:13:00 PM
Surr: 2-Fluorophenol	31.2	0	11-105		%REC	1	9/1/2011 6:13:00 PM
Surr: 4-Terphenyl-d14	88.3	0	21-132		%REC	1	9/1/2011 6:13:00 PM
Surr: Nitrobenzene-d5	56.5	0	18-116		%REC	1	9/1/2011 6:13:00 PM
Surr: Phenol-d6	31.8	0	12-110		%REC	1	9/1/2011 6:13:00 PM
CYANIDE, TOTAL			**SW9012A**		**SW9012A**		Analyst: **STP**

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-7C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 2:00:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-32A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
CYANIDE, TOTAL			**SW9012A**		**SW9012A**		Analyst: **STP**
Cyanide, Total & Amenable: Auto Colorimetric	1.04	0.06	0.113		mg/Kg-dry	1	9/6/2011
HEXAVALENT CHROMIUM			**SW7196A**				Analyst: **AB**
Chromium, Hexavalent	U	0.23	0.450		mg/Kg-dry	1	9/6/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-7C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 2:00:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-32B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP MERCURY			**SW1311/7471B**		**SW1311**		Analyst: **AB**
Mercury	U	0.0005	0.0200		mg/L	1	9/2/2011 10:41:44 AM
TCLP HERBICIDES SW-846 8151			**SW8151A**		**SW3510C**		Analyst: **SB**
2,4,5-TP	U	0.0002	0.0050		mg/L	1	9/7/2011 9:16:00 PM
2,4-D	U	0.0002	0.0050		mg/L	1	9/7/2011 9:16:00 PM
Surr: 2,4-DCAA	96.5	0	21-144		%REC	1	9/7/2011 9:16:00 PM
TCLP PESTICIDES SW-846 8081			**SW8081B**		**SW3510C**		Analyst: **SB**
Chlordane	U	0.0005	0.0010		mg/L	1	9/7/2011 6:25:00 PM
Endrin	U	0.0002	0.0010		mg/L	1	9/7/2011 6:25:00 PM
gamma-BHC	U	0.0002	0.0010		mg/L	1	9/7/2011 6:25:00 PM
Heptachlor	U	0.0002	0.0010		mg/L	1	9/7/2011 6:25:00 PM
Heptachlor epoxide	U	0.0002	0.0010		mg/L	1	9/7/2011 6:25:00 PM
Methoxychlor	U	0.0002	0.0010		mg/L	1	9/7/2011 6:25:00 PM
Toxaphene	U	0.002	0.010		mg/L	1	9/7/2011 6:25:00 PM
Surr: DCB	93.5	0	28-146		%REC	1	9/7/2011 6:25:00 PM
Surr: TCX	86.3	0	25-147		%REC	1	9/7/2011 6:25:00 PM
TCLP METALS			**SW1311/6010C**		**SW1311**		Analyst: **JP**
Arsenic	0.0120	0.01	0.0500	J	mg/L	1	9/1/2011 3:40:42 PM
Barium	U	1	5.00		mg/L	1	9/1/2011 3:40:42 PM
Cadmium	U	0.005	0.0500		mg/L	1	9/1/2011 3:40:42 PM
Chromium	0.00500	0.005	0.0500	J	mg/L	1	9/1/2011 3:40:42 PM
Lead	6.42	0.005	0.0500	*	mg/L	1	9/1/2011 3:40:42 PM
Selenium	U	0.01	0.0500		mg/L	1	9/1/2011 3:40:42 PM
Silver	U	0.005	0.0500		mg/L	1	9/1/2011 3:40:42 PM
TCLP SEMIVOLATILES SW-846 8270			**SW8270D**		**SW3510C**		Analyst: **LDS**
2,4,5-Trichlorophenol	U	0.005	0.050		mg/L	1	9/7/2011 11:03:00 AM
2,4,6-Trichlorophenol	U	0.005	0.085		mg/L	1	9/7/2011 11:03:00 AM
2,4-Dinitrotoluene	U	0.005	0.045		mg/L	1	9/7/2011 11:03:00 AM
2-Methylphenol	U	0.005	0.035		mg/L	1	9/7/2011 11:03:00 AM
3+4-Methylphenol	U	0.005	0.040		mg/L	1	9/7/2011 11:03:00 AM
Hexachlorobenzene	U	0.005	0.090		mg/L	1	9/7/2011 11:03:00 AM
Hexachlorobutadiene	U	0.005	0.15		mg/L	1	9/7/2011 11:03:00 AM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-7C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 2:00:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-32B		

Certificate of Results

Analyses	Sample Result		LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP SEMIVOLATILES SW-846 8270				**SW8270D**		**SW3510C**		Analyst: **LDS**
Hexachloroethane	U		0.005	0.040		mg/L	1	9/7/2011 11:03:00 AM
Nitrobenzene	U		0.005	0.035		mg/L	1	9/7/2011 11:03:00 AM
Pentachlorophenol	U		0.05	0.17		mg/L	1	9/7/2011 11:03:00 AM
Pyridine	U		0.05	0.12		mg/L	1	9/7/2011 11:03:00 AM
Surr: 2,4,6-Tribromophenol	60.5		0	36-133		%REC	1	9/7/2011 11:03:00 AM
Surr: 2-Fluorobiphenyl	97.6		0	20-131		%REC	1	9/7/2011 11:03:00 AM
Surr: 2-Fluorophenol	77.6		0	22-128		%REC	1	9/7/2011 11:03:00 AM
Surr: 4-Terphenyl-d14	97.8		0	22-132		%REC	1	9/7/2011 11:03:00 AM
Surr: Nitrobenzene-d5	80.4		0	19-133		%REC	1	9/7/2011 11:03:00 AM
Surr: Phenol-d6	56.0		0	18-128		%REC	1	9/7/2011 11:03:00 AM
TCLP VOLATILES				**SW8260C**				Analyst: **LA**
1,1-Dichloroethene	U		0.01	0.020		mg/L	20	9/1/2011 3:36:00 PM
1,2-Dichloroethane	U		0.01	0.020		mg/L	20	9/1/2011 3:36:00 PM
1,4-Dichlorobenzene	U		0.01	0.020		mg/L	20	9/1/2011 3:36:00 PM
2-Butanone	U		0.02	0.040		mg/L	20	9/1/2011 3:36:00 PM
Benzene	U		0.01	0.020		mg/L	20	9/1/2011 3:36:00 PM
Carbon tetrachloride	U		0.01	0.020		mg/L	20	9/1/2011 3:36:00 PM
Chlorobenzene	U		0.01	0.020		mg/L	20	9/1/2011 3:36:00 PM
Chloroform	U		0.01	0.020		mg/L	20	9/1/2011 3:36:00 PM
Tetrachloroethene	U		0.01	0.020		mg/L	20	9/1/2011 3:36:00 PM
Trichloroethene	U		0.01	0.020		mg/L	20	9/1/2011 3:36:00 PM
Vinyl chloride	U		0.01	0.020		mg/L	20	9/1/2011 3:36:00 PM
Surr: 4-Bromofluorobenzene	99.3		0	63-123		%REC	20	9/1/2011 3:36:00 PM
Surr: Dibromofluoromethane	109		0	68-124		%REC	20	9/1/2011 3:36:00 PM
Surr: Toluene-d8	98.6		0	67-125		%REC	20	9/1/2011 3:36:00 PM
TRIVALENT CHROMIUM				**SW6010C**				Analyst: **JP**
Chromium, Trivalent	15.7		0.11	0.438		mg/Kg-dry	1	9/2/2011
IGNITABILITY/FLASHPOINT SW-846 1020				**SW1020B**				Analyst: **STP**
Ignitability	>		0	140		°F	1	9/1/2011
SOIL PH MEASURED IN WATER				**SW9045C**				Analyst: **AB**
pH	7.40		0	1.00	H	pH Units	1	9/1/2011 1:50:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-7C (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 2:00:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-32B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TEMPERATURE			**M2550 B**				Analyst: **AB**
Temp at which pH was measured	21.0	0	0		°C	1	9/1/2011 1:50:00 PM
REACTIVE CYANIDE			**SW7.3.3.2**				Analyst: **STP**
Reactive Cyanide	U	0.06	0.113		mg/Kg-dry	1	9/8/2011
REACTIVE SULFIDE			**SW7.3.4.2**				Analyst: **STP**
Reactive Sulfide	U	1.13	2.25		mg/Kg-dry	1	9/8/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-7Ca (0-7 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 2:02:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-33A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TOTAL DRO AS #2 FUEL (C8-C40)			**SW8015C**		**SW3550C**		Analyst: **LDS**
Total DRO TPH	7.0	2.77	11	J	mg/Kg-dry	1	9/2/2011 6:26:00 PM
Surr: o-Terphenyl	38.0	0	31-137		%REC	1	9/2/2011 6:26:00 PM
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	11.0	0	0		wt%	1	9/1/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-8G (2 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 1:45:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-34A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	11.8	0	0		wt%	1	9/1/2011
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: **LA**
1,1,1,2-Tetrachloroethane	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
1,1,1-Trichloroethane	U	0.55	5.5	C	µg/Kg-dry	1	8/31/2011 11:13:00 PM
1,1,2,2-Tetrachloroethane	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
1,1,2-Trichloro-1,2,2-trifluoroethan	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
1,1,2-Trichloroethane	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
1,1-Dichloroethane	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
1,1-Dichloroethene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
1,1-Dichloropropene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
1,2,3-Trichlorobenzene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
1,2,3-Trichloropropane	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
1,2,4,5-Tetramethylbenzene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
1,2,4-Trichlorobenzene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
1,2,4-Trimethylbenzene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
1,2-Dibromo-3-chloropropane	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
1,2-Dibromoethane	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
1,2-Dichlorobenzene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
1,2-Dichloroethane	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
1,2-Dichloropropane	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
1,3,5-Trimethylbenzene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
1,3-Dichlorobenzene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
1,3-dichloropropane	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
1,4-Dichlorobenzene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
1,4-Dioxane	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
2,2-Dichloropropane	U	0.55	5.5	C	µg/Kg-dry	1	8/31/2011 11:13:00 PM
2-Butanone	U	1.7	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
2-Chloroethyl vinyl ether	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
2-Chlorotoluene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
2-Hexanone	U	1.7	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
2-Propanol	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
4-Chlorotoluene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-8G (2 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 1:45:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-34A		

Certificate of Results

Analyses	Sample Result		LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
VOLATILE SW-846 METHOD 8260				**SW8260C**				Analyst: **LA**
4-Isopropyltoluene	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
4-Methyl-2-pentanone	U		1.7	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Acetone	U		1.7	5.5	C	µg/Kg-dry	1	8/31/2011 11:13:00 PM
Acrolein	U		2.8	11	C	µg/Kg-dry	1	8/31/2011 11:13:00 PM
Acrylonitrile	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Benzene	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Bromobenzene	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Bromochloromethane	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Bromodichloromethane	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Bromoform	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Bromomethane	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Carbon disulfide	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Carbon tetrachloride	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Chlorobenzene	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Chlorodifluoromethane	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Chloroethane	U		0.55	5.5	C	µg/Kg-dry	1	8/31/2011 11:13:00 PM
Chloroform	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Chloromethane	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
cis-1,2-Dichloroethene	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
cis-1,3-Dichloropropene	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Dibromochloromethane	U		0.55	5.5	C	µg/Kg-dry	1	8/31/2011 11:13:00 PM
Dibromomethane	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Dichlorodifluoromethane	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Diisopropyl ether	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Ethanol	U		2.8	11		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Ethyl acetate	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Ethylbenzene	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Freon-114	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Hexachlorobutadiene	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Isopropyl acetate	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Isopropylbenzene	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
m,p-Xylene	U		1.1	11		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Methyl Acetate	U		0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-8G (2 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 1:45:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-34A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: **LA**
Methyl tert-butyl ether	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Methylene chloride	12	0.55	5.5	B	µg/Kg-dry	1	8/31/2011 11:13:00 PM
n-Amyl acetate	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Naphthalene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
n-Butyl acetate	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
n-Butylbenzene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
n-Propyl acetate	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
n-Propylbenzene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
o-Xylene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
p-Diethylbenzene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
p-Ethyltoluene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
sec-Butylbenzene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Styrene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
t-Butyl alcohol	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
tert-Butylbenzene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Tetrachloroethene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Toluene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
trans-1,2-Dichloroethene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
trans-1,3-Dichloropropene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Trichloroethene	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Trichlorofluoromethane	U	0.55	5.5	C	µg/Kg-dry	1	8/31/2011 11:13:00 PM
Vinyl acetate	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Vinyl chloride	U	0.55	5.5		µg/Kg-dry	1	8/31/2011 11:13:00 PM
Surr: 4-Bromofluorobenzene	90.7	0	42-133		%REC	1	8/31/2011 11:13:00 PM
Surr: Dibromofluoromethane	99.4	0	50-133		%REC	1	8/31/2011 11:13:00 PM
Surr: Toluene-d8	101	0	53-130		%REC	1	8/31/2011 11:13:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-8C (0-4 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 1:40:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-35A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
MERCURY			**SW7471B**		**SW7471B**		Analyst: **AB**
Mercury	0.0979	0.005	0.0104		mg/Kg-dry	1	9/2/2011 11:33:47 AM
TOTAL DRO AS #2 FUEL (C8-C40)			**SW8015C**		**SW3550C**		Analyst: **LDS**
Total DRO TPH	U	2.8	11		mg/Kg-dry	1	9/1/2011 6:11:00 PM
Surr: o-Terphenyl	31.0	0	31-137	S	%REC	1	9/1/2011 6:11:00 PM
HERBICIDES SW-846 8151			**SW8151A**		**SW8151**		Analyst: **SB**
2,4,5-T	4.6	1.12	11	JP	µg/Kg-dry	1	9/8/2011 4:38:00 PM
2,4,5-TP	12	1.12	11	P	µg/Kg-dry	1	9/8/2011 4:38:00 PM
2,4-D	U	1.12	11		µg/Kg-dry	1	9/8/2011 4:38:00 PM
Surr: 2,4-DCAA	73.7	0	14-148		%REC	1	9/8/2011 4:38:00 PM
PCB'S AS AROCLORS SW-846 METHOD 8082			**SW8082A**		**SW3550C**		Analyst: **SB**
Aroclor 1016	U	1.12	45		µg/Kg-dry	1	9/1/2011 10:50:00 PM
Aroclor 1221	U	1.12	45		µg/Kg-dry	1	9/1/2011 10:50:00 PM
Aroclor 1232	U	1.12	45		µg/Kg-dry	1	9/1/2011 10:50:00 PM
Aroclor 1242	U	1.12	45		µg/Kg-dry	1	9/1/2011 10:50:00 PM
Aroclor 1248	U	1.12	45		µg/Kg-dry	1	9/1/2011 10:50:00 PM
Aroclor 1254	U	1.12	45		µg/Kg-dry	1	9/1/2011 10:50:00 PM
Aroclor 1260	U	1.12	45		µg/Kg-dry	1	9/1/2011 10:50:00 PM
Aroclor 1262	U	1.12	45		µg/Kg-dry	1	9/1/2011 10:50:00 PM
Aroclor 1268	U	1.12	45		µg/Kg-dry	1	9/1/2011 10:50:00 PM
Surr: TCX	74.4	0	17-151		%REC	1	9/1/2011 10:50:00 PM
Surr: DCB	102	0	16-152		%REC	1	9/1/2011 10:50:00 PM
PESTICIDES SW-846 METHOD 8081			**SW8081B**		**SW3550C**		Analyst: **SB**
4,4'-DDD	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 4:05:00 PM
4,4'-DDE	0.44	0.22	2.2	JP	µg/Kg-dry	1	9/2/2011 4:05:00 PM
4,4'-DDT	2.8	0.22	2.2		µg/Kg-dry	1	9/2/2011 4:05:00 PM
Aldrin	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 4:05:00 PM
alpha-BHC	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 4:05:00 PM
beta-BHC	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 4:05:00 PM
Chlordane	22	1.12	2.2		µg/Kg-dry	1	9/2/2011 4:05:00 PM
Chlorobenzilate	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 4:05:00 PM
DBCP	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 4:05:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.	

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-8C (0-4 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 1:40:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-35A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PESTICIDES SW-846 METHOD 8081			**SW8081B**		**SW3550C**		Analyst: **SB**
delta-BHC	3.5	0.22	2.2	P	µg/Kg-dry	1	9/2/2011 4:05:00 PM
Dieldrin	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 4:05:00 PM
Endosulfan I	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 4:05:00 PM
Endosulfan II	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 4:05:00 PM
Endosulfan sulfate	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 4:05:00 PM
Endrin	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 4:05:00 PM
Endrin aldehyde	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 4:05:00 PM
Endrin ketone	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 4:05:00 PM
gamma-BHC	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 4:05:00 PM
Heptachlor	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 4:05:00 PM
Heptachlor epoxide	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 4:05:00 PM
Hexachlorobenzene	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 4:05:00 PM
Hexachlorocyclopentadiene	U	0.22	2.2		µg/Kg-dry	1	9/2/2011 4:05:00 PM
Methoxychlor	0.43	0.22	2.2	J	µg/Kg-dry	1	9/2/2011 4:05:00 PM
Toxaphene	U	5.6	11		µg/Kg-dry	1	9/2/2011 4:05:00 PM
Surr: DCB	72.1	0	23-157		%REC	1	9/2/2011 4:05:00 PM
Surr: TCX	52.7	0	21-151		%REC	1	9/2/2011 4:05:00 PM
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	11.1	0	0		wt%	1	9/1/2011
TARGET ANALYTE LIST METALS			**SW6010C**		**SW3050B**		Analyst: **JP**
Aluminum	9110	1.05	4.18		mg/Kg-dry	10	9/2/2011 1:03:11 PM
Antimony	U	0.21	0.523		mg/Kg-dry	1	9/2/2011 10:32:17 AM
Arsenic	2.20	0.21	0.523		mg/Kg-dry	1	9/2/2011 10:32:17 AM
Barium	57.5	0.21	0.418		mg/Kg-dry	1	9/2/2011 10:32:17 AM
Beryllium	U	0.10	0.418		mg/Kg-dry	1	9/2/2011 10:32:17 AM
Cadmium	U	0.10	0.418		mg/Kg-dry	1	9/2/2011 10:32:17 AM
Calcium	817	0.21	0.523		mg/Kg-dry	1	9/2/2011 10:32:17 AM
Chromium	11.9	0.10	0.418		mg/Kg-dry	1	9/2/2011 10:32:17 AM
Cobalt	3.26	0.10	0.418		mg/Kg-dry	1	9/2/2011 10:32:17 AM
Copper	108	0.10	0.418		mg/Kg-dry	1	9/2/2011 10:32:17 AM
Iron	11600	2.09	4.18		mg/Kg-dry	10	9/2/2011 1:03:11 PM
Lead	103	0.21	0.418		mg/Kg-dry	1	9/2/2011 10:32:17 AM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-8C (0-4 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 1:40:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-35A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TARGET ANALYTE LIST METALS			**SW6010C**		**SW3050B**		Analyst: **JP**
Magnesium	1980	0.10	0.418		mg/Kg-dry	1	9/2/2011 10:32:17 AM
Manganese	324	0.10	0.418		mg/Kg-dry	1	9/2/2011 10:32:17 AM
Nickel	13.9	0.10	0.418		mg/Kg-dry	1	9/2/2011 10:32:17 AM
Potassium	926	0.21	0.523		mg/Kg-dry	1	9/2/2011 10:32:17 AM
Selenium	U	0.21	0.523		mg/Kg-dry	1	9/2/2011 10:32:17 AM
Silver	U	0.10	0.418		mg/Kg-dry	1	9/2/2011 10:32:17 AM
Sodium	81.6	0.21	0.523		mg/Kg-dry	1	9/2/2011 10:32:17 AM
Thallium	U	0.31	0.523		mg/Kg-dry	1	9/2/2011 10:32:17 AM
Vanadium	13.9	0.10	0.418		mg/Kg-dry	1	9/2/2011 10:32:17 AM
Zinc	53.3	0.10	0.418		mg/Kg-dry	1	9/2/2011 10:32:17 AM
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
1,2,4-Trichlorobenzene	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
1,2-Dichlorobenzene	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
1,3-Dichlorobenzene	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
1,4-Dichlorobenzene	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
2,4,5-Trichlorophenol	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
2,4,6-Trichlorophenol	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
2,4-Dichlorophenol	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
2,4-Dimethylphenol	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
2,4-Dinitrophenol	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
2,4-Dinitrotoluene	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
2,6-Dinitrotoluene	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
2-Chloronaphthalene	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
2-Chlorophenol	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
2-Methylnaphthalene	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
2-Methylphenol	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
2-Nitroaniline	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
2-Nitrophenol	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
3,3'-Dichlorobenzidine	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
3+4-Methylphenol	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
3-Nitroaniline	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
4,6-Dinitro-2-methylphenol	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-8C (0-4 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 1:40:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-35A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
4-Bromophenyl phenyl ether	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
4-Chloro-3-methylphenol	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
4-Chloroaniline	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
4-Chlorophenyl phenyl ether	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
4-Nitroaniline	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
4-Nitrophenol	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Acenaphthene	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Acenaphthylene	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Acetophenone	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Aniline	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Anthracene	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Atrazine	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Azobenzene	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Benzaldehyde	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Benzidine	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Benzo(a)anthracene	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Benzo(a)pyrene	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Benzo(b)fluoranthene	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Benzo(g,h,i)perylene	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Benzo(k)fluoranthene	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Benzoic acid	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Benzyl alcohol	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Biphenyl	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Bis(2-chloroethoxy)methane	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Bis(2-chloroethyl)ether	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Bis(2-chloroisopropyl)ether	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Bis(2-ethylhexyl)phthalate	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Butyl benzyl phthalate	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Caprolactam	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Carbazole	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Chrysene	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Dibenzo(a,h)anthracene	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Dibenzofuran	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-8C (0-4 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 1:40:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-35A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270			**SW8270D**		**SW3550C**		Analyst: **LDS**
Diethyl phthalate	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Dimethyl phthalate	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Di-n-butyl phthalate	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Di-n-octyl phthalate	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Fluoranthene	47	28	280	J	µg/Kg-dry	1	9/1/2011 6:38:00 PM
Fluorene	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Hexachlorobenzene	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Hexachlorobutadiene	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Hexachlorocyclopentadiene	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Hexachloroethane	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Indeno(1,2,3-c,d)pyrene	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Isophorone	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Naphthalene	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Nitrobenzene	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
N-Nitrosodimethylamine	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
N-Nitrosodi-n-propylamine	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
N-Nitrosodiphenylamine	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Parathion	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Pentachlorophenol	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Phenanthrene	36	28	280	J	µg/Kg-dry	1	9/1/2011 6:38:00 PM
Phenol	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Pyrene	46	28	280	J	µg/Kg-dry	1	9/1/2011 6:38:00 PM
Pyridine	U	28	280		µg/Kg-dry	1	9/1/2011 6:38:00 PM
Surr: 2,4,6-Tribromophenol	57.3	0	21-119		%REC	1	9/1/2011 6:38:00 PM
Surr: 2-Fluorobiphenyl	81.0	0	21-117		%REC	1	9/1/2011 6:38:00 PM
Surr: 2-Fluorophenol	32.7	0	11-105		%REC	1	9/1/2011 6:38:00 PM
Surr: 4-Terphenyl-d14	87.8	0	21-132		%REC	1	9/1/2011 6:38:00 PM
Surr: Nitrobenzene-d5	63.8	0	18-116		%REC	1	9/1/2011 6:38:00 PM
Surr: Phenol-d6	33.9	0	12-110		%REC	1	9/1/2011 6:38:00 PM
CYANIDE, TOTAL			**SW9012A**		**SW9012A**		Analyst: **STP**
Cyanide, Total & Amenable: Auto Colorimetric	0.636	0.06	0.112		mg/Kg-dry	1	9/6/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-8C (0-4 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 1:40:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-35A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
HEXAVALENT CHROMIUM			**SW7196A**				Analyst: **AB**
Chromium, Hexavalent	U	0.22	0.450		mg/Kg-dry	1	9/6/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-8C (0-4 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 1:40:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-35B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP MERCURY			**SW1311/7471B**		**SW1311**		Analyst: **AB**
Mercury	U	0.0005	0.0200		mg/L	1	9/2/2011 10:43:52 AM
TCLP HERBICIDES SW-846 8151			**SW8151A**		**SW3510C**		Analyst: **SB**
2,4,5-TP	U	0.0002	0.0050		mg/L	1	9/7/2011 9:30:00 PM
2,4-D	U	0.0002	0.0050		mg/L	1	9/7/2011 9:30:00 PM
Surr: 2,4-DCAA	64.1	0	21-144		%REC	1	9/7/2011 9:30:00 PM
TCLP PESTICIDES SW-846 8081			**SW8081B**		**SW3510C**		Analyst: **SB**
Chlordane	U	0.0005	0.0010		mg/L	1	9/7/2011 6:39:00 PM
Endrin	U	0.0002	0.0010		mg/L	1	9/7/2011 6:39:00 PM
gamma-BHC	U	0.0002	0.0010		mg/L	1	9/7/2011 6:39:00 PM
Heptachlor	U	0.0002	0.0010		mg/L	1	9/7/2011 6:39:00 PM
Heptachlor epoxide	U	0.0002	0.0010		mg/L	1	9/7/2011 6:39:00 PM
Methoxychlor	U	0.0002	0.0010		mg/L	1	9/7/2011 6:39:00 PM
Toxaphene	U	0.002	0.010		mg/L	1	9/7/2011 6:39:00 PM
Surr: DCB	93.3	0	28-146		%REC	1	9/7/2011 6:39:00 PM
Surr: TCX	90.2	0	25-147		%REC	1	9/7/2011 6:39:00 PM
TCLP METALS			**SW1311/6010C**		**SW1311**		Analyst: **JP**
Arsenic	0.0100	0.01	0.0500	J	mg/L	1	9/1/2011 3:42:46 PM
Barium	1.08	1	5.00	J	mg/L	1	9/1/2011 3:42:46 PM
Cadmium	U	0.005	0.0500		mg/L	1	9/1/2011 3:42:46 PM
Chromium	0.00700	0.005	0.0500	J	mg/L	1	9/1/2011 3:42:46 PM
Lead	0.695	0.005	0.0500		mg/L	1	9/1/2011 3:42:46 PM
Selenium	U	0.01	0.0500		mg/L	1	9/1/2011 3:42:46 PM
Silver	U	0.005	0.0500		mg/L	1	9/1/2011 3:42:46 PM
TCLP SEMIVOLATILES SW-846 8270			**SW8270D**		**SW3510C**		Analyst: **LDS**
2,4,5-Trichlorophenol	U	0.005	0.050		mg/L	1	9/7/2011 11:28:00 AM
2,4,6-Trichlorophenol	U	0.005	0.085		mg/L	1	9/7/2011 11:28:00 AM
2,4-Dinitrotoluene	U	0.005	0.045		mg/L	1	9/7/2011 11:28:00 AM
2-Methylphenol	U	0.005	0.035		mg/L	1	9/7/2011 11:28:00 AM
3+4-Methylphenol	U	0.005	0.040		mg/L	1	9/7/2011 11:28:00 AM
Hexachlorobenzene	U	0.005	0.090		mg/L	1	9/7/2011 11:28:00 AM
Hexachlorobutadiene	U	0.005	0.15		mg/L	1	9/7/2011 11:28:00 AM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

ACCREDITED IN ACCORDANCE WITH nelac

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-8C (0-4 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 1:40:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-35B		

Certificate of Results

Analyses	Sample Result		LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP SEMIVOLATILES SW-846 8270				**SW8270D**		**SW3510C**		Analyst: **LDS**
Hexachloroethane	U		0.005	0.040		mg/L	1	9/7/2011 11:28:00 AM
Nitrobenzene	U		0.005	0.035		mg/L	1	9/7/2011 11:28:00 AM
Pentachlorophenol	U		0.05	0.17		mg/L	1	9/7/2011 11:28:00 AM
Pyridine	U		0.05	0.12		mg/L	1	9/7/2011 11:28:00 AM
Surr: 2,4,6-Tribromophenol	55.7		0	36-133		%REC	1	9/7/2011 11:28:00 AM
Surr: 2-Fluorobiphenyl	98.1		0	20-131		%REC	1	9/7/2011 11:28:00 AM
Surr: 2-Fluorophenol	87.2		0	22-128		%REC	1	9/7/2011 11:28:00 AM
Surr: 4-Terphenyl-d14	101		0	22-132		%REC	1	9/7/2011 11:28:00 AM
Surr: Nitrobenzene-d5	82.3		0	19-133		%REC	1	9/7/2011 11:28:00 AM
Surr: Phenol-d6	62.0		0	18-128		%REC	1	9/7/2011 11:28:00 AM
TCLP VOLATILES				**SW8260C**				Analyst: **LA**
1,1-Dichloroethene	U		0.01	0.020		mg/L	20	9/1/2011 4:00:00 PM
1,2-Dichloroethane	U		0.01	0.020		mg/L	20	9/1/2011 4:00:00 PM
1,4-Dichlorobenzene	U		0.01	0.020		mg/L	20	9/1/2011 4:00:00 PM
2-Butanone	U		0.02	0.040		mg/L	20	9/1/2011 4:00:00 PM
Benzene	U		0.01	0.020		mg/L	20	9/1/2011 4:00:00 PM
Carbon tetrachloride	U		0.01	0.020		mg/L	20	9/1/2011 4:00:00 PM
Chlorobenzene	U		0.01	0.020		mg/L	20	9/1/2011 4:00:00 PM
Chloroform	U		0.01	0.020		mg/L	20	9/1/2011 4:00:00 PM
Tetrachloroethene	U		0.01	0.020		mg/L	20	9/1/2011 4:00:00 PM
Trichloroethene	U		0.01	0.020		mg/L	20	9/1/2011 4:00:00 PM
Vinyl chloride	U		0.01	0.020		mg/L	20	9/1/2011 4:00:00 PM
Surr: 4-Bromofluorobenzene	102		0	63-123		%REC	20	9/1/2011 4:00:00 PM
Surr: Dibromofluoromethane	109		0	68-124		%REC	20	9/1/2011 4:00:00 PM
Surr: Toluene-d8	97.0		0	67-125		%REC	20	9/1/2011 4:00:00 PM
TRIVALENT CHROMIUM				**SW6010C**				Analyst: **JP**
Chromium, Trivalent	11.9		0.10	0.418		mg/Kg-dry	1	9/2/2011
IGNITABILITY/FLASHPOINT SW-846 1020				**SW1020B**				Analyst: **STP**
Ignitability	>		0	140		°F	1	9/1/2011
SOIL PH MEASURED IN WATER				**SW9045C**				Analyst: **AB**
pH	5.60		0	1.00	H	pH Units	1	9/1/2011 1:52:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-8C (0-4 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 1:40:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-35B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TEMPERATURE			**M2550 B**				Analyst: **AB**
Temp at which pH was measured	21.0	0	0		°C	1	9/1/2011 1:52:00 PM
REACTIVE CYANIDE			**SW7.3.3.2**				Analyst: **STP**
Reactive Cyanide	U	0.06	0.112		mg/Kg-dry	1	9/8/2011
REACTIVE SULFIDE			**SW7.3.4.2**				Analyst: **STP**
Reactive Sulfide	U	1.12	2.25		mg/Kg-dry	1	9/8/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-8Ca (0-4 ft.)
Lab Order:	1108200	**Collection Date:**	8/30/2011 1:30:00 PM
Project:	260 West 26th Street, NY, NY	**Matrix:**	SOIL
Lab ID:	1108200-36A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TOTAL DRO AS #2 FUEL (C8-C40)			**SW8015C**	**SW3550C**			Analyst: **LDS**
Total DRO TPH	U	2.83	11		mg/Kg-dry	1	9/2/2011 6:51:00 PM
Surr: o-Terphenyl	34.8	0	31-137		%REC	1	9/2/2011 6:51:00 PM
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	12.3	0	0		wt%	1	9/1/2011

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Sep-11*

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: CN_DRY

Sample ID: **BL**	SampType: **MBLK**	TestCode: **CN_DRY**	Units: **mg/Kg**	Prep Date: **9/6/2011**	RunNo: **59659**
Client ID: **PBS**	Batch ID: **33156**	TestNo: **SW9012A**	**SW9012A**	Analysis Date: **9/6/2011**	SeqNo: **838001**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Cyanide, Total & Amenable: Auto Color	U	0.100									

Sample ID: **LCS**	SampType: **LCS**	TestCode: **CN_DRY**	Units: **mg/Kg**	Prep Date: **9/6/2011**	RunNo: **59659**
Client ID: **LCSS**	Batch ID: **33156**	TestNo: **SW9012A**	**SW9012A**	Analysis Date: **9/6/2011**	SeqNo: **838002**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Cyanide, Total & Amenable: Auto Color	1.90	0.100	2.000	0	95.0	63	123				

Sample ID: **BLB**	SampType: **MBLK**	TestCode: **CN_DRY**	Units: **mg/Kg**	Prep Date: **9/6/2011**	RunNo: **59659**
Client ID: **PBS**	Batch ID: **33156**	TestNo: **SW9012A**	**SW9012A**	Analysis Date: **9/6/2011**	SeqNo: **838023**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Cyanide, Total & Amenable: Auto Color	U	0.100									

Sample ID: **LCSB**	SampType: **LCS**	TestCode: **CN_DRY**	Units: **mg/Kg**	Prep Date: **9/6/2011**	RunNo: **59659**
Client ID: **LCSS**	Batch ID: **33156**	TestNo: **SW9012A**	**SW9012A**	Analysis Date: **9/6/2011**	SeqNo: **838024**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Cyanide, Total & Amenable: Auto Color	1.90	0.100	2.000	0	95.0	63	123				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: CR6_DRY

Sample ID: **BL**	SampType: **MBLK**	TestCode: **CR6_DRY**	Units: **mg/Kg**	Prep Date:	RunNo: **59658**
Client ID: **PBS**	Batch ID: **R59658**	TestNo: **SW7196A**		Analysis Date: **9/6/2011**	SeqNo: **837982**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Chromium, Hexavalent	U	0.400									

Sample ID: **LCS**	SampType: **LCS**	TestCode: **CR6_DRY**	Units: **mg/Kg**	Prep Date:	RunNo: **59658**
Client ID: **LCSS**	Batch ID: **R59658**	TestNo: **SW7196A**		Analysis Date: **9/6/2011**	SeqNo: **837983**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Chromium, Hexavalent	9.77	0.400	10.00	0	97.7	80	120				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DRY_TAL_MET

Sample ID: **PBS-090111A**	SampType: **MBLK**	TestCode: **DRY_TAL_M**	Units: **mg/Kg**	Prep Date: **9/1/2011**	RunNo: **59638**
Client ID: **PBS**	Batch ID: **33139**	TestNo: **SW6010C**	**SW3050B**	Analysis Date: **9/2/2011**	SeqNo: **837621**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Aluminum	U	0.400									
Antimony	U	0.500									
Arsenic	U	0.500									
Barium	U	0.400									
Beryllium	U	0.400									
Cadmium	U	0.400									
Calcium	U	0.500									
Cobalt	U	0.400									
Copper	U	0.400									
Iron	U	0.400									
Lead	U	0.400									
Magnesium	U	0.400									
Manganese	U	0.400									
Nickel	U	0.400									
Potassium	U	0.500									
Selenium	U	0.500									
Silver	U	0.400									
Sodium	U	0.500									
Thallium	U	0.500									
Vanadium	U	0.400									
Zinc	U	0.400									

Sample ID: **LCSS-090111A**	SampType: **LCS**	TestCode: **DRY_TAL_M**	Units: **mg/Kg**	Prep Date: **9/1/2011**	RunNo: **59638**
Client ID: **LCSS**	Batch ID: **33139**	TestNo: **SW6010C**	**SW3050B**	Analysis Date: **9/2/2011**	SeqNo: **837622**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Aluminum	39.8	0.400	40.00	0	99.4	85	115				
Antimony	39.7	0.500	40.00	0	99.2	85	120				
Arsenic	40.2	0.500	40.00	0	101	82	118				
Barium	40.7	0.400	40.00	0	102	87	114				
Beryllium	40.3	0.400	40.00	0	101	87	115				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DRY_TAL_MET

Sample ID: **LCSS-090111A**	SampType: **LCS**	TestCode: **DRY_TAL_M**	Units: **mg/Kg**	Prep Date: **9/1/2011**	RunNo: **59638**
Client ID: **LCSS**	Batch ID: **33139**	TestNo: **SW6010C**	**SW3050B**	Analysis Date: **9/2/2011**	SeqNo: **837622**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Cadmium	39.8	0.400	40.00	0	99.4	88	112				
Calcium	40.1	0.500	40.00	0	100	84	116				
Cobalt	39.9	0.400	40.00	0	99.7	89	113				
Copper	39.6	0.400	40.00	0	99.0	88	112				
Iron	40.3	0.400	40.00	0	101	80	120				
Lead	40.3	0.400	40.00	0	101	81	119				
Magnesium	40.3	0.400	40.00	0	101	89	113				
Manganese	39.9	0.400	40.00	0	99.7	84	114				
Nickel	39.8	0.400	40.00	0	99.6	85	117				
Potassium	395	0.500	400.0	0	98.7	82	120				
Selenium	41.0	0.500	40.00	0	103	84	118				
Silver	39.8	0.400	40.00	0	99.5	83	115				
Sodium	40.2	0.500	40.00	0	100	81	119				
Thallium	39.9	0.500	40.00	0	99.7	83	116				
Vanadium	39.8	0.400	40.00	0	99.4	88	112				
Zinc	40.4	0.400	40.00	0	101	86	114				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: Dry8081_Soil

Sample ID: **MB-33117**	SampType: **MBLK**	TestCode: **Dry8081_Soil**	Units: **µg/Kg**	Prep Date: **9/1/2011**	RunNo: **59643**
Client ID: **PBS**	Batch ID: **33117**	TestNo: **SW8081B**	**SW3550C**	Analysis Date: **9/2/2011**	SeqNo: **837828**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
4,4´-DDD	U	2.0									
4,4´-DDE	U	2.0									
4,4´-DDT	U	2.0									
Aldrin	U	2.0									
alpha-BHC	U	2.0									
beta-BHC	U	2.0									
Chlordane	U	2.0									
Chlorobenzilate	U	2.0									
DBCP	U	2.0									
delta-BHC	U	2.0									
Dieldrin	U	2.0									
Endosulfan I	U	2.0									
Endosulfan II	U	2.0									
Endosulfan sulfate	U	2.0									
Endrin	U	2.0									
Endrin aldehyde	U	2.0									
Endrin ketone	U	2.0									
gamma-BHC	U	2.0									
Heptachlor	U	2.0									
Heptachlor epoxide	U	2.0									
Hexachlorobenzene	U	2.0									
Hexachlorocyclopentadiene	U	2.0									
Methoxychlor	U	2.0									
Toxaphene	U	10									
Surr: DCB	19		25.00		75.2	23	157				
Surr: TCX	19		25.00		75.4	21	151				

Sample ID: **LCS-33117**	SampType: **LCS**	TestCode: **Dry8081_Soil**	Units: **µg/Kg**	Prep Date: **9/1/2011**	RunNo: **59643**
Client ID: **LCSS**	Batch ID: **33117**	TestNo: **SW8081B**	**SW3550C**	Analysis Date: **9/2/2011**	SeqNo: **837829**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: Dry8081_Soil

Sample ID: **LCS-33117**	SampType: **LCS**	TestCode: **Dry8081_Soil**	Units: **µg/Kg**	Prep Date: **9/1/2011**	RunNo: **59643**
Client ID: **LCSS**	Batch ID: **33117**	TestNo: **SW8081B**	**SW3550C**	Analysis Date: **9/2/2011**	SeqNo: **837829**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
4,4´-DDD	2.7	2.0	5.000	0	54.6	27	149				
4,4´-DDE	2.7	2.0	5.000	0	53.8	26	144				
4,4´-DDT	2.8	2.0	5.000	0	56.8	25	145				
Aldrin	3.0	2.0	5.000	0	60.9	28	147				
alpha-BHC	2.7	2.0	5.000	0	53.9	34	146				
beta-BHC	3.3	2.0	5.000	0	66.7	25	155				
Chlorobenzilate	3.8	2.0	5.000	0	75.3	26	152				
DBCP	2.9	2.0	5.000	0	57.8	24	148				
delta-BHC	2.9	2.0	5.000	0	58.8	27	146				
Dieldrin	3.1	2.0	5.000	0	61.7	25	148				
Endosulfan I	2.8	2.0	5.000	0	56.4	26	146				
Endosulfan II	3.3	2.0	5.000	0	65.0	22	143				
Endosulfan sulfate	2.8	2.0	5.000	0	55.7	24	154				
Endrin	3.3	2.0	5.000	0	67.0	23	145				
Endrin aldehyde	3.4	2.0	5.000	0	68.6	25	153				
Endrin ketone	4.4	2.0	5.000	0	89.0	33	152				
gamma-BHC	2.8	2.0	5.000	0	55.6	27	147				
Heptachlor	3.1	2.0	5.000	0	61.9	33	150				
Heptachlor epoxide	3.0	2.0	5.000	0	59.2	33	148				
Hexachlorobenzene	3.1	2.0	5.000	0	62.4	20	145				
Hexachlorocyclopentadiene	3.5	2.0	5.000	0	69.3	29	144				
Methoxychlor	3.2	2.0	5.000	0	63.1	49	154				
Surr: DCB	14		25.00		56.5	23	157				
Surr: TCX	16		25.00		63.1	21	151				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: Dry8082_Soil

Sample ID: **MB-33116**	SampType: **MBLK**	TestCode: **Dry8082_Soil**	Units: **µg/Kg**	Prep Date: **9/1/2011**	RunNo: **59633**
Client ID: **PBS**	Batch ID: **33116**	TestNo: **SW8082A**	**SW3550C**	Analysis Date: **9/1/2011**	SeqNo: **837446**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Aroclor 1016	U	40									
Aroclor 1221	U	40									
Aroclor 1232	U	40									
Aroclor 1242	U	40									
Aroclor 1248	U	40									
Aroclor 1254	U	40									
Aroclor 1260	U	40									
Aroclor 1262	U	40									
Aroclor 1268	U	40									
Surr: TCX	19		25.00		77.2	17	151				
Surr: DCB	19		25.00		74.6	16	152				

Sample ID: **LCS-33116**	SampType: **LCS**	TestCode: **Dry8082_Soil**	Units: **µg/Kg**	Prep Date: **9/1/2011**	RunNo: **59633**
Client ID: **LCSS**	Batch ID: **33116**	TestNo: **SW8082A**	**SW3550C**	Analysis Date: **9/1/2011**	SeqNo: **837447**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Aroclor 1248	38	40	50.00	0	76.0	55	144				J
Surr: TCX	17		25.00		69.6	17	151				
Surr: DCB	17		25.00		67.0	16	152				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: Dry8151_Soil

Sample ID: **MB-33154**	SampType: **MBLK**	TestCode: **Dry8151_Soil**	Units: **µg/Kg**	Prep Date: **9/6/2011**	RunNo: **59685**
Client ID: **PBS**	Batch ID: **33154**	TestNo: **SW8151A**	**SW8151**	Analysis Date: **9/8/2011**	SeqNo: **838351**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
2,4,5-T	U	9.8									
2,4,5-TP	U	9.8									
2,4-D	U	9.8									
Dicamba	U	9.8									
Surr: 2,4-DCAA	12		16.33		74.7	14	148				

Sample ID: **LCS-33154**	SampType: **LCS**	TestCode: **Dry8151_Soil**	Units: **µg/Kg**	Prep Date: **9/6/2011**	RunNo: **59685**
Client ID: **LCSS**	Batch ID: **33154**	TestNo: **SW8151A**	**SW8151**	Analysis Date: **9/8/2011**	SeqNo: **838352**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
2,4,5-T	19	9.9	32.87	0	57.5	21	145				
2,4,5-TP	27	9.9	32.87	0	81.7	20	146				
2,4-D	18	9.9	32.87	0	54.8	21	143				
Dicamba	18	9.9	32.87	0	54.6	20	140				
Surr: 2,4-DCAA	9.3		16.42		56.7	14	148				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: Dry8270_Soil

Sample ID: **MB-33118** SampType: **MBLK** TestCode: **Dry8270_Soil** Units: **µg/Kg** Prep Date: **9/1/2011** RunNo: **59624**
Client ID: **PBS** Batch ID: **33118** TestNo: **SW8270D** **SW3550C** Analysis Date: **9/1/2011** SeqNo: **837362**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
1,2,4-Trichlorobenzene	U	250									
1,2-Dichlorobenzene	U	250									
1,3-Dichlorobenzene	U	250									
1,4-Dichlorobenzene	U	250									
2,4,5-Trichlorophenol	U	250									
2,4,6-Trichlorophenol	U	250									
2,4-Dichlorophenol	U	250									
2,4-Dimethylphenol	U	250									
2,4-Dinitrophenol	U	250									
2,4-Dinitrotoluene	U	250									
2,6-Dinitrotoluene	U	250									
2-Chloronaphthalene	U	250									
2-Chlorophenol	U	250									
2-Methylnaphthalene	U	250									
2-Methylphenol	U	250									
2-Nitroaniline	U	250									
2-Nitrophenol	U	250									
3,3´-Dichlorobenzidine	U	250									
3+4-Methylphenol	U	250									
3-Nitroaniline	U	250									
4,6-Dinitro-2-methylphenol	U	250									
4-Bromophenyl phenyl ether	U	250									
4-Chloro-3-methylphenol	U	250									
4-Chloroaniline	U	250									
4-Chlorophenyl phenyl ether	U	250									
4-Nitroaniline	U	250									
4-Nitrophenol	U	250									
Acenaphthene	U	250									
Acenaphthylene	U	250									
Acetophenone	U	250									
Aniline	U	250									

Qualifiers:
B Analyte detected in the associated Method Blank
C Calibration %RSD/%D exceeded for non-CCC analytes
E Value above quantitation range
H Holding times for preparation or analysis exceeded
J Analyte detected below quantitation limits
LOD Limit of Detection
LOQ Limit of Quantitation
P >40% diff for detected conc between the two GC column
PQL Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: Dry8270_Soil

Sample ID: **MB-33118**	SampType: **MBLK**	TestCode: **Dry8270_Soil**	Units: **µg/Kg**	Prep Date: **9/1/2011**	RunNo: **59624**
Client ID: **PBS**	Batch ID: **33118**	TestNo: **SW8270D**	**SW3550C**	Analysis Date: **9/1/2011**	SeqNo: **837362**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Anthracene	U	250									
Atrazine	U	250									
Azobenzene	U	250									
Benzaldehyde	U	250									
Benzidine	U	250									
Benzo(a)anthracene	U	250									
Benzo(a)pyrene	U	250									
Benzo(b)fluoranthene	U	250									
Benzo(g,h,i)perylene	U	250									
Benzo(k)fluoranthene	U	250									
Benzoic acid	U	250									
Benzyl alcohol	U	250									
Biphenyl	U	250									
Bis(2-chloroethoxy)methane	U	250									
Bis(2-chloroethyl)ether	U	250									
Bis(2-chloroisopropyl)ether	U	250									
Bis(2-ethylhexyl)phthalate	U	250									
Butyl benzyl phthalate	U	250									
Caprolactam	U	250									
Carbazole	U	250									
Chrysene	U	250									
Dibenzo(a,h)anthracene	U	250									
Dibenzofuran	U	250									
Diethyl phthalate	U	250									
Dimethyl phthalate	U	250									
Di-n-butyl phthalate	U	250									
Di-n-octyl phthalate	U	250									
Fluoranthene	U	250									
Fluorene	U	250									
Hexachlorobenzene	U	250									
Hexachlorobutadiene	U	250									

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: Dry8270_Soil

Sample ID: **MB-33118**	SampType: **MBLK**	TestCode: **Dry8270_Soil**	Units: **µg/Kg**	Prep Date: **9/1/2011**	RunNo: **59624**
Client ID: **PBS**	Batch ID: **33118**	TestNo: **SW8270D**	**SW3550C**	Analysis Date: **9/1/2011**	SeqNo: **837362**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Hexachlorocyclopentadiene	U	250									
Hexachloroethane	U	250									
Indeno(1,2,3-c,d)pyrene	U	250									
Isophorone	U	250									
Naphthalene	U	250									
Nitrobenzene	U	250									
N-Nitrosodimethylamine	U	250									
N-Nitrosodi-n-propylamine	U	250									
N-Nitrosodiphenylamine	U	250									
Parathion	U	250									
Pentachlorophenol	U	250									
Phenanthrene	U	250									
Phenol	U	250									
Pyrene	U	250									
Pyridine	U	250									
Surr: 2,4,6-Tribromophenol	650		2000		32.6	21	119				
Surr: 2-Fluorobiphenyl	810		1000		81.3	21	117				
Surr: 2-Fluorophenol	700		2000		34.8	11	105				
Surr: 4-Terphenyl-d14	890		1000		88.8	21	132				
Surr: Nitrobenzene-d5	630		1000		63.4	18	116				
Surr: Phenol-d6	520		2000		26.2	12	110				

Sample ID: **LCS-33118**	SampType: **LCS**	TestCode: **Dry8270_Soil**	Units: **µg/Kg**	Prep Date: **9/1/2011**	RunNo: **59624**
Client ID: **LCSS**	Batch ID: **33118**	TestNo: **SW8270D**	**SW3550C**	Analysis Date: **9/1/2011**	SeqNo: **837363**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
1,2,4-Trichlorobenzene	1700	250	2000	0	85.4	38	128				
1,3-Dichlorobenzene	1500	250	2000	0	75.7	36	122				
1,4-Dichlorobenzene	1500	250	2000	0	74.6	33	127				
2,4-Dinitrotoluene	1200	250	2000	0	62.2	28	126				
2-Chlorophenol	1300	250	2000	0	63.7	37	127				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: Dry8270_Soil

Sample ID: **LCS-33118**	SampType: **LCS**	TestCode: **Dry8270_Soil**	Units: **µg/Kg**	Prep Date: **9/1/2011**	RunNo: **59624**
Client ID: **LCSS**	Batch ID: **33118**	TestNo: **SW8270D**	**SW3550C**	Analysis Date: **9/1/2011**	SeqNo: **837363**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
2-Methylnaphthalene	1600	250	2000	0	80.9	30	130				
4-Chloroaniline	450	250	2000	0	22.4	17	110				
Acenaphthene	3100	250	6000	0	51.1	38	141				
Acenaphthylene	1600	250	2000	0	77.9	48	121				
Anthracene	1600	250	2000	0	79.0	40	120				
Benzo(a)anthracene	1600	250	2000	0	82.2	45	120				
Benzo(a)pyrene	1700	250	2000	0	86.1	47	137				
Benzo(b)fluoranthene	1800	250	2000	0	90.4	42	136				
Benzo(g,h,i)perylene	1800	250	2000	0	88.8	42	138				
Benzo(k)fluoranthene	1500	250	2000	0	73.4	32	147				
Chrysene	1600	250	2000	0	80.8	43	125				
Dibenzo(a,h)anthracene	1700	250	2000	0	87.1	43	133				
Fluoranthene	1400	250	2000	0	71.7	42	120				
Fluorene	1500	250	2000	0	75.4	38	122				
Indeno(1,2,3-c,d)pyrene	1700	250	2000	0	86.6	49	150				
Naphthalene	1600	250	2000	0	80.1	33	127				
N-Nitrosodi-n-propylamine	1300	250	2000	0	65.0	45	121				
Pentachlorophenol	530	250	2000	0	26.7	21	124				
Phenanthrene	1600	250	2000	0	79.7	49	126				
Phenol	530	250	2000	0	26.5	21	136				
Pyrene	2800	250	6000	0	46.9	39	123				
Surr: 2,4,6-Tribromophenol	1000		2000		49.8	21	119				
Surr: 2-Fluorobiphenyl	800		1000		80.3	21	117				
Surr: 2-Fluorophenol	710		2000		35.4	11	105				
Surr: 4-Terphenyl-d14	910		1000		91.3	21	132				
Surr: Nitrobenzene-d5	670		1000		66.8	18	116				
Surr: Phenol-d6	630		2000		31.5	12	110				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DryFull8260_Soil

Sample ID: **V624LCS-083111YS** SampType: **LCS** TestCode: **DryFull8260_** Units: **µg/Kg** Prep Date: **8/31/2011** RunNo: **59598**
Client ID: **LCSS** Batch ID: **R59598** TestNo: **SW8260C** Analysis Date: **8/31/2011** SeqNo: **837075**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
1,1,1-Trichloroethane	59	5.0	50.00	0	118	40	125				C
1,1,2,2-Tetrachloroethane	37	5.0	50.00	0	73.9	41	130				
1,1,2-Trichloroethane	45	5.0	50.00	0	90.5	43	121				
1,1-Dichloroethane	45	5.0	50.00	0	89.6	42	126				
1,1-Dichloroethene	53	5.0	50.00	0	105	40	126				
1,2-Dichlorobenzene	42	5.0	50.00	0	84.9	41	122				
1,2-Dichloroethane	57	5.0	50.00	0	114	42	133				C
1,2-Dichloropropane	42	5.0	50.00	0	83.7	41	128				
1,3-Dichlorobenzene	43	5.0	50.00	0	86.0	45	119				
1,4-Dichlorobenzene	44	5.0	50.00	0	88.0	46	121				
2-Chloroethyl vinyl ether	47	5.0	50.00	0	94.2	30	135				
Benzene	47	5.0	50.00	0	93.6	35	123				
Bromodichloromethane	50	5.0	50.00	0	99.8	37	130				
Bromoform	45	5.0	50.00	0	90.0	43	121				
Bromomethane	24	5.0	50.00	0	48.4	32	130				
Carbon tetrachloride	60	5.0	50.00	0	120	37	134				C
Chlorobenzene	46	5.0	50.00	0	91.1	40	124				
Chloroethane	29	5.0	50.00	0	59.0	35	141				
Chloroform	55	5.0	50.00	0	110	36	126				C
cis-1,3-Dichloropropene	46	5.0	50.00	0	91.6	30	130				
Dibromochloromethane	51	5.0	50.00	0	102	43	125				
Ethylbenzene	46	5.0	50.00	0	92.9	44	122				
Methylene chloride	42	5.0	50.00	0	83.0	32	132				B
Tetrachloroethene	46	5.0	50.00	0	93.0	31	120				
Toluene	48	5.0	50.00	0	95.7	42	124				
trans-1,2-Dichloroethene	45	5.0	50.00	0	89.6	38	122				
trans-1,3-Dichloropropene	48	5.0	50.00	0	95.9	45	123				
Trichloroethene	50	5.0	50.00	0	99.2	46	124				
Trichlorofluoromethane	48	5.0	50.00	0	96.1	45	137				
Vinyl chloride	35	5.0	50.00	0	69.5	46	139				
Surr: 4-Bromofluorobenzene	51		50.00		102	42	133				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DryFull8260_Soil

Sample ID: **V624LCS-083111YS**	SampType: **LCS**	TestCode: **DryFull8260_**	Units: **µg/Kg**	Prep Date: **8/31/2011**	RunNo: **59598**
Client ID: **LCSS**	Batch ID: **R59598**	TestNo: **SW8260C**		Analysis Date: **8/31/2011**	SeqNo: **837075**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Surr: Dibromofluoromethane	55		50.00		110	50	133				
Surr: Toluene-d8	51		50.00		101	53	130				

Sample ID: **VBLK-083111YS**	SampType: **MBLK**	TestCode: **DryFull8260_**	Units: **µg/Kg**	Prep Date: **8/31/2011**	RunNo: **59598**
Client ID: **PBS**	Batch ID: **R59598**	TestNo: **SW8260C**		Analysis Date: **8/31/2011**	SeqNo: **837076**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
1,1,1,2-Tetrachloroethane	U	5.0									
1,1,1-Trichloroethane	U	5.0									C
1,1,2,2-Tetrachloroethane	U	5.0									
1,1,2-Trichloro-1,2,2-trifluoroethane	U	5.0									
1,1,2-Trichloroethane	U	5.0									
1,1-Dichloroethane	U	5.0									
1,1-Dichloroethene	U	5.0									
1,1-Dichloropropene	U	5.0									
1,2,3-Trichlorobenzene	U	5.0									
1,2,3-Trichloropropane	U	5.0									
1,2,4,5-Tetramethylbenzene	U	5.0									
1,2,4-Trichlorobenzene	U	5.0									
1,2,4-Trimethylbenzene	U	5.0									
1,2-Dibromo-3-chloropropane	U	5.0									
1,2-Dibromoethane	U	5.0									
1,2-Dichlorobenzene	U	5.0									
1,2-Dichloroethane	U	5.0									C
1,2-Dichloropropane	U	5.0									
1,3,5-Trimethylbenzene	U	5.0									
1,3-Dichlorobenzene	U	5.0									
1,3-dichloropropane	U	5.0									
1,4-Dichlorobenzene	U	5.0									
1,4-Dioxane	U	5.0									
2,2-Dichloropropane	U	5.0									C

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DryFull8260_Soil

Sample ID: **VBLK-083111YS** SampType: **MBLK** TestCode: **DryFull8260_** Units: **µg/Kg** Prep Date: **8/31/2011** RunNo: **59598**
Client ID: **PBS** Batch ID: **R59598** TestNo: **SW8260C** Analysis Date: **8/31/2011** SeqNo: **837076**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
2-Butanone	U	5.0									
2-Chloroethyl vinyl ether	U	5.0									
2-Chlorotoluene	U	5.0									
2-Hexanone	U	5.0									
2-Propanol	U	5.0									
4-Chlorotoluene	U	5.0									
4-Isopropyltoluene	U	5.0									
4-Methyl-2-pentanone	U	5.0									
Acetone	U	5.0									C
Acrolein	U	10									C
Acrylonitrile	U	5.0									
Benzene	U	5.0									
Bromobenzene	U	5.0									
Bromochloromethane	U	5.0									
Bromodichloromethane	U	5.0									
Bromoform	U	5.0									
Bromomethane	U	5.0									
Carbon disulfide	U	5.0									
Carbon tetrachloride	U	5.0									C
Chlorobenzene	U	5.0									
Chlorodifluoromethane	U	5.0									
Chloroethane	U	5.0									
Chloroform	U	5.0									C
Chloromethane	U	5.0									C
cis-1,2-Dichloroethene	U	5.0									
cis-1,3-Dichloropropene	U	5.0									
Dibromochloromethane	U	5.0									
Dibromomethane	U	5.0									
Dichlorodifluoromethane	U	5.0									
Diisopropyl ether	U	5.0									
Ethanol	U	10									

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DryFull8260_Soil

Sample ID: **VBLK-083111YS** SampType: **MBLK** TestCode: **DryFull8260_** Units: **µg/Kg** Prep Date: **8/31/2011** RunNo: **59598**
Client ID: **PBS** Batch ID: **R59598** TestNo: **SW8260C** Analysis Date: **8/31/2011** SeqNo: **837076**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Ethyl acetate	U	5.0									
Ethylbenzene	U	5.0									
Freon-114	U	5.0									
Hexachlorobutadiene	U	5.0									
Isopropyl acetate	U	5.0									
Isopropylbenzene	U	5.0									
m,p-Xylene	U	10									
Methyl Acetate	U	5.0									
Methyl tert-butyl ether	U	5.0									
Methylene chloride	5.4	5.0									
n-Amyl acetate	U	5.0									
Naphthalene	U	5.0									
n-Butyl acetate	U	5.0									
n-Butylbenzene	U	5.0									
n-Propyl acetate	U	5.0									
n-Propylbenzene	U	5.0									
o-Xylene	U	5.0									
p-Diethylbenzene	U	5.0									
p-Ethyltoluene	U	5.0									
sec-Butylbenzene	U	5.0									
Styrene	U	5.0									
t-Butyl alcohol	U	5.0									
tert-Butylbenzene	U	5.0									
Tetrachloroethene	U	5.0									
Toluene	U	5.0									
trans-1,2-Dichloroethene	U	5.0									
trans-1,3-Dichloropropene	U	5.0									
Trichloroethene	U	5.0									
Trichlorofluoromethane	U	5.0									
Vinyl acetate	U	5.0									
Vinyl chloride	U	5.0									

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DryFull8260_Soil

Sample ID: **VBLK-083111YS** SampType: **MBLK** TestCode: **DryFull8260_** Units: **µg/Kg** Prep Date: **8/31/2011** RunNo: **59598**
Client ID: **PBS** Batch ID: **R59598** TestNo: **SW8260C** Analysis Date: **8/31/2011** SeqNo: **837076**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Surr: 4-Bromofluorobenzene	51		50.00		101	42	133				
Surr: Dibromofluoromethane	55		50.00		110	50	133				
Surr: Toluene-d8	51		50.00		102	53	130				

Sample ID: **V624LCS-083111YS** SampType: **LCS** TestCode: **DryFull8260_** Units: **µg/Kg** Prep Date: **8/31/2011** RunNo: **59598**
Client ID: **LCSS** Batch ID: **R59598A** TestNo: **SW8260C** Analysis Date: **8/31/2011** SeqNo: **837082**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
1,1,1-Trichloroethane	62	5.0	50.00	0	123	40	125				C
1,1,2,2-Tetrachloroethane	38	5.0	50.00	0	75.4	41	130				
1,1,2-Trichloroethane	46	5.0	50.00	0	91.7	43	121				
1,1-Dichloroethane	49	5.0	50.00	0	97.2	42	126				
1,1-Dichloroethene	56	5.0	50.00	0	112	40	126				
1,2-Dichlorobenzene	43	5.0	50.00	0	86.0	41	122				
1,2-Dichloroethane	59	5.0	50.00	0	118	42	133				C
1,2-Dichloropropane	42	5.0	50.00	0	84.1	41	128				
1,3-Dichlorobenzene	43	5.0	50.00	0	86.9	45	119				
1,4-Dichlorobenzene	44	5.0	50.00	0	88.1	46	121				
2-Chloroethyl vinyl ether	50	5.0	50.00	0	100	30	135				
Benzene	50	5.0	50.00	0	101	35	123				
Bromodichloromethane	50	5.0	50.00	0	99.2	37	130				
Bromoform	44	5.0	50.00	0	87.1	43	121				
Bromomethane	31	5.0	50.00	0	61.9	32	130				
Carbon tetrachloride	64	5.0	50.00	0	128	37	134				
Chlorobenzene	45	5.0	50.00	0	89.4	40	124				
Chloroethane	34	5.0	50.00	0	68.0	35	141				
Chloroform	56	5.0	50.00	0	111	36	126				C
Chloromethane	32	5.0	50.00	0	63.4	42	141				
cis-1,3-Dichloropropene	46	5.0	50.00	0	91.3	30	130				
Dibromochloromethane	51	5.0	50.00	0	102	43	125				
Ethylbenzene	46	5.0	50.00	0	92.3	44	122				

Qualifiers:
B Analyte detected in the associated Method Blank
C Calibration %RSD/%D exceeded for non-CCC analytes
E Value above quantitation range
H Holding times for preparation or analysis exceeded
J Analyte detected below quantitation limits
LOD Limit of Detection
LOQ Limit of Quantitation
P >40% diff for detected conc between the two GC column
PQL Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DryFull8260_Soil

Sample ID: **V624LCS-083111YS** SampType: **LCS** TestCode: **DryFull8260_** Units: **µg/Kg** Prep Date: **8/31/2011** RunNo: **59598**
Client ID: **LCSS** Batch ID: **R59598A** TestNo: **SW8260C** Analysis Date: **8/31/2011** SeqNo: **837082**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Methylene chloride	47	5.0	50.00	0	94.0	32	132				B
Tetrachloroethene	45	5.0	50.00	0	90.9	31	120				
Toluene	46	5.0	50.00	0	92.1	42	124				
trans-1,2-Dichloroethene	51	5.0	50.00	0	101	38	122				
trans-1,3-Dichloropropene	48	5.0	50.00	0	95.8	45	123				
Trichloroethene	49	5.0	50.00	0	97.8	46	124				
Trichlorofluoromethane	55	5.0	50.00	0	110	45	137				
Vinyl chloride	40	5.0	50.00	0	80.3	46	139				
Surr: 4-Bromofluorobenzene	52		50.00		104	42	133				
Surr: Dibromofluoromethane	60		50.00		121	50	133				
Surr: Toluene-d8	50		50.00		100	53	130				

Sample ID: **VBLK-083111YS** SampType: **MBLK** TestCode: **DryFull8260_** Units: **µg/Kg** Prep Date: **8/31/2011** RunNo: **59598**
Client ID: **PBS** Batch ID: **R59598A** TestNo: **SW8260C** Analysis Date: **8/31/2011** SeqNo: **837083**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
1,1,1,2-Tetrachloroethane	U	5.0									
1,1,1-Trichloroethane	U	5.0									C
1,1,2,2-Tetrachloroethane	U	5.0									
1,1,2-Trichloro-1,2,2-trifluoroethane	U	5.0									
1,1,2-Trichloroethane	U	5.0									
1,1-Dichloroethane	U	5.0									
1,1-Dichloroethene	U	5.0									
1,1-Dichloropropene	U	5.0									C
1,2,3-Trichlorobenzene	U	5.0									
1,2,3-Trichloropropane	U	5.0									
1,2,4,5-Tetramethylbenzene	U	5.0									
1,2,4-Trichlorobenzene	U	5.0									
1,2,4-Trimethylbenzene	U	5.0									
1,2-Dibromo-3-chloropropane	U	5.0									
1,2-Dibromoethane	U	5.0									

Qualifiers:
B Analyte detected in the associated Method Blank
C Calibration %RSD/%D exceeded for non-CCC analytes
E Value above quantitation range
H Holding times for preparation or analysis exceeded
J Analyte detected below quantitation limits
LOD Limit of Detection
LOQ Limit of Quantitation
P >40% diff for detected conc between the two GC column
PQL Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DryFull8260_Soil

Sample ID: **VBLK-083111YS** SampType: **MBLK** TestCode: **DryFull8260_** Units: **µg/Kg** Prep Date: **8/31/2011** RunNo: **59598**
Client ID: **PBS** Batch ID: **R59598A** TestNo: **SW8260C** Analysis Date: **8/31/2011** SeqNo: **837083**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
1,2-Dichlorobenzene	U	5.0									
1,2-Dichloroethane	U	5.0									C
1,2-Dichloropropane	U	5.0									
1,3,5-Trimethylbenzene	U	5.0									
1,3-Dichlorobenzene	U	5.0									
1,3-dichloropropane	U	5.0									
1,4-Dichlorobenzene	U	5.0									
1,4-Dioxane	U	5.0									
2,2-Dichloropropane	U	5.0									C
2-Butanone	U	5.0									
2-Chloroethyl vinyl ether	U	5.0									
2-Chlorotoluene	U	5.0									
2-Hexanone	U	5.0									
2-Propanol	U	5.0									
4-Chlorotoluene	U	5.0									
4-Isopropyltoluene	U	5.0									
4-Methyl-2-pentanone	U	5.0									
Acetone	U	5.0									C
Acrolein	U	10									C
Acrylonitrile	U	5.0									
Benzene	U	5.0									
Bromobenzene	U	5.0									
Bromochloromethane	U	5.0									
Bromodichloromethane	U	5.0									
Bromoform	U	5.0									
Bromomethane	U	5.0									
Carbon disulfide	U	5.0									
Carbon tetrachloride	U	5.0									
Chlorobenzene	U	5.0									
Chlorodifluoromethane	U	5.0									
Chloroethane	U	5.0									

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DryFull8260_Soil

Sample ID: **VBLK-083111YS** SampType: **MBLK** TestCode: **DryFull8260_** Units: **µg/Kg** Prep Date: **8/31/2011** RunNo: **59598**
Client ID: **PBS** Batch ID: **R59598A** TestNo: **SW8260C** Analysis Date: **8/31/2011** SeqNo: **837083**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Chloroform	U	5.0									C
Chloromethane	U	5.0									
cis-1,2-Dichloroethene	U	5.0									
cis-1,3-Dichloropropene	U	5.0									
Dibromochloromethane	U	5.0									
Dibromomethane	U	5.0									
Dichlorodifluoromethane	U	5.0									
Diisopropyl ether	U	5.0									
Ethanol	U	10									
Ethyl acetate	U	5.0									
Ethylbenzene	U	5.0									
Freon-114	U	5.0									
Hexachlorobutadiene	U	5.0									
Isopropyl acetate	U	5.0									
Isopropylbenzene	U	5.0									
m,p-Xylene	U	10									
Methyl Acetate	U	5.0									
Methyl tert-butyl ether	U	5.0									
Methylene chloride	5.6	5.0									
n-Amyl acetate	U	5.0									
Naphthalene	U	5.0									
n-Butyl acetate	U	5.0									
n-Butylbenzene	U	5.0									
n-Propyl acetate	U	5.0									
n-Propylbenzene	U	5.0									
o-Xylene	U	5.0									
p-Diethylbenzene	U	5.0									
p-Ethyltoluene	U	5.0									
sec-Butylbenzene	U	5.0									
Styrene	U	5.0									
t-Butyl alcohol	U	5.0									

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DryFull8260_Soil

Sample ID: **VBLK-083111YS** SampType: **MBLK** TestCode: **DryFull8260_** Units: **µg/Kg** Prep Date: **8/31/2011** RunNo: **59598**
Client ID: **PBS** Batch ID: **R59598A** TestNo: **SW8260C** Analysis Date: **8/31/2011** SeqNo: **837083**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
tert-Butylbenzene	U	5.0									
Tetrachloroethene	U	5.0									
Toluene	U	5.0									
trans-1,2-Dichloroethene	U	5.0									
trans-1,3-Dichloropropene	U	5.0									
Trichloroethene	U	5.0									
Trichlorofluoromethane	U	5.0									
Vinyl acetate	U	5.0									
Vinyl chloride	U	5.0									
Surr: 4-Bromofluorobenzene	53		50.00		107	42	133				
Surr: Dibromofluoromethane	57		50.00		115	50	133				
Surr: Toluene-d8	51		50.00		102	53	130				

Sample ID: **V624LCS-083111aY** SampType: **LCS** TestCode: **DryFull8260_** Units: **µg/Kg** Prep Date: **8/31/2011** RunNo: **59598**
Client ID: **LCSS** Batch ID: **R59598B** TestNo: **SW8260C** Analysis Date: **8/31/2011** SeqNo: **837134**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
1,1,1-Trichloroethane	60	5.0	50.00	0	119	40	125				C
1,1,2,2-Tetrachloroethane	34	5.0	50.00	0	68.2	41	130				
1,1,2-Trichloroethane	43	5.0	50.00	0	86.0	43	121				
1,1-Dichloroethane	43	5.0	50.00	0	86.2	42	126				
1,1-Dichloroethene	55	5.0	50.00	0	109	40	126				
1,2-Dichlorobenzene	41	5.0	50.00	0	82.3	41	122				
1,2-Dichloroethane	54	5.0	50.00	0	109	42	133				
1,2-Dichloropropane	40	5.0	50.00	0	79.6	41	128				
1,3-Dichlorobenzene	41	5.0	50.00	0	81.8	45	119				
1,4-Dichlorobenzene	43	5.0	50.00	0	85.1	46	121				
2-Chloroethyl vinyl ether	44	5.0	50.00	0	88.6	30	135				
Benzene	44	5.0	50.00	0	89.0	35	123				
Bromodichloromethane	47	5.0	50.00	0	93.6	37	130				
Bromoform	41	5.0	50.00	0	82.2	43	121				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DryFull8260_Soil

Sample ID: **V624LCS-083111aY** SampType: **LCS** TestCode: **DryFull8260_** Units: **µg/Kg** Prep Date: **8/31/2011** RunNo: **59598**
Client ID: **LCSS** Batch ID: **R59598B** TestNo: **SW8260C** Analysis Date: **8/31/2011** SeqNo: **837134**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Bromomethane	31	5.0	50.00	0	61.9	32	130				
Carbon tetrachloride	55	5.0	50.00	0	110	37	134				
Chlorobenzene	44	5.0	50.00	0	88.4	40	124				
Chloroethane	36	5.0	50.00	0	72.9	35	141				C
Chloroform	52	5.0	50.00	0	104	36	126				
Chloromethane	29	5.0	50.00	0	58.5	42	141				
cis-1,3-Dichloropropene	43	5.0	50.00	0	85.7	30	130				
Dibromochloromethane	51	5.0	50.00	0	102	43	125				C
Ethylbenzene	44	5.0	50.00	0	89.0	44	122				
Methylene chloride	44	5.0	50.00	0	88.3	32	132				B
Tetrachloroethene	47	5.0	50.00	0	93.2	31	120				
Toluene	45	5.0	50.00	0	90.1	42	124				
trans-1,2-Dichloroethene	49	5.0	50.00	0	97.7	38	122				
trans-1,3-Dichloropropene	45	5.0	50.00	0	89.5	45	123				
Trichloroethene	50	5.0	50.00	0	101	46	124				
Trichlorofluoromethane	56	5.0	50.00	0	111	45	137				C
Vinyl chloride	40	5.0	50.00	0	79.2	46	139				
Surr: 4-Bromofluorobenzene	51		50.00		101	42	133				
Surr: Dibromofluoromethane	57		50.00		114	50	133				
Surr: Toluene-d8	49		50.00		97.7	53	130				

Sample ID: **VBLK-083111aYS** SampType: **MBLK** TestCode: **DryFull8260_** Units: **µg/Kg** Prep Date: **8/31/2011** RunNo: **59598**
Client ID: **PBS** Batch ID: **R59598B** TestNo: **SW8260C** Analysis Date: **8/31/2011** SeqNo: **837135**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
1,1,1,2-Tetrachloroethane	U	5.0									
1,1,1-Trichloroethane	U	5.0									C
1,1,2,2-Tetrachloroethane	U	5.0									
1,1,2-Trichloro-1,2,2-trifluoroethane	U	5.0									
1,1,2-Trichloroethane	U	5.0									
1,1-Dichloroethane	U	5.0									

Qualifiers:
B Analyte detected in the associated Method Blank
C Calibration %RSD/%D exceeded for non-CCC analytes
E Value above quantitation range
H Holding times for preparation or analysis exceeded
J Analyte detected below quantitation limits
LOD Limit of Detection
LOQ Limit of Quantitation
P >40% diff for detected conc between the two GC column
PQL Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DryFull8260_Soil

Sample ID: **VBLK-083111aYS** SampType: **MBLK** TestCode: **DryFull8260_** Units: **µg/Kg** Prep Date: **8/31/2011** RunNo: **59598**
Client ID: **PBS** Batch ID: **R59598B** TestNo: **SW8260C** Analysis Date: **8/31/2011** SeqNo: **837135**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
1,1-Dichloroethene	U	5.0									
1,1-Dichloropropene	U	5.0									
1,2,3-Trichlorobenzene	U	5.0									
1,2,3-Trichloropropane	U	5.0									
1,2,4,5-Tetramethylbenzene	U	5.0									
1,2,4-Trichlorobenzene	U	5.0									
1,2,4-Trimethylbenzene	U	5.0									
1,2-Dibromo-3-chloropropane	U	5.0									
1,2-Dibromoethane	U	5.0									
1,2-Dichlorobenzene	U	5.0									
1,2-Dichloroethane	U	5.0									
1,2-Dichloropropane	U	5.0									
1,3,5-Trimethylbenzene	U	5.0									
1,3-Dichlorobenzene	U	5.0									
1,3-dichloropropane	U	5.0									
1,4-Dichlorobenzene	U	5.0									
1,4-Dioxane	U	5.0									
2,2-Dichloropropane	U	5.0									C
2-Butanone	U	5.0									
2-Chloroethyl vinyl ether	U	5.0									
2-Chlorotoluene	U	5.0									
2-Hexanone	U	5.0									
2-Propanol	U	5.0									
4-Chlorotoluene	U	5.0									
4-Isopropyltoluene	U	5.0									
4-Methyl-2-pentanone	U	5.0									
Acetone	U	5.0									C
Acrolein	U	10									C
Acrylonitrile	U	5.0									
Benzene	U	5.0									
Bromobenzene	U	5.0									

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DryFull8260_Soil

Sample ID: **VBLK-083111aYS** SampType: **MBLK** TestCode: **DryFull8260_** Units: **µg/Kg** Prep Date: **8/31/2011** RunNo: **59598**
Client ID: **PBS** Batch ID: **R59598B** TestNo: **SW8260C** Analysis Date: **8/31/2011** SeqNo: **837135**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Bromochloromethane	U	5.0									
Bromodichloromethane	U	5.0									
Bromoform	U	5.0									
Bromomethane	U	5.0									
Carbon disulfide	U	5.0									
Carbon tetrachloride	U	5.0									
Chlorobenzene	U	5.0									
Chlorodifluoromethane	U	5.0									
Chloroethane	U	5.0									C
Chloroform	U	5.0									
Chloromethane	U	5.0									
cis-1,2-Dichloroethene	U	5.0									
cis-1,3-Dichloropropene	U	5.0									
Dibromochloromethane	U	5.0									C
Dibromomethane	U	5.0									
Dichlorodifluoromethane	U	5.0									
Diisopropyl ether	U	5.0									
Ethanol	U	10									
Ethyl acetate	U	5.0									
Ethylbenzene	U	5.0									
Freon-114	U	5.0									
Hexachlorobutadiene	U	5.0									
Isopropyl acetate	U	5.0									
Isopropylbenzene	U	5.0									
m,p-Xylene	U	10									
Methyl Acetate	U	5.0									
Methyl tert-butyl ether	U	5.0									
Methylene chloride	4.7	5.0									J
n-Amyl acetate	U	5.0									
Naphthalene	U	5.0									
n-Butyl acetate	U	5.0									

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DryFull8260_Soil

Sample ID: **VBLK-083111aYS** SampType: **MBLK** TestCode: **DryFull8260_** Units: **µg/Kg** Prep Date: **8/31/2011** RunNo: **59598**
Client ID: **PBS** Batch ID: **R59598B** TestNo: **SW8260C** Analysis Date: **8/31/2011** SeqNo: **837135**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
n-Butylbenzene	U	5.0									
n-Propyl acetate	U	5.0									
n-Propylbenzene	U	5.0									
o-Xylene	U	5.0									
p-Diethylbenzene	U	5.0									
p-Ethyltoluene	U	5.0									
sec-Butylbenzene	U	5.0									
Styrene	U	5.0									
t-Butyl alcohol	U	5.0									
tert-Butylbenzene	U	5.0									
Tetrachloroethene	U	5.0									
Toluene	U	5.0									
trans-1,2-Dichloroethene	U	5.0									
trans-1,3-Dichloropropene	U	5.0									
Trichloroethene	U	5.0									
Trichlorofluoromethane	U	5.0									C
Vinyl acetate	U	5.0									
Vinyl chloride	U	5.0									
Surr: 4-Bromofluorobenzene	50		50.00		99.6	42	133				
Surr: Dibromofluoromethane	58		50.00		115	50	133				
Surr: Toluene-d8	50		50.00		99.4	53	130				

Sample ID: **V624LCS-083111aY** SampType: **LCS** TestCode: **DryFull8260_** Units: **µg/Kg** Prep Date: **8/31/2011** RunNo: **59598**
Client ID: **LCSS** Batch ID: **R59598C** TestNo: **SW8260C** Analysis Date: **8/31/2011** SeqNo: **837138**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
1,1,1-Trichloroethane	60	5.0	50.00	0	120	40	125				C
1,1,2,2-Tetrachloroethane	32	5.0	50.00	0	64.3	41	130				
1,1,2-Trichloroethane	42	5.0	50.00	0	84.0	43	121				
1,1-Dichloroethane	43	5.0	50.00	0	85.4	42	126				
1,1-Dichloroethene	52	5.0	50.00	0	103	40	126				

Qualifiers:
B Analyte detected in the associated Method Blank
C Calibration %RSD/%D exceeded for non-CCC analytes
E Value above quantitation range
H Holding times for preparation or analysis exceeded
J Analyte detected below quantitation limits
LOD Limit of Detection
LOQ Limit of Quantitation
P >40% diff for detected conc between the two GC column
PQL Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DryFull8260_Soil

Sample ID: **V624LCS-083111aY** SampType: **LCS** TestCode: **DryFull8260_** Units: **µg/Kg** Prep Date: **8/31/2011** RunNo: **59598**
Client ID: **LCSS** Batch ID: **R59598C** TestNo: **SW8260C** Analysis Date: **8/31/2011** SeqNo: **837138**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
1,2-Dichlorobenzene	40	5.0	50.00	0	79.5	41	122				
1,2-Dichloroethane	55	5.0	50.00	0	110	42	133				C
1,2-Dichloropropane	39	5.0	50.00	0	77.7	41	128				
1,3-Dichlorobenzene	41	5.0	50.00	0	81.0	45	119				
1,4-Dichlorobenzene	42	5.0	50.00	0	84.3	46	121				
2-Chloroethyl vinyl ether	44	5.0	50.00	0	87.9	30	135				
Benzene	45	5.0	50.00	0	89.3	35	123				
Bromodichloromethane	47	5.0	50.00	0	94.7	37	130				
Bromoform	41	5.0	50.00	0	82.7	43	121				
Bromomethane	27	5.0	50.00	0	53.8	32	130				
Carbon tetrachloride	62	5.0	50.00	0	125	37	134				C
Chlorobenzene	44	5.0	50.00	0	87.7	40	124				
Chloroethane	34	5.0	50.00	0	67.7	35	141				
Chloroform	52	5.0	50.00	0	105	36	126				
cis-1,3-Dichloropropene	43	5.0	50.00	0	85.6	30	130				
Dibromochloromethane	50	5.0	50.00	0	99.9	43	125				
Ethylbenzene	44	5.0	50.00	0	88.3	44	122				
Methylene chloride	40	5.0	50.00	0	79.3	32	132				B
Tetrachloroethene	46	5.0	50.00	0	92.8	31	120				
Toluene	46	5.0	50.00	0	91.0	42	124				
trans-1,2-Dichloroethene	43	5.0	50.00	0	85.2	38	122				
trans-1,3-Dichloropropene	44	5.0	50.00	0	88.9	45	123				
Trichloroethene	50	5.0	50.00	0	101	46	124				
Trichlorofluoromethane	48	5.0	50.00	0	95.5	45	137				
Vinyl chloride	34	5.0	50.00	0	67.5	46	139				
Surr: 4-Bromofluorobenzene	49		50.00		97.6	42	133				
Surr: Dibromofluoromethane	57		50.00		115	50	133				
Surr: Toluene-d8	49		50.00		98.2	53	130				

Qualifiers:
B Analyte detected in the associated Method Blank
C Calibration %RSD/%D exceeded for non-CCC analytes
E Value above quantitation range
H Holding times for preparation or analysis exceeded
J Analyte detected below quantitation limits
LOD Limit of Detection
LOQ Limit of Quantitation
P >40% diff for detected conc between the two GC column
PQL Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DryFull8260_Soil

Sample ID: **VBLK-083111aYS** SampType: **MBLK** TestCode: **DryFull8260_** Units: **µg/Kg** Prep Date: **8/31/2011** RunNo: **59598**
Client ID: **PBS** Batch ID: **R59598C** TestNo: **SW8260C** Analysis Date: **8/31/2011** SeqNo: **837139**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
1,1,1,2-Tetrachloroethane	U	5.0									
1,1,1-Trichloroethane	U	5.0									C
1,1,2,2-Tetrachloroethane	U	5.0									
1,1,2-Trichloro-1,2,2-trifluoroethane	U	5.0									
1,1,2-Trichloroethane	U	5.0									
1,1-Dichloroethane	U	5.0									
1,1-Dichloroethene	U	5.0									
1,1-Dichloropropene	U	5.0									
1,2,3-Trichlorobenzene	U	5.0									
1,2,3-Trichloropropane	U	5.0									
1,2,4,5-Tetramethylbenzene	U	5.0									
1,2,4-Trichlorobenzene	U	5.0									
1,2,4-Trimethylbenzene	U	5.0									
1,2-Dibromo-3-chloropropane	U	5.0									
1,2-Dibromoethane	U	5.0									
1,2-Dichlorobenzene	U	5.0									
1,2-Dichloroethane	U	5.0									C
1,2-Dichloropropane	U	5.0									
1,3,5-Trimethylbenzene	U	5.0									
1,3-Dichlorobenzene	U	5.0									
1,3-dichloropropane	U	5.0									
1,4-Dichlorobenzene	U	5.0									
1,4-Dioxane	U	5.0									
2,2-Dichloropropane	U	5.0									
2-Butanone	U	5.0									
2-Chloroethyl vinyl ether	U	5.0									
2-Chlorotoluene	U	5.0									
2-Hexanone	U	5.0									
2-Propanol	U	5.0									
4-Chlorotoluene	U	5.0									
4-Isopropyltoluene	U	5.0									

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DryFull8260_Soil

Sample ID: **VBLK-083111aYS** SampType: **MBLK** TestCode: **DryFull8260_** Units: **µg/Kg** Prep Date: **8/31/2011** RunNo: **59598**
Client ID: **PBS** Batch ID: **R59598C** TestNo: **SW8260C** Analysis Date: **8/31/2011** SeqNo: **837139**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
4-Methyl-2-pentanone	U	5.0									
Acetone	U	5.0									
Acrolein	U	10									
Acrylonitrile	U	5.0									
Benzene	U	5.0									
Bromobenzene	U	5.0									
Bromochloromethane	U	5.0									
Bromodichloromethane	U	5.0									
Bromoform	U	5.0									
Bromomethane	U	5.0									
Carbon disulfide	U	5.0									
Carbon tetrachloride	U	5.0									C
Chlorobenzene	U	5.0									
Chlorodifluoromethane	U	5.0									
Chloroethane	U	5.0									
Chloroform	U	5.0									
Chloromethane	U	5.0									C
cis-1,2-Dichloroethene	U	5.0									
cis-1,3-Dichloropropene	U	5.0									
Dibromochloromethane	U	5.0									
Dibromomethane	U	5.0									
Dichlorodifluoromethane	U	5.0									
Diisopropyl ether	U	5.0									
Ethanol	U	10									
Ethyl acetate	U	5.0									
Ethylbenzene	U	5.0									
Freon-114	U	5.0									
Hexachlorobutadiene	U	5.0									
Isopropyl acetate	U	5.0									
Isopropylbenzene	U	5.0									
m,p-Xylene	U	10									

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DryFull8260_Soil

Sample ID: **VBLK-083111aYS** SampType: **MBLK** TestCode: **DryFull8260_** Units: **µg/Kg** Prep Date: **8/31/2011** RunNo: **59598**
Client ID: **PBS** Batch ID: **R59598C** TestNo: **SW8260C** Analysis Date: **8/31/2011** SeqNo: **837139**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Methyl Acetate	U	5.0									
Methyl tert-butyl ether	U	5.0									
Methylene chloride	4.4	5.0									J
n-Amyl acetate	U	5.0									
Naphthalene	U	5.0									
n-Butyl acetate	U	5.0									
n-Butylbenzene	U	5.0									
n-Propyl acetate	U	5.0									
n-Propylbenzene	U	5.0									
o-Xylene	U	5.0									
p-Diethylbenzene	U	5.0									
p-Ethyltoluene	U	5.0									
sec-Butylbenzene	U	5.0									
Styrene	U	5.0									
t-Butyl alcohol	U	5.0									
tert-Butylbenzene	U	5.0									
Tetrachloroethene	U	5.0									
Toluene	U	5.0									
trans-1,2-Dichloroethene	U	5.0									
trans-1,3-Dichloropropene	U	5.0									
Trichloroethene	U	5.0									
Trichlorofluoromethane	U	5.0									
Vinyl acetate	U	5.0									
Vinyl chloride	U	5.0									
Surr: 4-Bromofluorobenzene	49		50.00		98.6	42	133				
Surr: Dibromofluoromethane	57		50.00		114	50	133				
Surr: Toluene-d8	50		50.00		101	53	130				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DRYHG_S

Sample ID: **LCSS-090211A**	SampType: **LCS**	TestCode: **DRYHG_S**	Units: **mg/Kg**	Prep Date: **9/2/2011**	RunNo: **59636**
Client ID: **LCSS**	Batch ID: **33147**	TestNo: **SW7471B**	**SW7471B**	Analysis Date: **9/2/2011**	SeqNo: **837569**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Mercury	0.204	0.0100	0.2000	0	102	80	120				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: TCLP_M

Sample ID: **PBW-083111AT** SampType: **MBLK** TestCode: **TCLP_M** Units: **mg/L** Prep Date: RunNo: **59619**
Client ID: **PBS** Batch ID: **33130** TestNo: **SW1311/6010 SW1311** Analysis Date: **9/1/2011** SeqNo: **837279**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Arsenic	U	0.0500									
Barium	U	5.00									
Cadmium	U	0.0500									
Chromium	U	0.0500									
Lead	U	0.0500									
Selenium	U	0.0500									
Silver	U	0.0500									

Sample ID: **LCSW-083111AT** SampType: **LCS** TestCode: **TCLP_M** Units: **mg/L** Prep Date: RunNo: **59619**
Client ID: **LCSS** Batch ID: **33130** TestNo: **SW1311/6010 SW1311** Analysis Date: **9/1/2011** SeqNo: **837280**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Arsenic	2.12	0.0500	2.000	0	106	63	120				
Barium	1.93	5.00	2.000	0	96.6	65	125				J
Cadmium	2.07	0.0500	2.000	0	103	66	124				
Chromium	1.98	0.0500	2.000	0	98.9	66	128				
Lead	1.98	0.0500	2.000	0	99.1	63	123				
Selenium	2.24	0.0500	2.000	0	112	66	124				
Silver	2.08	0.0500	2.000	0	104	67	123				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: TCLPBNA

Sample ID: LCSD-33150	SampType: LCSD	TestCode: TCLPBNA	Units: mg/L	Prep Date: 9/6/2011	RunNo: 59664
Client ID: LCSS02	Batch ID: 33150	TestNo: SW8270D	SW3510C	Analysis Date: 9/6/2011	SeqNo: 838058

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
2,4-Dinitrotoluene	0.031	0.0045	0.04000	0	77.9	27	121	0.03373	7.90	20	
Pentachlorophenol	0.026	0.017	0.04000	0	65.0	14	118	0.02889	10.5	20	
Surr: 2,4,6-Tribromophenol	0.031		0.04000		77.7	36	133		0	0	
Surr: 2-Fluorobiphenyl	0.018		0.02000		91.2	20	131		0	0	
Surr: 2-Fluorophenol	0.031		0.04000		77.6	22	128		0	0	
Surr: 4-Terphenyl-d14	0.019		0.02000		95.6	22	132		0	0	
Surr: Nitrobenzene-d5	0.016		0.02000		78.3	19	133		0	0	
Surr: Phenol-d6	0.025		0.04000		63.2	18	128		0	0	

Sample ID: MB-33150	SampType: MBLK	TestCode: TCLPBNA	Units: mg/L	Prep Date: 9/6/2011	RunNo: 59664
Client ID: PBS	Batch ID: 33150	TestNo: SW8270D	SW3510C	Analysis Date: 9/6/2011	SeqNo: 838068

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
2,4,5-Trichlorophenol	U	0.0050									
2,4,6-Trichlorophenol	U	0.0085									
2,4-Dinitrotoluene	U	0.0045									
2-Methylphenol	U	0.0035									
3+4-Methylphenol	U	0.0040									
Hexachlorobenzene	U	0.0090									
Hexachlorobutadiene	U	0.015									
Hexachloroethane	U	0.0040									
Nitrobenzene	U	0.0035									
Pentachlorophenol	U	0.017									
Pyridine	U	0.012									
Surr: 2,4,6-Tribromophenol	0.030		0.04000		74.7	36	133				
Surr: 2-Fluorobiphenyl	0.021		0.02000		103	20	131				
Surr: 2-Fluorophenol	0.033		0.04000		82.5	22	128				
Surr: 4-Terphenyl-d14	0.021		0.02000		105	22	132				
Surr: Nitrobenzene-d5	0.018		0.02000		90.9	19	133				
Surr: Phenol-d6	0.025		0.04000		63.1	18	128				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: TCLPBNA

Sample ID: **LCS-33150**	SampType: **LCS**	TestCode: **TCLPBNA**	Units: **mg/L**	Prep Date: **9/6/2011**	RunNo: **59664**
Client ID: **LCSS**	Batch ID: **33150**	TestNo: **SW8270D**	**SW3510C**	Analysis Date: **9/6/2011**	SeqNo: **838069**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
2,4-Dinitrotoluene	0.034	0.0045	0.04000	0	84.3	32	137				
Pentachlorophenol	0.029	0.017	0.04000	0	72.2	30	139				
Surr: 2,4,6-Tribromophenol	0.030		0.04000		74.9	36	133				
Surr: 2-Fluorobiphenyl	0.019		0.02000		96.0	20	131				
Surr: 2-Fluorophenol	0.034		0.04000		84.3	22	128				
Surr: 4-Terphenyl-d14	0.020		0.02000		101	22	132				
Surr: Nitrobenzene-d5	0.017		0.02000		86.3	19	133				
Surr: Phenol-d6	0.028		0.04000		70.5	18	128				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: TCLPHerb

Sample ID: **MB-33153**	SampType: **MBLK**	TestCode: **TCLPHerb**	Units: **mg/L**	Prep Date: **9/6/2011**	RunNo: **59683**
Client ID: **PBS**	Batch ID: **33153**	TestNo: **SW8151A**	**SW3510C**	Analysis Date: **9/7/2011**	SeqNo: **838329**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
2,4,5-TP	U	0.0050									
2,4-D	U	0.0050									
Surr: 2,4-DCAA	0.0048		0.005000		96.0	21	144				

Sample ID: **LCS-33153**	SampType: **LCS**	TestCode: **TCLPHerb**	Units: **mg/L**	Prep Date: **9/6/2011**	RunNo: **59683**
Client ID: **LCSS**	Batch ID: **33153**	TestNo: **SW8151A**	**SW3510C**	Analysis Date: **9/7/2011**	SeqNo: **838330**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
2,4,5-TP	0.0097	0.0050	0.01000	0	97.0	22	144				
2,4-D	0.0071	0.0050	0.01000	0	71.2	21	143				
Surr: 2,4-DCAA	0.0045		0.005000		89.5	21	144				

Sample ID: **LCSD-33153**	SampType: **LCSD**	TestCode: **TCLPHerb**	Units: **mg/L**	Prep Date: **9/6/2011**	RunNo: **59683**
Client ID: **LCSS02**	Batch ID: **33153**	TestNo: **SW8151A**	**SW3510C**	Analysis Date: **9/7/2011**	SeqNo: **838331**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
2,4,5-TP	0.0096	0.0050	0.01000	0	96.2	22	144	0.009696	0.797	20	
2,4-D	0.0078	0.0050	0.01000	0	77.8	21	143	0.007123	8.84	20	
Surr: 2,4-DCAA	0.0050		0.005000		101	21	144		0	0	

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: TCLPPest

Sample ID: MB-33151	SampType: MBLK	TestCode: TCLPPest	Units: mg/L	Prep Date: 9/6/2011	RunNo: 59682
Client ID: PBS	Batch ID: 33151	TestNo: SW8081B	SW3510C	Analysis Date: 9/7/2011	SeqNo: 838321

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Chlordane	U	0.00010									
Endrin	U	0.00010									
gamma-BHC	U	0.00010									
Heptachlor	U	0.00010									
Heptachlor epoxide	U	0.00010									
Methoxychlor	U	0.00010									
Toxaphene	U	0.0010									
Surr: DCB	0.00039		0.0005000		77.4	28	146				
Surr: TCX	0.00041		0.0005000		82.5	25	147				

Sample ID: LCS-33151	SampType: LCS	TestCode: TCLPPest	Units: mg/L	Prep Date: 9/6/2011	RunNo: 59682
Client ID: LCSS	Batch ID: 33151	TestNo: SW8081B	SW3510C	Analysis Date: 9/7/2011	SeqNo: 838322

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Endrin	0.00086	0.0010	0.001000	0	85.7	25	131				J
gamma-BHC	0.00092	0.0010	0.001000	0	91.6	30	131				J
Heptachlor	0.00075	0.0010	0.001000	0	75.2	25	125				J
Heptachlor epoxide	0.00070	0.0010	0.001000	0	69.8	21	127				J
Methoxychlor	0.00083	0.0010	0.001000	0	83.4	20	130				J
Surr: DCB	0.0041		0.005000		82.7	28	146				
Surr: TCX	0.0044		0.005000		88.1	25	147				

Sample ID: LCSD-33151	SampType: LCSD	TestCode: TCLPPest	Units: mg/L	Prep Date: 9/6/2011	RunNo: 59682
Client ID: LCSS02	Batch ID: 33151	TestNo: SW8081B	SW3510C	Analysis Date: 9/7/2011	SeqNo: 838323

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Endrin	0.00077	0.0010	0.001000	0	76.6	25	131	0.0008570	0	20	J
gamma-BHC	0.00067	0.0010	0.001000	0	66.8	30	131	0.0009159	0	20	J
Heptachlor	0.00070	0.0010	0.001000	0	70.0	25	125	0.0007520	0	20	J
Heptachlor epoxide	0.00068	0.0010	0.001000	0	68.3	21	127	0.0006980	0	20	J
Methoxychlor	0.00074	0.0010	0.001000	0	73.8	20	130	0.0008340	0	20	J

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: TCLPPest

Sample ID: **LCSD-33151**	SampType: **LCSD**	TestCode: **TCLPPest**	Units: **mg/L**	Prep Date: **9/6/2011**	RunNo: **59682**
Client ID: **LCSS02**	Batch ID: **33151**	TestNo: **SW8081B**	**SW3510C**	Analysis Date: **9/7/2011**	SeqNo: **838323**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Surr: DCB	0.0037		0.005000		74.1	28	146		0	0	
Surr: TCX	0.0040		0.005000		79.8	25	147		0	0	

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: TCLPVOA

Sample ID: **V624LCS-090111LW** SampType: **LCS** TestCode: **TCLPVOA** Units: **mg/L** Prep Date: **9/1/2011** RunNo: **59598**
Client ID: **LCSS** Batch ID: **R59598D** TestNo: **SW8260C** Analysis Date: **9/1/2011** SeqNo: **837427**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
1,1-Dichloroethene	0.051	0.0010	0.05000	0	102	48	128				
1,2-Dichloroethane	0.050	0.0010	0.05000	0	99.8	52	129				
1,4-Dichlorobenzene	0.044	0.0010	0.05000	0	88.0	54	128				
Benzene	0.049	0.0010	0.05000	0	98.3	53	131				
Carbon tetrachloride	0.055	0.0010	0.05000	0	111	46	135				
Chlorobenzene	0.046	0.0010	0.05000	0	91.5	53	121				
Chloroform	0.054	0.0010	0.05000	0	108	41	135				
Tetrachloroethene	0.040	0.0010	0.05000	0	79.2	26	126				
Trichloroethene	0.051	0.0010	0.05000	0	102	47	127				
Vinyl chloride	0.042	0.0010	0.05000	0	84.7	50	149				
Surr: 4-Bromofluorobenzene	0.053		0.05000		106	63	123				
Surr: Dibromofluoromethane	0.049		0.05000		98.0	68	124				
Surr: Toluene-d8	0.050		0.05000		100	67	125				

Sample ID: **VBLK-090111LW** SampType: **MBLK** TestCode: **TCLPVOA** Units: **mg/L** Prep Date: **9/1/2011** RunNo: **59598**
Client ID: **PBS** Batch ID: **R59598D** TestNo: **SW8260C** Analysis Date: **9/1/2011** SeqNo: **837428**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
1,1-Dichloroethene	U	0.0010									
1,2-Dichloroethane	U	0.0010									
1,4-Dichlorobenzene	U	0.0010									
2-Butanone	U	0.0020									
Benzene	U	0.0010									
Carbon tetrachloride	U	0.0010									
Chlorobenzene	U	0.0010									
Chloroform	U	0.0010									
Tetrachloroethene	U	0.0010									
Trichloroethene	U	0.0010									
Vinyl chloride	U	0.0010									
Surr: 4-Bromofluorobenzene	0.050		0.05000		100	63	123				
Surr: Dibromofluoromethane	0.054		0.05000		109	68	124				

Qualifiers:
B Analyte detected in the associated Method Blank
C Calibration %RSD/%D exceeded for non-CCC analytes
E Value above quantitation range
H Holding times for preparation or analysis exceeded
J Analyte detected below quantitation limits
LOD Limit of Detection
LOQ Limit of Quantitation
P >40% diff for detected conc between the two GC column
PQL Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: TCLPVOA

Sample ID: **VBLK-090111LW**	SampType: **MBLK**	TestCode: **TCLPVOA**	Units: **mg/L**	Prep Date: **9/1/2011**	RunNo: **59598**
Client ID: **PBS**	Batch ID: **R59598D**	TestNo: **SW8260C**		Analysis Date: **9/1/2011**	SeqNo: **837428**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Surr: Toluene-d8	0.050		0.05000		100	67	125				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: TOTAL8015DRODRY

Sample ID: MB-33119	SampType: MBLK	TestCode: TOTAL8015D	Units: mg/Kg	Prep Date: 9/1/2011	RunNo: 59631
Client ID: PBS	Batch ID: 33119	TestNo: SW8015C	SW3550C	Analysis Date: 9/1/2011	SeqNo: 837413

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Total DRO TPH	U	10									
Surr: o-Terphenyl	0.80		2.000		40.2	31	137				

Sample ID: LCS-33119	SampType: LCS	TestCode: TOTAL8015D	Units: mg/Kg	Prep Date: 9/1/2011	RunNo: 59631
Client ID: LCSS	Batch ID: 33119	TestNo: SW8015C	SW3550C	Analysis Date: 9/1/2011	SeqNo: 837414

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Total DRO TPH	84	10	200.0	0	42.2	36	138				
Surr: o-Terphenyl	1.0		2.000		50.0	31	137				

Sample ID: MB-33133	SampType: MBLK	TestCode: TOTAL8015D	Units: mg/Kg	Prep Date: 9/1/2011	RunNo: 59653
Client ID: PBS	Batch ID: 33133	TestNo: SW8015C	SW3550C	Analysis Date: 9/2/2011	SeqNo: 837931

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Total DRO TPH	U	9.7									
Surr: o-Terphenyl	0.84		1.939		43.4	31	137				

Sample ID: LCS-33133	SampType: LCS	TestCode: TOTAL8015D	Units: mg/Kg	Prep Date: 9/1/2011	RunNo: 59653
Client ID: LCSS	Batch ID: 33133	TestNo: SW8015C	SW3550C	Analysis Date: 9/2/2011	SeqNo: 837932

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Total DRO TPH	75	9.9	198.0	0	37.9	36	138				
Surr: o-Terphenyl	0.77		1.980		38.8	31	137				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: CN_DRY

Sample ID: **1108200-02A-MS**	SampType: **MS**	TestCode: **CN_DRY**	Units: **mg/Kg-dry**	Prep Date: **9/6/2011**	RunNo: **59659**
Client ID: **TP-1C (0-7 ft.)**	Batch ID: **33156**	TestNo: **SW9012A**	**SW9012A**	Analysis Date: **9/6/2011**	SeqNo: **838009**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Cyanide, Total & Amenable: Auto Color	2.20	0.115	2.303	0	95.5	63	123				

Sample ID: **1108200-02A-MSD**	SampType: **MSD**	TestCode: **CN_DRY**	Units: **mg/Kg-dry**	Prep Date: **9/6/2011**	RunNo: **59659**
Client ID: **TP-1C (0-7 ft.)**	Batch ID: **33156**	TestNo: **SW9012A**	**SW9012A**	Analysis Date: **9/6/2011**	SeqNo: **838010**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Cyanide, Total & Amenable: Auto Color	2.17	0.115	2.303	0	94.0	63	123	2.200	1.58	20	

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: CR6_DRY

Sample ID: **1108200-35AMS**	SampType: **MS**	TestCode: **CR6_DRY**	Units: **mg/Kg-dry**	Prep Date:	RunNo: **59658**
Client ID: **TP-8C (0-4 ft.)**	Batch ID: **R59658**	TestNo: **SW7196A**		Analysis Date: **9/6/2011**	SeqNo: **837996**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Chromium, Hexavalent	21.3	0.450	22.50	0	94.8	75	125				

Sample ID: **1108200-35AMSD**	SampType: **MSD**	TestCode: **CR6_DRY**	Units: **mg/Kg-dry**	Prep Date:	RunNo: **59658**
Client ID: **TP-8C (0-4 ft.)**	Batch ID: **R59658**	TestNo: **SW7196A**		Analysis Date: **9/6/2011**	SeqNo: **837997**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Chromium, Hexavalent	21.7	0.450	22.50	0	96.2	75	125	21.33	1.52	20	

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: Dry8081_Soil

Sample ID: **1108200-02A-MS** SampType: **MS** TestCode: **Dry8081_Soil** Units: **µg/Kg-dry** Prep Date: **9/1/2011** RunNo: **59643**
Client ID: **TP-1C (0-7 ft.)** Batch ID: **33117** TestNo: **SW8081B SW3550C** Analysis Date: **9/2/2011** SeqNo: **837833**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
4,4'-DDD	100	2.3	5.716	111.4	-203	25	155				S
4,4'-DDE	240	2.3	5.716	276.9	-590	20	141				S
4,4'-DDT	970	2.3	5.716	859.4	1920	22	140				S
Aldrin	4.9	2.3	5.716	0	85.8	24	154				
alpha-BHC	3.5	2.3	5.716	0	60.9	21	145				
beta-BHC	7.1	2.3	5.716	0	125	22	156				
Chlordane	700	2.3	0	559.9	0	20	145				
Chlorobenzilate	28	2.3	5.716	0	489	25	145				S
DBCP	18	2.3	5.716	19.18	-20.4	24	148				S
delta-BHC	7.1	2.3	5.716	0	124	26	150				
Dieldrin	39	2.3	5.716	52.40	-226	20	154				S
Endosulfan I	16	2.3	5.716	0	282	23	151				S
Endosulfan II	8.3	2.3	5.716	0	145	23	149				
Endosulfan sulfate	6.6	2.3	5.716	0	115	21	147				
Endrin	5.5	2.3	5.716	0	96.2	22	142				
Endrin aldehyde	7.5	2.3	5.716	0	132	20	145				
Endrin ketone	4.1	2.3	5.716	0	71.5	23	139				
gamma-BHC	15	2.3	5.716	0	271	21	147				S
Heptachlor	5.8	2.3	5.716	0	102	23	147				
Heptachlor epoxide	7.9	2.3	5.716	0	139	24	152				
Hexachlorobenzene	4.5	2.3	5.716	0	78.8	25	147				
Hexachlorocyclopentadiene	5.3	2.3	5.716	0	93.3	30	146				
Methoxychlor	31	2.3	5.716	29.24	35.1	26	149				
Surr: DCB	31		28.58		109	23	157				
Surr: TCX	15		28.58		53.7	21	151				

Sample ID: **1108200-02A-MSD** SampType: **MSD** TestCode: **Dry8081_Soil** Units: **µg/Kg-dry** Prep Date: **9/1/2011** RunNo: **59643**
Client ID: **TP-1C (0-7 ft.)** Batch ID: **33117** TestNo: **SW8081B SW3550C** Analysis Date: **9/2/2011** SeqNo: **837834**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
4,4'-DDD	110	2.3	5.727	111.4	44.8	25	155	99.78	13.2	0	

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: Dry8081_Soil

Sample ID: **1108200-02A-MSD**	SampType: **MSD**	TestCode: **Dry8081_Soil**	Units: **µg/Kg-dry**	Prep Date: **9/1/2011**	RunNo: **59643**						
Client ID: **TP-1C (0-7 ft.)**	Batch ID: **33117**	TestNo: **SW8081B**	**SW3550C**	Analysis Date: **9/2/2011**	SeqNo: **837834**						
Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
4,4´-DDE	360	2.3	5.727	276.9	1450	20	141	243.2	38.7	0	S
4,4´-DDT	1400	2.3	5.727	859.4	9700	22	140	969.3	37.4	0	S
Aldrin	14	2.3	5.727	0	240	24	154	4.902	94.7	0	S
alpha-BHC	4.7	2.3	5.727	0	81.5	21	145	3.480	29.1	0	
beta-BHC	9.1	2.3	5.727	0	158	22	156	7.148	23.7	0	S
Chlordane	890	2.3	0	559.9	0	20	145	702.5	23.5	0	
Chlorobenzilate	37	2.3	5.727	0	643	25	145	27.93	27.5	0	S
DBCP	23	2.3	5.727	19.18	67.5	24	148	18.02	24.5	0	
delta-BHC	7.7	2.3	5.727	0	134	26	150	7.066	8.02	0	
Dieldrin	40	2.3	5.727	52.40	-219	20	154	39.46	0.969	0	S
Endosulfan I	17	2.3	5.727	0	303	23	151	16.12	7.22	0	S
Endosulfan II	15	2.3	5.727	0	266	23	149	8.263	59.3	0	S
Endosulfan sulfate	7.1	2.3	5.727	0	124	21	147	6.590	7.50	0	
Endrin	4.6	2.3	5.727	0	81.2	22	142	5.500	16.8	0	
Endrin aldehyde	13	2.3	5.727	0	223	20	145	7.528	51.7	0	S
Endrin ketone	2.4	2.3	5.727	0	42.0	23	139	4.087	51.7	0	
gamma-BHC	19	2.3	5.727	0	332	21	147	15.47	20.5	0	S
Heptachlor	6.4	2.3	5.727	0	112	23	147	5.835	9.09	0	
Heptachlor epoxide	29	2.3	5.727	0	503	24	152	7.949	114	0	S
Hexachlorobenzene	6.2	2.3	5.727	0	108	25	147	4.505	31.8	0	
Hexachlorocyclopentadiene	6.6	2.3	5.727	0	115	30	146	5.334	20.9	0	
Methoxychlor	13	2.3	5.727	29.24	-283	26	149	31.24	82.2	0	S
Surr: DCB	30		28.63		106	23	157		0	0	
Surr: TCX	21		28.63		73.0	21	151		0	0	

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: Dry8082_Soil

Sample ID: **1108179-10A-MS** SampType: **MS** TestCode: **Dry8082_Soil** Units: **µg/Kg-dry** Prep Date: **9/1/2011** RunNo: **59633**
Client ID: **ZZZZZZ** Batch ID: **33116** TestNo: **SW8082A** **SW3550C** Analysis Date: **9/1/2011** SeqNo: **837449**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Aroclor 1248	54	43	54.28	0	99.9	30	130				
Surr: TCX	14		27.14		52.3	17	151				
Surr: DCB	20		27.14		74.7	16	152				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: Dry8151_Soil

Sample ID: 1109001-01A-MS	SampType: MS	TestCode: Dry8151_Soil	Units: µg/Kg-dry	Prep Date: 9/6/2011	RunNo: 59685
Client ID: ZZZZZZ	Batch ID: 33154	TestNo: SW8151A	SW8151	Analysis Date: 9/8/2011	SeqNo: 838354

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
2,4,5-T	25	12	38.38	6.175	48.3	16	143				
2,4,5-TP	30	12	38.38	0	78.1	18	154				
2,4-D	16	12	38.38	0	42.4	20	149				
Dicamba	19	12	38.38	0	50.2	20	145				
Surr: 2,4-DCAA	12		19.17		64.4	14	148				

Sample ID: 1109001-01A-MSD	SampType: MSD	TestCode: Dry8151_Soil	Units: µg/Kg-dry	Prep Date: 9/6/2011	RunNo: 59685
Client ID: ZZZZZZ	Batch ID: 33154	TestNo: SW8151A	SW8151	Analysis Date: 9/8/2011	SeqNo: 838355

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
2,4,5-T	21	12	39.07	6.175	36.8	16	143	24.72	18.4	20	
2,4,5-TP	25	12	39.07	0	64.4	18	154	29.99	17.5	20	
2,4-D	27	12	39.07	0	68.0	20	149	16.28	48.0	20	R
Dicamba	20	12	39.07	0	50.9	20	145	19.29	0	20	
Surr: 2,4-DCAA	13		19.52		68.0	14	148		0	0	

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: Dry8270_Soil

Sample ID: **1108200-35A-MS** SampType: **MS** TestCode: **Dry8270_Soil** Units: **µg/Kg-dry** Prep Date: **9/1/2011** RunNo: **59624**
Client ID: **TP-8C (0-4 ft.)** Batch ID: **33118** TestNo: **SW8270D SW3550C** Analysis Date: **9/1/2011** SeqNo: **837376**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
1,2,4-Trichlorobenzene	1700	280	2235	0	74.6	21	128				
1,3-Dichlorobenzene	1600	280	2235	0	71.5	19	122				
1,4-Dichlorobenzene	1600	280	2235	0	70.7	22	127				
2,4-Dinitrotoluene	1300	280	2235	0	56.7	21	124				
2-Chlorophenol	1400	280	2235	0	61.3	18	117				
2-Methylnaphthalene	1500	280	2235	0	68.6	20	120				
4-Chloroaniline	500	280	2235	0	22.5	15	103				
Acenaphthene	3400	280	6706	0	51.3	24	132				
Acenaphthylene	1700	280	2235	0	76.8	22	134				
Anthracene	1800	280	2235	0	80.1	23	139				
Benzo(a)anthracene	1900	280	2235	0	83.4	24	134				
Benzo(a)pyrene	1800	280	2235	0	79.5	23	136				
Benzo(b)fluoranthene	1700	280	2235	0	73.9	24	132				
Benzo(g,h,i)perylene	1800	280	2235	0	82.4	27	131				
Benzo(k)fluoranthene	1800	280	2235	0	79.2	25	135				
Chrysene	1800	280	2235	0	80.6	24	136				
Dibenzo(a,h)anthracene	1800	280	2235	0	81.4	24	134				
Fluoranthene	1700	280	2235	47.43	74.7	22	122				
Fluorene	1600	280	2235	0	71.7	22	124				
Indeno(1,2,3-c,d)pyrene	1800	280	2235	0	80.7	26	140				
Naphthalene	1700	280	2235	0	74.3	20	120				
N-Nitrosodi-n-propylamine	1400	280	2235	0	62.4	24	126				
Pentachlorophenol	890	280	2235	0	40.0	17	116				
Phenanthrene	1800	280	2235	36.39	79.8	18	126				
Phenol	630	280	2235	0	28.2	11	106				
Pyrene	3100	280	6706	46.10	45.6	20	137				
Surr: 2,4,6-Tribromophenol	1200		2235		52.2	21	119				
Surr: 2-Fluorobiphenyl	930		1118		82.8	21	117				
Surr: 2-Fluorophenol	800		2235		35.7	11	105				
Surr: 4-Terphenyl-d14	1000		1118		89.0	21	132				
Surr: Nitrobenzene-d5	660		1118		59.3	18	116				

Qualifiers:
B Analyte detected in the associated Method Blank
C Calibration %RSD/%D exceeded for non-CCC analytes
E Value above quantitation range
H Holding times for preparation or analysis exceeded
J Analyte detected below quantitation limits
LOD Limit of Detection
LOQ Limit of Quantitation
P >40% diff for detected conc between the two GC column
PQL Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: Dry8270_Soil

Sample ID: 1108200-35A-MS	SampType: MS	TestCode: Dry8270_Soil	Units: µg/Kg-dry	Prep Date: 9/1/2011	RunNo: 59624
Client ID: TP-8C (0-4 ft.)	Batch ID: 33118	TestNo: SW8270D	SW3550C	Analysis Date: 9/1/2011	SeqNo: 837376

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Surr: Phenol-d6	810		2235		36.4	12	110				

Sample ID: 1108200-35A-MSD	SampType: MSD	TestCode: Dry8270_Soil	Units: µg/Kg-dry	Prep Date: 9/1/2011	RunNo: 59624
Client ID: TP-8C (0-4 ft.)	Batch ID: 33118	TestNo: SW8270D	SW3550C	Analysis Date: 9/1/2011	SeqNo: 837377

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
1,2,4-Trichlorobenzene	1800	280	2239	0	78.5	21	128	1667	5.22	20	
1,3-Dichlorobenzene	1800	280	2239	0	78.8	19	122	1597	9.88	20	
1,4-Dichlorobenzene	1700	280	2239	0	77.6	22	127	1580	9.49	20	
2,4-Dinitrotoluene	1400	280	2239	0	61.5	21	124	1266	8.39	20	
2-Chlorophenol	1500	280	2239	0	67.4	18	117	1370	9.73	20	
2-Methylnaphthalene	1700	280	2239	0	74.9	20	120	1534	8.94	20	
4-Chloroaniline	530	280	2239	0	23.9	15	103	503.2	6.11	20	
Acenaphthene	3500	280	6716	0	52.5	24	132	3440	2.53	20	
Acenaphthylene	1900	280	2239	0	83.8	22	134	1717	8.79	20	
Anthracene	1700	280	2239	0	74.3	23	139	1791	7.36	20	
Benzo(a)anthracene	1800	280	2239	0	82.6	24	134	1863	0.752	20	
Benzo(a)pyrene	1900	280	2239	0	85.7	23	136	1777	7.63	20	
Benzo(b)fluoranthene	1900	280	2239	0	84.0	24	132	1652	12.9	20	
Benzo(g,h,i)perylene	1900	280	2239	0	85.9	27	131	1841	4.38	20	
Benzo(k)fluoranthene	1800	280	2239	0	82.5	25	135	1771	4.23	20	
Chrysene	1800	280	2239	0	79.0	24	136	1802	1.95	20	
Dibenzo(a,h)anthracene	2000	280	2239	0	90.2	24	134	1819	10.4	20	
Fluoranthene	1700	280	2239	47.43	71.7	22	122	1716	3.75	20	
Fluorene	1800	280	2239	0	78.3	22	124	1603	8.88	20	
Indeno(1,2,3-c,d)pyrene	2000	280	2239	0	87.5	26	140	1803	8.31	20	
Naphthalene	1700	280	2239	0	77.8	20	120	1660	4.87	20	
N-Nitrosodi-n-propylamine	1400	280	2239	0	63.4	24	126	1395	1.79	20	
Pentachlorophenol	690	280	2239	0	30.9	17	116	893.5	25.3	20	R
Phenanthrene	1700	280	2239	36.39	75.3	18	126	1819	5.54	20	
Phenol	730	280	2239	0	32.6	11	106	630.6	14.6	20	

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: Dry8270_Soil

Sample ID: **1108200-35A-MSD** SampType: **MSD** TestCode: **Dry8270_Soil** Units: **µg/Kg-dry** Prep Date: **9/1/2011** RunNo: **59624**
Client ID: **TP-8C (0-4 ft.)** Batch ID: **33118** TestNo: **SW8270D SW3550C** Analysis Date: **9/1/2011** SeqNo: **837377**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Pyrene	3000	280	6716	46.10	43.9	20	137	3102	3.61	20	
Surr: 2,4,6-Tribromophenol	1300		2239		59.5	21	119		0	0	
Surr: 2-Fluorobiphenyl	930		1119		83.1	21	117		0	0	
Surr: 2-Fluorophenol	850		2239		37.8	11	105		0	0	
Surr: 4-Terphenyl-d14	920		1119		82.2	21	132		0	0	
Surr: Nitrobenzene-d5	720		1119		64.3	18	116		0	0	
Surr: Phenol-d6	910		2239		40.6	12	110		0	0	

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DRYHG_S

Sample ID: 1108200-35A-MS	SampType: MS	TestCode: DRYHG_S	Units: mg/Kg-dry	Prep Date: 9/2/2011	RunNo: 59636
Client ID: TP-8C (0-4 ft.)	Batch ID: 33147	TestNo: SW7471B	SW7471B	Analysis Date: 9/2/2011	SeqNo: 837598

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Mercury	0.289	0.0118	0.2368	0.09790	80.7	80	120				

Sample ID: 1108200-35A-MSD	SampType: MSD	TestCode: DRYHG_S	Units: mg/Kg-dry	Prep Date: 9/2/2011	RunNo: 59636
Client ID: TP-8C (0-4 ft.)	Batch ID: 33147	TestNo: SW7471B	SW7471B	Analysis Date: 9/2/2011	SeqNo: 837599

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Mercury	0.298	0.0116	0.2319	0.09790	86.3	80	120	0.2889	3.11	20	

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1108200
Project: 260 West 26th Street, NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: TOTAL8015DRODRY

Sample ID: **1108200-36A-MS** SampType: **MS** TestCode: **TOTAL8015D** Units: **mg/Kg-dry** Prep Date: **9/1/2011** RunNo: **59653**
Client ID: **TP-8Ca (0-4 ft.)** Batch ID: **33133** TestNo: **SW8015C** **SW3550C** Analysis Date: **9/2/2011** SeqNo: **837945**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Total DRO TPH	91	11	225.6	0	40.3	27	152				
Surr: o-Terphenyl	1.2		2.256		52.2	31	137				

Sample ID: **1108200-36AMSD** SampType: **MSD** TestCode: **TOTAL8015D** Units: **mg/Kg-dry** Prep Date: **9/1/2011** RunNo: **59653**
Client ID: **TP-8Ca (0-4 ft.)** Batch ID: **33133** TestNo: **SW8015C** **SW3550C** Analysis Date: **9/2/2011** SeqNo: **837946**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Total DRO TPH	67	11	222.0	0	30.0	27	152	90.86	30.7	20	R
Surr: o-Terphenyl	1.1		2.220		48.3	31	137		0	0	

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

AMERICAN ANALYTICAL LABORATORIES

NYSDOH 11418
NJDEP NY050
CTDOH PH-0205
PADEP 68-00573

Wednesday, January 11, 2012

Steve Malinowski
CA Rich Consultants Inc.
17 Dupont Street
Plainview, NY 11803

TEL: (516) 576-8844
FAX (516) 576-0093

RE: 260 West 26th St., NY, NY

Order No.: 1201054

Dear Steve Malinowski:

American Analytical Laboratories, LLC. received 1 sample(s) on 1/11/2012 for the analyses presented in the following report.

Samples were analyzed in accordance with the test procedures documented on the chain of custody and detailed throughout the text of this report.

The results reported herein relate only to the items tested or to the samples as received by the laboratory. This report may not be reproduced, except in full, without the approval of American Analytical Laboratories, LLC and is not considered complete without a cover page and chain of custody documentation. The limits (LOQ) provided in the data package are analytical reporting limits and not Federal or Local mandated values to which the sample results should be compared.

There were no problems with the analyses and all data for associated QC met laboratory specifications. If there are any exceptions a Case Narrative is provided in the report or the data is qualified. This package has been reviewed by American Analytical Laboratories' QA Department/Laboratory Director to comply with NELAC standards prior to report submittal. This report consists of 11 pages.

If you have any questions regarding these tests results, please do not hesitate to call (631) 454-6100 or email me directly at lbeyer@american-analytical.com.

Sincerely,

Lori Beyer
Lab Director

American Analytical Laboratories, LLC.

Date: *11-Jan-12*

CLIENT: CA Rich Consultants Inc.
Project: 260 West 26th St., NY, NY
Lab Order: 1201054

Work Order Sample Summary

Lab Sample ID	Client Sample ID	Date Collected	Date Received
1201054-01A	WC- 1/10/12	1/10/2012 1:00:00 PM	1/11/2012

AMERICAN ANALYTICAL LABORATORIES
56 TOLEDO STREET • FARMINGDALE, NEW YORK 11735
(631) 454-6100 • FAX (631) 454-8027
www.american-analytical.com

NYSDOH	11418
CTDOH	PH-0205
NJDEP	NY050
PADEP	68-573

CHAIN OF CUSTODY / REQUEST FOR ANALYSIS DOCUMENT

CLIENT NAME/ADDRESS: Ca Rich Consultants, 17 Dupont St, Plainview NY

CONTACT: Steve Malinowski

SAMPLER (SIGNATURE):

SAMPLER NAME (PRINT): Jessica Prosca

SAMPLE(S) SEALED: YES / NO

CORRECT CONTAINER(S): YES / NO

TEMPERATURE (° C): 3.7

PROJECT LOCATION: 260 West 26th St NY, NY

LABORATORY ID# LAB USE ONLY	MATRIX/ TYPE	NO. OF CONTAINERS	SAMPLING DATE	SAMPLING TIME	SAMPLE # - LOCATION	ANALYSIS REQUIRED: VOCs 8260
12010S4-01A	S	1	1/10/12	1PM	WC-1/10/12	X

COMMENTS / INSTRUCTIONS

Samples must be on ICE (<6° C)

MATRIX S=SOIL; W=WATER; SL=SLUDGE; A=AIR; M=MISCELLANEOUS

TYPE (G=GRAB); C=COMPOSITE

TURNAROUND REQUIRED: STANDARD ☐ (7-10 business days) STAT ☐ 24 hour BY tat /

E-MAIL ADDRESS FOR RESULTS:

RELINQUISHED BY (SIGNATURE)	DATE / TIME	PRINTED NAME	RECEIVED BY LAB (SIGNATURE)	DATE / TIME	PRINTED NAME
	1/11/12 10:10	Stephen Malinowski		1-11-12 10:10	
	1/11/12 10:30			1/11/12 1022	

WHITE-OFFICE / CANARY-LAB / PINK-SAMPLE CUSTODIAN / GOLDENROD-CLIENT

American Analytical Laboratories, LLC.

Sample Receipt Checklist

Client Name **CA RICH** Date and Time Receive **1/11/2012 11:53:46 AM**

Work Order Numbe **1201054** RcptNo: **1** Received by **CD**

COC_ID: CoolerID:

Checklist completed by Signature 1/11/12 Date Reviewed by Initials 1/11/12 Date

Matrix: Carrier name AAL

Shipping container/cooler in good condition?	Yes ☑	No ☐	Not Presen ☐
Custody seals intact on shippping container/cooler?	Yes ☐	No ☐	Not Presen ☑
Custody seals intact on sample bottles?	Yes ☐	No ☐	Not Presen ☑
Chain of custody present?	Yes ☑	No ☐	
Chain of custody signed when relinquished and received?	Yes ☑	No ☐	
Chain of custody agrees with sample labels?	Yes ☑	No ☐	
Samples in proper container/bottle?	Yes ☑	No ☐	
Sample containers intact?	Yes ☑	No ☐	
Sufficient sample volume for indicated test?	Yes ☑	No ☐	
All samples received within holding time?	Yes ☑	No ☐	
Container/Temp Blank temperature in compliance?	Yes ☑	No ☐	
Water - VOA vials have zero headspace?	No VOA vials submitted ☑	Yes ☐	No ☐
Water - pH acceptable upon receipt?	Yes ☐	No ☐	N/A ☐

Adjusted? _____ Checked b _____

Any No and/or NA (not applicable) response must be detailed in the comments section be

Client contacted _____ Date contacted: _____ Person contacted _____

Contacted by: _____ Regarding: _____

Comments:

Corrective Action _____

American Analytical Laboratories, LLC.

Date: *11-Jan-12*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	WC- 1/10/12
Lab Order:	1201054	**Collection Date:**	1/10/2012 1:00:00 PM
Project:	260 West 26th St., NY, NY	**Matrix:**	SOIL
Lab ID:	1201054-01A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PERCENT MOISTURE			D2216				Analyst: CF
Percent Moisture	9.78	0	0		wt%	1	1/11/2012
VOLATILE SW-846 METHOD 8260			SW8260C				Analyst: LA
1,1,1,2-Tetrachloroethane	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
1,1,1-Trichloroethane	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
1,1,2,2-Tetrachloroethane	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
1,1,2-Trichloro-1,2,2-trifluoroethan	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
1,1,2-Trichloroethane	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
1,1-Dichloroethane	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
1,1-Dichloroethene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
1,1-Dichloropropene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
1,2,3-Trichlorobenzene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
1,2,3-Trichloropropane	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
1,2,4,5-Tetramethylbenzene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
1,2,4-Trichlorobenzene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
1,2,4-Trimethylbenzene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
1,2-Dibromo-3-chloropropane	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
1,2-Dibromoethane	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
1,2-Dichlorobenzene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
1,2-Dichloroethane	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
1,2-Dichloropropane	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
1,3,5-Trimethylbenzene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
1,3-Dichlorobenzene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
1,3-dichloropropane	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
1,4-Dichlorobenzene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
1,4-Dioxane	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
2,2-Dichloropropane	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
2-Butanone	U	1.7	5.6	C	µg/Kg-dry	1	1/11/2012 1:19:00 PM
2-Chloroethyl vinyl ether	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
2-Chlorotoluene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
2-Hexanone	U	1.7	5.6	C	µg/Kg-dry	1	1/11/2012 1:19:00 PM
2-Propanol	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
4-Chlorotoluene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *11-Jan-12*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	WC- 1/10/12
Lab Order:	1201054	**Collection Date:**	1/10/2012 1:00:00 PM
Project:	260 West 26th St., NY, NY	**Matrix:**	SOIL
Lab ID:	1201054-01A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: LA
4-Isopropyltoluene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
4-Methyl-2-pentanone	U	1.7	5.6	C	µg/Kg-dry	1	1/11/2012 1:19:00 PM
Acetone	U	1.7	5.6	C	µg/Kg-dry	1	1/11/2012 1:19:00 PM
Acrolein	U	2.8	11	C	µg/Kg-dry	1	1/11/2012 1:19:00 PM
Acrylonitrile	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Benzene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Bromobenzene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Bromochloromethane	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Bromodichloromethane	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Bromoform	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Bromomethane	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Carbon disulfide	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Carbon tetrachloride	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Chlorobenzene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Chlorodifluoromethane	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Chloroethane	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Chloroform	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Chloromethane	U	0.56	5.6	C	µg/Kg-dry	1	1/11/2012 1:19:00 PM
cis-1,2-Dichloroethene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
cis-1,3-Dichloropropene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Dibromochloromethane	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Dibromomethane	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Dichlorodifluoromethane	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Diisopropyl ether	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Ethanol	U	2.8	11		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Ethyl acetate	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Ethylbenzene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Freon-114	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Hexachlorobutadiene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Isopropyl acetate	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Isopropylbenzene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
m,p-Xylene	U	1.1	11		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Methyl Acetate	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *11-Jan-12*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	WC- 1/10/12
Lab Order:	1201054	**Collection Date:**	1/10/2012 1:00:00 PM
Project:	260 West 26th St., NY, NY	**Matrix:**	SOIL
Lab ID:	1201054-01A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: LA
Methyl tert-butyl ether	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Methylene chloride	7.8	0.56	5.6	B	µg/Kg-dry	1	1/11/2012 1:19:00 PM
n-Amyl acetate	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Naphthalene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
n-Butyl acetate	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
n-Butylbenzene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
n-Propyl acetate	U	0.56	5.6	C	µg/Kg-dry	1	1/11/2012 1:19:00 PM
n-Propylbenzene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
o-Xylene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
p-Diethylbenzene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
p-Ethyltoluene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
sec-Butylbenzene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Styrene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
t-Butyl alcohol	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
tert-Butylbenzene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Tetrachloroethene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Toluene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
trans-1,2-Dichloroethene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
trans-1,3-Dichloropropene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Trichloroethene	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Trichlorofluoromethane	U	0.56	5.6	C	µg/Kg-dry	1	1/11/2012 1:19:00 PM
Vinyl acetate	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Vinyl chloride	U	0.56	5.6		µg/Kg-dry	1	1/11/2012 1:19:00 PM
Surr: 4-Bromofluorobenzene	91.4	0	42-133		%REC	1	1/11/2012 1:19:00 PM
Surr: Dibromofluoromethane	100	0	50-133		%REC	1	1/11/2012 1:19:00 PM
Surr: Toluene-d8	95.3	0	53-130		%REC	1	1/11/2012 1:19:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *11-Jan-12*

CLIENT: CA Rich Consultants Inc.
Work Order: 1201054
Project: 260 West 26th St., NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DryFull8260_Soil

Sample ID: **V624LCS-011112HS** SampType: **LCS** TestCode: **DryFull8260_** Units: **µg/Kg** Prep Date: **1/11/2012** RunNo: **61649**
Client ID: **LCSS** Batch ID: **R61649** TestNo: **SW8260C** Analysis Date: **1/11/2012** SeqNo: **865580**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
1,1,1-Trichloroethane	49	5.0	50.00	0	97.6	40	125				
1,1,2,2-Tetrachloroethane	47	5.0	50.00	0	94.0	41	130				
1,1,2-Trichloroethane	49	5.0	50.00	0	98.3	43	121				
1,1-Dichloroethane	48	5.0	50.00	0	97.0	42	126				
1,1-Dichloroethene	50	5.0	50.00	0	101	40	126				
1,2-Dichlorobenzene	42	5.0	50.00	0	83.1	41	122				
1,2-Dichloroethane	48	5.0	50.00	0	95.1	42	133				
1,2-Dichloropropane	48	5.0	50.00	0	96.0	41	128				
1,3-Dichlorobenzene	43	5.0	50.00	0	86.4	45	119				
1,4-Dichlorobenzene	41	5.0	50.00	0	81.6	46	121				
2-Chloroethyl vinyl ether	46	5.0	50.00	0	91.8	30	135				
Benzene	47	5.0	50.00	0	94.5	35	123				
Bromodichloromethane	47	5.0	50.00	0	93.4	37	130				
Bromoform	44	5.0	50.00	0	89.0	43	121				
Bromomethane	25	5.0	50.00	0	49.2	32	130				
Carbon tetrachloride	51	5.0	50.00	0	103	37	134				
Chlorobenzene	41	5.0	50.00	0	81.9	40	124				
Chloroethane	45	5.0	50.00	0	90.9	35	141				
Chloroform	49	5.0	50.00	0	97.8	36	126				
Chloromethane	27	5.0	50.00	0	53.8	42	141				C
cis-1,3-Dichloropropene	47	5.0	50.00	0	94.4	30	130				
Dibromochloromethane	48	5.0	50.00	0	95.3	43	125				
Ethylbenzene	42	5.0	50.00	0	84.1	44	122				
Methylene chloride	44	5.0	50.00	0	87.6	32	132				B
Tetrachloroethene	47	5.0	50.00	0	93.7	31	120				
Toluene	46	5.0	50.00	0	92.6	42	124				
trans-1,2-Dichloroethene	46	5.0	50.00	0	92.2	38	122				
trans-1,3-Dichloropropene	47	5.0	50.00	0	94.4	45	123				
Trichloroethene	49	5.0	50.00	0	97.1	46	124				
Trichlorofluoromethane	56	5.0	50.00	0	112	45	137				C

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	H	Holding times for preparation or analy
J	Analyte detected below quantitation limits	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit
R	RPD outside accepted recovery limits	S	Spike Recovery outside accepted recovery limits	U	Indicates the compound was analyzed

CLIENT: CA Rich Consultants Inc.
Work Order: 1201054
Project: 260 West 26th St., NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DryFull8260_Soil

Sample ID: V624LCS-011112HS	SampType: LCS	TestCode: DryFull8260_	Units: µg/Kg	Prep Date: 1/11/2012	RunNo: 61649
Client ID: LCSS	Batch ID: R61649	TestNo: SW8260C		Analysis Date: 1/11/2012	SeqNo: 865580

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Vinyl chloride	49	5.0	50.00	0	97.3	46	139				
Surr: 4-Bromofluorobenzene	51		50.00		102	42	133				
Surr: Dibromofluoromethane	52		50.00		104	50	133				
Surr: Toluene-d8	52		50.00		104	53	130				

Sample ID: VBLK-011112HS	SampType: MBLK	TestCode: DryFull8260_	Units: µg/Kg	Prep Date: 1/11/2012	RunNo: 61649
Client ID: PBS	Batch ID: R61649	TestNo: SW8260C		Analysis Date: 1/11/2012	SeqNo: 865581

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
1,1,1,2-Tetrachloroethane	U	5.0									
1,1,1-Trichloroethane	U	5.0									
1,1,2,2-Tetrachloroethane	U	5.0									
1,1,2-Trichloro-1,2,2-trifluoroethane	U	5.0									
1,1,2-Trichloroethane	U	5.0									
1,1-Dichloroethane	U	5.0									
1,1-Dichloroethene	U	5.0									
1,1-Dichloropropene	U	5.0									
1,2,3-Trichlorobenzene	U	5.0									
1,2,3-Trichloropropane	U	5.0									
1,2,4,5-Tetramethylbenzene	U	5.0									
1,2,4-Trichlorobenzene	U	5.0									
1,2,4-Trimethylbenzene	U	5.0									
1,2-Dibromo-3-chloropropane	U	5.0									
1,2-Dibromoethane	U	5.0									
1,2-Dichlorobenzene	U	5.0									
1,2-Dichloroethane	U	5.0									
1,2-Dichloropropane	U	5.0									
1,3,5-Trimethylbenzene	U	5.0									
1,3-Dichlorobenzene	U	5.0									
1,3-dichloropropane	U	5.0									
1,4-Dichlorobenzene	U	5.0									

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	H	Holding times for preparation or analy
J	Analyte detected below quantitation limits	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit
R	RPD outside accepted recovery limits	S	Spike Recovery outside accepted recovery limits	U	Indicates the compound was analyzed

CLIENT: CA Rich Consultants Inc.
Work Order: 1201054
Project: 260 West 26th St., NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DryFull8260_Soil

Sample ID: **VBLK-011112HS** SampType: **MBLK** TestCode: **DryFull8260_** Units: **µg/Kg** Prep Date: **1/11/2012** RunNo: **61649**
Client ID: **PBS** Batch ID: **R61649** TestNo: **SW8260C** Analysis Date: **1/11/2012** SeqNo: **865581**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
1,4-Dioxane	U	5.0									
2,2-Dichloropropane	U	5.0									
2-Butanone	U	5.0									C
2-Chloroethyl vinyl ether	U	5.0									
2-Chlorotoluene	U	5.0									
2-Hexanone	U	5.0									C
2-Propanol	U	5.0									
4-Chlorotoluene	U	5.0									
4-Isopropyltoluene	U	5.0									
4-Methyl-2-pentanone	U	5.0									C
Acetone	U	5.0									C
Acrolein	U	10									C
Acrylonitrile	U	5.0									
Benzene	U	5.0									
Bromobenzene	U	5.0									
Bromochloromethane	U	5.0									
Bromodichloromethane	U	5.0									
Bromoform	U	5.0									
Bromomethane	U	5.0									
Carbon disulfide	U	5.0									
Carbon tetrachloride	U	5.0									
Chlorobenzene	U	5.0									
Chlorodifluoromethane	U	5.0									
Chloroethane	U	5.0									
Chloroform	U	5.0									
Chloromethane	U	5.0									C
cis-1,2-Dichloroethene	U	5.0									
cis-1,3-Dichloropropene	U	5.0									
Dibromochloromethane	U	5.0									
Dibromomethane	U	5.0									
Dichlorodifluoromethane	U	5.0									

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	H	Holding times for preparation or analy
J	Analyte detected below quantitation limits	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit
R	RPD outside accepted recovery limits	S	Spike Recovery outside accepted recovery limits	U	Indicates the compound was analyzed

CLIENT: CA Rich Consultants Inc.
Work Order: 1201054
Project: 260 West 26th St., NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DryFull8260_Soil

Sample ID: **VBLK-011112HS**	SampType: **MBLK**	TestCode: **DryFull8260_**	Units: **µg/Kg**	Prep Date: **1/11/2012**	RunNo: **61649**
Client ID: **PBS**	Batch ID: **R61649**	TestNo: **SW8260C**		Analysis Date: **1/11/2012**	SeqNo: **865581**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Diisopropyl ether	U	5.0									
Ethanol	U	10									
Ethyl acetate	U	5.0									
Ethylbenzene	U	5.0									
Freon-114	U	5.0									
Hexachlorobutadiene	U	5.0									
Isopropyl acetate	U	5.0									
Isopropylbenzene	U	5.0									
m,p-Xylene	U	10									
Methyl Acetate	U	5.0									
Methyl tert-butyl ether	U	5.0									
Methylene chloride	2.6	5.0									J
n-Amyl acetate	U	5.0									
Naphthalene	U	5.0									
n-Butyl acetate	U	5.0									
n-Butylbenzene	U	5.0									
n-Propyl acetate	U	5.0									C
n-Propylbenzene	U	5.0									
o-Xylene	U	5.0									
p-Diethylbenzene	U	5.0									
p-Ethyltoluene	U	5.0									
sec-Butylbenzene	U	5.0									
Styrene	U	5.0									
t-Butyl alcohol	U	5.0									
tert-Butylbenzene	U	5.0									
Tetrachloroethene	U	5.0									
Toluene	U	5.0									
trans-1,2-Dichloroethene	U	5.0									
trans-1,3-Dichloropropene	U	5.0									
Trichloroethene	U	5.0									
Trichlorofluoromethane	U	5.0									C

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	H	Holding times for preparation or analy
J	Analyte detected below quantitation limits	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit
R	RPD outside accepted recovery limits	S	Spike Recovery outside accepted recovery limits	U	Indicates the compound was analyzed

CLIENT: CA Rich Consultants Inc.
Work Order: 1201054
Project: 260 West 26th St., NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DryFull8260_Soil

Sample ID: **VBLK-011112HS**	SampType: **MBLK**	TestCode: **DryFull8260_**	Units: **µg/Kg**	Prep Date: **1/11/2012**		RunNo: **61649**	
Client ID: **PBS**	Batch ID: **R61649**	TestNo: **SW8260C**		Analysis Date: **1/11/2012**		SeqNo: **865581**	

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Vinyl acetate	U	5.0									
Vinyl chloride	U	5.0									
Surr: 4-Bromofluorobenzene	49		50.00		97.6	42	133				
Surr: Dibromofluoromethane	54		50.00		108	50	133				
Surr: Toluene-d8	48		50.00		95.6	53	130				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	H	Holding times for preparation or analy
J	Analyte detected below quantitation limits	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit
R	RPD outside accepted recovery limits	S	Spike Recovery outside accepted recovery limits	U	Indicates the compound was analyzed

AMERICAN ANALYTICAL LABORATORIES

NYSDOH 11418
NJDEP NY050
CTDOH PH-0205
PADEP 68-00573

Thursday, February 09, 2012

Steve Malinowski
CA Rich Consultants Inc.
17 Dupont Street
Plainview, NY 11803

TEL: (516) 576-8844
FAX (516) 576-0093

RE: 260 West 26th Street, New York, NY

Order No.: 1202043

Dear Steve Malinowski:

American Analytical Laboratories, LLC. received 6 sample(s) on 2/6/2012 for the analyses presented in the following report.

Samples were analyzed in accordance with the test procedures documented on the chain of custody and detailed throughout the text of this report.

The results reported herein relate only to the items tested or to the samples as received by the laboratory. This report may not be reproduced, except in full, without the approval of American Analytical Laboratories, LLC and is not considered complete without a cover page and chain of custody documentation. The limits (LOQ) provided in the data package are analytical reporting limits and not Federal or Local mandated values to which the sample results should be compared.

There were no problems with the analyses and all data for associated QC met laboratory specifications. If there are any exceptions a Case Narrative is provided in the report or the data is qualified. This package has been reviewed by American Analytical Laboratories' QA Department/Laboratory Director to comply with NELAC standards prior to report submittal. This report consists of 30 pages.

If you have any questions regarding these tests results, please do not hesitate to call (631) 454-6100 or email me directly at lbeyer@american-analytical.com.

Sincerely,

Lori Beyer
Lab Director

American Analytical Laboratories, LLC.

Date: *09-Feb-12*

CLIENT: CA Rich Consultants Inc.
Project: 260 West 26th Street, New York, NY
Lab Order: 1202043

Work Order Sample Summary

Lab Sample ID	Client Sample ID	Date Collected	Date Received
1202043-01A	B1 (16 ft.)	2/3/2012 12:15:00 PM	2/6/2012
1202043-02A	A1 (14-16 ft.)	2/3/2012 12:30:00 PM	2/6/2012
1202043-03A	A1 (16-18 ft.)	2/3/2012 12:40:00 PM	2/6/2012
1202043-04A	B1 (14-16 ft.)	2/3/2012 12:10:00 PM	2/6/2012
1202043-05A	B1 (16-18 ft.)	2/3/2012 12:20:00 PM	2/6/2012
1202043-06A	A1-B1 (14.18 ft.)	2/3/2012 12:45:00 PM	2/6/2012
1202043-06B	A1-B1 (14.18 ft.)	2/3/2012 12:45:00 PM	2/6/2012

AMERICAN ANALYTICAL LABORATORIES
56 TOLEDO STREET • FARMINGDALE, NEW YORK 11735
(631) 454-6100 • FAX (631) 454-8027
www.american-analytical.com

NYSDOH	11418
CTDOH	PH-0205
NJDEP	NY050
PADEP	68-573

CHAIN OF CUSTODY / REQUEST FOR ANALYSIS DOCUMENT

CLIENT NAME/ADDRESS: Ca Rich Consultants Inc, 17 Dupont St, Plainview NY 11803
CONTACT: Steve Malinowski (516) 576-8844
SAMPLER (SIGNATURE):
SAMPLER NAME (PRINT): Jessica Presicia
SAMPLE(S) SEALED: YES / NO
CORRECT CONTAINER(S): YES / NO
TEMPERATURE (° C): 4.0
PROJECT LOCATION: 260 West 26th St, NY, NY

LABORATORY ID# LAB USE ONLY	MATRIX/ TYPE	NO. OF CONTAINERS	SAMPLING DATE	SAMPLING TIME	SAMPLE # - LOCATION	VOCs 8260	TPH 8015	TCLP RCRA Metals	Total metals (listed below)	PCBs	PAH	Ignitability / Corrosivity / Reactivity	
1202043-01A	S/G	1	2/2/12	12:15	B1 (16Ft)	X							
02A	S/C	1	2/3/12	12:30	A1 (14-16Ft)		X						
03A	S/C	1	2/3/12	12:40	A1 (16-18Ft)		X	X	X	X	X	X	X — TPH only
04A	S/C	1	2/3/12	12:10	B1 (14-16Ft)		X	X	X	X	X	X	X
05A	S/C	1	2/3/12	12:20	B1 (16-18Ft)		X	X	X	X	X	X	X
06A[B]	S/C	1	2/3/12	12:45	A1-B1 (14-18Ft)			X	X	X	X	X	X

COMMENTS / INSTRUCTIONS: Total Metals include - Arsenic, antimony, barium, beryllium, Cadmium, copper, lead, nickel, thallium, zinc, chromium, mercury, Selenium and Silver.
Samples must be on ICE (<6° C)

MATRIX S=SOIL; W=WATER; SL=SLUDGE; A=AIR; M=MISCELLANEOUS
TYPE G=GRAB; C=COMPOSITE

TURNAROUND REQUIRED: STANDARD ☐ (7-10 business days) STAT ☐ ASAP BY / /
E-MAIL ADDRESS FOR RESULTS: Smalinowski@caRichinc.com

RELINQUISHED BY (SIGNATURE)	DATE / TIME	PRINTED NAME	RECEIVED BY LAB (SIGNATURE)	DATE / TIME	PRINTED NAME
	2/3/12	Jessica Presicia		2-6-12 9:45	
	2-6-12 10:05			2/6/12 10:05	

WHITE-OFFICE / CANARY-LAB / PINK-SAMPLE CUSTODIAN / GOLDENROD-CLIENT

American Analytical Laboratories, LLC.

Sample Receipt Checklist

Client Name **CA RICH** Date and Time Receive **2/6/2012 10:09:23 AM**

Work Order Numbe **1202043** RcptNo: **1** Received by **LB**

COC_ID: CoolerID:

Checklist completed by Signature Date **2/6/12** Reviewed by Initials **KBK** Date **2/6/12**

Matrix: Carrier name Lab Courier

Shipping container/cooler in good condition?	Yes ☑	No ☐	Not Presen ☐
Custody seals intact on shippping container/cooler?	Yes ☐	No ☐	Not Presen ☑
Custody seals intact on sample bottles?	Yes ☐	No ☐	Not Presen ☑
Chain of custody present?	Yes ☑	No ☐	
Chain of custody signed when relinquished and received?	Yes ☑	No ☐	
Chain of custody agrees with sample labels?	Yes ☑	No ☐	
Samples in proper container/bottle?	Yes ☑	No ☐	
Sample containers intact?	Yes ☑	No ☐	
Sufficient sample volume for indicated test?	Yes ☑	No ☐	
All samples received within holding time?	Yes ☑	No ☐	
Container/Temp Blank temperature in compliance?	Yes ☑	No ☐	
Water - VOA vials have zero headspace?	No VOA vials submitted ☐	Yes ☑	No ☐
Water - pH acceptable upon receipt?	Yes ☑	No ☐	N/A ☐

Adjusted? _____ Checked b _____

Any No and/or NA (not applicable) response must be detailed in the comments section be

Client contacted _____ Date contacted: _____ Person contacted _____

Contacted by: _____ Regarding: _____

Comments:

Corrective Action _____

American Analytical Laboratories, LLC.

Date: *09-Feb-12*

ELAP ID : 11418

CLIENT: CA Rich Consultants Inc.
Lab Order: 1202043
Project: 260 West 26th Street, New York, NY
Lab ID: 1202043-01A

Client Sample ID: B1 (16 ft.)
Collection Date: 2/3/2012 12:15:00 PM
Matrix: SOIL

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	14.0	0	0		wt%	1	2/6/2012
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: **LA**
1,1,1,2-Tetrachloroethane	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
1,1,1-Trichloroethane	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
1,1,2,2-Tetrachloroethane	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
1,1,2-Trichloro-1,2,2-trifluoroethan	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
1,1,2-Trichloroethane	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
1,1-Dichloroethane	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
1,1-Dichloroethene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
1,1-Dichloropropene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
1,2,3-Trichlorobenzene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
1,2,3-Trichloropropane	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
1,2,4,5-Tetramethylbenzene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
1,2,4-Trichlorobenzene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
1,2,4-Trimethylbenzene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
1,2-Dibromo-3-chloropropane	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
1,2-Dibromoethane	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
1,2-Dichlorobenzene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
1,2-Dichloroethane	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
1,2-Dichloropropane	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
1,3,5-Trimethylbenzene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
1,3-Dichlorobenzene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
1,3-dichloropropane	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
1,4-Dichlorobenzene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
1,4-Dioxane	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
2,2-Dichloropropane	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
2-Butanone	U	1.73	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
2-Chloroethyl vinyl ether	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
2-Chlorotoluene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
2-Hexanone	U	1.73	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
2-Propanol	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
4-Chlorotoluene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.	

American Analytical Laboratories, LLC.

Date: *09-Feb-12*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	B1 (16 ft.)
Lab Order:	1202043	**Collection Date:**	2/3/2012 12:15:00 PM
Project:	260 West 26th Street, New York, NY	**Matrix:**	SOIL
Lab ID:	1202043-01A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: LA
4-Isopropyltoluene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
4-Methyl-2-pentanone	U	1.73	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Acetone	U	1.73	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Acrolein	U	2.88	12		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Acrylonitrile	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Benzene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Bromobenzene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Bromochloromethane	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Bromodichloromethane	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Bromoform	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Bromomethane	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Carbon disulfide	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Carbon tetrachloride	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Chlorobenzene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Chlorodifluoromethane	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Chloroethane	U	0.58	5.8	C	µg/Kg-dry	1	2/7/2012 12:29:00 AM
Chloroform	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Chloromethane	U	0.58	5.8	C	µg/Kg-dry	1	2/7/2012 12:29:00 AM
cis-1,2-Dichloroethene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
cis-1,3-Dichloropropene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Dibromochloromethane	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Dibromomethane	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Dichlorodifluoromethane	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Diisopropyl ether	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Ethanol	U	2.88	12		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Ethyl acetate	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Ethylbenzene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Freon-114	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Hexachlorobutadiene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Isopropyl acetate	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Isopropylbenzene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
m,p-Xylene	U	1.15	12		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Methyl Acetate	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.	

American Analytical Laboratories, LLC.

Date: *09-Feb-12*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	B1 (16 ft.)
Lab Order:	1202043	**Collection Date:**	2/3/2012 12:15:00 PM
Project:	260 West 26th Street, New York, NY	**Matrix:**	SOIL
Lab ID:	1202043-01A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
VOLATILE SW-846 METHOD 8260			**SW8260C**				Analyst: LA
Methyl tert-butyl ether	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Methylene chloride	5.9	0.58	5.8	B	µg/Kg-dry	1	2/7/2012 12:29:00 AM
n-Amyl acetate	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Naphthalene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
n-Butyl acetate	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
n-Butylbenzene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
n-Propyl acetate	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
n-Propylbenzene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
o-Xylene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
p-Diethylbenzene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
p-Ethyltoluene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
sec-Butylbenzene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Styrene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
t-Butyl alcohol	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
tert-Butylbenzene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Tetrachloroethene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Toluene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
trans-1,2-Dichloroethene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
trans-1,3-Dichloropropene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Trichloroethene	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Trichlorofluoromethane	U	0.58	5.8	C	µg/Kg-dry	1	2/7/2012 12:29:00 AM
Vinyl acetate	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Vinyl chloride	U	0.58	5.8		µg/Kg-dry	1	2/7/2012 12:29:00 AM
Surr: 4-Bromofluorobenzene	83.8	0	42-133		%REC	1	2/7/2012 12:29:00 AM
Surr: Dibromofluoromethane	100	0	50-133		%REC	1	2/7/2012 12:29:00 AM
Surr: Toluene-d8	89.3	0	53-130		%REC	1	2/7/2012 12:29:00 AM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Feb-12*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	A1 (14-16 ft.)
Lab Order:	1202043	**Collection Date:**	2/3/2012 12:30:00 PM
Project:	260 West 26th Street, New York, NY	**Matrix:**	SOIL
Lab ID:	1202043-02A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TOTAL DRO AS #2 FUEL (C8-C40)			**SW8015C**		**SW3550C**		Analyst: **LDS**
Total DRO TPH	280	3.06	12		mg/Kg-dry	1	2/8/2012 5:50:00 PM
Surr: o-Terphenyl	101	0	31-137		%REC	1	2/8/2012 5:50:00 PM
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	19.1	0	0		wt%	1	2/6/2012

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.

American Analytical Laboratories, LLC.

Date: *09-Feb-12*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	A1 (16-18 ft.)
Lab Order:	1202043	**Collection Date:**	2/3/2012 12:40:00 PM
Project:	260 West 26th Street, New York, NY	**Matrix:**	SOIL
Lab ID:	1202043-03A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TOTAL DRO AS #2 FUEL (C8-C40)			**SW8015C**		**SW3550C**		Analyst: **LDS**
Total DRO TPH	450	2.94	12		mg/Kg-dry	1	2/8/2012 6:24:00 PM
Surr: o-Terphenyl	108	0	31-137		%REC	1	2/8/2012 6:24:00 PM
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	15.7	0	0		wt%	1	2/6/2012

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Feb-12*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	B1 (14-16 ft.)
Lab Order:	1202043	**Collection Date:**	2/3/2012 12:10:00 PM
Project:	260 West 26th Street, New York, NY	**Matrix:**	SOIL
Lab ID:	1202043-04A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TOTAL DRO AS #2 FUEL (C8-C40)			**SW8015C**		**SW3550C**		Analyst: **LDS**
Total DRO TPH	340	2.76	11		mg/Kg-dry	1	2/8/2012 6:57:00 PM
Surr: o-Terphenyl	109	0	31-137		%REC	1	2/8/2012 6:57:00 PM
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	9.79	0	0		wt%	1	2/6/2012

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Feb-12*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	B1 (16-18 ft.)
Lab Order:	1202043	**Collection Date:**	2/3/2012 12:20:00 PM
Project:	260 West 26th Street, New York, NY	**Matrix:**	SOIL
Lab ID:	1202043-05A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TOTAL DRO AS #2 FUEL (C8-C40)			**SW8015C**		**SW3550C**		Analyst: **LDS**
Total DRO TPH	58	2.73	11		mg/Kg-dry	1	2/8/2012 7:31:00 PM
Surr: o-Terphenyl	99.1	0	31-137		%REC	1	2/8/2012 7:31:00 PM
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	9.15	0	0		wt%	1	2/6/2012

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.

American Analytical Laboratories, LLC.

Date: *09-Feb-12*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	A1-B1 (14.18 ft.)
Lab Order:	1202043	**Collection Date:**	2/3/2012 12:45:00 PM
Project:	260 West 26th Street, New York, NY	**Matrix:**	SOIL
Lab ID:	1202043-06A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
MERCURY			**SW7471B**		**SW7471B**		Analyst: **JP**
Mercury	U	0.005	0.0103		mg/Kg-dry	1	2/6/2012 1:56:51 PM
PCB'S AS AROCLORS SW-846 METHOD 8082			**SW8082A**		**SW3550C**		Analyst: **SB**
Aroclor 1016	U	1.06	42		µg/Kg-dry	1	2/8/2012 3:22:00 PM
Aroclor 1221	U	1.06	42		µg/Kg-dry	1	2/8/2012 3:22:00 PM
Aroclor 1232	U	1.06	42		µg/Kg-dry	1	2/8/2012 3:22:00 PM
Aroclor 1242	U	1.06	42		µg/Kg-dry	1	2/8/2012 3:22:00 PM
Aroclor 1248	U	1.06	42		µg/Kg-dry	1	2/8/2012 3:22:00 PM
Aroclor 1254	U	1.06	42		µg/Kg-dry	1	2/8/2012 3:22:00 PM
Aroclor 1260	U	1.06	42		µg/Kg-dry	1	2/8/2012 3:22:00 PM
Aroclor 1262	U	1.06	42		µg/Kg-dry	1	2/8/2012 3:22:00 PM
Aroclor 1268	U	1.06	42		µg/Kg-dry	1	2/8/2012 3:22:00 PM
Surr: TCX	80.9	0	17-151		%REC	1	2/8/2012 3:22:00 PM
Surr: DCB	64.8	0	16-152		%REC	1	2/8/2012 3:22:00 PM
PERCENT MOISTURE			**D2216**				Analyst: **KK**
Percent Moisture	9.67	0	0		wt%	1	2/6/2012
PRIORITY POLLUTANT METALS + BARIUM			**SW6010C**		**SW3050B**		Analyst: **JP**
Antimony	U	0.22	0.547		mg/Kg-dry	1	2/6/2012 1:54:20 PM
Arsenic	0.854	0.22	0.547		mg/Kg-dry	1	2/6/2012 1:54:20 PM
Barium	53.5	0.22	0.438		mg/Kg-dry	1	2/6/2012 1:54:20 PM
Beryllium	U	0.11	0.438		mg/Kg-dry	1	2/6/2012 1:54:20 PM
Cadmium	U	0.11	0.438		mg/Kg-dry	1	2/6/2012 1:54:20 PM
Chromium	13.5	0.11	0.438		mg/Kg-dry	1	2/6/2012 1:54:20 PM
Copper	7.30	0.11	0.438		mg/Kg-dry	1	2/6/2012 1:54:20 PM
Lead	14.8	0.22	0.438		mg/Kg-dry	1	2/6/2012 1:54:20 PM
Nickel	19.7	0.11	0.438		mg/Kg-dry	1	2/6/2012 1:54:20 PM
Selenium	U	0.22	0.547		mg/Kg-dry	1	2/6/2012 1:54:20 PM
Silver	U	0.11	0.438		mg/Kg-dry	1	2/6/2012 1:54:20 PM
Thallium	0.804	0.33	0.547		mg/Kg-dry	1	2/6/2012 1:54:20 PM
Zinc	21.4	0.11	0.438		mg/Kg-dry	1	2/6/2012 1:54:20 PM
SEMIVOLATILE SW-846 METHOD 8270 (PAH)			**SW8270D**		**SW3550C**		Analyst: **LDS**
Acenaphthene	U	27.5	280		µg/Kg-dry	1	2/8/2012 7:10:00 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.	

American Analytical Laboratories, LLC.

Date: *09-Feb-12*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	A1-B1 (14.18 ft.)
Lab Order:	1202043	**Collection Date:**	2/3/2012 12:45:00 PM
Project:	260 West 26th Street, New York, NY	**Matrix:**	SOIL
Lab ID:	1202043-06A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
SEMIVOLATILE SW-846 METHOD 8270 (PAH)			**SW8270D**		**SW3550C**		Analyst: **LDS**
Acenaphthylene	U	27.5	280		µg/Kg-dry	1	2/8/2012 7:10:00 PM
Anthracene	U	27.5	280		µg/Kg-dry	1	2/8/2012 7:10:00 PM
Benzo(a)anthracene	56	27.5	280	J	µg/Kg-dry	1	2/8/2012 7:10:00 PM
Benzo(a)pyrene	55	27.5	280	J	µg/Kg-dry	1	2/8/2012 7:10:00 PM
Benzo(b)fluoranthene	61	27.5	280	J	µg/Kg-dry	1	2/8/2012 7:10:00 PM
Benzo(g,h,i)perylene	42	27.5	280	J	µg/Kg-dry	1	2/8/2012 7:10:00 PM
Benzo(k)fluoranthene	51	27.5	280	J	µg/Kg-dry	1	2/8/2012 7:10:00 PM
Chrysene	55	27.5	280	J	µg/Kg-dry	1	2/8/2012 7:10:00 PM
Dibenzo(a,h)anthracene	U	27.5	280		µg/Kg-dry	1	2/8/2012 7:10:00 PM
Fluoranthene	120	27.5	280	J	µg/Kg-dry	1	2/8/2012 7:10:00 PM
Fluorene	U	27.5	280		µg/Kg-dry	1	2/8/2012 7:10:00 PM
Indeno(1,2,3-c,d)pyrene	51	27.5	280	J	µg/Kg-dry	1	2/8/2012 7:10:00 PM
Naphthalene	U	27.5	280		µg/Kg-dry	1	2/8/2012 7:10:00 PM
Phenanthrene	63	27.5	280	J	µg/Kg-dry	1	2/8/2012 7:10:00 PM
Pyrene	110	27.5	280	J	µg/Kg-dry	1	2/8/2012 7:10:00 PM
Surr: 2-Fluorobiphenyl	91.2	0	21-117		%REC	1	2/8/2012 7:10:00 PM
Surr: 4-Terphenyl-d14	92.2	0	21-132		%REC	1	2/8/2012 7:10:00 PM
Surr: Nitrobenzene-d5	82.1	0	18-116		%REC	1	2/8/2012 7:10:00 PM
IGNITABILITY/FLASHPOINT SW-846 1020			**SW1020B**				Analyst: **STP**
Ignitability	>	0	140		°F	1	2/6/2012
SOIL PH MEASURED IN WATER			**SW9045C**				Analyst: **JP**
pH	9.32	0	1.00		pH Units	1	2/8/2012 3:28:00 PM
TEMPERATURE			**M2550 B**				Analyst: **JP**
Temp at which pH was measured	18.5	0	0		°C	1	2/8/2012 3:28:00 PM
REACTIVE CYANIDE			**SW7.3.3.2**				Analyst: **STP**
Reactive Cyanide	U	0.06	0.111		mg/Kg-dry	1	2/6/2012
REACTIVE SULFIDE			**SW7.3.4.2**				Analyst: **STP**
Reactive Sulfide	U	1.11	2.21		mg/Kg-dry	1	2/6/2012

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank
C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range
H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits
LOD	Limit of Detection
LOQ	Limit of Quantitation
P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit
S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.	

American Analytical Laboratories, LLC.

Date: *09-Feb-12*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	A1-B1 (14.18 ft.)
Lab Order:	1202043	**Collection Date:**	2/3/2012 12:45:00 PM
Project:	260 West 26th Street, New York, NY	**Matrix:**	SOIL
Lab ID:	1202043-06B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP MERCURY			**SW1311/7471B**		**SW1311**		Analyst: **JP**
Mercury	U	0.0005	0.0200		mg/L	1	2/7/2012 2:54:00 PM
TCLP METALS			**SW1311/6010C**		**SW1311**		Analyst: **JP**
Arsenic	U	0.01	0.0500		mg/L	1	2/8/2012 3:48:13 PM
Barium	1.28	1	5.00	J	mg/L	1	2/8/2012 3:48:13 PM
Cadmium	U	0.005	0.0500		mg/L	1	2/8/2012 3:48:13 PM
Chromium	0.00645	0.005	0.0500	J	mg/L	1	2/8/2012 3:48:13 PM
Lead	0.343	0.005	0.0500		mg/L	1	2/8/2012 3:48:13 PM
Selenium	U	0.01	0.0500		mg/L	1	2/8/2012 3:48:13 PM
Silver	U	0.005	0.0500		mg/L	1	2/8/2012 3:48:13 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *09-Feb-12*

CLIENT: CA Rich Consultants Inc.
Work Order: 1202043
Project: 260 West 26th Street, New York, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DRY_PPMET_BA

Sample ID: **MB020612B**	SampType: **MBLK**	TestCode: **DRY_PPMET**	Units: **mg/Kg**	Prep Date: **2/6/2012**	RunNo: **62027**
Client ID: **PBS**	Batch ID: **34618**	TestNo: **SW6010C**	**SW3050B**	Analysis Date: **2/6/2012**	SeqNo: **870189**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Antimony	U	0.500									
Arsenic	U	0.500									
Barium	U	0.400									
Beryllium	U	0.400									
Cadmium	U	0.400									
Chromium	U	0.400									
Copper	U	0.400									
Lead	U	0.400									
Nickel	U	0.400									
Selenium	U	0.500									
Silver	U	0.400									
Thallium	U	0.500									
Zinc	U	0.400									

Sample ID: **LCS020612B**	SampType: **LCS**	TestCode: **DRY_PPMET**	Units: **mg/Kg**	Prep Date: **2/6/2012**	RunNo: **62027**
Client ID: **LCSS**	Batch ID: **34618**	TestNo: **SW6010C**	**SW3050B**	Analysis Date: **2/6/2012**	SeqNo: **870190**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Antimony	39.6	0.500	40.00	0	98.9	80	120				
Arsenic	37.4	0.500	40.00	0	93.6	80	120				
Barium	38.1	0.400	40.00	0	95.1	80	120				
Beryllium	41.0	0.400	40.00	0	103	80	120				
Cadmium	41.1	0.400	40.00	0	103	80	120				
Chromium	41.5	0.400	40.00	0	104	80	120				
Copper	41.6	0.400	40.00	0	104	80	120				
Lead	41.3	0.400	40.00	0	103	80	120				
Nickel	40.7	0.400	40.00	0	102	80	120				
Selenium	40.7	0.500	40.00	0	102	80	120				
Silver	37.4	0.400	40.00	0	93.6	80	120				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	H	Holding times for preparation or analy
J	Analyte detected below quantitation limits	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit
R	RPD outside accepted recovery limits	S	Spike Recovery outside accepted recovery limits	U	Indicates the compound was analyzed

CLIENT: CA Rich Consultants Inc.
Work Order: 1202043
Project: 260 West 26th Street, New York, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DRY_PPMET_BA

Sample ID: LCS020612B	SampType: LCS	TestCode: DRY_PPMET	Units: mg/Kg	Prep Date: 2/6/2012	RunNo: 62027
Client ID: LCSS	Batch ID: 34618	TestNo: SW6010C	SW3050B	Analysis Date: 2/6/2012	SeqNo: 870190

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Thallium	39.4	0.500	40.00	0	98.6	80	120				
Zinc	41.6	0.400	40.00	0	104	80	120				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	H	Holding times for preparation or analy
J	Analyte detected below quantitation limits	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit
R	RPD outside accepted recovery limits	S	Spike Recovery outside accepted recovery limits	U	Indicates the compound was analyzed

CLIENT: CA Rich Consultants Inc.
Work Order: 1202043
Project: 260 West 26th Street, New York, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: Dry8082_Soil

Sample ID: **MB-34614**	SampType: **MBLK**	TestCode: **Dry8082_Soil**	Units: **µg/Kg**	Prep Date: **2/7/2012**	RunNo: **62084**
Client ID: **PBS**	Batch ID: **34614**	TestNo: **SW8082A**	**SW3550C**	Analysis Date: **2/8/2012**	SeqNo: **871223**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Aroclor 1016	U	39									
Aroclor 1221	U	39									
Aroclor 1232	U	39									
Aroclor 1242	U	39									
Aroclor 1248	U	39									
Aroclor 1254	U	39									
Aroclor 1260	U	39									
Aroclor 1262	U	39									
Aroclor 1268	U	39									
Surr: TCX	31		24.68		124	17	151				
Surr: DCB	29		24.68		119	16	152				

Sample ID: **LCS-34614**	SampType: **LCS**	TestCode: **Dry8082_Soil**	Units: **µg/Kg**	Prep Date: **2/7/2012**	RunNo: **62084**
Client ID: **LCSS**	Batch ID: **34614**	TestNo: **SW8082A**	**SW3550C**	Analysis Date: **2/8/2012**	SeqNo: **871224**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Aroclor 1221	58	40	49.50	0	117	50	135				
Aroclor 1262	52	40	49.50	0	105	30	145				
Surr: TCX	30		24.75		122	17	151				
Surr: DCB	30		24.75		119	16	152				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	H	Holding times for preparation or analy
J	Analyte detected below quantitation limits	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit
R	RPD outside accepted recovery limits	S	Spike Recovery outside accepted recovery limits	U	Indicates the compound was analyzed

CLIENT: CA Rich Consultants Inc.
Work Order: 1202043
Project: 260 West 26th Street, New York, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: Dry8270PAH_Soil

Sample ID: MB-34633	SampType: MBLK	TestCode: Dry8270PAH_	Units: µg/Kg	Prep Date: 2/8/2012	RunNo: 62077
Client ID: PBS	Batch ID: 34633	TestNo: SW8270D	SW3550C	Analysis Date: 2/8/2012	SeqNo: 871065

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Acenaphthene	U	250									
Acenaphthylene	U	250									
Anthracene	U	250									
Benzo(a)anthracene	U	250									
Benzo(a)pyrene	U	250									
Benzo(b)fluoranthene	U	250									
Benzo(g,h,i)perylene	U	250									
Benzo(k)fluoranthene	U	250									
Chrysene	U	250									
Dibenzo(a,h)anthracene	U	250									
Fluoranthene	U	250									
Fluorene	U	250									
Indeno(1,2,3-c,d)pyrene	U	250									
Naphthalene	U	250									
Phenanthrene	U	250									
Pyrene	U	250									
Surr: 2-Fluorobiphenyl	710		1000		71.0	21	117				
Surr: 4-Terphenyl-d14	750		1000		74.9	21	132				
Surr: Nitrobenzene-d5	680		1000		68.3	18	116				

Sample ID: LCS-34633	SampType: LCS	TestCode: Dry8270PAH_	Units: µg/Kg	Prep Date: 2/8/2012	RunNo: 62077
Client ID: LCSS	Batch ID: 34633	TestNo: SW8270D	SW3550C	Analysis Date: 2/8/2012	SeqNo: 871066

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Acenaphthene	1700	250	2000	0	86.0	38	122				
Acenaphthylene	1700	250	2000	0	85.6	48	121				
Anthracene	1800	250	2000	0	90.3	40	120				
Benzo(a)anthracene	1800	250	2000	0	91.7	45	120				
Benzo(a)pyrene	1800	250	2000	0	88.4	47	120				
Benzo(b)fluoranthene	1700	250	2000	0	87.2	42	119				
Benzo(g,h,i)perylene	1400	250	2000	0	72.2	42	138				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	H	Holding times for preparation or analy
J	Analyte detected below quantitation limits	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit
R	RPD outside accepted recovery limits	S	Spike Recovery outside accepted recovery limits	U	Indicates the compound was analyzed

CLIENT: CA Rich Consultants Inc.
Work Order: 1202043
Project: 260 West 26th Street, New York, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: Dry8270PAH_Soil

Sample ID: **LCS-34633**	SampType: **LCS**	TestCode: **Dry8270PAH_**	Units: **µg/Kg**		Prep Date: **2/8/2012**			RunNo: **62077**			
Client ID: **LCSS**	Batch ID: **34633**	TestNo: **SW8270D**	**SW3550C**		Analysis Date: **2/8/2012**			SeqNo: **871066**			
Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Benzo(k)fluoranthene	1800	250	2000	0	87.6	35	130				
Chrysene	1800	250	2000	0	91.9	43	125				
Dibenzo(a,h)anthracene	1700	250	2000	0	85.6	43	133				
Fluoranthene	1800	250	2000	0	90.0	42	120				
Fluorene	1700	250	2000	0	82.5	38	122				
Indeno(1,2,3-c,d)pyrene	2100	250	2000	0	103	49	150				
Naphthalene	1600	250	2000	0	81.8	33	127				
Phenanthrene	1700	250	2000	0	86.4	49	126				
Pyrene	1800	250	2000	0	89.8	39	123				
Surr: 2-Fluorobiphenyl	730		1000		73.2	21	117				
Surr: 4-Terphenyl-d14	760		1000		76.0	21	132				
Surr: Nitrobenzene-d5	670		1000		67.3	18	116				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	H	Holding times for preparation or analy
J	Analyte detected below quantitation limits	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit
R	RPD outside accepted recovery limits	S	Spike Recovery outside accepted recovery limits	U	Indicates the compound was analyzed

CLIENT: CA Rich Consultants Inc.
Work Order: 1202043
Project: 260 West 26th Street, New York, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DryFull8260_Soil

Sample ID: **V624LCS-020612aH** SampType: **LCS** TestCode: **DryFull8260_** Units: **µg/Kg** Prep Date: **2/6/2012** RunNo: **62033**
Client ID: **LCSS** Batch ID: **R62033** TestNo: **SW8260C** Analysis Date: **2/6/2012** SeqNo: **870292**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
1,1,1-Trichloroethane	49	5.0	50.00	0	97.9	40	125				
1,1,2,2-Tetrachloroethane	57	5.0	50.00	0	115	41	130				
1,1,2-Trichloroethane	52	5.0	50.00	0	103	43	121				
1,1-Dichloroethane	45	5.0	50.00	0	90.9	42	126				
1,1-Dichloroethene	49	5.0	50.00	0	98.2	40	126				
1,2-Dichlorobenzene	48	5.0	50.00	0	96.5	41	122				
1,2-Dichloroethane	48	5.0	50.00	0	95.4	42	133				
1,2-Dichloropropane	52	5.0	50.00	0	103	41	128				
1,3-Dichlorobenzene	48	5.0	50.00	0	95.0	45	119				
1,4-Dichlorobenzene	48	5.0	50.00	0	96.2	46	121				
2-Chloroethyl vinyl ether	52	5.0	50.00	0	105	30	135				
Benzene	46	5.0	50.00	0	93.0	35	123				
Bromodichloromethane	48	5.0	50.00	0	96.7	37	130				
Bromoform	55	5.0	50.00	0	109	43	121				
Bromomethane	27	5.0	50.00	0	53.3	32	130				
Carbon tetrachloride	51	5.0	50.00	0	101	37	134				
Chlorobenzene	48	5.0	50.00	0	95.0	40	124				
Chloroethane	21	5.0	50.00	0	41.1	35	141				C
Chloroform	49	5.0	50.00	0	98.6	36	126				
Chloromethane	30	5.0	50.00	0	60.5	42	141				C
cis-1,3-Dichloropropene	47	5.0	50.00	0	94.2	30	130				
Dibromochloromethane	53	5.0	50.00	0	105	43	125				
Ethylbenzene	47	5.0	50.00	0	94.6	44	122				
Methylene chloride	43	5.0	50.00	0	85.1	32	132				B
Tetrachloroethene	46	5.0	50.00	0	91.6	31	120				
Toluene	49	5.0	50.00	0	97.7	42	124				
trans-1,2-Dichloroethene	46	5.0	50.00	0	92.9	38	122				
trans-1,3-Dichloropropene	52	5.0	50.00	0	104	45	123				
Trichloroethene	55	5.0	50.00	0	109	46	124				
Trichlorofluoromethane	50	5.0	50.00	0	101	45	137				C
Vinyl chloride	39	5.0	50.00	0	77.5	46	139				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	H	Holding times for preparation or analy
J	Analyte detected below quantitation limits	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit
R	RPD outside accepted recovery limits	S	Spike Recovery outside accepted recovery limits	U	Indicates the compound was analyzed

CLIENT: CA Rich Consultants Inc.
Work Order: 1202043
Project: 260 West 26th Street, New York, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DryFull8260_Soil

Sample ID: V624LCS-020612aH	SampType: LCS	TestCode: DryFull8260_	Units: µg/Kg	Prep Date: 2/6/2012	RunNo: 62033
Client ID: LCSS	Batch ID: R62033	TestNo: SW8260C		Analysis Date: 2/6/2012	SeqNo: 870292

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Surr: 4-Bromofluorobenzene	49		50.00		97.7	42	133				
Surr: Dibromofluoromethane	47		50.00		95.0	50	133				
Surr: Toluene-d8	49		50.00		98.7	53	130				

Sample ID: VBLK-020612aHS	SampType: MBLK	TestCode: DryFull8260_	Units: µg/Kg	Prep Date: 2/6/2012	RunNo: 62033
Client ID: PBS	Batch ID: R62033	TestNo: SW8260C		Analysis Date: 2/6/2012	SeqNo: 870293

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
1,1,1,2-Tetrachloroethane	U	5.0									
1,1,1-Trichloroethane	U	5.0									
1,1,2,2-Tetrachloroethane	U	5.0									
1,1,2-Trichloro-1,2,2-trifluoroethane	U	5.0									
1,1,2-Trichloroethane	U	5.0									
1,1-Dichloroethane	U	5.0									
1,1-Dichloroethene	U	5.0									
1,1-Dichloropropene	U	5.0									
1,2,3-Trichlorobenzene	U	5.0									
1,2,3-Trichloropropane	U	5.0									
1,2,4,5-Tetramethylbenzene	U	5.0									
1,2,4-Trichlorobenzene	U	5.0									
1,2,4-Trimethylbenzene	U	5.0									
1,2-Dibromo-3-chloropropane	U	5.0									
1,2-Dibromoethane	U	5.0									
1,2-Dichlorobenzene	U	5.0									
1,2-Dichloroethane	U	5.0									
1,2-Dichloropropane	U	5.0									
1,3,5-Trimethylbenzene	U	5.0									
1,3-Dichlorobenzene	U	5.0									
1,3-dichloropropane	U	5.0									
1,4-Dichlorobenzene	U	5.0									
1,4-Dioxane	U	5.0									

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	H	Holding times for preparation or analy
J	Analyte detected below quantitation limits	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit
R	RPD outside accepted recovery limits	S	Spike Recovery outside accepted recovery limits	U	Indicates the compound was analyzed

CLIENT: CA Rich Consultants Inc.
Work Order: 1202043
Project: 260 West 26th Street, New York, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DryFull8260_Soil

Sample ID: **VBLK-020612aHS**	SampType: **MBLK**	TestCode: **DryFull8260_**	Units: **µg/Kg**	Prep Date: **2/6/2012**	RunNo: **62033**
Client ID: **PBS**	Batch ID: **R62033**	TestNo: **SW8260C**		Analysis Date: **2/6/2012**	SeqNo: **870293**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
2,2-Dichloropropane	U	5.0									
2-Butanone	U	5.0									
2-Chloroethyl vinyl ether	U	5.0									
2-Chlorotoluene	U	5.0									
2-Hexanone	U	5.0									
2-Propanol	U	5.0									
4-Chlorotoluene	U	5.0									
4-Isopropyltoluene	U	5.0									
4-Methyl-2-pentanone	U	5.0									
Acetone	U	5.0									
Acrolein	U	10									
Acrylonitrile	U	5.0									
Benzene	U	5.0									
Bromobenzene	U	5.0									
Bromochloromethane	U	5.0									
Bromodichloromethane	U	5.0									
Bromoform	U	5.0									
Bromomethane	U	5.0									
Carbon disulfide	U	5.0									
Carbon tetrachloride	U	5.0									
Chlorobenzene	U	5.0									
Chlorodifluoromethane	U	5.0									
Chloroethane	U	5.0									C
Chloroform	U	5.0									
Chloromethane	U	5.0									C
cis-1,2-Dichloroethene	U	5.0									
cis-1,3-Dichloropropene	U	5.0									
Dibromochloromethane	U	5.0									
Dibromomethane	U	5.0									
Dichlorodifluoromethane	U	5.0									
Diisopropyl ether	U	5.0									

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	H	Holding times for preparation or analy
J	Analyte detected below quantitation limits	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit
R	RPD outside accepted recovery limits	S	Spike Recovery outside accepted recovery limits	U	Indicates the compound was analyzed

CLIENT: CA Rich Consultants Inc.
Work Order: 1202043
Project: 260 West 26th Street, New York, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DryFull8260_Soil

Sample ID: **VBLK-020612aHS** SampType: **MBLK** TestCode: **DryFull8260_** Units: **µg/Kg** Prep Date: **2/6/2012** RunNo: **62033**
Client ID: **PBS** Batch ID: **R62033** TestNo: **SW8260C** Analysis Date: **2/6/2012** SeqNo: **870293**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Ethanol	U	10									
Ethyl acetate	U	5.0									
Ethylbenzene	U	5.0									
Freon-114	U	5.0									
Hexachlorobutadiene	U	5.0									
Isopropyl acetate	U	5.0									
Isopropylbenzene	U	5.0									
m,p-Xylene	U	10									
Methyl Acetate	U	5.0									
Methyl tert-butyl ether	U	5.0									
Methylene chloride	3.8	5.0									J
n-Amyl acetate	U	5.0									
Naphthalene	U	5.0									
n-Butyl acetate	U	5.0									
n-Butylbenzene	U	5.0									
n-Propyl acetate	U	5.0									
n-Propylbenzene	U	5.0									
o-Xylene	U	5.0									
p-Diethylbenzene	U	5.0									
p-Ethyltoluene	U	5.0									
sec-Butylbenzene	U	5.0									
Styrene	U	5.0									
t-Butyl alcohol	U	5.0									
tert-Butylbenzene	U	5.0									
Tetrachloroethene	U	5.0									
Toluene	U	5.0									
trans-1,2-Dichloroethene	U	5.0									
trans-1,3-Dichloropropene	U	5.0									
Trichloroethene	U	5.0									
Trichlorofluoromethane	U	5.0									C
Vinyl acetate	U	5.0									

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	H	Holding times for preparation or analy
J	Analyte detected below quantitation limits	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit
R	RPD outside accepted recovery limits	S	Spike Recovery outside accepted recovery limits	U	Indicates the compound was analyzed

CLIENT: CA Rich Consultants Inc.
Work Order: 1202043
Project: 260 West 26th Street, New York, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DryFull8260_Soil

Sample ID: **VBLK-020612aHS** SampType: **MBLK** TestCode: **DryFull8260_** Units: **µg/Kg** Prep Date: **2/6/2012** RunNo: **62033**
Client ID: **PBS** Batch ID: **R62033** TestNo: **SW8260C** Analysis Date: **2/6/2012** SeqNo: **870293**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Vinyl chloride	U	5.0									
Surr: 4-Bromofluorobenzene	43		50.00		86.4	42	133				
Surr: Dibromofluoromethane	54		50.00		108	50	133				
Surr: Toluene-d8	45		50.00		90.1	53	130				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	H	Holding times for preparation or analy
J	Analyte detected below quantitation limits	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit
R	RPD outside accepted recovery limits	S	Spike Recovery outside accepted recovery limits	U	Indicates the compound was analyzed

CLIENT: CA Rich Consultants Inc.
Work Order: 1202043
Project: 260 West 26th Street, New York, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DRYHG_S

Sample ID: PBS-020612B	SampType: MBLK	TestCode: DRYHG_S	Units: mg/Kg	Prep Date: 2/6/2012	RunNo: 62019
Client ID: PBS	Batch ID: 34626	TestNo: SW7471B	SW7471B	Analysis Date: 2/6/2012	SeqNo: 869937

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Mercury	U	0.0100									

Sample ID: LCSS-020612B	SampType: LCS	TestCode: DRYHG_S	Units: mg/Kg	Prep Date: 2/6/2012	RunNo: 62019
Client ID: LCSS	Batch ID: 34626	TestNo: SW7471B	SW7471B	Analysis Date: 2/6/2012	SeqNo: 869938

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Mercury	0.202	0.0100	0.2000	0	101	80	120				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	H	Holding times for preparation or analy
J	Analyte detected below quantitation limits	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit
R	RPD outside accepted recovery limits	S	Spike Recovery outside accepted recovery limits	U	Indicates the compound was analyzed

CLIENT: CA Rich Consultants Inc.
Work Order: 1202043
Project: 260 West 26th Street, New York, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: TCLP_HG

Sample ID: PBW-020712A	SampType: MBLK	TestCode: TCLP_HG	Units: mg/L	Prep Date:	RunNo: 62046
Client ID: PBS	Batch ID: 34630	TestNo: SW1311/7471 SW1311		Analysis Date: 2/7/2012	SeqNo: 870472

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Mercury	U	0.0200									

Sample ID: LCSW-020712A	SampType: LCS	TestCode: TCLP_HG	Units: mg/L	Prep Date:	RunNo: 62046
Client ID: LCSS	Batch ID: 34630	TestNo: SW1311/7471 SW1311		Analysis Date: 2/7/2012	SeqNo: 870473

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Mercury	0.00389	0.0200	0.004000	0	97.2	64	123				J

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	H	Holding times for preparation or analy
J	Analyte detected below quantitation limits	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit
R	RPD outside accepted recovery limits	S	Spike Recovery outside accepted recovery limits	U	Indicates the compound was analyzed

CLIENT: CA Rich Consultants Inc.
Work Order: 1202043
Project: 260 West 26th Street, New York, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: TCLP_M

Sample ID: **PBW-020612AT** SampType: **MBLK** TestCode: **TCLP_M** Units: **mg/L** Prep Date: RunNo: **62069**
Client ID: **PBS** Batch ID: **34630** TestNo: **SW1311/6010 SW1311** Analysis Date: **2/8/2012** SeqNo: **870951**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Arsenic	U	0.0500									
Barium	U	5.00									
Cadmium	U	0.0500									
Chromium	U	0.0500									
Lead	U	0.0500									
Selenium	U	0.0500									
Silver	U	0.0500									

Sample ID: **LCSW-020612AT** SampType: **LCS** TestCode: **TCLP_M** Units: **mg/L** Prep Date: RunNo: **62069**
Client ID: **LCSS** Batch ID: **34630** TestNo: **SW1311/6010 SW1311** Analysis Date: **2/8/2012** SeqNo: **870952**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Arsenic	2.18	0.0500	2.000	0	109	80	120				
Barium	2.10	5.00	2.000	0	105	80	120				J
Cadmium	2.23	0.0500	2.000	0	111	80	120				
Chromium	2.21	0.0500	2.000	0	110	80	120				
Lead	2.15	0.0500	2.000	0	107	80	120				
Selenium	2.38	0.0500	2.000	0	119	80	120				
Silver	1.94	0.0500	2.000	0	97.2	80	120				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	H	Holding times for preparation or analy
J	Analyte detected below quantitation limits	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit
R	RPD outside accepted recovery limits	S	Spike Recovery outside accepted recovery limits	U	Indicates the compound was analyzed

CLIENT: CA Rich Consultants Inc.
Work Order: 1202043
Project: 260 West 26th Street, New York, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: TOTAL8015DRODRY

Sample ID: MB-34634	SampType: MBLK	TestCode: TOTAL8015D	Units: mg/Kg	Prep Date: 2/8/2012	RunNo: 62080
Client ID: PBS	Batch ID: 34634	TestNo: SW8015C	SW3550C	Analysis Date: 2/8/2012	SeqNo: 871117

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Total DRO TPH	U	10									
Surr: o-Terphenyl	2.6		3.000		85.6	31	137				

Sample ID: LCS-34634	SampType: LCS	TestCode: TOTAL8015D	Units: mg/Kg	Prep Date: 2/8/2012	RunNo: 62080
Client ID: LCSS	Batch ID: 34634	TestNo: SW8015C	SW3550C	Analysis Date: 2/8/2012	SeqNo: 871118

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Total DRO TPH	260	10	200.0	0	128	36	138				
Surr: o-Terphenyl	2.8		3.000		92.3	31	137				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	H	Holding times for preparation or analy
J	Analyte detected below quantitation limits	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit
R	RPD outside accepted recovery limits	S	Spike Recovery outside accepted recovery limits	U	Indicates the compound was analyzed

American Analytical Laboratories, LLC.

Date: *09-Feb-12*

CLIENT: CA Rich Consultants Inc.
Work Order: 1202043
Project: 260 West 26th Street, New York, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DRYHG_S

Sample ID: **1202012-01B-MSD**	SampType: **MSD**	TestCode: **DRYHG_S**	Units: **mg/Kg-dry**	Prep Date: **2/6/2012**	RunNo: **62019**
Client ID: **ZZZZZZ**	Batch ID: **34626**	TestNo: **SW7471B**	**SW7471B**	Analysis Date: **2/6/2012**	SeqNo: **869936**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Mercury	0.215	0.0105	0.2107	0	102	80	120				

Sample ID: **1202010-05A-MS**	SampType: **MS**	TestCode: **DRYHG_S**	Units: **mg/Kg-dry**	Prep Date: **2/6/2012**	RunNo: **62019**
Client ID: **ZZZZZZ**	Batch ID: **34626**	TestNo: **SW7471B**	**SW7471B**	Analysis Date: **2/6/2012**	SeqNo: **869963**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Mercury	1.82	0.0402	0.8117	0.9323	109	80	120				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	H	Holding times for preparation or analy
J	Analyte detected below quantitation limits	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit
R	RPD outside accepted recovery limits	S	Spike Recovery outside accepted recovery limits	U	Indicates the compound was analyzed

CLIENT: CA Rich Consultants Inc.
Work Order: 1202043
Project: 260 West 26th Street, New York, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: TOTAL8015DRODRY

Sample ID: 1202043-05A-MS	SampType: MS	TestCode: TOTAL8015D	Units: mg/Kg-dry	Prep Date: 2/8/2012	RunNo: 62080
Client ID: B1 (16-18 ft.)	Batch ID: 34634	TestNo: SW8015C SW3550C		Analysis Date: 2/8/2012	SeqNo: 871124

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Total DRO TPH	330	11	218.7	58.06	126	27	152				
Surr: o-Terphenyl	2.8		3.281		86.2	31	137				

Sample ID: 1202043-05A-MSD	SampType: MSD	TestCode: TOTAL8015D	Units: mg/Kg-dry	Prep Date: 2/8/2012	RunNo: 62080
Client ID: B1 (16-18 ft.)	Batch ID: 34634	TestNo: SW8015C SW3550C		Analysis Date: 2/8/2012	SeqNo: 871125

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Total DRO TPH	360	11	218.5	58.06	136	27	152	334.7	5.89	20	
Surr: o-Terphenyl	3.0		3.278		92.3	31	137		0	0	

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	H	Holding times for preparation or analy
J	Analyte detected below quantitation limits	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit
R	RPD outside accepted recovery limits	S	Spike Recovery outside accepted recovery limits	U	Indicates the compound was analyzed

APPENDIX H

Disposal Approval Letters and Operating Permits

Soil Safe®
Recycling and Beneficial Re-use of Soils

October 14, 2011

Mr. Amnon Soloman
Chelsea W. 26th LLC
C/o Artimus Construction Inc
37 W. 65th St.
NY, NY. 10023

Re: Chelsea Green-260 West 26th Street/ for 1500 tons of soil

Dear Amnon,

Soil Safe, Inc has reviewed the Material Characterization Report (MCR) along with the laboratory analysis (lab number 1108200) submitted from the referenced project. We have approved the soil represented by:TP1 (0-7), TP1 (7-14), TP2 (0-7), TP2 (7-14), TP3 (0-7), TP3 (7-14), TP4 (0-7), TP4 (7-14), TP6 (0-8), TP8 (0-4) and **non-hazardous portions of TP-5 and TP-7** for acceptance at our Logan Township,NJ Facility under approval number C4-8199.
Please ensure the appropriate TP is listed on each manifest.
The soil that we will not be able to accept is: TP5 (0-11) and TP7 (0-7).

If you have any questions regarding this approval please call Amy Ralston at (410) 872-3990 x 1122

Don Wallace
Material Acceptance Manager

Cc: Amy Ralston
Logan Facility
File

State of New Jersey
DEPARTMENT OF ENVIRONMENTAL PROTECTION

JON S. CORZINE
Governor

Solid & Hazardous Waste Program
P.O. Box 414 401 East State Street
Trenton, New Jersey 08625-0414
Telephone: (609) 984-5950 Telecopier: (609) 633-9839
http://www.state.nj.us/dep/dshw

MARK N. MAURIELLO
Acting Commissioner

RECYCLING CENTER GENERAL APPROVAL FOR CLASS B RECYCLABLE MATERIAL FOR PETROLEUM CONTAMINATED SOIL THAT MAY ALSO CONTAIN CONCRETE, ASPHALT, BRICK, AND BLOCK

Under the provisions of N.J.S.A. 13:1E-1 *et seq.* and N.J.S.A. 13:1E-99.11 *et seq.*, known as the Solid Waste Management Act and New Jersey Statewide Mandatory Source Separation and Recycling Act, respectively, and pursuant to N.J.A.C. 7:26A-1 *et seq.*, known as the Recycling Regulations, this approval is hereby issued to:

Soil Safe, Inc.

Facility Type:	Recycling Center for Class B Materials
Lot & Block Nos.:	Block 201, Lots 1 through 5
Municipality:	Logan Township
County:	Gloucester County
Facility ID No.:	203493
Permit No.:	CBG080003

This General Approval is subject to compliance with all conditions specified herein and all regulations promulgated by the Department of Environmental Protection (Department). This General Approval shall not prejudice any claim the State may have to riparian land nor does it allow the registrant to fill or alter, or allow to be filled or altered, in any way, lands that are deemed to be riparian, wetlands, stream encroachment or flood plains, or within the Coastal Area Facility Review Act (CAFRA) zone or are subject to the Pinelands Protection Act of 1979, nor shall it allow the discharge of pollutants to waters of this State without prior acquisition of the necessary grants, permits, or approvals from the Department of Environmental Protection.

April 2, 2009
Issuance Date

Anthony Fontana

Anthony Fontana, Chief
Bureau of Transfer Stations &
Recycling Facilities

April 27, 2009
Modification Date

December 19, 2013
Expiration Date

Scope of Approval

This General Approval (approval), along with the referenced application documents herein specified, shall constitute the sole approval of Recycling Center operations for a Class B Recyclable Material storage and process center by **Soil Safe, Inc.** located in Logan Township, Gloucester County, New Jersey. The facility is authorized to accept petroleum contaminated soil that may also contain concrete, asphalt, brick, and block. Any registration, approval or permit previously issued by the Solid and Hazardous Waste Management Program, or its predecessor agencies, for the specific activities as described below and as conditioned herein, is hereby superseded.

This general approval does not convey any property rights of any sort, or any exclusive privilege. Failure to comply with all of the conditions specified herein may result in revocation of this approval and/or may result in such other regulatory or legal actions that the Department is authorized by law to institute, including but not limited to, civil and administrative penalty assessments.

This general approval does not approve any activities by Soil Safe, Inc. outside of the boundaries of the Class B Recycling operations and limits of the Dredge Material Blending Facility. All other operations being conducted by Soil Safe, Inc. at the Logan Township site are under the permits and approvals from other divisions within the Department, including but not limited to Air, Site Remediation, Wetlands, and NJPDES Storm Water and Ground Water.

Items 1 through 39 of this approval contain the general conditions applicable to all recycling centers. Items 40 through 80 of this approval contain general operating requirements for all recycling centers for receipt, storage, processing, or transfer of Class B recyclable material and specific conditions applicable to the operations of the recycling center.

Facility Description

The recycling center is a Class B Recycling Facility. The recycling center is located at Route 130 and Birch Creek on Block 201, Lots 1 through 5, in Logan Township, Gloucester County. This regional recycling center receives petroleum contaminated soil from soil remediation contractors. The recycling center is authorized to accept and process petroleum contaminated soil Monday through Saturday.

The recycling center produces a Soil Cement (petroleum contaminated soil and cement) and Blended Soil Product (soil cement and Delaware River Maintenance Dredge Material) utilized in the site improvement for three Brownfield sites including the Bridgeport Land Development Parcel (a.k.a. Birch Creek Property), the Gloucester County Improvement Authority Equine Park, and the Gloucester County Improvement Authority County Park. The blending of the Class B product (soil cement) with Delaware River Maintenance Dredge requires approval from the Department's Office of Dredging & Sediment Technology.

This modification includes minor changes to the Approval (Conditions # 46, 47, 65, 74, 79) issued on April 2, 2009.

Approved General Approval Application and Associated Documents

The registrant shall construct and operate the facility in accordance with N.J.A.C. 7:26A-1 *et seq.*, the conditions of this Approval, and the following documents:

(1) Site plan: prepared by Kernan Consulting Engineers, signed and sealed by J. Timothy Kernan, P.E., dated September 8, 2003, last revised November 5, 2003.

(2) Site Plan: prepared by EastStar Environmental Group, Inc. and sealed by Albert P.Free, P.E., dated March 26, 2009 for Dredge Blending Operations.

(3) Soil Safe, Inc. - Class B Recycling Center General Approval Modification Application, signed by Milt Morris, Vice President, Soil Safe Inc, dated April 10, 2009.

(4) Soil Safe, Inc. - Class B Recycling Center General Approval Application, prepared by Christopher L. Daul of Alman Group, and signed by Edwin J. Kilpela of Soil Safe, Inc., dated June 10, 2003.

In case of conflict, the provisions of N.J.A.C. 7:26A-1 *et seq.* shall have precedence over the conditions of this Approval, and the conditions of this Approval shall have precedence over plans and specifications listed above.

BELLMAWR WATERFRONT DEVELOPMENT
APPROVAL NOTIFICATION

DATE OF APPROVAL: Tuesday, October 11, 2011

SITE: Chelsea Green Site

VOLUME: 3,000 CY [4,500 Tons]

RESIDENTIAL/NON-RES: Non-Residential

DATE SUBMITTED TO DEP: Monday, October 10, 2011 [Letter Attached]

X A.M. _____ P.M.

DATE MATERIAL CAN SHIP TO BWD: Wednesday, October 12, 2011

INCOMING LOAD PROCEDURES:

1. No materials will be accepted unless credit approval and material acceptance approval is obtained in advance from Haines and Kibblehouse (H&K).

2. Materials approved for soil reuse containing more than 1% deleterious material or more than 5-10% stone or concrete will be rejected upon visual inspection at BWD Facility, unless prior approval has been issued for concrete materials.

3. Materials containing concrete must be characterized per NJDEP's concrete guidance prior to shipment.

4. Materials being moved to the Bellmawr Waterfront Development facility must be the material represented by the application and analytical data furnished. Different materials will be rejected.

5. Soil and granular materials must have 100% of materials passing a 1" sieve and shall not have more than 60% of materials passing the 200 mesh sieve.

6. No contaminated materials will be accepted without NJDEP approval in advance.

7. No materials will be accepted which have free draining liquids nor which are excessively wet (all materials must pass the paint filter test at a minimum).

8. No materials will be accepted which cause objectionable odors.

To schedule incoming loads at BWD, please contact Jennifer Berg of RT Environmental at 610-506-5802.

RT Environmental Services, Inc.

October 10, 2011

Mr. Ronald J. Wienckoski, Jr.
Landfill Remediation and Redevelopment
Office of Brownfield Reuse
NJ Department of Environmental Protection
401 E. State Street
P.O. Box 420
Trenton, NJ 08625-0420
(609) 984-4617

RE: BELLMAWR WATERFRONT DEVELOPMENT
SELF CERTIFICATION TO RECEIVE 4,500 TONS
FROM THE CHELSEA GREEN SITE
NEW YORK, NEW YORK 10001
RT PROJECT #70779-52

Dear Mr. Wienckoski:

RT Environmental Services, Inc. (RT) is pleased to provide a package of documents from Chelsea W. 26 LLC for the receipt of up to ~4,500 tons (3,000 cubic yards) of material at the Bellmawr Waterfront Development (BWD) Site. The site is located at 260 West 26th Street, New York, New York. Material will be generated during the construction and redevelopment activities at the site.

Twelve (12) representative samples are included within this application package. Samples were collected from *in-situ* material, as shown in the enclosed sample location maps. Six sample areas exceed the BWD non-residential acceptance criteria for lead. The following sample areas will not be accepted at BWD:

- TP-1 (0-7)
- TP-2 (0-7)
- TP-3 (0-7)
- TP-4 (7-14)
- TP-5 (0-11)
- TP-7 (0-7)

All material generated from the following six sample areas will be managed as non-residential material, only to be placed in designated areas of the site and subject to future covering activities:

- TP-1 (7-14)
- TP-2 (7-14)
- TP-3 (7-14)
- TP-4 (0-7)
- TP-6 (0-8)
- TP-8 (0-4)

Certifications from the persons responsible for sampling and the appropriate signatures are included in the application package. Also enclosed are the analytical data and sample location map. A Remedial Investigation Report prepared by CA Rich Consultants, Inc. dated April 2011 is included within this application. CA Rich Consultants will be present on site to oversee separation activities.

215 West Church Road ■ King of Prussia, PA 19406 ■ (610) 265-1510 ■ Fax: (610) 265-0687
E-Mail RTENV@AOL.COM ■ Web Address http://www.RTENV.COM

We plan to begin moving material on site after three business days.

Please call if any questions.

Very truly yours,

RT ENVIRONMENTAL SERVICES, INC.

Gary R. Brown, P.E.
President

G:\RT Projects\70700 SERIES\70779-52\7077952499.doc

Enclosures:
Material Certification Form,
Self Certification Check List,
Application,
Remedial Investigation Report,
Sample Location Map,
Analytical Data.

cc: M. Esposito, C. Gallub – BWD,
J. Litka– H & K,
W. Hungarter, K. Foldes – RT

State of New Jersey

Jon S. Corzine
Governor

Department of Environmental Protection
Site Remediation Program
Office of Brownfield Reuse
P.O. Box 028 401 E. State Street
Trenton, New Jersey 08625-0028
http://www.state.nj.us/dep/srp

Mark N. Mauriello
Acting Commissioner

May 5, 2009

Mr. Charles Gallub
Managing Member
Bellmawr Waterfront Development, LLC
204 Harding Avenue
Bellmawr, New Jersey 08031

Re: Landfill Closure Plan Approval
BELLMAWR WATERFRONT DEVELOPMENT LLC
SW Landfill (Class C) Closure
Bellmawr Boro, Camden County
Deptford Towhship, Gloucester County
NJEMS Program Interest No.: 131997
Permit No.: LCC090001

Dear Mr. Gallub:

Enclosed please find a Landfill Closure Plan Approval for the above-referenced site. This approval incorporates the approval to install the storm water replacement pipe along Route 42, approval to construct and operate a temporary Class B Recycling Center on the Bellmawr Borough Landfill portion of the site and the approval of the closure and development of the referenced site. This approval supersedes Permit Nos. LCC070004, LCC080001, LCC080002, LCC080003.

Conditions have been incorporated within this Approval that must be complied with in order for it to remain valid. The Department will consider amendment or modification of the specific terms of the conditions of this Approval if the applicant submits a written request by certified mail within twenty (20) calendar days of receipt of this letter. Said written request must clearly state the proposed amendment or modification and the factual basis for the request. This Approval is non-transferable.

If you have any questions concerning this matter, please contact me by telephone at (609) 984-2001, or by email at timothy.bartle@dep.state.nj.us.

Sincerely,

Timothy T. Bartle, P.E.
Section Chief
Office of Brownfield Reuse

Enclosure
c: G. Brown, RT
C. Sauter, Bellmawr Municipal Clerk
D. Zawadski, Deptford Municipal Clerk
P. Farraro, Solid Waste Enforcement

State of New Jersey

Jon S. Corzine
Governor

Department of Environmental Protection
Site Remediation Program
Office of Brownfield Reuse
P.O. Box 028 401 E. State Street
Trenton, New Jersey 08625-0028
http://www.state.nj.us/dep/srp

Mark N. Mauriello
Acting Commissioner

CLOSURE PLAN APPROVAL

Under the provisions of N.J.S.A. 13:1E-1 et seq. known as the Solid Waste Management Act, this Landfill Closure Plan Approval is hereby issued to:

BELLMAWR WATERFRONT DEVELOPMENT LLC

FACILITY TYPE:	Sanitary Landfill
FACILITY ID NO.:	131997
PERMIT NO.:	LCC090001
BLOCK & LOT NOS.:	79.01/9.01 and 78/1,2,3,4
MUNICIPALITY:	Bellmawr Borough
COUNTY:	Camden
BLOCK & LOT NOS:	1.02/1
MUNICIPALITY;	Deptford Township
COUNTY'	Gloucester County

This Approval is subject to compliance with all conditions specified herein and all regulations promulgated by the Department of Environmental Protection.

This Approval shall not prejudice any claim the State may have to riparian land, nor does it permit the registrant to fill or alter or allow to be filled or altered, in any way, lands that are deemed to be riparian, wetlands, stream encroachment areas or flood plains, or that are within the Coastal Area Facility Review Act (CAFRA) zone or are subject to the Pinelands Protection Act of 1979, nor shall it allow the discharge of pollutants to waters of this state without prior acquisition of the necessary grants, permits or approvals from the Department of Environmental Protection.

July 31, 2008
Issuance Date

May 5, 2009
Date of Modification

Timothy T. Bartle, P.E.
Section Chief
Office of Brownfield Reuse

Approved Closure Plan and Associated Documents

The owner shall close and maintain the landfill in accordance with N.J.A.C. 7:26-2A.9, the conditions of this Approval, and the following documents, which are the approved Closure Plan:

A. The following documents that were submitted as part of a Multiple Permit Application under a cover letter addressed to Ms. (Dr.) Ruth Foster dated July 21, 2006 and signed by Gary Brown, P.E. of RT Environmental Services, Inc. for the installation of the stormwater replacement pipe along the border of the site with Route 42:

1. A Solid Waste Facility Permit Application Form notarized by Barbara McCullen on July 21, 2006 and signed by Joseph Esposito, Sr. and Gary R. Brown.

2. A Solid Waste Facility Permit Application Form notarized by Barbara McCullen on July 21, 2006 and signed by Frank R. Filipek and Gary R. Brown.

3. Section V of the Multiple Permit Application entitled, "Major Landfill Disruption Permit Application for Installation of Replacement Stormwater Pipes".

4. Attachment 2 of Section V-Topographic Map.

5. Attachment 3 of Section V-Health and Safety Plan.

6. Appendix T, "Stormwater Pipe Design", of the Multiple Permit Application.

B. The following documents that were submitted for the construction and operation of a Class B Recycling Center at the Bellmawr Borough Landfill for soil screening, and the processing and storage of rock, recycled concrete, brick and block. Soils will be used for interim fill at the site and processed rock and recyclable material will be used for sub grade and drainage layer material for future development of the site. Additionally, the construction of this facility shall be in accordance with the provisions of N.J.A.C. 7:26A-1 *et seq.*, the New Jersey Uniform Construction Code, and this Approval.

1. A transmittal letter addressed to Mr. John Edwards, Office of Brownfield Reuse, dated November 27, 2007 and signed by Gray R. Brown, P.E., President, RT Environmental Services, Inc. This letter serves as the Landfill Disruption Approval Application.

2. Application for a Class B Recycling Center Approval, dated August 2007, prepared by RT Environmental Services, Inc.

3. Site Plan, entitled "Figure 2, Site Plan Class B Facility, Bellmawr Landfill", sheets 1 of 2 and 2 of 2, dated July 11, 2007, **last revised May 1, 2009**, signed and sealed by Gary R. Brown, P.E.

4. Response to October 12, 2007 NJDEP comments document prepared by RT Environmental Services, Inc., dated October 19, 2007.

C. The following documents that were submitted for approval of the Remedial Action Work Plan and Landfill Closure and Post-Closure Plan:

1. A Solid Waste Facility Permit Application Form notarized by Kelly Young on February 4, 2008 and signed by Frank R. Filipek for Bellmawr Borough, Joseph Esposito, Sr. for Bell Harbor, Inc. and Gary R. Brown (agent for Bellmawr Waterfront Development LLC).

2. "Landfill Closure & Post Closure Plan for the Bellmawr Waterfront Development Project, Former Fazzio & Dewey Blanton Landfills, Bellmawr, Camden County, Deptford, Gloucester County," prepared by RT Environmental Services, Inc. dated January 2008 with last revision dated July 2008.

3. "Quality Assurance/Quality Control Manual for the Bellmawr Waterfront Development Project, Former Fazzio & Dewey Blanton Landfills, Bellmawr, Camden County, Deptford, Gloucester County," prepared by RT Environmental Services, Inc. dated January 2008.

4. "Health and Safety Plan, Former Fazzio & Dewey Blanton Landfills, Bellmawr, Camden County & Deptford, Gloucester County," prepared by RT Environmental Services, Inc. dated January 2008.

5. Letter of December 5, 2008 from RT Environmental Services, Inc. to the Department submitting updated drawings and generally describing the revisions made.

6. Letter of March 30, 2009 from RT Environmental Services, Inc. to the Department submitting updated drawings and generally describing the revisions made.

7. Sheets 1 of 49 through 49 of 49 prepared by Nave Newell, Inc. and dated 12/10/07, submitted as part of the document entitled, "Remedial Action Selection Report, Remedial Action Work Plan, Landfill Closure & Post Closure Plan and Environmental Assessment Statement Addendum for the Bellmawr Waterfront Development Project, Former Fazzio & Dewey Blanton Landfills, Bellmawr, Camden County & Deptford, Gloucester County," and., signed and sealed by Samuel Renauro III, P.E. (unless otherwise noted) with latest revisions as indicated below:

- Sheet No. 1 of 49 Base Map **revised 11/26/08**
- Sheet No. 2 of 49 Environmental Permit Base Map – Sheet 1 **revised 4/29/08**
- Sheet No. 3 of 49 Environmental Permit Base Map – Sheet 2
- Sheet No. 4 of 49 Environmental Monitoring Base Map **revised 11/26/08**
- Sheet No. 5 of 49 Proposed Final Cap Contours **revised 11/26/08**

- Sheet No. 6 of 49 Key Map
- Sheet No. 7 of 49 Key Map
- Sheet No. 8 of 49 Key Map
- Sheet No. 9 of 49 Vicinity Map **revised 11/26/08**
- Sheet No. 10 of 49 Vicinity Map **revised 11/26/08**
- Sheet No. 11 of 49 Site Redevelopment Plan **revised 11/26/08**
- Sheet No. 12 of 49 Soils Map
- Sheet No. 13 of 49 Geologic Features Map
- Sheet No. 14 of 49 Top of Interim cover Plan **revised 11/26/08**
- Sheet No. 15 of 49 Top of Liner Elevations w/Utilities **revised 11/26/08**
- Sheet No. 16 of 49 Top of Final Grade **revised 11/26/08**
- Sheet No. 17 of 49 295 Fill-In Area **revised 11/26/08**
- Sheet No. 18 of 49 Culvert Outlet Area **revised 11/26/08**
- Sheet No. 19 of 49 Cutoff Wall &Underdrain Plan **revised 11/26/08**
- Sheet No. 20 of 49 Cutoff Wall Plan & Profile **revised 11/26/08**
- Sheet No. 21 of 49 Cutoff Wall Cross Section Sheet 1 **signed and sealed by Gregory Newell, P.E. revised 3/27/09**
- Sheet No. 22 of 49 Cutoff Wall Cross Section Sheet 2 **signed and sealed by Gregory Newell, P.E. revised 3/27/09**
- Sheet No. 23 of 49 Cutoff Wall Cross Section Sheet 3 **signed and sealed by Gregory Newell, P.E. revised 3/27/09**
- Sheet No. 24 of 49 Landfill Cross Sections Layout Plan **revised 11/26/08**
- Sheet No. 25 of 49 Fazzio-Bellmawr Landfill Cross Section 3-3' **revised 11/26/08**
- Sheet No. 26 of 49 Fazzio-Deptford Landfill Cross Section F-F' **revised 11/26/08**
- Sheet No. 27 of 49 Dewey Blanton Landfill Cross Section A-A' **revised 11/26/08**
- Sheet No. 28 of 49 Landfill Cross Section B-B' **revised 11/26/08**
- Sheet No. 29 of 49 Plan & Profile: 295 Storm Drain **revised 11/26/08**
- Sheet No. 30 of 49 Cross Sections: 295 Strom Drain **revised 11/26/08**
- Sheet No. 31 of 49 Plan & Profile: Bulkhead **revised 11/26/08**
- Sheet No. 32 of 49 Cross Sections: Bulkhead **revised 11/26/08**
- Sheet No. 33 of 49 Stormwater Control Plan 1 – Dewey-Blanton Area **revised 11/26/08**
- Sheet No. 34 of 49 Stormwater Control Plan 2 – Deptford-Fazzio/Petrongolo Area **revised 11/26/08**
- Sheet No. 35 of 49 Stormwater Control Plan 3 – Bellmawr-Fazzio Area **revised 11/26/08**
- Sheet No. 36 of 49 Landfill Gas Collection Plan 1 – Overall Site **revised 11/26/08**
- Sheet No. 37 of 49 Landfill Gas Collection Plan 2 – Dewey-Blanton Area **revised 11/26/08**
- Sheet No. 38 of 49 Landfill Gas Collection Plan 3 – Deptford-Fazzio Area **revised 11/26/08**
- Sheet No. 39 of 49 Landfill Gas Collection Plan 4 – Bellmawr-Fazzio Area - North **revised 11/26/08**
- Sheet No. 40 of 49 Landfill Gas Collection Plan 5 – Bellmawr-Fazzio Area - South **revised 11/26/08**

- Sheet No. 41 of 49 Erosion & Sedimentation Control Plan 1 – Dewey-Blanton Area
- Sheet No. 42 of 49 Erosion & Sedimentation Control Plan 2 – Deptford-Fazzio Area
- Sheet No. 43 of 49 Erosion & Sedimentation Control Plan 3 – Bellmawr-Fazzio Area
- Sheet No. 44 of 49 Detail Sheet **revised 11/26/08**
- Sheet No. 45 of 49 Detail Sheet **revised 11/26/08**
- Sheet No. 46 of 49 Detail Sheet **revised 7/28/08**
- Sheet No. 47 of 49 Detail Sheet
- Sheet No. 48 of 49 Classification Exception Area Plan
- Sheet No. 49 of 49 Groundwater Flows Plan **revised 7/28/08**

In case of conflict, the provisions of N.J.A.C. 7:26-1 and N.J.A.C. 7:26A-1 *et seq.* shall have precedence over the conditions of this Approval, and the conditions of this Approval shall have precedence over plans and specifications listed above.

Attachments

The conditions of this Approval are found in the attached documents entitled "SPECIFIC CONDITIONS FOR CLASS B GENERAL APPROVAL" and "Bellmawr Waterfront Development LLC, 131997 LCC090001 SW Landfill (Class C) Closure –Closure Plan Major Modification, Requirements Report."

SPECIFIC CONDITIONS FOR CLASS B GENERAL APPROVAL

A. Separation and Processing of Materials

1. All activities shall occur within the designated areas as shown on the approved site plan drawing signed and sealed by Gary R. Brown, P.E., dated July 11, 2007, last revised **May 1, 2009.**
2. All processing activities at the Class B Recycling Center shall be performed by Bellmawr Waterfront Development, LLC as per the Class B Recycling Center General Approval Application, dated August 2007.
3. Any materials that do not meet applicable criteria shall be segregated and disposed of as solid waste. Bellmawr Waterfront Development, LLC shall retain all copies of the sampling plan and analysis and, if applicable, shall retain copies of any waste disposal receipts as evidence that the materials have been disposed of properly.

B. Operational Standards

1. All processing activities shall be in conformance with this Approval.
2. Hours of operation for receiving, storing, processing or transferring the source separated recyclable material shall be limited to: 7:00 a.m. to 5:00 p.m. Monday through Friday and 7:00 a.m. to 3:00 p.m. Saturday.
3. The following equipment shall be available for site operations and shall be maintained in operable condition:
   a. Terex Pegson 1412 Trakpactor
   b. CAT 973 Track Loader
4. Materials to be processed at the Class B Recycling Center are limited to the following:
   a. Source-separated concrete, brick and block
5. Material deliveries to the Class B Recycling Center shall be scheduled in such a manner as to minimize truck queuing on the property. Under no circumstances shall delivery trucks be allowed to back-up or queue onto public roads.
6. Bellmawr Waterfront Development, LLC may receive no more than 1,350 tons of recyclable materials per day.
7. The total amount of unprocessed recyclable material stored on-site shall not exceed 25,300 cubic yards. Unprocessed materials stored on-site shall be stored only in those areas designated for that purpose as indicated on the approved site plan drawing.

8. If, at any time, the amount of unprocessed material stored on-site exceeds 25,300 cubic yards, Bellmawr Waterfront Development, LLC shall immediately cease receiving any additional unprocessed materials until the amount of unprocessed material stored on-site falls below 25,300 cubic yards.

9. The total amount of processed recyclable material stored on-site shall not exceed 41,800 cubic yards. Processed materials stored on-site shall be stored only in those areas designated for that purpose as indicated on the approved site plan drawing.

10. If, at any time, the amount of processed material stored on-site exceeds 41,800 cubic yards, Bellmawr Waterfront Development, LLC shall immediately cease processing activities until the amount of processed material falls below 41,800 cubic yards.

11. Horizontal and vertical control points for the unprocessed and processed materials stockpile areas shall be set and maintained on-site. Horizontal limitation markers shall be set at the corners of the stockpile areas as depicted on the approved site plan. Vertical limitation markers shall be set at locations in close proximity to the stockpile areas and shall clearly establish elevation heights of the following:

    a. Unprocessed clean concrete/brick/rock/soil: 20 feet

    b. Unprocessed concrete with metal/rebar: 21 feet

    c. Unprocessed rock: 21 feet

    d. Unprocessed additional stockpile: 15 feet

    e. Processed 4-inch concrete/brick: 38 feet

    f. Processed blend concrete/brick: 19 feet

    g. Processed fines: 18 feet

    h. Processed crushed rock: 22 feet

12. The operation and related activities of this facility shall be in conformance with all applicable federal, State, county, municipal and local statutes, rules and ordinances including but not limited to nuisance, noise, fire and safety codes.

13. The operation of the facility shall be in conformance with the Occupational Safety and Health Act (OSHA) regulations as contained in the General Industry Standards 29 CFR 1910. Construction activities shall be in conformance with the OSHA regulations as contained in the Construction Industry Standards 29 CFR 1926. A copy of the safety procedures shall be posted on-site.

14. Routine housekeeping and maintenance procedures shall be implemented within the facility's interior to prevent the accumulation of litter, dust and debris and to maintain general cleanliness in the working environment.

15. The operation of this facility shall not cause any air contaminant, including any air contaminant detectable by the sense of smell, to be present in the outdoor atmosphere in such quantity and duration that is, or tends to be, injurious to human health or welfare, animal or plant life or property, except for malodorous emissions

emanating from the facility which result in odors in areas over which the owner and/or operator has exclusive use or occupancy.

16. Dust shall be controlled by the spraying of water or equivalent means as approved by the Department.

17. Noise controls shall be implemented so that noise levels generated at the facility shall not exceed the standards set forth by New Jersey State Noise Control Regulations at N.J.A.C. 7:29-1.2.

18. Fire fighting and emergency procedures shall be posted and shall include the telephone number of local fire, police, ambulance and hospital facilities. In the event of an on-site fire, Bellmawr Waterfront Development, LLC shall immediately notify the local fire official and within 24 hours, report the incident to the NJDEP Hotline at 1-877- WARNDEP.

19. Mud, soils or other materials shall not be tracked onto any public roads by any exiting vehicles. Effective measures shall be implemented to comply with this condition.

20. Ingress and egress of the facility shall be restricted to Creek Road as shown on the approved site plan.

21. Any suspected or prohibited hazardous waste, as defined at N.J.A.C. 7:26G-5, found in any of the material shall be segregated and stored in a secure manner and shall immediately be reported to the NJDEP Hotline at 1-877- WARNDEP.

22. A copy of the approved documents as referenced within this Approval shall be maintained at the facility and shall be made available for inspection by Department personnel or its designated representatives.

23. The NJDEP shall have the right to enter and inspect, without prior notice, any building or other portion of the facility, or any other location of the company or its affiliated companies at that time. This right to inspect includes, but is not limited to, the right to engage in the following activities:

    a. Sampling of any materials on-site;

    b. Photographing or videotaping any portion of the facility;

    c. actual or suspected source of pollution of the environment;

    d. Ascertaining compliance or non-compliance with the statutes, rules or regulations of the NJDEP, including the conditions of the this approval issued by the NJDEP; or

    e. Reviewing and copying all applicable records, which shall be made available to the NJDEP during an inspection and submitted to the NJDEP upon request.

C. Reporting

1. Bellmawr Waterfront Development, LLC shall submit an annual report for the operation of the Class B Recycling Center, which contains, at a minimum, the following information:
   a. Monthly and cumulative breakdowns of the amounts and types of materials received and processed;
   b. Residue/recyclables stored on-site for off-site transport;
   c. Any rejected materials and materials that do not meet the applicable criteria for materials placed beneath the barrier layer along with a copy of the disposal receipts as evidence that the material has been disposed of accordingly.
2. All data shall be recorded chronologically by date.
3. The annual report shall be submitted to the Bureau of Transfer Stations & Recycling Facilities, Solid and Hazardous Waste Management Program, PO Box 414, Trenton, New Jersey, 08625-0414 on or before March 1 of each year, for the previous calendar year.

BELLMAWR WATERFRONT DEVELOPMENT LLC
131997 LCC090001 SW Landfill (Class C) Closure -Closure Plan Major Modification
Requirements Report

Subject Item: PI 131997 -

1. Bellmawr Waterfront Developement, LLC shall close and maintain the landfill in accordance with N.J.A.C. 7:26-2A.9, the conditions of this Approval, and the approved Closure Plan as referenced herein. [N.J.A.C. 7:26-2A.9(d)8]
2. The final cover shall completely isolate the landfilled solid waste from the surrounding environment and shall comply with the specifications identified in the plans and documents approved herein. The final cover shall be graded in accordance with the approved Closure Plan. There shall not be any future use of the landfill that may result in the alteration of the final cover, subsequent to closure activities, without review and approval by the Department. [N.J.A.C. 7:26-2A.9(e)2ii]
3. The disruption of waste during closure operations shall be conducted in accordance with N.J.A.C.-2.A.8(j). [N.J.A.C. 7:26-2A.8(j)]
4. A minimum of 6 inches of clean soil shall be placed over any exposed waste at the end of each workday or more frequently if odors or vectors are a problem. A minimum of 12 inches of clean soil shall be applied to all waste exposed for any period exceeding 24 hours and extending up to six months. Thereafter, a minimum of 2 feet of final cover shall be applied and maintained over the waste material. [N.J.A.C. 7:26-2A.8(b)7]
5. The disruption activities shall not cause any air contaminant to be emitted in violation of N.J.A.C. 7:27-5.2(a). Malodorous emissions shall be controlled by the use of daily cover. In the event that this is not satisfactory, a suitable deodorant shall be used. Malodorous solid waste shall be covered immediately after excavation, unloading or re-deposition with a minimum of six inches of cover material or approved alternative material. [N.J.A.C. 7:26-2A.8(j)4]
6. In the event that chemical or hazardous waste materials are encountered during the disruption, operations shall cease immediately and the area shall be secured. The contractor shall notify the Department by calling the Environmental Action Hot Line at 1-877-WARN DEP and take all necessary precautions for the safe removal and disposal of the waste to an approved facility under the direction of the department. [N.J.A.C. 7:26-2A.8(b)4]
7. The contractor shall follow the Occupational Safety and Health Administration (OSHA) standards and the Health and Safety Plan submitted as part of the application during all on-site activities for the safety of employees and for others entering the site. A copy of the operating procedures shall be posted on-site. On-site air monitoring (OVA, HNU, etc.) shall be provided to ensure worker safety during all disruption activities. [N.J.A.C. 7:26-2A.9]
8. Soil erosion and sediment control shall be achieved in accordance with the Soil Erosion and Sediment Control Plan certified by the Camden County Soil Conservation District. The plan shall be certified by the District prior to the start of construction. [N.J.A.C. 7:26-2A.9(e)]
9. Access to the site shall be controlled to prevent unauthorized entry to the landfill. [N.J.A.C. 7:26-2A.8(b)]
10. The final cover shall be maintained to minimize infiltration and ponded water. All cracks, erosion swales and rills shall be repaired by the replacement of cover material and reseeding. Settled areas shall be filled to promote run-off. The final cover vegetation shall be fertilized, limed and mowed to promote growth of the planted species and discourage weed infestation. [N.J.A.C. 7:26-2A.9(e)]
11. The issuance of this Approval does not exempt the applicant from obtaining all other permits or approvals required by law or regulations. [N.J.A.C. 7:26-2.8(h)]

Subject Item: PI 131997 -

12. Department inspectors shall have the right to enter and inspect the facility at any time. The right to inspect includes, but is not limited to: (a) Sampling materials on site; (b) Photographing any portion of the facility; (c) Investigating an actual or suspected source of pollution of the environment; (d) Ascertaining compliance or non-compliance with the statues, rules or regulations of the Department, including conditions or any permit or approval issued by the Department; (e) Reviewing and copying all applicable records, which shall be furnished upon request and made available at all reasonable times for inspection. [N.J.A.C. 7:26-2.11(d)]

Subject Item: SWLG874000 - Final Cap Construction

13. The final cover for the landfill shall consist of the following capping system in descending order:
- 6-inch amended topsoil layer (grassed)
- fabric filter/geotextile
- 6-inch drainage layer of granular/crushed stone or recycled masonry product meeting unrestricted use soil cleanup criteria
- geotextile
- 2-foot layer of processed dredge material provided as a protective layer
- 1-foot cap layer of processed dredge material having an in-place hydraulic conductivity no greater than 1 X 10^(-6) cm/sec
- geotextile
- 6- inch gas collection layer of granular/crushed stone or recycled masonry product meeting unrestricted use soil cleanup criteria

Alternatively, areas of the site that will be developed with asphalt pavement and building structures, the cap shall be in conformance with the sections depicted on Sheet 47 of 49 entitled Detail Sheet. [N.J.A.C. 7:26-2A.7(i)]

14. A quality assurance inspector, independent of the quality control inspector, approved by the Department and reporting directly to the Department, shall be at the site at all times during the initial construction phase of the cap and containment systems to observe and perform all required systems audits of the quality control inspections to insure proper implementation of the design and permit requirements. For the purposes of this section, quality control assurance means the periodic testing and observations performed by the owner and/or operator of a landfill as a check on the construction contractor's quality control activities. [N.J.A.C. 7:26-2A.7(a)7]

15. Quality control inspectors shall be at the site during all phases of construction to ensure and verify that the approved closure plan design is properly implemented. The quality control inspectors shall, at a minimum, be at the site at all times during the construction of the approved engineering controls. For the purposes of this section, quality control means those activities and responsibilities assigned to the construction contractor, manufacturer, installer or supplier to measure and regulate the characteristics or properties of an item in order to ensure that the applicable landfill construction requirements at N.J.A.C. 7:26-2A.7, (a)12 and 13 are met. This includes those actions taken before, during, or after construction to ensure that the materials used and the completed workmanship are in conformance with the construction requirements at N.J.A.C. 7:26-2A.7. [N.J.A.C. 7:26-2A.7(a)9]

16. The quality control measures and tests required by N.J.A.C. 7:26-2A.7 and described in the QA and QC plan submitted in accordance with N.J.A.C. 7:26-2A.5(a)7 shall be employed to ensure that the construction requirements are properly implemented and that the design and performance standards are achieved. [N.J.A.C. 7:26-2A.7(a)10]

Subject Item: SWLG874000 - Final Cap Construction

17. Best available engineering construction practices shall be employed for all phases of construction. [N.J.A.C. 7:26-2A.7(a)18]

18. A New Jersey licensed professional engineer shall certify, in writing, to the Department that he or she has supervised the inspection of the construction of each major phase of the sanitary landfill's closure. He or she shall further certify that each phase has been prepared and constructed in accordance with the closure design approved by the Department. The certification shall include as-built drawings. [N.J.A.C. 7:26-2A.9(d)10I]

19. A New Jersey licensed professional engineer shall certify that the materials utilized in the closure of the sanitary landfill are in conformance with and meet the specifications of the approved closure design. [N.J.A.C. 7:26-2A.9(d)10Ii]

20. There shall be no deviation from the approved closure design without the prior written approval of the design engineer and, at a minimum, prior verbal approval by the Department. [N.J.A.C. 7:26-2A.9(d)10Iii]

21. All certifications shall bear the raised seal of the New Jersey licensed professional engineer, his or her signature, and the date of certification. [N.J.A.C. 7:26-2A.9(d)10Iv]

22. The closure certification shall include the following statement: I certify under penalty of law that I have personally examined and am familiar with the information submitted in this document and all attachments and that, based on my inquiry of those individuals under my supervision, I believe the submitted information is true, accurate and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment. I understand that, in addition to criminal penalties, I may be liable for civil administrative penalty pursuant to N.J.A.C. 7:26-5 and that submitting false information may be grounds for denial, revocation or termination of any solid waste facility permit for which I may be seeking approval or now hold. [N.J.A.C. 7:26-2A.9(d)10V]

Subject Item: SWLG874115 - Monitoring

23. A methane gas venting system shall be installed along with the installation of the final cover as indicated on the closure plan. An Air Pollution Control Permit shall be obtained for the gas venting system pursuant to N.J.A.C. 7:27-8.2(a)16. [N.J.A.C. 7:26-2A.7(f)]

24. A ground water monitoring system shall be maintained and the ground water shall be monitored in conformance with the the approved monitoring plan. [N.J.A.C. 7:26-2A.9(e)]

25. The owner shall monitor and maintain the landfill in accordance with the Post-Closure Care Plan through implementation of the following maintenance programs: (a) A program for the maintenance of final cover and final cover vegetation; (b) A program for the maintenance of side slopes; (c) A program for the maintenance of run-on and run-off control programs; (d) A program for the maintenance of groundwater monitoring wells; (e) A program for the maintenance of methane gas venting or evacuation system; (f) A program for the operation and maintenance of a leachate collection and\or control system; (g) A program for the maintenance of the facility access control system; (h) A program for the maintenance of measures to conform the site to the surrounding areas. [N.J.A.C. 7:26-2A.9(e)]

26. Periodic inspections of the facility, as presented in the Closure and Post-Closure Care Plan, shall be conducted on a quarterly basis. Reports of the inspections shall be submitted to the Site Remediation Program as a condition of this Approval. [N.J.A.C. 7:26-2A.9(e)]

Subject Item: SWLG874115 - Monitoring

27. The following information shall be submitted on a quarterly basis (February, May, August and November of each calendar year) to the Site Remediation Program: Ground water monitoring results; methane monitoring results and facility inspection reports. [N.J.A.C. 7:26-2A.9(e)]

28. The Department may reduce the post-closure care period to less than thirty (30) years when it has been adequately demonstrated that the reduced period is sufficient to protect human health and the environment. Prior to the time that the post-closure care period is due to expire, the Department may extend the post-closure care period upon a finding that such extended period is necessary to protect human health and/or the environment. Any aggrieved person may petition the Department for an extension or reduction to the post-closure care period, based on good cause. [N.J.A.C. 7:26-2A.9(c)]

29. A copy of the approved Closure and Post-Closure Care Plan shall be filed with the municipal clerk after closure is complete. [N.J.A.C. 7:26-2A.9(d)]

CLEANEARTH

Faster, smarter, greener solutions.

September 29, 2011

Mr. Amson Solomon
Artimus Construction
37 W. 65th Street
New York, NY 10023

Re: Chelsea W. 26th LLC
Waste Type: D008
Approval Code Number: 113082075

Dear Mr Solomon,

In compliance with 40 CFR Part 264.12 (b) and 6 NYCRR 373-2.2 (d) (2) this letter notifies you that Clean Earth of North Jersey (CENJ) has the appropriate permits and the capacity to accept the above refereed waste stream.

CENJ has based the approval of this waste stream on the information provided including the Waste Material Profile Sheet and any accompanying information such as lab data or Material Safety Data Sheets.

If you may have any questions concerning this approval please call us at your earliest convenience.

Sincerely,

Robert Fixter
General Manager

Mydoc/Artimus

State of New Jersey

DEPARTMENT OF ENVIRONMENTAL PROTECTION

JON S. CORZINE
Governor

LISA P. JACKSON
Commissioner

Solid & Hazardous Waste Management Program
P.O. Box 414
Trenton, NJ 08625-0414
Tel. No. (609) 984-5950
Fax. No. (609) 633-9839
http://www.state.nj.us/dep/dshw

Solid and Hazardous Waste Facility Permit

Under the provisions of N.J.S.A. 13:1E-1 et seq. known as the Solid Waste Management Act, this permit is hereby issued to:

CLEAN EARTH OF NORTH JERSEY INC
105 Jacobus Ave
Kearny, New Jersey 07032

For the Purpose of Operating a:	Solid and Hazardous Waste Treatment, Storage and Transfer Facility
Lot & Block Nos:	14,14A, 289
In the Municipality of:	Kearny Town
County:	Hudson
Under Facility Permit No.:	HWP050002
EPA ID No.:	NJD991291105

This permit is subject to compliance with all conditions specified herein and all regulations promulgated by the Department of Environmental Protection.

This permit shall not prejudice any claim the State may have to riparian land, nor does it allow the permittee to fill or alter or allow to be filled or altered in any way, lands that are deemed to be riparian, wetlands, stream encroachment areas or flood plains, or that are within the Coastal Area Facility Review Act (CAFRA) zone or are subject to the Pinelands Protection Act of 1979, nor shall it allow the discharge of pollutants to waters of this State without prior acquisition of the necessary grants, permits, or approvals from the Department of Environmental Protection or the U.S. Environmental Protection Agency.

Anthony Fontana

Anthony Fontana, Chief
Bureau of Solid and Hazardous Waste Permitting – North

July 18, 1994
Issuance Date

October 23, 2006
Latest Modification Date

August 18, 2004
Expiration Date

Richard J Codey
Acting Governor

State of New Jersey
Department of Environmental Protection
Division of Solid and Hazardous Waste
401 East State Street
P.O. Box 414
Trenton, New Jersey 08625-0414
Tel. # (609) 292-9880
Fax. # (609)-633-9839
http://www.state.nj.us/dep/dshw/

Bradley M. Campbell
Commissioner

August 1, 2005

Robert Fixter
President
Clean Earth of North Jersey, Inc.
115 Jacobus Avenue
Kearny, New Jersey 07032

Re: Continuation of Expiring Permit, Clean Earth of North Jersey, Inc , Kearny, Hudson County, USEPA ID No. NJD 991 291 105, NJ Hazardous Waste Facility Permit No.: 0907N1HP14

Dear Mr. Fixter:

The purpose of this letter is to clarify the current status of Hazardous Waste Facility Permit No. 0907N1HP14 issued to Clean Earth of North Jersey, Inc. (CENJ) for the above referenced facility.

The current hazardous waste facility permit for the CENJ facility lists an expiration date of August 18, 2004 However, CENJ has submitted an application for renewal of the hazardous waste facility permit that is currently under review by the Division. Therefore, Hazardous Waste Facility Permit No. 0907N1HP14, and any subsequent modifications, shall remain in effect and enforceable until such time as the Division makes a final determination regarding the renewal application.

Should you have any questions regarding this matter, please call John Scott of my staff at 609-984-2040 or e-mail him at john.scott@dep.state.nj.us.

Very truly yours,

Anthony Fontana, Chief
Bureau of Hazardous Waste and Transfer Facilities

C: Barry Tornick, USEPA, Region II
Jeffery Sterling, BHWCE-Northern
Document: Continuation of permit

APPENDIX I

Disposal Manifests for Hazardous Waste Disposal Activities

Please print or type. (Form designed for use on elite (12-pitch) typewriter.) Form Approved. OMB No. 2050-0039

UNIFORM HAZARDOUS WASTE MANIFEST

1. Generator ID Number	2. Page 1 of	3. Emergency Response Phone	4. Manifest Tracking Number
NYR000184218	1	(516) 576-8844	008930754 JJK

GENERATOR

5. Generator's Name and Mailing Address
Chelsea W26 LLC
37 65th Street-2nd floor
New York, NY 10023
Generator's Phone:

Generator's Site Address (if different than mailing address)
Chelsea W26 LLC
260 West 26th Street
New York, NY 10023

6. Transporter 1 Company Name (516) 576-8844
L & D TRUCKING INC. Haz Waste AM469H NJ #3
U.S. EPA ID Number: NJR000029967

7. Transporter 2 Company Name
U.S. EPA ID Number:

8. Designated Facility Name and Site Address
Clean Earth of North Jersey, Inc.
105 Jacobus Ave
South Kearny, NJ 07032
Facility's Phone: (973) 344-4004
U.S. EPA ID Number: NJD991291103

9a. HM	9b. U.S. DOT Description (including Proper Shipping Name, Hazard Class, ID Number, and Packing Group (if any))	10. Containers No.	10. Containers Type	11. Total Quantity	12. Unit Wt./Vol.	13. Waste Codes
X	1. RQ Hazardous Waste Solid, NOS (Lead) 9 NA 3077 PG:III	1	DT	45 / 22	Y	D008
	2.					
	3.					
	4.					

14. Special Handling Instructions and Additional Information
CEI 308000064430 App: 113082075;
(1) ERG# 171; 65% Medium Grained Sand; 30% Brick

15. **GENERATOR'S/OFFEROR'S CERTIFICATION:** I hereby declare that the contents of this consignment are fully and accurately described above by the proper shipping name, and are classified, packaged, marked and labeled/placarded, and are in all respects in proper condition for transport according to applicable international and national governmental regulations. If export shipment and I am the Primary Exporter, I certify that the contents of this consignment conform to the terms of the attached EPA Acknowledgment of Consent.
I certify that the waste minimization statement identified in 40 CFR 262.27(a) (if I am a large quantity generator) or (b) (if I am a small quantity generator) is true.

Generator's/Offeror's Printed/Typed Name: Jason T. Cooper As Agent For Gen. Signature: Jason T. Cooper Month: 10 Day: 5 Year: 2011

INT'L

16. International Shipments ☐ Import to U.S. ☐ Export from U.S. Port of entry/exit:
Transporter signature (for exports only): Date leaving U.S.:

TRANSPORTER

17. Transporter Acknowledgment of Receipt of Materials

Transporter 1 Printed/Typed Name: Ed Conn Signature: Ed Conn Month: 10 Day: 5 Year: 11

Transporter 2 Printed/Typed Name: Signature: Month: Day: Year:

DESIGNATED FACILITY

18. Discrepancy

18a. Discrepancy Indication Space ☒ Quantity ☐ Type ☐ Residue ☐ Partial Rejection ☐ Full Rejection
Rec'd 37960 lbs
Manifest Reference Number:

18b. Alternate Facility (or Generator) U.S. EPA ID Number:
Facility's Phone:

RECEIVED PENDING MANIFEST REVIEW AND QUALITY CONTROL

18c. Signature of Alternate Facility (or Generator) Month: Day: Year:

19. Hazardous Waste Report Management Method Codes (i.e., codes for hazardous waste treatment, disposal, and recycling systems)

1.	2.	3.	4.
H111			

20. Designated Facility Owner or Operator: Certification of receipt of hazardous materials covered by the manifest except as noted in Item 18a

Printed/Typed Name: Doug Murray Signature: Month: 10 Day: Year:

EPA Form 8700-22 (Rev. 3-05) ~~Previous~~ editions are obsolete.

DESIGNATED FACILITY TO DESTINATION STATE (IF REQUIRED)

Clean Earth of North Jersey
115 Jacobus Avenue
South Kearny, NJ 07032
Ph: (973) 344-0004 Fax: (973) 344-2652

Ticket: 3880500643883

	Date	Time	Scale
In:	10/5/2011	09:36:29	Scale 1
Out:	10/5/2011	10:55:09	Scale 1

******* Reprinted Ticket - Edited *******

	Lbs	Tns
Gross:	84060	42.13
Tare:	26300	13.15
Net:	57760	28.98

Manifest: 088930754JJK
Vehicle ID: JRD-A
Vehicle Permit: 067389
Customer: GRIFFUS CONSTRUCTION, INC
Hauler DEP#: 50183
Facility Approval#: NA
Generator: Chelsea W26 LLC
Gen Address: 37 65th Street-2nd floor
New York, NY 10023
Job Name: UNDERGROUND PROJECTS W/O APPROVAL
Job Address: , "

Origin	Materials & Services	Quantity	Unit
New York	Hazardous Soil - Tons	28.98	Tns
	Contaminate Type: Not Applicable		
	Treatment Type: Not Applicable		
	Fac Waste Code: C.P.TOX-LEAD		

Comments:

Drivers: _____

Facility: _____
Morlash, Douglas

Please print or type. (Form designed for use on elite (12-pitch) typewriter.) Form Approved. OMB No. 2050-0039

UNIFORM HAZARDOUS WASTE MANIFEST

1. Generator ID Number	2. Page 1 of	3. Emergency Response Phone	4. Manifest Tracking Number
NYR000184218	1	(516) 576-8844	008930750 JJK

GENERATOR

5. Generator's Name and Mailing Address
Chelsea W26 LLC
37 65th Street-2nd floor
New York, NY 10023
Generator's Phone:

Generator's Site Address (if different than mailing address)
Chelsea W26 LLC
260 West 26th Street
New York, NY 10023

6. Transporter 1 Company Name (516) 576-8844
J & D TRUCKING INC. Haz Waste

U.S. EPA ID Number
NJR000029967

7. Transporter 2 Company Name

U.S. EPA ID Number

8. Designated Facility Name and Site Address
Clean Earth of North Jersey, Inc.
105 Jacobus Ave
South Kearny, NJ 07032
Facility's Phone: (973) 344-4004

U.S. EPA ID Number
NJD991291105

9a. HM	9b. U.S. DOT Description (including Proper Shipping Name, Hazard Class, ID Number, and Packing Group (if any))	10. Containers No.	10. Containers Type	11. Total Quantity	12. Unit Wt./Vol.	13. Waste Codes
X	1. RQ Hazardous Waste Solid, NOS (Lead) 9 NA 3077 PG:III	1	DT	22	Y	D008
	2.					
	3.					
	4.					

14. Special Handling Instructions and Additional Information
CEI 308000064433 App: 113082075;
(1) ERG# 171; 65% Medium Grained Sand; 30% Brick

15. **GENERATOR'S/OFFEROR'S CERTIFICATION:** I hereby declare that the contents of this consignment are fully and accurately described above by the proper shipping name, and are classified, packaged, marked and labeled/placarded, and are in all respects in proper condition for transport according to applicable International and national governmental regulations. If export shipment and I am the Primary Exporter, I certify that the contents of this consignment conform to the terms of the attached EPA Acknowledgment of Consent.
I certify that the waste minimization statement identified in 40 CFR 262.27(a) (if I am a large quantity generator) or (b) (if I am a small quantity generator) is true.

Generator's/Offeror's Printed/Typed Name: Jason T. Cooper As Agent For Gen. Signature: Jason T Cooper Month: 10 Day: 5 Year: 11

INT'L

16. International Shipments ☐ Import to U.S. ☐ Export from U.S. Port of entry/exit:
Transporter signature (for exports only): Date leaving U.S.:

TRANSPORTER

17. Transporter Acknowledgment of Receipt of Materials
Transporter 1 Printed/Typed Name: ED CONN Signature: Month: 10 Day: 5 Year: 11
Transporter 2 Printed/Typed Name: Signature: Month: Day: Year:

DESIGNATED FACILITY

18. Discrepancy
18a. Discrepancy Indication Space ☒ Quantity ☐ Type ☐ Residue ☐ Partial Rejection ☐ Full Rejection
Recd 62860lbs Manifest Reference Number:

18b. Alternate Facility (or Generator) U.S. EPA ID Number

RECEIVED PENDING MANIFEST REVIEW AND QUALITY CONTROL

18c. Signature of Alternate Facility (or Generator) Month: Day: Year:

19. Hazardous Waste Report Management Method Codes (i.e., codes for hazardous waste treatment, disposal, and recycling systems)

1.	2.	3.	4.
H111			

20. Designated Facility Owner or Operator: Certification of receipt of hazardous materials covered by the manifest except as noted in Item 18a
Printed/Typed Name: Doug Morath Signature: Month: 10 Day: 5 Year: 11

EPA Form 8700-22 (Rev. 3-05). Previous editions are obsolete.

DESIGNATED FACILITY TO DESTINATION STATE (IF REQUIRED)

Clean Earth of North Jersey
115 Jacobus Avenue
South Kearny, NJ 07032
Ph: (973) 444-4004 Fax: (973) 344-2652

Ticket: 3000000653816

	Date	Time	Scale
In:	10/5/2011	15:25:25	Scale 1
Out:	10/5/2011	15:34:46	Scale 1

	Lbs	Tns
Gross:	89860	44.94
Tare:	26020	13.01
Net:	63860	31.93

Manifest: 000338750JJK
Vehicle ID: JKD-3
Vehicle Permit: 007309
Customer: ARTIMUS CONSTRUCTION, INC
Hauler DEP: 50181
Facility ApprovalNr: NA
Generator: Chelsea W26 LLC
Job Name: INBOUND PROJECTS W/O APPROVAL
Gen Address: 37 65th Street-2nd floor
New York, NY 10023
Job Address: ,

Origin	Materials & Services	Quantity	Unit
New York	Hazardous Soil - Tons	31.93	Tns
	Contaminate Type: Not Applicable		
	Treatment Type: Not Applicable		
	Fac Waste Code: E.P.TOX-LEAD		

Comments:

Driver: _____

Facility: _____
Moriarti, Douglas

Please print or type. (Form designed for use on elite (12-pitch) typewriter.) Form Approved. OMB No. 2050-0039

UNIFORM HAZARDOUS WASTE MANIFEST

1. Generator ID Number: NYR000184318
2. Page 1 of: 1
3. Emergency Response Phone: (516) 576-8844
4. Manifest Tracking Number: 008930749 JJK

GENERATOR

5. Generator's Name and Mailing Address
Chelsea W26 LLC
37 65th Street-2nd floor
New York, NY 10023
Generator's Phone:

Generator's Site Address (if different than mailing address)
Chelsea W26 LLC
260 West 26th Street
New York, NY 10023

6. Transporter 1 Company Name: (516) 576-8844 J & D TRUCKING INC Haz Waste Am469H NJ #3
U.S. EPA ID Number: NJR000029967

7. Transporter 2 Company Name
U.S. EPA ID Number

8. Designated Facility Name and Site Address: Clean Earth of North Jersey, Inc.
105 Jacobus Ave
South Kearny, NJ 07032
Facility's Phone: (973) 344-4004
U.S. EPA ID Number: NJD991291105

9a. HM	9b. U.S. DOT Description (including Proper Shipping Name, Hazard Class, ID Number, and Packing Group (if any))	10. Containers No.	10. Containers Type	11. Total Quantity	12. Unit Wt./Vol.	13. Waste Codes
X	1. RQ Hazardous Waste Solid, NOS (Lead) 9 NA 3077 PG:III	1	DT	22	Y	D008
	2.					
	3.					
	4.					

14. Special Handling Instructions and Additional Information
CEI 308000064432 App: 113082075;
(1) ERG# 171; 65% Medium Grained Sand; 30% Brick

15. **GENERATOR'S/OFFEROR'S CERTIFICATION:** I hereby declare that the contents of this consignment are fully and accurately described above by the proper shipping name, and are classified, packaged, marked and labeled/placarded, and are in all respects in proper condition for transport according to applicable international and national governmental regulations. If export shipment and I am the Primary Exporter, I certify that the contents of this consignment conform to the terms of the attached EPA Acknowledgment of Consent.
I certify that the waste minimization statement identified in 40 CFR 262.27(a) (if I am a large quantity generator) or (b) (if I am a small quantity generator) is true.

Generator's/Offeror's Printed/Typed Name: Jason T. Cooper As Agent For Gen
Signature:
Month: 10 Day: 5 Year: 11

INT'L

16. International Shipments ☐ Import to U.S. ☐ Export from U.S. Port of entry/exit:
Transporter signature (for exports only): Date leaving U.S.:

TRANSPORTER

17. Transporter Acknowledgment of Receipt of Materials
Transporter 1 Printed/Typed Name: EJ Cain
Signature:
Month: 10 Day: 5 Year: 11
Transporter 2 Printed/Typed Name
Signature
Month Day Year

DESIGNATED FACILITY

18. Discrepancy
18a. Discrepancy Indication Space ☒ Quantity ☐ Type ☐ Residue ☐ Partial Rejection ☐ Full Rejection
Recd 61060163
Manifest Reference Number:

18b. Alternate Facility (or Generator)
U.S. EPA ID Number
RECEIVED PENDING MANIFEST REVIEW AND QUALITY CONTROL
Facility's Phone:
18c. Signature of Alternate Facility (or Generator)
Month Day Year

19. Hazardous Waste Report Management Method Codes (i.e., codes for hazardous waste treatment, disposal, and recycling systems)

1.	2.	3.	4.
H111			

20. Designated Facility Owner or Operator: Certification of receipt of hazardous materials covered by the manifest except as noted in Item 18a
Printed/Typed Name: Doug Morales
Signature:
Month: 10 Day: 5 Year: 11

EPA Form 8700-22 (Rev. 3-05) Previous editions are obsolete.

DESIGNATED FACILITY TO DESTINATION STATE (IF REQUIRED)

Clean Earth of North Jersey
115 Jacobus Avenue
South Kearny, NJ 07032
Ph: (973) 444-4004 Fax: (973) 344-2652

Ticket: 2000000064993

	Date	Time	Scale
In:	10/5/2011	13:19:23	Scale 1
Out:	10/5/2011	13:21:31	Scale 1

	Lbs	Tns
Gross:	97260	43.63
Tare:	26200	13.10
Net:	61060	30.53

Manifest: 008930740JJK
Vehicle ID: J&D-3
Vehicle Permit: 007389
Customer: ORTIMUS CONSTRUCTION, INC
Hauler DEP: 50181
Facility Approval#: NO
Generator: Chelsea W26 LLC
Gen Address: 37 55th Street-2nd floor
New York, NY 10023
Job Name: INBOUND PROJECTS W/O APPROVAL
Job Address: , -

Origin	Materials & Services	Quantity	Unit
New York	Hazardous Soil - Tons	30.53	Tns
	Contaminate Type: Not Applicable		
	Treatment Type: Not Applicable		
	Fac Waste Codes: E.P.TOX-LEAD		

Comments:

Drivers: _____

Facility: _____
Moriasi, Douglas

Please print or type. (Form designed for use on elite (12-pitch) typewriter.) Form Approved. OMB No. 2050-0039

UNIFORM HAZARDOUS WASTE MANIFEST

1. Generator ID Number: NYR000184218
2. Page 1 of: 1
3. Emergency Response Phone: (516) 576-8844
4. Manifest Tracking Number: 008930771 JJK

GENERATOR

5. Generator's Name and Mailing Address
Chelsea W26 LLC
37 65th Street-2nd floor
New York, NY 10023
Generator's Phone:

Generator's Site Address (if different than mailing address)
Chelsea W26 LLC
260 West 26th Street
New York, NY 10023

6. Transporter 1 Company Name: (516) 576-8844 — J & D TRUCKING INC. Haz Waste — AM469H #3
U.S. EPA ID Number: NJR000029967

7. Transporter 2 Company Name
U.S. EPA ID Number

8. Designated Facility Name and Site Address: Clean Earth of North Jersey, Inc.
105 Jacobus Ave
South Kearny, NJ 07032
Facility's Phone: (973) 344-4004
U.S. EPA ID Number: NJD991291105

9a. HM	9b. U.S. DOT Description (including Proper Shipping Name, Hazard Class, ID Number, and Packing Group (if any))	10. Containers No.	10. Containers Type	11. Total Quantity	12. Unit Wt./Vol.	13. Waste Codes
X	1. RQ Hazardous Waste Solid, NOS (Lead) 9 NA 3077 PG:III	1	DT	27	Y	D008
	2.					
	3.					
	4.					

14. Special Handling Instructions and Additional Information
CEI 308000064497 App: 113082075;
(1) ERG# 171; 65% Medium Grained Sand; 30% Brick

15. **GENERATOR'S/OFFEROR'S CERTIFICATION:** I hereby declare that the contents of this consignment are fully and accurately described above by the proper shipping name, and are classified, packaged, marked and labeled/placarded, and are in all respects in proper condition for transport according to applicable international and national governmental regulations. If export shipment and I am the Primary Exporter, I certify that the contents of this consignment conform to the terms of the attached EPA Acknowledgment of Consent.
I certify that the waste minimization statement identified in 40 CFR 262.27(a) (if I am a large quantity generator) or (b) (if I am a small quantity generator) is true.

Generator's/Offeror's Printed/Typed Name: as agent for Generator Jessica Proscia — Signature — Month 10 Day 7 Year 11

INT'L

16. International Shipments ☐ Import to U.S. ☐ Export from U.S. Port of entry/exit:
Transporter signature (for exports only): Date leaving U.S.:

TRANSPORTER

17. Transporter Acknowledgment of Receipt of Materials
Transporter 1 Printed/Typed Name: EN Conn — Signature — Month 10 Day 7 Year 11
Transporter 2 Printed/Typed Name — Signature — Month Day Year

DESIGNATED FACILITY

18. Discrepancy
18a. Discrepancy Indication Space ☒ Quantity ☐ Type ☐ Residue ☐ Partial Rejection ☐ Full Rejection
Rcvd 53540lbs
Manifest Reference Number:
18b. Alternate Facility (or Generator) — U.S. EPA ID Number
RECEIVED PENDING MANIFEST REVIEW AND QUALITY CONTROL
Facility's Phone:
18c. Signature of Alternate Facility (or Generator) — Month Day Year

19. Hazardous Waste Report Management Method Codes (i.e., codes for hazardous waste treatment, disposal, and recycling systems)
1. H111 2. 3. 4.

20. Designated Facility Owner or Operator: Certification of receipt of hazardous materials covered by the manifest except as noted in Item 18a
Printed/Typed Name: Doug Murphy — Signature — Month 10 Day 7 Year 11

EPA Form 8700-22 (Rev. 3-05) Previous editions are obsolete.

DESIGNATED FACILITY TO DESTINATION STATE (IF REQUIRED)

Clean Earth of North Jersey
115 Jacobus Avenue
South Kearny, NJ 07032
Ph: (973) 444-4004 Fax: (973) 344-2652

Ticket: 308000065205

	Date	Time	Scale
In:	10/7/2011	11:59:03	Scale 1
Out:	10/7/2011	12:20:49	Scale 1

	Lbs	Tns
Gross:	79660	39.83
Tare:	25820	12.91
Net:	53840	26.92

Manifest: 008930770JJK
Vehicle ID: J&D-3
Vehicle Permit: 087309
Customer: ARTIMUS CONSTRUCTION, INC
Hauler DEP: 50181
Facility Approval#: NA
Job Name: INBOUND PROJECTS W/O APPROVAL
Job Address: , -

Generator: Chelsea W26 LLC
Gen Address: 37 65th Street-2nd floor
New York, NY 10023

Origin	Materials & Services	Quantity	Unit
New York	Hazardous Soil - Tons	26.92	Tns

Contaminate Type: Not Applicable
Treatment Type: Not Applicable
Fac Waste Code: E.P.TOX-LEAD

Comment:

Driver: _____

Facility: _____
Moriasi, Douglas

Please print or type. (Form designed for use on elite (12-pitch) typewriter.) Form Approved. OMB No. 2050-0039

UNIFORM HAZARDOUS WASTE MANIFEST

1. Generator ID Number: NYR000184218
2. Page 1 of: 1
3. Emergency Response Phone: (516) 576-8844
4. Manifest Tracking Number: 008930770 JJK

GENERATOR

5. Generator's Name and Mailing Address
Chelsea W26 LLC
37 65th Street-2nd floor
New York, NY 10023
Generator's Phone: (516) 576-8844

Generator's Site Address (if different than mailing address)
Chelsea W26 LLC
260 West 26th Street
New York, NY 10023

6. Transporter 1 Company Name: J & D TRUCKING INC. Haz Waste — Dm469H NJ TJ
U.S. EPA ID Number: NJR000029967

7. Transporter 2 Company Name
U.S. EPA ID Number

8. Designated Facility Name and Site Address: Clean Earth of North Jersey, Inc.
105 Jacobus Ave
South Kearny, NJ 07032
Facility's Phone: (973) 344-4004
U.S. EPA ID Number: NJD991291105

9a. HM	9b. U.S. DOT Description (including Proper Shipping Name, Hazard Class, ID Number, and Packing Group (if any))	10. Containers No.	10. Containers Type	11. Total Quantity	12. Unit Wt./Vol.	13. Waste Codes
X	1. RQ Hazardous Waste Solid, NOS (Lead) 9 NA 3077 PG:III	1	DT	CST 22	T	D008
	2.					
	3.					
	4.					

14. Special Handling Instructions and Additional Information
CEI 308000064498 App: 113082075;
(1) ERG# 171; 65% Medium Grained Sand; 30% Brick

15. **GENERATOR'S/OFFEROR'S CERTIFICATION:** I hereby declare that the contents of this consignment are fully and accurately described above by the proper shipping name, and are classified, packaged, marked and labeled/placarded, and are in all respects in proper condition for transport according to applicable international and national governmental regulations. If export shipment and I am the Primary Exporter, I certify that the contents of this consignment conform to the terms of the attached EPA Acknowledgment of Consent.
I certify that the waste minimization statement identified in 40 CFR 262.27(a) (if I am a large quantity generator) or (b) (if I am a small quantity generator) is true.

Generator's/Offeror's Printed/Typed Name: as agent to generator Jessica Proctor
Signature:
Month: 10 Day: 7 Year: 11

INT'L

16. International Shipments ☐ Import to U.S. ☐ Export from U.S. Port of entry/exit:
Transporter signature (for exports only): Date leaving U.S.:

TRANSPORTER

17. Transporter Acknowledgment of Receipt of Materials
Transporter 1 Printed/Typed Name: J D Conn
Signature:
Month: 10 Day: 7 Year: 11
Transporter 2 Printed/Typed Name
Signature
Month Day Year

DESIGNATED FACILITY

18. Discrepancy
18a. Discrepancy Indication Space ☒ Quantity ☐ Type ☐ Residue ☐ Partial Rejection ☐ Full Rejection
Rec'd 59680lbs
Manifest Reference Number:
18b. Alternate Facility (or Generator)
U.S. EPA ID Number
Facility's Phone:
RELEASED PENDING MANIFEST REVIEW AND QUALITY CONTROL
18c. Signature of Alternate Facility (or Generator)
Month Day Year

19. Hazardous Waste Report Management Method Codes (i.e., codes for hazardous waste treatment, disposal, and recycling systems)
1. H111 2. 3. 4.

20. Designated Facility Owner or Operator: Certification of receipt of hazardous materials covered by the manifest except as noted in Item 18a
Printed/Typed Name: Doug Moriarty
Signature:
Month: 10 Day: 7 Year: 11

EPA Form 8700-22 (Rev. 3-05) Previous editions are obsolete.

DESIGNATED FACILITY TO DESTINATION STATE (IF REQUIRED)

Clean Earth of North Jersey
115 Jacobus Avenue
South Kearny, NJ 07032
Ph: (973) 444-4884 Fax: (973) 344-2632

Ticket: 3000000065178

	Date	Time	Scale
In:	10/7/2011	08:49:27	Scale 1
Out:	10/7/2011	09:46:36	Scale 1

	Lbs	Tns
Gross:	85840	42.92
Tare:	26160	13.08
Net:	59680	29.84

Manifest: 000530771JJK
Vehicle ID: JAD-3
Vehicle Permit: M87389
Customer: ARTIMUS CONSTRUCTION, INC
Hauler DEP: 52101
Facility Approval#: NA
Generator: Chelsea W26 LLC
Gen Address: 37 65th Street-2nd floor
New York, NY 10023
Job Name: INBOUND PROJECTS W/O APPROVAL
Job Address: ,

Origin	Materials & Services	Quantity	Unit
New York	Hazardous Soil - Tons	29.84	Tns

Contaminate Types: Not Applicable
Treatment Types: Not Applicable
Fac Waste Code: E.P.TOX-LEAD

Comments:

Drivers: _____

Facility: _____
Moriasi, Douglas

APPENDIX J

Soil Test Results for Post-Excavation Samples from Test Pits TP-5 and TP-7

AMERICAN ANALYTICAL LABORATORIES

NYSDOH 11418
NJDEP NY050
CTDOH PH-0205
PADEP 68-00573

Thursday, October 06, 2011

Steve Malinowski
CA Rich Consultants Inc.
17 Dupont Street
Plainview, NY 11803

TEL: (516) 576-8844
FAX (516) 576-0093

RE: Artimus, 260 W. 26th Street, New York, N

Order No.: 1110040

Dear Steve Malinowski:

American Analytical Laboratories, LLC. received 8 sample(s) on 10/5/2011 for the analyses presented in the following report.

Samples were analyzed in accordance with the test procedures documented on the chain of custody and detailed throughout the text of this report.

The results reported herein relate only to the items tested or to the samples as received by the laboratory. This report may not be reproduced, except in full, without the approval of American Analytical Laboratories, LLC and is not considered complete without a cover page and chain of custody documentation. The limits (LOQ) provided in the data package are analytical reporting limits and not Federal or Local mandated values to which the sample results should be compared.

There were no problems with the analyses and all data for associated QC met laboratory specifications. If there are any exceptions a Case Narrative is provided in the report or the data is qualified. This package has been reviewed by American Analytical Laboratories' QA Department/Laboratory Director to comply with NELAC standards prior to report submittal. This report consists of 22 pages.

If you have any questions regarding these tests results, please do not hesitate to call (631) 454-6100 or email me directly at lbeyer@american-analytical.com.

Sincerely,

Lori Beyer
Lab Director

American Analytical Laboratories, LLC.

Date: *06-Oct-11*

CLIENT: CA Rich Consultants Inc.
Project: Artimus, 260 W. 26th Street, New York, NY
Lab Order: 1110040

Work Order Sample Summary

Lab Sample ID	Client Sample ID	Date Collected	Date Received
1110040-01A	TP-5 (0-11') North	10/5/2011 9:20:00 AM	10/5/2011
1110040-01B	TP-5 (0-11') North	10/5/2011 9:20:00 AM	10/5/2011
1110040-02A	TP-5 (0-11') South	10/5/2011 9:25:00 AM	10/5/2011
1110040-02B	TP-5 (0-11') South	10/5/2011 9:25:00 AM	10/5/2011
1110040-03A	TP-5 (0-11') East	10/5/2011 9:30:00 AM	10/5/2011
1110040-03B	TP-5 (0-11') East	10/5/2011 9:30:00 AM	10/5/2011
1110040-04A	TP-5 (0-6') West	10/5/2011 9:35:00 AM	10/5/2011
1110040-04B	TP-5 (0-6') West	10/5/2011 9:35:00 AM	10/5/2011
1110040-05A	TP-7 (0-7') North	10/5/2011 11:25:00 AM	10/5/2011
1110040-05B	TP-7 (0-7') North	10/5/2011 11:25:00 AM	10/5/2011
1110040-06A	TP-7 (0-7') South	10/5/2011 11:30:00 AM	10/5/2011
1110040-06B	TP-7 (0-7') South	10/5/2011 11:30:00 AM	10/5/2011
1110040-07A	TP-7 (0-7') East	10/5/2011 11:35:00 AM	10/5/2011
1110040-07B	TP-7 (0-7') East	10/5/2011 11:35:00 AM	10/5/2011
1110040-08A	TP-7 (0-7') West	10/5/2011 11:40:00 AM	10/5/2011
1110040-08B	TP-7 (0-7') West	10/5/2011 11:40:00 AM	10/5/2011

AMERICAN ANALYTICAL LABORATORIES
56 TOLEDO STREET • FARMINGDALE, NEW YORK 11735
(631) 454-6100 • FAX (631) 454-8027
www.american-analytical.com

NYSDOH	11418
CTDOH	PH-0205
NJDEP	NY050
PADEP	68-573

CHAIN OF CUSTODY / REQUEST FOR ANALYSIS DOCUMENT

CLIENT NAME/ADDRESS: CA Rich, 17 Dupont Street, Plainview, NY
CONTACT: Steve Malinowski

SAMPLER (SIGNATURE): Jason T. Cooper
SAMPLER NAME (PRINT): Jason T. Cooper

SAMPLE(S) SEALED: YES / NO
CORRECT CONTAINER(S): YES / NO
TEMPERATURE (° C): 4.7

PROJECT LOCATION: Artimus, 260 W. 26th Street, New York, NY

LABORATORY ID# LAB USE ONLY	MATRIX/ TYPE	NO. OF CONTAINERS	SAMPLING DATE	SAMPLING TIME	SAMPLE # - LOCATION	ANALYSIS REQUIRED: TCLP Pb	Total Pb
1110C410-01AB	S	1	10/5/11	0920	TP-5(0-11') North	X	X
02AB	S	1	10/5/11	0925	TP-5 (0-11') South	X	X
03AB	S	1	10/5/11	0930	TP-5(0-11') East	X	X
04AB	S	1	10/5/11	0935	TP-5 (0-6') West	X	X
05AB	S	1	10/5/11	1125	TP-7 (0-7') North	X	X
06AB	S	1	10/5/11	1130	TP-7(0-7') South	X	X
07AB	S	1	10/5/11	1135	TP-7(0-7') East	X	X
08AB	S	1	10/5/11	1140	TP-7(0-7') West	X	X

COMMENTS / INSTRUCTIONS: 24hr. TAT ✱ TP-5- Bedrock encountered @ 6'

Samples must be on ICE (<6° C)

MATRIX S=SOIL; W=WATER; SL=SLUDGE; A=AIR; M=MISCELLANEOUS
TYPE G=GRAB; C=COMPOSITE

TURNAROUND REQUIRED
STANDARD ☐ STAT ☐ (7-10 business days)
24 hr BY / /

E-MAIL ADDRESS FOR RESULTS: Smalinowski@carichinc.com

RELINQUISHED BY (SIGNATURE)	DATE / TIME	PRINTED NAME	RECEIVED BY LAB (SIGNATURE)	DATE / TIME	PRINTED NAME
Jason T. Cooper	10/5/11	Jason T. Cooper	P. Masi	10/5/11 1:30pm	P Masi
RELINQUISHED BY (SIGNATURE)	DATE / TIME	PRINTED NAME	RECEIVED BY LAB (SIGNATURE)	DATE / TIME	PRINTED NAME

WHITE-OFFICE / CANARY-LAB / PINK-SAMPLE CUSTODIAN / GOLDENROD-CLIENT

American Analytical Laboratories, LLC.

Sample Receipt Checklist

Client Name **CA RICH** Date and Time Receive **10/5/2011 1:51:30 PM**

Work Order Numbe **1110040** RcptNo: **1** Received by **PM**

COC_ID: CoolerID:

Checklist completed by Signature 10/05/11 Date Reviewed by Initials 10/6/11 Date

Matrix: Carrier name Courier

Shipping container/cooler in good condition?	Yes ☑	No ☐	Not Presen ☐
Custody seals intact on shippping container/cooler?	Yes ☐	No ☐	Not Presen ☑
Custody seals intact on sample bottles?	Yes ☐	No ☐	Not Presen ☑
Chain of custody present?	Yes ☑	No ☐	
Chain of custody signed when relinquished and received?	Yes ☑	No ☐	
Chain of custody agrees with sample labels?	Yes ☑	No ☐	
Samples in proper container/bottle?	Yes ☑	No ☐	
Sample containers intact?	Yes ☑	No ☐	
Sufficient sample volume for indicated test?	Yes ☑	No ☐	
All samples received within holding time?	Yes ☑	No ☐	
Container/Temp Blank temperature in compliance?	Yes ☑	No ☐	
Water - VOA vials have zero headspace?	No VOA vials submitted ☑	Yes ☐	No ☐
Water - pH acceptable upon receipt?	Yes ☐	No ☐	N/A ☐

Adjusted? _____ Checked b _____

Any No and/or NA (not applicable) response must be detailed in the comments section be

Client contacted _____ Date contacted: _____ Person contacted _____

Contacted by: _____ Regarding: _____

Comments:

Corrective Action _____

American Analytical Laboratories, LLC.

Date: *06-Oct-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-5 (0-11') North
Lab Order:	1110040	**Collection Date:**	10/5/2011 9:20:00 AM
Project:	Artimus, 260 W. 26th Street, New York, NY	**Matrix:**	SOIL
Lab ID:	1110040-01A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PERCENT MOISTURE			**D2216**				Analyst: **CF**
Percent Moisture	11.6	0	0		wt%	1	10/5/2011
LEAD,TOTAL			**SW6010C**		**SW3050B**		Analyst: **JP**
Lead	283	0.21	0.421		mg/Kg-dry	1	10/6/2011 2:11:49 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *06-Oct-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-5 (0-11') North
Lab Order:	1110040	**Collection Date:**	10/5/2011 9:20:00 AM
Project:	Artimus, 260 W. 26th Street, New York, NY	**Matrix:**	SOIL
Lab ID:	1110040-01B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP LEAD			**SW1311/6010C**		**SW1311**		Analyst: **JP**
Lead	8.54	0.005	0.0500	*	mg/L	1	10/6/2011 1:40:14 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *06-Oct-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-5 (0-11') South
Lab Order:	1110040	**Collection Date:**	10/5/2011 9:25:00 AM
Project:	Artimus, 260 W. 26th Street, New York, NY	**Matrix:**	SOIL
Lab ID:	1110040-02A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PERCENT MOISTURE			**D2216**				Analyst: **CF**
Percent Moisture	15.1	0	0		wt%	1	10/5/2011
LEAD,TOTAL			**SW6010C**		**SW3050B**		Analyst: **JP**
Lead	267	0.20	0.408		mg/Kg-dry	1	10/6/2011 2:14:02 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

ACCREDITED IN ACCORDANCE WITH nelac

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *06-Oct-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-5 (0-11') South
Lab Order:	1110040	**Collection Date:**	10/5/2011 9:25:00 AM
Project:	Artimus, 260 W. 26th Street, New York, NY	**Matrix:**	SOIL
Lab ID:	1110040-02B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP LEAD			**SW1311/6010C**		**SW1311**		Analyst: **JP**
Lead	1.18	0.005	0.0500		mg/L	1	10/6/2011 1:42:26 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *06-Oct-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-5 (0-11') East
Lab Order:	1110040	**Collection Date:**	10/5/2011 9:30:00 AM
Project:	Artimus, 260 W. 26th Street, New York, NY	**Matrix:**	SOIL
Lab ID:	1110040-03A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PERCENT MOISTURE			**D2216**				Analyst: **CF**
Percent Moisture	12.2	0	0		wt%	1	10/5/2011
LEAD,TOTAL			**SW6010C**		**SW3050B**		Analyst: **JP**
Lead	150	0.20	0.401		mg/Kg-dry	1	10/6/2011 2:19:31 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *06-Oct-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-5 (0-11') East
Lab Order:	1110040	**Collection Date:**	10/5/2011 9:30:00 AM
Project:	Artimus, 260 W. 26th Street, New York, NY	**Matrix:**	SOIL
Lab ID:	1110040-03B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP LEAD			**SW1311/6010C**		**SW1311**		Analyst: **JP**
Lead	0.817	0.005	0.0500		mg/L	1	10/6/2011 1:53:27 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *06-Oct-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-5 (0-6') West
Lab Order:	1110040	**Collection Date:**	10/5/2011 9:35:00 AM
Project:	Artimus, 260 W. 26th Street, New York, NY	**Matrix:**	SOIL
Lab ID:	1110040-04A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PERCENT MOISTURE			**D2216**				Analyst: **CF**
Percent Moisture	13.5	0	0		wt%	1	10/5/2011
LEAD,TOTAL			**SW6010C**		**SW3050B**		Analyst: **JP**
Lead	63.2	0.22	0.443		mg/Kg-dry	1	10/6/2011 2:21:44 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

ACCREDITED IN ACCORDANCE WITH nelac

Qualifiers:	B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
	E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
	J	Analyte detected below quantitation limits	LOD	Limit of Detection
	LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
	PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
	U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *06-Oct-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-5 (0-6') West
Lab Order:	1110040	**Collection Date:**	10/5/2011 9:35:00 AM
Project:	Artimus, 260 W. 26th Street, New York, NY	**Matrix:**	SOIL
Lab ID:	1110040-04B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP LEAD			**SW1311/6010C**		**SW1311**		Analyst: **JP**
Lead	0.144	0.005	0.0500		mg/L	1	10/6/2011 1:46:51 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *06-Oct-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-7 (0-7') North
Lab Order:	1110040	**Collection Date:**	10/5/2011 11:25:00 AM
Project:	Artimus, 260 W. 26th Street, New York, NY	**Matrix:**	SOIL
Lab ID:	1110040-05A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PERCENT MOISTURE			**D2216**				Analyst: **CF**
Percent Moisture	13.7	0	0		wt%	1	10/5/2011
LEAD,TOTAL			**SW6010C**		**SW3050B**		Analyst: **JP**
Lead	97.1	0.23	0.455		mg/Kg-dry	1	10/6/2011 2:32:07 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *06-Oct-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-7 (0-7') North
Lab Order:	1110040	**Collection Date:**	10/5/2011 11:25:00 AM
Project:	Artimus, 260 W. 26th Street, New York, NY	**Matrix:**	SOIL
Lab ID:	1110040-05B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP LEAD			**SW1311/6010C**		**SW1311**		Analyst: **JP**
Lead	2.52	0.005	0.0500		mg/L	1	10/6/2011 1:49:03 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *06-Oct-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-7 (0-7') South
Lab Order:	1110040	**Collection Date:**	10/5/2011 11:30:00 AM
Project:	Artimus, 260 W. 26th Street, New York, NY	**Matrix:**	SOIL
Lab ID:	1110040-06A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PERCENT MOISTURE			**D2216**				Analyst: **CF**
Percent Moisture	11.4	0	0		wt%	1	10/5/2011
LEAD,TOTAL			**SW6010C**		**SW3050B**		Analyst: **JP**
Lead	254	0.22	0.444		mg/Kg-dry	1	10/6/2011 2:34:19 PM

Qualifiers:	B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
	E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
	J	Analyte detected below quantitation limits	LOD	Limit of Detection
	LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
	PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
	U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *06-Oct-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-7 (0-7') South
Lab Order:	1110040	**Collection Date:**	10/5/2011 11:30:00 AM
Project:	Artimus, 260 W. 26th Street, New York, NY	**Matrix:**	SOIL
Lab ID:	1110040-06B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP LEAD			**SW1311/6010C**		**SW1311**		Analyst: **JP**
Lead	0.875	0.005	0.0500		mg/L	1	10/6/2011 1:51:15 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *06-Oct-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-7 (0-7') East
Lab Order:	1110040	**Collection Date:**	10/5/2011 11:35:00 AM
Project:	Artimus, 260 W. 26th Street, New York, NY	**Matrix:**	SOIL
Lab ID:	1110040-07A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PERCENT MOISTURE			**D2216**				Analyst: **CF**
Percent Moisture	11.7	0	0		wt%	1	10/5/2011
LEAD,TOTAL			**SW6010C**		**SW3050B**		Analyst: **JP**
Lead	847	0.2	0.395		mg/Kg-dry	1	10/6/2011 2:36:31 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

ACCREDITED IN ACCORDANCE WITH nelac

Qualifiers:	B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
	E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
	J	Analyte detected below quantitation limits	LOD	Limit of Detection
	LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
	PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
	U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *06-Oct-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-7 (0-7') East
Lab Order:	1110040	**Collection Date:**	10/5/2011 11:35:00 AM
Project:	Artimus, 260 W. 26th Street, New York, NY	**Matrix:**	SOIL
Lab ID:	1110040-07B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP LEAD			**SW1311/6010C**		**SW1311**		Analyst: **JP**
Lead	17.5	0.005	0.0500	*	mg/L	1	10/6/2011 1:44:39 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *06-Oct-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-7 (0-7') West
Lab Order:	1110040	**Collection Date:**	10/5/2011 11:40:00 AM
Project:	Artimus, 260 W. 26th Street, New York, NY	**Matrix:**	SOIL
Lab ID:	1110040-08A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PERCENT MOISTURE			**D2216**				Analyst: **CF**
Percent Moisture	13.7	0	0		wt%	1	10/5/2011
LEAD,TOTAL			**SW6010C**		**SW3050B**		Analyst: **JP**
Lead	310	0.22	0.431		mg/Kg-dry	1	10/6/2011 2:38:42 PM

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *06-Oct-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-7 (0-7') West
Lab Order:	1110040	**Collection Date:**	10/5/2011 11:40:00 AM
Project:	Artimus, 260 W. 26th Street, New York, NY	**Matrix:**	SOIL
Lab ID:	1110040-08B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP LEAD			**SW1311/6010C**		**SW1311**		Analyst: **JP**
Lead	0.203	0.005	0.0500		mg/L	1	10/6/2011 1:55:39 PM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *06-Oct-11*

CLIENT: CA Rich Consultants Inc.
Work Order: 1110040
Project: Artimus, 260 W. 26th Street, New York, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DRY_PB

Sample ID: **LCSS-100611A**	SampType: **LCS**	TestCode: **DRY_PB**	Units: **mg/Kg**	Prep Date: **10/6/2011**	RunNo: **60116**
Client ID: **LCSS**	Batch ID: **33446**	TestNo: **SW6010C**	**SW3050B**	Analysis Date: **10/6/2011**	SeqNo: **844125**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Lead	39.9	0.400	40.00	0	99.8	81	119				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

CLIENT: CA Rich Consultants Inc.
Work Order: 1110040
Project: Artimus, 260 W. 26th Street, New York, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: TCLP_PB

Sample ID: **PBW-100511AT** SampType: **MBLK** TestCode: **TCLP_PB** Units: **mg/L** Prep Date: RunNo: **60111**
Client ID: **PBS** Batch ID: **33438** TestNo: **SW1311/6010 SW1311** Analysis Date: **10/6/2011** SeqNo: **844047**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Lead	U	0.0500									

Sample ID: **LCSS-100511AT** SampType: **LCS** TestCode: **TCLP_PB** Units: **mg/L** Prep Date: RunNo: **60111**
Client ID: **LCSS** Batch ID: **33438** TestNo: **SW1311/6010 SW1311** Analysis Date: **10/6/2011** SeqNo: **844048**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Lead	1.90	0.0500	2.000	0	95.2	63	123				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

AMERICAN ANALYTICAL LABORATORIES

NYSDOH 11418
NJDEP NY050
CTDOH PH-0205
PADEP 68-00573

Monday, October 10, 2011

Steve Malinowski
CA Rich Consultants Inc.
17 Dupont Street
Plainview, NY 11803

TEL: (516) 576-8844
FAX (516) 576-0093

RE: 260 West 26th St., NY, NY

Order No.: 1110074

Dear Steve Malinowski:

American Analytical Laboratories, LLC. received 2 sample(s) on 10/7/2011 for the analyses presented in the following report.

Samples were analyzed in accordance with the test procedures documented on the chain of custody and detailed throughout the text of this report.

The results reported herein relate only to the items tested or to the samples as received by the laboratory. This report may not be reproduced, except in full, without the approval of American Analytical Laboratories, LLC and is not considered complete without a cover page and chain of custody documentation. The limits (LOQ) provided in the data package are analytical reporting limits and not Federal or Local mandated values to which the sample results should be compared.

There were no problems with the analyses and all data for associated QC met laboratory specifications. If there are any exceptions a Case Narrative is provided in the report or the data is qualified. This package has been reviewed by American Analytical Laboratories' QA Department/Laboratory Director to comply with NELAC standards prior to report submittal. This report consists of 9 pages.

If you have any questions regarding these tests results, please do not hesitate to call (631) 454-6100 or email me directly at lbeyer@american-analytical.com.

Sincerely,

Lori Beyer
Lab Director

American Analytical Laboratories, LLC.

Date: *10-Oct-11*

CLIENT: CA Rich Consultants Inc.
Project: 260 West 26th St., NY, NY
Lab Order: 1110074

Work Order Sample Summary

Lab Sample ID	Client Sample ID	Date Collected	Date Received
1110074-01A	TP-5 (North) 1	10/7/2011 11:00:00 AM	10/7/2011
1110074-01B	TP-5 (North) 1	10/7/2011 11:00:00 AM	10/7/2011
1110074-02A	TP-7 (East) 1	10/7/2011 11:10:00 AM	10/7/2011
1110074-02B	TP-7 (East) 1	10/7/2011 11:10:00 AM	10/7/2011

AMERICAN ANALYTICAL LABORATORIES
56 TOLEDO STREET • FARMINGDALE, NEW YORK 11735
(631) 454-6100 • FAX (631) 454-8027
www.american-analytical.com

NYSDOH	11418
CTDOH	PH-0205
NJDEP	NY050
PADEP	68-573

CHAIN OF CUSTODY / REQUEST FOR ANALYSIS DOCUMENT

CLIENT NAME/ADDRESS
Carlyle Consultants
17 DuPont St
Plainview NY 11803

CONTACT:
Steve Malinowski
516 576 5844

SAMPLER (SIGNATURE)

SAMPLER NAME (PRINT)
Jessica Prascin

SAMPLE(S) SEALED — YES / NO
CORRECT CONTAINER(S) — YES / NO
TEMPERATURE (° C) 3.1

PROJECT LOCATION: 260 West 26th Street NY, NY

LABORATORY ID# LAB USE ONLY	MATRIX/ TYPE	NO. OF CONTAINERS	SAMPLING DATE	SAMPLING TIME	SAMPLE # - LOCATION	ANALYSIS REQUIRED: Total Lead	TCLP Lead
1110024-01AB	S/C	1	10/7/11	11am	TP-5 (North) 1	X	X
02AB	S/C	1	10/7/11	11:10am	TP-7 (East) 1	X	X

COMMENTS / INSTRUCTIONS: *24hour TAT*

Samples must be on ICE (<6° C)

MATRIX S=SOIL; W=WATER; SL=SLUDGE; A=AIR; M=MISCELLANEOUS
TYPE G=GRAB; C=COMPOSITE

TURNAROUND REQUIRED: STANDARD ☐ (7-10 business days) STAT ☐ BY 24hour* TAT*

E-MAIL ADDRESS FOR RESULTS: Smalinowski@Carlyleinc.com

RELINQUISHED BY (SIGNATURE)	DATE / TIME	PRINTED NAME	RECEIVED BY LAB (SIGNATURE)	DATE / TIME	PRINTED NAME
Steven Malinowski	10/7/11 1605	Steven Malinowski		10/7/11 1605	
	10/7/11 1630		Catherine Ferrara	10/7/11 1630	Catherine Ferrara

WHITE-OFFICE / CANARY-LAB / PINK-SAMPLE CUSTODIAN / GOLDENROD-CLIENT

American Analytical Laboratories, LLC.

Sample Receipt Checklist

Client Name **CA RICH** Date and Time Receive **10/7/2011 4:31:07 PM**

Work Order Numbe **1110074** RcptNo: **1** Received by **CD**

COC_ID: CoolerID:

Checklist completed by Signature C Renaud Date 10/7/11 Reviewed by Initials JA B Date 10/10/11

Matrix: Carrier name AAL

Shipping container/cooler in good condition?	Yes ☑	No ☐	Not Presen ☐
Custody seals intact on shippping container/cooler?	Yes ☐	No ☐	Not Presen ☑
Custody seals intact on sample bottles?	Yes ☐	No ☐	Not Presen ☑
Chain of custody present?	Yes ☑	No ☐	
Chain of custody signed when relinquished and received?	Yes ☑	No ☐	
Chain of custody agrees with sample labels?	Yes ☑	No ☐	
Samples in proper container/bottle?	Yes ☑	No ☐	
Sample containers intact?	Yes ☑	No ☐	
Sufficient sample volume for indicated test?	Yes ☑	No ☐	
All samples received within holding time?	Yes ☑	No ☐	
Container/Temp Blank temperature in compliance?	Yes ☑	No ☐	
Water - VOA vials have zero headspace?	No VOA vials submitted ☑	Yes ☐	No ☐
Water - pH acceptable upon receipt?	Yes ☐	No ☐	N/A ☐

Adjusted? Checked b

Any No and/or NA (not applicable) response must be detailed in the comments section be

Client contacted Date contacted: Person contacted

Contacted by: Regarding:

Comments:

Corrective Action

American Analytical Laboratories, LLC.

Date: *10-Oct-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-5 (North) 1
Lab Order:	1110074	**Collection Date:**	10/7/2011 11:00:00 AM
Project:	260 West 26th St., NY, NY	**Matrix:**	SOIL
Lab ID:	1110074-01A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PERCENT MOISTURE			**D2216**				Analyst: **CF**
Percent Moisture	9.93	0	0		wt%	1	10/10/2011
LEAD,TOTAL			**SW6010C**		**SW3050B**		Analyst: **AB**
Lead	4.03	0.22	0.435		mg/Kg-dry	1	10/10/2011 11:28:12 AM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *10-Oct-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-5 (North) 1
Lab Order:	1110074	**Collection Date:**	10/7/2011 11:00:00 AM
Project:	260 West 26th St., NY, NY	**Matrix:**	SOIL
Lab ID:	1110074-01B		

Certificate of Results

Analyses	Sample Result	Qual	LOD	LOQ	Units	DF	Date/Time Analyzed
TCLP LEAD				**SW1311/6010C** **SW1311**			Analyst: **AB**
Lead	U		0.005	0.0500	mg/L	1	10/10/2011 11:13:56 AM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *10-Oct-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-7 (East) 1
Lab Order:	1110074	**Collection Date:**	10/7/2011 11:10:00 AM
Project:	260 West 26th St., NY, NY	**Matrix:**	SOIL
Lab ID:	1110074-02A		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
PERCENT MOISTURE			**D2216**				Analyst: **CF**
Percent Moisture	6.10	0	0		wt%	1	10/10/2011
LEAD,TOTAL			**SW6010C**		**SW3050B**		Analyst: **AB**
Lead	6.66	0.21	0.424		mg/Kg-dry	1	10/10/2011 11:30:24 AM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

ACCREDITED IN ACCORDANCE WITH nelac

Qualifiers:	B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
	E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
	J	Analyte detected below quantitation limits	LOD	Limit of Detection
	LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
	PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
	U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *10-Oct-11*

ELAP ID : 11418

CLIENT:	CA Rich Consultants Inc.	**Client Sample ID:**	TP-7 (East) 1
Lab Order:	1110074	**Collection Date:**	10/7/2011 11:10:00 AM
Project:	260 West 26th St., NY, NY	**Matrix:**	SOIL
Lab ID:	1110074-02B		

Certificate of Results

Analyses	Sample Result	LOD	LOQ	Qual	Units	DF	Date/Time Analyzed
TCLP LEAD			**SW1311/6010C**		**SW1311**		Analyst: **AB**
Lead	0.0140	0.005	0.0500	J	mg/L	1	10/10/2011 11:16:08 AM

American Analytical Laboratories, LLC., 56 Toledo Street, Farmingdale, NY, Zip - 11735
Tel - 6314546100 Fax - 6314548027 www.American-Analytical.com

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes
E	Value above quantitation range	H	Holding times for preparation or analysis exceeded
J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC columns
PQL	Practical Quantitation Limit	S	Spike Recovery outside accepted recovery limits
U	Indicates the compound was analyzed but not detected.		

American Analytical Laboratories, LLC.

Date: *10-Oct-11*

CLIENT: CA Rich Consultants Inc.
Work Order: 1110074
Project: 260 West 26th St., NY, NY

ANALYTICAL QC SUMMARY REPORT

TestCode: DRY_PB

Sample ID: **PBS-101011A**	SampType: **MBLK**	TestCode: **DRY_PB**	Units: **mg/Kg**	Prep Date: **10/10/2011**	RunNo: **60150**
Client ID: **PBS**	Batch ID: **33472**	TestNo: **SW6010C**	**SW3050B**	Analysis Date: **10/10/2011**	SeqNo: **844679**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Lead	U	0.400									

Sample ID: **LCSS-101011A**	SampType: **LCS**	TestCode: **DRY_PB**	Units: **mg/Kg**	Prep Date: **10/10/2011**	RunNo: **60150**
Client ID: **LCSS**	Batch ID: **33472**	TestNo: **SW6010C**	**SW3050B**	Analysis Date: **10/10/2011**	SeqNo: **844680**

Analyte	Result	PQL	SPK value	SPK Ref Val	%REC	LowLimit	HighLimit	RPD Ref Val	%RPD	RPDLimit	Qual
Lead	41.8	0.400	40.00	0	104	81	119				

Qualifiers:

B	Analyte detected in the associated Method Blank	C	Calibration %RSD/%D exceeded for non-CCC analytes	E	Value above quantitation range
H	Holding times for preparation or analysis exceeded	J	Analyte detected below quantitation limits	LOD	Limit of Detection
LOQ	Limit of Quantitation	P	>40% diff for detected conc between the two GC column	PQL	Practical Quantitation Limit

APPENDIX K

Disposal Manifests for Non-Hazardous Waste Disposal Activities
(electronic copies only)

Aggregate Receipt Log
Bellmawr Waterfront Development, L.L.C.
Harding Avenue
Bellmawr, New Jersey
October 19, 2011

TASK # 9000-1327

DATE	SENDING SITE LOCATION	TRUCKING COMPANY	TRUCK #	LOADS	TONS	PLATE	MATERIAL
10/19/11	Soil Safe/Chelsea Green	AMG Industries	AMG1	1	36.94	142896	INRS
10/19/11	Soil Safe/Chelsea Green	AMG Industries	AMG9	1	28.92	142908	INRS
10/19/11	Soil Safe/Chelsea Green	DI Trucking	DID1	1	30.61	142883	INRS
10/19/11	Soil Safe/Chelsea Green	DI Trucking	DI02	1	28.18	142884	INRS
10/19/11	Soil Safe/Chelsea Green	Shirley	SH02	1	30.36	142892	INRS
10/19/11	Soil Safe/Chelsea Green	Shirley	SH06	1	32.70	142891	INRS
10/19/11	Soil Safe/Chelsea Green	Shirley	SH20	1	29.93	142888	INRS
			TOTAL:	7	217.64	7	

ACCEPTED FILL

BELLMAWR waterfront

An Equal Opportunity Employer

BELLMAWR WATERFRONT DEVELOPMENT, LLC

INBOUND CONTAMINATED SOILS

P.O. Box 336
Bellmawr, NJ 18099

Phone: (856) 931-6050
Fax: (856) 931-6287
www.bellmawrwaterfront.com

Control No. 142908

PURCHASE ORDER NO.		DATE		TICKET NO.	142908
CUSTOMER		PROJECT NUMBER	NAME		
		MATERIAL CODE	TYPE		
GROSS	TIME	TRUCK NO.		UNIT PRICE	
TARE	QUANTITY ORDERED	CHARGE DEL		NET PRICE	
NET	QUANTITY DELIVERED			HAUL CHARGES	
UNITS/TONS	QUANTITY RECEIVED				
QTY. DEL. RCV. TODAY	QUANTITY REMAINING			RA SALES TAX	
LOAD NO.	I hereby acknowledge that the load is loaded to the specified quantity and is correct and in accordance with SELLER WILL NOT BE RESPONSIBLE FOR ANY DAMAGE CAUSED BY THE SELLER'S TRUCKS AFTER LEAVING STREET PAVEMENT.			GRAND TOTAL	
	SIGNATURE	COMMENTS			

WEIGHMASTER

X

DRIVER

NOTICE: SEE REVERSE SIDE FOR TERMS OF PURCHASE AGREEMENT.

SIGN & RETURN

TP-4 (0-2)
TP-6 (0-8)

SOIL SAFE, INC.

Log Number 007

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Carlson Corp
Address 260 West St
New York, NY

Generator Site/Location Same
Address 19402

Phone No.

Phone No.

Approval Number

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Gregory Tomaino 10/19/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries
Address Hyde, MS

Driver Name (Print) Charles Crosby

Vehicle License No. / State / EPA No.

Truck Number

I hereby certify that the above named material was picked up at the generator site listed above.

10/19/11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/19/11

Driver Signature | Delivery Date

DESTINATION

Site Name Soil Safe, Inc. - Bridgeport Phone No. 1-856-467-8030

Address 378 Route 130 Logan Township, NJ 08085 Bridgeport Bellmawr

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

10/19/11

Name of Authorized Agent | Signature | Receipt Date

White - Facility | Green - Facility | Yellow - Generator | Pink - Broker | Goldenrod - Contractor | Blue - Trucking Co.

ACCEPTED FILL

BELLMAWR waterfront

An Equal Opportunity Employer

BELLMAWR WATERFRONT DEVELOPMENT, LLC

INBOUND CONTAMINATED SOILS

P.O. Box 336
Bellmawr, NJ 18099

Phone: (856) 931-6050
Fax: (856) 931-6287
www.bellmawrwaterfront.com

Control No. 142896

PURCHASE ORDER NO.			DATE			TICKET NO.	
CUSTOMER			PROJECT NUMBER		NAME		
			MATERIAL CODE				
GROSS		TIME		TRUCK NO.		UNIT PRICE	
TARE		QUANTITY ORDERED		CHARGE DEL.		NET PRICE	
NET		QUANTITY DELIVERED				HAUL CHARGE	
UNITS/TONS		QUANTITY RECEIVED					
QTY. DEL./RECV. TODAY		QUANTITY REMAINING				P/SALES TAX	
LOAD NO.						GRAND TOTAL	

SELLER WILL NOT BE RESPONSIBLE FOR ANY DAMAGE CAUSED BY THE SELLER'S TRUCK AFTER LEAVING STREET PAVEMENT

SIGNATURE

X

WEIGHMASTER

DRIVER

COMMENTS

NOTICE: SEE REVERSE SIDE FOR TERMS OF PURCHASE AGREEMENT.

SIGN & RETURN

Log Number 006

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green — Generator Site/Location SAME

Address 240 West St — Address

Newark, NJ — 19382

Phone No. — Phone No.

Approval Number 1901-121

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Generator Authorized Agent Name — Signature — Shipment Date 10/6/11

TRANSPORTER

Transporter Name AMS Trucking — Driver Name (Print) Alex Roebuck

Address Hillside NJ — Vehicle License No. / State / EPA No. C72524

Truck Number 1

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date 10/6/11

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** — Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085** 284 Harding Hwy Carneys Point, NJ

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — Receipt Date 10/6/11

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

ACCEPTED FILL

BELLMAW waterfront

An Equal Opportunity Employer

BELLMAWR WATERFRONT DEVELOPMENT, LLC

INBOUND CONTAMINATED SOILS

P.O. Box 336
Bellmawr, NJ 18099

Phone: (856) 931-6050
Fax: (856) 931-6287
www.bellmawrwaterfront.com

Control No. 1412868

PURCHASE ORDER NO.

DATE

TICKET NO.

CUSTOMER

PROJECT NUMBER

NAME

MATERIAL CODE

TYPE

GROSS

TIME

TRUCK NO.

UNIT PRICE

TARE

QUANTITY ORDERED

CHARGE DEL

NET PRICE

NET

QUANTITY DELIVERED

HAUL CHARGE

UNIT STONE

QUANTITY RECEIVED

QTY. DEL. RECV. TODAY

QUANTITY REMAINING

PA SALES TAX

DEAL NO.

SELLER WILL NOT BE RESPONSIBLE FOR ANY DAMAGE CAUSED BY THE SELLER'S TRUCKS AFTER LEAVING STREET PAVEMENT.

GRAND TOTAL

SIGNATURE

COMMENTS

X

WEIGHMASTER

DRIVER

NOTICE! SEE REVERSE SIDE FOR TERMS OF PURCHASE AGREEMENT

SIGN & RETURN

TF-1603
TP-6603

Log Number 003

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Grea
Address 261 Lake St
Newark NJ
Phone No.

Generator Site/Location Sharp Rd
Address
Phone No.

Approval Number 10m-1bm

Description of Material
Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name AMG Industries
Address Hillside, NJ

Driver Name (Print) Paul
Vehicle License No. / State / EPA No. 2 Tone Co
Truck Number

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature Shipment Date 10-19-11

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature Delivery Date 10-19-11

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085** 201 Harding Ave Bellmawr NJ

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent Signature Receipt Date 10/19/11

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co

ACCEPTED FILL

BELLMAWR waterfront

An Equal Opportunity Employer

BELLMAWR WATERFRONT DEVELOPMENT, LLC

INBOUND CONTAMINATED SOILS

P.O. Box 336
Bellmawr, NJ 18099

Phone: (856) 931-6050
Fax: (856) 931-6287
www.bellmawrwaterfront.com

Control No. 142094

PURCHASE ORDER NO.			DATE			TICKET NO.	
CUSTOMER			PROJECT NUMBER	NAME			
			MATERIAL CODE	TYPE			
GROSS		TIME	TRUCK NO.			UNIT PRICE	
TARE		QUANTITY ORDERED	CHARGE DEL			NET PRICE	
NET		QUANTITY DELIVERED				HAUL CHARGES	
UNITS/TONS		QUANTITY RECEIVED					
QTY. DELIVERED TODAY		QUANTITY REMAINING				SALES TAX	
LOAD NO.						GRAND TOTAL	

I certify that the contents of this truckload meet the specifications and regulations as set forth by the purchaser. SELLER WILL NOT BE RESPONSIBLE FOR ANY DAMAGE CAUSED BY THE SELLER'S TRUCKS AFTER LEAVING STREET PAVEMENT.

SIGNATURE

X

WEIGHMASTER

DRIVER

COMMENTS

NOTICE: SEE REVERSE SIDE FOR TERMS OF PURCHASE AGREEMENT

SIGN & RETURN

Log Number 201

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 26th St

New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Description of Material

Approval Number 100-134

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print)

Vehicle License No. / State / EPA No.

Truck Number

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature Delivery Date

DESTINATION

Site Name Soil Safe, Inc. - Bridgeport Phone No. 1-856-467-8030

Address 378 Route 130 Logan Township, NJ 08085

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

ACCEPTED FILL

BELLMAWR waterfront

An Equal Opportunity Employer

BELLMAWR WATERFRONT DEVELOPMENT, LLC

INBOUND CONTAMINATED SOILS

P.O. Box 336
Bellmawr, NJ 18099

Phone: (856) 931-6050
Fax: (856) 931-6287
www.bellmawrwaterfront.com

Control No. 142083

PURCHASE ORDER NO.			DATE			TICKET NO	
CUSTOMER			PROJECT NUMBER	NAME			
			MATERIAL CODE	TYPE			
GROSS		TIME		TRUCK NO		UNIT PRICE	
TARE		QUANTITY ORDERED		CHARGE TO		NET PRICE	
NET		QUANTITY DELIVERED				HAUL CHARGES	
UNITS/TONS		QUANTITY RECEIVED					
QTY. DEL. / REC'V TODAY		QUANTITY REMAINING				PA SALES TAX	
LOAD NO		This is to certify that the material listed is as specified in accordance with the agreement. SELLER WILL NOT BE RESPONSIBLE FOR ANY DAMAGE CAUSED BY THE SELLER'S TRUCKS AFTER LEAVING STREET PAVEMENT.				GRAND TOTAL	

SIGNATURE

X

WEIGHMASTER

DRIVER

COMMENTS

NOTICE: SEE REVERSE SIDE FOR TERMS OF PURCHASE AGREEMENT

SIGN & RETURN

TP-4 (0-2)
TP-6 (0-8)

Log Number 002

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

14283

GENERATOR

Generator Name Welsh Cities
Address 261 Warren St
Newark NJ
Phone No.

Generator Site/Location SAME
Address
Phone No.

Approval Number 1058-D2

Description of Material
Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As Authorized Agent | Signature | 10/19/11
Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name Alex Towing
Address 1 Route 25
Driver Name (Print) Alex Lowe
Vehicle License No. / State / EPA No. AM6378
Truck Number 702

I hereby certify that the above named material was picked up at the generator site listed above.

Alex Lowe 10-19-11
Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Alex Lowe
Driver Signature | Delivery Date

DESTINATION

Site Name Soil Safe, Inc. - Bridgeport
Phone No. 1-856-467-8030
Address 378 Route 130 Logan Township, NJ 08085 284 Rahway Ave Elizabeth, NJ
No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

[signature] 10-19-11
Name of Authorized Agent | Signature | Receipt Date

White - Facility | Green - Facility | Yellow - Generator | Pink - Broker | Goldenrod - Contractor | Blue - Trucking Co.

JP-6(03)
JP-4(07)

SOIL SAFE, INC.

Log Number 004

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Brun

Generator Site/Location SAME

Address 20 Wilson St

Address

New York, NY

11282

Phone No.

Phone No.

Approval Number

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Agent to sign 10/19/11

Generator Authorized Agent Name / Signature Shipment Date

TRANSPORTER

Transporter Name AMG Trucking

Driver Name (Print)

Address Hillside, NJ

Vehicle License No. / State / EPA No.

Truck Number 22

I hereby certify that the above named material was picked up at the generator site listed above.

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature Shipment Date

Driver Signature Delivery Date

DESTINATION

Site Name Bellmawr **Soil Safe, Inc. - Bridgeport**

Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085** 309 Harrison Ave Bellmawr, NJ

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

RK 10/19/11

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 005

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Delivery Green

Address 160 Old Rt 17 New York NY

Phone No.

Generator Site/Location R-4 (03) Rt 603 Edison

Address 10/2871

Phone No.

Approval Number 1001-3

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name AMG Trucking

Address Hillside NJ

Driver Name (Print) Carlos

Vehicle License No. / State / EPA No. AM NOT

Truck Number Shirley 2 OC

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature 10-19-4 Delivery Date

DESTINATION

Site Name Bellmawr Soil Safe, Inc. - Bridgeport Phone No. 1-856-467-8030

Address 378 Route 130 Logan Township, NJ 08085 Rt 130 Hartford Bellmawr NJ

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent Signature 10/19/4 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Aggregate Receipt Log
Bellmawr Waterfront Development, L.L.C.
Harding Avenue
Bellmawr, New Jersey
October 20, 2011

TASK # 9000-1327

DATE	SENDING SITE LOCATION	TRUCKING COMPANY	TRUCK #	LOADS	TONS	PLATE	MATERIAL
10/20/11	Soil Safe/Chelsea Green	Shirley	SH02	1	29.15	142914	INRS
10/20/11	Soil Safe/Chelsea Green	Shirley	SH06	1	33.13	142942	INRS
10/20/11	Soil Safe/Chelsea Green	Shirley	SH20	1	32.99	142915	INRS
			TOTAL:	**1**	**29.15**	**1**	

ACCEPTED FILL

BELLMAWR waterfront

An Equal Opportunity Employer

BELLMAWR WATERFRONT DEVELOPMENT, LLC

INBOUND CONTAMINATED SOILS

P.O. Box 336
Bellmawr, NJ 18099

Phone: (856) 931-6050
Fax: (856) 931-6287
www.bellmawrwaterfront.com

Control No. 142942

PURCHASE ORDER NO.				DATE		TICKET NO.	
CUSTOMER				PROJECT NUMBER		NAME	
				MATERIAL CODE		TYPE	
GROSS		TIME		TRUCK NO.		UNIT PRICE	
TARE		QUANTITY ORDERED		CHARGE DEL		NET PRICE	
NET		QUANTITY DELIVERED				HAUL CHARGES	
UNITS/TONS		QUANTITY RECEIVED					
QTY. DEL./RECV. TODAY		QUANTITY REMAINING				PA SALES TAX	
LOAD NO.		The signature below certifies that this material meets the applicable contract specifications and requirements. SELLER WILL NOT BE RESPONSIBLE FOR ANY DAMAGE CAUSED BY THE SELLER'S TRUCKS AFTER LEAVING STREET PAVEMENT.				GRAND TOTAL	
		SIGNATURE			COMMENTS		

X

WEIGHMASTER DRIVER

SIGN & RETURN

TP-4009 & 2
TP-6089

SOIL SAFE, INC.

Log Number 009

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 210 Middle St

New York, NY

Phone No.

Generator Site/Location Same

Address

Phone No. 1402-10

Approval Number

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Al Agar to email | 10/19/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name Ang Trucking

Address Hillside NJ

Driver Name (Print) Carlos

Vehicle License No. / State / EPA No. Agnuo T

Truck Number Shirley 2 06

I hereby certify that the above named material was picked up at the generator site listed above.

10-19-11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-19-11

Driver Signature | Delivery Date

DESTINATION

Site Name Bellmawr **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085** 201 Harding Ave Bellmawr, NJ

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent | Signature | Receipt Date 10/20/11

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

ACCEPTED FILL

BELLMAWR waterfront

An Equal Opportunity Employer

BELLMAWR WATERFRONT DEVELOPMENT, LLC

INBOUND CONTAMINATED SOILS

P.O. Box 336
Bellmawr, NJ 18099

Phone: (856) 931-6050
Fax: (856) 931-6287
www.bellmawrwaterfront.com

Control No. 142914

PURCHASE ORDER NO				DATE		TICKET NO.	
CUSTOMER				PROJECT NUMBER	NAME		
				MATERIAL CODE	TYPE		
GROSS		TIME		TRUCK NO		UNIT PRICE	
TARE		QUANTITY ORDERED		CHARGE DEL		NET PRICE	
NET		QUANTITY DELIVERED				HAUL CHARGES	
UNITS/TONS		QUANTITY RECEIVED					
QTY. DEL./RECV. TODAY		QUANTITY REMAINING				PA SALES TAX	
LOAD NO		The signature below certifies that this material meets the applicable contract specifications and requirements. SELLER WILL NOT BE RESPONSIBLE FOR ANY DAMAGE CAUSED BY THE SELLER'S TRUCKS AFTER LEAVING STREET PAVEMENT.				GRAND TOTAL	
		SIGNATURE					

X

WEIGHMASTER DRIVER

COMMENTS

SIGN & RETURN

TP-4107 [illegible]
TP-6082

Log Number 010

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 140 Main St

New York NY

Phone No.

Generator Site/Location Same

Address

11/29/14

Phone No.

Approval Number [illegible]

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent for owner [signature] 10/10/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Trucking

Address Hills NJ

Driver Name (Print) [illegible]

Vehicle License No. / State / EPA No. [illegible]

Truck Number [illegible]

I hereby certify that the above named material was picked up at the generator site listed above.

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature | Shipment Date

Driver Signature | Delivery Date

DESTINATION

Site Name Soil Safe, Inc. - Bridgeport

Phone No. 1-856-467-8030

Address 378 Route 130 Logan Township, NJ 08085 207 Harding Hy Gibbstown NJ

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

[signature] 10 20 11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

ACCEPTED FILL

BELLMAWR WATERFRONT DEVELOPMENT, LLC

Phone: (856) 931-6050
Fax: (856) 931-6287
www.bellmawrwaterfront.com

BELLMAWR waterfront

An Equal Opportunity Employer

INBOUND CONTAMINATED SOILS

P.O. Box 336
Bellmawr, NJ 18099

Control No. 142915

PURCHASE ORDER NO.				DATE		TICKET NO.	
CUSTOMER				PROJECT NUMBER		NAME	
				MATERIAL CODE		TYPE	
GROSS		TIME		TRUCK NO.		UNIT PRICE	
TARE		QUANTITY ORDERED		CHARGE DEL		NET PRICE	
NET		QUANTITY DELIVERED				HAUL CHARGES	
UNITS/TONS		QUANTITY RECEIVED					
QTY. DEL./RECV. TODAY		QUANTITY REMAINING				PA SALES TAX	
LOAD NO.						GRAND TOTAL	

The undersigned certifies that this material does not contain any hazardous substances and complies with all applicable statutes, regulations and requirements.
SELLER WILL NOT BE RESPONSIBLE FOR ANY DAMAGE CAUSED BY THE SELLER'S TRUCKS AFTER LEAVING STREET PAVEMENT.

SIGNATURE

X

WEIGHMASTER

DRIVER

COMMENTS

SIGN & RETURN

SEE REVERSE SIDE FOR TERMS OF PURCHASE AGREEMENT

TP-402 & TP-603

Log Number 002

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 240 West St

New York NY

Phone No.

Generator Site/Location SAME

Address

10285

Description of Material

Approval Number 100-122

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AC Environmental — 10/19/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name RMS Trucking

Address 44 Rt 10

Driver Name (Print) Paul

Vehicle License No. / State / EPA No. AW3904

Truck Number Schaefer 2

I hereby certify that the above named material was picked up at the generator site listed above.

10-19-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-19-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085** 204 Harding Ave Bellmawr NJ

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

10/20/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

ACCEPTED FILL

BELLMAWR waterfront DEVELOPMENT

An Equal Opportunity Employer

BELLMAWR WATERFRONT DEVELOPMENT, LLC

INBOUND CONTAMINATED SOILS

P.O. Box 336
Bellmawr, NJ 18099

Phone: (856) 931-6050
Fax: (856) 931-6287
www.bellmawrwaterfront.com

Control No. 142891

PURCHASE ORDER NO.		DATE	10/19/11 I	TICKET NO.	142891

CUSTOMER: SOIL SAFE INC. BS0400
6700 ALEXANDER BELL BLVD.
COLUMBIA MD 21046
(410)-872-3990

PROJECT — NUMBER: 9-1327 NAME: CHELSEA GREEN

MATERIAL — CODE: INRS TYPE: INBOUND NON-RES SOIL

GROSS	95,020 lb	TIME	12:01	TRUCK NO.	OWN/SH06	UNIT PRICE	
TARE	29,620 lb	QUANTITY ORDERED		CHARGE DEL.		NET PRICE	
NET	65,400 lb	QUANTITY DELIVERED	.00	Zone:		HAUL CHARGES	
UNITS/TONS	32.70 TN	QUANTITY RECEIVED	121.42			Util Tax:	.00
QTY. DEL./RECV. TODAY	121.42- TN	QUANTITY REMAINING		U.O.M.:	TN	PA SALES TAX	NJ
LOAD NO.	4	The signature below certifies that this material meets the applicable contract, specifications and requirements. SELLER WILL NOT BE RESPONSIBLE FOR ANY DAMAGE CAUSED BY THE SELLER'S TRUCKS AFTER LEAVING STREET PAVEMENT.			AM110T	GRAND TOTAL	
M.G.W.	80,000						

KM29993

SIGNATURE

WEIGHMASTER X DRIVER

NOTICE: SEE REVERSE SIDE FOR TERMS OF PURCHASE AGREEMENT.

COMMENTS

CUSTOMER COPY

ACCEPTED FILL

BELLMAWR WATERFRONT DEVELOPMENT, LLC

INBOUND CONTAMINATED SOILS

P.O. Box 336
Bellmawr, NJ 18099

Phone: (856) 931-6050
Fax: (856) 931-6287
www.bellmawrwaterfront.com

BELLMAWR waterfront redevelopment

An Equal Opportunity Employer

Control No. 142892

PURCHASE ORDER NO.		DATE	10/19/11 I	TICKET NO.	142892

CUSTOMER: SOIL SAFE INC. BS0400
6700 ALEXANDER BELL BLVD.
COLUMBIA MD 21046
(410)-872-3990

PROJECT — NUMBER: 9-1327 NAME: CHELSEA GREEN

MATERIAL — CODE: INRS TYPE: INBOUND NON-RES SOIL

GROSS	89,040 lb	TIME	12:02	TRUCK NO.	OWN/SH02	UNIT PRICE	
TARE	28,320 lb	QUANTITY ORDERED		CHARGE DEL.		NET PRICE	
NET	60,720 lb	QUANTITY DELIVERED	.00	Zone:		HAUL CHARGES	
UNITS/TONS	30.36 TN	QUANTITY RECEIVED	151.78			Tax:	.00
QTY. DEL./RECV. TODAY	151.78- TN	QUANTITY REMAINING		U.O.M.:	TN	PA SALES TAX	NJ
LOAD NO.	5	The signature below certifies that this material meets the applicable contract, specifications and requirements. SELLER WILL NOT BE RESPONSIBLE FOR ANY DAMAGE CAUSED BY THE SELLER'S TRUCKS AFTER LEAVING STREET PAVEMENT.			- Lic # - AM111T	GRAND TOTAL	
M.G.W.	80,000						

KM29993

SIGNATURE

X

WEIGHMASTER — DRIVER

NOTICE: SEE REVERSE SIDE FOR TERMS OF PURCHASE AGREEMENT.

COMMENTS

(1)

CUSTOMER COPY

Aggregate Receipt Log
Bellmawr Waterfront Development, L.L.C.
Harding Avenue
Bellmawr, New Jersey
October 24, 2011

TASK # 9000-1327

DATE	SENDING SITE LOCATION	TRUCKING COMPANY	TRUCK #	LOADS	TONS	PLATE	MATERIAL
10/24/11	Soil Safe/Chelsea Green	Carsillo	CT14	1	33.13	142990	INRS
10/24/11	Soil Safe/Chelsea Green	Carsillo	Ct16	1	35.04	142986	INRS
10/24/11	Soil Safe/Chelsea Green	Carsillo	CT17	1	35.56	143007	INRS
10/24/11	Soil Safe/Chelsea Green	Salazaar	SA10	1	29.10	142993	INRS
10/24/11	Soil Safe/Chelsea Green	Salazaar	SA11	2	64.33	142989	INRS
10/24/11	Soil Safe/Chelsea Green	Salazaar	ST53	1	30.92	142992	INRS
			TOTAL:	7	228.08	6	

ACCEPTED FILL

BELLMAWR WATERFRONT DEVELOPMENT, LLC

INBOUND CONTAMINATED SOILS

P.O. Box 336
Bellmawr, NJ 18099

Phone: (856) 931-6050
Fax: (856) 931-6287
www.bellmawrwaterfront.com

BELLMAWR waterfront

An Equal Opportunity Employer

Control No. 143036

PURCHASE ORDER NO			DATE			TICKET NO	143036
CUSTOMER	SOIL SAFE, INC. 6700 ALEXANDER BELL DR. #110 OLLANSEA, NJ 08248 (443)982-5000		PROJECT NUMBER	NAME	9-11-23 CHI-CHA GREEN		
			MATERIAL CODE	TYPE	INBOUND NON-REG FILL		
GROSS	80,240 LB	TIME		TRUCK NO		UNIT PRICE	
TARE	26,540 LB	QUANTITY ORDERED		CHARGE DEL		NET PRICE	
NET	53,700 LB	QUANTITY DELIVERED				HAUL CHARGES	0.0
UNITS/TONS	26.85 TN	QUANTITY RECEIVED					
QTY DEL/RECV TODAY	26.85 TN	QUANTITY REMAINING				PA SALES TAX	0.0
LOAD NO		The signature below verifies that this material meets the applicable contract specifications and that the SELLER WILL NOT BE RESPONSIBLE FOR ANY DAMAGE CAUSED BY THE SELLER'S TRUCKS AFTER LEAVING STREET PAVEMENT				GRAND TOTAL	
TIME	8:04 AM	SIGNATURE		COMMENTS			

KMD 9-11-23

WEIGHMASTER — DRIVER

SIGN & RETURN

TP-8

SOIL SAFE, INC.

Log Number

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name _____ Generator Site/Location _____

Address _____ Address _____

_____ _____

Phone No. _____ Phone No. _____

Approval Number

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Generator Authorized Agent Name _____ Signature _____ Shipment Date _____

TRANSPORTER

Transporter Name _____ Driver Name (Print) _____

Address _____ Vehicle License No. / State / EPA No. _____

_____ Truck Number _____

I hereby certify that the above named material was picked up at the generator site listed above.

I hereby certify that the above named material was delivered without incident to the destination listed below.

_____ _____

Driver Signature Shipment Date Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

_____ _____ _____

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

ACCEPTED FILL

BELLMAWR WATERFRONT DEVELOPMENT, LLC

BELLMAWR waterfront

An Equal Opportunity Employer

INBOUND CONTAMINATED SOILS
P.O. Box 336
Bellmawr, NJ 18099

Phone: (856) 931-6050
Fax: (856) 931-6287
www.bellmawrwaterfront.com

Control No. 143007

PURCHASE ORDER NO.			DATE			TICKET NO.	143007
CUSTOMER		PROJECT NUMBER		NAME			
		MATERIAL CODE		TYPE			
GROSS		TIME		TRUCK NO.		UNIT PRICE	
TARE		QUANTITY ORDERED		CHARGE DEL		NET PRICE	
NET		QUANTITY DELIVERED				HAUL CHARGES	
UNITS/TONS		QUANTITY RECEIVED					
QTY DEL / RECV TODAY		QUANTITY REMAINING				PA SALES TAX	
LOAD NO.		The signature below certifies that this material meets the applicable contract specifications and was within the SELLER WILL NOT BE RESPONSIBLE FOR ANY DAMAGE CAUSED BY THE SELLER'S TRUCKS AFTER LEAVING STREET PAVEMENT				GRAND TOTAL	
TRUCK NO.		SIGNATURE			COMMENTS		

WEIGHMASTER DRIVER

NOTICE: SEE REVERSE SIDE FOR TERMS OF PURCHASE AGREEMENT

SIGN & RETURN

TP-8

SOIL SAFE, INC.

Log Number 0514

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Grow

Address 266 Wash St

Phone No.

Generator Site/Location

Address Same

Phone No. 14 3007

Approval Number 9112-13371

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Generator Authorized Agent Name Signature Shipment Date 10/24/11

TRANSPORTER

Transporter Name Carville & Son

Address 11 Fornelli Ave

East Hanover NJ

Driver Name (Print) Ed Chamberlain

Vehicle License No. / State / EPA No. AM572 NJ 05

Truck Number 10.17

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature 10-24-11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature 10-24-11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent Signature 10/24/11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

ACCEPTED FILL

BELLMAWR WATERFRONT DEVELOPMENT, LLC

BELLMAWR waterfront

An Equal Opportunity Employer

INBOUND CONTAMINATED SOILS

P.O. Box 336
Bellmawr, NJ 18099

Phone: (856) 931-6050
Fax: (856) 931-6287
www.bellmawrwaterfront.com

Control No. 142395

PURCHASE ORDER NO.			DATE			TICKET NO.	142395
CUSTOMER			PROJECT NUMBER	NAME			
			MATERIAL CODE	TYPE			
GROSS		TIME		TRUCK NO.		UNIT PRICE	
TARE		QUANTITY ORDERED		CHARGE DEL		NET PRICE	
NET		QUANTITY DELIVERED				HAUL CHARGES	
UNITS/TONS		QUANTITY RECEIVED					
QTY DEL/RECV TODAY		QUANTITY REMAINING				PA SALES TAX	
LOAD NO.		SELLER WILL NOT BE RESPONSIBLE FOR ANY DAMAGE CAUSED BY THE SELLER'S TRUCKS AFTER LEAVING STREET PAVEMENT				GRAND TOTAL	

SIGNATURE

WEIGHMASTER

DRIVER

COMPLETED

NOTICE: SEE REVERSE SIDE FOR TERMS OF PURCHASE AGREEMENT

SIGN & RETURN

TP-8

SOIL SAFE, INC.

Log Number 0751a

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Sanq

Address Sanq

Phone No.

Generator Site/Location Chelsea Group

Address 240 W. 26th Street

New York, NY

Phone No. 1000016

Approval Number 27-80 1327

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent Towards 10/24/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name PA Castillo

Address Lacuna NJ

Driver Name (Print) Orlando Jimenez

Vehicle License No. / State / EPA No. [illegible]

Truck Number 16-596

I hereby certify that the above named material was picked up at the generator site listed above.

[signature] 10-24-11

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

[signature] 10-24-11

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

[signature] 10-24-11

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

ACCEPTED FILL

BELLMAWR waterfront

An Equal Opportunity Employer

BELLMAWR WATERFRONT DEVELOPMENT, LLC

INBOUND CONTAMINATED SOILS

P.O. Box 336
Bellmawr, NJ 18099

Phone: (856) 931-6050
Fax: (856) 931-6287
www.bellmawrwaterfront.com

Control No. 442093

PURCHASE ORDER NO.			DATE			TICKET NO.	16393
CUSTOMER	SOIL SAFE INC. 6700 ALEXANDRIA BELL BLVD COLUMBIA (410) 381-5550		PROJECT - MATERIAL	NUMBER	NAME		
				CODE	TYPE	INBOUND NON REG SOIL	
GROSS	44,000 LB	TIME		TRUCK NO.		UNIT PRICE	
TARE	30,240 LB	QUANTITY ORDERED		CHARGE TO		NET PRICE	
NET	13,760 LB	QUANTITY DELIVERED				HAUL CHARGES	.00
UNITS/TONS	6.88 TN	QUANTITY RECEIVED					
QTY. DEL/RECV TODAY	6.88 TONS	QUANTITY REMAINING				TAX	
LOAD NO.		The signature below certifies that the material meets the specifications and requirements. SELLER WILL NOT BE RESPONSIBLE FOR ANY DAMAGE CAUSED BY THE SELLER'S TRUCKS AFTER LEAVING STREET PAVEMENT.				GRAND TOTAL	
11:00	8/6/2018	SIGNATURE					
WEIGHMASTER		X DRIVER		COMMENTS		SIGN & RETURN	

TP-8

SOIL SAFE, INC.

Log Number 07511

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name _____ Generator Site/Location _____

Address _____ Address _____

_____ _____

Phone No. _____ Phone No. _____

Approval Number _____

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

_____ _____ _____

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name _____ Driver Name (Print) _____

Address _____ Vehicle License No. / State / EPA No. _____

_____ Truck Number _____

I hereby certify that the above named material was picked up at the generator site listed above.

_____ _____

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

_____ _____

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

_____ _____ _____

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

ACCEPTED FILL

BELLMAWR WATERFRONT DEVELOPMENT, LLC

INBOUND CONTAMINATED SOILS

P.O. Box 336
Bellmawr, NJ 18099

Phone: (856) 931-6050
Fax: (856) 931-6287
www.bellmawrwaterfront.com

BELLMAWR waterfront

An Equal Opportunity Employer

Control No. 142992

PURCHASE ORDER NO.			DATE			TICKET NO.	
CUSTOMER			PROJECT NUMBER	NAME			
			MATERIAL CODE	TYPE			
GROSS		TIME		TRUCK NO.		UNIT PRICE	
TARE		QUANTITY ORDERED		CHARGE DEL		NET PRICE	
NET		QUANTITY DELIVERED				HAUL CHARGES	.00
UNITS/TONS		QUANTITY RECEIVED					
QTY. DEL./RECV. TODAY		QUANTITY REMAINING				PA SALES TAX	NJ
LOAD NO.		SELLER WILL NOT BE RESPONSIBLE FOR ANY DAMAGE CAUSED BY THE SELLER'S TRUCKS AFTER LEAVING STREET PAVEMENT				GRAND TOTAL	

SIGNATURE

WEIGHMASTER

DRIVER

COMMENTS

SIGN & RETURN

NOTICE: SEE REVERSE SIDE FOR TERMS OF PURCHASE AGREEMENT

TP-8

Log Number

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name _____ Generator Site/Location _____

Address _____ Address _____

_____ 11/2/12

Phone No. _____ Phone No. _____

Approval Number

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Generator Authorized Agent Name _____ Signature _____ Shipment Date 10/29/12

TRANSPORTER

Transporter Name _____ Driver Name (Print) _____

Address _____ Vehicle License No. / State / EPA No. _____

_____ Truck Number _____

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature _____ Shipment Date 10-29-12

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature _____ Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent _____ Signature _____ Receipt Date 10/29/12

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

ACCEPTED FILL

BELLMAWR waterfront

An Equal Opportunity Employer

BELLMAWR WATERFRONT DEVELOPMENT, LLC

INBOUND CONTAMINATED SOILS

P.O. Box 336
Bellmawr, NJ 18099

Phone: (856) 931-6050
Fax: (856) 931-6287
www.bellmawrwaterfront.com

Control No. 142990

PURCHASE ORDER NO				DATE		TICKET NO	142990
CUSTOMER		PROJECT	NUMBER	NAME			
		MATERIAL	CODE	TYPE			
GROSS		TIME		TRUCK NO		UNIT PRICE	
TARE		QUANTITY ORDERED		CHARGE DEL		NET PRICE	
NET		QUANTITY DELIVERED				HAUL CHARGES	
UNITS/TONS		QUANTITY RECEIVED					
QTY DEL/REC TODAY		QUANTITY REMAINING				TAX SALES TAX	
LOAD NO		The signature below confirms that the material meets the applicable zoning, specifications and regulations. SELLER WILL NOT BE RESPONSIBLE FOR ANY DAMAGE CAUSED BY THE SELLER'S TRUCKS AFTER LEAVING STREET PAVEMENT.				GRAND TOTAL	

SIGNATURE

WEIGHMASTER

X

DRIVER

COMMENTS

SIGN & RETURN

TP-8

SOIL SAFE, INC.

Log Number: MMWW 0750

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name: CHELSEA Glen

Address: 260 W 36th St

New York NY

Phone No.:

Generator Site/Location:

Address:

11 D 990

Phone No.:

Description of Material

Approval Number: 9000-4320

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS Gen Foreman — Signature — 10/24/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name: PA Carrillo

Address: E Hanover NJ

Driver Name (Print): Henry Carrillo

Vehicle License No. / State / EPA No.: Am185 m NJ

Truck Number: 14

I hereby certify that the above named material was picked up at the generator site listed above.

10/24/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/24/11

Driver Signature — Delivery Date

DESTINATION

Bellmawr water Plant

Site Name: **Soil Safe, Inc. - Bridgeport** Phone No.: **1-856-467-8030**

Address: **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

10/24/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

ACCEPTED FILL

BELLMAWR waterfront

An Equal Opportunity Employer

BELLMAWR WATERFRONT DEVELOPMENT, LLC

INBOUND CONTAMINATED SOILS

P.O. Box 336
Bellmawr, NJ 18099

Phone: (856) 931-6050
Fax: (856) 931-6287
www.bellmawrwaterfront.com

Control No. 112999

PURCHASE ORDER NO			DATE			TICKET NO	
CUSTOMER			PROJECT NUMBER	NAME			
			MATERIAL CODE	TYPE			
GROSS		TIME		TRUCK NO		UNIT PRICE	
TARE		QUANTITY ORDERED		CHARGE DEL		NET PRICE	
NET		QUANTITY DELIVERED				HAUL CHARGES	
UNIT STONS		QUANTITY RECEIVED					
QTY DEL/RECV TODAY		QUANTITY REMAINING				PA SALES TAX	
LOAD NO		The signature below ratifies all of the terms & conditions on the reverse side and acknowledges that SELLER WILL NOT BE RESPONSIBLE FOR ANY DAMAGE CAUSED BY THE SELLER'S TRUCKS AFTER LEAVING STREET PAVEMENT.				GRAND TOTAL	
		SIGNATURE	COMMENTS				
WEIGHMASTER		X DRIVER				SIGN & RETURN	

Log Number

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name _____ Generator Site/Location _____

Address _____ Address _____

_____ _____

Phone No. _____ Phone No. _____

Approval Number

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name _____ Driver Name (Print) _____

Address _____ Vehicle License No. / State / EPA No. _____

_____ Truck Number _____

I hereby certify that the above named material was picked up at the generator site listed above.

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature Shipment Date Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/03/12 Ticket #: 168957
Time: 11:25 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: CASTIL
CASTILLO
Truck: AH847Y
License: CASTILLO 1

Phase: 0

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 5 Amount: 152.32 Tn 138.18 Mg
(To-Date) Loads: 11 Amount: 336.99 Tn 305.72 Mg

Gross:	44.21 Tn	88420 lb	40.11 Mg
Tare:	15.19 Tn	30380 lb	13.78 Mg
Net:	29.02 Tn	58040 lb	26.33 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

TP-3(7-14)

SOIL SAFE, INC.

Log Number 004

NON-HAZARDOUS MATERIAL MANIFEST

88420

GENERATOR

Generator Name Chelsea

Address 200 West 26th NY NY

Phone No.

Generator Site/Location

Address Same

Phone No.

Approval Number 20104

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — Signature — 2/3/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Casella #1

Driver Name (Print) Hector

Address

Vehicle License No. / State / EPA No.

Truck Number AH847Y

I hereby certify that the above named material was picked up at the generator site listed above.

Hector Mun 2-3-12

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Hector 2-3-12

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

LC 2-3-12

Name of Authorized Agent — Signature — Receipt Date

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/03/12 Ticket #: 168958
Time: 11:26 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: CASTIL
CASTILLO
Phase: 0
Truck: AN581J
License: CASTILLO 3

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 6 Amount: 189.49 Tn 171.91 Mg
(To-Date) Loads: 12 Amount: 374.16 Tn 339.44 Mg

Gross:	49.98 Tn	99960 lb	45.34 Mg
Tare:	12.81 Tn	25620 lb	11.62 Mg
Net:	37.17 Tn	74340 lb	33.72 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

99960

TP-3
(7-14)

Log Number 003

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea

Address 260 West 20th St
NY NY

Phone No.

Generator Site/Location

Address Same

Phone No.

Approval Number 120144

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Agent to generator — Generator Authorized Agent Name

Signature

2/3/12 — Shipment Date

TRANSPORTER

Transporter Name Castillo Trucking

Address Kearny, NJ

Driver Name (Print) Carlos Castillo

Vehicle License No. / State / EPA No. ANS81J

Truck Number 3

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 02/03/12 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 02/03/12 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent

Signature

2-3-12 — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/03/12 Ticket #: 168953
Time: 11:05 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990
P.O.#:

Carrier: CARILL
CARSILLO TRUCKING Phase: 0
Truck: AN280R
License: CARSILLO 19
Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 3 Amount: 94.23 Tn 85.49 Mg
(To-Date) Loads: 9 Amount: 278.90 Tn 253.02 Mg

Gross:	48.81 Tn	97620 lb	44.28 Mg
Tare:	14.72 Tn	29440 lb	13.35 Mg
Net:	34.09 Tn	68180 lb	30.93 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

Log Number

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name _____ Generator Site/Location _____

Address _____ Address _____

_____ _____

Phone No. _____ Phone No. _____

Approval Number

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Generator Authorized Agent Name _____ Signature _____ Shipment Date _____

TRANSPORTER

Transporter Name _____ Driver Name (Print) _____

Address _____ Vehicle License No. / State / EPA No. _____

_____ Truck Number _____

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature _____ Shipment Date _____

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature _____ Delivery Date 2-3-12

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent _____ Signature _____ Receipt Date 2-3-12

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/03/12 Ticket #: 168944
Time: 10:16 Plant: P1
*** Recycled ***

Customer: 0006435
SOIL SAFE INC.
6900 ALEXANDER BELL DRIV
COLUMBIA, MD 21046
(410) 872-3990

Job: 1201044
260 W. 26TH STREET
260 W. 26TH STREET
NEW YORK, NY 10001

P.O.#:

Carrier: CARILL
CARSILLO TRUCKING
Truck: AM185A
License: CARSILLO 14

Phase: 0

Zone:

Product: JR66
JR66 SOIL
JMF:

DEFAULT ZONE NAME

(Daily) Loads: 2 Amount: 60.14 Tn 54.56 Mg
(To-Date) Loads: 8 Amount: 244.81 Tn 222.09 Mg

Gross:	42.06 Tn	84120 lb	38.16 Mg
Tare:	14.53 Tn	29060 lb	13.18 Mg
Net:	27.53 Tn	55060 lb	24.98 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

Log Number

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name _____ Generator Site/Location _____

Address _____ Address _____

_____ _____

Phone No. _____ Phone No. _____

Approval Number	Description of Material	
	Non-Regulated Petroleum Contaminated Soil Non DOT/RCRA Regulated	**GROSS** **TARE** **NET** **TONNAGE**

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Generator Authorized Agent Name _____ Signature _____ Shipment Date 2/3/12

TRANSPORTER

Transporter Name _____ Driver Name (Print) _____

Address _____ Vehicle License No. / State / EPA No. _____

_____ Truck Number _____

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature _____ Shipment Date _____

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature _____ Delivery Date _____

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent _____ Signature _____ Receipt Date 2-3-12

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/03/12 Ticket #: 168955
Time: 11:18 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: CARILL
CARSILLO TRUCKING Phase: 0
Truck: AM678D
License: CARSILLO 16

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 4 Amount: 123.30 Tn 111.86 Mg
(To-Date) Loads: 10 Amount: 307.97 Tn 279.39 Mg

Gross:	43.39 Tn	86780 lb	39.36 Mg
Tare:	14.32 Tn	28640 lb	12.99 Mg
Net:	29.07 Tn	58140 lb	26.37 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

Log Number

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name _____ Generator Site/Location _____

Address _____ Address _____

_____ _____

Phone No. _____ Phone No. _____

Approval Number

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

_____ _____ _____

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name _____ Driver Name (Print) _____

Address _____ Vehicle License No. / State / EPA No. _____

_____ Truck Number _____

I hereby certify that the above named material was picked up at the generator site listed above.

_____ _____

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

_____ _____

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

_____ _____ _____

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/03/12 Ticket #: 168941
Time: 10:06 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: Pedro
PEDRO TEIXEIRA Phase: 0
Truck: AK833H
License: PEDRO 1

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 1 Amount: 32.61 Tn 29.58 Mg
(To-Date) Loads: 7 Amount: 217.28 Tn 197.12 Mg

Gross:	45.74 Tn	91480 lb	41.50 Mg
Tare:	13.13 Tn	26260 lb	11.91 Mg
Net:	32.61 Tn	65220 lb	29.58 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

Log Number 001

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Atlas

Address 211 W 26th St

Ocean City

Phone No. _____

Generator Site/Location _____

Address Same

Phone No. _____

Approval Number 20149

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Al Scott for Jonathan 2/13/17

Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name Ted Dietz Trucking Driver Name (Print) Norton

Address Rio Grande

Vehicle License No. / State / EPA No. _____

Truck Number 21

I hereby certify that the above named material was picked up at the generator site listed above.

Norton 2/13/17

Driver Signature / Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Norton 2/13/17

Driver Signature / Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

[illegible] 2.13.17

Name of Authorized Agent / Signature / Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/03/12 Ticket #: 168964
Time: 11:48 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: TMAK
T-MAK SERVICE Phase: 0
Truck: AM295T
License: T MAK #2

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 7 Amount: 223.08 Tn 202.38 Mg
(To-Date) Loads: 13 Amount: 407.75 Tn 369.91 Mg

Gross:	47.78 Tn	95560 lb	43.35 Mg
Tare:	14.19 Tn	28380 lb	12.87 Mg
Net:	33.59 Tn	67180 lb	30.47 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

TP-3
2-14

Log Number 007

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea

Address 366 Lee St E

Ny Ny

Phone No.

Generator Site/Location

Address Lot

Phone No.

Approval Number D2407H

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Generator Authorized Agent Name | Signature | 2/3/12 Shipment Date

TRANSPORTER

Transporter Name Chelsea Transport

Address Kearny

Driver Name (Print)

Vehicle License No. / State / EPA No.

Truck Number

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent | Signature | 2-3-12 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/03/12 Ticket #: 168971
Time: 13:03 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: JENCAR
JENCAR Phase: 0
Truck: AN546M
License: JENCAR 22

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 8 Amount: 255.22 Tn 231.54 Mg
(To-Date) Loads: 14 Amount: 439.89 Tn 399.07 Mg

Gross:	46.14 Tn	92280 lb	41.86 Mg
Tare:	14.00 Tn	28000 lb	12.70 Mg
Net:	32.14 Tn	64280 lb	29.16 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

92280

Log Number 008

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name _____ Generator Site/Location _____

Address _____ Address _____

Phone No. _____ Phone No. _____

Approval Number

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Generator Authorized Agent Name _____ Signature _____ Shipment Date _____

TRANSPORTER

Transporter Name _____ Driver Name (Print) _____

Address _____ Vehicle License No. / State / EPA No. _____

Truck Number _____

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature _____ Shipment Date _____

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature _____ Delivery Date _____

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent _____ Signature _____ Receipt Date 2-3-17

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 01/31/12 Ticket #: 168777
Time: 10:02 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: JDC
JDC TRUCKING Phase: 0
Truck: AK817R
License: JDC 3

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 1 Amount: 32.10 Tn 29.12 Mg
(To-Date) Loads: 1 Amount: 32.10 Tn 29.12 Mg

Gross:	46.26 Tn	92520 lb	41.97 Mg
Tare:	14.16 Tn	28320 lb	12.85 Mg
Net:	32.10 Tn	64200 lb	29.12 Mg

Received By._____
Weighmaster: LARRY CORREA NJWMS# 30175

TPH (7-14)

Log Number 001

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

92520

GENERATOR

Generator Name CHELSEA W.26 LLC Generator Site/Location SAME

Address 260 W. 26th ST Address

NY NY

Phone No. Phone No.

Approval Number	Description of Material	GROSS / TARE / NET / TONNAGE
120184 120104H	Non-Regulated Petroleum Contaminated Soil Non DOT/RCRA Regulated	

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS Agent to generator 1/31/12

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name JDC TRUCKING Driver Name (Print) CARLOS OLIVEIRA

Address 75 WINDSOR ST Vehicle License No. / State / EPA No. AK617R

KEARNY NJ 07032 Truck Number 305

I hereby certify that the above named material was picked up at the generator site listed above.

1/31/12

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

1/31/12

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

1-31-12

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 01/31/12 Ticket #: 168778
Time: 10:05 Plant: P1
*** Recycled ***

Customer: 0006435
SOIL SAFE INC.
6900 ALEXANDER BELL DRIV
COLUMBIA, MD 21046
(410) 872-3990

Job: 1201044
260 W. 26TH STREET
260 W. 26TH STREET
NEW YORK, NY 10001

P.O.#:

Carrier: JDC
JDC TRUCKING
Truck: AL876T
License: JDC 2

Phase: 0

Zone:

DEFAULT ZONE NAME

Product: JR66
JR66 SOIL
JMF:
(Daily) Loads: 2 Amount: 54.54 Tn 49.48 Mg
(To-Date) Loads: 2 Amount: 54.54 Tn 49.48 Mg

Gross:	36.73 Tn	73460 lb	33.32 Mg
Tare:	14.29 Tn	28580 lb	12.96 Mg
Net:	22.44 Tn	44880 lb	20.36 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

Log Number 003

NON-HAZARDOUS MATERIAL MANIFEST

73480

GENERATOR

Generator Name CHELSEA WOG LLC

Address 260 W. 26th ST NY NY

Phone No. X

Generator Site/Location SAME

Address

Phone No.

Approval Number 120144 120104

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Assigned to generator — Signature — 1/31/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name JDC TRUCKING

Address 75 WINDSOR ST KEARNY NJ 07032

Driver Name (Print) Junior

Vehicle License No. / State / EPA No. AL876T

Truck Number 31

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 1/31/12 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 1/31/12 Delivery Date

DESTINATION

Site Name Soil Safe, Inc. - Bridgeport Phone No. 1-856-467-8030

Address 378 Route 130 Logan Township, NJ 08085

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — 1-31-12 Receipt Date

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 01/31/12 Ticket #: 168799
Time: 12:55 Plant: P1
*** Delivery ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: TMAK
T-MAK SERVICE Phase: 0
Truck: AM295T
License: T MAK #2

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 3 Amount: 89.97 Tn 81.62 Mg
(To-Date) Loads: 3 Amount: 89.97 Tn 81.62 Mg

Gross:	49.62 Tn	99240 lb	45.02 Mg
Tare:	14.19 Tn	28380 lb	12.87 Mg
Net:	35.43 Tn	70860 lb	32.14 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

TR-1-(12-14)

SOIL SAFE, INC.

Log Number 003

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea W 26 LLC

Address 260 West 26th St NY NY

Phone No. _____

Generator Site/Location _____

Address Same

Phone No. _____

Approval Number 120184

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to operator — Signature — 11/31/12

Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name CARSILO T-MAK

Address KEARNY

Driver Name (Print) Pedro Tejeda

Vehicle License No. / State / EPA No. AM295T

Truck Number T-MAK #2

I hereby certify that the above named material was picked up at the generator site listed above.

Pedro Tejeda 11/31/12

Driver Signature / Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Pedro Tejeda 11/31/12

Driver Signature / Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

_____ KC 1-31-12

Name of Authorized Agent / Signature / Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 01/31/12 Ticket #: 168802
Time: 13:41 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: Pedro
PEDRO TEIXEIRA Phase: 0
Truck: AK833H
License: PEDRO 01

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 4 Amount: 120.68 Tn 109.48 Mg
(To-Date) Loads: 4 Amount: 120.68 Tn 109.48 Mg

Gross:	43.84 Tn	87680 lb	39.77 Mg
Tare:	13.13 Tn	26260 lb	11.91 Mg
Net:	30.71 Tn	61420 lb	27.86 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

TP-1 (7-14)

87680

Log Number 004

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea

Address 260 West 28th St NY NY

Generator Site/Location

Address SAME

Phone No.

Phone No.

Approval Number 12dd14

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agnt to generator — 1/31/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name CARSILO T-MAK

Driver Name (Print) Victor

Address KEARNY

Vehicle License No. / State / EPA No. AK833H

Truck Number T-MAK #1

I hereby certify that the above named material was picked up at the generator site listed above.

Victor — 1/31/12

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Victor — 1/31/12

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate

[signature] — 1-31-12

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 01/31/12
Time: 14:13
*** Recycled ***

Ticket #: 168807
Plant: P1

Customer: 0006435
SOIL SAFE INC.
6900 ALEXANDER BELL DRIV
COLUMBIA, MD 21046
(410) 872-3990

Job: 1201044
260 W. 26TH STREET
260 W. 26TH STREET
NEW YORK, NY 10001

P.O.#:

Carrier: JDC
JDC TRUCKING
Truck: AK817R
License: JDC 3

Phase: 0

Zone:

DEFAULT ZONE NAME

Product: JR66
JR66 SOIL
JMF:
(Daily) Loads: 5 Amount: 152.21 Tn 138.08 Mg
(To-Date) Loads: 5 Amount: 152.21 Tn 138.08 Mg

Gross:	45.69 Tn	91380 lb	41.45 Mg
Tare:	14.16 Tn	28320 lb	12.85 Mg
Net:	31.53 Tn	63060 lb	28.60 Mg

Received By: _____
Weighmaster: LARRY CORREA NJWMS# 30175

PR-L (0-14)

SOIL SAFE, INC.

Log Number 005

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA W26 LLC

Address 260 W. 26th ST NY NY

Phone No. X

Generator Site/Location SAME

Address X

Phone No. X

Approval Number 120144

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS agent to generator — Signature — 1/31/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name JDC TRUCKING

Address 75 WINDSOR ST KEARNY NJ 07032

Driver Name (Print) CARLOS OLIVEIRA

Vehicle License No. / State / EPA No. AK817R

Truck Number 305

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 1/31/12 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 1/31/12 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — 1-31-12 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 01/31/12 Ticket #: 168808
Time: 14:15 Plant: P1
*** Recycled ***

Customer: 0006435
SOIL SAFE INC.
6900 ALEXANDER BELL DRIV
COLUMBIA, MD 21046
(410) 872-3990

Job: 1201044
260 W. 26TH STREET
260 W. 26TH STREET
NEW YORK, NY 10001

P.O.#:

Carrier: JDC
JDC TRUCKING
Truck: AL876T
License: JDC 2

Phase: 0

Zone:

Product: JR66
JR66 SOIL
JMF:

DEFAULT ZONE NAME

(Daily) Loads: 6 Amount: 184.67 Tn 167.53 Mg
(To-Date) Loads: 6 Amount: 184.67 Tn 167.53 Mg

Gross:	46.75 Tn	93500 lb	42.41 Mg
Tare:	14.29 Tn	28580 lb	12.96 Mg
Net:	32.46 Tn	64920 lb	29.45 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

TPH 7-14

Log Number 006

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA W26 LLC Generator Site/Location SAME

Address 260 W. 26th ST
NY, NY

Phone No. X

Address

Phone No.

Approval Number 120142

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As Agent to generator — 1/31/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name JJC TRUCKING Driver Name (Print) Jun. Jr.

Address 75 WINDSOR ST Vehicle License No. / State / EPA No. AL876T
KEARNY NJ 07032 Truck Number 311

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 1/31/12 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 1/31/12 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

KC — 1-31-12

Name of Authorized Agent — Signature — Receipt Date

Log Number 001

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

TP1 & TP2

GENERATOR

Generator Name Chelsea Green

Address 260 W 26th Street
New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No. ID 1087

Approval Number 24-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS 48.22 T GROSS
TARE 14.47 TARE
RECALCED NET 33.75 NET
LOG 3
10/10/2011 TONNAGE
09:26AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Dany — 10/10/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

BUTTAL TRUCK

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Antonio Pavon

Vehicle License No. / State / EPA No. AN523H

Truck Number 1087 2006 BUTTAL

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 10/10/11 — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 10/10/11 — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature (Coarse) — 10.10.11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number: 002

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST TP-1 & TP-2

GENERATOR

Generator Name: Chelsea Green

Address: 260 W. 26th Street
New York, NY

Phone No.:

Generator Site/Location: SAME

Address:

Phone No.:

Approval Number: C4-8197

Description of Material:
Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

ID 758
GROSS 47.97 T — GROSS
TARE 14.09 T — TARE
RECALLED
NET 33.88 T — NET
LOG 4
10/10/2011
09:36AM
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Danny — 10/10/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name: AMG Industrial Contr.

Address: Wallside, NJ

Driver Name (Print): Carlos Pinto

Vehicle License No. / State / EPA No.: AK70LK # 803

Truck Number: 758

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date: 10/10/11

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date: 10/10/11

DESTINATION

Site Name: **Soil Safe, Inc. - Bridgeport** Phone No.: **1-856-467-8030**

Address: **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garau — 10-10-11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 004

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

TP1 & TP2

GENERATOR

Generator Name: Chelsea Green

Address: 260 W. 26th Street, New York, NY

Phone No.:

Generator Site/Location: SAME

Address:

Phone No.:

Approval Number: C4-8199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 865
GROSS 47.01 T
TARE 12.68 T
RECALLED
NET 34.33 T
LOG 6
10/10/2011
09:48AM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Danny — 10/10/11

Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name: AMG Industries

Address: Hillsdale, NJ

Driver Name (Print): Kleberson

Vehicle License No. / State / EPA No.: AC 939V

Truck Number: 803 & SS # 865

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature / Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature / Delivery Date

DESTINATION

Site Name: **Soil Safe, Inc. - Bridgeport** Phone No.: **1-856-467-8030**

Address: **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 10.10.11

Name of Authorized Agent / Signature / Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 005

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST TP1 & TP2

GENERATOR

Generator Name Chelsea Groups | Generator Site/Location Same

Address 260 W. 26th Street, Newyork, NY | Address

Phone No. | Phone No.

Approval Number: C4-8149

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 381
GROSS
TARE
RECALLED
NET 7
LOG
10/10/2011
09:54AM

GROSS	44.94 T	
TARE	13.15 T	TARE
NET	31.79 T	NET
		TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Danny | Signature | 10/10/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print) Marcos Lopez

Address Hillside, NJ | Vehicle License No. / State / EPA No. AM 4184 A

Truck Number 10

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature | Shipment Date 10/10/11

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

E. J. Carlon | 10:10:11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 003

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST TP1 & TP2

GENERATOR

Generator Name Chelsea Green

Address 260 W 26th Street

New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

ID 751

GROSS 49.93 T GROSS
TARE 13.56 T
RECALLED TARE
NET 36.37 T
LOG 9 NET
10/10/2011
09:53AM TONNAGE

Approval Number 04-0199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Dan [signature] 10/10/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) WASHINGTON

Vehicle License No. / State / EPA No. AU584 NJ

Truck Number 1802 SA 751

I hereby certify that the above named material was picked up at the generator site listed above.

[signature] 10/10/11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

[signature] 10/10/11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia 10/10/11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 007

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST Tp 1+2

GENERATOR

Generator Name Chelsea Green | Generator Site/Location SAME

Address 260 W. 26th St | Address

New York, NY

Phone No. | Phone No.

Approval Number 04-6149

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID .001
GROSS 49.85 T GROSS
RECALLED
TARE 12.75 T TARE
NET 12 37.10 T NET
LOG
10/10/2011
10:36AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Danny | 10/10/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AME Industries | Driver Name (Print) Ramiro Nol

Address Hillside, NJ | Vehicle License No. / State / EPA No. C22524

Truck Number 09 001

I hereby certify that the above named material was picked up at the generator site listed above.

Ramiro Nol 10 10 11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Ramiro Nol 10 10 11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Carlos 10 10 11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co

Log Number 006

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST TP1+2

GENERATOR

Generator Name Chelsea Green | Generator Site/Location SAME

Address 260 W. 26th St | Address

New York, NY

Phone No. | Phone No.

Approval Number 248199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 791
GROSS 46.43 T
TARE 13.08 T
RECALLED
NET 33.35 T
LOG 20
10/10/2011
11:03AM

GROSS / TARE / NET / TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Danny | 10/10/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print) Frank V.

Address Hillside, NJ | Vehicle License No. / State / EPA No. AM113A

Truck Number 302

I hereby certify that the above named material was picked up at the generator site listed above.

Frank V. 10/10/11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Frank V. 10/10/11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

A Corso | 10-10-11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 010

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST PT-6

GENERATOR

Generator Name Chelsea Green | Generator Site/Location SAME

Address 260 W. 26th St | Address

New York, NY

Phone No. | Phone No.

Approval Number 04-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 1087
GROSS 50.58 T GROSS
TARE 14.47 T TARE
RECALLED
NET 36.11 T NET
LOG 44
10/10/2011 TONNAGE
03:20PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Danny | 10/10/11

Generator Authorized Agent Name | Signature | Shipment Date

BAFFAL TRUCK

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print) ANT. PAVIA

Address Hillside, NJ | Vehicle License No. / State / EPA No. ANS23H

Truck Number 1087 306 BAFFAL

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature | Shipment Date 10/10/11

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature | Delivery Date 10/10/11

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia | 10 10 11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 009

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST pg 6

GENERATOR

Generator Name Chelsea Green

Address 260 W. 26th St

New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number 24-8119

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

10 TSB
GROSS 50.02 GROSS
TARE 14.09 T TARE
RECALLED
NET 35.93 T NET
LOG 45
10/10/2011
03:22PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Danny — 10/10/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries North

Address Hillside, NJ

Driver Name (Print) Carlos I.

Vehicle License No. / State / EPA No. AK774 #605

Truck Number 75d

I hereby certify that the above named material was picked up at the generator site listed above.

10/10/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/10/11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Carlos — 10 10 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 011

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST PTG.

GENERATOR

Generator Name Chelsea Green | Generator Site/Location SAME

Address 260 W. 26th St, New York, NY | Address

Phone No. | Phone No.

Approval Number C4-8199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 381
GROSS 53.91 T GROSS
TARE 15.15 T TARE
RECYCLED
NET 38.86 T NET
LOG 47
10/10/2011
03:25PM
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Danny | Signature | 10/10/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print) Hector

Address Hillside, NJ | Vehicle License No. / State / EPA No. AM4854A

Truck Number #10

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature | 10/10/11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia | 10/10/11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 008

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST pt. 6

GENERATOR

Generator Name Chelsea Green

Address 260 W. 26th St

New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No. 10 -0704

Approval Number 24-2141

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS 53.48 T
RECALLED
TARE 12.74 T
NET 40.74 T
LOG 48
10/10/2011
03:27PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Danny 10/10/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Gilberto Salazar

Vehicle License No. / State / EPA No. C725240

Truck Number 49

I hereby certify that the above named material was picked up at the generator site listed above.

10-10-11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-10-11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Carlos 10/10/11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 012

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST pg

GENERATOR

Generator Name Chelsea Green | Generator Site/Location SAME

Address 260 W. 26th St | Address

New York, NY

Phone No. | Phone No.

Description of Material

Approval Number 14-6199

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 751
GROSS 52.08 T GROSS
TARE 13.56 T TARE
RECALCED
NET 38.52 T NET
LOG 49
10/10/2011
03:29PM
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Danny | 10/6/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print) WASHINGTON

Address Hillside, NJ | Vehicle License No. / State / EPA No. AM 584 M

Truck Number 4807 751

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia | 10/6/11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 013

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST PTG

GENERATOR

Generator Name Chelsea Green | Generator Site/Location SAME

Address 260 W. 26th St, New York, NY | Address

Phone No. | Phone No.

Approval Number 24-8491

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

10 Tons

GROSS 55.64 T
TARE 12.71 T
RECALLED
NET 42.93 T
LOG SO
10/10/2011
09:31PM

GROSS / TARE / NET / TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Danny | 10/10/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print) Romulo Ortiz

Address Hillside, NJ | Vehicle License No. / State / EPA No. C723 241

Truck Number 09

I hereby certify that the above named material was picked up at the generator site listed above.

Romulo Ortiz | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Romulo Ortiz 10 10 11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia 10/10/11

Name of Authorized Agent | Signature | Receipt Date

White - Facility | Green - Facility | Yellow - Generator | Pink - Broker | Goldenrod - Contractor | Blue - Trucking Co.

Log Number 014

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST pt. 6

GENERATOR

Generator Name Chelsea Green | Generator Site/Location Same

Address 260 W. 26th St | Address

New York, NY

Phone No. | Phone No.

Approval Number: CU-2199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 731
GROSS 44.86 T GROSS
TARE 13.08 TARE
RECALLED
NET 31.78 T NET
LOG 51
10/10/2011 TONNAGE
03:33PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Danny | 10/10/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print) Frank U.

Address Hillside, NJ | Vehicle License No. / State / EPA No. AU1134

Truck Number 82

I hereby certify that the above named material was picked up at the generator site listed above.

Frank U. 10/10/11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Frank U. 10/10/11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Carlos | 10/10/11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 015

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST PT 6

GENERATOR

Generator Name Chelsea Green | Generator Site/Location SAME

Address 260 W. 26th St | Address

New York, NY

Phone No. | Phone No.

Approval Number 24-899

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 865
GROSS 46.67 T
TARE 12.68 T
RECALLED
NET 33.99 T
LOG 54
10/10/2011
03:53PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Danny | 10/10/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print)

Address Hillside, NJ | Vehicle License No. / State / EPA No. AC339V

Truck Number 803 # SS 865

I hereby certify that the above named material was picked up at the generator site listed above.

10-10-11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-10-11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia | 10 10 11

Name of Authorized Agent | Signature | Receipt Date

White - Facility | Green - Facility | Yellow - Generator | Pink - Broker | Goldenrod - Contractor | Blue - Trucking Co.

Soil Exp.

CLEAN EARTH

Manifest # 547897
PT. 6

GLOBAL JOB NUMBER: Chelsea Green **FACILITY APPROVAL NUMBER:** Sand Approval - CH-8199

Please Check One:

☐ Clean Earth of Carteret
24 Middlesex Avenue
Carteret, NJ 07008
Ph: 732-541-8909

☐ Clean Earth of Maryland
1469 Oak Ridge Place
Hagerstown, MD 21740
Ph: 301-791-6220

☐ Clean Earth of New Castle
94 Pyles Lane
New Castle, DE 19720
Ph: 302-427-6633

☐ Other

☐ Clean Earth of Philadelphia
3201 S. 61st Street
Philadelphia, PA 19153
Ph: 215-724-5520

☐ Clean Earth of North Jersey
115 Jacobus Avenue
Kearny, NJ 07032
Ph: 973-344-4004

☐ Clean Earth of Southeast Pennsylvania
7 Steel Road East
Morrisville, PA 19067
Ph: 215-428-1700

Non-Hazardous Material Manifest

10 PM

(Type or Print Clearly)

GENERATOR'S NAME & SITE ADDRESS:	GROSS WEIGHT: ☐Tons ☐Yards	53.05 T
	TARE WEIGHT: ☐Tons ☐Yards	13.06 T 39.99 T
GENERATOR'S PHONE:	NET WEIGHT: ☐Tons ☐Yards	

TARE ED
NET
59
10/2011
PM

DESCRIPTION OF MATERIAL/SAMPLE ID AND LOCATION

GENERATOR'S CERTIFICATION – Incomplete and/or unsigned manifests will cause the load to be delayed and/or rejected.

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, is not a DOT hazardous substance as defined by 49 CFR Part 172 or any applicable state law, has been fully and accurately described above, classified, packaged and is in proper condition for transportation according to all applicable state and federal regulations.

Name: Danny Title: Sup

Signature: Date and Time: 10/10/11

TRANSPORTER

Company: AMES TRUCKING Phone Number:

Address: Truck # and License Plate: AM 323 Y

Driver: SW Haulers Permit #:

(Type or Print Clearly) (applicable state permit #)

I hereby certify that the above named material was picked up at the site listed above.

Driver Signature: CARLOS DEL? Date and Time: 10-10-11

DESTINATION

I hereby certify that the above named material was delivered without incident to the facility noted above.

Driver Signature: Date and Time:

I hereby certify that the above named material has been accepted at the above referenced facility.

Authorized Signature: Date and Time: 10/10/11

CLEAN EARTH INTERNAL

Soil e Safe

CLEAN EARTH

Manifest # 547900

PT 6

GLOBAL JOB NUMBER: Chelsea Green **FACILITY APPROVAL NUMBER:** _____

Please Check One: Approval # C4-8199

☐ Clean Earth of Carteret
24 Middlesex Avenue
Carteret, NJ 07008
Ph: 732-541-8909

☐ Clean Earth of Maryland
1469 Oak Ridge Place
Hagerstown, MD 21740
Ph: 301-791-6220

☐ Clean Earth of New Castle
94 Pyles Lane
New Castle, DE 19720
Ph: 302-427-6633

☐ Other
_____
_____
_____

☐ Clean Earth of Philadelphia
3201 S. 61st Street
Philadelphia, PA 19153
Ph: 215-724-5520

☐ Clean Earth of North Jersey
115 Jacobus Avenue
Kearny, NJ 07032
Ph: 973-344-4004

☐ Clean Earth of Southeast Pennsylvania
7 Steel Road East
Morrisville, PA 19067
Ph: 215-428-1700

Non-Hazardous Material Manifest

(Type or Print Clearly)

GENERATOR'S NAME & SITE ADDRESS:	GROSS WEIGHT: ☐ Tons ☑ Yards 49.54 T
	TARE WEIGHT: ☐ Tons ☐ Yards 13.28 T
GENERATOR'S PHONE: _____	NET WEIGHT: ☐ Tons ☐ Yards 36.26 T

10 TRK
GROSS
SCALED
NET
61
10/10/2011

DESCRIPTION OF MATERIAL/SAMPLE ID AND LOCATION

GENERATOR'S CERTIFICATION – Incomplete and/or unsigned manifests will cause the load to be delayed and/or rejected.

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, is not a DOT hazardous substance as defined by 49 CFR Part 172 or any applicable state law, has been fully and accurately described above, classified, packaged and is in proper condition for transportation according to all applicable state and federal regulations.

Name: Denny Title: T5

Signature: _____ Date and Time: 10.10.11

TRANSPORTER

Company: PMC Ltd Phone Number: _____

Address: _____ Truck # and License Plate: AM 38K

Driver: _____ SW Haulers Permit #: _____

(Type or Print Clearly) (applicable state permit #)

I hereby certify that the above named material was picked up at the site listed above.

Driver Signature: Jose Lopez Date and Time: _____

DESTINATION

I hereby certify that the above named material was delivered without incident to the facility noted above.

Driver Signature: _____ Date and Time: _____

I hereby certify that the above named material has been accepted at the above referenced facility.

Authorized Signature: _____ Date and Time: 10.10.11

CLEAN EARTH INTERNAL

SoilSafe.
Recycling of Contaminated Soil and Industrial Waste.
6700 Alexander Bell Drive, Suite 300, Columbia, MD 21046
(410) 872-3990, Fax (410) 872-3978

Invoice

55610

Bill To:

Chelsea West 26, LLC c/o Artimus Construction, Inc.
Attention: Amnon Solomon
37 West 65th Street
2nd Floor
New York, NY 10023

Project:

Chelsea Green
260 West 26th Street
New York, NY 10001

APPROVAL #: C4-8199
PROPOSAL #: 441
PO #:
INVOICED VOLUME OF SOIL: 2,627.83
 # OF TRUCKS: 81
INVOICE DATE: 11/3/11
DUE DATE: 12/3/11

BILLING PERIOD: 10/24/11 TO 10/26/11

DESCRIPTION:	UNITS INVOICED:	RATE:	AMOUNT:
Recycling & Transportation Fees - Tons	2,627.83	$ 42.00	$ 110,368.86

1) REC'D 11/12/11 2) ENTERED/JDE 11/15/11
3) PS MATCHED
4) SCANNED & MOVED
5) PM APPPROVED & UPDATED ENTRY
6) CONTROLLER REVIEW
7) EXEC 1 REVW 7a) EXEC 2 REVW
7b) CHK CUT 7c) EXEC 3 REVW
8) CHECK DATE CHECK#
CHECK AMOUNT

GROSS INVOICE	$ 110,368.86
SALES TAX	0.00
LESS: PREPAYMENTS	0.00
INVOICE TOTAL	$ 110,368.86

Contact:

**NOTE* Payments are Net 30 days. Overdue balances are subject to a 1.5% charge per month or the maximum allowed by law.*

Remit to: (Payments Only) Soil Safe, Inc., P.O. Box 824062, Philadelphia, PA 19182-4062

TP-360-D

SOIL SAFE, INC.

Log Number 1009

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 250 W 26th St NY, NY

Phone No.

Generator Site/Location

Address Sand

Phone No.

Approval Number C4-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 647
GROSS 41.72 GROSS
TARE 14.48 T
RECALLED TARE
NET 27.24 T NET
LOG 12
10/24/2011
10:03AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS Agent for Gaunt 10/24/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name AMB Industries

Address Hillside, NJ

Driver Name (Print) Mario Velarde

Vehicle License No. / State / EPA No. AN931F

Truck Number 16

I hereby certify that the above named material was picked up at the generator site listed above.

10/24/11

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/24/11

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

A. Garcia 10/24/11

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3 (10-7)

SOIL SAFE, INC.

Log Number 10294002

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 39th St NY, NY

Phone No.

Generator Site/Location

Address Same

Phone No.

Approval Number CY-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 593
GROSS 42.56 T GROSS
TARE 14.31 T TARE
RECALLED
NET 28.25 T NET
LOG 13
10/24/2011 TONNAGE
10:06AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — Signature — 10/24/11 Shipment Date

Generator Authorized Agent Name

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Benjamin Pond

Vehicle License No. / State / EPA No. AM10SE

Truck Number 18

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 10/24/11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 10/24/11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

A. Gatch — 10.24.11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4(0-2)

SOIL SAFE, INC.

Log Number 10B6004

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 36th St NY, NY

Phone No.

Generator Site/Location

Address Same

Phone No.

Approval Number 04-899

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 758
GROSS 45.14 GROSS
TARE 14.09 T
RECALLED TARE
NET 31.05 T
LOC 14 NET
10/24/2011
10:08AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — 10/24/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMK Industries

Address Hillside, NJ

Driver Name (Print) Carlos P.

Vehicle License No. / State / EPA No. AK 776K

Truck Number 805 (73)

I hereby certify that the above named material was picked up at the generator site listed above.

10/24/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/24/11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Gonce — 10 24 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-360-9

SOIL SAFE, INC.

Log Number 0888 003

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 26th St NY, NY

Phone No.

Generator Site/Location

Address Same

Phone No.

Approval Number 04-899

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 646
GROSS 45.76 T
TARE 14.52 T
RECYCLED
NET 31.24 T
LOG 17
10/24/2011
10:14AM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 10/24/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Robinson Velarde

Vehicle License No. / State / EPA No. AM3952

Truck Number 9

I hereby certify that the above named material was picked up at the generator site listed above.

Robinson 10-24-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Robinson 10-24-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Carol 10 24 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-3 (0-7)

SOIL SAFE, INC.

Log Number 007

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W26 ST

New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number 34-819

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 865

GROSS	47.53	GROSS
TARE	12.68 T	
RECALLED		TARE
NET	34.85 T	
		NET
LOG 20		
10/24/2011		
10:28AM		TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As Agent to Operator — 10/24/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) K Gibson

Vehicle License No. / State / EPA No. AL 938 V

Truck Number 803 # 28-14 867

I hereby certify that the above named material was picked up at the generator site listed above.

10-24-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-24-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 10 24 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Page 3 (0-7)

Log Number 006

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name: Chelsea Green
Generator Site/Location: SAME
Address: 260 W26th St
New York, NY
Address:
Phone No.:
Phone No.: ID 342

Approval Number: 04-3199

Description of Material:
Non-Regulated Petroleum
Contaminated Soil
Non DOT/RCRA Regulated

GROSS 46.45 T
TARE 14.80 T
RECALLED
NET 31.65 T
LOS 21
10/24/2011
10:32AM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — 10/24/11
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Shirley
Transporter Name: AMG Industries
Driver Name (Print): Luis
Address: Hillside, NJ
Vehicle License No. / State / EPA No.: AM 316 M
Truck Number: 05

I hereby certify that the above named material was picked up at the generator site listed above.
Luis — 10/24/11
Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.
Luis — 10/24/11
Driver Signature — Delivery Date

DESTINATION

Site Name: **Soil Safe, Inc. - Bridgeport**
Phone No.: **1-856-467-8030**
Address: **378 Route 130 Logan Township, NJ 08085**
No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia — 10-24-11
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TT-3 (0-7)

SOIL SAFE, INC.

Log Number 005

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 200 W 25th St NY, NY

Phone No.

Generator Site/Location

Address Same

Phone No.

Approval Number C4-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

TO 107

GROSS	44.53 T	GROSS
TARE	13.86 T	
RECALLED		TARE
NET	30.67 T	NET
LOG 22		
10/24/2011		
10:34PM		TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 10/24/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillsboro, NJ

Driver Name (Print) JAIRO

Vehicle License No. / State / EPA No. AN96YF

Truck Number R25 # 38

I hereby certify that the above named material was picked up at the generator site listed above.

10-24-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-24-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

A Corea — 10/24/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

RR-3 (10-7)

SOIL SAFE, INC.

Log Number 008

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 26th St

New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number 24-3199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 531
GROSS 46.25 GROSS
TARE 14.69 T
RECALLED
NET 31.56 T TARE
LOG 23 NET
10/24/2011
10:38AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

CLS agent to generator — 10/24/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Paul

Vehicle License No. / State / EPA No. NJ 8704A

Truck Number Shirley 20

I hereby certify that the above named material was picked up at the generator site listed above.

Paul — 10-24-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Paul — 10-24-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3 (0-2)

Log Number 009

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location SAME

Address 260 W26th St, New York, NY | Address

Phone No. | Phone No.

ID 589
GROSS 46.01 T GROSS
TARE 14.91 T TARE
RECALLED
NET 31.10 T NET
LOG 25
10/24/2011
10:44AM TONNAGE

Approval Number 04-7199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AC Sent to smarlow | 10/24/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print) Carlos

Address Millsdale | Vehicle License No. / State / EPA No. AMNOT

Truck Number Shirley 06

I hereby certify that the above named material was picked up at the generator site listed above.

10-24-11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-24-11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia | 10 24 11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-30-7

SOIL SAFE, INC.

Log Number 010

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W26th St
New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No. 10 486

Approval Number 04-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS 47.40 GROSS
TARE 14.21 TARE
RECALLED
NET 33.19 NET
LOG 26
10/24/2011
10:58AM
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

OS agent to Generator — 10/24/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Leonardo Saltos

Vehicle License No. / State / EPA No. AM181J

Truck Number 02 4106

I hereby certify that the above named material was picked up at the generator site listed above.

10-24-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-24-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

A Garcia — 10-24-11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-3 (6-7)

SOIL SAFE, INC.

Log Number 011

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 26th St
New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number NY-919

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 766
GROSS 46.33 T GROSS
TARE 13.61 T TARE
RECALCED
NET 32.72 T NET
LOG 27
10/24/2011 TONNAGE
11:01AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to Generator — 10/24/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Julio Barcelos

Vehicle License No. / State / EPA No. AM1194

Truck Number Barbo Trucking 804

I hereby certify that the above named material was picked up at the generator site listed above.

10/24/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/24/11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130, Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 10-24-11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PP3 (0-7)

SOIL SAFE, INC.

Log Number: 01

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name: Nicholson Group

Address: 260 W 36th St
New York, NY

Phone No.:

Generator Site/Location: SAME

Address:

Phone No.:

Approval Number: 04-1199

Description of Material:

Non-Regulated Petroleum
Contaminated Soil

Non DOT/RCRA Regulated

ID 751
GROSS 48.77 T GROSS
TARE 13.56 T TARE
RECALCLED
NET 35.21 T NET
LOG 28
10/24/2011 TONNAGE
11:03AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

GS 9 SOIL TO CRANDON — 10/24/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name: AMG Industries

Address: Hillside, NJ 07182

Driver Name (Print): WASHINGTON

Vehicle License No. / State / EPA No.: AM58414

Truck Number: #802

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date: 10/24/11

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date: 10/24/11

DESTINATION

Site Name: **Soil Safe, Inc. - Bridgeport** Phone No.: **1-856-467-8030**

Address: **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 10-24-11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3007

SOIL SAFE, INC.

Log Number 013

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green Generator Site/Location SAME

Address 260 W 25th St Address

New York, NY

Phone No. Phone No.

Description of Material

Approval Number 04-8199

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 466
GROSS 43.76 T GROSS
TARE 12.40 T TARE
RECALCED
NET 31.36 T NET
LOC 29
10/24/2011 TONNAGE
11:06AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS agent to generator 10/24/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name AMG Industries Driver Name (Print) Nestor

Address Hillside, NJ Vehicle License No. / State / EPA No. C037634

Truck Number 9

I hereby certify that the above named material was picked up at the generator site listed above.

10-24-11

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Carroll 10.24.11

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-3 (6-7)

SOIL SAFE, INC.

Log Number 014

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 26th St

New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number 24-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 1087
GROSS 48.94 T GROSS
TARE 14.47 T TARE
RECALLED
NET 34.47 T NET
LOG 30
10/24/2011 TONNAGE
11:08AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

CE agent to Generator — 10/24/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillsdale, NJ

Driver Name (Print) Alfo Pavia

Vehicle License No. / State / EPA No. AM583H

Truck Number 1087 & 806

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date 10/24/11

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date 10/24/11

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Conca — 10 24 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3 (07)

SOIL SAFE, INC.

Log Number 05

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 360 W 126th ST

New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number 24-8149

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 747
GROSS 42.85 T GROSS
TARE 14.68 T TARE
RECALLED
NET 28.17 T NET
LOG 31
10/24/2011 TONNAGE
11:12AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

QC agent to generator — 10/24/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Dan 05

Driver Name (Print) Bryan Machado

Vehicle License No. / State / EPA No. AD/992 NJ 74

Truck Number 04 747

I hereby certify that the above named material was picked up at the generator site listed above.

10-23-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-23-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia — 10 24 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR3(07)

Log Number 016

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W26th St
New York, NY

Phone No.

Generator Site/Location

Address

Phone No.

Description of Material

Approval Number 04-899

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 515
GROSS 43.14 T GROSS
TARE 12.99 T TARE
RECALLED
NET 30.15 T NET
LOG 34
10/24/2011
11:37AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent for Chelsea Green 10/24/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name D&G Industries

Address Hillside NJ

Driver Name (Print) Oscar

Vehicle License No. / State / EPA No. NJ1536

Truck Number 515

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature 10/24/11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature 10/24/11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130, Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia 10.24.11

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-30-2

SOIL SAFE, INC.

Log Number 017

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Grear | Generator Site/Location SAME

Address 260 W 26th St, New York, NY | Address

Phone No. | Phone No.

Approval Number 24-8199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 680
GROSS 49.15 T — GROSS
TARE 13.69 T — TARE
RECALLED
NET 35.46 T — NET
LOG 37
10/24/2011
12:01PM — TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

US agent to sign for | 10/24/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name Avino Industries | Driver Name (Print) WALTON

Address Millville, NJ | Vehicle License No. / State / EPA No. AM 331D

Truck Number 704

I hereby certify that the above named material was picked up at the generator site listed above.

10/24/11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/24/11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Cerick | 10 24 11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3(07)

Log Number 018

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location SAME

Address 260 W26th St, New York, NY | Address

Phone No. | Phone No.

ID 1015
GROSS 53.22 GROSS
TARE 13.50 T
RECALLED TARE
NET 39.72 T
LOG 43 NET
10/24/2011
12:34PM TONNAGE

Approval Number 24-11 99

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent for Quality | 10/24/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print) Jose

Address Hillside, NJ | Vehicle License No. / State / EPA No. [illegible]

Truck Number 43

I hereby certify that the above named material was picked up at the generator site listed above.

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature | Shipment Date | Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia | 10 24 11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3 (0-7)

SOIL SAFE, INC.

Log Number 019

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W25th St
New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number 24-3109

Description of Material

Non-Regulated Petroleum
Contaminated Soil

Non DOT/RCRA Regulated

10 TON
GROSS 49.03 GROSS
TARE 14.09 T
RECALLED TARE
NET 34.94 T
LOG 59 NET
10/24/2011
02:13PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Scott Bryant — 10/24/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Carlos Pinto

Vehicle License No. / State / EPA No. AK776K

Truck Number 758

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 10/24/11 — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Goyco — 10/24/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3 (0-7)

Log Number 020

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W26th St

New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number 04-3199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 647

GROSS	47.99 T	GROSS
TARE	14.48 T	TARE
RECALLED		
NET	33.51 T	NET

LOG 61

10/24/2011 12:36PM

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

GS agent to Generator — 10/24/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Mario Mendo

Vehicle License No. / State / EPA No. MV 931 T

Truck Number 16

I hereby certify that the above named material was picked up at the generator site listed above.

10/24/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/24/11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Garcia — 10 24 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-3079

Log Number 091

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Generator Site/Location SAME

Address 260 W26th St
New York, NY

Address

Phone No.

Phone No.

Approval Number 24-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 5333
GROSS 46.30 GROSS
TARE 14.31 T
RECHILLED TARE
NET 31.99 T
LOG 62 NET
10/24/2011
02:40PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 10/24/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Driver Name (Print) Benjamin Picard

Address Hillside, NJ

Vehicle License No. / State / EPA No. DN1KPE

Truck Number 13

I hereby certify that the above named material was picked up at the generator site listed above.

10/24/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/24/11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

D Garcia — 10-24-11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3 (0-7)

SOIL SAFE, INC.

Log Number 023

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 26th St

New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number 24-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 865

GROSS 41.78 T GROSS

TARE 12.68 T TARE

RECALLED

NET 29.10 T NET

LOG 63

10/24/2011

02:43PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

QS agent to generator 10/24/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Kuharson

Vehicle License No. / State / EPA No. PC 939 V

Truck Number 803 # SS # 865

I hereby certify that the above named material was picked up at the generator site listed above.

10-24-11

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/24/11

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Garcia 10-24-11

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3 (0-2)

SOIL SAFE, INC.

Log Number 082

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W26th St
New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number C4-61M

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

IN 6:46
GROSS 45.52 T GROSS
TARE 14.52 T
RECALLED TARE
NET 31.00 T NET
LOG 64
10/24/2011 TONNAGE
02:50PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

QS agent to generator — 10/24/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Denny C

Vehicle License No. / State / EPA No. AM3952

Truck Number 9

I hereby certify that the above named material was picked up at the generator site listed above.

Denny C — 10-24-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Denny C — 10-24-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 10-24-11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-3007

Log Number 007

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Grove | Generator Site/Location SAME

Address 260 W 26th St, New York, NY | Address

Phone No. | Phone No.

Approval Number 24-8199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 751
GROSS 47.14 T GROSS
TARE 13.56 T TARE
RECALLED
NET 33.58 T NET
LOG 67
10/24/2011 TONNAGE
03:13PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to Brigata | 10/24/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print) WASHINGTON

Address Hillside, NJ | Vehicle License No. / State / EPA No. AW584H

BA Trac | Truck Number #807

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent | Signature Corra | 10 24 11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3607

SOIL SAFE, INC.

Log Number 4824

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W26th St

New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number 84-1199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 342
GROSS 45.53 T
TARE 14.80 T
RECALLED
NET 30.73 T
LOG 68
10/24/2011
1:03:15PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to Shirley 10/24/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Luis

Vehicle License No. / State / EPA No. AM 216 H

Truck Number 85

I hereby certify that the above named material was picked up at the generator site listed above.

Luis 10/24/11

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Luis 10/24/11

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Conroy 10-24-11

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3 (0-2)

SOIL SAFE, INC.

Log Number 025

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Generator Site/Location SAME

Address 260 W 26th St

New York, NY

Address

Phone No.

Phone No. ID 107

Approval Number 24-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS 45.23 T
TARE 13.86 GROSS
RECALCED
NET 31.37 T TARE
LOG 69
10/24/2011 NET
03:18PM
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — 10/24/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMS Industries

Driver Name (Print) Saro

Address Hillside, NJ

Vehicle License No. / State / EPA No. AN 469F

Truck Number R25 FT 25

I hereby certify that the above named material was picked up at the generator site listed above.

10.24.11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10.24.11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Garcia — 10.24.11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-3057

SOIL SAFE, INC.

Log Number: D26

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name: Chelsea Green
Generator Site/Location: SAME
Address: 260 W26th St
New York, NY
Address:
Phone No.:
Phone No.:

Approval Number: 24-899

Description of Material:
Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

ID 591 GROSS
GROSS 44.60 T
TARE 14.69 T TARE
RECALLED
NET 29.91 T NET
LOG 73
10/24/2011 TONNAGE
03:28PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent for Chelsea Green — Signature — 10/24/11
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name: AMS Industries
Driver Name (Print): Paul
Address: Hillside, NJ
Vehicle License No. / State / EPA No.: AM8400
Truck Number: Shorley 20

I hereby certify that the above named material was picked up at the generator site listed above.

Paul 10/24/11
Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Paul 10/24/11
Driver Signature — Delivery Date

DESTINATION

Site Name: **Soil Safe, Inc. - Bridgeport** Phone No.: **1-856-467-8030**

Address: **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia 10-24-11
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3007

SOIL SAFE, INC.

Log Number 089

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Cotton

Address 260 W26th St
New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number CH-3194

Description of Material

Non-Regulated Petroleum
Contaminated Soil

Non DOT/RCRA Regulated

ID 405
GROSS 46.73 T GROSS
TARE 14.21 T TARE
RECALLED
NET 32.52 T NET
LOG 74
10/24/2011 TONNAGE
08:32PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS Agent to Cotton 10/24/11
Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Leonardo Solano

Vehicle License No. / State / EPA No. AM 181 J

Truck Number 02

I hereby certify that the above named material was picked up at the generator site listed above.

10-24-11
Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-24-11
Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Cotton 10.24.11
Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4 (0-7)

Log Number 031

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Piers | Generator Site/Location SAME

Address 20 W 26th St | Address

New York, NY

Phone No. | Phone No.

Description of Material

Approval Number 24-4199

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 1087 **GROSS**

GROSS 50.21 T

TARE 14.47 T **TARE**

RECALLED

NET 35.74 T **NET**

LOG 75

10/24/2011 **TONNAGE**

11:34PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Gus ocall to Generate BATAL 806 | 10/24/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMS Industries | Driver Name (Print) ANT PAIVA

Address Hillside, NJ | Vehicle License No. / State / EPA No. AN533H

Truck Number 1087 806

I hereby certify that the above named material was picked up at the generator site listed above.

10/24/11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/24/11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130, Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Coach 10.24.11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3 (10-7)

SOIL SAFE, INC.

Log Number 028

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 26th St
New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number
CU-9199

Description of Material

Non-Regulated Petroleum
Contaminated Soil

Non DOT/RCRA Regulated

ID 766
GROSS 47.11 T GROSS
TARE 13.61 T TARE
RECALLED
NET 33.50 T NET
LOG 76
10/24/2011
03:36PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

US Vest for Generator — 10/24/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Julio Garcia

Vehicle License No. / State / EPA No. AN1194

Truck Number Bottom Box

I hereby certify that the above named material was picked up at the generator site listed above.

10/24/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/24/11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia — 10-24-11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-40-2

SOIL SAFE, INC.

Log Number 030

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Generator Site/Location SAME

Address 260 W 26th St

New York, NY

Address

Phone No.

Phone No.

Approval Number 421-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 589
GROSS 43.01 T GROSS
TARE 14.91 T TARE
RECALLED
NET 28.10 T NET
LOG 77
10/24/2011
03:38PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

GS Agent for Generator — 10/24/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Driver Name (Print) Carlos

Address Hillside, NJ

Vehicle License No. / State / EPA No. AM10T

Truck Number Shirley 06

I hereby certify that the above named material was picked up at the generator site listed above.

10-24-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-24-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

10-24-11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-24 (05-07)

SOIL SAFE, INC.

Log Number 032

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Garden Generator Site/Location SAME

Address 260 W26th St Address

New York, NY

Phone No. Phone No.

Description of Material

Approval Number 24-0199

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 747
GROSS 44.26 T
TARE 14.68 T
RECALLED
NET 29.58 T
LOG 79
10/24/2011
04:11PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

GS agent for Chelsea Garden 10/24/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name AMG Industries Driver Name (Print) Bayron Martinez

Address Hillside, NJ Vehicle License No. / State / EPA No. AN199L NJ

Queens, NY Truck Number 04 747

I hereby certify that the above named material was picked up at the generator site listed above.

10-23-11

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-23-11

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Garcia 10/24/11

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4 (07)
TP-3 (07)

Log Number 003

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location SAME

Address 260 W25th St | Address

New York, NY

Phone No. | Phone No.

Approval Number 24-8149

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 865
GROSS 45.97 T GROSS
TARE 12.68 T TARE
RECALLED
NET 33.29 T NET
LOG 6
10/25/2011 TONNAGE
09:57AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS Agent for Chelsea Green — 10/25/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMS Industries | Driver Name (Print) Kilpatrick

Address Hillside, NJ | Vehicle License No. / State / EPA No. ML939V

Truck Number 603 CS # 865

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature | Shipment Date 10-25-11

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature | Delivery Date 10-25-11

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

A. Garcia — 10-25-11

Name of Authorized Agent | Signature | Receipt Date

White - Facility | Green - Facility | Yellow - Generator | Pink - Broker | Goldenrod - Contractor | Blue - Trucking Co.

TP-1 (0-7)
TP-3 (0-7)

Log Number 001

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green Generator Site/Location SAME

Address 260 W 26th St Address

New York, NY

Phone No. Phone No.

Approval Number 24-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

10 TSB

GROSS	45.56 T	GROSS
TARE	14.09 T	TARE
RECALLED NET	31.47 T	NET
LOG 7 10/25/2011 09:58AM		TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent for Chelsea Green 10/25/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name AMG Industries Driver Name (Print) Carlos Prato

Address Hillside, NJ Vehicle License No. / State / EPA No.

Truck Number 25

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM, 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Colon 10 25 11

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3 (0-2)
TP-1 (0-2)

Log Number 004

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location SAME

Address 260 W 25th St, New York, NY | Address

Phone No. | Phone No.

Approval Number 04-8179

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 107
GROSS 44.14 T
TARE 13.86 T
RECALLED
NET 30.28 T
LOG 8
10/25/2011
10:18AM

GROSS / TARE / NET / TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

CAS Agent to sign for Generator | 10/25/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMB Industries | Driver Name (Print) JARED

Address Hillside, NJ | Vehicle License No. / State / EPA No. AN969F

Truck Number ECS # 38

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature | 10-25-11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature | 10-25-11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent | J Carlin Signature | 10 25 11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-1 (0-2)
TP-3 (0-2)

Log Number 0002

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green
Address 260 W 26th St
New York, NY
Phone No.

Generator Site/Location SAME
Address
Phone No.

Approval Number 24-1199

Description of Material
Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

ID 342
GROSS 47.79 T GROSS
TARE 13.52 T TARE
RECALLED
NET 34.27 T NET
LOG 9
10/25/2011
10:20AM
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

OS agent to generator — 10/25/11
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Shirley AMG Industries
Address Hillside, NJ
Driver Name (Print) Luis.
Vehicle License No. / State / EPA No. AN316N
Truck Number 05

I hereby certify that the above named material was picked up at the generator site listed above.
Luis — 10/25/11
Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.
Luis — 10/25/11
Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**
Address **378 Route 130 Logan Township, NJ 08085**
No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 10 25 11
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-1 (0-2')
TP-3 (0-2')

Log Number 005

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green
Address 260 W26th St
New York, NY
Phone No.

Generator Site/Location Same
Address
Phone No.

Approval Number 9-2/09

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 593
GROSS 44.94 GROSS
TARE 14.31 T
RECALLED TARE
NET 11 30.63 T NET
LOG
10/25/2011
10:24AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 10/25/11
Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name AMG Industries
Address Hillside, NJ
Driver Name (Print) Benjamin Pierro
Vehicle License No. / State / EPA No. AN109E
Truck Number 18

I hereby certify that the above named material was picked up at the generator site listed above.
Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.
Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**
Address **378 Route 130 Logan Township, NJ 08085**
No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 10/25/11
Name of Authorized Agent / Signature / Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-1 (0-2)
TP-3 (0-2)

Log Number 006

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name: Chelsea Green | Generator Site/Location: SAME

Address: 260 W26th St, New York, NY | Address:

Phone No. | Phone No.

Approval Number: 01-8199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 647
GROSS 44.55 T GROSS
TARE 14.48 T TARE
RECALCLED
NET 30.07 T NET
LOG 12
10/25/2011 TONNAGE
10:28AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Chelsea Green Generator | Signature | 10/25/11
Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name: AMG Industries | Driver Name (Print): Mario Velarde

Address: Hillside, NJ | Vehicle License No. / State / EPA No.: AN931F

Truck Number: 16

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature | 10/25/11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature | 10/25/11 Delivery Date

DESTINATION

Site Name: **Soil Safe, Inc. - Bridgeport** | Phone No.: **1-856-467-8030**

Address: **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia | 10/25/11
Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-9 (0-1)
TP-3 (0-2)

Log Number 010

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Glen | Generator Site/Location SAME

Address 260 W26th St, New York, NY | Address

Phone No. | Phone No.

ID 10827

Approval Number 24-8199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

GROSS 44.00 T
TARE 14.47 T
RECALLED
NET 29.53 T
LOG 14
10/25/2011
10:32AM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

US ASPH Corporate | 10/25/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

CATTAC

Transporter Name AMG Industries | Driver Name (Print) ANTONIO

Address Hillside, NJ | Vehicle License No. / State / EPA No. AM-8834

Truck Number 1087 806

I hereby certify that the above named material was picked up at the generator site listed above.

10/25/11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/25/11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Cancia | 10 25 11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4(0-7)

SOIL SAFE, INC.

Log Number 007

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Carrier | Generator Site/Location SAME

Address 260 W26th St, New York, NY | Address

Phone No. | Phone No.

Approval Number Cy-8149

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 589
GROSS 46.76 T — GROSS
TARE 13.39 T — TARE
RECALLED
NET 33.37 T — NET
LOG IS
10/25/2011 — TONNAGE
10:34AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — Signature — 10/25/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Trucking | Driver Name (Print) Carlos

Address Hillside, NJ | Vehicle License No. / State / EPA No. AM110T

Truck Number Shirley 06

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 10-25-11 — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 10-25-11 — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Carlos — Signature — 10 25 11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-460-21

Log Number 029

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green — Generator Site/Location SAME

Address 260 W26th St — Address

New York, NY

Phone No. — Phone No.

Approval Number 24-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 749

GROSS	49.30 T	GROSS
TARE	12.71 T	TARE
RECALLED		
NET	36.59 T	NET
LOG 16		
10/25/2011 10:36AM		TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

QS Grot to generate — 10/25/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries — Driver Name (Print) Ramiro V

Address Hillside, NJ — Vehicle License No. / State / EPA No. C72524

Truck Number 09

I hereby certify that the above named material was picked up at the generator site listed above.

Ramiro V — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Ramiro V — 10 25 11

Driver Signature — Shipment Date — Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** — Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

A Garcia — 10 25 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4(07)

SOIL SAFE, INC.

Log Number 008

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 20 W26th St

New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number 24-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 845
GROSS 48.26 GROSS
TARE 14.52 T
REGALLED TARE
NET 33.74 T
LOG 17 NET
10/25/2011
10:37AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — 10/25/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Robinson Velarde

Vehicle License No. / State / EPA No. AM3982

Truck Number 9

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 10-25-11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 10-25-11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 10 25-11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-1 (0-7)
TA-3 (0-7)

Log Number 012

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 26th St
New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No. ID 405

Description of Material

Approval Number 24-8199

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS 13.30 T
TARE 13.68 GROSS
RECALLED 29.62 TARE
NET 19 NET
LOG
10/25/2011
10:56AM
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Agent to Gonzalez — 10/25/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Leonardo Santos

Vehicle License No. / State / EPA No. AM181J

Truck Number 02

I hereby certify that the above named material was picked up at the generator site listed above.

10-25-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-25-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

A. Garcia — 10 25 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-400

SOIL SAFE, INC.

Log Number: 013

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name: Chelsea Green
Address: 260 W 26th St
New York, NY
Phone No.:

Generator Site/Location: SAME
Address:
Phone No.:

Approval Number: 04-3199

Description of Material:
Non-Regulated Petroleum
Contaminated Soil
Non DOT/RCRA Regulated

ID 680
GROSS 49.23 T GROSS
TARE 13.69 T TARE
RECALLED
NET 35.54 T NET
LOG 20
10/25/2011
11:02AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

A.S. Gabel transportation — 10/25/11
Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name: AMG Industries
Address: Hillside, NJ
Driver Name (Print): Walton W
Vehicle License No. / State / EPA No.: AM331D
Truck Number: 401

I hereby certify that the above named material was picked up at the generator site listed above.
Driver Signature / Shipment Date: 10/25/11

I hereby certify that the above named material was delivered without incident to the destination listed below.
Driver Signature / Delivery Date: 10/25/11

DESTINATION

Site Name: **Soil Safe, Inc. - Bridgeport** Phone No.: **1-856-467-8030**
Address: **378 Route 130 Logan Township, NJ 08085**
No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 10/25/11
Name of Authorized Agent / Signature / Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co

TP-4C0-7

SOIL SAFE, INC.

Log Number 015

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location SAME

Address 260 W26th St | Address

New York, NY

Phone No. | Phone No.

Approval Number C4-8-19

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

10 1015

GROSS	51.37	GROSS
TARE	13.50 T	
RECEIVED		TARE
NET	37.87 T	
LOG 21		NET
10/25/2011		
11 *06AM		TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Gregory Cooper | 10/25/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print) Jose

Address Hillside, NJ | Vehicle License No. / State / EPA No. AM1441C

Truck Number #3

I hereby certify that the above named material was picked up at the generator site listed above.

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature | Shipment Date | Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Cooper | 10 25 11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3 (0-2)
TP-1 (0-7)

Log Number 014

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name: Chelsea Green — Generator Site/Location: SAME

Address: 260 W 26th St, New York, NY — Address:

Phone No. — Phone No.

Approval Number: 20-8199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 515
GROSS 42.14 T GROSS
TARE 12.99 TARE
RECALLED
NET 29.15 T NET
LOG 22
10/25/2011 TONNAGE
11:10AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

GC agent to generate — 10/25/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name: AMG Industries — Driver Name (Print): Oscar

Address: Hillside, NJ — Vehicle License No. / State / EPA No.: AM5365

Truck Number: 515

I hereby certify that the above named material was picked up at the generator site listed above.

10/25/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/25/11

Driver Signature — Delivery Date

DESTINATION

Site Name: **Soil Safe, Inc. - Bridgeport** — Phone No.: **1-856-467-8030**

Address: **378 Route 130, Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 10 25 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TPH (607)

SOIL SAFE, INC.

Log Number 011

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 25th St
New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number
EW-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

10 265
GROSS 50.64 GROSS
TARE 13.39 T
RECALLED
NET 37.25 T TARE
LOG 23
10/25/2011 NET
11:16AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

CLS agent for Generator — 10/25/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Julio Barrelos

Vehicle License No. / State / EPA No. AN114A

Truck Number Bottalo 604

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date 10/25/11

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date 10/25/11

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — Receipt Date 10-25-11

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-9(07)
TP-30(07)

Log Number 018

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green
Address 260 West 26th St
New York, NY
Phone No.

Generator Site/Location SAME
Address
Phone No.

Approval Number 24-2179

Description of Material
Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

ID 591
GROSS 46.24 T GROSS
TARE 13.40 T TARE
RECALLED
NET 32.84 T NET
LOG 25
10/25/2011 TONNAGE
11:25AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

CAS Agent to Generator — 10/25/11
Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name AMG Industries
Address Hillside, NJ
Driver Name (Print) Paul
Vehicle License No. / State / EPA No. AN890D
Truck Number 5 Heavy 20

I hereby certify that the above named material was picked up at the generator site listed above.
Paul 10-25-11
Driver Signature / Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.
Paul 10-25-11
Driver Signature / Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**
Address **378 Route 130 Logan Township, NJ 08085**
No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.
J. Garcia 10 25 11
Name of Authorized Agent / Signature / Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-1 [0-7]
TP-3 [0-7]

Log Number 6/6

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name: Chelsea Green
Address: 260 W 26th St
New York, NY
Phone No.:

Generator Site/Location: SAME
Address:
Phone No.:

Approval Number: 24-8199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID T48
GROSS 45.22 T — GROSS
TARE 12.89 T — TARE
RECALLED
NET 33.33 T — NET
LOG 26
10/25/2011
11:27AM — TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

OS clean to generator — Signature — 10/25/11
Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name: AMG Industries
Address: Hillside, NJ
Driver Name (Print): Tommy
Vehicle License No. / State / EPA No.: AW916A NJ
Truck Number: 11 Diesel #02 NJ 847

I hereby certify that the above named material was picked up at the generator site listed above.
Driver Signature — 10/25/11 — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.
Driver Signature — 10/25/11 — Delivery Date

DESTINATION

Site Name: **Soil Safe, Inc. - Bridgeport** Phone No.: **1-856-467-8030**
Address: **378 Route 130 Logan Township, NJ 08085**
No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature (Garau) — 10 25 11 — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-1 (07)
TP-3 (07)

Log Number 017

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name: Chelsea Green
Address: 260 W26th St
New York, NY
Phone No.:

Generator Site/Location: SAME
Address:
Phone No.: 10 7901

Approval Number: 24-3199

Description of Material:
Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

GROSS 47.92 T
TARE 13.99 T
RECALLED
NET 33.93 T
LOG 27
10/25/2011
11:31AM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Generator Authorized Agent Name: [illegible] Signature: [signature] Shipment Date: 10/25/11

TRANSPORTER

Transporter Name: AMG Industries
Address: Hillside, NJ
Driver Name (Print): JR
Vehicle License No. / State / EPA No.: NJ AL5586
Truck Number: T-3 Soil Safe #7

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature: [signature] Shipment Date:

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature: [signature] Delivery Date:

DESTINATION

Site Name: **Soil Safe, Inc. - Bridgeport** Phone No.: **1-856-467-8030**

Address: **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent: J. Garcia Signature: [signature] Receipt Date: 10-25-11

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co

TP-1 (0-7)
TP-3 (0-7)

SOIL SAFE, INC.

Log Number 019

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location SAME

Address 260 W 26th St, New York, NY | Address

Phone No. | Phone No.

Approval Number 24-8199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 747
GROSS 44.48 T GROSS
TARE 14.68 T TARE
RECALLED
NET 29.80 T NET
LOG 33
10/25/2011 TONNAGE
11:46AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 10/25/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print) Byron Martinez

Address Hillside, NJ 2nd 25 | Vehicle License No. / State / EPA No. AM92 N.J.

Truck Number 05 - 750

I hereby certify that the above named material was picked up at the generator site listed above.

10-25-11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-25-11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Corcia — 10 25 11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co

TP-3 (0-7)

SOIL SAFE, INC.

Log Number 022

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 26th St NY, NY

Phone No.

Generator Site/Location Same

Address

Phone No.

Approval Number 04-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 758
GROSS 43.58 T
TARE 14.09 T
RECALLED
NET 29.49 T
LOG 44
10/25/2011
02:09PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 10/25/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Logistics

Address Hillside, NJ Bayonne

Driver Name (Print) Carlos P

Vehicle License No. / State / EPA No. AK7UK

Truck Number 825 (758)

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date 10/25/11

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date 10/25/11

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature Gaycia — Receipt Date 10 25 11

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TPHs (0-2)

SOIL SAFE, INC.

Log Number 020

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W26th St
New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number 24-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 751

GROSS	48.31 T	GROSS
TARE	13.56 T	TARE
RECALLED		
NET	34.75 T	NET
LOG 45		TONNAGE
10/25/2011 @ 1946 PM		

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

GS agent to complete — 10/25/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name APG Industries

Address Hillside, NJ
07205

Driver Name (Print) WASHINGTON

Vehicle License No. / State / EPA No. NJ5644

Truck Number #607

I hereby certify that the above named material was picked up at the generator site listed above.

10/25/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/25/11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia — 10 25 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-307

SOIL SAFE, INC.

Log Number 8211

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 250 W 26th St NY, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number CY-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 791

GROSS 42.57 T GROSS

TARE 13.08 T TARE

RECALLED

NET 29.49 T NET

LOG 46

10/25/2011 12:49PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator 10/25/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillsdale, Alloway NJ

Driver Name (Print)

Vehicle License No. / State / EPA No. AW 113A

Truck Number 202

I hereby certify that the above named material was picked up at the generator site listed above.

10/25/11

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/25/11

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia 10.25.11

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4 (07)

Log Number 025

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 39th St NY, NY

Phone No.

Generator Site/Location Same

Address

Phone No. ID 647

GROSS 44.52 T
TARE 14.48 T
RECALLED
NET 30.04 T
LOG 48
10/25/2011
03:01PM

GROSS
TARE
NET
TONNAGE

Approval Number 4-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 10/25/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Marco Velarde

Vehicle License No. / State / EPA No. AH931F

Truck Number 16

I hereby certify that the above named material was picked up at the generator site listed above.

10/25/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/25/11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Garcia — 10 25 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-307

SOIL SAFE, INC.

Log Number 024

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location Same

Address 260 W 26th St NY, NY | Address

Phone No. | Phone No.

ID 342
GROSS 45.38 T GROSS
TARE 13.52 T TARE
RECALLED
NET 31.86 T NET
LOG #9
10/25/2011
08:04PM TONNAGE

Approval Number 04-8199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator | Signature | 10/25/11

Generator Authorized Agent Name | Shipment Date

TRANSPORTER

Transporter Name Shirley AMB Industries | Driver Name (Print) Luis

Address Hillside, NJ | Vehicle License No. / State / EPA No. AN 316 H

Truck Number 05

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature | 10/25/11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature | 10/25/11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia | 10 25 11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4(0-2)

SOIL SAFE, INC.

Log Number 023

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 26th St NY, NY

Phone No.

Generator Site/Location Same

Address

Phone No.

ID 107

Approval Number CH-819

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS 58.21 T
TARE 19.86 T
RECALLED
NET 38.35 T
LOG CO
10/25/2011
13:06PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator 10/25/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) JNIDO

Vehicle License No. / State / EPA No. AN969A

Truck Number R-45 FF38

I hereby certify that the above named material was picked up at the generator site listed above.

10-25-11

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-25-11

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia 10-25-11

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4(0-2)

SOIL SAFE, INC.

Log Number 027

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 26th St NY, NY

Phone No.

Generator Site/Location Same

Address

Phone No.

Approval Number 04-8999

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

111 BBS

GROSS 43.20 T GROSS
TARE 12.68 T
RECALLED
NET 36.52 T TARE
NET
LOG 51
10/25/2011
08:08PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — 10/25/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name ACM Industries

Address Hillside, NJ

Driver Name (Print) Klaassen

Vehicle License No. / State / EPA No. AC 933V

Truck Number 803 # 554 865

I hereby certify that the above named material was picked up at the generator site listed above.

10-25-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-25-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Ecrio — 10 25 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-360-07

SOIL SAFE, INC.

Log Number: 026

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name: Chelsea Green
Address: 260 West 26th St
NY, NY
Phone No.:

Generator Site/Location: Same
Address:
Phone No.:

Approval Number: C4-8199

Description of Material: Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

ID 583
GROSS 45.92 GROSS
TARE 14.31 T
RECALLED TARE
NET 31.61 T NET
LOG 52
10/25/2011
03:10PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 10/25/11
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name: AME Industries
Address: Hillside, NJ
Driver Name (Print): Benjamin Rivera
Vehicle License No. / State / EPA No.: AN/09E
Truck Number: 18

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date

DESTINATION

Site Name: **Soil Safe, Inc. - Bridgeport** Phone No.: **1-856-467-8030**

Address: **378 Route 130, Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Gary Cia — 10 25 11
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3007

Log Number 028

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 26th St NY, NY

Phone No.

Generator Site/Location

Address Same

Phone No.

Approval Number 124-2199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 589
GROSS 46.87 T GROSS
TARE 13.39 T TARE
RECALLED
NET 33.48 T NET
LOG 53
10/25/2011 TONNAGE
03:21PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 10/25/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Hauling — Driver Name (Print) Carlos

Address Hillside, NJ — Vehicle License No. / State / EPA No. AM110T

Truck Number Shirley 06

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 10-25-11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 10-25-11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — 10-25-11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4 (0-7)

SOIL SAFE, INC.

Log Number 089

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 26th St
New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number
24-8/99

Description of Material

Non-Regulated Petroleum
Contaminated Soil

Non DOT/RCRA Regulated

ID 646
GROSS 49.18 T
TARE 14.52 T
RECALLED
NET 34.66 T
LOG 54
10/25/2011
08:24PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 10/25/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMS Industries

Address Hillside, NJ

Driver Name (Print) Robinson Eduardo

Vehicle License No. / State / EPA No. AJM3952

Truck Number 4

I hereby certify that the above named material was picked up at the generator site listed above.

Robinson — 10-25-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-25-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Conroy — 10 25 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3007

SOIL SAFE, INC.

Log Number 031

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W26th St
New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No. ID 765

Approval Number C4-2199

Description of Material

Non-Regulated Petroleum
Contaminated Soil

Non DOT/RCRA Regulated

GROSS 46.24 T
TARE 13.39
RECALLED
NET 32.85 T
LOG 55
10/25/2011
03:40PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 10/25/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Juan Borrelos

Vehicle License No. / State / EPA No. AW1164

Truck Number Bobtail 806

I hereby certify that the above named material was picked up at the generator site listed above.

10/25/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/25/11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia — 10 25 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-360-7

SOIL SAFE, INC.

Log Number 6030

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Generator Site/Location SAME

Address 260 West 26th St
New York, NY

Address

Phone No.

Phone No.

Approval Number 24-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

10 406
GROSS 46.43 T GROSS
TARE 13.68 T
RECALLED TARE
NET 32.75 T NET
LOG 56
10/25/2011
03:42PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator 10/25/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Driver Name (Print) Leonardo Sacros

Address Hillside, NJ

Vehicle License No. / State / EPA No. AM 131 J

Truck Number 02

I hereby certify that the above named material was picked up at the generator site listed above.

10-25-11

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-25-11

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent Signature 10 25 11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4007

SOIL SAFE, INC.

Log Number 032

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Generator Site/Location SAME

Address 260 W26th St

New York, NY

Address

Phone No.

Phone No. ID 591

Description of Material

Approval Number 14-8149

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS 46.07 T
TARE 13.40
RECALLED
NET 32.67 T

LOG 57
10/25/2011
04:00PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 10/25/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Driver Name (Print) Paul

Address Hillside, NJ

Vehicle License No. / State / EPA No. AN 890 D

Truck Number Shorty 20

I hereby certify that the above named material was picked up at the generator site listed above.

Paul 10-25-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Paul 10-25-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Curtis 10 25 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4(0-7)

SOIL SAFE, INC.

Log Number 034

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W26th St
New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number CGH-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

— Non DOT/RCRA Regulated

11 790
GROSS 49.03 GROSS
TARE 13.99 T
RECALLED
NET 35.04 T TARE
LOG 56 NET
10/25/2011
04:30PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — 10/25/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hibbing, MN

Driver Name (Print) SR

Vehicle License No. / State / EPA No. MN NC558

Truck Number #3 Soil Safe #790

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — 10.25.11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4(0-7)

SOIL SAFE, INC.

Log Number 033

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Generator Site/Location SAME

Address 260 W26th St

New York, NY

Address

Phone No.

Phone No.

Approval Number 04-3199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 740
GROSS 46.50 T GROSS
TARE 12.89 T TARE
RECALLED
NET 33.61 T NET
LOG 59
10/25/2011
04:35PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS agent to generator 10/25/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name MMG Industries

Driver Name (Print) Sammy

Address Hillside, NJ

Dawn

Vehicle License No. / State / EPA No. AJ946A NJ

Truck Number Dump Truck 2 S.S. #778

I hereby certify that the above named material was picked up at the generator site listed above.

10/25/11

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/25/11

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Carlos 10.25.11

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TF-4 (10-7)

SOIL SAFE, INC.

Log Number 035

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 26th St
New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number 24-799

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 747
GROSS 47.66 T GROSS
TARE 14.68 T TARE
RECALLED
NET 32.98 T NET
LOG 61
10/25/2011 TONNAGE
04:42PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 10/25/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillsdale, NJ
Dan

Driver Name (Print) Byron Martinez

Vehicle License No. / State / EPA No. A01 FRZ NJ

Truck Number 04-795

I hereby certify that the above named material was picked up at the generator site listed above.

10-25-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/25/11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Colon — 10.25.11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-6 (0-2)

SOIL SAFE, INC.

Log Number 001

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 360 W 26th St

NY, NY

Phone No.

Generator Site/Location Same

Address

Phone No.

ID 382

GROSS 13.68 GROSS
TARE 13.52 T
RECYCLED TARE
NET 30.16 T
LOG 3 NET
10/26/2011
1:19:57AM TONNAGE

Approval Number
24-3199

Description of Material

Non-Regulated Petroleum
Contaminated Soil

Non DOT/RCRA Regulated

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — 10/26/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries Shirley

Address Hillside, NJ

Driver Name (Print) Luis

Vehicle License No. / State / EPA No. A01316M

Truck Number 05

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 10/26/11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 10/26/11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130, Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia — 10-26-11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-6 (0-7)

SOIL SAFE, INC.

Log Number 002

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 280 W 26th St
NY, NY

Phone No.

Generator Site/Location Same

Address

Phone No.

Approval Number
C4-899

Description of Material

Non-Regulated Petroleum
Contaminated Soil

Non DOT/RCRA Regulated

ID 645
GROSS 45.29 T GROSS
TARE 14.52 T TARE
RECALCED
NET 30.77 T NET
LOG 4
10/28/2011
09:59AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 10/26/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Ames Industries

Address Hillside, NJ

Driver Name (Print) Dennis V

Vehicle License No. / State / EPA No. AM995Z

Truck Number 9

I hereby certify that the above named material was picked up at the generator site listed above.

Dennis — 10-26-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Dennis — 10-26-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 10 26 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-6(6-7)

SOIL SAFE, INC.

Log Number 003

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Grow | Generator Site/Location SAME

Address 260 W 26th St, New York, NY | Address

Phone No. | Phone No.

Approval Number 24-8199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 591
GROSS 42.97 T GROSS
TARE 13.40 T TARE
RECALLED
NET 29.57 T NET
LOG 9
10/26/2011
10:22AM
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator | 10/26/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print) Paul

Address Hillside, NJ | Vehicle License No. / State / EPA No. AM890A

Truck Number Shirley #20

I hereby certify that the above named material was picked up at the generator site listed above.

Paul 10/26/11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Paul 10/26/11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

D. Garcia 10 26 11

Name of Authorized Agent | Signature | Receipt Date

White - Facility | Green - Facility | Yellow - Generator | Pink - Broker | Goldenrod - Contractor | Blue - Trucking Co.

TP-5 (0-7)

SOIL SAFE, INC.

Log Number 004

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W26th St
New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number 24-2199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 749
GROSS 47.39 T GROSS
TARE 12.71 T TARE
RECALLED
NET 34.68 T NET
LOG ID
10/26/2011
10:26AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 10/26/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Romino Vali

Vehicle License No. / State / EPA No. C72524J

Truck Number 09

I hereby certify that the above named material was picked up at the generator site listed above.

Romino Vali 10 26 11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Romino Vali 10 26 11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Gaiol 10 26 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PRES (10-7)

SOIL SAFE, INC.

Log Number 005

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Generator Site/Location SAME

Address 260 W26th St

New York, NY

Address

Phone No.

Phone No.

Approval Number 24-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 508

GROSS 46.45 GROSS

TARE 13.39 T

RECALLED TARE

NET 33.07 T

LOG 16 NET

10/26/2011

10:45AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent for Generator — 10/26/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print)

Vehicle License No. / State / EPA No. 605

Truck Number Amilot

I hereby certify that the above named material was picked up at the generator site listed above.

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature | Shipment Date 10-26-11

Driver Signature | Delivery Date 10-26-11

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 10 26 11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-S(0-7)

SOIL SAFE, INC.

Log Number 006

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 26th NY NY

Phone No.

Generator Site/Location Same

Address

Phone No. ID 607

GROSS 45.12 T
TARE 12.91 T
RECALLED
NET 32.21 T
LOG 17
10/26/2011
10:47AM

GROSS
TARE
NET
TONNAGE

Approval Number CH-899

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 10/26/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Ame Industries

Address Wilson, NC

Driver Name (Print) Mario Velasco

Vehicle License No. / State / EPA No. AN93F

Truck Number 16

I hereby certify that the above named material was picked up at the generator site listed above.

10/26/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/26/11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

A Garcia — 10 26 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TPSC07

SOIL SAFE, INC.

Log Number 007

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location SAME

Address 260 West 25th NY, NY | Address

Phone No. | Phone No.

Approval Number C4-8819

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 865
GROSS 43.07 T GROSS
TARE 12.68 T TARE
RECALLED
NET 31.39 T NET
LOG 53
10/26/2011 TONNAGE
02:08PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator | 10/26/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AAA Industries | Driver Name (Print) Kuhlsen

Address Hillside, NJ | Vehicle License No. / State / EPA No. AL 4391

Truck Number 803 # CS# 165

I hereby certify that the above named material was picked up at the generator site listed above.

10-26-11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-26-11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Carlos | 10-26-11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-5(10-7)

SOIL SAFE, INC.

Log Number 008

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 250 W 26th St

NY, NY

Phone No.

Generator Site/Location Sand

Address

Phone No.

Approval Number 4-999

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 342
GROSS 45.08 T
TARE 13.52 T
RECALLED
NET 31.56 T
LOG 57
10/26/2011
02:57PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator

Generator Authorized Agent Name — Signature — 10/26/11 Shipment Date

TRANSPORTER

Shirley E.

Transporter Name Ams Industries

Address Hillside, NJ

Driver Name (Print) Luis

Vehicle License No. / State / EPA No. AN316W

Truck Number 05

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 10/25/11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 10/25/11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — 10.26.11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

FP-5(10-7)

SOIL SAFE, INC.

Log Number 609

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 36th St NY, NY

Phone No.

Generator Site/Location Same

Address

Phone No.

Approval Number BF-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 646
GROSS 48.12 T GROSS
TARE 14.52 T TARE
RECALCED
NET 33.60 T NET
LOG 58
10/25/2011 TONNAGE
02:59PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — Signature — 10/26/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, N.J.

Driver Name (Print) Penny V

Vehicle License No. / State / EPA No. AN395Z

Truck Number 9

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 10-26-11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 10-26-11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

A Garcia — 10 26 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-SC(0-7)

SOIL SAFE, INC.

Log Number 010

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green 8 | Generator Site/Location Same

Address 260 W 26th St NY, NY | Address

Phone No. | Phone No.

Approval Number 04-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 591
GROSS 47.02 T — GROSS
TARE 13.40 T — TARE
RECALLED
NET 33.62 T — NET
LOG 65
10/26/2011 — TONNAGE
03:25PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator | Signature | 10/26/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print) Paul

Address Hillside, NJ | Vehicle License No. / State / EPA No. AM/89 OR

Truck Number Shelby #20

I hereby certify that the above named material was picked up at the generator site listed above.

Paul 10-26-11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Paul 10-26-11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia 10 26 11

Name of Authorized Agent | Signature | Receipt Date

White - Facility | Green - Facility | Yellow - Generator | Pink - Broker | Goldenrod - Contractor | Blue - Trucking Co.

TR-5007

SOIL SAFE, INC.

Log Number 011

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green Generator Site/Location Same

Address 260 W 26th St Address

NY, NY

Phone No. Phone No.

Description of Material

Approval Number 24-8119

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 743
GROSS 50.36 T — GROSS
TARE 12.71 T — TARE
RECALLED
NET 37.65 T — NET
LOG 70
10/26/2011
08:37PM — TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator 10/26/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name AMG Industries Driver Name (Print) Ramiro D

Address Hillside, N.J. Vehicle License No. / State / EPA No. C 726 241

Truck Number 89

I hereby certify that the above named material was picked up at the generator site listed above.

Ramiro D 10 25 11

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Ramiro D 10 25 11

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Carlo 10 26 11

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-5(0-7)

SOIL SAFE, INC.

Log Number: 013

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name: Chelsea Green

Address: 250 W 26th St NY, NY

Phone No.:

Generator Site/Location: Same

Address:

Phone No.:

Approval Number: C4-299

Description of Material:

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

10 64 T
GROSS 44.10 T GROSS
TARE 14.48 T TARE
RECALLED
NET 29.62 T NET
LOG 73
10/26/2011
03:43PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 10/25/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name: AmG Industries

Address: Hillside, NJ

Driver Name (Print): Marco Velarde

Vehicle License No. / State / EPA No.: AN9317

Truck Number: 16

I hereby certify that the above named material was picked up at the generator site listed above.

10/25/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/25/11

Driver Signature — Delivery Date

DESTINATION

Site Name: **Soil Safe, Inc. - Bridgeport** Phone No.: **1-856-467-8030**

Address: **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 10-26-11

Agent — Signature — Receipt Date

White - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PSE&G TP-5 (8-3)

SOIL SAFE, INC.

Log Number 012

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 26th St NY, NY

Phone No.

Generator Site/Location Sam 2

Address

Phone No.

Approval Number 04-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 7514
GROSS 46.18 T
TARE 13.56 T
RECALLED
NET 32.62 T
LOG 75
10/26/2011
03:47PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent for Generator 10/26/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name Arm Industries

Address Hillside, NJ Bethel

Driver Name (Print) Washington

Vehicle License No. / State / EPA No. AV58F4

Truck Number #802

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature 10/26/11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent Signature 10/26/11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-560-71

SOIL SAFE, INC.

Log Number 014

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 26th St
NY, NY

Phone No.

Generator Site/Location Same

Address

Phone No.

Approval Number 04-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 1087
GROSS 45.43 T GROSS
TARE 14.47 T TARE
RECALLED
NET 30.96 T NET
LOG 76
10/26/2011 TONNAGE
03:51PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator BATTAL 10/26/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name Arro Industries

Address Hillsdale, NJ

Driver Name (Print) Auto Pavia

Vehicle License No. / State / EPA No. AN5854

Truck Number 1027 806

I hereby certify that the above named material was picked up at the generator site listed above.

10/26/11

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/26/11

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent Signature 10 26 11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-2 (0-7)

SOIL SAFE, INC.

Log Number 001

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W26th St

New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number 04-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 289

GROSS	48.27 T	GROSS
TARE	12.71 T	TARE
RECALLED		
NET	35.56 T	NET

LOG 1
10/20/2011
10:33AM

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 10/20/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Ramiro — 725 241

Vehicle License No. / State / EPA No.

Truck Number 509

I hereby certify that the above named material was picked up at the generator site listed above.

Ramiro

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Ramiro NJ 10 20 11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Carlos — 10 20 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-1 (0-7)
TP-2 (0-7)

Log Number 002

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location SAME

Address 260 W26th St | Address

New York, NY | NY NY 10001

Phone No. | Phone No.

Approval Number 24-8199

Description of Material

Non-Regulated Petroleum
Contaminated Soil

Non DOT/RCRA Regulated

10 TON
GROSS 41.98 GROSS
TARE 12.74 TARE
RECALLED
NET 29.24 NET
LOG 4
10/20/2011
11:04AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator | 10/

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print) Alan Rombosky

Address Hillside, NJ | Vehicle License No. / State / EPA No. C72340

Truck Number

I hereby certify that the above named material was picked up at the generator site listed above.

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature | Shipment Date | Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent | Signature | Receipt Date

White - Facility | Green - Facility | Yellow - Generator | Pink - Broker | Goldenrod - Contractor | Blue - Trucking Co.

TP-1(07)
TP-2(07)

SOIL SAFE, INC.

Log Number: 006

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name: Chelsea Green
Generator Site/Location: SAME
Address: 260 West 26th ST
New York, NY
Address:
Phone No.:
Phone No.:

Approval Number: 24-3149

Description of Material:
Non-Regulated Petroleum
Contaminated Soil
Non DOT/RCRA Regulated

10 SSID
GROSS 46.26 T GROSS
TARE 14.58 T TARE
RECALCED
NET 7 31.69 T NET
LOG 7
10/20/2011
11:23AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 10/20/11
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name: AMG Industries
Driver Name (Print): Fabian Velarde
Address: Hillside, NJ
Vehicle License No. / State / EPA No.: AN 934F
Truck Number: Sherly L2

I hereby certify that the above named material was picked up at the generator site listed above.

10-20-11
Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-20-11
Driver Signature — Delivery Date

DESTINATION

Site Name: **Soil Safe, Inc. - Bridgeport** Phone No.: **1-856-467-8030**

Address: **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Garcia — 10/20/11
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-1 (0-7)
TP-2 (0-7)

SOIL SAFE, INC.

Log Number 005

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green
Address 260 W 26th St
New York, NY
Phone No.

Generator Site/Location SAME
Address
Phone No.

Approval Number Ca-8199

Description of Material
Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

ID 342
GROSS 46.58 GROSS
TARE 14.80 T
RECALLED TARE
NET 31.78 T
LOG 8 NET
10/20/2011
11:23AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS AGENT TO generator 10/20/11
Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Shirley Types.
Transporter Name AMG Industries
Address Hillside, NJ

Driver Name (Print) Luis.
Vehicle License No. / State / EPA No. AH316N
Truck Number 05

I hereby certify that the above named material was picked up at the generator site listed above.
Driver Signature 10/20/11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.
Driver Signature 10/20/11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**
Address **378 Route 130 Logan Township, NJ 08085**
No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

L. Garcia 10-20-11
Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-1 (0-7)
TP-2 (0-7)

SOIL SAFE, INC.

Log Number 003

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location SAME

Address 260 W26th St, New York, NY | Address

Phone No. | Phone No.

Approval Number 24-6199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 647
GROSS 38.56 T GROSS
TARE 14.48 T TARE
RECYCLED
NET 24.08 T NET
LOG 9
10/20/2011 TONNAGE
11:46AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS AGENT TO GENERATOR — 10/20/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name Shirley Exp. AMG Industries | Driver Name (Print) Mario Velarde

Address Hillsboro, NJ | Vehicle License No. / State / EPA No. AN 931F NJ

Truck Number 16 647

I hereby certify that the above named material was picked up at the generator site listed above.

10/20/11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/24/11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

10/24/11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-1 (0-7)
TP-2 (0-7)

Log Number 604

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Carey | Generator Site/Location SAME

Address 260 W 26th St, New York, NY | Address

Phone No. | Phone No.

Approval Number 24-2199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 646
GROSS 43.37 T
TARE 14.52 T
RECALLED
NET 28.85 T
LOG 10
10/20/2011
11:48AM

GROSS / TARE / NET / TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator | Signature | 10/20/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print) Robinson Velosa

Address Hillside, NJ | Vehicle License No. / State / EPA No. AM3952

Truck Number 9

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature | 10-20-11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature | 10-20-11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia | 10.20.11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-1 (0-2)
TP-2 (0-2)

SOIL SAFE, INC.

Log Number 007

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green
Address 260 W26th St
New York, NY
Phone No.

Generator Site/Location SAME
Address
Phone No.

Approval Number: CY-8199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 591
GROSS 42.85 T
TARE 14.69 T
RECALLED
NET 28.16 T
LOG 12
10/20/2011 12:11PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent for Gordon — 10/20/11
Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name AMG Industries
Address Hillside, NJ

Driver Name (Print) Paul
Vehicle License No. / State / EPA No. AU890A
Truck Number 20

I hereby certify that the above named material was picked up at the generator site listed above.
Paul — 10-20-11
Driver Signature / Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.
Paul — 10-20-11
Driver Signature / Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

[illegible] Garcia — 10 20 11
Name of Authorized Agent / Signature / Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-1 (0-7)
TP-2 (0-7)

Log Number 009

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Grow | Generator Site/Location SAME

Address 260 W26th St | Address

New York, NY

Phone No. | Phone No.

Approval Number 14-2149

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID S15
GROSS 41.90 T GROSS
TARE 12.99 T TARE
RECALLED
NET 28.91 T NET
LOG 26
10/20/2011 TONNAGE
02:23PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to consolidate — 10/20/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name Tcran APEX Industries | Driver Name (Print) Dscane

Address Hillside, NJ | Vehicle License No. / State / EPA No. AM536E

Truck Number S15

I hereby certify that the above named material was picked up at the generator site listed above.

10/20/11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/20/11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 10/20/11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4 (0-2)
TP-5 (0-7)

Log Number 011

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green
Address 260 W26th St
New York, NY
Phone No.

Generator Site/Location SAME
Address
Phone No.

Approval Number C4-8199

Description of Material
Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

ID 1015
GROSS 48.01 GROSS
TARE 13.50 T
RECALLED TARE
NET 34.51 T
LOG 28 NET
10/20/2011
02:45PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS agent to generation — 10/20/11
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries
Address Hillside, NJ
Driver Name (Print) Jose
Vehicle License No. / State / EPA No. LM14WL
Truck Number #3

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garon — 10.20.11
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-1 (0-7)
TP-2 (0-7)

Log Number 010

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location SAME

Address 260 W 26th St, New York, NY | Address

Phone No. | Phone No.

Approval Number 64-7199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 6811

GROSS 39.26 T
TARE 13.69 T
RECALLED
NET 25.57 T
LOG 30
10/20/2011
12:57PM

GROSS / TARE / NET / TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator | 10/20/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print) WALTON

Address Hillside, NJ | Vehicle License No. / State / EPA No. AM 331D

Truck Number 401

I hereby certify that the above named material was picked up at the generator site listed above.

10/20/11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/20/11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Garcia | 10-20-11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-1 (0-7)
TP-2 (0-7)

Log Number 008

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location SHME

Address 260 W 26th St | Address

New York, NY

Phone No. | Phone No.

Approval Number 04-3109

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 406
GROSS 45.67 T — GROSS
TARE 14.21 T — TARE
RECALLED
NET 31.46 T — NET
LOG 32
10/20/2011
08:15PM — TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS agnt to generator — 10/20/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print) Leonardo Sosa-Ruiz

Address Hillside, NJ | Vehicle License No. / State / EPA No. AM 1PJ

Truck Number 02

I hereby certify that the above named material was picked up at the generator site listed above.

10-20-11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-20-11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Carlos — 10-20-11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-1 (07)
TP-2 (07)

Log Number 013

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green
Address 260 W26th St
New York, NY
Phone No.

Generator Site/Location SAME
Address
Phone No.

Approval Number 8199

Description of Material
Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

ID 704
GROSS 46.98 T
TARE 12.74 T
RECALLED
NET 34.24 T
LOG 34
10/20/2011
03:31PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 10/20/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries
Address Hillside, NJ

Driver Name (Print) Allan Ramdass
Vehicle License No. / State / EPA No. CTZ52WD
Truck Number 3-1

I hereby certify that the above named material was picked up at the generator site listed above.

10/20/11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/20/11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia — 10/20/11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-1 (0-3)
TP-2 (0-7)

Log Number 012

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name: Chelsea Green
Generator Site/Location: SAME
Address: 260 W26th Street
New York, NY
Address:
Phone No.:
Phone No.:

Approval Number: CH-8149

Description of Material:
Non-Regulated Petroleum
Contaminated Soil

Non DOT/RCRA Regulated

ID 749
GROSS 48.82 T GROSS
TARE 12.71 T TARE
RECALLED
NET 35 36.11 T NET
LOG
10/20/2011 TONNAGE
03:33PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

OS agent to generator — 10/20/11
Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name: AMG Industries
Driver Name (Print): Romulo N.
Address: Hillside, NJ
Vehicle License No. / State / EPA No.: CJ25241
Truck Number: 09

I hereby certify that the above named material was picked up at the generator site listed above.

Romulo N. 10-20-11
Driver Signature / Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Romulo N. 10 20 11
Driver Signature / Delivery Date

DESTINATION

Site Name: **Soil Safe, Inc. - Bridgeport** Phone No.: **1-856-467-8030**

Address: **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 10-20-11
Name of Authorized Agent / Signature / Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4 (0-2)
TP-3 (0-2)

Log Number 014

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location SAME

Address 260 W26th St | Address

New York, NY

Phone No. | Phone No. ID 590

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

Approval Number C4-5199

GROSS 49.75 T GROSS
TARE 14.58 TARE
RECALLED
NET 35.17 T NET
LOG 36
10/20/2011
04:16PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AC Agent to Generator | 10/20/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print) Fabian Ucelay

Address Hillside, NJ | Vehicle License No. / State / EPA No. AN934F

Truck Number Sherly - 12

I hereby certify that the above named material was picked up at the generator site listed above.

10-20-11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-20-11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

10 20 11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-1 (0-7)
TP-2 (0-7)

Log Number 10915

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green
Address 260 W26th St
New York, NY
Phone No.

Generator Site/Location SAME
Address
Phone No. ID 342

Approval Number CH-0199

Description of Material
Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

GROSS 49.03 T
TARE 14.80 T
RECALLED
NET 34.23 T
L0837
10/20/2011
04:19PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — 10/20/11
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries (Shirley)
Address Hillside, NJ
Driver Name (Print) Luis.
Vehicle License No. / State / EPA No. AM 316 14
Truck Number 05

I hereby certify that the above named material was picked up at the generator site listed above.
Driver Signature — 10/20/11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.
Driver Signature — 10/2011 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**
Address **378 Route 130 Logan Township, NJ 08085**
No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Cosco — 10/20/11
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-1 (0-2)
TP-2 (0-2)

Log Number 019

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green
Address 260 W26th St New York, NY
Phone No.

Generator Site/Location SAME
Address
Phone No.

Approval Number 04-8199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 645
GROSS 51.18 T GROSS
TARE 14.52 T TARE
RECALLED NET 36.66 T NET
LOG 10/20/2011 04:57PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

GS agnt to generator — 10/20/11
Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name AMG Industries
Address Hillside, NJ
Driver Name (Print) Rubinson Velarde
Vehicle License No. / State / EPA No. AMG
Truck Number 9

I hereby certify that the above named material was picked up at the generator site listed above.
10-20-11
Driver Signature / Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.
10-20-11
Driver Signature / Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**
Address **378 Route 130 Logan Township, NJ 08085**
No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent / Signature / Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-1 (0-7)
TR-2 (0-7)

Log Number 017

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chilson Group | Generator Site/Location SAME

Address 260 W 26th St
New York, NY | Address

Phone No. | Phone No.

Approval Number 04-6199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

10 SBS
GROSS 49.31 T GROSS
TARE 14.81 T TARE
RECALLED
NET 34.50 T NET
LOG 39
10/20/2011 TONNAGE
04:59PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS Agent to Walker | 10/20/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AWS Industries | Driver Name (Print) Carlos

Address Hillside, NJ | Vehicle License No. / State / EPA No. Ammo T

Truck Number 06 - Shirley

I hereby certify that the above named material was picked up at the generator site listed above.

10-20-11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-20-11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Gary Cio | 10 20 11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-1 (0-3)
TP-2 (0-3)

Log Number 018

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location SAME

Address 260 W 26th St, New York, NY | Address

Phone No. | Phone No.

Approval Number 24-8199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 647
GROSS 13:33 T GROSS
TARE 14:48 T TARE
RECALCED
NET 29.45 T NET
LOG 40
10/20/2011 TONNAGE
05:02PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

QS agent to generator | Signature | 10/20/11
Generator Authorized Agent Name | Shipment Date

TRANSPORTER

Transporter Name Shirley Exp AMG Industries | Driver Name (Print) Mario Velarde

Address Hillside, NJ | Vehicle License No. / State / EPA No. AM931F

Truck Number 16

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature | Shipment Date 10/20/11

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature | Delivery Date 10/20/11

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent | Signature | 10 20 11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-1 (0-2)
TP-2 (0-2)

Log Number 020

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green
Address 260 W26th St
New York, NY
Phone No.

Generator Site/Location SAME
Address
Phone No. ID 591

Description of Material

Approval Number 24-8199

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS 49.62 GROSS
TARE 14.69 TARE
RECEIVED
NET 34.93 NET
41
LOG
10/20/2011
08:22PM
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent for Generator — 10/20/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries
Address Hillside, NJ

Driver Name (Print) Paul
Vehicle License No. / State / EPA No. AN 8900
Truck Number Shirley 20

I hereby certify that the above named material was picked up at the generator site listed above.

Paul — 10-20-11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Paul — 10-20-11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia — 10.20.11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-1(07)
TR-2(07)

Log Number 002023

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

GROSS 49.56 T
TARE 13.28 T
RECALLED
NET SAME T

Generator Name Chelsea Green

Generator Site/Location SAME

Address 260 W 26th St
New York, NY

Address LOG 10/20/2011 05:43PM 36.28

Phone No.

Phone No.

ID 279
GROSS 21.34 GROSS
TARE 13.28 TARE
RECALLED
NET 8.06 NET
LOG 42
10/20/2011
05:42PM TONNAGE

Approval Number
04-899

Description of Material

Non-Regulated Petroleum
Contaminated Soil

Non DOT/RCRA Regulated

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Driver Name (Print) José Lopez

Address Hillside, NJ
Rosetta Stan. Trucking

Vehicle License No. / State / EPA No. AM3861

Truck Number

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature | Shipment Date 10-26-11

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature | Delivery Date 10-26-11

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent | Signature Carlos | Receipt Date 10 20 11

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-1 (0-7)
TP-2 (0-7)

Log Number 022

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green
Address 260 W 26th St
New York, NY
Phone No.

Generator Site/Location SAME
Address
Phone No.

Approval Number 24-8199

Description of Material
Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

ID 765
GROSS 50.20 T GROSS
TARE 13.61 T TARE
RECALLED
NET 1 36.59 T NET
LOG
10/21/2011
07:04AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Generator Authorized Agent Name [illegible] Signature 10/20/11 Shipment Date

TRANSPORTER

Transporter Name AMG Industries
Address Hillside, NJ

Driver Name (Print) Julio Barcelos
Vehicle License No. / State / EPA No. AM1164A
Truck Number Sole Trucking Trucking LLC Sole Trucking #3 765

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature Julio Barcelos Shipment Date 10/21/11

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature Delivery Date 10/21/11

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent Signature Receipt Date 10 21 11

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-1 (0-3')
TP-2 (0-7')

Log Number 021

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green
Address 260 W26th St
New York, NY
Phone No.

Generator Site/Location SAME
Address
Phone No.

Approval Number 24-049

Description of Material
Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

10 751
GROSS 46.75 T GROSS
TARE 13.56 T TARE
NET 33.19 T NET
LOG 0
10/21/2011 TONNAGE
07:09AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

GS Agent to sign for

Generator Authorized Agent Name — Signature — Shipment Date 10/21/11

TRANSPORTER

Transporter Name AMG Industries
Address Hillside, NJ 07205

Driver Name (Print) WASHING Jose Luis Sal
Vehicle License No. / State / EPA No. #309
Truck Number

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date 10/21/11

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date 10/21/11

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — Receipt Date 10/21/11

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-1(0-7)
TP-2(0-7)

SOIL SAFE, INC.

Log Number 101506

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location SAME

Address 260 W 26th St, New York, NY | Address

Phone No. | Phone No.

Approval Number 11-4199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 758 46.88 GROSS
GROSS 61.02 T
TARE 14.09 T TARE
RECALLED
NET 3 34.79 T NET
LOG
10/21/2011 TONNAGE
07:36AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

GS agent to Generator | 10/20/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print) Carlos Pinto

Address Hillside, NJ | Vehicle License No. / State / EPA No. AK776C

Bayonne, NJ | Truck Number # 753

I hereby certify that the above named material was picked up at the generator site listed above.

10/20/11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/21/11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130, Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Carlson | 10/21/11

Name of Authorized Agent | Signature | Receipt Date

White - Facility | Green - Facility | Yellow - Generator | Pink - Broker | Goldenrod - Contractor | Blue - Trucking Co.

Log Number 001

SOIL SAFE, INC.

TP 1 & 2

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Generator Site/Location SAME

Address 260 W 26th St

New York, NY

Address

Phone No.

Phone No.

Description of Material

Approval Number 04-2199

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

10 704
GROSS 14.83 GROSS
TARE 12.74 T
RECALLED TARE
NET 7 32.09 T NET
LOG 7
10/21/2011 TONNAGE
10:48AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Christine Kraak — Signature — 10/21/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Driver Name (Print) Alex Rodriguez

Address Hillside, NJ

Vehicle License No. / State / EPA No. L-725290

Truck Number 1

I hereby certify that the above named material was picked up at the generator site listed above.

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Shipment Date

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Corey Cox 10/21/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-1 (0-7)
TP-2 (0-7)

Log Number 003

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name: Chelsea Green
Address: 260 W26th St
New York, NY
Phone No.:

Generator Site/Location: SAME
Address:
Phone No.:

Approval Number: 24-8149

Description of Material:
Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

ID 598
GROSS 48.91 T GROSS
TARE 14.31 T TARE
RECYCLED
NET 34.60 T NET
LOG 9
10/21/2011
10:53AM
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent for generator — 10/21/11
Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name: AMG Industries
Address: Hillside, NJ
Driver Name (Print): Fabian Velez
Vehicle License No. / State / EPA No.: AN9347
Truck Number: Shorty 12 S90

I hereby certify that the above named material was picked up at the generator site listed above.
10-21-11
Driver Signature / Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.
10-21-11
Driver Signature / Delivery Date

DESTINATION

Site Name: **Soil Safe, Inc. - Bridgeport** Phone No.: **1-856-467-8030**
Address: **378 Route 130 Logan Township, NJ 08085**
No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Corcia — 10/21/11
Name of Authorized Agent / Signature / Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP 1 & 2 (0-7)

SOIL SAFE, INC.

Log Number 002

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location SAME

Address 260 W26th St, New York, NY | Address

Phone No. | Phone No.

Approval Number 24-3199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 593
GROSS 41.04 T GROSS
TARE 14.31 T TARE
RECALLED
NET 26.73 T NET
LOG 10
10/21/2011
10:56AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AC agent to generator | Signature | 10/21/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print)

Address Hillside, NJ | Vehicle License No. / State / EPA No.

Truck Number

I hereby certify that the above named material was picked up at the generator site listed above.

Signature 10/21/11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Signature 10/21/11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130, Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia 10 21 11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-1 (0-7)
TP-2 (0-7)

Log Number 004

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green
Address 260 W 26th St
New York, NY
Phone No.

Generator Site/Location SAME
Address
Phone No.

Approval Number 24-819

Description of Material
Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

ID 646
GROSS 46.84 T GROSS
TARE 14.52 T TARE
RECALLED
NET 32.32 T NET
LOG \\
10/21/2011
11:00AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

G.S. agent for generator — 10/21/11
Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name AMG Industries
Address Hillside, NJ
Driver Name (Print) Robinson Velez
Vehicle License No. / State / EPA No. AM39[illegible]
Truck Number 9

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature 10-21-11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature 10-21-11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia 10 21 11
Name of Authorized Agent / Signature / Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

FP-3902PS
TP-10-21-11
TP-410-7

Log Number 007

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location SAME

Address 260 W 26th St | Address

New York, NY

Phone No. | Phone No. 10 342

Description of Material

Approval Number 24-8199

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS 49.64 T GROSS
TARE 14.80 T TARE
RECALLED
NET 34.84 T NET
LOG 12
10/21/2011
11:01AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

GC agent to generate | 10/21/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Shirley

Transporter Name AMG Industries | Driver Name (Print) Luis

Address Hillside, NJ | Vehicle License No. / State / EPA No. AN316N

Truck Number 05

I hereby certify that the above named material was picked up at the generator site listed above.

Luis Velarde 10/21/11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Luis Velarde 10/21/11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130, Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia 10 21 11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3 (0-2)
TP-1 (0-7)

Log Number 005

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green
Address 260 W26th St
New York, NY
Phone No.

Generator Site/Location SAME
Address
Phone No.

Approval Number 8199

Description of Material
Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

ID 107
GROSS 50.76 GROSS
TARE 13.86 T TARE
RECALLED
NET 36.90 T NET
LOG 13
10/21/2011
11:07AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — 10/21/11
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries
Address Hillside, NJ
Driver Name (Print) JORGE TAPIA
Vehicle License No. / State / EPA No. AN7076 NJ
Truck Number 28

I hereby certify that the above named material was picked up at the generator site listed above.
10-21-11
Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.
10-21-11
Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**
Address **378 Route 130 Logan Township, NJ 08085**
No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia — 10 21 11
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-1°(7-14)

SOIL SAFE, INC.

Log Number 010

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location SAME

Address 260 W26th St, New York, NY | Address

Phone No. | Phone No.

Approval Number 14-8149

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 589
GROSS 47.96 T GROSS
TARE 14.91 T TARE
RECALLED
NET 33.05 T NET
LOD 17
10/21/2011 TONNAGE
11:20AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

C.S. agent approved | Signature | 10/21/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print) Carlos

Address Hillside, NJ | Vehicle License No. / State / EPA No. AM1107

Truck Number Shirley - 06

I hereby certify that the above named material was picked up at the generator site listed above.

10-21-11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-21-11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Corcia | 10 21 11

Name of Authorized Agent | Signature | Receipt Date

White - Facility | Green - Facility | Yellow - Generator | Pink - Broker | Goldenrod - Contractor | Blue - Trucking Co.

TP-4 (07)

SOIL SAFE, INC.

Log Number 009

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W26th St

New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number 24-JM

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 153
GROSS 42.93 GROSS
TARE 16.03 T
RECALLED TARE
NET 26.90 T NET
LOG ID
10/21/2011
11:22AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to Generator — 10/21/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Mark Longley

Vehicle License No. / State / EPA No. AM32

Truck Number #3

I hereby certify that the above named material was picked up at the generator site listed above.

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Shipment Date — Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-2 (8-10')

Log Number 0088

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W26th St
New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number 24-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 101
GROSS 41.21 GROSS
TARE 13.03 T
RECALLED TARE
NET 19 28.18 T NET
LOG
10/21/2011 TONNAGE
11:25AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent for generator — 10/21/11

Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Carlos Adams

Vehicle License No. / State / EPA No. AL8443 NJ

Truck Number #4 / 101

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date 10/21/11

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date 10/21/11

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — Receipt Date 10/21/11

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-1 (7-14)
TP-2 (7-14)

Log Number 011

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location SAME

Address 260 W26th St, New York, NY | Address

Phone No. | Phone No.

Approval Number 24-7199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 148
GROSS 44.58 T GROSS
TARE 14.94 T TARE
RECALLED
NET 29.64 T NET
LOG 20
10/21/2011 TONNAGE
11:28AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

DK agent to amount of | 10/21/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print) Sonny Fox

Address Hillside, NJ | Vehicle License No. / State / EPA No. AW 42D NJ

Truck Number T2/148

I hereby certify that the above named material was picked up at the generator site listed above.

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature | Shipment Date | Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130, Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia | 10-21-11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-1(7-14)
TP-2(7-14)

Log Number 012

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green
Address 260 W26th St
New York, NY
Phone No.

Generator Site/Location SAME
Address
Phone No. 10 591

Approval Number CU-8199

Description of Material
Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

GROSS 48.74 T
TARE 14.69 GROSS
RECALLED
NET 34.05 T TARE
LOG 21
10/21/2011 NET
11:31AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to Generator — 10/21/11
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries
Address Hillside, NJ

Driver Name (Print) Paul
Vehicle License No. / State / EPA No. AN 3904
Truck Number 20 Shirley

I hereby certify that the above named material was picked up at the generator site listed above.

Paul
Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Paul
Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia — 10 21 11
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4 (0-7)

Log Number 015

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 26th St
New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number 04-8194

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 748
GROSS 52.94 GROSS
TARE 12.89 T TARE
RECALCED
NET 40.05 T NET
LOG 24
10/21/2011
11:40AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — 10/21/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Soil #748

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Tomasz Sarna

Vehicle License No. / State / EPA No. AM 4164 NY

Truck Number DM33 #62 NJ 847

I hereby certify that the above named material was picked up at the generator site listed above.

10/21/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/21/11

Driver Signature — Delivery Date

DESTINATION

Site Name Soil Safe, Inc. - Bridgeport Phone No. 1-856-467-8030

Address 378 Route 130 Logan Township, NJ 08085

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia 10 21 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-1 (7-14)
TP-3 (7-14)

Log Number 014

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green
Address 260 W26th St
New York, NY
Phone No.

Generator Site/Location SAME
Address
Phone No.

Approval Number 541-8199

Description of Material
Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

ID 515
GROSS 46.61 T GROSS
TARE 12.99 T TARE
RECALLED
NET 33.62 T NET
LOG 26
10/21/2011
11:54:7AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent for Chelsea Green — 10/21/11
Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name AMG Industries
Address Hillside, NJ
Driver Name (Print) Ryan Johnson
Vehicle License No. / State / EPA No. PM536
Truck Number 515

I hereby certify that the above named material was picked up at the generator site listed above.
Driver Signature — Shipment Date 10/21/11

I hereby certify that the above named material was delivered without incident to the destination listed below.
Driver Signature — Delivery Date 10/21/11

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**
Address **378 Route 130 Logan Township, NJ 08085**
No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Coarse — 10/21/11
Name of Authorized Agent / Signature / Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TF-1(7-14)
TF-2(7-14)

SOIL SAFE, INC.

Log Number 013

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green
Address 260 W26th St
New York, NY
Phone No.

Generator Site/Location SAME
Address
Phone No.

Approval Number CH-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 1015
GROSS 52.76 GROSS
TARE 13.50 T
RECALLED TARE
NET 39.26 T NET
LOG 31
10/21/2011
12:00PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS Agent to Gergalow — 10/21/11
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries
Address Hillside, NJ
Driver Name (Print) Jake Jerton
Vehicle License No. / State / EPA No. BM 1446
Truck Number A3

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia — 10/21/11
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-9 (7-14)
TP-2 (7-14)

Log Number 016

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green
Address 260 West St
New York, NY
Phone No.

Generator Site/Location SAME
Address
Phone No.

Approval Number 24-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 680
GROSS 47.20 GROSS
TARE 13.69 T
RECALLED TARE
NET 33.51 T
LOG 32 NET
10/21/2011
12:02PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS a/m to agent to 10/21/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries
Address Hillside, NJ

Driver Name (Print) WALTON
Vehicle License No. / State / EPA No. AM33D
Truck Number FF 01

I hereby certify that the above named material was picked up at the generator site listed above.

10/21/11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/21/11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130, Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Gaylor 10/21/11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-2 (5-14)

SOIL SAFE, INC.

Log Number 017

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location SAME

Address 260 W26th St, New York, NY | Address

Phone No. | Phone No.

Approval Number 24-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 747
GROSS 46.75 T
TARE 14.68 T
RECALLED
NET 32.07 T
LOG 39
10/21/2011
12:40PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS agent to generator | 10/21/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print) Bayron Martinez

Address Hillside, NJ | Vehicle License No. / State / EPA No. AW99L NJ

Dan Os Materials | Truck Number 04 Dan Os Materials

I hereby certify that the above named material was picked up at the generator site listed above.

10-21-11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-21-11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130, Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Corcio | 10 21 11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 020

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W26th St
New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No. 111 7558

Description of Material

Approval Number 24-8199

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS 52.30 GROSS
TARE 14.09 TARE
RECALLED
NET 38.21 T NET
LOG 48
10/21/2011
12:09PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

OS agent to generator 10/21/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ
Lower Road

Driver Name (Print) Chris

Vehicle License No. / State / EPA No. K726K

Truck Number #759

I hereby certify that the above named material was picked up at the generator site listed above.

10/21/11

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/21/11

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Colleen 10-21-11

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TTRad (7-19)

Log Number 019

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location SAME

Address 260 W26th St, New York, NY | Address

Phone No. | Phone No.

Approval Number 24-8119

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 647
GROSS 50.40 T GROSS
TARE 14.48 T TARE
RECALLED
NET 35.92 T NET
LOG 470
10/21/2011
02:19PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to Gaetano Shirley Exp. | 10/21/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print) Marco DeLaVade

Address Hillside, NJ | Vehicle License No. / State / EPA No. AM931F

Truck Number 16

I hereby certify that the above named material was picked up at the generator site listed above.

10/21/11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/21/11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Conlon | 10-21-11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-207-14

Log Number 018

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W26th St
New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number 24-8199

Description of Material

Non-Regulated Petroleum
Contaminated Soil

Non DOT/RCRA Regulated

ID 763
GROSS 51.21
TARE 14.93
RECALLED
NET 36.28
LOG 49
10/21/2011
02:19PM

GROSS
T
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator

Generator Authorized Agent Name

Signature

10/21/11

Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Hernando Russ

Vehicle License No. / State / EPA No. AM232H

Truck Number 763

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature

Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature

Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport**

Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent

Signature

10/21/11

Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-2
(7-14)

Log Number 023

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 26th St
New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number 24-8149

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 266
GROSS 51.28 T
TARE 13.61 T
RECALLED
NET 37.67 T
LOAD 1
10/21/2011
03:10PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

QC agent to complete

Generator Authorized Agent Name

Signature

10/21/11

Shipment Date

766

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Julio Barcelos

Vehicle License No. / State / EPA No. AN114A

Truck Number Bob Burton Trucking

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature

10/21/11

Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature

10/21/11

Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport**

Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent

Signature

10/21/11

Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-2
(3-14)

SOIL SAFE, INC.

Log Number 021

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W26th St
New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number 04-8199

Description of Material

Non-Regulated Petroleum
Contaminated Soil

Non DOT/RCRA Regulated

ID 406
GROSS 51.87 T GROSS
TARE 14.21 T TARE
RECALLED
NET 37.66 T NET
LOG 52
10/21/2011 TONNAGE
03:14PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to operate 10/21/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Leonardo Santos

Vehicle License No. / State / EPA No. AZ 151J

Truck Number 02

I hereby certify that the above named material was picked up at the generator site listed above.

10-21-11

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-21-11

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent Signature 10 21 11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

FP-a (7-14)

SOIL SAFE, INC.

Log Number 024

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location SAME

Address 260 W26th St, New York, NY | Address

Phone No. | Phone No.

Approval Number 04-8199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

10 SOS
GROSS 51.47 T — GROSS
TARE 14.31 T — TARE
RECALLED
NET 37.16 T — NET
LOG
10/21/2011 — TONNAGE
11:30PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — Signature — 10/21/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print) Julian Velez

Address Hillside, NJ | Vehicle License No. / State / EPA No. CA N934F

Truck Number Shelly 02

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 10-21-11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 10-21-11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent | Signature | Receipt Date

White - Facility | Green - Facility | Yellow - Generator | Pink - Broker | Goldenrod - Contractor | Blue - Trucking Co.

TR-2-D-47

SOIL SAFE, INC.

Log Number 026

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 26th St
New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number
124-8199

Description of Material

Non-Regulated Petroleum
Contaminated Soil

Non DOT/RCRA Regulated

ID 342
GROSS 52.00 T GROSS
TARE 14.80 T TARE
RECALLED
NET 37.20 T NET
LOG 55
10/21/2011 TONNAGE
03:54PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS Agent for Generator — 10/21/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Shirley AMG Industries

Address Hillside, NJ

Driver Name (Print) Luis

Vehicle License No. / State / EPA No. AM 316 N

Truck Number 05

I hereby certify that the above named material was picked up at the generator site listed above.

L Velarde — 10/21/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

L Velarde — 10/21/11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Gallo — 10-21-11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4 (0-2)

SOIL SAFE, INC.

Log Number 025

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W26th St

New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number 24-8119

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 646
GROSS 52.66 T GROSS
TARE 14.52 T TARE
RECALLED
NET 38.14 T NET
LOG 56
10/21/2011 TONNAGE
03:57PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

QS agent to generator — 10/21/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AVMG Industries

Address Hillside, NJ

Driver Name (Print) Robinson Velez

Vehicle License No. / State / EPA No. AV9482

Truck Number 9

I hereby certify that the above named material was picked up at the generator site listed above.

10-21-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-21-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — 10-21-11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 0d

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 36th St
New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number 24-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 751
GROSS 49.36 T GROSS
TARE 13.56 T TARE
RECALCED
NET 35.80 T NET
LOG 57
10/21/2011 TONNAGE
10:04 10:04PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to Generator — 10/21/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ
07205

Driver Name (Print) WASHINGTON

Vehicle License No. / State / EPA No. AU584H

Truck Number 807

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date 10/21/11

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date 10/21/11

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — 10 21 11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-6 (0-2)

SOIL SAFE, INC.

Log Number 028

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 26th St
New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number 24-6199

Description of Material

Non-Regulated Petroleum
Contaminated Soil

Non DOT/RCRA Regulated

ID 589
GROSS 51.62 T
TARE 14.91 T
RECALLED
NET 36.71 T
LOG 59
10/21/2011
04:15PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 10/21/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Carlos

Vehicle License No. / State / EPA No. Am110T

Truck Number Shirley - 06

I hereby certify that the above named material was picked up at the generator site listed above.

10-21-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-21-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Conner

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-6
(0-7)

Log Number 030

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 360 W 36 St
NY, NY

Phone No.

Generator Site/Location

Address Same

Phone No. 10 748

GROSS 50.78 T
TARE 12.89 GROSS
RECALLED
NET 37.89 TARE
LOG 63
10/21/2011 NET
04:26PM
TONNAGE

Approval Number C4-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

I as agent to generator — 10/21/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Tommy S

Vehicle License No. / State / EPA No. AM4164 NJ
Sci C2-748 DM05402

Truck Number

I hereby certify that the above named material was picked up at the generator site listed above.

10/21/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/21/11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Garcia — 10 21 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3 (0-2)
TP-1 (0-2)

SOIL SAFE, INC.

Log Number 006

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green
Generator Site/Location SAME
Address 260 W 26th St
New York, NY
Address
Phone No.
Phone No.

Approval Number 8190

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 743
GROSS 52.84 T GROSS
TARE 12.71 T TARE
RECALLED
NET 40.13 T NET
LOG 64
10/21/2011
04:29PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Agent to Generator — 10/21/11
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries
Driver Name (Print) Ramiro D
Address Hilda, NJ
Vehicle License No. / State / EPA No. C725241
Truck Number 09

I hereby certify that the above named material was picked up at the generator site listed above.

Ramiro D 10-21-11
Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Ramiro D 10 21 11
Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia 10 21 11
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-5 (0-7)

Log Number 031

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 26th St NY, NY

Phone No.

Generator Site/Location

Address Same

Phone No.

ID 279

Approval Number 04-899

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS 50.50 T
TARE 13.28 T
RECALLED
NET 37.22 T
LOG 2
10/22/2011
07:27AM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — 10/21/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Jose Tapia

Vehicle License No. / State / EPA No. AM3867

Truck Number 22-279

I hereby certify that the above named material was picked up at the generator site listed above.

10-21-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-21-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Esposito — 10/21/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-2
0-14'

Log Number 002

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location SAME

Address 260 West 36th St, New York, NY | Address

Phone No. | Phone No.

Approval Number 101-8199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 107
GROSS 55.17 GROSS
TARE 13.86 T
RECALLED TARE
NET 41.31 T
LOG# 54 NET
10/22/2011
08:41AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

GC agent to Generator | 10/22/11

Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print) Jorge Tapia

Address Hillside, NJ | Vehicle License No. / State / EPA No. AN7076

Truck Number 28

I hereby certify that the above named material was picked up at the generator site listed above.

Jorge L 10-21-11

Driver Signature / Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Jorge L 10-21-11

Driver Signature / Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Garcia | 10 27 11

Name of Authorized Agent / Signature / Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-5 (0-2')

Log Number 029

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 35th St

NY, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number C4-8190

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 591
GROSS 49.74 T GROSS
TARE 14.69 T TARE
RECALLED
NET 35.05 T NET
LOG # 5
10/22/2011
08:46AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent for Chelsea Green — 10/21/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ

Driver Name (Print) Paul

Vehicle License No. / State / EPA No. AV/B404

Truck Number Sherley 20

I hereby certify that the above named material was picked up at the generator site listed above.

Paul — 10-21-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Paul — 10-21-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Esposito — 10/21/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-5 (0-7)

Log Number 033

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 26th St NY, NY

Phone No.

Generator Site/Location

Address Same

Phone No. ID 747

Approval Number CY-849

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS 48.08 I
TARE 14.68
RECALLED
NET 33.40 T
LOAD 6
10/22/2011
08:49AM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 10/21/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside, NJ NJ

Driver Name (Print) Byron Martinez

Vehicle License No. / State / EPA No. AW192 NJ

Truck Number 04 Soil Safe 747

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 10-21-11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 10-21-11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — Receipt Date 10.22.11

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TF-S (0-7)

Log Number 032

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 360 W 36th St Ny, NY

Phone No.

Generator Site/Location

Address

Phone No.

Approval Number 04-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 746
GROSS 48.11 T GROSS
TARE 13.03 T TARE
RECALLED
NET 35.08 T NET
LOG 7
10/22/2011
10:01 AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

GC agent to generate — 10/21/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name ABC Industries

Address Hillside, NJ

Driver Name (Print) Jose Ortiz

Vehicle License No. / State / EPA No. AN 375K

Truck Number 88

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 10/21/11 — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 10/21/11 — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Garcia — 10 22 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 005

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

TP1 & TP-2

GENERATOR

Generator Name Chelsea W. 26th LLC
Address 37 W. 65th ST
New York, NY
Phone No.

Generator Site/Location Chelsea W 26th LLC
Address 260 W. 26th St
New York, NY
Phone No. 10 .01

Approval Number
~~C4-8200~~
C4-8199

Description of Material
Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

RECEIVED
OCT 07 2011
LOG 4/4
10/07/2011
03:49PM

GROSS 47.36 T
TARE 18.58 T
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — Generator/Authorized Agent Name
Signature
10/7/11 — Shipment Date

TRANSPORTER

Transporter Name AMG IN
Address Hillside NJ
Driver Name (Print) Jerry Valentine
Vehicle License No. / State / EPA No. AN478D
Truck Number #1

I hereby certify that the above named material was picked up at the generator site listed above.
Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.
Driver Signature — 1-10 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**
Address **378 Route 130 Logan Township, NJ 08085**
No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent
J Gorgo — Signature
10 7 11 — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-8(09)

SOIL SAFE, INC.

Log Number 001

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No. _____

Generator Site/Location _____

Address SAME

Phone No. _____

Approval Number C4-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 122
GROSS 45.07 T GROSS
TARE 13.72 T TARE
RECALLED
NET 31.35 T NET
LOG 89
11/21/2011 TONNAGE
10:06AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator _____ 11/21/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) Marco Muñoz

Vehicle License No. / State / EPA No. AL 363C

Truck Number 69

I hereby certify that the above named material was picked up at the generator site listed above.

Marco Muñoz 11-21-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Marco Muñoz 11-21-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia 11/21/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-8(10-4)

SOIL SAFE, INC.

Log Number 002

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 240 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 1065

GROSS	46.49 T	GROSS
TARE	14.04 T	TARE
RECALLED		
NET	32.45 T	NET

LOG 16

11/21/2011 10:30AM

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS AGENT TO GENERATOR — 11/21/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name J&J SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) Cristian Muñoz

Vehicle License No. / State / EPA No. AM849M NJ

Truck Number 38 / 1065

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 11/21/11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 11/21/11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — 11-21-11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-307-11

SOIL SAFE, INC.

Log Number 0083

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4 8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 590
GROSS 49.45 T GROSS
TARE 13.68 T TARE
RECALLED
NET 35.77 T NET
LOG 19
11/21/2011
10:35AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

agent to generator — 11/21/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) Chris Ulandc

Vehicle License No. / State / EPA No. RN934 F

Truck Number Sherly 12

I hereby certify that the above named material was picked up at the generator site listed above.

11-21-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

11-21-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

A. Garcia — 11/21/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3(7-14ft)

SOIL SAFE, INC.

Log Number 005

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 36th St NY NY

Phone No.

Generator Site/Location Same

Address

Phone No.

Approval Number 04-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 645
GROSS 49.27 T
TARE 13.42 T
RECALLED
NET 35.85 T
LOG 29
11/21/2011
11:11AM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

GS agent to generator — 11/21/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somer Sh LLC

Driver Name (Print) Robinson Velarde

Address

Vehicle License No. / State / EPA No. AP3952

Truck Number 9

I hereby certify that the above named material was picked up at the generator site listed above.

Demys — 11-21-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Demys — 11-21-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-407-14FD

SOIL SAFE, INC.

Log Number 006

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 36th St
NY, NY

Phone No.

Generator Site/Location Same

Address

Phone No.

Approval Number CY-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 291
GROSS 43.50 T GROSS
TARE 13.65 T TARE
RECALLED
NET 29.85 T NET
LOG 39
11/21/2011
11:38AM
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — 11/21/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somer Set LLC

Address

Driver Name (Print) Jona Hom

Vehicle License No. / State / EPA No. AN40UP

Truck Number Shirley # 04

I hereby certify that the above named material was picked up at the generator site listed above.

11/21/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

11/21/11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia — 11 21 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3(17+41)

SOIL SAFE, INC.

Log Number 004

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 26th St NY, NY

Phone No.

Generator Site/Location Same

Address

Phone No. TO 130

Approval Number CY-8119

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS 46.31 T GROSS
TARE 12.84 T TARE
RECALLED NET 33.47 T NET
LOG(J) 11/21/2011 01:08PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

D.S. agent for generator — Signature — 11/21/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somer Set LLC

Driver Name (Print) Alex Leiva

Address

Vehicle License No. / State / EPA No. AL 3940

Truck Number #1

I hereby certify that the above named material was picked up at the generator site listed above.

Alvaro Leiva 11-21-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Alvaro Leiva 11-21-11

Driver Signature — Delivery Date

DESTINATION

Site Name Soil Safe, Inc. - Bridgeport Phone No. 1-856-467-8030

Address 378 Route 130 Logan Township, NJ 08085

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

D. Garcia 11-21-11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

10-2-11 TP1 (0-2') TP2 (0-2')

Log Number 001

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea W26 LLC

Address 260 West 26th St 37 6th St NY NY

Phone No.

Generator Site/Location Chelsea W26 LLC

Address 260 West 26th Street NY NY

Phone No.

Approval Number 04-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

1087 # 24 11:26

44.04 GROSS

14.47 TARE

29.57 NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

asagent to engineer — 10/7/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name (AMG) BATTAL

Address 87 Bramhall Ave Jamaica NY

Driver Name (Print) ANTONI PAIVA

Vehicle License No. / State / EPA No. AN523H

Truck Number 1087, 806

I hereby certify that the above named material was picked up at the generator site listed above.

Antoni Paiva 10/8/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10/8/11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP1 (of 2)
TP2 (of 2)

Log Number 002

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea W26 LLC
Address 32 65th St
NY NY
Phone No.

Generator Site/Location Chelsea W26 LLC
Address 260 West 26th St
NY NY
Phone No.

Approval Number: C4-899

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 381
GROSS 42.49 T
TARE 13.15 T
RECYCLED
NET 29.34 T
LOG 26
10/07/2011
11:30AM

GROSS / TARE / NET / TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — 10/7/11
Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name A. M. V.
Address Leadwood, MO
Driver Name (Print) Hector C
Vehicle License No. / State / EPA No. AW 484A
Truck Number 10

I hereby certify that the above named material was picked up at the generator site listed above.
Driver Signature / Shipment Date 10/7/11

I hereby certify that the above named material was delivered without incident to the destination listed below.
Driver Signature / Delivery Date 10/7/11

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**
Address **378 Route 130 Logan Township, NJ 08085**
No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Corcin — 10 7 11
Name of Authorized Agent / Signature / Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP1 (0-7) (0-2)
TP2

Log Number 003

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea NJ 28 LLC
Address 37 65th St
NY NY
Phone No.

Generator Site/Location Chelsea NJ 28 LLC
Address 260 West 28th St
NY NY
Phone No.

Approval Number CU-8198

Description of Material
Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

ID 273
GROSS 47.17 T
TARE 13.28 T
NET 33.89 T
Loc 25
10/07/2011
11:29AM

GROSS
TARE
NET
TONNAGE

RECEIVED OCT 11

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Assign to generator — 10/7/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Ind.
Address
Driver Name (Print) Vox Topi
Vehicle License No. / State / EPA No. AM386Y
Truck Number 22

I hereby certify that the above named material was picked up at the generator site listed above.

10-7-11
Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

10-7-11
Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**
Address **378 Route 130 Logan Township, NJ 08085**
No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Cour Cu — 10.7.11
Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 004

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

TP1 & TP-2

GENERATOR

Generator Name Chelsea W36 LLC

Address 37 65th St

NY NY

Phone No.

Generator Site/Location Chelsea W36 LLC

Address 360 West 36th St

NY NY

Phone No. 10 .02

Approval Number C4-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS 35.54 T
RECALLED
TARE 14.81 T
NET 24.73 T
10/07/2011
03:52PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent for generator — 10/7/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries

Address Hillside NJ

Driver Name (Print) Karl Bingley

Vehicle License No. / State / EPA No. AN4-TD

Truck Number 72

I hereby certify that the above named material was picked up at the generator site listed above.

Karl Bingley 10-7-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Karl Bingley 10-7-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

[illegible] 10-7-11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 006

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST TP 106

GENERATOR

Generator Name Chelsea W 26 LLC
Address 37 W. 65th St
New York, NY
Phone No.

Generator Site/Location Chelsea W 26 LLC
Address 840 W. 26th St
New York, NY
Phone No.

Approval Number CY-8199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 361
GROSS 49.90 T — GROSS
TARE 13.15 T — TARE
RECALLED
NET 36.75 T — NET
LOG 50
10/07/2011
04:50PM — TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

asagal to generator — 10/7/11
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name A. M. U
Address Lodgewood, NJ
Driver Name (Print) Hector G
Vehicle License No. / State / EPA No. A Hector G
Truck Number 60

I hereby certify that the above named material was picked up at the generator site listed above.
Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.
Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**
Address **378 Route 130 Logan Township, NJ 08085**
No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 067

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea W. 20 LLC
Address 37 W. 65th ST
New York, NY
Phone No. 212-

Generator Site/Location Chelsea W. 20 LLC
Address 420 W. 20th St
New York, NY
Phone No. 212-

Description of Material

Approval Number	Description of Material		
C4-8198	Non-Regulated Petroleum Contaminated Soil Non DOT/RCRA Regulated	GROSS 49.64 T TARE 13.06 T NET 36.58 T LOG 10/08/2011 08:44PM	GROSS TARE NET TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Generator Authorized Agent Name _____ Signature _____ Shipment Date _____

TRANSPORTER

Transporter Name Rosetta Stone
Address Avon Industries
Hillside, NJ

Driver Name (Print) _____
Vehicle License No. / State / EPA No. _____
Truck Number _____

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature _____ Shipment Date _____

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature _____ Delivery Date _____

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent _____ Signature _____ Receipt Date _____

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-4(0-14)

SOIL SAFE, INC.

Log Number 001

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4-9199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 515
GROSS 45.21 T GROSS
TARE 12.99 T TARE
RECALLED
NET 32.22 T NET
LOG 9
12/13/2011 TONNAGE
10:27PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 12/13/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4030

Driver Name (Print) Brad Solano

Vehicle License No. / State / EPA No. AN536E

Truck Number 515

I hereby certify that the above named material was picked up at the generator site listed above.

12/13/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12/13/11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

12/13/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-4 (7-94)

SOIL SAFE, INC.

Log Number 002

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4 5199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 680
GROSS 49.19 T GROSS
TARE 13.69 T TARE
RECALLED
NET 35.49 T NET
LOG 8
12/13/2011 TONNAGE
10:50PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS agent to generator — 12/13/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) WALTON

Vehicle License No. / State / EPA No. AM 331D

Truck Number # 01

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 12/13/11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 12/13/11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — 12/13/11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-4(7-14)

SOIL SAFE, INC.

Log Number 004

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN Generator Site/Location _____

Address 280 WEST 20TH STREET Address SAME

NY, NY

Phone No. _____ Phone No. _____

Approval Number C4-8199

Description of Material: Non-Regulated Petroleum Contaminated Soil - Non DOT/RCRA Regulated

ID 740
GROSS 49.22 T GROSS
TARE 13.06 T TARE
RECALLED
NET 35.16 T NET
LOG 21
12/13/2011 TONNAGE
10:55PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 12/13/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET LLC Driver Name (Print) ORLANDO ORTIZ

Address MONTVILLE, NJ Vehicle License No. / State / EPA No. AU312Q

(973) 794-4020 Truck Number 2

I hereby certify that the above named material was picked up at the generator site listed above.

12-13-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-13-11

Driver Signature — Delivery Date

DESTINATION

Site Name Soil Safe, Inc. - Bridgeport Phone No. 1-856-467-8030

Address 378 Route 130 Logan Township, NJ 08085

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

12/13/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-407-14

Log Number 005

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN | Generator Site/Location

Address 260 WEST 26TH STREET | Address SAME

NY, NY

Phone No. | Phone No.

Approval Number C43199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

10 749
GROSS 50.30 T GROSS
TARE 12.71 T TARE
RECALLED
NET 37.59 T NET
LOG 23
12/13/2011
11:08PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 12/13/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC | Driver Name (Print) Jose

Address MONTVILLE, NJ | Vehicle License No. / State / EPA No. AN-375K

(973) 794-4020 | Truck Number 11 CB - NJ S

I hereby certify that the above named material was picked up at the generator site listed above.

Jose Vicente — 12/13/11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Jose Vicente — 12/13/11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are; Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

12/13/11

Name of Authorized Agent | Signature | Receipt Date

White - Facility | Green - Facility | Yellow - Generator | Pink - Broker | Goldenrod - Contractor | Blue - Trucking Co.

TR-4(7-4)

SOIL SAFE, INC.

Log Number 003

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 36TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 761

GROSS 49.48 T GROSS

TARE 13.22 T TARE

RECALLED

NET 36.26 T NET

LOG 27

12/13/2011 TONNAGE

11:23PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 12/13/11

Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name SOMERSET LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) Angel Lugo

Vehicle License No. / State / EPA No. AM 3J 31K

Truck Number 01

I hereby certify that the above named material was picked up at the generator site listed above.

12-13-11

Driver Signature / Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-13-11

Driver Signature / Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

12/13/11

Name of Authorized Agent / Signature / Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-407-14

Log Number 006

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4 8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 279

GROSS	49.82 T	GROSS
TARE	13.28 T	TARE
RECYCLED		
NET	36.54 T	NET

LOG 55
12/13/2011
02:00PM

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator 12/13/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) Jose Tapia

Vehicle License No. / State / EPA No. AM386Y

Truck Number 22 229

I hereby certify that the above named material was picked up at the generator site listed above.

12-13-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-13-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

12/13/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4(3-14)

SOIL SAFE, INC.

Log Number 007

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Generator Site/Location _____

Address 260 WEST 26TH STREET

Address SAME

NY, NY

Phone No. _____

Phone No. _____

Approval Number C43199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 515
GROSS 46.64 T GROSS
TARE 12.99 T TARE
RECALLED
NET 33.65 T NET
LOG 12/13/2011 TONNAGE
03:18PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Tom K as agent to generator 12/13/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name SOMERSET LLC

Driver Name (Print) Oscar Lara

Address MONTVILLE, NJ

Vehicle License No. / State / EPA No. NHS366

(973) 794-4020

Truck Number 515

I hereby certify that the above named material was picked up at the generator site listed above.

12/13/11

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12/13/11

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

12/13/11

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-HC7-14

SOIL SAFE, INC.

Log Number 008

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4.8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 740
GROSS 47.40 T GROSS
TARE 13.06 T TARE
RECALLED
NET 34.34 T NET
LOG 75
12/13/2011 TONNAGE
08:31PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS agent to Generator 12/13/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE NJ

(973) 794-4020

Driver Name (Print) CAR LOAD OUT

Vehicle License No. / State / EPA No. AN3120

Truck Number (2) 740

I hereby certify that the above named material was picked up at the generator site listed above.

12-13-11

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-13-11

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

12/13/11

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-4(7-14)

SOIL SAFE, INC.

Log Number 009

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 240 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4.5199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 746

GROSS 49.59 T GROSS

TARE 13.03 T TARE

RECALLED

NET 36.56 T NET

LOG 82

12/13/2011

04:06PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — Signature — 12/12/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) JOSE

Vehicle License No. / State / EPA No. AN-375K

Truck Number # 80 - NJT 246

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 12-13-11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — 12/13/11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-4C7-14D

SOIL SAFE, INC.

Log Number 011

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 360 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4.9199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 680 GROSS
GROSS 49.25 T
TARE 13.69 T TARE
RECALLED
NET 35.56 T NET
LOG 85 TONNAGE
12/13/2011
1:14:47 PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS AGNT TO Generator — 12/13/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) WALTON

Vehicle License No. / State / EPA No. AM1 331D

Truck Number 404 680

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 12/13/11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 12/13/11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — 12/13/11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4(7-14)

Log Number 010

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C1319

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 1015
GROSS 58.20 T
TARE 13.50 T
RECALLED
NET 44.70 T
LOG 87
12/13/2011
05:04PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 12/13/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4920

Driver Name (Print) Jake

Vehicle License No. / State / EPA No. AM1442

Truck Number #3 1015

I hereby certify that the above named material was picked up at the generator site listed above.

12/13/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

12/13/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-407-11

Log Number 013

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

Approval Number C4-9199

ID 761
GROSS 44.87 T GROSS
TARE 13.22 T TARE
RECALLED
NET 31.65 T NET
LOG 88
12/13/2011 TONNAGE
05:07PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS AGT TO GENERATOR — 12/13/11

Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) Angel Munoz AM 3/13/12

Vehicle License No. / State / EPA No. 07

Truck Number

I hereby certify that the above named material was picked up at the generator site listed above.

12-13-11

Driver Signature / Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-13-11

Driver Signature / Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

12/13/11

Name of Authorized Agent / Signature / Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4(6-7)

Log Number 001

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4 8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 740

GROSS 38.05 T GROSS

TARE 13.06 T TARE

RECALLED

NET 24.99 T NET

LOG 11

12/14/2011 TONNAGE

09:50AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS Agent for generator 12/14/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 734-4020

Driver Name (Print) CARLOS ORTIZ

Vehicle License No. / State / EPA No. AN32R

Truck Number 9

I hereby certify that the above named material was picked up at the generator site listed above.

12-14-11

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-14-11

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia 12/14/11

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4 (5-14)

Log Number 002

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Generator Site/Location

Address 260 WEST 26TH STREET

Address SAME

NY, NY

Phone No.

Phone No.

Approval Number C4.8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 746
GROSS 44.59 T GROSS
TARE 13.03 T TARE
RECALLED
NET 31.56 T NET
LOG 20
12/14/2011
10:23AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — 12/14/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET LLC

Driver Name (Print) Jose

Address MONTVILLE, NJ

Vehicle License No. / State / EPA No. AM-375-K

Truck Number # 88-10-J

(973) 794-4020

I hereby certify that the above named material was picked up at the generator site listed above.

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Shipment Date

Driver Signature — 12/14/11 — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 12 14 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4(7-14)

SOIL SAFE, INC.

Log Number 003

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 360 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C43199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

10 YDS

GROSS	44.88 T	GROSS
TARE	13.22 T	TARE
RECALLED NET	31.66 T	NET
LOG 29 12/14/2011 10:40AM		TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to operator — 12/14/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET LLC

Address MONTVILLE, NJ

(973) 784-4020

Driver Name (Print) Angel Nunez

Vehicle License No. / State / EPA No. AW 3132

Truck Number 01

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date 12-14-11

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date 12-14-11

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 12/14/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-407-14

SOIL SAFE, INC.

Log Number 004

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C43199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 279

GROSS 48.85 T GROSS

TARE 13.28 T TARE

RECALCED NET 35.57 T NET

LOG TONNAGE

12/14/2011

11:15AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 12/14/11

Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) Jose Tapia

Vehicle License No. / State / EPA No. AM386Y

Truck Number 22

I hereby certify that the above named material was picked up at the generator site listed above.

Jose Tapia — 12-14-11

Driver Signature / Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature / Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia — 12/14/11

Name of Authorized Agent / Signature / Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4C7-14FH

Log Number 005

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4.8190

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

10 740

GROSS	50.02 T	GROSS
TARE	13.06 T	TARE
RECALLED NET	36.96 T	NET

LOG 76
12/14/2011
02:39PM

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 12/14/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) CHARLES OLIVO

Vehicle License No. / State / EPA No. A U 3 1 2 R

Truck Number CE 740

I hereby certify that the above named material was picked up at the generator site listed above.

12-14-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-14-

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

12/14/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4
(7-14-11)

SOIL SAFE, INC.

Log Number 006

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

Approval Number C4.8199

ID 746
GROSS 45.20 T
TARE 13.03 T
RECALLED
NET 32.17 T
LOG 89
12/14/2011
1:14:47PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 12/14/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 784-4020

Driver Name (Print) JOSE

Vehicle License No. / State / EPA No. AN-375K-

Truck Number TRB-NJ-746

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 12/14/11 — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — 12/14/11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4 (7-14 FP)

SOIL SAFE, INC.

Log Number 007

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 240 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4.9199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 761
GROSS 44.33 T GROSS
TARE 13.22 T TARE
RECALLED
NET 31.11 T NET
LOG 91
12/14/2011 TONNAGE
04:53PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator 12/14/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name SOMERSET LLC

Address MONTVILLE NJ

(973) 794-4020

Driver Name (Print) Miguel Munoz

Vehicle License No. / State / EPA No. AM313R

Truck Number 01

I hereby certify that the above named material was picked up at the generator site listed above.

12-14-11

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-14-11

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

12/14/11

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4 (7-14 Ft)

Log Number 008

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4 8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

10 279

GROSS 49.83 T GROSS

TARE 13.28 T TARE

RECALLED

NET 36.55 T NET

LOG 92 TONNAGE

12/14/2011

(6:14PM)

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 12/14/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) José Tapia

Vehicle License No. / State / EPA No. AM386Y

Truck Number 22

I hereby certify that the above named material was picked up at the generator site listed above.

12-14-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-14-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

12/14/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-4(3-14)

SOIL SAFE, INC.

Log Number 001

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 360 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4.3199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 590

GROSS 49.81 T GROSS

TARE 13.68 T TARE

RECALLED

NET 35.13 T NET

LOG 13

12/15/2011 TONNAGE

CR: SOAR

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

GC agent to approval — 12/15/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 784-4020

Driver Name (Print) Fabian Velarde

Vehicle License No. / State / EPA No. AN434F

Truck Number Shirley L2

I hereby certify that the above named material was picked up at the generator site listed above.

12-15-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-15-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

12/15/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-402-14

Log Number 002

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 28TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C48199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

10 740

GROSS 46.84 GROSS

TARE 13.06 T

RECALLED

NET 33.78 T TARE

LOG 16 NET

12/15/2011

10:02AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

GS agent to generator 12/15/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) CARLOS SERRO

Vehicle License No. / State / EPA No. 4MV 312 D

Truck Number 2

I hereby certify that the above named material was picked up at the generator site listed above.

12-15-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-15-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia 12.15.11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4 (7'-14 Ft)

SOIL SAFE, INC.

Log Number 003

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4.8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 342

GROSS 51.19 T

TARE 13.52 T

RECALLED

NET 37.67 T

LOG 23

12/15/2011

10:18AM

ID 342

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator

Generator Authorized Agent Name

Signature

12/15/11

Shipment Date

RECALLED

NET 37.76 T

LOG 12/15/11

12/15/2011

10:21AM

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print)

Vehicle License No. / State / EPA No. AH 316 M

Truck Number 05

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature

12/15/11

Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature

12/15/11

Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport**

Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Correia

Name of Authorized Agent

Signature

12/15/11

Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-4
(7-14)

SOIL SAFE, INC.

Log Number 005

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 140 WEST 26TH STREET

NI, NY

Phone No.

Generator Site/Location

Address SAME

Phone No. 10 515

Approval Number C4 8196

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS 43.75 I
TARE 12.99 GROSS
RECALLED
NET 30.76 TARE
LOG 25
12/15/2011 NET
10:38AM
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 12/15/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) Oscar Solano

Vehicle License No. / State / EPA No. DH5366

Truck Number 1575

I hereby certify that the above named material was picked up at the generator site listed above.

12/15/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12/15/11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 12-15-11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4
(7-14)

SOIL SAFE, INC.

Log Number 006

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 240 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No. 10 6560

Description of Material

Approval Number C4.8199

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS 45.96 T GROSS
TARE 13.69 T TARE
RECALLED
NET 32.27 T NET
LOG 27
12/15/2011
10:52AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS AGENT TO GENERATOR — 12/15/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) WALTON

Vehicle License No. / State / EPA No. AM 33D

Truck Number FF 02

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 12/15/11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 12/15/11 Delivery Date

DESTINATION

Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

378 Route 130, Logan Township, NJ 08085

n on Rt. 130 North into the facility.

ours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appoint-

fy that the above named material has been accepted and to the best of my knowledge the foregoing is true

J. Garcia — 12/15/11

ed Agent — Signature — Receipt Date

e - Facility | Green - Facility | Yellow - Generator | Pink - Broker | Goldenrod - Contractor | Blue - Trucking Co.

TR-4(7-17)

SOIL SAFE, INC.

Log Number 007

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No. _____

Generator Site/Location _____

Address SAME

Phone No. _____

Approval Number C49199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 761
GROSS 39.97 T GROSS
TARE 13.22 T TARE
RECALLED
NET 26.75 T NET
LOG 33
12/15/2011 TONNAGE
11 *23PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to Generation _____ 12/15/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) Angel A Lopez

Vehicle License No. / State / EPA No. AH 3132

Truck Number 01

I hereby certify that the above named material was picked up at the generator site listed above.

_____ 12-15-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

_____ 12-15-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

_____ 12.15.11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 008

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C43199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 1015

GROSS	50.86 T	GROSS
TARE	13.50 T	TARE
RECALLED		
NET	37.36 T	NET
LOG 36		
12/15/2011 11:39AM		TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to Generator — 12/15/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) Jose

Vehicle License No. / State / EPA No. AM 1442

Truck Number #3

I hereby certify that the above named material was picked up at the generator site listed above.

12-15-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12/15/11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

A. Garcia — 12-15-11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-467-14

Log Number 009

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 36TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4.3199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID .712

GROSS 44.67 T — GROSS

RECALLED

TARE 14.51 T — TARE

NET 30.16 T — NET

LOG 72

12/15/2011

02:06PM

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS agent to generator — 12/15/11

Generator/Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name NIKOBellas SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794 4020

Driver Name (Print) Jose Ortiz

Vehicle License No. / State / EPA No. AM732R

Truck Number 28

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 12/15/11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 12/15/11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 12 15 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-467-19

Log Number 010

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NL, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C48199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID - 456
GROSS 43.90 GROSS
RECALLED
TARE 14.14 TARE
NET 29.76 T NET
LOG 73
12/15/2011
02:03PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 12/15/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 784-4020

Driver Name (Print) Jorge Ruiz

Vehicle License No. / State / EPA No. AM200H

Truck Number #2

I hereby certify that the above named material was picked up at the generator site listed above.

12-15-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-15-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Carlos — 12/15/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4 (0-14)'

Log Number 011

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 360 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C43199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 740
GROSS 42.64 T GROSS
TARE 13.06 T TARE
RECALLED
NET 29.58 T NET
LOG 81
12/15/2011 TONNAGE
02:55PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator 12/15/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) Carlos Cano

Vehicle License No. / State / EPA No. AU 3122

Truck Number 42

I hereby certify that the above named material was picked up at the generator site listed above.

12-15-11

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-15-11

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Carla 12-15-11

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4 (7-14)

SOIL SAFE, INC.

Log Number 012

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 240 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4.8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 515
GROSS 44.56 T GROSS
TARE 12.59 T TARE
RECALLED
NET 31.97 T NET
LOG 95
12/15/2011 TONNAGE
03:38PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator 12/15/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794 4020

Driver Name (Print) OSCAR

Vehicle License No. / State / EPA No. HK1536E

Truck Number 515

I hereby certify that the above named material was picked up at the generator site listed above.

12/15/11

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12/15/11

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Garcia 12/15/11

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4(7-14)

Log Number 613

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 360 WEST 36TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Description of Material

Approval Number C4.8199

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 680

GROSS 48.25 GROSS

TARE 13.69 TARE

RECALCED

NET 34.56 NET

LOG 100

12/15/2011

04:00PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent for generator — 12/15/11

Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) WALTON

Vehicle License No. / State / EPA No. AM 33LD

Truck Number #01

I hereby certify that the above named material was picked up at the generator site listed above.

12/15/11

Driver Signature / Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12/15/11

Driver Signature / Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 12 15 11

Name of Authorized Agent / Signature / Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

R-407-14

SOIL SAFE, INC.

Log Number 004

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 340 WEST 28TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4.3199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

TO 652

GROSS 45.04 T — GROSS

TARE 14.24 T — TARE

RECALLED

NET 30.80 T — NET

LOG 107

12/15/2011

04:42PM — TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 12/15/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC / MCB

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) Roberto Rosales

Vehicle License No. / State / EPA No. AM612M

Truck Number 3 / 652

I hereby certify that the above named material was picked up at the generator site listed above.

12-15-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-15-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Gorch — 12/15/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-4 (7-14)

SOIL SAFE, INC.

Log Number 014

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Generator Site/Location

Address 240 WEST 26TH STREET

Address SAME

NY, NY

Phone No.

Phone No.

Description of Material

Approval Number	Description of Material		
C4-8199	Non-Regulated Petroleum Contaminated Soil Non DOT/RCRA Regulated	GROSS 50.08 T TARE 13.50 T RECALLED NET 36.58 T LOG 106 12/15/2011 04:54PM	GROSS TARE NET TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 12/15/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Driver Name (Print) Jake

Address MONTVILLE, NJ

Vehicle License No. / State / EPA No. AM494

(973) 794-4020

Truck Number #3

I hereby certify that the above named material was picked up at the generator site listed above.

I hereby certify that the above named material was delivered without incident to the destination listed below.

No. 38331 — 12/15/11

Driver Signature — Shipment Date

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Carlos — 12/15/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-467-14

SOIL SAFE, INC.

Log Number 015

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 360 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C43199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 761
GROSS 42.82 T GROSS
TARE 13.22 T TARE
RECYCLED
NET 29.60 T NET
LOG 107
12/15/2011
08:04PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 12/15/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) Angel Muniz

Vehicle License No. / State / EPA No. AW313 NJ

Truck Number 01

I hereby certify that the above named material was picked up at the generator site listed above.

12-15-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-15-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 12/15/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-4(7-14)

Log Number 017

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 360 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4-3199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID #45

GROSS 45.50 T GROSS

TARE 13.03 T TARE

RECALLED

NET 32.47 T NET

LOG 110

12/15/2011

06:25PM

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 12/15/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) Jose Vicente

Vehicle License No. / State / EPA No. AM 375K

Truck Number 81

I hereby certify that the above named material was picked up at the generator site listed above.

12-15-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date

DESTINATION

Site Name Soil Safe, Inc. - Bridgeport Phone No. 1-856-467-8030

Address 378 Route 130 Logan Township, NJ 08085

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 12/15/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP Lot (1-9-14)

SOIL SAFE, INC.

Log Number 8016

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No. 646-258-5

Generator Site/Location

Address SAME

Phone No.

Approval Number	Description of Material	
C4 8199	Non-Regulated Petroleum Contaminated Soil Non DOT/RCRA Regulated	GROSS TARE NET TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 12/15/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SCHAEFFER

Address 92 MONTVILLE NJ 07045

Driver Name (Print) Tony Tapia

Vehicle License No. / State / EPA No. AM386Y

Truck Number 22

I hereby certify that the above named material was picked up at the generator site listed above.

12-15-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

SoilSafe.
Recycling of Contaminated Soil and Industrial Waste.
6700 Alexander Bell Drive, Suite 300, Columbia, MD 21046
(410) 872-3990, Fax (410) 872-3978

Invoice
55983

Bill To:	Project:
Chelsea West 26, LLC c/o Artimus Construction, Inc. Attention: Amnon Solomon 37 West 65th Street 2nd Floor New York, NY 10023	Chelsea Green 260 West 26th Street New York, NY 10001

APPROVAL #: C4-8199 **PROPOSAL #:** 441 **PO #:**
INVOICED VOLUME OF SOIL: 451.06 **# OF TRUCKS:** 13
INVOICE DATE: 12/16/11 **DUE DATE:** 1/15/12

BILLING PERIOD: 12/6/11 TO 12/7/11

DESCRIPTION:	UNITS INVOICED:	RATE:	AMOUNT:
Recycling & Transportation Fees - Tons	451.06	$ 42.00	$ 18,944.52

1) RECD 12/23/11 5) ENTERED/VOD 12/26/11
3) PS MATCH
4) SCANNED & ARCHIVED
5) PM APPROVED & UPDATED ENTRY
6) CONTROLLER REVIEW
7) EXEC 1 REVW 7b) EXEC 2 REVW
7a) CHK CUT 7c) EXEC 3 REVW
*) CHECK DATE CHECK#
CHECK AMOUNT

GROSS INVOICE	$ 18,944.52
SALES TAX	0.00
LESS: PREPAYMENTS	0.00
INVOICE TOTAL	$ 18,944.52

Contact:

**NOTE* Payments are Net 30 days. Overdue balances are subject to a 1.5% charge per month or the maximum allowed by law.*

Remit to: (Payments Only) Soil Safe, Inc., P.O. Box 824062, Philadelphia, PA 19182-4062

Log Number 120601

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

TP-2 7-14

ID 740
GROSS 40.19 T
TARE 13.06 T
RECALLED
NET 27.13 T
LOG 47
12/06/2011
09:51AM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS Agent Stephen Malinowski 12-06-11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4030

Driver Name (Print) CARLOS ORTIZ

Vehicle License No. / State / EPA No. AV 312 12

Truck Number (2) 3040

I hereby certify that the above named material was picked up at the generator site listed above.

12-06-11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-06-11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

12/6/11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 120602

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 360 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number CL5159

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

TP-2 (7-11)

ID 745
GROSS 44.71 T GROSS
TARE 13.03 T TARE
RECALLED
NET 31.68 T NET
LOG 59
12/06/2011 TONNAGE
10:32AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS Agent Stephen Matuszki Stephen Matuszki 12-06-11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) LOGE

Vehicle License No. / State / EPA No. AM-295 K

Truck Number H 88 M.S. 746

I hereby certify that the above named material was picked up at the generator site listed above.

LOGE VILLEATE

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature 12/6/11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent Signature 12/6/11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 120604

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

TP-24 TP9 (7-14)

ID SSS

GROSS 46.94 T GROSS

TARE 13.91 T TARE

RECALLED

NET 33.03 T NET

LOG 65

12/06/2011

10:51AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

ASheet Snyder McIntosh — 12-06-11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) Steve B LEMA

Vehicle License No. / State / EPA No. H182R

Truck Number 7 (555)

I hereby certify that the above named material was picked up at the generator site listed above.

Steve Bruno 12.6.11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Steve Bruno 12.6.11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

12/6/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 12003

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

TP-2 & TP-4 7-14

18 761

GROSS 45.98 T GROSS

TARE 12.22 T TARE

RECALLED...

NET 33.76 T NET

LOG 66

12/06/2011

10:54AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Agent Stephen Malinowski 12-06-11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name SOMERSET LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) Angel Nunez

Vehicle License No. / State / EPA No. AW 31312 761

Truck Number 01

I hereby certify that the above named material was picked up at the generator site listed above.

12-6-11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-06-11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

12/6/11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 120605

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Generator Site/Location

Address 260 WEST 26TH STREET

Address SAME

NY, NY

Phone No.

Phone No.

Approval Number C4-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

TP2 7-14

ID 279
GROSS 48.47 T GROSS
TARE 13.28 T TARE
RECALLED
NET 35.19 T NET
LOG 67
12/06/2011
10:57AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS Agent Stoller/Malinowski — 12/6/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Driver Name (Print) Jose Tapia

Address MONTVILLE, NJ

Vehicle License No. / State / EPA No. AM38Y

Truck Number 22 (871)

(973) 794-4020

I hereby certify that the above named material was picked up at the generator site listed above.

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Shipment Date

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

12/5/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 12606

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 36TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4-8190

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

TP-2 TP-4 (7-4)

ID 1065

GROSS	49.32 T	GROSS
TARE	14.04 T	TARE
NET	35.28 T	NET

RECALLED

LOG 72

12/06/2011 11:23AM

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As Agent Steph Matousek 12-06-11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name J & J Bird SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-1020

Driver Name (Print) CRISTIAN MUÑOZ

Vehicle License No. / State / EPA No. AN844H

Truck Number 98/1065

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature 12/6/11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature 12/6/11 Delivery Date

DESTINATION

Site Name Soil Safe, Inc. - Bridgeport Phone No. 1-856-467-8030

Address 378 Route 130 Logan Township, NJ 08085

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent Signature 12/6/11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 120607

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4S190

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

TP-2(7-14)

ID T40
GROSS 49.83 T GROSS
TARE 13.06 T TARE
RECALLED,
NET 36.77 T NET
LOG 145
12/06/2011
03:56PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Asphalt Stephen Malowski 12-06-11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) CHARLES DETZ

Vehicle License No. / State / EPA No. AV312

Truck Number 20

I hereby certify that the above named material was picked up at the generator site listed above.

12-06-11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-6-11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

12/6/11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 120608

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 360 WEST 20TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

TP-2 07-14

ID 746

GROSS	48.95 T	GROSS
TARE	13.03 T	TARE
NET	35.92 T	NET

RECALLED

LOG 150

12/06/2011 04:23PM

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As Agent Stefan Matuszek — Stefan Matuszek — 12-06-11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET LLC

Address MONTVILLE NJ

(973) 794-4020

Driver Name (Print) JOSE

Vehicle License No. / State / EPA No. AN-325K

Truck Number H 88-N3 246

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 12-06-11 — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — 12/6/11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 120609

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 39TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4-8190

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

TP-2 (7-14)

ID 279
GROSS 51.78 GROSS
TARE 13.28 T TARE
RECALLED
NET 38.50 T NET
LOG 152
12/06/2011 TONNAGE
04:32PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As Agent Stefan Matousek 12-06-11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) Walt Tarn

Vehicle License No. / State / EPA No. AM JKY

Truck Number 22

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent Signature 12/6/11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 12612

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4-5199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

TP-2 (7-14)

10 YDS

GROSS 50.18 T GROSS

TARE 13.22 T TARE

RECALLED

NET 36.96 T NET

LOG 153

12/06/2011

04:47PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Robert Stephen Mahoney — 12-6-11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) Angel Munoz

Vehicle License No. / State / EPA No. AM 313

Truck Number 01

I hereby certify that the above named material was picked up at the generator site listed above.

12-6-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-06-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

12/6/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 120610

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 360 WEST 36TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No. 111 1055

GROSS 50.68 GROSS
TARE 14.04 T
RECYCLED
NET 36.64 T TARE
LOG
12/07/2011
07:06AM NET
TONNAGE

Approval Number CA3199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

TP-2 (7-9)

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

A. Agent Stryker Mahowsk 12-06-11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

J & J Disp

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) Carmine Muniz

Vehicle License No. / State / EPA No. AN84444

Truck Number 98/1065

I hereby certify that the above named material was picked up at the generator site listed above.

12-6-11

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-6-11

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

12/7/11

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 12611

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

TP-2 (7-9)

ID 1002

GROSS 45.82 GROSS

TARE 13.02 T TARE

RECALLED

NET 1 TON 32.80 T NET

LOG 6

12/07/2011

07:18PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Robert Stephenson/Mahwah 12-06-11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) JERRY MOLINO

Vehicle License No. / State / EPA No. AK2312

Truck Number JF187

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature 12-6-11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature 12-6-11 Delivery Date

DESTINATION

Site Name Soil Safe, Inc. - Bridgeport Phone No. 1-856-467-8030

Address 378 Route 130 Logan Township, NJ 08085

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent Signature 12/7/11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 12613

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Generator Site/Location _____

Address 760 WEST 26TH STREET

Address SAME

NY, NY

Phone No. _____

Phone No. _____

Approval Number C48199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

TP-2 (7-9)

ID 122

GROSS 51.12 T

TARE 13.72 T

RECALLED

NET 37.40 T

LOG 7

12/07/2011

07:24AM

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

M. Noel Stahelin-Houck — 12-06-11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET LLC

Driver Name (Print) Marco Muro

Address MONTVILLE, NJ

Vehicle License No. / State / EPA No. AL 363C

Truck Number 69 122

(973) 794-4020

I hereby certify that the above named material was picked up at the generator site listed above.

I hereby certify that the above named material was delivered without incident to the destination listed below.

Marco Muro 12-06-11

Driver Signature — Shipment Date

Marco Muro 12-06-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

_____ 12/7/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-5 (0-2)
TP-6 (0-2)

Log Number 001

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location Same

Address 260 West St, NY, NY | Address

Phone No. | Phone No.

Approval Number: Cu-8109

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 1015
GROSS 56.21 T
TARE 13.50 T
RECYCLED
NET 42.71 T
LOG 7
11/01/2011
10:24AM

GROSS / TARE / NET / TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Agent to generator | Signature | 11/1/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print) Jarrod

Address Hillsdale, NJ | Vehicle License No. / State / EPA No. AM149L

Truck Number 43

I hereby certify that the above named material was picked up at the generator site listed above.

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature | Shipment Date | Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent | Signature | 11/1/11 Receipt Date

White - Facility | Green - Facility | Yellow - Generator | Pink - Broker | Goldenrod - Contractor | Blue - Trucking Co.

TP-5 (0-3)
TP-6 (0-3)

Log Number 002

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green
Address 260 W 26th St
NY, NY
Phone No.

Generator Site/Location Same
Address
Phone No.

Approval Number C4-8199

Description of Material
Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

ID 555
GROSS 48.60 T GROSS
TARE 13.91 T TARE
RECALCED
NET 34.69 T NET
LOG 19
11/01/2011 TONNAGE
11:02AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 11/1/11
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMG Industries Soil
Address Hillside, NJ
Driver Name (Print) Jaime & LPM
Vehicle License No. / State / EPA No. AL 862 R
Truck Number 7 - 556

I hereby certify that the above named material was picked up at the generator site listed above.
Driver Signature — 11-1-11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.
Driver Signature — 11-1-11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**
Address **378 Route 130 Logan Township, NJ 08085**
No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Garcia — 11-1-11
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-5 (0-7)
TP-6 (0-7)

Log Number 003

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green
Address 260 W 36th St NY, NY
Phone No.

Generator Site/Location SOMA
Address
Phone No.

Approval Number C4-8199

Description of Material
Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

ID 1065
GROSS 50.01 T GROSS
TARE 14.04 T TARE
RECALLED
NET 35.97 T NET
LOG 21
11/01/2011 TONNAGE
11:06AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 11/1/11
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name J & J Bros Trucking AMG Industries
Address Hillside, NJ

Driver Name (Print) J. Jefferson Mun2
Vehicle License No. / State / EPA No. AN 844M NJ
Truck Number 98/1005

I hereby certify that the above named material was picked up at the generator site listed above.
Driver Signature — 11/1/11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.
Driver Signature — 11/1/11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**
Address **378 Route 130 Logan Township, NJ 08085**
No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 11-1-11
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-5 (0-2)
TP-6 (0-2)

Log Number 005

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location Same

Address 260 West 36th St NY, NY | Address

Phone No. | Phone No. 10 515

Approval Number 04-299

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS 48.13 T
TARE 12.99
RECALLED
NET 35.14 T
LOG 30
11/01/2011
11:31AM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator | 11/1/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Logistics | Driver Name (Print) Oscar

Address Hillside, N.J. | Vehicle License No. / State / EPA No. AM536E

Truck Number 515

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Oscar | 11/1/11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Garcia | 11-1-11

Name of Authorized Agent | Signature | Receipt Date

White - Facility | Green - Facility | Yellow - Generator | Pink - Broker | Goldenrod - Contractor | Blue - Trucking Co.

TP-5 (0-2)
TP-6 (0-2)

Log Number 004

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location Same

Address 260 W 25th St NY, NY | Address

Phone No. | Phone No.

Approval Number CY-0199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID .122
GROSS 48.11 T GROSS
RECALLED
TARE 13.99 T TARE
NET 34.12 T NET
LOG 32
11/01/2011
11:34AM
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator | 11/1/11

Generator/Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AMG Industries | Driver Name (Print) Mario Mones

Address Hillside, NJ. | Vehicle License No. / State / EPA No. AL362

Truck Number 69

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature | 10-01-11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature | Delivery Date

DESTINATION

Site Name Soil Safe, Inc. - Bridgeport | Phone No. 1-856-467-8030

Address 378 Route 130 Logan Township, NJ 08085

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Corra | 11-1-11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-5 (0-7)
TP-6 (0-7)

SOIL SAFE, INC.

Log Number 006

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location Same

Address 260 West 26th St NY, NY | Address

Phone No. | Phone No.

Approval Number 04 9144

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

TO GBO
GROSS 50.89 T GROSS
TARE 13.69 T TARE
RECALLED
NET 37.20 T NET
LOG 41
11/01/2011
12:06PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to owner — 11/1/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name AM6 Industries | Driver Name (Print) Watson

Address Hillsdale, NJ. | Vehicle License No. / State / EPA No. AM331D

Truck Number 10-2

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature | Shipment Date 11/1/11

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature | Delivery Date 11/1/11

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Gonon — 11/1/11

Name of Authorized Agent | Signature | Receipt Date

White - Facility | Green - Facility | Yellow - Generator | Pink - Broker | Goldenrod - Contractor | Blue - Trucking Co.

TP-5(07)
TP-6(07)

Log Number 002

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green
Address 260 W 26th St NY, NY
Phone No.

Generator Site/Location Same
Address
Phone No.

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

Approval Number 04-8199

ID 279
GROSS 51.89 T GROSS
TARE 13.28 T TARE
RECYCLED
NET 38.61 T NET
LOG 20
11/02/2011 TONNAGE
11:10AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 11/2/11
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somers Sel LLC. Truck 1
Address 822 Union Ave Belmar NJ 07719

Driver Name (Print) Jose Tapia
Vehicle License No. / State / EPA No. AM 3867
Truck Number 22

I hereby certify that the above named material was picked up at the generator site listed above.

11-2-11
Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

11-2-11
Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Conroy — 11 2 11
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

IP-S (0-1)
TP-6 (0-7)

Log Number 001

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green
Address 260 W 26th St NY, NY
Phone No.

Generator Site/Location Same
Address
Phone No. 111-291

Description of Material

Approval Number C4-8199

Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

GROSS 50.24 GROSS
RECALLED
TARE 13.65 TARE
NET 36.59 NET
LOC 22
11/02/2011 TONNAGE
11:16AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 11/2/11
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somerset LLC Transportation
Address Vineland, NJ

Driver Name (Print) Jonathon Uttaro
Vehicle License No. / State / EPA No. AN 404P
Truck Number Shuler # 09

I hereby certify that the above named material was picked up at the generator site listed above.

11/2/11
Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

11/2/11
Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

A. Garcia — 11.2.11
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TPS (7-14)

Log Number 003

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 26th St NY, NY

Phone No.

Generator Site/Location Same

Address

Phone No.

Approval Number CY-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

10 S90

GROSS 53.82 T GROSS

TARE 13.68 T TARE

RECALCED

NET 40.14 T NET

LOG 29

11/02/2011

11:00PM

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — Signature — 11/1/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Soil Safe, LLC

Address 4 Middle Rd

Driver Name (Print) Fabian Velasquez

Vehicle License No. / State / EPA No. DR 9345

Truck Number Shorty 12

I hereby certify that the above named material was picked up at the generator site listed above.

11-02-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

11-02-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Garcia — 11.2.11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-5 (0-2)

SOIL SAFE, INC.

Log Number 004

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location Same

Address 260 West 28th St NY, NY | Address

Phone No. | Phone No.

Approval Number C4-8196

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 646
GROSS 51.66 T — GROSS
TARE 13.42 T — TARE
RECALCED
NET 38.24 T — NET
LOG 32
11/02/2011 — TONNAGE
01:20PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator | 11/1/11
Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name Sapsucker Farm Landscapes | Driver Name (Print) Ramiro V

Address Montpelier VT | Vehicle License No. / State / EPA No. AM395

Truck Number 9

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature | 11-2-11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature | 11-2-11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent | Signature | 11.2.11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP5 (0-7)

SOIL SAFE, INC.

Log Number 005

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 26th St NY, NY

Phone No.

Generator Site/Location Same

Address

Phone No.

Approval Number 04-8119

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 406
GROSS 50.93 T
TARE 13.60 T
RECALLED
NET 37.31 T
LOG 43
11/02/2011
03:05PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

agent to generator — 11/8/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Some Sol Management

Address Mickleton NJ 08

Driver Name (Print) Leonardo Sacros Alan J.

Vehicle License No. / State / EPA No.

Truck Number

I hereby certify that the above named material was picked up at the generator site listed above.

11-2-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

11-2-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Coaton 11 2 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-S (07)

SOIL SAFE, INC.

Log Number 007

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Generator Site/Location Same

Address 260 West 26th St

NY, NY

Address

Phone No.

Phone No. 10 107

Approval Number C4-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS 55.38 T
TARE 13.86 GROSS
RECALLED 41.52 TTARE
NET 45 NET
LOG
11/02/2011 TONNAGE
03:28PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 11/2/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Same Set

Transporter Name — Driver Name (Print) JAIRO

Address — Vehicle License No. / State / EPA No. AN969F

Truck Number RLS # 38

I hereby certify that the above named material was picked up at the generator site listed above.

11-2-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

11-2-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 11 2 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-5 (MM) (7-14)

SOIL SAFE, INC.

Log Number 006

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 28th St NY, NY

Phone No.

Generator Site/Location Same

Address

Phone No.

Approval Number cy-899

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 655
GROSS 55.56 T GROSS
TARE 13.95 T TARE
RECALCED
NET 41.61 T NET
LOG 46
11/02/2011 TONNAGE
03:31PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 11/2/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Some Set (Apex Interstate)

Address 1111 Route 220

Juggle Trucking LLC.

Driver Name (Print) Juler Tapia

Vehicle License No. / State / EPA No. AP870W

Truck Number 14 #655 Soil Safe

I hereby certify that the above named material was picked up at the generator site listed above.

11/2/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

11/2/11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Carlo — 11/2/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-6 (07)
TP-SC7-14

Log Number 008

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green
Address 260 West 26th St
NY NY
Phone No.

Generator Site/Location Same
Address
Phone No.

ID 588
GROSS 51.23 T GROSS
TARE 14.31 T
RECALLED
NET 36.92 T TARE
LOG 47 NET
11/02/2011
09:37PM TONNAGE

Approval Number C4-899

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 11/1/11
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somerset Area Recycling
Address Branchville, Conn.

Driver Name (Print) Benjamin Rowe
Vehicle License No. / State / EPA No. AM1096
Truck Number #12

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 11/2/11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 11/2/11 Delivery Date

DESTINATION

Site Name Soil Safe, Inc. - Bridgeport
Phone No. 1-856-467-8030

Address 378 Route 130 Logan Township, NJ 08085

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Corna — 11-2-11
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-SC(7-14)

Log Number 009

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Generator Site/Location Same

Address 260 West 36th St

NY, NY

Address

Phone No.

Phone No.

Approval Number 04-8194

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

10 515

GROSS 49.88 T GROSS

TARE 12.99 T TARE

RECALLED

NET 51 36.89 T NET

LOG

11/02/2011 TONNAGE

03:55PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

CAS agent for generator — 11/2/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somerset — Driver Name (Print) Dan Gilson

Address Green — Vehicle License No. / State / EPA No. CDM536E

Truck Number 525

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date 11/2/11

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date 11/2/11

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Gorman — 11/2/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-SC7-14

SOIL SAFE, INC.

Log Number 009010

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 26th St NY, NY

Phone No.

Generator Site/Location Same

Address

ID 680

Phone No.

GROSS 47.31 T
TARE 13.69 T
RECALLED
NET 33.62 T
LOG 5 2
11/02/2011
08:59PM

GROSS
TARE
NET
TONNAGE

Approval Number 04-899

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 11/2/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somer Set

Driver Name (Print) WALTON

Address

Vehicle License No. / State / EPA No. AM1331D

Truck Number F02 SS680

I hereby certify that the above named material was picked up at the generator site listed above.

11/02/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

11/02/11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Escio — 11 2 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 012

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST TP5 (7-14)

GENERATOR

Generator Name Chelsea Green | Generator Site/Location

Address 200 W. 26th St. NY, NY | Address

Phone No. | Phone No.

Approval Number C4- 8199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 279
GROSS 55.09 T GROSS
TARE 13.28 T TARE
RECALLED
NET 41.81 T NET
LOG SY
11/02/2011 TONNAGE
05:37PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

CHRISTINE MIEHR | Signature | 11/2/11
Generator Authorized Agent Name | Shipment Date

TRANSPORTER

Transporter Name Sonner Sct | Driver Name (Print) Jose Tapia

Address Rosetta Stone Trucking Inc 123 Onion A. Blvd Nw | Vehicle License No. / State / EPA No. AM 3864

Truck Number 22

I hereby certify that the above named material was picked up at the generator site listed above.

11-2-11
Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

11-2-11
Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent | Signature | 11/2/11 Receipt Date

White - Facility | Green - Facility | Yellow - Generator | Pink - Broker | Goldenrod - Contractor | Blue - Trucking Co.

Log Number 011

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

TP5 (7-14)
JG (6-7)

GENERATOR

Generator Name Chelsea Green
Address 240 W. 24th St. NY, NY
Phone No.

Generator Site/Location
Address SAME
Phone No.

Approval Number C9 2197

Description of Material
Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

ID 758
GROSS 51.87 T
TARE 14.09 T
RECALLED
NET 37.78 T
LOG 1
11/03/2011
07:43AM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

CHRISTINE HEAR — 11/2/11
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Omer Set
Address Metal Trucking
Driver Name (Print) Carlos ?
Vehicle License No. / State / EPA No. AK776K 682
Truck Number 758

I hereby certify that the above named material was picked up at the generator site listed above.

11/02/11
Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

11/02/11
Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**
Address **378 Route 130 Logan Township, NJ 08085**
No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 11/3/11
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-5 (6-7)

SOIL SAFE, INC.

Log Number 001

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 36th St NY NY

Phone No.

Generator Site/Location Same

Address

Phone No.

Approval Number 04-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

10 108
GROSS 52.81 T GROSS
TARE 13.68 T TARE
RECALLED
NET 39.13 T NET
LOG 12
11/03/2011
11:05AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 11/3/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somerset

Address

Driver Name (Print) SPIRO

Vehicle License No. / State / EPA No. AN 969F

Truck Number RLS # 38

I hereby certify that the above named material was picked up at the generator site listed above.

11-3-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

11-3-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Carla — 11.3.11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-5 (0-7)

SOIL SAFE, INC.

Log Number 002

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 26th St NY, NY

Phone No.

Generator Site/Location Sand

Address

Phone No.

Approval Number C4-8149

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 593
GROSS
TARE
RECALLED
NET
LOG 16
11/03/2011
11:30AM

52.98 T	GROSS
14.31 T	TARE
38.67 T	NET
	TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent for generator — 11/3/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name

Address

Driver Name (Print) Benjamin Picard

Vehicle License No. / State / EPA No. NJ 109E

Truck Number 18 593

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 11/3/11 — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 11/3/11 — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Gavon — 10/3/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-5 (10-19)
16 (0-7)

Log Number 005

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green
Address 260 West 26th St
N.Y., NY
Phone No.

Generator Site/Location Same
Address
Phone No.

Description of Material

Approval Number C4-9199

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 279
GROSS 50.82 T
TARE 13.28 T
RECALLED
NET 37.54 T
LOG 22
11/03/2011
12:21PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — 11/3/11

Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name Somer Set
Address Rosetta Stone Trucking
125 Union Ave.

Driver Name (Print) Jose Tapia
Vehicle License No. / State / EPA No. AM38 6V
Truck Number 22

I hereby certify that the above named material was picked up at the generator site listed above.

11-3-11
Driver Signature / Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

11-3-11
Driver Signature / Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 11.3.11
Name of Authorized Agent / Signature / Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-5(0-7)

Log Number 006

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location Same

Address 260 W 26th St NY, NY | Address

Phone No. | Phone No.

Approval Number 01-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 1055
GROSS 50.68 GROSS
TARE 14.04
RECALCED
NET 23 36.64 TARE
LOG NET
11/03/2011
12:24PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator | 11/3/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name J&J Sewer Set | Driver Name (Print) Gustavo Muñoz

Address 67 Winthrop St Newark NJ | Vehicle License No. / State / EPA No. [redacted] TAN844MG

Truck Number 98/1065

I hereby certify that the above named material was picked up at the generator site listed above.

11/3/11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

11/3/11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia | 11-3-11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-S(6-7)

SOIL SAFE, INC.

Log Number: 004

NON-HAZARDOUS MATERIAL MANIFEST

Arrive 7:00 am Leave 9:30 am

GENERATOR

Generator Name: 260 Chelsea Green | Generator Site/Location: Same

Address: 260 W 26th St NY, NY | Address:

Phone No. | Phone No.

Approval Number: 04-899

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID .0293
GROSS 49.49 T GROSS
RECALLED
TARE 13.13 T TARE
NET 36.00 T NET
LOG 24
11/03/2011 TONNAGE
12:27PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 11/3/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name: Somers Cat | Driver Name (Print): Ray F Toro

Address | Vehicle License No. / State / EPA No.: 5A44SK

Truck Number: 20

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature | Shipment Date: 11/3/11

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature | Delivery Date: 11/3/11

DESTINATION

Site Name: Soil Safe, Inc. - Bridgeport | Phone No.: 1-856-467-8030

Address: 378 Route 130 Logan Township, NJ 08085

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Gorog — 11.3.11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-S (0-14)
26 (07)

Log Number 003

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location Same

Address 260 W 26th St NY, NY | Address

Phone No. | Phone No. 10 646

Approval Number C4-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS 55.03 GROSS
TARE 13.42 TARE
RECALLED
NET 29 41.61 NET
LOG
11/03/2011
01:01PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator 11/3/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name Somer Set | Driver Name (Print) Robinson Velarde

Address | Vehicle License No. / State / EPA No. AM3452

Truck Number 9

I hereby certify that the above named material was picked up at the generator site listed above.

Robinson Velarde 11-3-11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Robinson 11-3-11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

A. Garcia 11.3.11

Name of Authorized Agent | Signature | Receipt Date

White - Facility | Green - Facility | Yellow - Generator | Pink - Broker | Goldenrod - Contractor | Blue - Trucking Co.

TP-S(0-7)

Log Number 007

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location Same

Address 260 W 36th St NY, NY | Address

Phone No. | Phone No.

Approval Number 24-8199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 740
GROSS 49.44 T — GROSS
TARE 13.06 T — TARE
RECALLED
NET 36.38 T — NET
LOG 34
11/03/2011
02:34PM — TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — Signature — 11/3/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name Soms Set | Driver Name (Print) Angel Gomez

Address Melville N.Y. | Vehicle License No. / State / EPA No. AV375K

Truck Number 88

I hereby certify that the above named material was picked up at the generator site listed above.

11-3-11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

11-3-11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia — 11.3.11

Name of Authorized Agent | Signature | Receipt Date

White - Facility | Green - Facility | Yellow - Generator | Pink - Broker | Goldenrod - Contractor | Blue - Trucking Co.

TP-S (0-9)

SOIL SAFE, INC.

Log Number 008

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 26th Street NY, NY

Phone No.

Generator Site/Location Same

Address

Phone No.

Approval Number C4-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 108
GROSS 50.05 GROSS
TARE 13.68 T
RECALLED TARE
NET 36.37 T
LOG 37 NET
11/03/2011
03:49PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 11/3/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somer Set

Address

Driver Name (Print) JAIRO

Vehicle License No. / State / EPA No. AN9694F

Truck Number R25 FF 38

I hereby certify that the above named material was picked up at the generator site listed above.

11-3-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

11-3-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Gaton 11.3.11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TRES(0-7)

SOIL SAFE, INC.

Log Number 009

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 36th Street NY, NY

Phone No.

Generator Site/Location Sand

Address

Phone No.

Approval Number CY-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 593
GROSS 48.94 T
TARE 13.43 T
RECYCLED
NET 35.45 T
LOG 42
11/03/2011
04:04PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 11/3/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somer Set

Address

Driver Name (Print) Benjamin Reams

Vehicle License No. / State / EPA No. AR 107E

Truck Number 18

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 11.3.11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-5(0-2)

SOIL SAFE, INC.

Log Number 010

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 26th St NY, NY

Phone No.

Generator Site/Location Same

Address

Phone No. 11 SSU

Approval Number 24299

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS 48.70 GROSS
TARE 13.68 T
RECALLED TARE
NET 44 35.02 T
LOC NET
11/03/2011
04:51PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 11/3/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Sonar Set

Address

Driver Name (Print) Fabian Velarde

Vehicle License No. / State / EPA No. AM 934F

Truck Number Shelly 12

I hereby certify that the above named material was picked up at the generator site listed above.

11-03-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

11-03-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130, Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Coucu — 11.3.11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-S
C&D

SOIL SAFE, INC.

Log Number: 011

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name: Chelsea Green
Address: 260 West 26th St
NY, NY
Phone No.:

Generator Site/Location: Same
Address:
Phone No.:

Approval Number: C4-8199

Description of Material:
Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

ID 279
GROSS 48.75 T
TARE 13.28 T
RECALLED
NET 35.47 T
LOG 45
11/03/2011
05:12PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS agent to generator — Signature — 11/3/11
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name: Somer Sat
Address: Route 130 Logan Twp. NJ
125 Union Ave.

Driver Name (Print): Jose Tapia
Vehicle License No. / State / EPA No.: P M386
Truck Number: 28

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 11-3-11 — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 11-3-11 — Delivery Date

DESTINATION

Site Name: **Soil Safe, Inc. - Bridgeport** Phone No.: **1-856-467-8030**

Address: **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garon — 11-3-11
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co

TP-5 (0-7 ft)

SOIL SAFE, INC.

Log Number 001

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Grand — Generator Site/Location Same

Address 260 West 26th St — Address

NY, NY

Phone No. — Phone No.

Approval Number 5199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 740		GROSS
GROSS	43.64 T	TARE
TARE	13.06 T	
RECALLED		NET
NET	30.58 T	
LOG 1		TONNAGE
11/04/2011		
10:50AM		

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 11/4/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somer Set — Driver Name (Print) Angel Nunez

Address — Vehicle License No. / State / EPA No. AM 375 KC

Truck Number

I hereby certify that the above named material was picked up at the generator site listed above.

11-4-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** — Phone No. **1-856-467-8030**

Address **378 Route 130, Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Carew — 11 4 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-SCO-7 (4)

SOIL SAFE, INC.

Log Number 003

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 260 W 26th St NY, NY

Phone No.

Generator Site/Location Same

Address

Phone No.

Approval Number 04-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 279
GROSS 47.90 T GROSS
TARE 13.28 T TARE
RECALLED
NET 34.62 T NET
LOG
11/04/2011
10:06AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 11/4/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Soma Sol

Address Roscitano Trucking 125 Union Ave Belleville NJ

Driver Name (Print) Jose Tapia

Vehicle License No. / State / EPA No. PM386Y

Truck Number 22

I hereby certify that the above named material was picked up at the generator site listed above.

11-4-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

11-4-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Carai — 11-4-11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-S(0-7 FT)

SOIL SAFE, INC.

Log Number 23002

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 23rd St

NY, NY

Phone No.

Generator Site/Location Same

Address

Phone No. 10 655

Approval Number 24-8189

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS 50.03 GROSS
TARE 13.95 TARE
RECALLED
NET 36.08 NET
LOG 3
11/04/2011
10:08AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — 11/4/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Soil Set

Address Augusta Trucking LLC. (Manufacturer) Ft. Myers FL

Driver Name (Print) James Tapia

Vehicle License No. / State / EPA No. AU870W

Truck Number # 14 Soil Safe 655

I hereby certify that the above named material was picked up at the generator site listed above.

11/4/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

11/4/11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 11-4-11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4(0-2)

SOIL SAFE, INC.

Log Number 001

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 25th St

NY, NY

Phone No.

Generator Site/Location

Address

Phone No.

Approval Number C4-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 1065

GROSS	47.93 T	GROSS
TARE	14.04 T	TARE
RECALLED		
NET	33.89 T	NET

LOG 17
11/15/2011
09:46AM

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 11/15/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somer Set

Address 64 Wentworth

Newark NJ 07107

Driver Name (Print) Cristian Muñoz

Vehicle License No. / State / EPA No. AN84YM NJ

Truck Number 98 / 1065

I hereby certify that the above named material was picked up at the generator site listed above.

11/15/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

11/15/11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 11-15-11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-2(0-7)

SOIL SAFE, INC.

Log Number 002

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 25th St
NY, NY

Phone No.

Generator Site/Location

Address

Phone No.

Approval Number
CH-2199

Description of Material

Non-Regulated Petroleum
Contaminated Soil

Non DOT/RCRA Regulated

ID 122
GROSS 43.92 T GROSS
TARE 13.72 T TARE
RECALLED
NET 30.20 T NET
LOG 18
11/15/2011
09:42AM
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator
Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name Soler SU

Address JRJ Bros
Newark NJ

Driver Name (Print) Marco Munoz

Vehicle License No. / State / EPA No. AL 3632

Truck Number 69 / 122

I hereby certify that the above named material was picked up at the generator site listed above.

Marco Munoz
as agent to Soler SU 11-15-11
Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

MarcoM 11-15-11
Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130, Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia 11-15-11
Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-2 (7-14)

Log Number 003

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 26th St NY, NY

Phone No.

Generator Site/Location Same

Address

Phone No.

Approval Number C4-879

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 279
GROSS 48.22 T GROSS
TARE 13.28 T TARE
RECALCED
NET 34.94 T NET
LOG 24
11/15/2011 TONNAGE
10:20AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator Jeff 11/15/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name Somar SW

Address Montville, NJ

Driver Name (Print) Jose Tapia

Vehicle License No. / State / EPA No. AM38K

Truck Number 92

I hereby certify that the above named material was picked up at the generator site listed above.

11-15-11

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

11-15-11

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia 11.15.11

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

(OITP-4(0->)

Log Number 004

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 250 W 26th St NY, NY

Phone No.

Generator Site/Location

Address

Phone No.

Approval Number 4-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID SSS
GROSS 44.13 GROSS
TARE 13.91 T TARE
RECALLED
NET 30.22 T NET
LOG 34
11/15/2011
10:53AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent for Jhonald 11/15/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name Somer Sal

Address Montville, NJ

Driver Name (Print) Shane B Zeman

Vehicle License No. / State / EPA No. AL 862 K

Truck Number 7 - 553

I hereby certify that the above named material was picked up at the generator site listed above.

11.15.11

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

11.15.11

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Conlon 11.15.11

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-2(07)

Log Number 007

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 26th St NY, NY

Phone No.

Generator Site/Location Same

Address

Phone No.

Approval Number C4-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 279
GROSS 50.83 T GROSS
TARE 13.28 T TARE
RECALLED
NET 37.55 T NET
LOG 109
11/15/2011
08:30PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — 11/15/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name SomerSet

Address Route 1 South Truck, 125 Union Ave. Bldg

Driver Name (Print) José Tapia

Vehicle License No. / State / EPA No. AM 386Y

Truck Number 9C

I hereby certify that the above named material was picked up at the generator site listed above.

11-15-11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

11-15-11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent | Signature | 11.15.11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4 (07)

Log Number 005

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location Same

Address 260 West 25th St NY, NY | Address

Phone No. | Phone No.

Approval Number CY-899

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 1065
GROSS 41.49 T GROSS
TARE 14.04 T TARE
RECALLED
NET 27.45 T NET
LOG 1
11/16/2011
07:09AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator | 11/15/11

Generator/Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

307

Transporter Name Sonar Sol | Driver Name (Print) Cristian Muñoz

Address 67 Winthrop Ct Lawrenceville | Vehicle License No. / State / EPA No. AN8442 (NJ)

Truck Number 98 / 1065

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature | Shipment Date 11/15/11

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature | Delivery Date 11/15/11

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

2 | Corcia | 11-16-11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-20(0-7)

SOIL SAFE, INC.

Log Number 006

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 26th St

NY, NY

Phone No.

Generator Site/Location Same

Address

Phone No.

Approval Number SU-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 122
GROSS 49.94 T
TARE 13.72 T
RECALCED
NET 36.22 T
LOG 2
11/15/2011
07:32AM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 11/15/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somerset

Address JK J Bros

Newark NJ

Driver Name (Print) Marco Muñoz

Vehicle License No. / State / EPA No. AL 363C

Truck Number 69

I hereby certify that the above named material was picked up at the generator site listed above.

Marco Muñoz 11-15-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Marco Muñoz 11-15-11

Driver Signature — Delivery Date

DESTINATION

Site Name Soil Safe, Inc. - Bridgeport Phone No. 1-856-467-8030

Address 378 Route 130, Logan Township, NJ 08085

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Garcia 11-16-11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-400-7

SOIL SAFE, INC.

Log Number 001

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4-5190

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

LOT 240

GROSS 49.76 T GROSS

TARE 13.06 T TARE

RECALLED NET 36.70 T NET

LOG 9

11/17/2011

10:05AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to Monarch — 11/17/11

Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 291-4020

Driver Name (Print) ONRUBIA, OBED

Vehicle License No. / State / EPA No. AN312R

Truck Number 2

I hereby certify that the above named material was picked up at the generator site listed above.

11-17-11

Driver Signature / Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

11-17-11

Driver Signature / Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. GARCIA — 11/17/11

Name of Authorized Agent / Signature / Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-8 (second)
(C-47)

Log Number 002

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4 8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID T73
GROSS 42.07 T GROSS
TARE 13.60 T TARE
RECALLED
NET 28.47 T NET
LOG 14
11/17/2011 TONNAGE
10:23AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 11/17/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 784-4020

Driver Name (Print) Angel Nunez

Vehicle License No. / State / EPA No. AW 325K

Truck Number 88 551(279)

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 11-17-11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 11-17-11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 11/17/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-1 (7-14)

SOIL SAFE, INC.

Log Number 804

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4 8199

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 555
GROSS 48.14 T
TARE 13.91 T
RECALLED
NET 34.23 T
48
LOG
11/17/2011
03:09PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 11/17/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) JAIME L. EMA

Vehicle License No. / State / EPA No. AL862R

Truck Number 7 555

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 11.17.11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 11.17.11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 11/17/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-10-14

Log Number 003

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Generator Site/Location

Address 240 WEST 26TH STREET

Address SAME

NY, NY

Phone No.

Phone No.

Description of Material

Approval Number	Description of Material
C48199	Non-Regulated Petroleum Contaminated Soil Non DOT/RCRA Regulated

ID TAG
GROSS 54.43 GROSS
TARE 13.06 T
RECALLED TARE
NET 41.37 T
49 NET
LOG
11/17/2011
09:19PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS AGENT TO GENERATOR 11/17/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Driver Name (Print) CHRIS ORT

Address MONTVILLE, NJ

Vehicle License No. / State / EPA No. 748 AU 3128

Truck Number 12

(973) 784-4020

I hereby certify that the above named material was picked up at the generator site listed above.

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature 11/17/11 Shipment Date

Driver Signature 11/17/11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia 11/17/11

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3 @ 1'
0-14'

Log Number 005

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 28TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number	Description of Material
C4-8199	Non-Regulated Petroleum Contaminated Soil Non DOT/RCRA Regulated

ID 612
GROSS 53.30 T
TARE 12.50 T
RECALLED
NET 40.80 T
LOG S2
11/17/2011
08:51PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 11/17/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 394-6020

Driver Name (Print) FRED

Vehicle License No. / State / EPA No. AK 5177

Truck Number (62)

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature | 11/17/11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent | Signature | 11/17/11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3 1'
P-14

Log Number 005

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 26th St
NY NY

Phone No.

Generator Site/Location Same

Address

Phone No.

Approval Number 24-9199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 279
GROSS 45.12 T
TARE 13.28 T
REJECTED
NET 31.84 T
LOG 55
11/17/2011
@ 2PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

QS agent for generator — 11/17/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somers Spt

Address Montville, NJ

Driver Name (Print) Angel Nunez

Vehicle License No. / State / EPA No. 277

Truck Number

I hereby certify that the above named material was picked up at the generator site listed above.

11-17-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garc. G — 11/17/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 111811

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C45199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

TP-3 (7-14)

10 T40

GROSS 40.56 T GROSS

TARE 13.06 T TARE

RECALLED

NET 27.50 T NET

LOG 31

11/18/2011 TONNAGE

10:03AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Abbot Stephen Mahowski — 11/18/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 394-4020

Driver Name (Print) CARLOS OLIVO

Vehicle License No. / State / EPA No. AW-312R NJ

Truck Number 12

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date 11/18/11

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date 11-18-11

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 11.18.11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 1118103

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4.8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

TP-3 7-14

ID 279
GROSS 46.91 GROSS
TARE 13.28 T
RECALLED TARE
NET 33.63 T NET
LOG 43
11/18/2011 TONNAGE
10:29AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As Agent Stephanowski 11/18/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) Jose Tapia

Vehicle License No. / State / EPA No. AN 375 KM

Truck Number 88

I hereby certify that the above named material was picked up at the generator site listed above.

11-18-11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

11-18-11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia 11-18-11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 111811 02

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN | Generator Site/Location

Address 260 WEST 26TH STREET | Address SAME

NY, NY

Phone No. | Phone No.

Approval Number C4.8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

TP-3 7-14

ID 761
GROSS 12.08 T GROSS
TARE 13.22 T
RECALLED TARE
NET 28.86 T NET
LOG 53
11/18/2011 TONNAGE
10:52AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as Agent Stefan Malinowski | Stefan Malinowski | 11/13/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC | Driver Name (Print) Angel Nieves

Address MONTVILLE, NJ | Vehicle License No. / State / EPA No. AV-313R NJ

(973) 794-4020 | Truck Number 761

I hereby certify that the above named material was picked up at the generator site listed above.

11-18-11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

11-18-11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia | 11-18-11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 111811 04

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4-5190

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

TP-3 (7-14

ID 740
GROSS 49.87 T GROSS
TARE 13.06 T TARE
RECALCED
NET 36.81 T NET
LOG 98
11/18/2011 TONNAGE
02:35PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Generator Authorized Agent Name | Signature | Shipment Date 11/18/11

TRANSPORTER

Transporter Name SOMERSET LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) CAROL CERZ

Vehicle License No. / State / EPA No. AN312R

Truck Number 92

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature | Shipment Date 11-18-11

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature | Delivery Date 11-18-11

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent | Signature Carol | Receipt Date 11-18-11

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number
1118106

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No. 10 279

Approval Number
C4 8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

TP-3 11 7-14

GROSS 47.31 GROSS
TARE 13.28 TARE
RECALLED
NET 34.03 NET
LOG 12
11/18/2011
04:12PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Dan T 11-18-11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 701-4020

Driver Name (Print) José Tapia

Vehicle License No. / State / EPA No. AN 375K

Truck Number 80 279

I hereby certify that the above named material was picked up at the generator site listed above.

11-18-11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

11-18-11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

E J Curtis 11/18/11

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 111805

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No. 10 761

Approval Number C4 8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

TP-3 7-14

GROSS 42.10 T
TARE 19.22
RECALLED
NET 28.88 T
LOG 115
11/18/2011
04:41PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Generator Authorized Agent Name | Signature | Shipment Date 11/18/11

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) Angel Lluna

Vehicle License No. / State / EPA No. AV 313 H

Truck Number 01 761

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature | Shipment Date 11-18-11

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature | Delivery Date 11-18-11

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent | Signature | Receipt Date 11/18/11

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3 (07-11)

Log Number 001

SOIL SAFE, INC.

26.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 36th St NY, NY

Phone No.

Generator Site/Location Same

Address

Phone No.

Approval Number C-H 8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 600
GROSS 46.62 T
TARE 13.28 T
RECALLED
NET 33.34 T
LOGS
01/16/2012
09:46AM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — 1/16/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Carlo Lanza

Address 11 Rosset Ave East Hanover NJ

Driver Name (Print) Edchampion

Vehicle License No. / State / EPA No. AM 185 A

Truck Number 20, 14

I hereby certify that the above named material was picked up at the generator site listed above.

Edward Champion 1-16-12

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Edward Champion 1-16-12

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130, Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia 1/16/12

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3(7-14)

SOIL SAFE, INC.

Log Number 002

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Grn Sq. | Generator Site/Location

Address 260 West 20th NY, NY | Address Same

Phone No. | Phone No.

Approval Number 04-819

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID TSB
GROSS 50.85 T GROSS
TARE 14.69 T TARE
RECALLED
NET 36.16 T NET
LOG 6
01/16/2012 TONNAGE
09:43AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent for generator — 1/16/12

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name Patten Trucking | Driver Name (Print) Carlos F

Address Wayne NJ | Vehicle License No. / State / EPA No. AW 770K

Truck Number 807

I hereby certify that the above named material was picked up at the generator site listed above.

1/16/12

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

1/16/12

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3(7-14)

SOIL SAFE, INC.

Log Number 003

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W. 26th Street

Phone No.

Generator Site/Location Same

Address

Phone No.

Approval Number C4-8M

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 536
GROSS 54.27 T GROSS
TARE 14.44 T TARE
RECEIVED
NET 39.83 T NET
LOG 9
01/16/2012 TONNAGE
10:13AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent for generator — 1/16/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name R. Castillo & Sons

Address 44 Bedford St.
East Orange NJ

Driver Name (Print) Stephen Bianculli

Vehicle License No. / State / EPA No. AM(789)

Truck Number 16

I hereby certify that the above named material was picked up at the generator site listed above.

1-16-12

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

1-16-12

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Carlos — 1/16/12

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3 (0-14)

SOIL SAFE, INC.

Log Number 004

JG.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W. 28th St

New York, NY

Phone No.

Generator Site/Location

Address Same

Phone No.

Approval Number C4 8179

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 738
GROSS 51.17 T
TARE 14.37 T
RECALLED
NET 36.80 T
LOG 12
01/18/2012
10:19AM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 1/16/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name P.A. Carrillo

Address E. Orange, N.J.

Driver Name (Print) Orlando Jackson

Vehicle License No. / State / EPA No. AN280R-NJ

Truck Number 738

I hereby certify that the above named material was picked up at the generator site listed above.

Orlando Carrillo 1-16-12

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

1-16-12

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 1/16/12

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3 (5-14)

Log Number 005

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 209 West 20th St NY, NY

Phone No.

Generator Site/Location

Address Same

Phone No.

ID 628

GROSS 47.59 GROSS
TARE 13.42 T TARE
REBILLED NET 34.17 T NET
LOG 27 TONNAGE
01/16/2012
11:53AM

Approval Number CY-899

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS Agent to Generator — 1/16/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name T-MAX

Address Kearny, NJ

Driver Name (Print) Juan

Vehicle License No. / State / EPA No. AK 833 H

Truck Number 628

I hereby certify that the above named material was picked up at the generator site listed above.

01 16 12

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 1/16/12

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

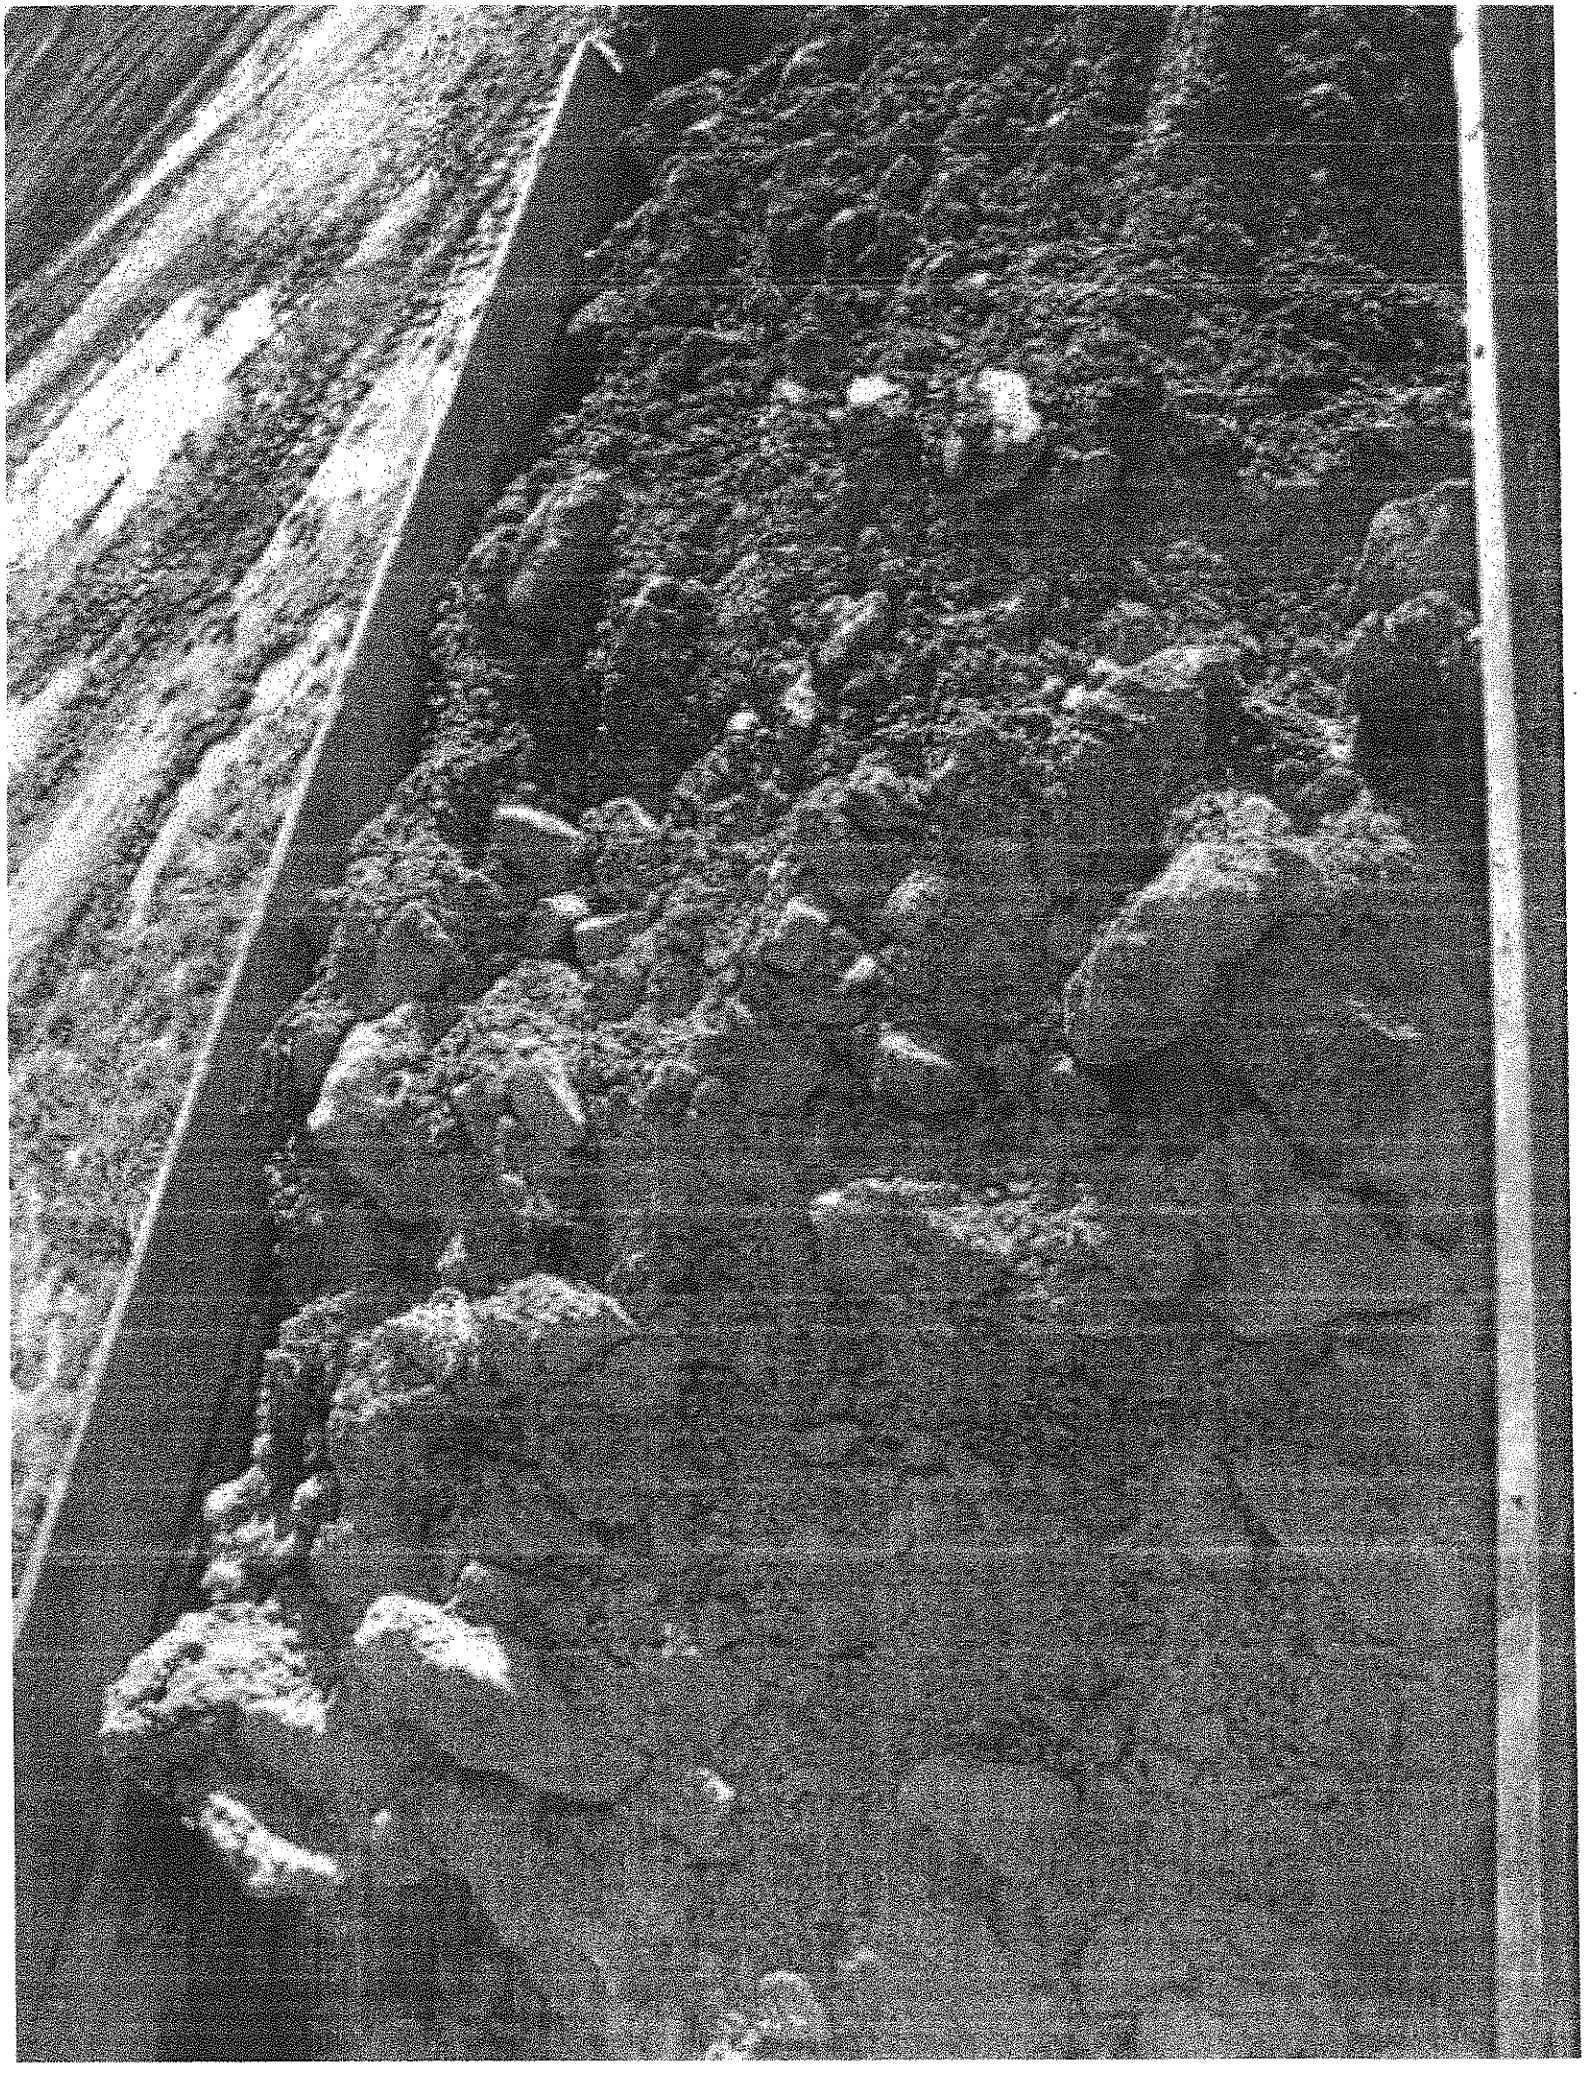

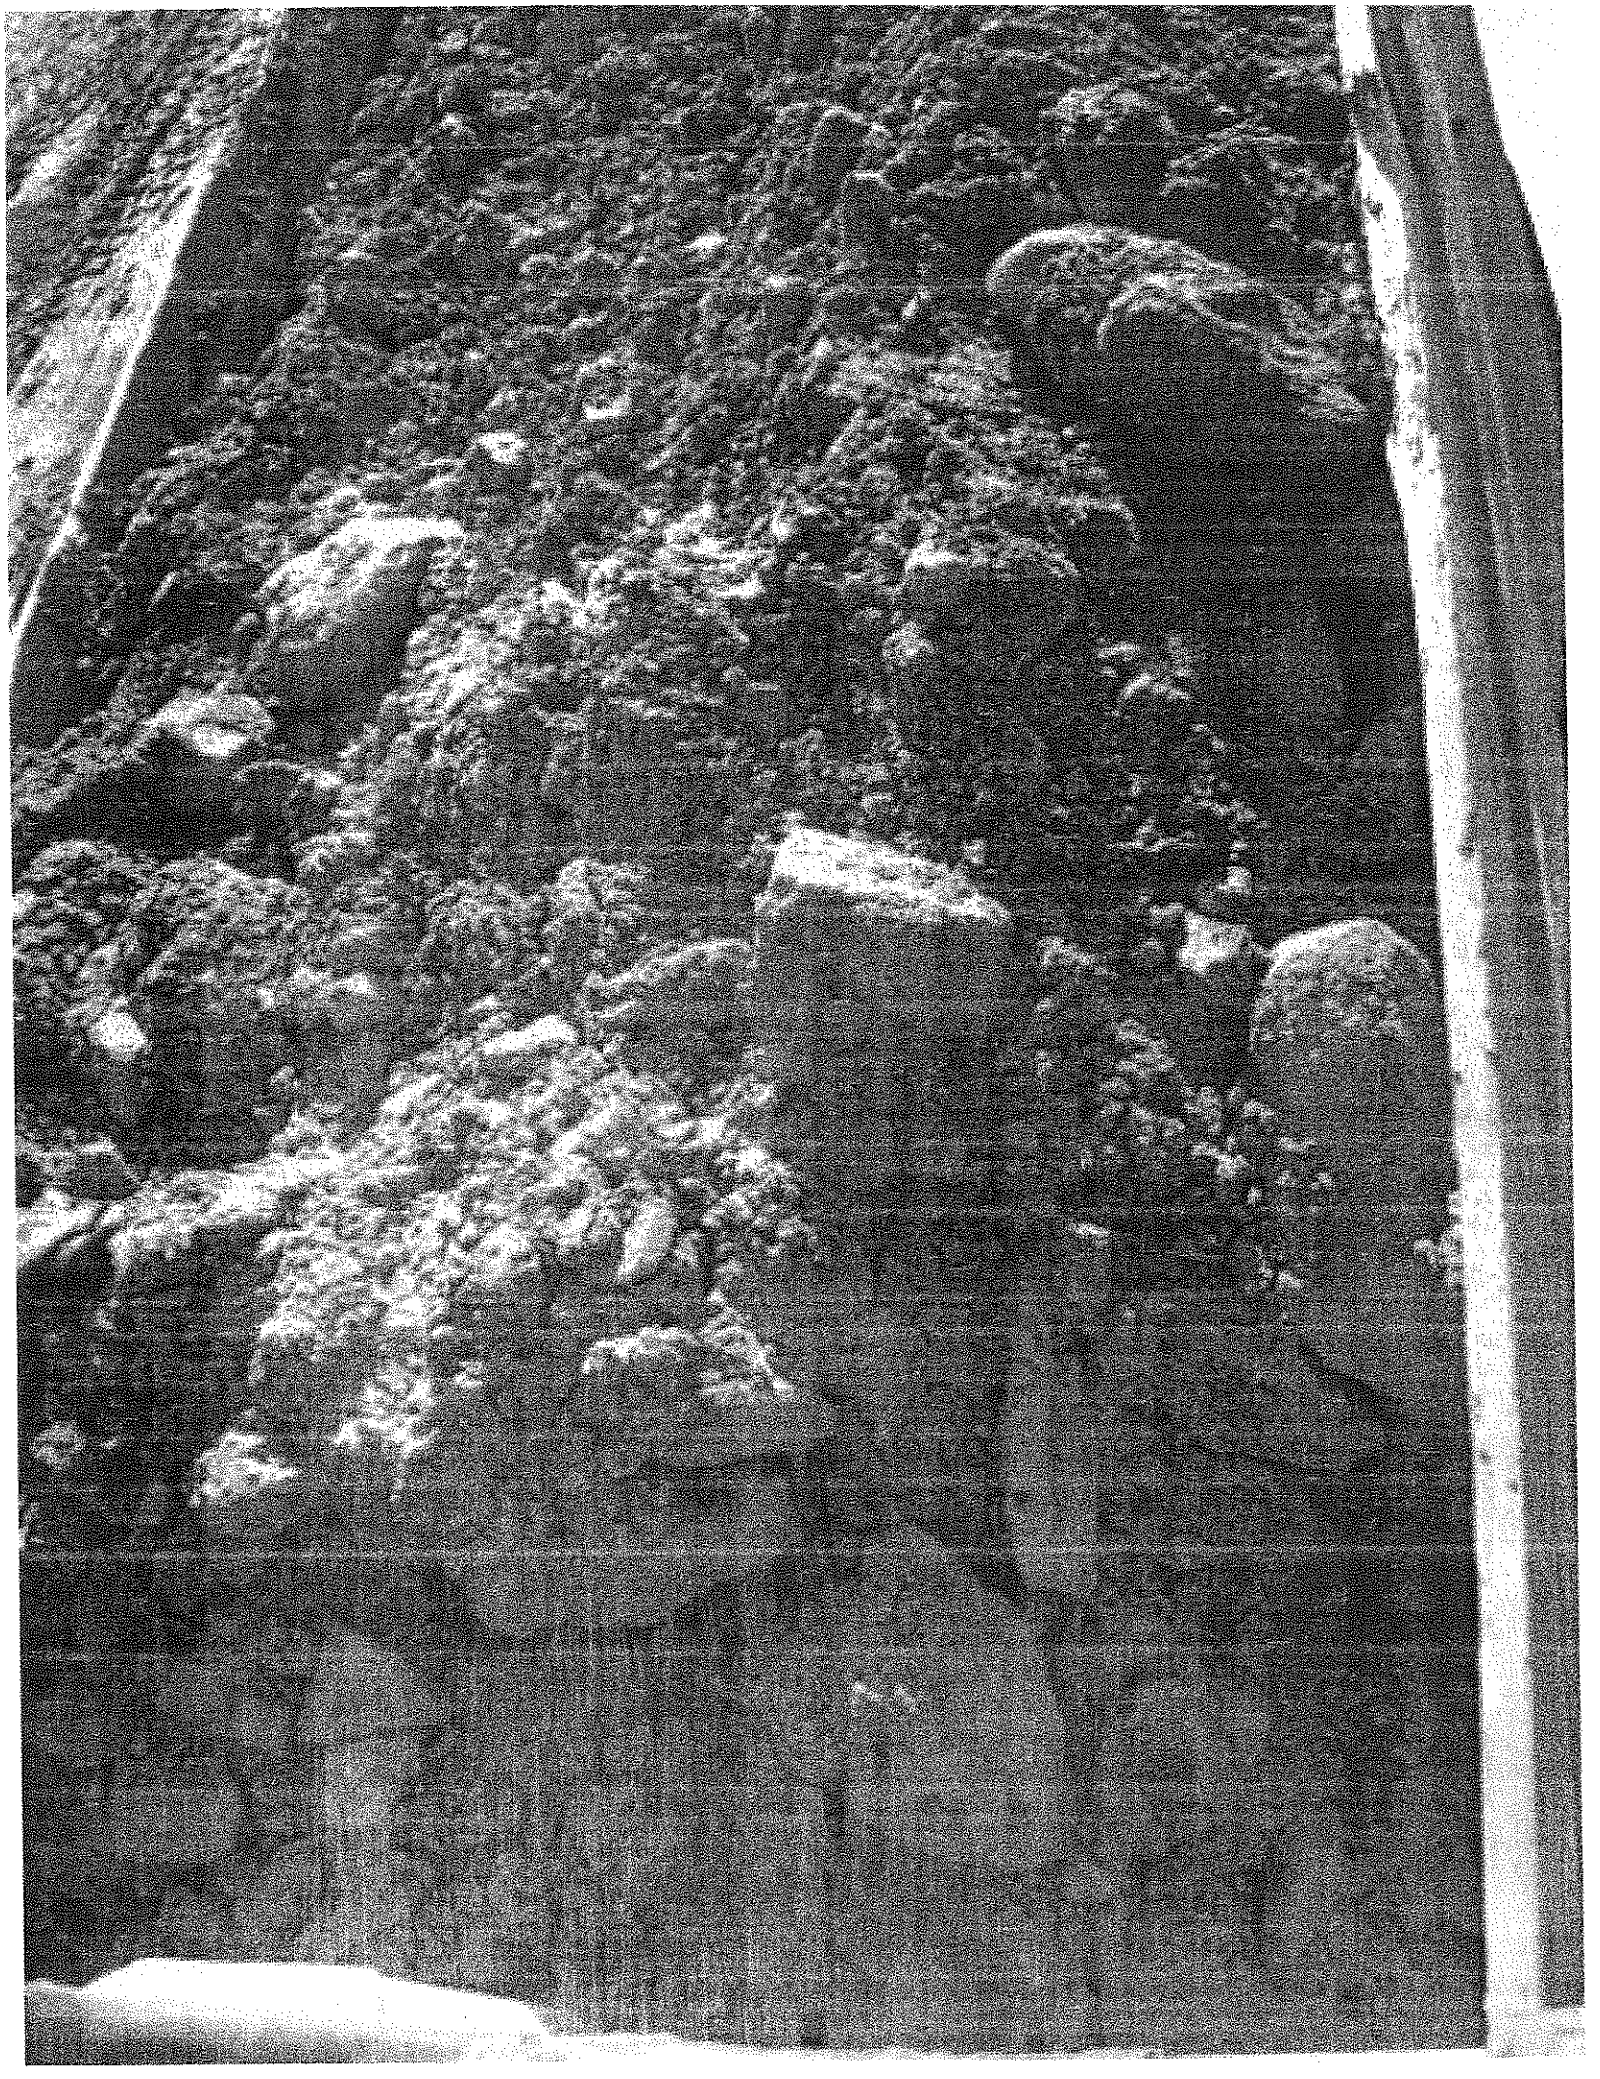

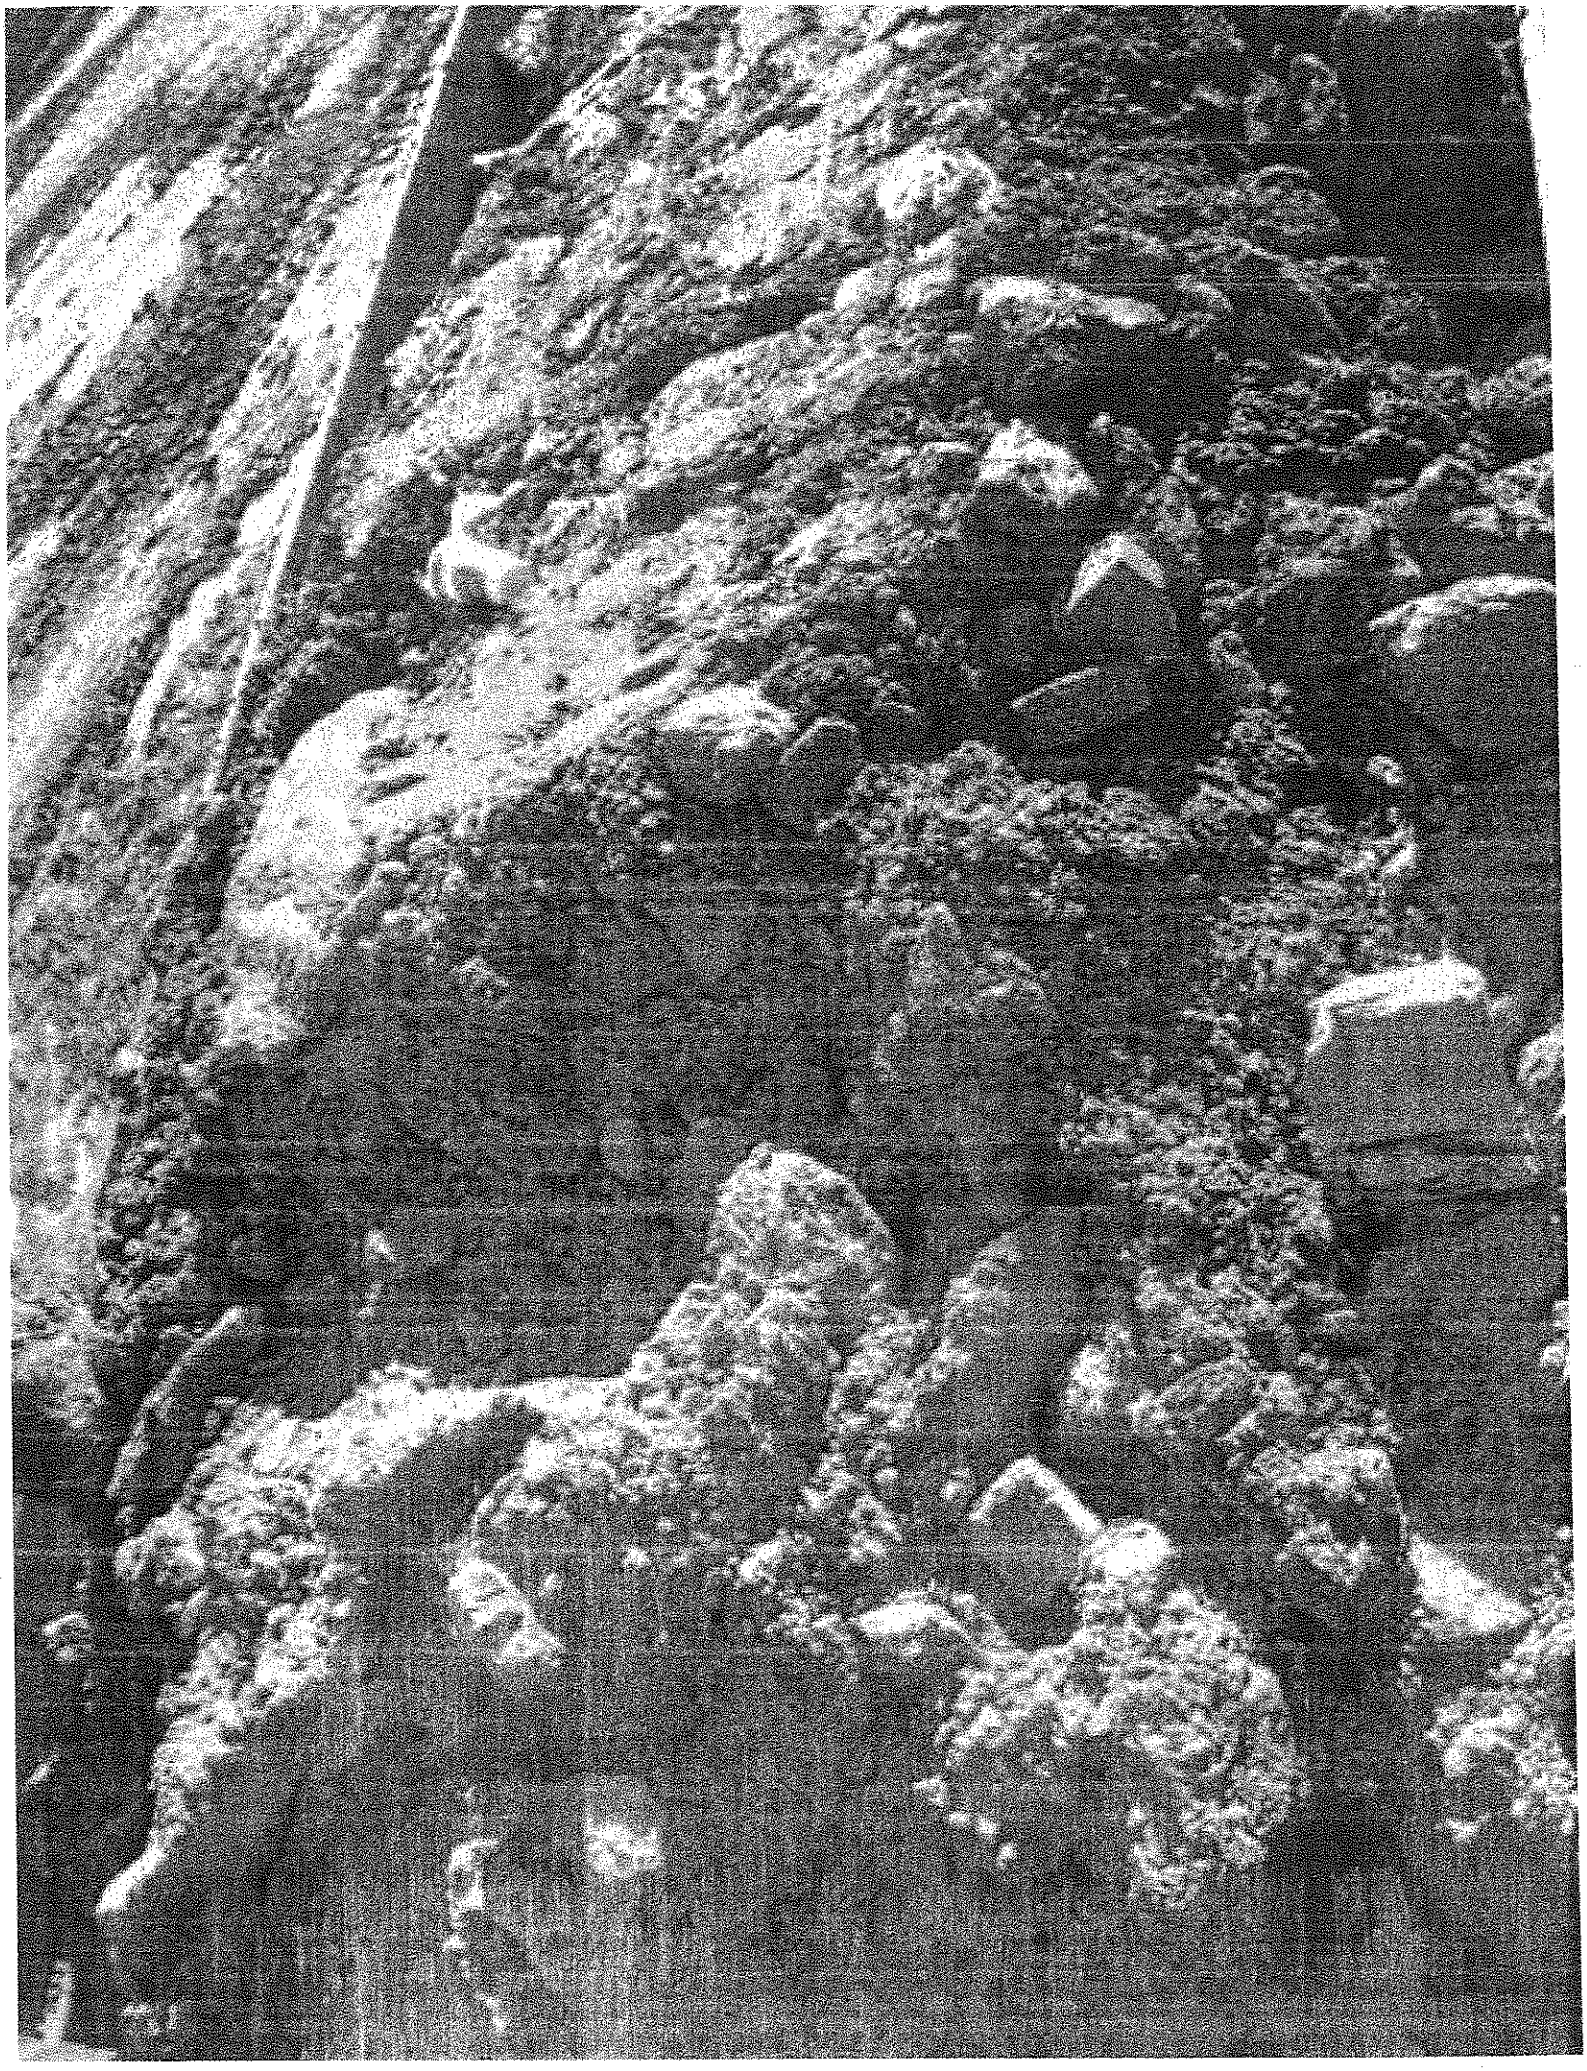

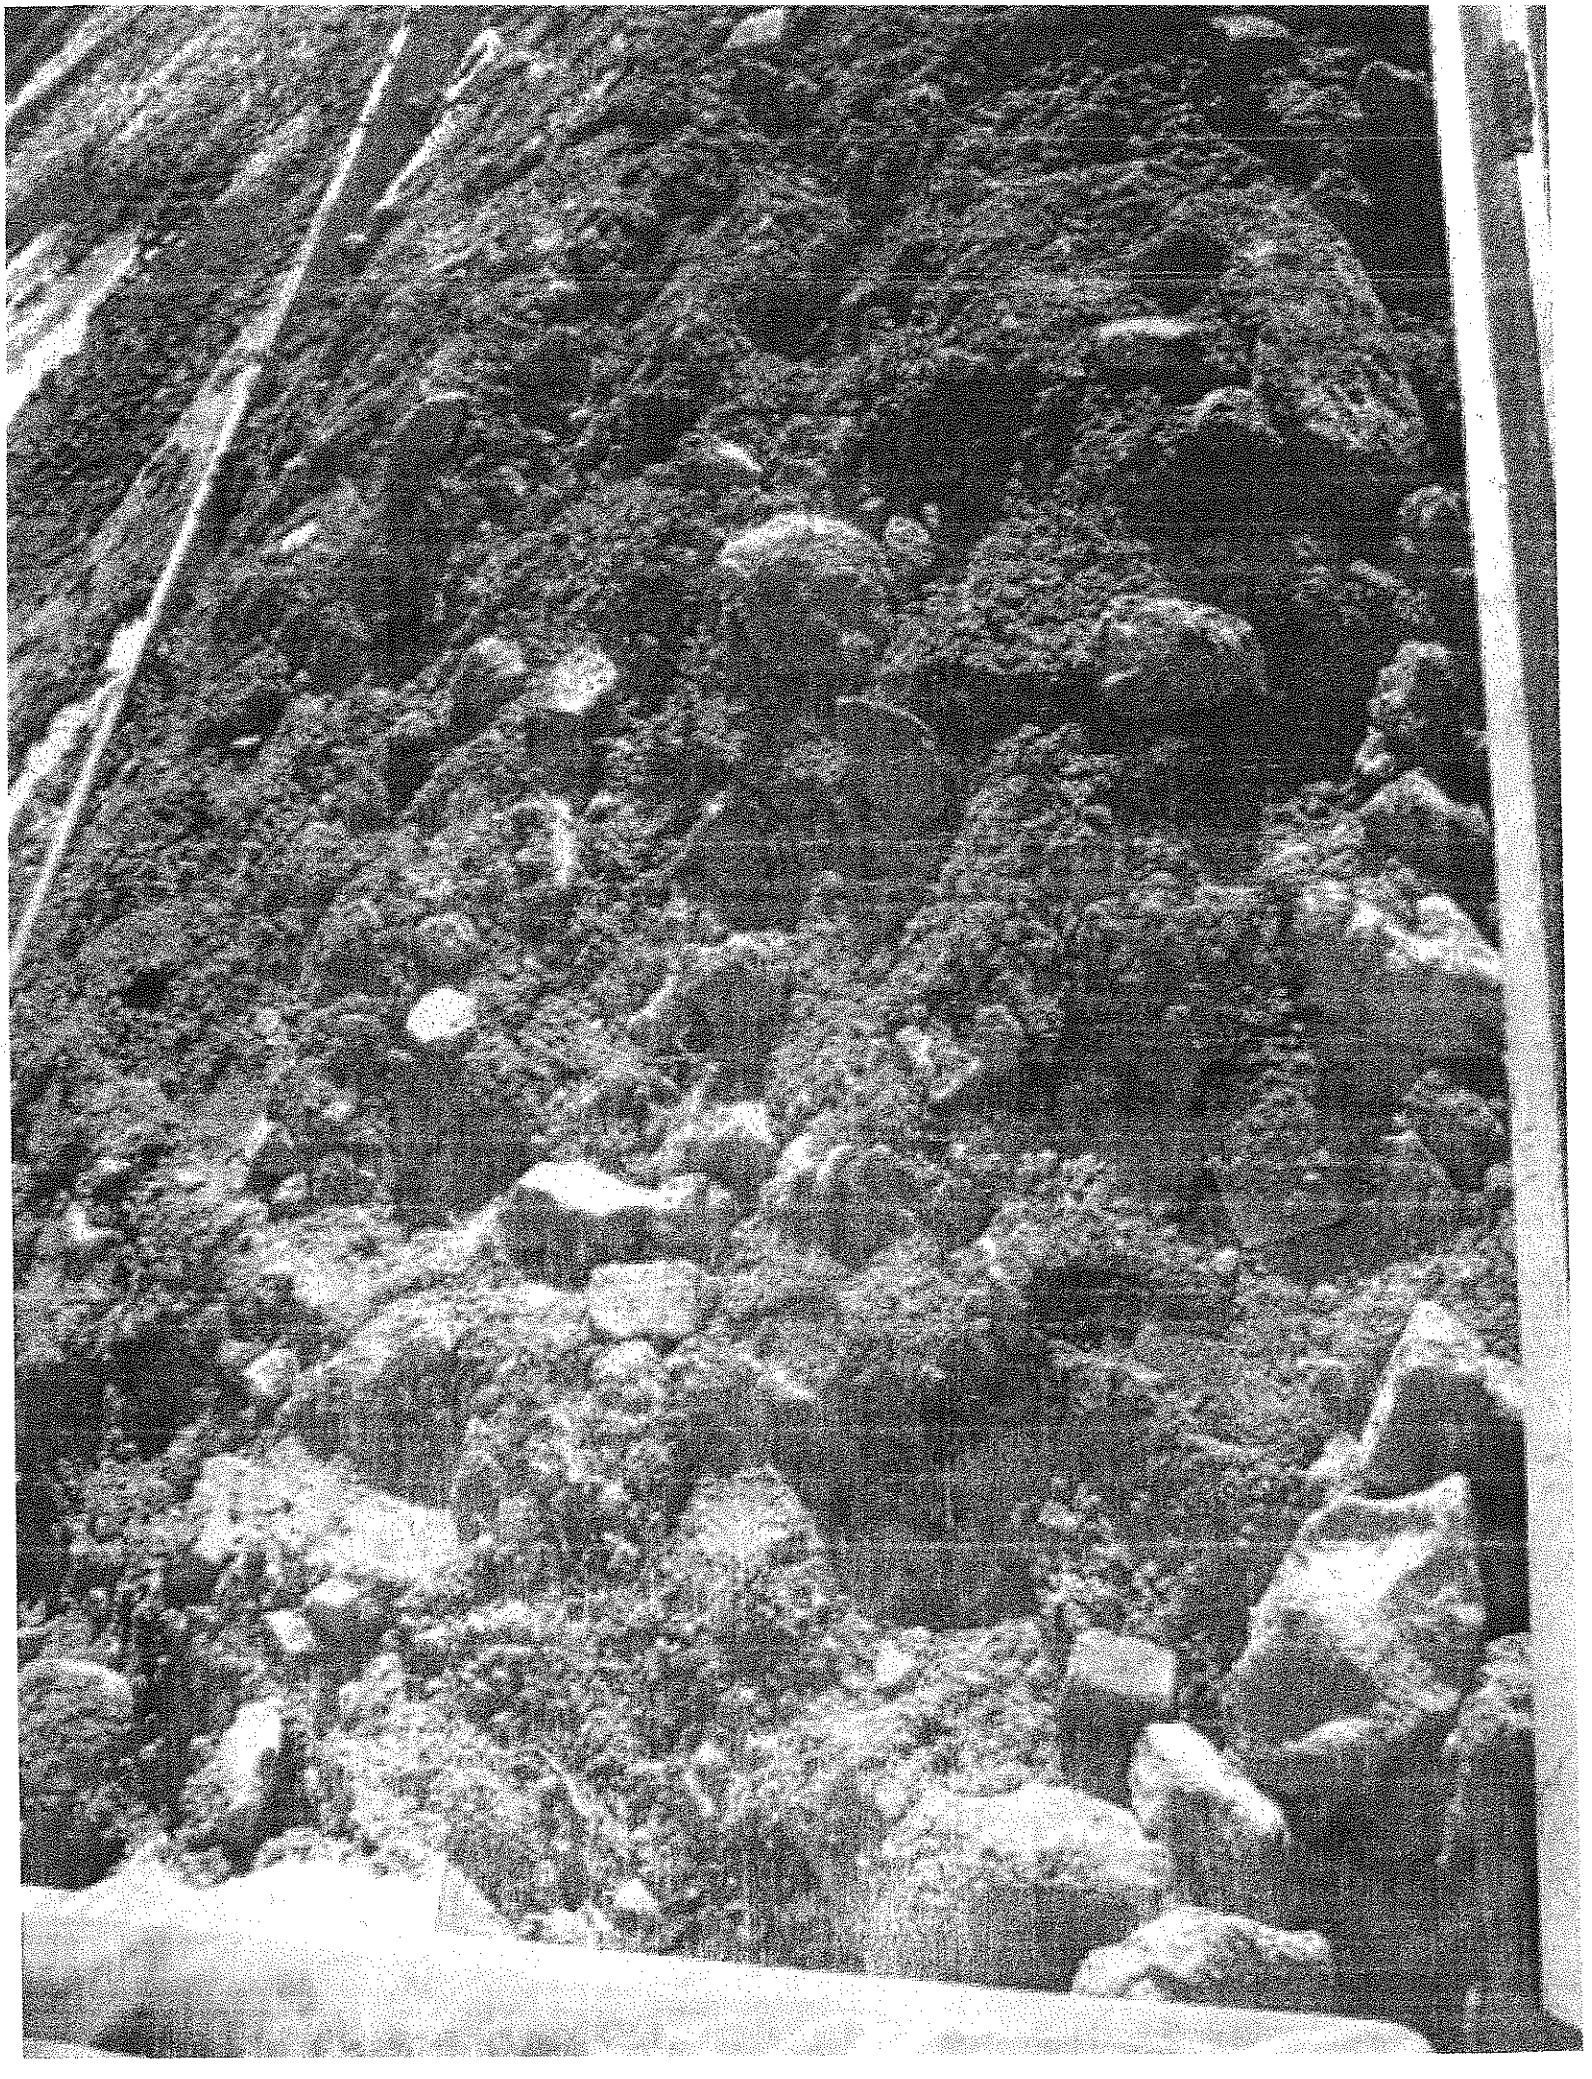

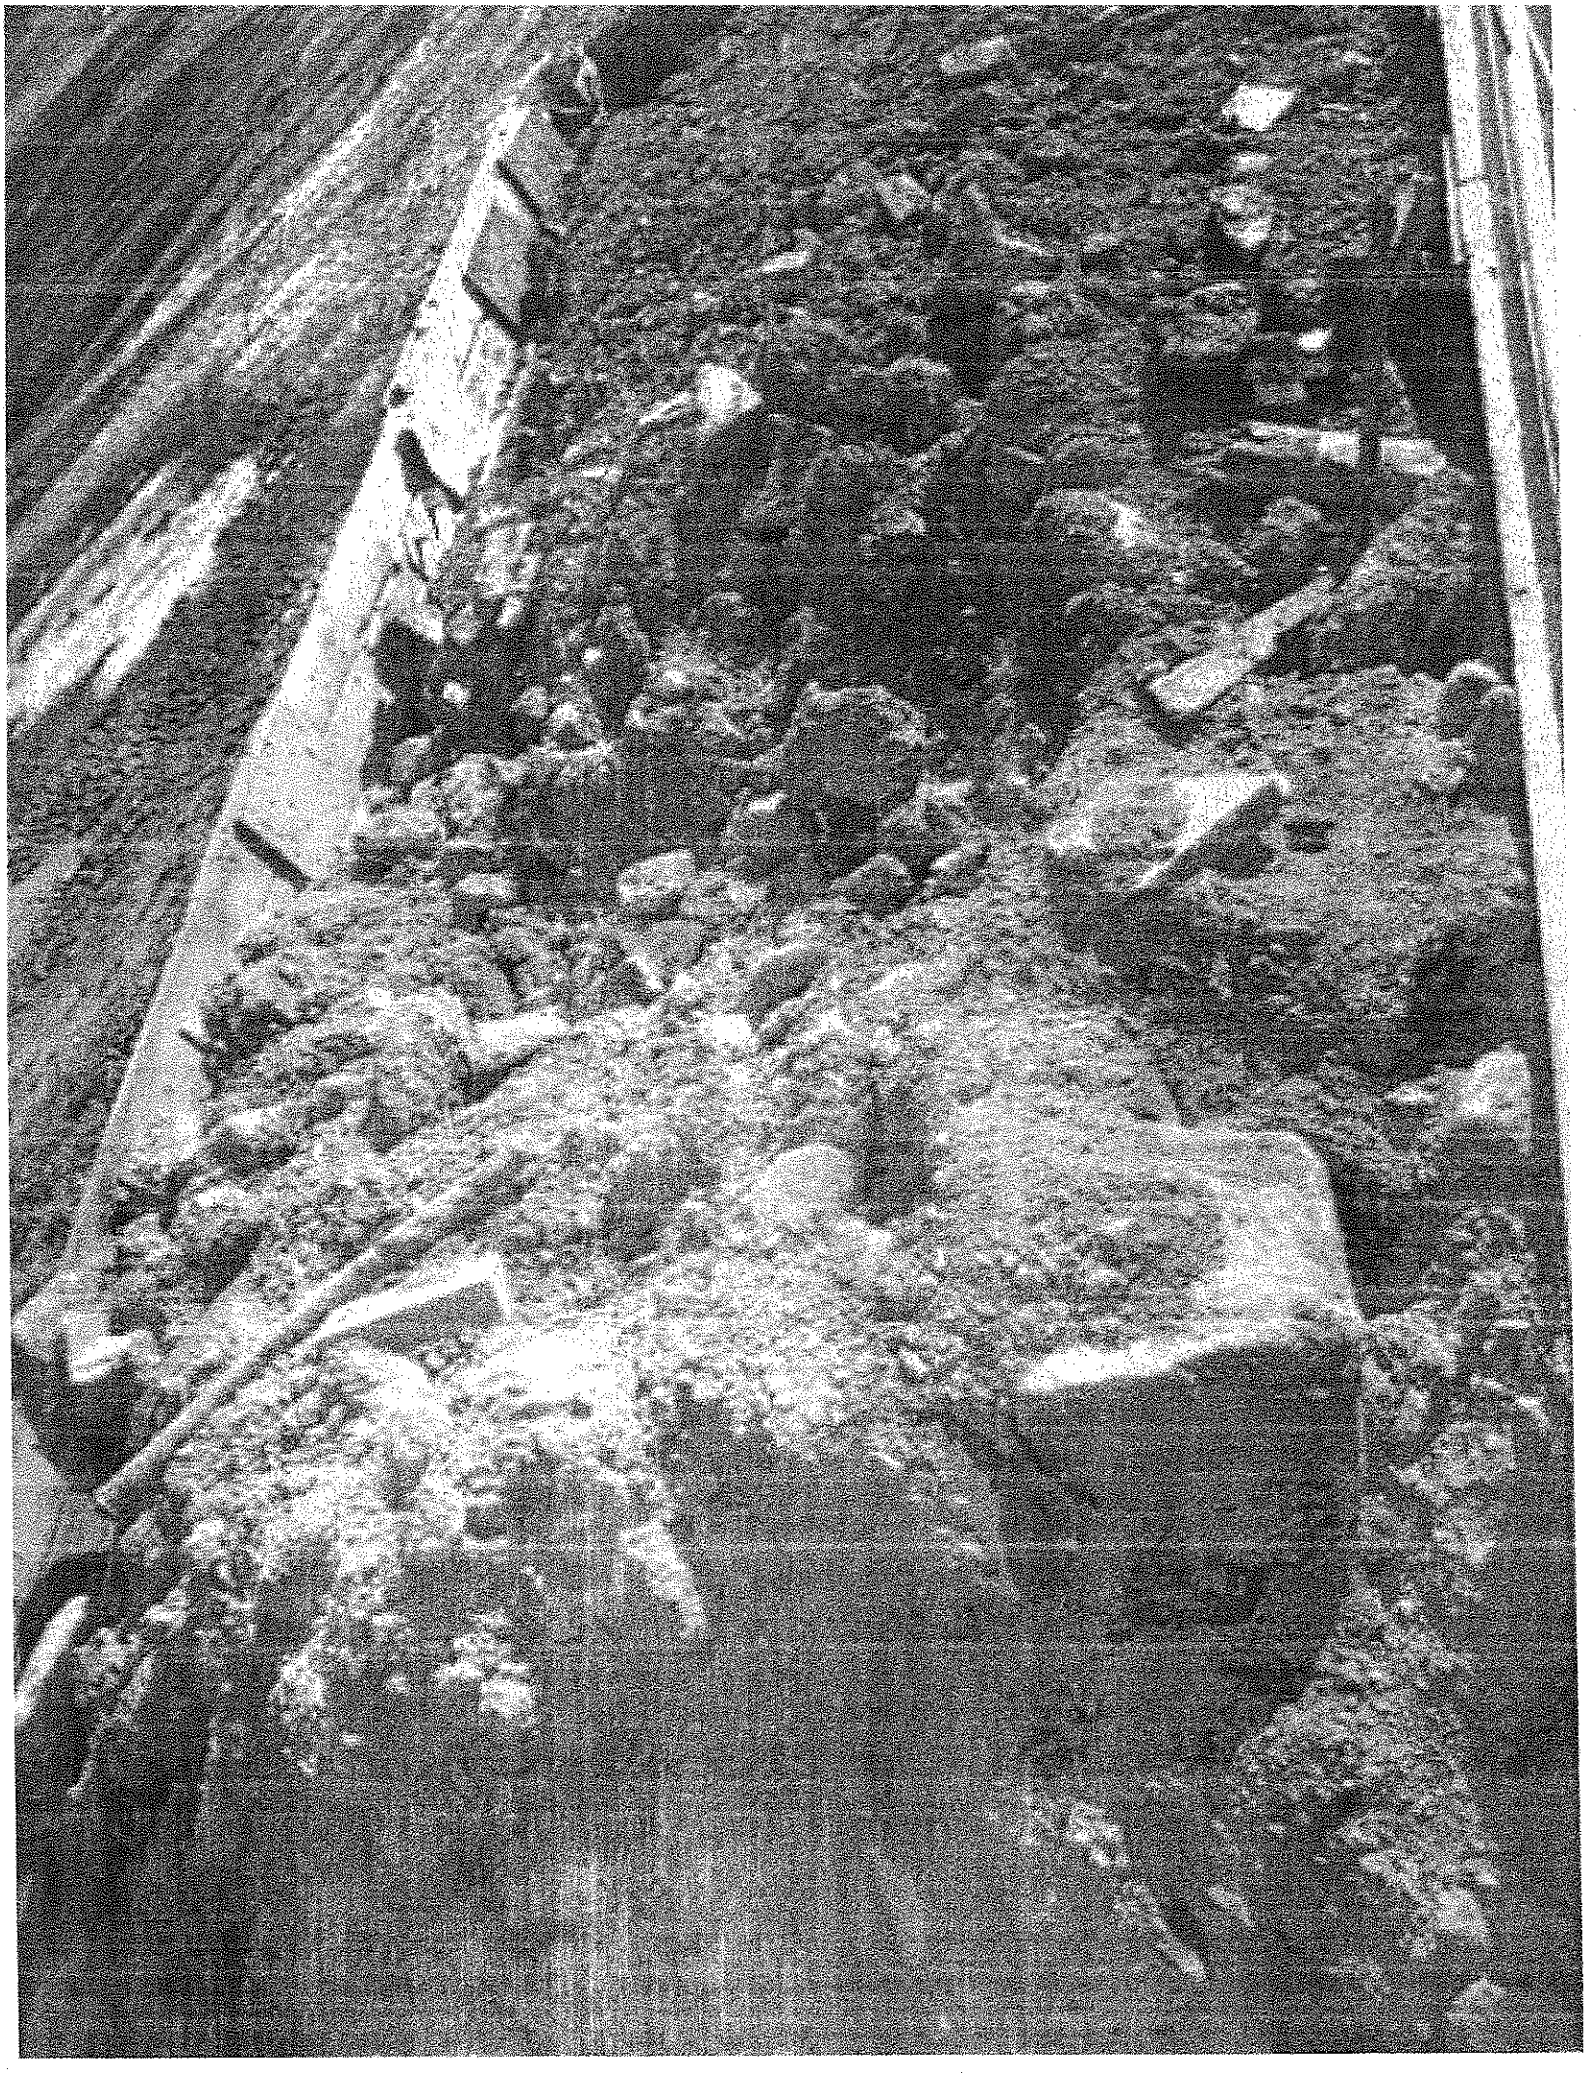

Log Number 001

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST T.P-4 @ 7.0-7'

GENERATOR

Generator Name Chelsea Green

Address 260 W 20th St NY NY

Phone No.

Generator Site/Location same

Address

Phone No.

Approval Number C4-871

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

TO 590

GROSS 40.68 T GROSS

TARE 13.68 T

RECALLED

NET 27.00 T TARE

LOG 18 NET

11/07/2011

03:10PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Dan Monroe 11-7-11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name Sweet Soil LLC

Address

Driver Name (Print) Jonathon

Vehicle License No. / State / EPA No. A11931F

Truck Number Shirley #16

I hereby certify that the above named material was picked up at the generator site listed above.

11/7/11

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

11/7/11

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 002

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 26th St NY NY

Phone No.

Generator Site/Location Same

Address

Phone No.

Approval Number C4-3179

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 509

GROSS 45.34 GROSS
TARE 13.39 T
RECALLED TARE
NET 31.95 T NET
LOG 30
11/07/2011
04:18PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

J Dunmore 11-7-11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name Soil Safe LLC

Address

Driver Name (Print) Carlos

Vehicle License No. / State / EPA No. AYM107

Truck Number Shirley - 06

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature 11-7-11 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature 11-7-11 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Curran 11 7 11

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4 NON
0-19

Log Number 001

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 240 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

ID 589

GROSS 47.15 GROSS
TARE 13.39 T
RECALLED TARE
NET 33.76 T NET
LOG 3
12/27/2011
10:06AM TONNAGE

Description of Material

Approval Number C4 8199

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator 12/27/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) Carlos

Vehicle License No. / State / EPA No. AM107

Truck Number OC - Shirley

I hereby certify that the above named material was picked up at the generator site listed above.

12-27-11

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-27-11

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Carlos 12.27.11

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4 (7-14) NW

Log Number 002

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Generator Site/Location

Address 260 WEST 26TH STREET

Address SAME

NY, NY

Phone No.

Phone No.

Approval Number C4.8190

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 539
GROSS 47.02 T GROSS
TARE 14.50 T TARE
RECALLED
NET 32.52 T NET
LOG 4
12/27/2011 TONNAGE
10:09AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator 12/27/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Driver Name (Print) Fabian Velarde

Address MONTVILLE, NJ

Vehicle License No. / State / EPA No. AN 934F

(973) 794-4020

Truck Number Sharky 12

I hereby certify that the above named material was picked up at the generator site listed above.

12-27-11

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-27-11

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

A. Gonsch 12.27.11

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4
(7-14) 30

Log Number 003

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN | Generator Site/Location

Address 360 WEST 26TH STREET | Address SAME

NY, NY

Phone No. | Phone No.

ID 3442

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

Approval Number C4 8199

GROSS 18.84 T
TARE 13.52 T
RECALLED
NET 35.12 T
LOG 11
12/27/2011
10:29AM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agnt to generator | 12/27/11

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC | Driver Name (Print)

Address MONTVILLE, NJ | Vehicle License No. / State / EPA No. AN316N

Truck Number 05

(973) 794-4020

I hereby certify that the above named material was picked up at the generator site listed above.

12/27/11

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12/27/11

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

12-27-11

Name of Authorized Agent | Signature | Receipt Date

White - Facility | Green - Facility | Yellow - Generator | Pink - Broker | Goldenrod - Contractor | Blue - Trucking Co.

TP-4 (7-14) 16.

SOIL SAFE, INC.

Log Number 004

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

MT. NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4.8190

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 515
GROSS 45.55 GROSS
TARE 12.99 T TARE
RECALLED
NET 31 32.56 T NET
LOG
12/27/2011
01:14PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 12/27/11

Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) OSCAR

Vehicle License No. / State / EPA No. 1MH3365

Truck Number 515

I hereby certify that the above named material was picked up at the generator site listed above.

Oscar Sle 12/27/11

Driver Signature / Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Oscar Sle 12/27/11

Driver Signature / Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Oscar 12/27/11

Name of Authorized Agent / Signature / Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4(7-14)

SOIL SAFE, INC.

Log Number 005

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 240 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 1015
GROSS 50.04 T GROSS
TARE 13.50 T TARE
RECALLED
NET 36.54 T NET
LOG 53
12/27/2011
04:42PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

CAS agent to generator — 12/27/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) JAIME

Vehicle License No. / State / EPA No. AM 194L

Truck Number 43

I hereby certify that the above named material was picked up at the generator site listed above.

12/27/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12/27/11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Corina — 12-27-11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-467-14

SOIL SAFE, INC.

Log Number 006

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4 8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 279
GROSS 48.41 T GROSS
TARE 13.28 T TARE
RECALLED
NET 35.13 T NET
LOG 54
12/27/2011 TONNAGE
04:49PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agnt to generator — 12/20/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973)794-4020

Driver Name (Print) Josi Tapia

Vehicle License No. / State / EPA No. AM 286Y

Truck Number 22

I hereby certify that the above named material was picked up at the generator site listed above.

12-27-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Garcia — 12 27 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-4 (7-14) sc.

SOIL SAFE, INC.

Log Number 007

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Generator Site/Location

Address 260 WEST 26TH STREET

Address SAME

NY, NY

Phone No.

Phone No.

Approval Number C4.8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 7761
GROSS 45.21 T GROSS
TARE 13.22 T TARE
RECALLED
NET 31.99 T NET
LOG SS
12/27/2011 TONNAGE
04:53PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator 12/27/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Driver Name (Print) Arcid Alvarez

Address MONTVILLE, NJ

Vehicle License No. / State / EPA No. AM373R

Truck Number 01

(973) 794-4020

I hereby certify that the above named material was picked up at the generator site listed above.

12-27-11

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-27-

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent Signature 12-27-11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4(D-14)26

Log Number 008

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 360 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No. ID 746

Approval Number E4-8190

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS 47.15 T
TARE 13.03 GROSS
RECALLED
NET 34.12 T TARE
LOG 57
12/27/2011 NET
@ 1:15PM
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 12/27/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) Jose

Vehicle License No. / State / EPA No. AN-375-K

Truck Number N.J. - # 88

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Gaycon — 12 27 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-462-14

Log Number 009

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name 36 CHELSEA GREEN

Address 360 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No. 10 660

Approval Number C4-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS 47.55 GROSS
TARE 13.69 TARE
RECALLED
NET 33.86 NET
LOG 2
12/28/2011
10AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator 12/27/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name SOMERSET LLC

Address MONTVILLE NJ

(973) 794-4020

Driver Name (Print) WALTON

Vehicle License No. / State / EPA No. AM33D

Truck Number FF 04

I hereby certify that the above named material was picked up at the generator site listed above.

12/27/11

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Galan 12 28 11

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4 (7-14)

SOIL SAFE, INC.

Log Number 001

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 240 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Description of Material

Approval Number C48199

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID T310

GROSS 45.24
TARE RECALLED 13.06
NET 32.18
LOG 17
12/28/2011
10:15AM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

GS agent to generator — 12/28/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) CARLOS ORTIZ

Vehicle License No. / State / EPA No. AU312R

Truck Number 2

I hereby certify that the above named material was picked up at the generator site listed above.

12-28-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-28-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Carlos — 12-28-11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4 (7-14 A)

SOIL SAFE, INC.

Log Number 002

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Generator Site/Location

Address 260 WEST 26TH STREET

Address SAME

NY, NY

Phone No.

Phone No. 10 736

Approval Number C4-3199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS 17.56 T GROSS
TARE 13.03 T TARE
RECALLED
NET 4.53 T NET
LOG 18
12/28/2011
10:25AM
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 12/28/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Driver Name (Print) JOSE

Address MONTVILLE, NJ

Vehicle License No. / State / EPA No. AN-375 K

(973) 794-4020

Truck Number # 88 - N.J.

I hereby certify that the above named material was picked up at the generator site listed above.

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Shipment Date

Driver Signature — 12-28-1 — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130, Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Concie — 12-28-11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP4
(7-14 Ft) 36'

Log Number 004

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No. 10-1087

Approval Number C4 8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS 50.19 T GROSS
TARE 14.47 T TARE
RECALLED
NET 35.72 T NET
LOG 23
12/28/2011 TONNAGE
10:08AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 12/28/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) ANTONIO PAIVA

Vehicle License No. / State / EPA No. AW 969K

Truck Number 1087 BATTAL 806

I hereby certify that the above named material was picked up at the generator site listed above.

I hereby certify that the above named material was delivered without incident to the destination listed below.

ANTONIO PAIVA 12/28/11 — 12.28.11

Driver Signature — Shipment Date — Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Conor — 12 28 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

-TP-407-14-FD

SOIL SAFE, INC.

Log Number 003

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4 3199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 761

GROSS	44.80 T	GROSS
TARE	13.22 T	TARE
RECALLED		
NET	31.58 T	NET
LOG 24		
12/28/2011 10:42AM		TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 12/28/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print)

Vehicle License No. / State / EPA No.

Truck Number 01

I hereby certify that the above named material was picked up at the generator site listed above.

12-28-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-28-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Gar Cio — 12 28 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4 (7-1447) 36

Log Number 006

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4.8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

10 791
GROSS 49.68 T GROSS
TARE 13.08 T TARE
RECALCED
NET 30.60 T NET
LOG 35
12/28/2011
11:11AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 12/28/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 784-4020

Driver Name (Print) Frank V.

Vehicle License No. / State / EPA No. AN 113A

Truck Number #802

I hereby certify that the above named material was picked up at the generator site listed above.

Frank V. — 12/28/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Frank V. — 12/28/11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Gordon — 12-28-11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4
(7 -14ft)
DC

Log Number 005

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4-3199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 751
GROSS 45.99 T GROSS
TARE 13.56 T TARE
RECALLED
NET 32.43 T NET
LOG 36
12/28/2011 TONNAGE
11:13AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS agent to generator — 12/28/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) Sean Garrity

Vehicle License No. / State / EPA No. [illegible]

Truck Number 807 - NJ - 751

I hereby certify that the above named material was picked up at the generator site listed above.

12/28/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12/28/11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

A. Garcia 12 28 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4 (7-14B)

Log Number 007

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Generator Site/Location

Address 260 WEST 26TH STREET

Address SAME

NY, NY

Phone No.

Phone No.

Description of Material

Approval Number	Description of Material	
C4.8199	Non-Regulated Petroleum Contaminated Soil Non DOT/RCRA Regulated	ID 273 GROSS 47.80 T GROSS TARE 13.28 T TARE RECALLED NET 34.52 T NET LOG 44 12/28/2011 11:35AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 12/28/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Driver Name (Print) Jose Tapia

Address MONTVILLE, NJ

Vehicle License No. / State / EPA No. AM386Y

(973) 794-4020

Truck Number 28

I hereby certify that the above named material was picked up at the generator site listed above.

12-28-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-28-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Carlos — 12-28-11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4 C-3-14

Log Number 008

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4.9190

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 1087
GROSS 46.02 T GROSS
TARE 14.47 T TARE
RECALLED
NET 31.55 T NET
LOG 16
12/28/2011 TONNAGE
03:58PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS AGENT TO GENERATOR — 12/28/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) ANTONIO PAIVA

Vehicle License No. / State / EPA No. AN969R

Truck Number 1087 BATTALION

I hereby certify that the above named material was picked up at the generator site listed above.

12/28/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12/28/11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Carlos — 12/28/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR4 (7-14 FT)

Log Number 009

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 360 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4-3199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 740
GROSS 45.79 T GROSS
TARE 13.06 T TARE
RECALLED
NET 77 32.73 T NET
LOG
12/28/2011 TONNAGE
1:14 :02PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agnt to generator — 12/28/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) CARLOS ORTIZ

Vehicle License No. / State / EPA No. AW3122

Truck Number 2

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date 12-28-11

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date 12-28-11

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — Receipt Date 12-28-11

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4 (7-14)

Log Number 010

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

10 T46
GROSS 46.02 T GROSS
TARE 13.03 T TARE
RECALLED
NET 32.99 T NET
LOG 78
12/28/2011
04:25PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent for generator — 12/28/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 784-4020

Driver Name (Print) JOSE

Vehicle License No. / State / EPA No. AU-325K

Truck Number #88 - NJ

I hereby certify that the above named material was picked up at the generator site listed above.

12-28-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — 12 28 11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-4 (07-14)

SOIL SAFE, INC.

Log Number 012

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Description of Material

Approval Number C4 8190

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 701

GROSS	45.61 T	GROSS
TARE	13.08 T	TARE
RECALLED NET	32.53 T	NET
LOG 80		TONNAGE
12/28/2011 04:52PM		

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — 12/28/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) Frank Garcia

Vehicle License No. / State / EPA No. DM 1172A

Truck Number 802

I hereby certify that the above named material was picked up at the generator site listed above.

Frank G. — 12/28/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Frank G. — 12/28/11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Garcia — 12 28 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Log Number 011

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Generator Site/Location

Address 260 WEST 36TH STREET

Address SAME

NY, NY

Phone No.

Phone No.

Approval Number C48199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 761
GROSS 45.34 T GROSS
TARE 13.22 T TARE
RECYCLED
NET 32.12 T NET
LOG
12/28/2011 TONNAGE
05:20PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 12/28/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Driver Name (Print) Angel Munoz

Address MONTVILLE, NJ

Vehicle License No. / State / EPA No. AU343K

(973) 794-4020

Truck Number 01

I hereby certify that the above named material was picked up at the generator site listed above.

12-28-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-28-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Carlos — 12 28 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4 (12-14)

Log Number 014

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4.8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

JU 279
GROSS 45.57 GROSS
TARE 13.28 T TARE
PREPAID
NET 32.29 T NET
LOG 82
12/28/2011
06:40PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

QS agent for owner 12/28/11

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name SOMERSET, LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) Jose Tapia

Vehicle License No. / State / EPA No. AM38CY

Truck Number 22

I hereby certify that the above named material was picked up at the generator site listed above.

Jose

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-27-11

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130, Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent Signature 12-28-11 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-407-14

Log Number 013

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN

Address 260 WEST 26TH STREET

NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number C4.3190

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 751
GROSS 44.74 T GROSS
TARE 13.56 T TARE
RECALLED
NET 31.18 T NET
LOG 6
12/28/2011 TONNAGE
08:36AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS agent to generator — 12/28/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name SOMERSET LLC

Address MONTVILLE, NJ

(973) 794-4020

Driver Name (Print) Sam Bittel

Vehicle License No. / State / EPA No. AW-584 H

Truck Number 807 - NJ-714

I hereby certify that the above named material was picked up at the generator site listed above.

12/27/11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12/28/11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Garcia 12-29-11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4(7-14) NW

SOIL SAFE, INC.

Log Number 001

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 26th St NY, NY

Phone No.

Generator Site/Location

Address Same

Phone No.

Approval Number 04-8194

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 740
GROSS 45.46 T
TARE 13.06 T
RECALLED
NET 32.40 T
LOG 21
12/29/2011
10 WORK

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

GS agent to generator — 12/29/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somers, LLC

Address Montville NJ

Driver Name (Print) CARLOS ORTIZ

Vehicle License No. / State / EPA No. AN 312 R

Truck Number 12

I hereby certify that the above named material was picked up at the generator site listed above.

12-29-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-29-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Carlos — 12-29-11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-7(0-7ft) mulch 1/29/11

SOIL SAFE, INC.

Log Number 003

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 26th St NY, NY

Phone No.

Generator Site/Location

Address Same

Phone No.

Approval Number C4-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 746
GROSS 49.69 T GROSS
TARE 13.03 T TARE
RECALLED
NET 36.66 T NET
LOG 30
12/29/2011
10:25AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 12/29/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somerset LLC

Address Montville NJ

Driver Name (Print) Jose

Vehicle License No. / State / EPA No. AM-375K

Truck Number # 88 - NJ

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Carlos — 12-29-11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4 (7-14)

Log Number 004

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 36th St. NY, NY

Phone No.

Generator Site/Location

Address Soma

Phone No.

Approval Number CY-8849

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 279
GROSS 47.90 T
TARE 13.28 T
RECALCED
NET 34.62 T
LOG 18
12/29/2011
11:04AM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent for generator — 12/29/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somerset LLC

Address Montville, NJ

Driver Name (Print) José Tapia

Vehicle License No. / State / EPA No. AM386Y

Truck Number 22

I hereby certify that the above named material was picked up at the generator site listed above.

12-29-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12/29/11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Carlos — 12/29/11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4 (7-14) NMK

SOIL SAFE, INC.

Log Number 003

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 26th St NY, NY

Phone No.

Generator Site/Location

Address Same

Phone No.

Approval Number 04-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID TB1
GROSS 46.33 T
TARE 13.22 T
REBILLED
NET 33.11 T
LOG 49
12/29/2011
11:20:26AM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to Geowaste — 12/29/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somerset LLC

Address Montville, NJ

Driver Name (Print) Angel Munoz

Vehicle License No. / State / EPA No. A43B12

Truck Number 01

I hereby certify that the above named material was picked up at the generator site listed above.

12-29-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-29-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

A Carou — 12 29 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-7 (0-7) MW

SOIL SAFE, INC.

Log Number 005

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 26th St NY NY

Phone No.

Generator Site/Location

Address Same

Phone No.

Approval Number 04-8149

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 740
GROSS 49.51 T GROSS
TARE 13.06 T TARE
RECALCED
NET 36.49 T NET
LOG 80
12/29/2011 TONNAGE
03:15PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to Wastec — 12/29/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somerset LLC

Address Manville, NJ

Driver Name (Print) CARLOS ORTIZ

Vehicle License No. / State / EPA No. AN312R

Truck Number 2

I hereby certify that the above named material was picked up at the generator site listed above.

12-29-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-29-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

12-29-11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-7 (0-7) MW

SOIL SAFE, INC.

Log Number 006

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Grea

Address 260 west 26th St NY, NY

Phone No.

Generator Site/Location

Address Same

Phone No.

ID T-46
GROSS 46.73 GROSS
TARE 13.03 T
RECALLED TARE
NET 33.70 T
LOG 82 NET
12/29/2011
09:29PM TONNAGE

Approval Number C4-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 12/29/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somerset LLC

Address Montville, N.J.

Driver Name (Print) Jose Vivas

Vehicle License No. / State / EPA No. AR-3375K

Truck Number N.J. # 88

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 12-29-11 — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — 12-29-11 — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4 (7-14)

Log Number 007

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 36th St NY, NY

Phone No.

Generator Site/Location

Address Same

Phone No.

Approval Number 04-899

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 279
GROSS 51.08 T
TARE 13.28 T
RECALCED
NET 37.80 T
LOG 96
12/29/2011
04:41PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 12/29/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somerset LLC

Address Montville, N.J.

Driver Name (Print) José Tapia

Vehicle License No. / State / EPA No. AM386V

Truck Number 22

I hereby certify that the above named material was picked up at the generator site listed above.

12-29-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-29-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Garcia — 12 29 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4 (9-14)

16

Log Number 008

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 36th St NY, NY

Phone No.

Generator Site/Location

Address Same

Phone No.

Approval Number CH-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 761

GROSS	45.43 T	GROSS
TARE	13.22 T	TARE
RECALLED		
NET	32.21 T	NET

LOG 99
12/29/2011
04:53PM

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 12/29/11

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somerset LLC

Address Manville, NJ

Driver Name (Print) Angel Nunez

Vehicle License No. / State / EPA No. AM313R

Truck Number 01

I hereby certify that the above named material was picked up at the generator site listed above.

12-29-11

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

12-29-11

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Carlos — 12 29 11

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4 (7-4)

Log Number 001

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 360 West 21st St NY NY

Phone No.

Generator Site/Location

Address Same

Phone No.

Description of Material

Approval Number C4-9/99

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

10 601
GROSS 46.23 T GROSS
TARE 11.43 T
RECALLED 34.77 T TARE
LOG 1 NET
01/09/2012 TONNAGE
09:57 AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent for generator — 1/9/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somerset

Address Montville NJ

Driver Name (Print) Hector

Vehicle License No. / State / EPA No. AM 8901 NJ

Truck Number # 22 Kenmore

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

HC — 1-9-12

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-4 (7-14)

Jc

Log Number 002

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 26th St NY NY

Phone No.

Generator Site/Location

Address SWMP

Phone No.

Approval Number 24-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

10 T40

GROSS	40.15 T	GROSS
TARE	13.06 T	TARE
RECALLED NET	27.09 T	NET
LOG		
01/09/2012 10:34AM		TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent for gmcb

Generator Authorized Agent Name — Signature — 1/9/12 Shipment Date

TRANSPORTER

Transporter Name Sumosh LLC

Address Manville, NJ

Driver Name (Print) Angel Nunez

Vehicle License No. / State / EPA No. A-43112

Truck Number 02

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 1-9-12 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 1-9-12 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — 1/9/12 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

CTR-467-14

SOIL SAFE, INC.

Log Number 003

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West Bay St Ste Nyc NY

Phone No.

Generator Site/Location

Address

Phone No.

Approval Number C4-9111

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID .08
GROSS 41.51 T GROSS
RECALLED
TARE 13.91 T TARE
NET 27.60 T NET
LOG 6
01/09/2012 TONNAGE
10:37AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent for the generator

Generator Authorized Agent Name | Signature | Shipment Date 1/9/12

TRANSPORTER

Transporter Name Emwest LLC

Address Melville NY

Driver Name (Print)

Vehicle License No. / State / EPA No.

Truck Number 8

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Corona 1/9/12

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PM (7-14)
TP-3 16'

Log Number 004

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 26th St

NY, NY

Phone No.

Generator Site/Location

Address

Same

Approval Number CY-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

12 CYDS
GROSS 44.42 GROSS
TARE 14.24 TARE
RECEIVED NET 30.18 NET
LOG 5
01/09/2012 TONNAGE
10:48AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to agents — 1/9/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Sorvil LLC

Address Montville, NJ

MC# 3

Driver Name (Print) Rolando Rosales

Vehicle License No. / State / EPA No. AM624

Truck Number 3 / 652

I hereby certify that the above named material was picked up at the generator site listed above.

1-9-12

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

1-9-12

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

1/9/12

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-41C7-14

JC

SOIL SAFE, INC.

Log Number 005

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 256 West 36th St

NY NY

Phone No.

Generator Site/Location Same

Address

Phone No.

ID 601
GROSS 46.21 T
TARE 11.43 T
RECALLED
NET 34.78 T
LOG 01/09/2012
02:25PM

GROSS
TARE
NET
TONNAGE

Approval Number C4-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — 1/9/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somerset, LLC

Address Bridgeville NJ

Driver Name (Print) Hector C

Vehicle License No. / State / EPA No. AM 8800 NJ

Truck Number 03 ANDRADES

I hereby certify that the above named material was picked up at the generator site listed above.

1-9-12

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

1_9_2012

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Garcia — 1-9-12

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3(7-14)

Log Number 006

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Generator Site/Location Same

Address 460 36th

Address Same

Phone No.

Phone No.

Description of Material

Approval Number 04-619

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 740

GROSS	48.30 T	GROSS
TARE	13.06 T	TARE
RECALLED		
NET	35.24 T	NET

LOG 23

01/09/2012 03:20PM

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 1/9/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somerset LLC

Driver Name (Print) Ronald Wonzo

Address Melville, NY

Vehicle License No. / State / EPA No. AU312K

Truck Number 02

I hereby certify that the above named material was picked up at the generator site listed above.

1-9-12

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

1-9-12

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Carlos — 1/9/12

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-307-14

SOIL SAFE, INC.

Log Number 007

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Group — Generator Site/Location

Address 260 Industrial Way East — Address Same

Eatontown, NJ

Phone No. — Phone No.

Approval Number EV-8PM

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

ID 746
GROSS 48.55 T GROSS
TARE 13.03 T TARE
RECYCLED
NET 35.52 T NET
LOG 26
01/09/2012 TONNAGE
03:46PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS AGENT TO GENERATOR — 1/9/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somerset LLC — Driver Name (Print) Jose

Address Pittsville MD — Vehicle License No. / State / EPA No. DW-395-K

Truck Number 188 - NJ - 741

I hereby certify that the above named material was picked up at the generator site listed above.

Jose Hernandez — 1-9-12

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** — Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 1/9/12

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-307-14

36.

Log Number 008

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 31st St

NY NY

Phone No.

Generator Site/Location

Address Same

Phone No.

Approval Number CY-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 279
GROSS 49.43 T GROSS
TARE 13.28 T TARE
RECEIVED
NET 36.15 T NET
LOG 27
01/09/2012 TONNAGE
03:52PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to Generator — 1/9/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somerset LLC

Address Mayville NJ

Driver Name (Print) Jose Tapia

Vehicle License No. / State / EPA No. AM36CY

Truck Number

I hereby certify that the above named material was picked up at the generator site listed above.

1-9-12

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

1-9-12

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

1/9/12

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co

TT-3107-1491

SOIL SAFE, INC.

Log Number 009

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Sand

Address 260 West 26th St NY, NY

Phone No.

Generator Site/Location

Address Camp

Phone No.

Approval Number 14-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID .08
GROSS 46.78 T
RECALLED
TARE 14.11 T
NET 32.67 T
LOG 28
01/09/2012
04:04PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 1/9/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somerset LLC

Address Montville, NJ

Driver Name (Print) Pedro Rodriguez

Vehicle License No. / State / EPA No. [illegible]

Truck Number 05

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Pedro — 1-09-12

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

[illegible] — 1/9/12

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-3(7-14)
AC

Log Number 001

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Generator Site/Location

Address 260 W 26th St NY NY

Address Same

Phone No.

Phone No.

Approval Number 04-0199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 515
GROSS 46.48 T GROSS
TARE 12.98 T TARE
RECALLED
NET 33.50 T NET
LOG 18
01/10/2012 TONNAGE
09:26AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator 1/10/12

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name Somerset LLC

Driver Name (Print) Chris Colaw

Address Monmouth Jct. NJ

Vehicle License No. / State / EPA No. AH5366

Truck Number 515

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Colaw 1/10/12

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Carlo 1/10/12

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-367-19

Log Number 002

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 36th St

NY, NY

Phone No.

Generator Site/Location

Address Same

Phone No. ID 1015

Description of Material

Approval Number 04-8149

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS 31.49 T
TARE 13.50 T
RECALCED
NET 37.99 T
LOG 29
01/10/2012
11:02AM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

GC agent for generator — Signature — 1/10/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Connville NJ

Address Conrail

Driver Name (Print) WALTON

Vehicle License No. / State / EPA No. AM 3370

Truck Number #03 1442

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — 1/10/12 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-367-14

JG

SOIL SAFE, INC.

Log Number 002

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 39th St NY, NY

Phone No.

Generator Site/Location Same

Address

Phone No.

Approval Number 01-8M

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 660
GROSS 43.71 T GROSS
TARE 13.69 T TARE
NET 30.02 T NET
LOG 30
01/10/2012 TONNAGE
11:05AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

95 cans to go to site

Generator Authorized Agent Name Signature 1/10/12 Shipment Date

TRANSPORTER

Transporter Name Sommers LLC

Address Hamilton NJ

Driver Name (Print) John Quinn

Vehicle License No. / State / EPA No. AM331D

Truck Number

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature 1/10/12 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent Signature 1/10/12 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3(7-14)

SOIL SAFE, INC.

Log Number 004

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Group

Address 350 Lwr 36th St

NY NY

Phone No.

Generator Site/Location

Address Same

Phone No.

Approval Number 04899

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 290
GROSS 46.15 T GROSS
TARE 14.11 T TARE
RECALCED
NET 32.04 T NET
LOG 35
01/10/2012 TONNAGE
11:18AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent for generator — 1/10/12

Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name Somerset LLC

Address Millville, NJ

Driver Name (Print) Hector

Vehicle License No. / State / EPA No. C 427228

Truck Number 11

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature Shipment Date 1-10-12

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature Delivery Date 1-10-12

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3(7-14-11)

Log Number 005

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 360 West 36th St

NY, NY

Phone No.

Generator Site/Location

Address Same

Phone No.

Approval Number 04-8169

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

10 1020

GROSS 43.55 T — GROSS

TARE 13.65 T — TARE

RECALCED

NET 29.91 T — NET

LOG 36

01/10/2012 — TONNAGE

11:21AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somerset, LLC

Address Montville NJ

Driver Name (Print) Johnathan Valverde

Vehicle License No. / State / EPA No. AM 3535

Truck Number 20

I hereby certify that the above named material was picked up at the generator site listed above.

Johnathan Valverde

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Johnathan Valverde

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

A Cano 1/10/12

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3(7-14A) SOIL SAFE, INC.

Log Number 006

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green | Generator Site/Location Same

Address 260 West 26th St NY, NY | Address

Phone No. | Phone No.

Approval Number CH-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 740
GROSS 46.36 T GROSS
TARE 13.06 T TARE
RECALLED
NET 33.30 T NET
LOG #303
01/10/2012 TONNAGE
11:51AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS agent to generator 1/10/12

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name Soma Sol LLC | Driver Name (Print)

Address 8 Montville NJ | Vehicle License No. / State / EPA No. AW 3132

Truck Number 07

I hereby certify that the above named material was picked up at the generator site listed above.

1-10-12

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

1-10-12

Driver Signature | Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** | Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia 1/10/12

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

#17-307-14

SOIL SAFE, INC.

Log Number 007

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 360 West 24th

NYNY

Phone No.

Generator Site/Location

Address Same

Phone No.

Approval Number 04-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 279

GROSS	49.07 T	GROSS
TARE	13.28 T	TARE
RECALLED		
NET	35.79 T	NET

LOG 89

01/10/2012 03:37PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Joseph Fagenson — 1/10/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Rapid Star Inc.

Address Same St

Driver Name (Print) Joe Tagi

Vehicle License No. / State / EPA No. AM386Y

Truck Number 22

I hereby certify that the above named material was picked up at the generator site listed above.

1-10-12

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

1-10-12

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Garcia — 1/10/12

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

T-83(7-19)

36

SOIL SAFE, INC.

Log Number 008

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 Wright Det Rd
NY, NY

Phone No.

Generator Site/Location

Address Same

Phone No.

Approval Number 04-819 Q

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 515
GROSS 48.83 T GROSS
TARE 12.99 T TARE
RECALLED
NET 33.84 T NET
LOG 90
01/10/2012 TONNAGE
03:42PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS agent to Generator — 1/10/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Connect Trans

Address

Driver Name (Print) Oscar Ale

Vehicle License No. / State / EPA No. AH53CE

Truck Number 515

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date 1/10/12

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date 1/10/12

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature Carcia — Receipt Date 1-10-12

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR3(7-14)
36.

Log Number 010

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Ocean
Address 350 West 28th St
NY NY
Phone No.

Generator Site/Location
Address Same
Phone No.

Description of Material

Approval Number CY-819

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 290
GROSS 47.07 T GROSS
TARE 14.11 T TARE
RECALLED
NET 32.96 T NET
LOG 96
01/10/2012 TONNAGE
04:07PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent for generator — 01/10/12
Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name Somerset LLC
Address Lake Ln
Ledgewood, NJ
Driver Name (Print) Hector
Vehicle License No. / State / EPA No. C927228
Truck Number 11

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date 01-10-12

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date 01-10-12

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 1/10/12
Name of Authorized Agent / Signature / Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3(7-14)

Log Number 009

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Generator Site/Location

Address 362 West 30th NY, NY

Address Grove

Phone No.

Phone No.

Approval Number 04-899

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 600
GROSS 48.73 GROSS
TARE 13.69 T
RECALCED
NET 35.04 T TARE
LOG 97 NET
01/10/2012
04:11PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

GC agent for company 1/10/12

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name Scarsdale

Driver Name (Print) JUAN OLIVERA

Address

Vehicle License No. / State / EPA No. AM 3317

Truck Number #1

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Carroll 1/10/12

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-31D-14

36

SOIL SAFE, INC.

Log Number 011

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 360 West 36th NY NY

Phone No.

Generator Site/Location

Address Same

Phone No.

Approval Number CH-8191

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

JU 1020

GROSS 43.97 GROSS

TARE 13.65 T TARE

RECALLED

NET 30.32 T NET

LOG 98

01/10/2012

04:16PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Cus agent to generate — 1/10/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Sanvr(p)

Address Montv. NJ

Driver Name (Print) Johnston C

Vehicle License No. / State / EPA No. AW3535

Truck Number 0 P

I hereby certify that the above named material was picked up at the generator site listed above.

Johnston C

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Johnston C

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 1.10.12

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3(7-11)

Log Number 018

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Grey

Address 262 West 26th NJ NJ

Phone No.

Generator Site/Location

Address

Phone No.

Approval Number CH-999

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

TO 1015
GROSS 46.23 GROSS
TARE 13.50 T
RECALLED TARE
NET 32.73 T
LOG 106 NET
01/10/2012
05:15PM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to collect 1/10/12

Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name Somerset

Driver Name (Print) WALTON

Address

Vehicle License No. / State / EPA No. AM 1442

Truck Number 403

I hereby certify that the above named material was picked up at the generator site listed above.

1/10/12

Driver Signature / Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature / Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130, Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia 1/10/12

Name of Authorized Agent / Signature / Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3 (04)

Log Number 0002

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W 39th St

NY NY

Generator Site/Location SAME

Address

Phone No.

Phone No.

Approval Number CH-BAR

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 680
GROSS 44.75 GROSS
TARE 13.69 T
RECALLED TARE
NET 31.06 T
LOG 18 NET
01/11/2012
11:01AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Agent to Generator — 1/11/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Synergy

Driver Name (Print) Joao Oliveira

Address

Vehicle License No. / State / EPA No. AM331D

Truck Number #1

I hereby certify that the above named material was picked up at the generator site listed above.

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Shipment Date

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia — 1/11/12

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4(7-19)

Log Number 003

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 360 West 26th St

NY, NY

Generator Site/Location

Address Same

Phone No.

Phone No.

Approval Number CH8196

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 1065
GROSS 45.31 T GROSS
TARE 14.04 T TARE
RECALLED *
NET 31.27 T NET
LOG 20
01/11/2012 TONNAGE
11:10AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

(as agent to generator) 1/11/12

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name Somerset J&J

Address 67 Washington St Warwick NY 02,104

Driver Name (Print) Cristian Montes

Vehicle License No. / State / EPA No. NN844M NJ

Truck Number 98 / 1065

I hereby certify that the above named material was picked up at the generator site listed above.

1/11/12

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

1/11/12

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

A. Garcia 1/11/12

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-411(2-14)

SOIL SAFE, INC.

Log Number 00414

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W Scott St

NJ NY

Phone No.

Generator Site/Location

Address

Phone No.

Approval Number C4-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 122
GROSS 41.41 T
TARE 13.42 T
RECYCLED
NET 33.69 T
LOG 21
01/11/2012
11:12PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Agent Agent Name) Signature 1/11/12

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name Somers

Address T & T Bros

Newark NJ

Driver Name (Print) Marco Moro

Vehicle License No. / State / EPA No. AL362C

Truck Number 69.

I hereby certify that the above named material was picked up at the generator site listed above.

Marco Moro 1/11/12

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Marco Moro 1/11/12

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Agent Signature 1/11/12

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4(3-4)

36

Log Number 005

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 250 West 26th

NY, NY

Phone No.

Generator Site/Location

Address Same

Phone No.

Approval Number 04-8190

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

11:12AM

GROSS	47.29 T	GROSS
TARE	13.91 T	TARE
RECALLED NET	33.38 T	NET
LOG 29		TONNAGE
01/11/2012		
11:54AM		

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Generator Authorized Agent Name Signature 1/11/12 Shipment Date

TRANSPORTER

Transporter Name JG #13

Address

Driver Name (Print) MARIO CHICA

Vehicle License No. / State / EPA No. AZ76UC

Truck Number 13 136

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature 1-11-12 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature 1/11/12 Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent Signature 1/11/12 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-407-14

Log Number 006

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 26th NY, NY

Phone No.

Generator Site/Location

Address Soma

Phone No. ID 515

Approval Number 04-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS 41.64 GROSS
TARE 12.99 TARE
RECALLED NET 31.65 NET
LOG 55 TONNAGE
01/11/2012
04:01PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 1/11/12

Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name Somerset LLC

Driver Name (Print)

Address

Vehicle License No. / State / EPA No. AM536E

Truck Number 515

I hereby certify that the above named material was picked up at the generator site listed above.

1/11/12

Driver Signature / Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

1/11/12

Driver Signature / Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

1/11/12

Name of Authorized Agent / Signature / Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-4(2-14)

Log Number 007

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Group

Address 260 West 39th
NY, NY

Phone No.

Generator Site/Location

Address Same

Phone No.

Description of Material

Approval Number 04-8199

Non-Regulated Petroleum
Contaminated Soil

Non DOT/RCRA Regulated

ID 680
GROSS 44.47 T GROSS
TARE 13.69 T TARE
RECALLED
NET 30.78 T NET
LOG 56
01/11/2012 TONNAGE
04:07PM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

QS agent to generate — 1/11/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Somerset LLC

Address

Driver Name (Print) JOAO OLIVEIRA

Vehicle License No. / State / EPA No. AM33LD

Truck Number #4

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia — 1-11-12

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

1, 4 TR4(7-14)

JC

Log Number 001

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green Generator Site/Location Same

Address 260 W. 26th Street Address

New York, N.Y.

Phone No. Phone No.

Approval Number CA 8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 738
GROSS 51.26 T GROSS
TARE 14.37 T TARE
RECALLED
NET 36.89 T NET
LOG 3
01/12/2012 TONNAGE
10:15AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator 1/10/12

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name P.A. Carrillo Driver Name (Print) Orlando Jackson

Address Vehicle License No. / State / EPA No. AN280R-NJ

E Orange N.J. Truck Number 738

I hereby certify that the above named material was picked up at the generator site listed above.

1-12-12

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

1-12-12

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia 1/12/12

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3(744)

SOIL SAFE, INC.

Log Number 003

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Generator Site/Location

Address 260 West 26th St

NY NY

Address

Phone No.

Phone No.

Approval Number CA 8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 600
GROSS 47.55 T GROSS
TARE 13.28 T TARE
RECALLED
NET 34.27 T NET
LOG S
01/12/2012
10:57AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent for Gordon 1/12/12

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name Carlo e Sons

Driver Name (Print) EDCHampion

Address 11 Rennett Ave

East Rockaway

Vehicle License No. / State / EPA No.

Truck Number NO: 14

I hereby certify that the above named material was picked up at the generator site listed above.

Edward Champion 1-12-12

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Edward Champion 1-12-12

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Garcia 1/12/12

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3 TP-3 (7-14)
36 TP-3 (7-14)

Log Number 003

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name: Chelsea Green
Address: 260 W. 26th Street
New York, NY
Phone No.:

Generator Site/Location: Same
Address:
Phone No.:

Approval Number: C4-8171

Description of Material:
Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

ID 5516
GROSS 44.55 T — GROSS
TARE 14.44 T — TARE
REGRILLED
NET 30.11 T — NET
LOG 6
01/12/2012
11:00AM — TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

GS a/a/f TOPSOIL — 1/10/12
Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name: P.A. Carsillo & Sons
Address: 44 Bedford Street
East Orange, NJ
Driver Name (Print): Stephen Siencull
Vehicle License No. / State / EPA No.: AM678D
Truck Number: 16

I hereby certify that the above named material was picked up at the generator site listed above.
1-12-12
Driver Signature / Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.
1-12-12
Driver Signature / Delivery Date

DESTINATION

Site Name: **Soil Safe, Inc. - Bridgeport** Phone No.: **1-856-467-8030**
Address: **378 Route 130 Logan Township, NJ 08085**
No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Gordo — 1/12/12
Name of Authorized Agent / Signature / Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-2 (7-4)
JC.

Log Number 004

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA GREEN Generator Site/Location SAME

Address 260 WEST 26th ST Address

NEW YORK

Phone No. Phone No.

Approval Number C4 8109

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 311
GROSS 45.34 T GROSS
TARE 14.29 T TARE
RECALLED
NET 31.65 T NET
LOG 0
01/12/2012 TONNAGE
11:18AM

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS agent for Chelsea Green 1/12/12

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name JDC TRUCKING Driver Name (Print) CARLOS OLIVEIRA

Address 75 WINDSOR ST Vehicle License No. / State / EPA No. AL8760T

KEARNY NJ Truck Number 311

I hereby certify that the above named material was picked up at the generator site listed above.

1/12/12

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

1/12/12

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J Correia 1-12-12

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3 (7-14)

SOIL SAFE, INC.

Log Number 006

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W. 26th St

New York NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number CA 8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 738

GROSS 51.74 T

TARE 14.37 T TARE

RECALLED

NET 37.37 T NET

LOG 32

01/12/2012

02:32PM

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 1/12/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name PA Carting

Address E Orange NJ

Driver Name (Print) Orlando Jackson

Vehicle License No. / State / EPA No. ANZ80C NJ

Truck Number 738

I hereby certify that the above named material was picked up at the generator site listed above.

1-12-12

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

1-12-12

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

A. Garcia — 1/12/12

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3 (7-14)

SC

SOIL SAFE, INC.

Log Number 007

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 960 Lucas Ave NW

Generator Site/Location

Address

Phone No.

Phone No. 10 600

Approval Number C-A 8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS 47.85 T
TARE 13.28 T
RECALCED
NET 34.57 T
LOG 42
01/12/2012
1:13:56PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

C Sagoff to Marin — 1/12/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Brindle & Sons

Address 11 Roosevelt Ave

East Hanover NJ

Driver Name (Print) E D Champion

Vehicle License No. / State / EPA No. AM185-A

Truck Number 10, 14

I hereby certify that the above named material was picked up at the generator site listed above.

E Champion 1-12-12

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Edward Champion 1-12-12

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Garcia 1/12/12

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3 (7-14)

J6.

SOIL SAFE, INC.

Log Number 008

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 W. 26th Street
New York, NY

Phone No.

Generator Site/Location SAME

Address

Phone No.

Approval Number 04-8199

Description of Material

Non-Regulated Petroleum
Contaminated Soil

Non DOT/RCRA Regulated

ID 595
GROSS 43.85 T
TARE 14.44 T
RECALLED
NET 29.41 T
LOG 45
01/12/2012
04:03PM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent for generator — 1/12/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name P.A. Castillo Trans

Address 44 Bedford St.
East Orange, NJ

Driver Name (Print) Stephen Siancutti

Vehicle License No. / State / EPA No. 446780

Truck Number 16

I hereby certify that the above named material was picked up at the generator site listed above.

1-12-12

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

1-12-12

Driver Signature — Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Collier — 1/12/12

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TR-3(7-14)

SOIL SAFE, INC.

Log Number 0091

NON-HAZARDOUS MATERIAL MANIFEST

SG.

GENERATOR

Generator Name Chelsea Green

Address 360 W 36th St NY NY

Phone No.

Generator Site/Location

Address Same

Phone No.

Approval Number 04-8199

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

ID 1015
GROSS 54.08 GROSS
TARE 13.50 T
RECALLED TARE
NET 40.58 T
LOG 1 NET
01/12/2012
08:14AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

GS agent to agent 1/11/12

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name Sunset

Address

Driver Name (Print) WALTON

Vehicle License No. / State / EPA No. AM 1442

Truck Number #03

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature 01/11/12 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature Delivery Date

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

J. Gore 1/12/12

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

TP-3(7-14)

JG.

Log Number 005

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Piers

Address 260 W 26ST NY, NY

Phone No.

Generator Site/Location

Address

Phone No.

Approval Number CH 21 99

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

10 311

GROSS 40.29 T GROSS

TARE 14.29 T TARE

RECALLED

NET 26.00 T NET

LOG !

01/13/2012

07:35AM TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS AGNT TO Generator — 1/12/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name JDC

Address LEAH NY

Driver Name (Print) Jack

Vehicle License No. / State / EPA No. AC 5767

Truck Number SS 31

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date 1/12/12

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date 1/12/12

DESTINATION

Site Name **Soil Safe, Inc. - Bridgeport** Phone No. **1-856-467-8030**

Address **378 Route 130 Logan Township, NJ 08085**

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Garcia — 1/13/12

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

Tonnages for C4-8199 by Date, Log Number

From 1/9/2012 To 1/14/2012

Date	Log #	Truck Number	Truck Company	City	Batch#	Net
C4-8199						
			1/9/2012			
1/9/2012	1	601	SOMER		9000	34.77
1/9/2012	4	740	SOMER		9000	27.09
1/9/2012	6	8	SOMER		9000	27.60
1/9/2012	8	652	SOMER		9000	30.18
1/9/2012	21	601	SOMER		9000	34.78
1/9/2012	23	740	SOMER		9000	35.24
1/9/2012	26	746	SOMER		9000	35.52
1/9/2012	27	279	SOMER		9000	36.15
1/9/2012	28	8	SOMER		9000	32.67
	Total volume for Date = 1/9/2012 (9 detail records)		294	Average Weight: 32.66666667		
			1/10/2012			
1/10/2012	18	515	SOMER		9000	33.50
1/10/2012	29	1015	SOMER		9000	37.93
1/10/2012	30	680	SOMER		9000	30.02
1/10/2012	35	290	SOMER		9000	32.04
1/10/2012	36	1020	SOMER		9000	29.91
1/10/2012	43	740	SOMER		9000	33.90
1/10/2012	89	279	SOMER		9000	35.79
1/10/2012	90	515	SOMER		9000	33.84
1/10/2012	96	290	SOMER		9000	32.96
1/10/2012	97	680	SOMER		9000	35.04
1/10/2012	98	1020	SOMER		9000	30.32
1/10/2012	106	1015	SOMER		9000	32.73
	Total volume for Date = 1/10/2012 (12 detail records)		397.98	Average Weight: 33.165		
			1/11/2012			
1/11/2012	18	680	SOMER		9000	31.06
1/11/2012	20	1065	SOMER		9000	31.27
1/11/2012	21	122	SOMER		9000	33.69
1/11/2012	29	138	SOMER		9000	33.38
1/11/2012	55	515	SOMER		9000	31.65
1/11/2012	56	680	SOMER		9000	30.78
	Total volume for Date = 1/11/2012 (6 detail records)		191.83	Average Weight: 31.97166667		
			1/12/2012			
1/12/2012	1	1015	SOMER		9000	40.58
1/12/2012	3	738	CARSILLO		9000	36.89
1/12/2012	5	600	CARSILLO		9000	34.27
1/12/2012	6	596	CARSILLO		9000	30.11
1/12/2012	8	311	CARSILLO		9000	31.65
1/12/2012	32	738	CARSILLO		9000	37.37
1/12/2012	42	600	CARSILLO		9000	34.57

Date	Log #	Truck Number	Truck Company	City	Batch#	Net
1/12/2012	45	596	CARSILLO		9000	29.41
	Total volume for Date = 1/12/2012 (8 detail records)		274.85	Average Weight:	34.35625	
			1/13/2012			
1/13/2012	1	311	CARSILLO		9000	26.00
	Total volume for Date = 1/13/2012 (1 detail record)		26	Average Weight:	26	
Total Volume for Approval Number = C4-8199 (36 detail records)					1184.66	
Total Trucks: 36						
Grand Total				1184.66		

1/10/12 Log 3 Sec 3

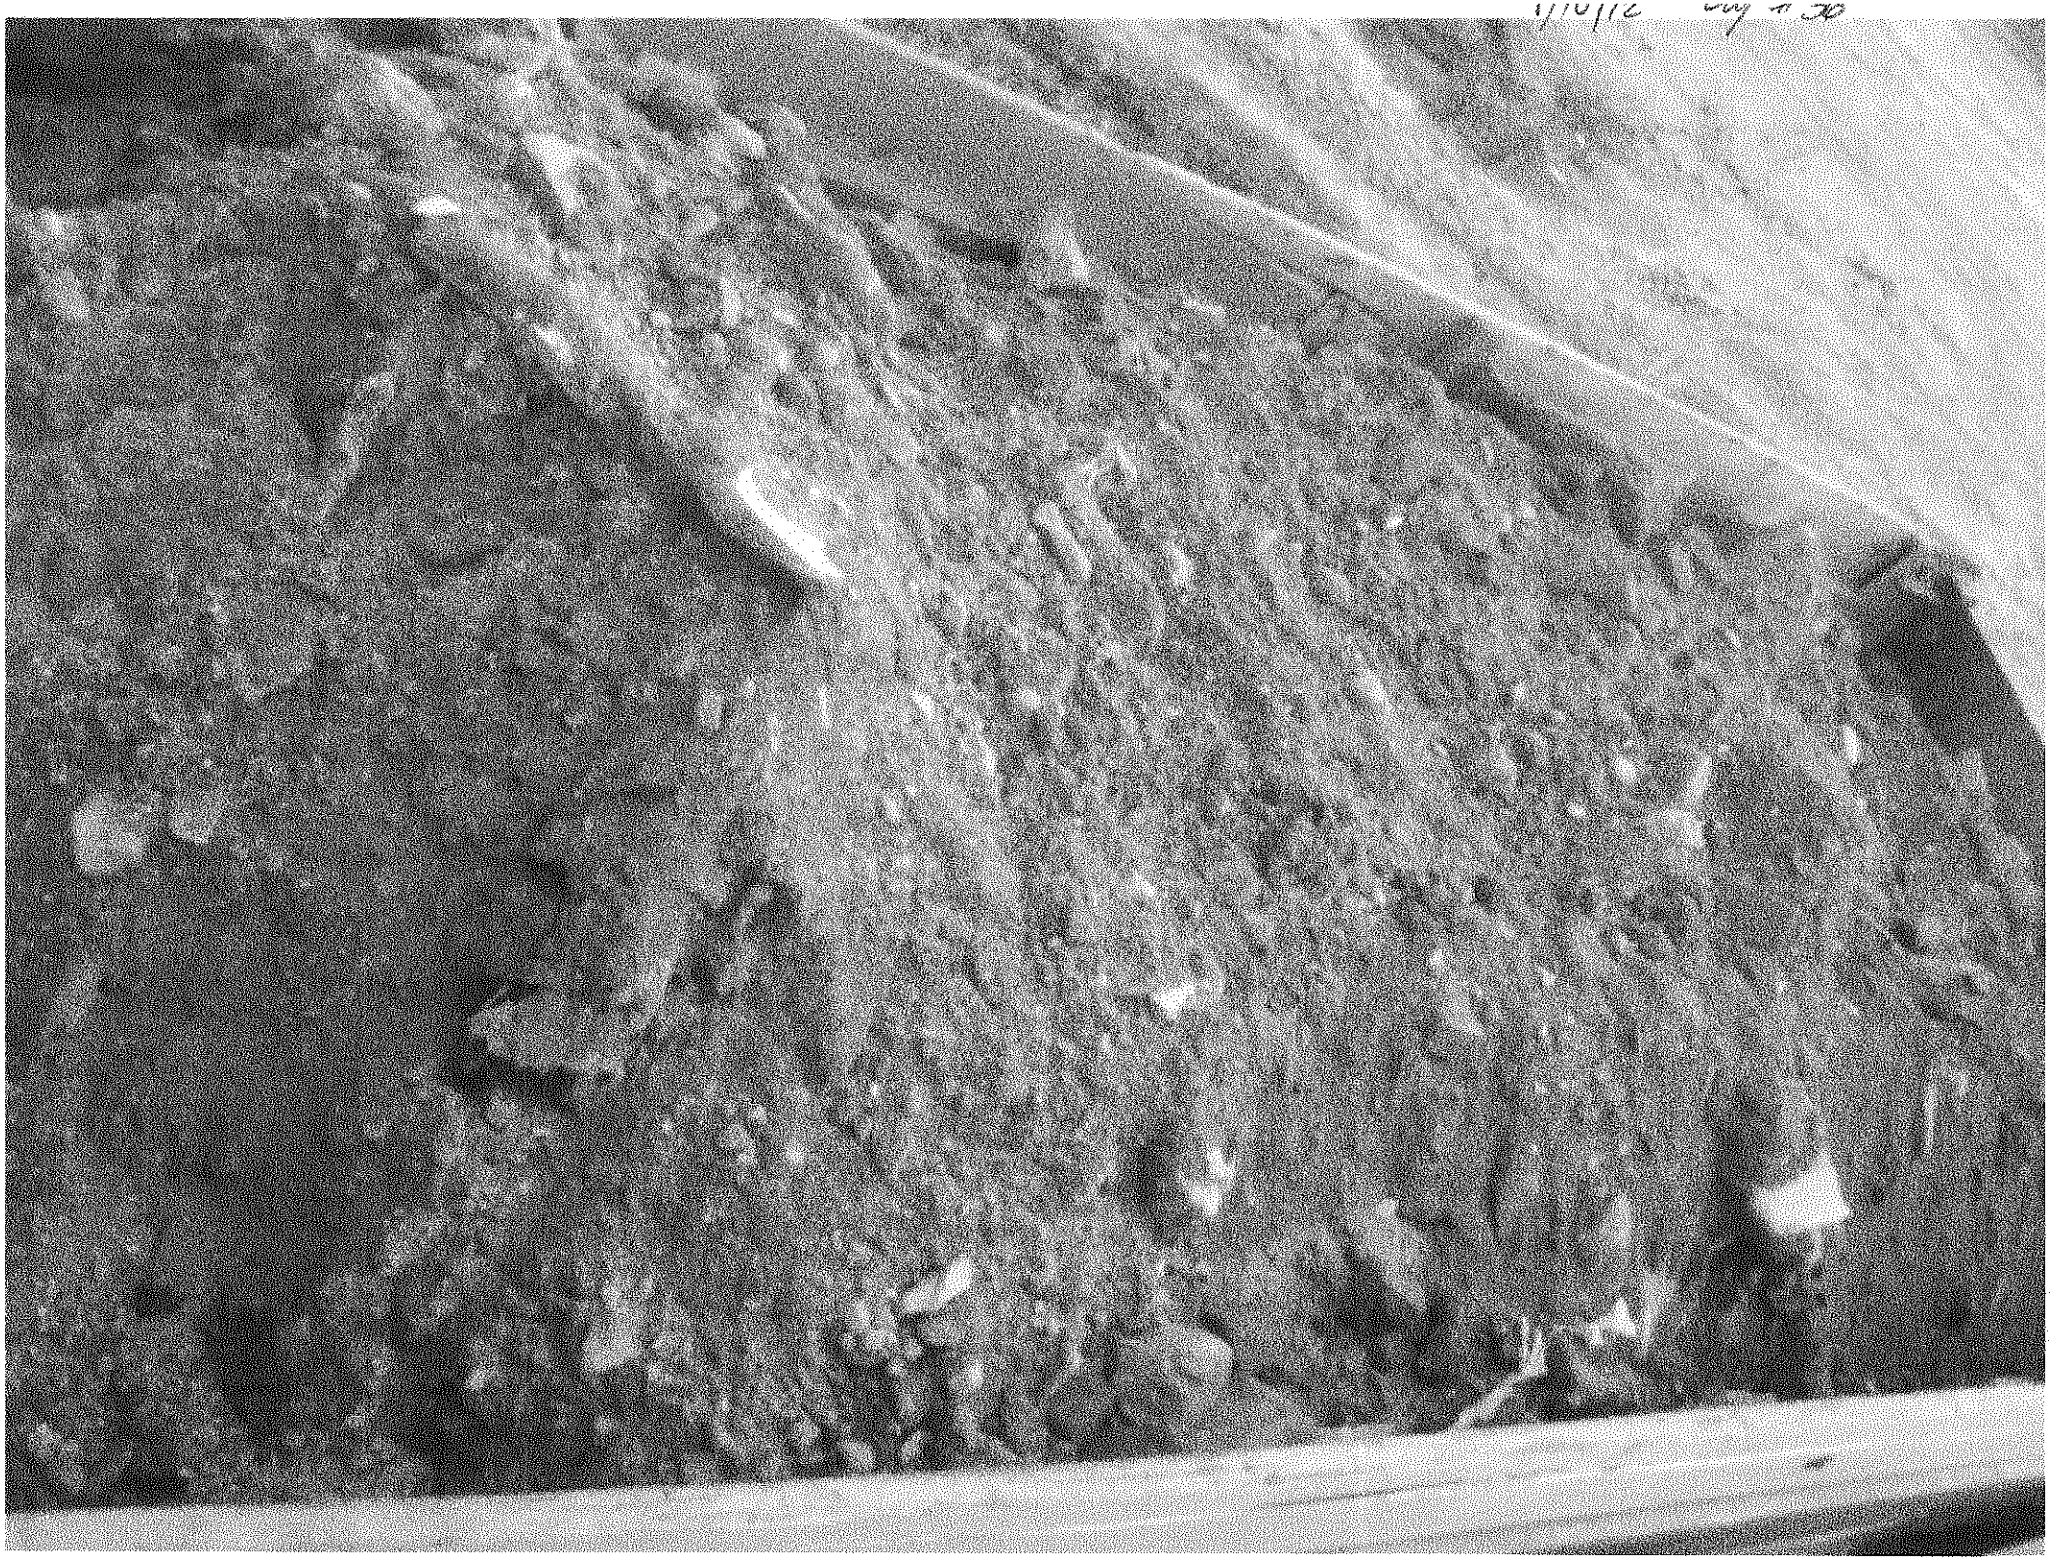

11/11/12 cwy #10

1/11/12 Log #36

1/12/12 Log #42

1/12/12
Log #5

1/15/12 Log #1

SoilSafe
Solutions Group

6700 Alexander Bell Drive, Suite 300, Columbia, MD 21046
(410) 872-3990, Fax (410) 872-3978

Invoice

10371

Bill To:	**Project:**
Chelsea West 26, LLC c/o Artimus Construction, Inc. Attention: Amnon Solomon 37 West 65th Street New York, NY 10023	Chelsea Green 260 West 26th Street New York, NY 10001

APPROVAL #: 451
PROPOSAL #: 570
PO #:
INVOICED VOLUME OF SOIL: 996.58
 # OF TRUCKS: 31
INVOICE DATE: 2/27/12
DUE DATE: 3/28/12

BILLING PERIOD: 2/13/12 TO 2/14/12

DESCRIPTION:	UNITS INVOICED:	RATE:	AMOUNT:
Disposal & Transportation Fees - tons	996.58	$ 48.00	$ 47,835.84

1) REC'D 3/6/12 2) ENTERED/JOB 3/6/12
3) PS MATCHED
4) SCANNED & MOVED
5) PM APPROVED & UPDATED ENTRY
6) CONTROLLER REVIEW
7) EXEC 1 REVW 7a) EXEC 2 REVW
7b) CHK CUT 7c) EXEC 3 REVW
8) CHECK DATE CHECK#
CHECK AMOUNT

GROSS INVOICE	$ 47,835.84
SALES TAX	0.00
LESS: PREPAYMENTS	0.00
INVOICE TOTAL	$ 47,835.84

Contact:

**NOTE* Payments are Net 30 days. Overdue balances are subject to a 1.5% charge per month or the maximum allowed by law.*

Remit to: (Payments Only) P.O. Box 824062, Philadelphia, PA 19182-4062

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/13/12 Ticket #: 169281
Time: 09:14 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: JENCAR
JENCAR Phase: 0
Truck: AN546M
License: JENCAR 22

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 1 Amount: 36.18 Tn 32.82 Mg
(To-Date) Loads: 15 Amount: 476.07 Tn 431.89 Mg

Gross: 50.18 Tn 100360 lb 45.52 Mg
Tare: 14.00 Tn 28000 lb 12.70 Mg
Net: 36.18 Tn 72360 lb 32.82 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

Log Number 001

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

JENCAR # 22

Generator Name Chelsea Green

Address 260 West 26th St NY, NY

Phone No.

Generator Site/Location

Address SAME

Phone No.

Approval Number 120144

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

agent to generator — Signature — 2/13/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Carrillo (Quickballas)

Address

Driver Name (Print) Aldobera Hernandez

Vehicle License No. / State / EPA No. AN546IM

Truck Number # 22

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 2-13-12 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 2-13-12 Delivery Date

DESTINATION

Site Name Pure Soil Tech — Soil Safe, Inc. - Edgeboro

Phone No. 732-657-8551 — [redacted]

Address [redacted] 655 South Hope Chapel Rd. Jackson NJ 08527

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — 2-13-12 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/13/12 Ticket #: 169283
Time: 09:33 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: NICK
NICKABELLAS Phase: 0
Truck: AN700H
License:

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 2 Amount: 70.60 In 64.05 Mg
(To-Date) Loads: 16 Amount: 510.49 Tn 463.12 Mg

Gross:	48.73 Tn	97460 lb	44.21 Mg
Tare:	14.31 Tn	28620 lb	12.98 Mg
Net:	34.42 Tn	68840 lb	31.23 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

97460

Log Number 002

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea

Address 260 West 20th St NY, NY

Phone No.

Generator Site/Location

Address SOIL

Phone No.

Approval Number R0144

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

QS agent to generator — Signature — 2/13/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Nickolellas

Driver Name (Print) Jorge Pelaez

Address

Vehicle License No. / State / EPA No. AN700H

Truck Number #26

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 2-13-12 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 2-13-12 Delivery Date

DESTINATION

Site Name Pure Soil Tech — Soil Safe, Inc. Bridgeport — Phone No. 732-657-8551 — [redacted]

Address [redacted] 655 South Hope Chapel Rd. Jackson, NJ 0852

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — 2-13-12 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/13/12 Ticket #: 169284
Time: 09:38 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: CARILL
CARSILLO TRUCKING Phase: 0
Truck: AN280R
License: CARSILLO 19

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 3 Amount: 104.12 Tn 94.46 Mg
(To-Date) Loads: 17 Amount: 544.01 Tn 493.53 Mg

Gross:	48.24 Tn	96480 lb	43.76 Mg
Tare:	14.72 Tn	29440 lb	13.35 Mg
Net:	33.52 Tn	67040 lb	30.41 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

Log Number 003

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea W26 LLC
Address 37 W. 65th ST
NEW York NY
Phone No.

Generator Site/Location 260 W 26th St
Address 260 W. 26th St
NEW YORK, N.Y.
Phone No.

Approval Number	Description of Material	
1201044	Non-Regulated Petroleum Contaminated Soil Non DOT/RCRA Regulated	GROSS TARE NET TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 2/13/12
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name P.A. CARTING
Address E. ORANGE N.J.
Driver Name (Print) Orlando Jackson
Vehicle License No. / State / EPA No. AW280IC-NJ
Truck Number 19

I hereby certify that the above named material was picked up at the generator site listed above.

2-13-12
Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

2/13-12
Driver Signature — Delivery Date

DESTINATION

Site Name ~~Soil Safe, Inc. Bridgeport~~ Rare Soil Tech
Phone No. ~~1-856-467-0050~~ 732-657-8551
Address ~~375 Route 130 Logan Township, NJ 08085~~ 655 South Hope Chapel Rd. Jackson, NJ 08527
No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

2-13-12
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/13/12 Ticket #: 169287
Time: 10:03 Plant: P1
*** Recycled ***

Customer: 0006435
SOIL SAFE INC.
6900 ALEXANDER BELL DRIV
COLUMBIA, MD 21046
(410) 872-3990

Job: 1201044
260 W. 26TH STREET
260 W. 26TH STREET
NEW YORK, NY 10001

P.O.#:

Carrier: CARILL
CARSILLO TRUCKING

Phase: 0

Truck: AM185A
License: CARSILLO 14

Zone:

Product: JR66
JR66 SOIL
JMF:

DEFAULT ZONE NAME

(Daily) Loads: 4 Amount: 136.28 Tn 123.63 Mg
(To-Date) Loads: 18 Amount: 576.17 Tn 522.70 Mg

Gross:	46.69 Tn	93380 lb	42.36 Mg
Tare:	14.53 Tn	29060 lb	13.18 Mg
Net:	32.16 Tn	64320 lb	29.18 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

Log Number 005

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green
Address 260 West 26th St
NY NY
Phone No. /

Generator Site/Location
Address Same
Phone No.

Approval Number 120044

Description of Material
Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — Generator Authorized Agent Name
Signature
2/13/12 — Shipment Date

TRANSPORTER

Transporter Name Carsillo & Sons
Address 11 Roosevelt Ave
E. Hanover, NJ

Driver Name (Print) Cesar Machado
Vehicle License No. / State / EPA No. AM185M NJ
Truck Number 14

I hereby certify that the above named material was picked up at the generator site listed above.
Driver Signature
2/13/12 — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.
Driver Signature
2/13/12 — Delivery Date

DESTINATION

Pine Soil Tech — Site Name
Soil Safe, Inc. - Contact
732-657-8551 — Phone No.
Address 372 Route 130 Logan Township, NJ 08085
655 South Hope Chapel Rd, Jackson, NJ 08527

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent
Signature
2-13-12 — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/13/12 Ticket #: 169288
Time: 10:07 Plant: P1
*** Recycled ***

Customer: 0006435
SOIL SAFE INC.
6900 ALEXANDER BELL DRIV
COLUMBIA, MD 21046
(410) 872-3990

Job: 1201044
260 W. 26TH STREET
260 W. 26TH STREET
NEW YORK, NY 10001

P.O.#:

Carrier: CARILL
CARSILLO TRUCKING
Truck: AM572U
License: CARSILLO 17

Phase: 0

Zone:

Product: JR66
JR66 SOIL
JMF:

DEFAULT ZONE NAME

(Daily) Loads: 5 Amount: 168.93 Tn 153.25 Mg
(To-Date) Loads: 19 Amount: 608.82 Tn 552.32 Mg

Gross:	45.81 Tn	91620 lb	41.56 Mg
Tare:	13.16 Tn	26320 lb	11.94 Mg
Net:	32.65 Tn	65300 lb	29.62 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

91620

Log Number 004

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 26th St NY NY

Phone No. /

Generator Site/Location Same

Address

Phone No.

Approval Number 1A81014

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator. 2/13/12

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name Carillo & Sons

Address 11 Roosevelt Ave East Hanover NJ

Driver Name (Print) ED Champion

Vehicle License No. / State / EPA No. AM5782-J

Truck Number No. 17

I hereby certify that the above named material was picked up at the generator site listed above.

Edward Champion 2-13-12

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Edward Champion 2-13-12

Driver Signature | Delivery Date

DESTINATION

Site Name Pure Soil Tech. Soil Safe, Inc. - Bridgeport

Phone No. 732-657-8551 856-467-8080

Address 655 South Hope Chapel Rd, Jackson, NJ 08527 ~~3721 Route 130 Logan Township, NJ 08085~~

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

2-13-12

Name of Authorized Agent | Signature | Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/13/12 Ticket #: 169297
Time: 11:33 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: CVTRUC
CV TRUCKING Phase: 0
Truck: AL347A
License:

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 6 Amount: 197.84 Tn 179.48 Mg
(To-Date) Loads: 20 Amount: 637.73 Tn 578.55 Mg

Gross:	42.31 Tn	84620 lb	38.38 Mg
Tare:	13.40 Tn	26800 lb	12.16 Mg
Net:	28.91 Tn	57820 lb	26.23 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

84600

SOIL SAFE, INC.

Log Number 07546 007

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name W.26 LLC CHELSEA

Address 37. W. 65TH N.Y., N.Y. 10025

Phone No.

Generator Site/Location 260 W. 26

Address N.Y., N.Y. 10025

Phone No.

Approval Number 12011 044

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

3 HRS B-4 LOADED
ARR 7AM
LOADED 10AM

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Dennis Mormile — Signature — 2/13/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name CV 56

Address NWK NJ.

Driver Name (Print) B. HARTMAN

Vehicle License No. / State / EPA No. AL347A

Truck Number CV 56

I hereby certify that the above named material was picked up at the generator site listed above.

BH 2-13-12

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

BH 2-13-12

Driver Signature — Delivery Date

DESTINATION

Pure Soil Tech — 732-602-8551

Site Name — Phone No.

Address [redacted] 655 South Hope Chapel Rd, Jackson, NJ 08527

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

2-13-12

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 C. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/13/12 Ticket #: 169298
Time: 11:47 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: CVTRUC
CV TRUCKING Phase: 0
Truck: AN392P
License:

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 7 Amount: 229.49 Tn 208.19 Mg
(To-Date) Loads: 21 Amount: 669.38 Tn 607.26 Mg

Gross:	45.76*Tn	91520*lb	41.51*Mg
Tare:	14.11 Tn	28220 lb	12.80 Mg
Net:	31.65 Tn	63300 lb	28.71 Mg

* - Manual Weight

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

91520

SOIL SAFE, INC.

Log Number 008
07546

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA W.26 LLC
Address 37 W. 65 TH STREET
NEW YORK, NY 10023
Phone No.

Generator Site/Location 260 W 26 TH STREET
Address 260 W. 26 TH STREET
NEW YORK, NY
Phone No.

Approval Number	Description of Material		
1201044	Non-Regulated Petroleum Contaminated Soil Non DOT/RCRA Regulated	Time In 7:20am Time Out 10:20	GROSS TARE NET TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — Signature — 2/13/12
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name CV-TEV TRUCK, INC
Address 182 CALCUTTA ST NEWARK
N.J. 07114
Driver Name (Print) ERIC N. Fuentes
Vehicle License No. / State / EPA No. AM304Z N.J.
Truck Number #99

I hereby certify that the above named material was picked up at the generator site listed above.

Eric N. Fuentes — 2/13/12
Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Eric N. Fuentes — 2/13/12
Driver Signature — Delivery Date

DESTINATION

Pure Soil Tech — 732-602-8551
Site Name — Phone No.
Address 655 South Hope Chapel Rd Jackson, NJ 08527
No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

RA — 2-13-12
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/13/12 Ticket #: 169299
Time: 11:49 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: CVTRUC
CV TRUCKING Phase: 0
Truck: AM303S
License:

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 8 Amount: 262.41 Tn 238.06 Mg
(To-Date) Loads: 22 Amount: 702.30 Tn 637.13 Mg

Gross:	46.14 Tn	92280 lb	41.86 Mg
Tare:	13.22 Tn	26440 lb	11.99 Mg
Net:	32.92 Tn	65840 lb	29.87 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

92342

Log Number 006
07546

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea W. 26 LLC
Address 37 W. 65th Street
New York, NY 10025
Phone No.

Generator Site/Location 260 W. 26th Street
Address New York, NY
Phone No.

Approval Number 1201044

Description of Material
Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

Time In 7:30
Out 9:35

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as a agent to generator
Generator Authorized Agent Name

Signature

2/13/12
Shipment Date

TRANSPORTER

Transporter Name CV Trucking
Address 182 Calcutta St Port Newark NJ.

Driver Name (Print) Juan R. Ruiz
Vehicle License No. / State / EPA No. AM3035
Truck Number 21

I hereby certify that the above named material was picked up at the generator site listed above.

Juan R Ruiz
Driver Signature

02/13/12
Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature

Delivery Date

DESTINATION

Pure Soil Tech
Site Name

732-657-8551
Phone No.

Address 655 South Hope Chapel Rd. Jackson, NJ 08527

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

2-13-12
Name of Authorized Agent

Signature

Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/13/12 Ticket #: 169303
Time: 13:00 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: NICK
NICKABELLAS Phase: 0
Truck: AN700H
License:

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 9 Amount: 296.30 Tn 268.80 Mg
(To-Date) Loads: 23 Amount: 736.19 Tn 667.87 Mg

Gross:	48.20 Tn	96400 lb	43.73 Mg
Tare:	14.31 Tn	28620 lb	12.98 Mg
Net:	33.89 Tn	67780 lb	30.75 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

Log Number 009

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 250 West 26th St NY NY

Phone No.

Generator Site/Location

Address Same

Phone No.

Approval Number 12014

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — Signature — 2/13/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Nickabellas

Driver Name (Print) Jorge Pelaez

Address

Vehicle License No. / State / EPA No. AN700H

Truck Number 26

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 2-13-12 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 2-13-12 Delivery Date

DESTINATION

Site Name Pure Soil Tech ~~Soil Safe, Inc. Bridgeport~~

Phone No. 732-657-8551 ~~(856) 467-8080~~

Address ~~376 Route 130 Logan Township, NJ 08085~~ 655 South Hope Chapel Rd. Jackson, NJ 08527

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — 2-13-12 Receipt Date

White – Facility Green – Facility Yellow – Driver Pink – Customer Goldenrod – Customer Blue – Facility

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/13/12 Ticket #: 169306
Time: 13:21 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: CARILL
CARSILLO TRUCKING Phase: 0
Truck: AN280R
License: CARSILLO 19

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 10 Amount: 331.70 Tn 300.92 Mg
(To-Date) Loads: 24 Amount: 771.59 Tn 699.99 Mg

Gross:	50.12 Tn	100240 lb	45.47 Mg
Tare:	14.72 Tn	29440 lb	13.35 Mg
Net:	35.40 Tn	70800 lb	32.12 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

Log Number 010

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea W 20 LLC
Address 37 W. 65th St
NEW YORK, N.Y.
Phone No.

Generator Site/Location 260 W 26th ST.
Address
NEW YORK, N.Y.
Phone No.

Approval Number 120104

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 2/13/12
Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name P.A. Carsillo
Address
E ORANGE NJ
Driver Name (Print) ORLANDO JACKSON
Vehicle License No. / State / EPA No. AN2802 - NJ
Truck Number 19

I hereby certify that the above named material was picked up at the generator site listed above.
Driver Signature 2-13-12 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.
Driver Signature 2-13-12 Delivery Date

DESTINATION

Site Name Pure Soil Tech. — Soil Safe, Inc. - Bridgeport
Phone No. 732-657-8551 — [illegible]
Address [illegible] 655 South Hope Chapel Rd Jackson, NJ 08527
No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent / Signature / 2-13-12 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
255 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/13/12 Ticket #: 169313
Time: 13:50 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: CARILL
CARSILLO TRUCKING Phase: 0
Truck: AM572U
License: CARSILLO 17

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 11 Amount: 366.35 Tn 332.35 Mg
(To-Date) Loads: 25 Amount: 806.24 Tn 731.42 Mg

Gross:	47.81 Tn	95620 lb	43.37 Mg
Tare:	13.16 Tn	26320 lb	11.94 Mg
Net:	34.65 Tn	69300 lb	31.43 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

Log Number 011

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 26th St NY NY

Phone No.

Generator Site/Location

Address Same

Phone No.

Approval Number Bdoxy

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 2/13/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Carella & Sons

Address 11 Roosevelt Ave East Hanover NJ

Driver Name (Print) ED Champion

Vehicle License No. / State / EPA No. AM 572-N

Truck Number No: 17

I hereby certify that the above named material was picked up at the generator site listed above.

Edward Champion — 2-13-12

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Edward Champion — 2-13-12

Driver Signature — Delivery Date

DESTINATION

Site Name Pine Soil Tech. ~~Soil Safe, Inc. - Bridgeport~~

Phone No. 732-657-8551 ~~[illegible]~~

Address ~~375 Route 130 Bordentown Township, NJ 08505~~ 655 South Hope Chapel Rd, Jackson, NJ 08527

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

2-13-12

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/13/12 Ticket #: 169314
Time: 13:57 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: CARILL
CARSILLO TRUCKING Phase: 0
Truck: AM185A
License ARSILLO 14

Zone:

Product: 166 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 12 Amount: 398.95 Tn 361.93 Mg
(To-Date) Loads: 26 Amount: 838.84 Tn 761.00 Mg

Gross:	47.13 Tn	94260 lb	42.76 Mg
Tare:	14.53 Tn	29060 lb	13.18 Mg
Net:	32.60 Tn	65200 lb	29.58 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

Log Number 012

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 26th St. NY, NY

Phone No.

Generator Site/Location

Address Same

Phone No.

Approval Number 1201041

Description of Material

Non-Regulated Petroleum Contaminated Soil

Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Assistant to Gerard — 2/13/12

Generator Authorized Agent Name | Signature | Shipment Date

TRANSPORTER

Transporter Name Carillo & Sons

Address 11 Roosevelt Ave E. Hanover, NJ

Driver Name (Print) Cesar Machado

Vehicle License No. / State / EPA No. AM185A NJ

Truck Number 14

I hereby certify that the above named material was picked up at the generator site listed above.

2-13-12

Driver Signature | Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

2/13/12

Driver Signature | Delivery Date

DESTINATION

Site Name Pure Soil Tech. (Soil Safe, Inc. - Brookport)

Phone No. 732-657-8551 (Phone: 45/ 3060)

Address 1055 South Hope Chapel Rd. Jackson, NJ 08527 (370 Route 130 Logan Township, NJ 08085)

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

2-13-12

Name of Authorized Agent | Signature | Receipt Date

White - Facility | Green - Facility | Yellow - Generator | Pink - Broker | Goldenrod - Contractor | Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/13/12 Ticket #: 169317
Time: 15:34 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: CVTRUC
CV TRUCKING Phase: 0
Truck: AN392P
License:

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 13 Amount: 429.88 Tn 389.99 Mg
(To-Date) Loads: 27 Amount: 869.77 Tn 789.06 Mg

Gross:	45.04 Tn	90080 lb	40.86 Mg
Tare:	14.11 Tn	28220 lb	12.80 Mg
Net:	30.93 Tn	61860 lb	28.06 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

Log Number 014
07546

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name CHELSEA W. 26 LLC
Address 37 W. 65TH STREET
NEW YORK, NY 10025
Phone No.

Generator Site/Location 260 W 26TH STREET
Address 260 W. 26TH STREET
NEW YORK, NY
Phone No.

Approval Number 1201044

Description of Material
Non-Regulated Petroleum Contaminated Soil
Non DOT/RCRA Regulated

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 2/13/12
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name CV-TEV TRUCK FNB
Address 182 CALCUTTA ST NEWARK
N.J. 07114

Driver Name (Print) Eric N. Fuentes
Vehicle License No. / State / EPA No. ~~H21 3043~~ N.J. AN392D
Truck Number #99

I hereby certify that the above named material was picked up at the generator site listed above.

Eric N. Fuentes 2/13/12
Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Eric N. Fuentes 2/13/12
Driver Signature — Delivery Date

DESTINATION

Pure Soil Tech. 732-657-8551
Site Name Soil Safe, Inc. Bridgeport Phone No. [redacted]
Address [redacted] 655 South Hope Chapel Rd. Jackson, NJ 08527
No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

2-13-12
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/13/12 Ticket #: 169318
Time: 15:35 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: CVTRUC
CV TRUCKING Phase: 0
Truck: AM303S
License:

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 14 Amount: 465.25 Tn 422.07 Mg
(To-Date) Loads: 28 Amount: 905.14 Tn 821.14 Mg

Gross:	48.59 Tn	97180 lb	44.08 Mg
Tare:	13.22 Tn	26440 lb	11.99 Mg
Net:	35.37 Tn	70740 lb	32.09 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

Log Number 013

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea W. 26 LLC
Address 37 W. 65th Street New York, NY 10025
Phone No.

Generator Site/Location 260 W. 26th Street
Address New York, NY
Phone No.

Approval Number 201044

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — Signature — 2/13/12
Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name CV Trucking
Address 182 Calcutta St Port Newark NJ
Driver Name (Print) Juan R. Ruiz
Vehicle License No. / State / EPA No. AH3035
Truck Number 21

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature / Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature / Delivery Date

DESTINATION

Pure Soil Tech
Site Name Soil Safe, Inc. - Bridgeport
Address 378 Route 130 Logan Township, NJ 08085 655 South Hope Chapel Rd Jackson NJ 08527
Phone No. 732-657-8551 [redacted]

No left turn on Rt. 130 North into the facility.
Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent / Signature / Receipt Date: 2-13-12

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/13/12 Ticket #: 169320
Time: 15:40 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: CVTRUC
CV TRUCKING Phase: 0
Truck: AL347A
License:

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 15 Amount: 494.34 Tn 448.47 Mg
(To-Date) Loads: 29 Amount: 934.23 Tn 847.53 Mg

Gross:	42.49 Tn	84980 lb	38.55 Mg
Tare:	13.40 Tn	26800 lb	12.16 Mg
Net:	29.09 Tn	58180 lb	26.39 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

Log Number 07546 015

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name W.26, LLC CHELSEA

Address 37 W. 65TH N.Y., N.Y. 10025

Phone No.

Generator Site/Location 260 W 26TH N.Y., N.Y. 10025

Address

Phone No.

Approval Number 12010 44

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 2/13/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name CV 56

Address NWK N.J.

Driver Name (Print) B HARTMAN

Vehicle License No. / State / EPA No. AL347A

Truck Number CV 56

I hereby certify that the above named material was picked up at the generator site listed above.

BH — 2-13-12

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

BH — 2-13-12

Driver Signature — Delivery Date

DESTINATION

Site Name Pure Soil Tech [Soil Safe, Inc. - Bridgeport] Phone No. 732-657-8551 [redacted]

Address [redacted] 655 South Hope Chapel Rd. Jackson, NJ 08527

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

2-13-12

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/13/12 Ticket #: 169321
Time: 16:11 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: MAPYKA
MAPYKA TRUCKING INC Phase: 0
Truck: AM216V
License:

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 16 Amount: 526.89 Tn 477.99 Mg
(To-Date) Loads: 30 Amount: 966.78 Tn 877.06 Mg

Gross:	45.66 Tn	91320 lb	41.42 Mg
Tare:	13.11 Tn	26220 lb	11.89 Mg
Net:	32.55 Tn	65100 lb	29.53 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

2-13-12

Log Number 0208 016

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea Green

Address 260 West 26th NY, NY

Phone No.

Generator Site/Location

Address Same

Phone No.

Approval Number 120044

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — Signature — 2/13/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Mayka T/K

Address 239 Jumper Way NJ Hawthenside NJ

Driver Name (Print) Manuel Barbosa

Vehicle License No. / State / EPA No. AH 216V

Truck Number #3

I hereby certify that the above named material was picked up at the generator site listed above.

02/13/12

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

02/13/12

Driver Signature — Delivery Date

DESTINATION

Pure Soil. 615 South Lupe

Site Name ~~Soil Safe, Inc. - Bridgeport~~ — Phone No. ~~1-856-467-8030~~

Address ~~378 Route 130 Logan Township, NJ 08085~~ Jackson NJ. 08527.

No left turn on Rt. 130 North into the facility.

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/14/12 Ticket #: 169331
Time: 09:24 Plant: P1
*** Delivery ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: DI
D&I Phase: 0
Truck: AN786K
License: D I TRUCK 02

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 1 Amount: 33.70 Tn 30.57 Mg
(To-Date) Loads: 31 Amount:1000.48 Tn 907.64 Mg

Gross:	48.61 Tn	97220 lb	44.10 Mg
Tare:	14.91 Tn	29820 lb	13.53 Mg
Net:	33.70 Tn	67400 lb	30.57 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

Log Number: 03108

GENERATOR

Generator Name: Chelsea W. 26 LLC
Address: 37 W. 65th Str.
New York, NY
Phone No.:

Shipping Location: 260 W. 26th Str.
Address: 260 W. 26th Str.
New York, NY
Phone No.:

Approval Number: 120104

Description of Material: Non Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — Generator Authorized Agent Name
Signature
2/14/12 — Shipment Date

TRANSPORTER

Transporter Name: AMV/Nabon Trk
Address: 190 Drake Lane
Hedgewood, NJ

Driver Name (Print): RONPEHP DESOUZA
Vehicle License No./State: AW 786K - NJ
Truck Number: # 07

I hereby certify that the above named material was picked up at the generator site listed above.

RONPEHP DESOUZA 02-14-12
Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date

DESTINATION

Site Name: Pure Soil
Phone No.: 732-657-8551
Address: Hwy Rt. 547 Jackson, NJ
CBG-020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent
Signature
2-14-12 — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/14/12 Ticket #: 169343
Time: 10:09 Plant: P1
*** Recycled ***

Customer: 0006435
SOIL SAFE INC.
6900 ALEXANDER BELL DRIV
COLUMBIA, MD 21046
(410) 872-3990

Job: 1201044
260 W. 26TH STREET
260 W. 26TH STREET
NEW YORK, NY 10001

P.O.#:

Carrier: AMV
AMV TRUCKING
Truck: AN202U
License:

Phase: 0

Zone:

DEFAULT ZONE NAME

Product: JR66
JR66 SOIL
JMF:
(Daily) Loads: 2 Amount: 68.53 Tn 62.17 Mg
(To-Date) Loads: 32 Amount:1035.31 Tn 939.23 Mg

Gross:	49.01 Tn	98020 lb	44.46 Mg
Tare:	14.18 Tn	28360 lb	12.86 Mg
Net:	34.83 Tn	69660 lb	31.60 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

Log Number: 03107

GENERATOR

Generator Name: Chelsea W. 26 LLC
Address: 37 W. 65th Str. NY, NY 10025
Phone No.:

Shipping Location: 260 W. 26th Str.
Address: 260 W. 26th Str. New York, NY
Phone No.:

Approval Number: 120 1044

Description of Material: Non Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — Generator Authorized Agent Name
Signature
2/14/12 — Shipment Date

TRANSPORTER

Transporter Name: AMW Dobin
Address: 190 Drake Lane Hedgewood, NJ
Driver Name (Print): Nestor Garcia
Vehicle License No./State: AN 202 U
Truck Number: # 11

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature
02-14-12 — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature
02-14-12 — Delivery Date

DESTINATION

Site Name: Pure Soil Tech
Phone No.: 732-657-8551
Address: Cty Rt. 547 Jackson, NJ
CBG020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent
Signature
2-14-12 — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/14/12 Ticket #: 169345
Time: 10:13 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: AMV
AMV TRUCKING Phase: 0
Truck: AN520R
License:

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 3 Amount: 102.83 Tn 93.29 Mg
(To-Date) Loads: 33 Amount:1069.61 Tn 970.35 Mg

Gross:	46.76*Tn	93520*lb	42.42*Mg
Tare:	12.46 Tn	24920 lb	11.30 Mg
Net:	34.30 Tn	68600 lb	31.12 Mg

* - Manual Weight

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

93520

SOIL SAFE, INC.

Log Number 03101

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea W. 26 LLC
Address 37 W. 65th Street
New York, NY 10025
Phone No.

Shipping Location 260 W. 26th Str.
Address 260 W. 26th Str.
New York, NY
Phone No.

Approval Number 120 1044

Description of Material: NON Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — Generator Authorized Agent Name
Signature
2/14/12 — Shipment Date

TRANSPORTER

Transporter Name Amv/Dabin Trk.
Address 190 Drake Lane
Hedgewood, NJ

Driver Name (Print) Paul Rodriguez.
Vehicle License No./State ANS20R NJ
Truck Number V9

I hereby certify that the above named material was picked up at the generator site listed above.

Paul Rodriguez — Driver Signature
02-14-12 — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Paul R — Driver Signature
02-14-12 — Delivery Date

DESTINATION

Site Name Pure Soil Tech. Phone No. 732-657-8551
Address County Rt. 547 Jackson, NJ CBG020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent
Signature
2-14-12 — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/14/12 Ticket #: 169353
Time: 10:38 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: AMV
AMV TRUCKING Phase: 0
Truck: AN470U
License:

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 4 Amount: 136.52 Tn 123.85 Mg
(To-Date) Loads: 34 Amount:1103.30 Tn 1000.91 Mg

Gross:	47.90 Tn	95800 lb	43.45 Mg
Tare:	14.21 Tn	28420 lb	12.89 Mg
Net:	33.69 Tn	67380 lb	30.56 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

7580U

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

Log Number 03106

GENERATOR

Generator Name Chelsea W. 26 LLC
Address 37W. 65th Str. New York, NY 10025
Phone No.

Shipping Location 260 W. 26th Str.
Address 260 W. 26th Str. New York, NY.
Phone No.

Approval Number 120 1044

Description of Material: Non Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — Generator Authorized Agent Name
Signature
2/14/12 — Shipment Date

TRANSPORTER

Transporter Name Amvi Dabin Trk.
Address 190 Drake Lane Hedgewood, NJ 07852
Driver Name (Print) Gilberto Salazar
Vehicle License No./State AN 470U
Truck Number #12

I hereby certify that the above named material was picked-up at the generator site listed above.

Driver Signature — 2-14-12 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 2-14-12 Delivery Date

DESTINATION

Site Name Pure Soil Tech. Phone No. 732-657-8551
Address Cty Rt. 547 Jackson, NJ CBG020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent
Signature
2-14-12 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/14/12 Ticket #: 169354
Time: 10:39 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: BATTAL
BATTAL TRUCKING Phase: 0
Truck: AN113A
License:

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 5 Amount: 170.00 Tn 154.22 Mg
(To-Date) Loads: 35 Amount:1136.78 Tn 1031.29 Mg

Gross:	46.52 Tn	93040 lb	42.20 Mg
Tare:	13.04 Tn	26080 lb	11.83 Mg
Net:	33.48 Tn	66960 lb	30.37 Mg

Received By: _____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

Log Number 03105

GENERATOR

Generator Name Chelsea W. 26 LLC
Address 371 W. 65th Str.
New York, NY
Phone No.

Shipping Location 260 W. 26th Str.
Address 260 W. 26th Str.
New York, NY.
Phone No.

Approval Number 1201 044

Description of Material: Non Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — Generator Authorized Agent Name
Signature
2/14/12 — Shipment Date

TRANSPORTER

Transporter Name AMV Dabin
Address 190 Drake Ln.
Ledgewood, NJ
Driver Name (Print) Frank V.
Vehicle License No./State AMV13A
Truck Number 802

I hereby certify that the above named material was picked up at the generator site listed above.

Frank V. — Driver Signature
02/14/12 — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Frank V — Driver Signature
02/14/12 — Delivery Date

DESTINATION

Site Name Pure Soil Tech
Phone No. 732-657-8551
Address Hwy Rt. 547 Jackson, NJ
CB6020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent
Signature
2.12.12 — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/14/12 Ticket #: 169355
Time: 10:49 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990
P.O.#:

Carrier: BATTAL
BATTAL TRUCKING Phase: 0
Truck: AN584H
License:
Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 6 Amount: 203.94 Tn 185.01 Mg
(To-Date) Loads: 36 Amount:1170.72 Tn 1062.08 Mg

Gross:	47.56 Tn	95120 lb	43.15 Mg
Tare:	13.62 Tn	27240 lb	12.36 Mg
Net:	33.94 Tn	67880 lb	30.79 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

Log Number 03245

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea W. 26 LLC
Address 37 W. 65th Str. New York, NJ 10025
Phone No.

Shipping Location 260 W. 26th Str.
Address 260 W. 26th Str. New York, NY
Phone No.

Approval Number 1201044

Description of Material

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — Signature — 2/14/12
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMV Saber Trucking
Address 190 Drake Lane Hedgewood, NJ 07852

Driver Name (Print) WASHINGTON
Vehicle License No./State AW 584 NY
Truck Number #807

I hereby certify that the above named material was picked up at the generator site listed above.

02/14/12
Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

02/14/12
Driver Signature — Delivery Date

DESTINATION

Site Name Pure Rock
Phone No. 732-657-8551
Address County Rt. 547 Jackson, NJ 08527
C&D F020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

2-14-12
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/14/12 Ticket #: 169358
Time: 11:08 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: BATTAL
BATTAL TRUCKING Phase: 0
Truck: AN969R
License:

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 7 Amount: 233.36 Tn 211.70 Mg
(To-Date) Loads: 37 Amount:1200.14 Tn 1088.77 Mg

Gross:	44.13 Tn	88260 lb	40.04 Mg
Tare:	14.71 Tn	29420 lb	13.35 Mg
Net:	29.42 Tn	58840 lb	26.69 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

Log Number 03248

GENERATOR

Generator Name Chelsea W. 26 LLC Shipping Location 260 W. 26th Str.

Address 37 W. 65th Str. Address 260 W. 26 Str.

New York, New York New York, NY

Phone No. _____ Phone No. _____

Approval Number 1201 044

Description of Material: Non Hazardous Petroleum Contaminated Soil

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent for generator — 2/14/12

Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name AMV/Dabin Trk. Driver Name (Print) ANT PAIVA

Address 190 Drake Lane Vehicle License No./State [redacted] AN:969R

Ledgewood, NJ Truck Number BATTAL 806

I hereby certify that the above named material was picked up at the generator site listed above.

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 02/14/12 Shipment Date — Driver Signature — 02/14/12 Delivery Date

DESTINATION

Site Name Pure Soil Tech. Phone No. 732-657-8551

Address County Rt. 547 Jackson NJ CBG 020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

2-14-12

Name of Authorized Agent / Signature / Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/14/12 Ticket #: 169361
Time: 11:16 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: BATTAL
BATTAL TRUCKING Phase: 0
Truck: AL939V
License:

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 8 Amount: 267.01 Tn 242.23 Mg
(To-Date) Loads: 38 Amount:1233.79 Tn 1119.29 Mg

Gross:	46.49*Tn	92980*lb	42.18*Mg
Tare:	12.84 Tn	25680 lb	11.65 Mg
Net:	33.65 Tn	67300 lb	30.53 Mg

* - Manual Weight

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

Log Number 03249

GENERATOR

Generator Name Chelsea W. 26 LLC Shipping Location 260 W. 26th Str.

Address 37 W. 125th Street Address 260 W. 26th Str.

New York, NY 10025 New York, NY

Phone No. _____ Phone No. _____

Approval Number	Description of Material	
120 1044	Non Hazardous Petroleum Contaminated Soil	GROSS TARE NET TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator _____ 2/14/12

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name Dom/Dawn Trk Driver Name (Print) Julio C Gonzalez

Address 190 Drake Lane Vehicle License No./State AL 939V

Lodgewood, NJ Truck Number 803

I hereby certify that the above named material was picked up at the generator site listed above.

_____ 2/14/12

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

_____ 2/14/12

Driver Signature Delivery Date

DESTINATION

Site Name Pure Soil Tech Phone No. 732-657-8551

Address City Rt 547 Jackson, NJ CBG 020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

_____ 2.14.12

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/14/12 Ticket #: 169364
Time: 11:54 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: AMV
AMV TRUCKING Phase: 0
Truck: AN353S
License:

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 9 Amount: 293.33 Tn 266.11 Mg
(To-Date) Loads: 39 Amount:1260.11 Tn 1143.17 Mg

Gross:	40.05 Tn	80100 lb	36.33 Mg
Tare:	13.73 Tn	27460 lb	12.46 Mg
Net:	26.32 Tn	52640 lb	23.88 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

80100

SOIL SAFE, INC.

Log Number

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea W 26 LLC Generator Site/Location 260 W. 26th St

Address 37 W 65th ST Address 260 W 26th ST

New York 10025 New York NY

Phone No. _____ Phone No. _____

Approval Number	Description of Material	
120 1044	Non-Regulated Petroleum Contaminated Soil Non DOT/RCRA Regulated	GROSS TARE NET TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Generator Authorized Agent Name _____ Signature _____ Shipment Date _____

TRANSPORTER

Transporter Name Dobin Trucking/AMV Driver Name (Print) E Mata

Address 190 drake LN Vehicle License No. / State / EPA No. _____

Ledgewood NJ Truck Number #1 AN3535

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature _____ Shipment Date 2/14/12

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature _____ Delivery Date 2/14/12

DESTINATION

Site Name Pure Soil Tech ~~Soil Safe, Inc. - Bridgeport~~ Phone No. ~~1-856-467-8030~~ 732-657-

Address ~~378 Route 130 Logan Township, NJ 08085~~ County Rt 547 Jackson NJ 08527

~~No left turn on Rt. 130 North into the facility.~~

Business hours are: Monday through Friday 7 AM to 5 PM; 5 PM to 10 PM By Appointment only. Saturday by appointment only.

C&D-02002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent _____ Signature _____ Receipt Date 2-14-12

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/14/12 Ticket #: 169365
Time: 11:55 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: BATTAL
BATTAL TRUCKING Phase: 0
Truck: AN114A
License:

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 10 Amount: 327.22 Tn 296.85 Mg
(To-Date) Loads: 40 Amount:1294.00 Tn 1173.92 Mg

Gross:	47.56 Tn	95120 lb	43.15 Mg
Tare:	13.67 Tn	27340 lb	12.40 Mg
Net:	33.89 Tn	67780 lb	30.75 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

19020

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

Log Number 03252

GENERATOR

Generator Name Chelsea W. 26 LLC Shipping Location 260 W. 26th Str.

Address 37 W. 65th Str. New York, NY 10025 Address 260 W. 26th Str. New York, NY

Phone No. _____ Phone No. _____

Approval Number 120 1044

Description of Material: Non-Hazardous Petroleum Contaminated Soil

GROSS

TARE

NET

TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator _____ 2/14/12

Generator Authorized Agent Name Signature Shipment Date

TRANSPORTER

Transporter Name AMV/Dawn Trk. Driver Name (Print) Humberto Peraza 6

Address 190 Drake Lane Hedgewood, NJ Vehicle License No./State AN 114 R

Truck Number 814

I hereby certify that the above named material was picked up at the generator site listed above.

Humberto Peraza 6

Driver Signature Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Humberto Peraza 6

Driver Signature Delivery Date

DESTINATION

Site Name Pure Soil Tech. Phone No. 732-657-8551

Address County Rt. 547 Jackson, NJ 08527 CB-020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

2-14-12

Name of Authorized Agent Signature Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/14/12 Ticket #: 169366
Time: 11:56 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: BATTAL
BATTAL TRUCKING Phase: 0
Truck: AK776K
License:

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 11 Amount: 355.48 Tn 322.49 Mg
(To-Date) Loads: 41 Amount:1322.26 Tn 1199.55 Mg

Gross:	42.59 Tn	85180 lb	38.64 Mg
Tare:	14.33 Tn	28660 lb	13.00 Mg
Net:	28.26 Tn	56520 lb	25.64 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

85160

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

Log Number 03104

GENERATOR

Generator Name Chelsea W. 26 LLC
Address 37 W. 65th Str. New York, ny
Phone No.

Shipping Location 260 W. 26th Str.
Address 260 W. 26th Str. New York, NY
Phone No.

Approval Number 1201-044

Description of Material: Non Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — Signature — 2/14/12
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMV/Dalan
Address 190 Dale Ln. Hedgewood, NJ

Driver Name (Print) Ramiro Vd
Vehicle License No./State NJ AK776K
Truck Number 805

I hereby certify that the above named material was picked up at the generator site listed above.

Ramiro Vdaz 02 14 12
Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Ramiro Vdaz 02 14 12
Driver Signature — Delivery Date

DESTINATION

Site Name Pure Soil Tech. Phone No. 732-657-8551
Address Cty Rt. 547 Jackson, NJ CB6020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/14/12 Ticket #: 169368
Time: 12:08 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: NICK
NICKABELLAS Phase: 0
Truck: AN700H
License:

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 12 Amount: 384.03 Tn 348.39 Mg
(To-Date) Loads: 42 Amount:1350.81 Tn 1225.45 Mg

Gross:	42.86 Tn	85720 lb	38.88 Mg
Tare:	14.31 Tn	28620 lb	12.98 Mg
Net:	28.55 Tn	57100 lb	25.90 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

Log Number 03247

GENERATOR

Generator Name Chelsea, W. 26th St LLC
Address 37 W. 65th Street
New York, NY
Phone No.

Shipping Location 260 W 26th Street
Address 260 W 26th Str.
New York, NY
Phone No.

Approval Number 120/044

Description of Material: non Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — Generator Authorized Agent Name
Signature
2/14/12 — Shipment Date

TRANSPORTER

Transporter Name AMV/Dabin Trk.
Address 190 Drake Lane
Ledgewood, NJ 07852

Driver Name (Print) Jorge Palacz
Vehicle License No./State AN700H
Truck Number #26

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature
2-14-12 — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature
2-14-12 — Delivery Date

DESTINATION

Site Name Pure Soil Technologies
Phone No. 732-657-8551
Address Cty. Rt. 547 Jackson, NJ 08527 CBG-020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent
Signature
2-14-12 — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/14/12 Ticket #: 169369
Time: 12:18 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: VVSL
VVSL TRUCKING Phase: 0
Truck: AM536A
License:

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 13 Amount: 411.67 Tn 373.47 Mg
(To-Date) Loads: 43 Amount:1378.45 Tn 1250.53 Mg

Gross:	41.21 Tn	82420 lb	37.39 Mg
Tare:	13.57 Tn	27140 lb	12.31 Mg
Net:	27.64 Tn	55280 lb	25.08 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

E2340

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

Log Number 03246

GENERATOR

Generator Name Chelsea W. 26 LLC
Address 37 W. 65th Street New York, NY
Phone No.

Shipping Location 260 W. 26th Str.
Address 260 W. 26th Str. New York, NY
Phone No.

Approval Number 120104Y

Description of Material: Non Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Agent for generator — Signature — 2/14/12
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMV Dalen Trk
Address 190 Drake Lane Ledgewood, NJ

Driver Name (Print) Avelino R. Sanchez
Vehicle License No./State # AM536A NJ
Truck Number #8

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 2-14-2012 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 2-14-12 Delivery Date

DESTINATION

Site Name Pure Soil Tech. Phone No. 732-657-8551
Address County Rt. 547, Jackson, NJ CBG-020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — 2-14-12 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/14/12 Ticket #: 169371
Time: 12:37 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: NICK
NICKABELLAS Phase: 0
Truck: AN809P
License:

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 14 Amount: 442.36 Tn 401.31 Mg
(To-Date) Loads: 44 Amount:1409.14 Tn 1278.37 Mg

Gross:	44.33 Tn	88660 lb	40.22 Mg
Tare:	13.64 Tn	27280 lb	12.37 Mg
Net:	30.69 Tn	61380 lb	27.84 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC. 88600

NON-HAZARDOUS MATERIAL MANIFEST

Log Number 03250

GENERATOR

Generator Name Chelsea W. 26 LLC
Address 37 W. 65th Sts.
New York, NY
Phone No.

Shipping Location 260 W. 26th Sts.
Address 260 W. 26th Sts.
New York, NY
Phone No.

Approval Number 1201 044

Description of Material: NON Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

GS agent to generator — Signature — 2/14/12
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMV Cabin Trk.
Address 190 Drake Lane
Ledgewood, NJ 07852

Driver Name (Print) Jesus Castro
Vehicle License No./State AW 809 P.
Truck Number 2y.

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 2/14/12
Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 2/14/12
Delivery Date

DESTINATION

Site Name Pure Soil Tech.
Phone No. 732-657-8551
Address County Rt. 547 Jackson, NJ
CBG 020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — 2-14-12
Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/14/12 Ticket #: 169376
Time: 13:07 Plant: P1
*** Recycled ***

Customer: 0006435
SOIL SAFE INC.
6900 ALEXANDER BELL DRIV
COLUMBIA, MD 21046
(410) 872-3990

Job: 1201044
260 W. 26TH STREET
260 W. 26TH STREET
NEW YORK, NY 10001

P.O.#:

Carrier: NICK
NICKABELLAS
Truck: AN732R
License:

Phase: 0

Zone:

DEFAULT ZONE NAME

Product: JR66
JR66 SOIL
JMF:
(Daily) Loads: 15 Amount: 469.69 Tn 426.10 Mg
(To-Date) Loads: 45 Amount:1436.47 Tn 1303.17 Mg

Gross:	42.02 Tn	84040 lb	38.12 Mg
Tare:	14.69 Tn	29380 lb	13.33 Mg
Net:	27.33 Tn	54660 lb	24.79 Mg

Received By: _____
Weighmaster: LARRY CORREA NJWMS# 30175

Log Number 03253

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea W 26 LLC
Address 37 W. 65th Street
New York New York

Generator Site/Location 260 W. 26th
Address 260 W 26th St
New York NY

Phone No.

Phone No.

Approval Number 120 1044

Description of Material: Non-Regulated Petroleum Contaminated Soil; Non DOT/RCRA Regulated

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 2/14/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMV/Dobin Trucking
Address 190 Drake Lane
Ledgewood NJ 07852

Driver Name (Print) Jose Ortiz
Vehicle License No. / State / EPA No. AN752R
Truck Number 28

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 2/14/12 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 2/14/12 Delivery Date

DESTINATION

Site Name Pure Soil ~~Soil Safe, Inc. - Bridgeport~~ Phone No. 732-657-8551 ~~1-856-467-8030~~

Address ~~378 Route 130 Logan Township, NJ 08085~~ CH Rt 549, Jackson NJ 08527

No left turn on Rt. 130 North into the facility.

CB6902000?

Business hours are: Monday through Friday 7 AM to 5 PM. 5 PM to 10 PM By Appointment only. Saturday by appointment only.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

2-14-12

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

SoilSafe
Solutions Group
6700 Alexander Bell Drive, Suite 300, Columbia, MD 21046
(410) 872-3990, Fax (410) 872-3978

Invoice
10378

Bill To:	Project:
Chelsea West 26, LLC c/o Artimus Construction, Inc. Attention: Amnon Solomon 37 West 65th Street New York, NY 10023	Chelsea Green 260 West 26th Street New York, NY 10001

APPROVAL #: 451 **PROPOSAL #:** 570 **PO #:**
INVOICED VOLUME OF SOIL: 975.77 **# OF TRUCKS:** 30
INVOICE DATE: 3/7/12 **DUE DATE:** 4/6/12

BILLING PERIOD: 2/22/12 TO 2/23/12

DESCRIPTION:	UNITS INVOICED:	RATE:	AMOUNT:
Disposal & Transportation Fees - tons	975.77	$ 48.00	$ 46,836.96

GROSS INVOICE	$ 46,836.96
SALES TAX	0.00
LESS: PREPAYMENTS	0.00
INVOICE TOTAL	$ 46,836.96

Contact:

**NOTE* Payments are Net 30 days. Overdue balances are subject to a 1.5% charge per month or the maximum allowed by law.*

Remit to: (Payments Only) P.O. Box 824062, Philadelphia, PA 19182-4062

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/22/12 Ticket #: 169775
Time: 10:15 Plant: P1
*** Recycled ***

Customer: 0008435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990
P.O.#:

Carrier: AMV
AMV TRUCKING Phase: 0
Truck: AN520R
License: AMV V9
Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 1 Amount: 36.37 Tn 32.99 Mg
(To-Date) Loads: 46 Amount:1472.84 Tn 1336.16 Mg

Gross: 48.83 Tn 97660 lb 44.30 Mg
Tare: 12.46 Tn 24920 lb 11.30 Mg
Net: 36.37 Tn 72740 lb 33.00 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

Log Number 03116

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea W. 26 LLC
Address 37 W. 65th Street
New York, NY 10025
Phone No.

Shipping Location 260 W 26th Street
Address 260 W 26th Street
New York, NY
Phone No.

Approval Number 120104

Description of Material: Non-Hazardous Peholeum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — Signature — 2/22/12
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AmV/ Dobin Trucking
Address 190 Drake Lane
Ledgewood, NJ 07852

Driver Name (Print) Paul Rodriguez
Vehicle License No./State AN520R/ New Jersey
Truck Number V9

I hereby certify that the above named material was picked up at the generator site listed above.

Paul — 02-22-12
Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Paul — 02-22-12
Driver Signature — Delivery Date

DESTINATION

Site Name Pure Soil Technologies
Address County Route 547 Jackson, NJ 08527
Phone No. 732-657-8551
CBG 020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

2-22-12
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/22/12 Ticket #: 169778
Time: 10:20 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
5900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990
P.O.#:

Carrier: RLS
RLS TRANSPORTATION LLC Phase: 0
Truck: AN109E
License: RLS 18
Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 2 Amount: 69.03 Tn 62.62 Mg
(To-Date) Loads: 47 Amount:1505.50 Tn 1365.79 Mg

Gross: 47.02 Tn 94040 lb 42.66 Mg
Tare: 14.36 Tn 28720 lb 13.03 Mg
Net: 32.66 Tn 65320 lb 29.63 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

Log Number 03241

NON-HAZARDOUS MATERIAL MANIFEST

940640

GENERATOR

Generator Name Chelsea W. 26 LLC
Address 37 W. 65th Street
New York, NY 10025
Phone No.

Shipping Location 260 W. 26th Stree
Address 260 W. 26th Street
New York, NY
Phone No.

Approval Number 1201044

Description of Material: Non-Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — Signature — 2/22/12
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMV / Dobin Trucking
Address 190 Drake Lane
Ledgewood, NJ 07852

Driver Name (Print) RLS Bergamo
Vehicle License No./State AV-109F
Truck Number 18

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date

DESTINATION

Site Name Pure Soil Technologies
Address County Route 547 Jackson, NJ 08527
Phone No. 732-657-8551
CBG 020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

LC — 2-22-12
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/22/12 Ticket #: 169782
Time: 10:33 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: AMV
AMV TRUCKING Phase: 0
Truck: AN353S
License: AMV V8

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 3 Amount: 101.87 Tn 92.42 Mg
(To-Date) Loads: 48 Amount:1538.34 Tn 1395.58 Mg

Gross: 46.57 Tn 93140 lb 42.25 Mg
Tare: 13.73 Tn 27460 lb 12.46 Mg
Net: 32.84 Tn 65680 lb 29.79 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

Log Number 03120

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea W. 26 LLC
Address 37 W. 65th Street
New York, NY 10025
Phone No.

Shipping Location 260 W. 26th Street
Address 260 W. 26th Street
New York, NY
Phone No.

Approval Number 201044

Description of Material: Non-Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — 2/22/12
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMV / Dabin Trucking
Address 190 Drake Lane
Ledgewood, NJ 07852

Driver Name (Print) Roger Mesen
Vehicle License No./State AN 3335
Truck Number 8

I hereby certify that the above named material was picked up at the generator site listed above.

2/22/12
Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

2/22/12
Driver Signature — Delivery Date

DESTINATION

Site Name Pure Soil Technologies
Address County Route 547
Jackson, NJ 08527

Phone No. 732-657-8551
CBG 020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

2-22-12
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/22/12 Ticket #: 169786
Time: 10:56 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: AMV
AMV TRUCKING Phase: 0
Truck: AN484A
License: AMV 10

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loa[illegible] Amount: 136.75 Tn 124.06 Mg
(To-Date) Loads: 49 Amount:1573.22 Tn 1427.23 Mg

Gross: 48.01 Tn 96020 lb 43.55 Mg
Tare: 13.13 Tn 26260 lb 11.91 Mg
Net: 34.88 Tn 69760 lb 31.64 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

Log Number 03136

NON-HAZARDOUS MATERIAL MANIFEST

96020

GENERATOR

Generator Name Chelsea W. 26 LLC
Address 27 W. 6th Street
New York, NY 10025
Phone No.

Shipping Location 260 W 26th Street
Address 260 W. 26th Street
New York, NY
Phone No.

Approval Number 1201044

Description of Material: Non-Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — Generator Authorized Agent Name
Signature
2/22/12 — Shipment Date

TRANSPORTER

Transporter Name AMV / Nolan Trucking
Address 190 Drake Lane
Ledgewood, NJ 07852

Driver Name (Print) Ramiro Vargas
Vehicle License No./State NJ AN4845
Truck Number 10

I hereby certify that the above named material was picked up at the generator site listed above.

Ramiro Vargas — Driver Signature
02 22 12 — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Ramiro Vargas — Driver Signature
02 22 12 — Delivery Date

DESTINATION

Site Name Pure Soil Technologies
Address County Route 547
Jackson, NJ 07752

Phone No. 732 - 657 - 855
CBE 02002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent
Signature
2-22-12 — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/22/12 Ticket #: 169787
Time: 11:05 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: AMV
AMV TRUCKING Phase: 0
Truck: AN202U
License: AMV V11

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 5 Amount: 170.29 Tn 154.49 Mg
(To-Date) Loads: 50 Amount:1606.76 Tn 1457.65 Mg

Gross: 47.72 Tn 95440 lb 43.29 Mg
Tare: 14.18 Tn 28360 lb 12.86 Mg
Net: 33.54 Tn 67080 lb 30.43 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

Log Number 03146

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea W. 26 LLC
Address 37 W. 65th Street
New York, NY 10025
Phone No.

Shipping Location 260 W 26th Street
Address 260 W 26th Street
New York, NY
Phone No.

Approval Number 1201044

Description of Material: Non-Hazadous Petroleum Contaminated Soil.

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — Signature — 2/22/12
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AmV/Dabin Trucking
Address 190 Drake Lane
Ledgewood, NJ 07852

Driver Name (Print) Nestor Garcia
Vehicle License No./State AN 202 U
Truck Number # 11

I hereby certify that the above named material was picked up at the generator site listed above.

02-22-12
Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

02-22-12
Driver Signature — Delivery Date

DESTINATION

Site Name Pure Soil Technologies
Address County Route 527 Jackson, NJ 08527

Phone No. 732-657-8551
CBE 020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

2-22-12
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

---

ate: 02/22/12 Ticket #: 169788
ime: 11:06 Plant: P1
** Recycled ***

ustomer: 0006435 Job: 1201044
OIL SAFE INC. 260 W. 26TH STREET
900 ALEXANDER BELL DRIV 260 W. 26TH STREET
OLUMBIA, MD 21046 NEW YORK, NY 10001
410) 872-3990
P.O.#:

arrier: AMV
MV TRUCKING Phase: 0
ruck: AN470U
icense: AMV V12
Zone:

roduct: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 6 Amount: 207.29 Tn 188.05 Mg
(To-Date) Loads: 51 Amount:1643.76 Tn 1491.22 Mg

Gross: 51.21 Tn 102420 lb 46.46 Mg
Tare: 14.21 Tn 28420 lb 12.89 Mg
Net: 37.00 Tn 74000 lb 33.57 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

Log Number 03138

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea W. 26 LLC
Address 37 W 65th Street
New York NY 10025
Phone No.

Shipping Location 260 W 26th Street
Address 260 W. 26th Street.
New York, NY
Phone No.

Approval Number 1201044

Description of Material: Non-Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — 2/22/12
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AmV/ Dobin Trucking
Address 190 Drake Lane
Ledgewood, NJ 07852

Driver Name (Print) Gilberto Salazar
Vehicle License No./State AN490U
Truck Number # 12

I hereby certify that the above named material was picked up at the generator site listed above.
Driver Signature — 2-22-12 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.
Driver Signature — 2-22-12 Delivery Date

DESTINATION

Site Name Pure Soil Technologies
Address County Route 547
Jackson, NJ 08527

Phone No. 732-657-8551
CBG 020002.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — 2-22-12 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/22/12 Ticket #: 169795
Time: 11:54 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER LL DRIV 260 W. 26TH STREET
COLUMBIA, MD 2 3 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: SHIF
SHIRLY EXP Phase: 0
Truck: AM3
License: SHIF 09

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 7 Amount: 239.87 Tn 217.61 Mg
(To-Date) Loads: 52 Amount:1676.34 Tn 1520.78 Mg

Gross:	47.21 Tn	94420 lb	42.83 Mg
Tare:	14.63 Tn	29260 lb	13.27 Mg
Net:	32.58 Tn	65160 lb	29.56 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

Log Number 03145

NON-HAZARDOUS MATERIAL MANIFEST

94420

GENERATOR

Generator Name Chelsea W. 26 LLC
Address 27 W. 65th Street
New York, NY 10025
Phone No.

Shipping Location 260 W 26th Sheet.
Address 260 W. 26th Sheet.
New York, NY
Phone No.

Approval Number 12010114

Description of Material: Non-Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby cer y that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any appli ble state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has bee properly described, classified and packaged, and is in proper condition for transportation according t pplicable regulations.

GS agent for generator — Signature — 2/23/12
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMV/Dobin Trucking
Address 190 Drake Lane
Ledgewood, NJ 07852

Driver Name (Print) Robinson V
Vehicle License No./State AM395Z
Truck Number 9

I hereby certify that the above named material was picked up at the generator site listed above.

3-22-12
Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

3-22-12
Driver Signature — Delivery Date

DESTINATION

Site Name Pure Soil Technologies
Address County Route 547
Jackson, NJ 08527

Phone No. 732-657-8551
CBG 020002.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

2-22-12
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/22/12 Ticket #: 169796
Time: 11:56 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: RLS
RLS TRANSPORTATION LLC Phase: 0
Truck: AN969F
License: RLS TRANS 38

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 8 Amount: 272.11 Tn 246.86 Mg
(To-Date) Loads: 53 Amount:1708.58 Tn 1550.02 Mg

Gross:	47.05 Tn	94100 lb	42.68 Mg
Tare:	14.81 Tn	29620 lb	13.44 Mg
Net:	32.24 Tn	64480 lb	29.25 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

Log Number 03142

NON-HAZARDOUS MATERIAL MANIFEST

94100

GENERATOR

Generator Name Chelsea W. 26 LLC
Address 37 W. 65th Street
New York, NY 10025
Phone No.

Shipping Location 260 W 26th Stree
Address 260 W 26th Street
New York, NY
Phone No.

Approval Number 1201044

Description of Material: Non-Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

agent to generator — Signature — 2/22/12
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AmV / Dabin Trucking
Address 190 Drake Lane
Ledgewood, NJ 07852

Driver Name (Print) JDIRO
Vehicle License No./State AN969F
Truck Number R25 #38

I hereby certify that the above named material was picked up at the generator site listed above.

02-22-12
Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

02-22-12
Driver Signature — Delivery Date

DESTINATION

Site Name Pure Soil Technologies
Phone No. 732-657-8551
Address County Route 547 @ Jackson, NJ 08527
CRG 020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

2-22-12
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/22/12 Ticket #: 169801
Time: 12:29 Plant: P1
*** Recycled ***

Customer: 0006435
SOIL SAFE INC.
6900 ALEXANDER BELL DRIV
COLUMBIA, MD 21046
(410) 872-3990

Job: 1201044
260 W. 26TH STREET
260 W. 26TH STREET
NEW YORK, NY 10001

P.O.#:

Carrier: SHIRLE
SHIRLY EXP
Truck: AN934F
License: SHIRLEY 12

Phase: 0

Zone:

Product: JR66
JR66 SOIL
JMF:

DEFAULT ZONE NAME

(Daily) Loads: 9 Amount: 302.42 Tn 274.36 Mg
(To-Date) Loads: 54 Amount:1738.89 Tn 1577.52 Mg

Gross:	44.91 Tn	89820 lb	40.74 Mg
Tare:	14.60 Tn	29200 lb	13.25 Mg
Net:	30.31 Tn	60620 lb	27.50 Mg

Received By: _____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

Log Number 03134

NON-HAZARDOUS MATERIAL MANIFEST

89820

GENERATOR

Generator Name Chelsea W 26 LLC
Address 37 W. 65th Street
New York, NY 10025
Phone No.

Shipping Location 260 W 26th Street
Address 260 W 26th Street
New York, NY
Phone No.

Approval Number D010644

Description of Material: Non-Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — Signature — 2/22/12
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMV/Dobin Trucking
Address 190 Drake Lane
Ledgewood, NJ 07852

Driver Name (Print) Jaime L Diaz
Vehicle License No./State AW934/F
Truck Number 12 Shirley

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 2/22/12 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date

DESTINATION

Site Name Pure Soil Technologies — Phone No. 732-657-8551
Address County Route 547 Jackson, NJ 08527

CBG 020000

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — 2-22-12 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/22/12 Ticket #: 169802
Time: 12:30 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: SHIRLE
SHIRLY EXP Phase: 0
Truck: AM110T
License: SHIRLEY 6

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 10 Amount: 335.23 Tn 304.12 Mg
(To-Date) Loads: 55 Amount:1771.70 Tn 1607.29 Mg

Gross:	47.62 Tn	95240 lb	43.20 Mg
Tare:	14.81 Tn	29620 lb	13.44 Mg
Net:	32.81 Tn	65620 lb	29.77 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

Log Number 03126

95240

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea W 26 LLC
Address 37 W. 65th Street
New York, NY

Shipping Location 260 W. 26th Stree
Address 260 W. 26th Street
New York, NY

Phone No.

Phone No.

Approval Number 1201044

Description of Material: Non-Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — Generator Authorized Agent Name
Signature
2/22/12 — Shipment Date

TRANSPORTER

Transporter Name AMV / Dubin Trucking
Address 190 Drake Lane
Ledgewood, NJ 07852

Driver Name (Print) Carlos
Vehicle License No./State AM110T
Truck Number 06 - Shirley

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 02-22-12 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 02-22-12 Delivery Date

DESTINATION

Site Name Pure Soil Technologies
Phone No. 732-657-8551
Address County Route 527
Jackson, NJ 08527
CBG D20002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent
Signature
LC 2-22-12 — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/22/12 Ticket #: 169806
Time: 12:46 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: FEIJOO
C.FEIJOO Phase: 0
Truck: AJ106H
License: C.FEIJOO 78

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 11 Amount: 364.47 Tn 330.65 Mg
(To-Date) Loads: 56 Amount:1800.94 Tn 1633.81 Mg

Gross:	43.71 Tn	87420 lb	39.65 Mg
Tare:	14.47 Tn	28940 lb	13.13 Mg
Net:	29.24 Tn	58480 lb	26.53 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

Log Number 03124

NON-HAZARDOUS MATERIAL MANIFEST

87400

GENERATOR

Generator Name Chelsea W 26 LLC
Address 27 W. 65th Street
New York, NY
Phone No.

Shipping Location 260 W. 26th Street
Address 260 W 26th Sheet
New York, NY
Phone No.

Approval Number 1201044

Description of Material: Non-Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS agent to generator — Signature — 2/22/12
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Amv / Dobin Trucking
Address 190 Drake Lane
Ledgewood, NJ 07852

Driver Name (Print) Julio
Vehicle License No./State AJ106H
Truck Number #78

I hereby certify that the above named material was picked up at the generator site listed above.

Julio Dobz
Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date

DESTINATION

Site Name Pure Soil Technologies
Address County Rock 547
Jackson, NJ 08527

Phone No. 732-657-8551
CBG 020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

LC — 2-22-12
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/22/12 Ticket #: 169808
Time: 12:59 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: KAS
KAS TRUCKING Phase: 0
Truck: AM309P
License: KAS 02

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads. 12 Amount: 396.12 Tn 359.36 Mg
(To-Date) Loads: 57 Amount:1832.59 Tn 1662.53 Mg

Gross:	46.97 Tn	93940 lb	42.61 Mg
Tare:	15.32 Tn	30640 lb	13.90 Mg
Net:	31.65 Tn	63300 lb	28.71 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

Log Number 03123

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea W. 26 LLC
Address 37 W. 65th Street
New York, NY 10025
Phone No.

Shipping Location 260 W 26th Street
Address 260 W. 26th Street
New York, NY
Phone No.

Approval Number 1201044

Description of Material: Non-Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS agent to generator — Signature — 2/22/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMV / Dabin Trucking
Address 190 Dixie Lane
Ledgewood, NJ 07852

Driver Name (Print) Juan S Portillo
Vehicle License No./State AM 309 P
Truck Number 02

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 02/22/12 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date

DESTINATION

Site Name Pure Soil Technologies
Address County Route 547
Jackson, NJ 08527

Phone No. 732-657-8551
CBE 020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — 2-22-12 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/22/12 Ticket #: 169831
Time: 13:50 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: SHIRLE
SHIRLY EXP Phase: 0
Truck: AN316N
License: SHIRLEY 05

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 13 Amount: 428.37 Tn 388.62 Mg
(To-Date) Loads: 58 Amount:1864.84 Tn 1691.78 Mg

Gross:	47.20 Tn	94400 lb	42.82 Mg
Tare:	14.95 Tn	29900 lb	13.56 Mg
Net:	32.25 Tn	64500 lb	29.26 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

Log Number: 03128

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name: Chelsea W. 26 LLC
Address: 37 W. 65th Street
New York, NY 10025
Phone No.:

Shipping Location: 260 W. 26th Street
Address: 260 W. 26th Street
New York, NY
Phone No.:

Approval Number: R201044

Description of Material: Non-Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS AGENT TO GENERATOR — 2/22/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name: AMV/ Dabin Trucking
Address: 190 Drake Lane
Ledgewood, NJ 07852

Driver Name (Print):
Vehicle License No./State: AN 316 H
Truck Number: 05

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 2/22/12 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 2/22/12 Delivery Date

DESTINATION

Site Name: Pure Soil Technologies
Phone No.: 732-657-8551
Address: County Route 547
Jackson, NJ 08527
CBG 020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

2-22-12

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/22/12 Ticket #: 169833
Time: 13:54 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: SHIRLE
SHIRLY EXP Phase: 0
Truck: AN931F
License:

Zone:

Product: JR6 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 14 Amount: 460.81 Tn 418.05 Mg
(To-Date) Loads: 59 Amount:1897.28 Tn 1721.21 Mg

Gross:	46.94 Tn	93880 lb	42.58 Mg
Tare:	14.50 Tn	29000 lb	13.15 Mg
Net:	32.44 Tn	64880 lb	29.43 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

Log Number 03130

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea W26 LLC
Address 37 W. 65th Street
New York, NY 10025
Phone No.

Shipping Location 260 W. 26th Street
Address 260 W. 26th Street
New York, NY
Phone No.

Approval Number 1201044

Description of Material: Non-Hazardous Petroleum Contaminated Soil.

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — Signature — 2/22/12
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMV/ Dobin Trucking
Address 190 Drake Lane
Ledgewood, NJ 07852

Driver Name (Print) Samuel
Vehicle License No./State AN 931F
Truck Number 16

I hereby certify that the above named material was picked up at the generator site listed above.

Samuel 2-22-12
Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Samuel 02-22-12
Driver Signature — Delivery Date

DESTINATION

Site Name Pure Soil Technologies
Address County Route 547
Jackson, NJ 08527

Phone No. 732-657-8551
CRC 020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

2-22-12
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/22/12 Ticket #: 169844
Time: 14:22 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: RLS
RLS TRANSPORTATION LLC Phase: 0
Truck: AN109E
License: RLS 18

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 15 Amount: 492.24 Tn 446.56 Mg
(To-Date) Loads: 60 Amount:1928.71 Tn 1749.73 Mg

Gross:	45.79 Tn	91580 lb	41.54 Mg
Tare:	14.36 Tn	28720 lb	13.03 Mg
Net:	31.43 Tn	62860 lb	28.51 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

Log Number 03242

GENERATOR

Generator Name Chelsea W. 26 LLC
Address 27 W. 65th Street
New York, NY 10025
Phone No.

Shipping Location 260 W 26th Street
Address 260 W 26th Street
New York, NY
Phone No.

Approval Number 1201044

Description of Material: Non-Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — Generator Authorized Agent Name
Signature
2/22/12 — Shipment Date

TRANSPORTER

Transporter Name AMV / Dobin Trucking
Address 190 Drake Lane
Ledgewood, NJ 07852

Driver Name (Print) R L S Bergamm
Vehicle License No./State DM-109-E
Truck Number 15

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature
Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature
Delivery Date

DESTINATION

Name Pure Soil Technologies
Phone No. 732-657-855
County Route 547
Jackson, NJ 08527
CEG 020002.

I certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Authorized Agent
Signature
2-22-12 — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/22/12 Ticket #: 169845
Time: 14:25 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: RLS
RLS TRANSPORTATION LLC Phase: 0
Truck: AM496Z
License: RLS TRANS 48

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 16 Amount: 524.49 Tn 475.82 Mg
(To-Date) Loads: 61 Amount:1960.96 Tn 1778.98 Mg

Gross:	47.02 Tn	94040 lb	42.66 Mg
Tare:	14.77 Tn	29540 lb	13.40 Mg
Net:	32.25 Tn	64500 lb	29.26 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

Log Number 03243

NON-HAZARDOUS MATERIAL MANIFEST

041020

GENERATOR

Generator Name Chelsea W. 26 LLC
Address 37 W. 65th Street
New York, NY 10025
Phone No.

Shipping Location 260 W 26th Shee
Address 260 W. 26th Street
New York, NY
Phone No.

Approval Number 1201044

Description of Material: Non-Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — Generator Authorized Agent Name
Signature
2/22/12 — Shipment Date

TRANSPORTER

Transporter Name Amv/Dobin Trucking
Address 190 Drake Lane.
Ledgewood, NJ 07852
Driver Name (Print) Ruben
Vehicle License No./State ANM496 ZNJ
Truck Number 48

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature
02/22/12 — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature
02.22/12 — Delivery Date

DESTINATION

Site Name Pure Soil Technologies
Phone No. 732-657-8551
Address County Route 547
Jackson, NJ 08527
CRG 020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent
Signature
2-22-12 — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/22/12 Ticket #: 169849
Time: 14:36 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: AMV
AMV TRUCKING Phase: 0
Truck: AN520R
License: AMV V9

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 17 Amount: 557.75 Tn 505.99 Mg
(To-Date) Loads: 62 Amount:1994.22 Tn 1809.16 Mg

Gross:	45.72 Tn	91440 lb	41.48 Mg
Tare:	12.46 Tn	24920 lb	11.30 Mg
Net:	33.26 Tn	66520 lb	30.17 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

Log Number 03117

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea W. 26 LLC
Address 37 W. 65th Street
New York, NY 10025
Phone No.

Shipping Location 260 W. 26th Street
Address 260 W. 26th Street
New York, NY
Phone No.

Approval Number 1201044

Description of Material: Non-Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent for Sanrok — 2/22/12
Generator Authorized Agent Name / Signature / Shipment Date

TRANSPORTER

Transporter Name AmV / Dobin Trucking
Address 190 Dixie Lane
Ledgewood, NJ 07852

Driver Name (Print) Paul Rodriguez
Vehicle License No./State ANS20R New Jer
Truck Number 19

I hereby certify that the above named material was picked up at the generator site listed above.

Paul — 02.22.12
Driver Signature / Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Paul — 02-22-1
Driver Signature / Delivery Date

DESTINATION

Site Name Pure Soil Technologies
Phone No. 732-657-8551
Address County Route 547
Jackson, NJ 08527
CBG 020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

2-22-12
Name of Authorized Agent / Signature / Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/22/12 Ticket #: 169853
Time: 14:49 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: AMV
AMV TRUCKING Phase: 0
Truck: AN353S
License: AMV V8

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 18 Amount: 589.96 Tn 535.21 Mg
(To-Date) Loads: 63 Amount:2026.43 Tn 1838.38 Mg

Gross:	45.94 Tn	91880 lb	41.68 Mg
Tare:	13.73 Tn	27460 lb	12.46 Mg
Net:	32.21 Tn	64420 lb	29.22 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

Log Number 03119

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea W. 26 LLC
Address 37 W. 65th Street
New York, NY 10025
Phone No.

Shipping Location 260 W. 26th Street
Address 260 W. 26th Street
New York, NY
Phone No.

Approval Number 120644

Description of Material: Non-Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AC agent to generator — Generator Authorized Agent Name
Signature
2/22/12 — Shipment Date

TRANSPORTER

Transporter Name Amy / Dobin Trucking
Address 190 Drake Lane
Ledgewood, NJ 07852

Driver Name (Print) Roger Mesen
Vehicle License No./State AW353S
Truck Number 8

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature
2/22/12 — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature
2/22/12 — Delivery Date

DESTINATION

Site Name Pure Soil Technologies
Address County Route 547
Jackson, NJ 08527

Phone No. 732-657-8551
CBG 02002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent
Signature
2-22-12 — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/22/12 Ticket #: 169860
Time: 15:18 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990
P.O.#:

Carrier: AMV
AMV TRUCKING Phase: 0
Truck: AN484A
License: AMV 10
Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 19 Amount: 625.06 Tn 567.05 Mg
(To-Date) Loads: 64 Amount:2061.53 Tn 1870.22 Mg

Gross:	48.23 Tn	96460 lb	43.75 Mg
Tare:	13.13 Tn	26260 lb	11.91 Mg
Net:	35.10 Tn	70200 lb	31.84 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

Log Number 03137

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea W. 26 LLC
Address 37 W. 65th Street.
New York, NY 10025
Phone No.

Shipping Location 260 W 26th Stre
Address 260 W. 26th Street
New York, NY
Phone No.

Approval Number 120104

Description of Material: Non-Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as a agent to generator — Signature — 2/22/12
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Any/ Dobin Trucking
Address 190 Drake Lane
Ledgewood, NJ 07852
Driver Name (Print) Ramiro N
Vehicle License No./State NJ AN484S
Truck Number 10

I hereby certify that the above named material was picked up at the generator site listed above.

Ramiro N 02 22 12
Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Ramiro N 02 12
Driver Signature — Delivery Date

DESTINATION

Site Name Pure Soil Technologies
Address County Route 547 J
Jackson, NJ 07852
Phone No. 732-657-8551
CBG 020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

LC — 2-22-12
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/22/12 Ticket #: 169862
Time: 15:36 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: AMV
AMV TRUCKING Phase: 0
Truck: AN202U
License: AMV V11

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 20 Amount: 658.98 Tn 597.83 Mg
(To-Date) Loads: 65 Amount:2095.45 Tn 1900.99 Mg

Gross:	48.10 Tn	96200 lb	43.64 Mg
Tare:	14.18 Tn	28360 lb	12.86 Mg
Net:	33.92 Tn	67840 lb	30.77 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

Log Number 03118

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea W. 26 LLC
Address 37 W. 65th Street
New York, NY 10025
Phone No.

Shipping Location 260 W 26th Street
Address 260 W 26th Street
New York, NY
Phone No.

Approval Number D01044

Description of Material: Non-Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — Generator Authorized Agent/Name
Signature
2/22/12 — Shipment Date

TRANSPORTER

Transporter Name AMV/Dabin Trucking
Address 190 Drake Lane.
Ledgewood, NJ 07852

Driver Name (Print) Nestor Garcia
Vehicle License No./State AW 202 U
Truck Number # 11

I hereby certify that the above named material was picked up at the generator site listed above.
Driver Signature
02-22-12 — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.
Driver Signature
02-22-1 — Delivery Date

DESTINATION

Site Name Pure Soil Technologies
Address County Route 547
Jackson, NJ 08527
Phone No. 732-657-8551
CBG 020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent
Signature
2-22-12 — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/22/12 Ticket #: 169863
Time: 15:41 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: SHIRLE
SHIRLY EXP Phase: 0
Truck: AN890A
License: SHIRLEY 20

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 21 Amount: 688.02 Tn 624.17 Mg
(To-Date) Loads: 66 Amount:2124.49 Tn 1927.34 Mg

Gross:	43.59 Tn	87180 lb	39.55 Mg
Tare:	14.55 Tn	29100 lb	13.20 Mg
Net:	29.04 Tn	58080 lb	26.35 Mg

Received By: _____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

Log Number 03141

NON-HAZARDOUS MATERIAL MANIFEST

87180

GENERATOR

Generator Name Chelsea W. 26 LLC
Address 27 W 65th Street
New York, NY 10025
Phone No.

Shipping Location 260 W 26th Street
Address 260 W 26th Street.
New York, NY
Phone No.

Approval Number 1201044

Description of Material: Non-Hazadous Petroleum Contominated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

GS agent for generator — Signature — 2/22/12
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Amv/ Dobin Trucking
Address 190 Drake Lane
Ledgewood, NJ 07852

Driver Name (Print) Jonathan Valverde
Vehicle License No./State AH890A
Truck Number Shirley # 20

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 02/22/12 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 02/22/12 Delivery Date

DESTINATION

Site Name Pure Soil Technologies — Phone No. 732-657-8551
County Route 547
Address Jackson, NJ 08527 — CBE 020002.

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

AC — 2-22-12

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/22/12 Ticket #: 169864
Time: 16:00 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: AMV
AMV TRUCKING Phase: 0
Truck: AN470U
License: AMV V12

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 22 Amount: 721.93 Tn 654.93 Mg
(To-Date) Loads: 67 Amount:2158.40 Tn 1958.10 Mg

Gross:	48.12 Tn	96240 lb	43.65 Mg
Tare:	14.21 Tn	28420 lb	12.89 Mg
Net:	33.91 Tn	67820 lb	30.76 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

Log Number 03139

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea W. 26 LLC
Address 37 W. 65th Street
New York, NY 10025
Phone No.

Shipping Location 260 W 26th Stre
Address 260 W. 26th Street
New York, NY
Phone No.

Approval Number 1201044

Description of Material: Non-Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — Signature — 2/22/12
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AmV / Dobin Trucking
Address 190 Drake Lane
Ledgewood, NJ 07852

Driver Name (Print) Gilberto Salazar
Vehicle License No./State AN 430 U
Truck Number #12

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 2-22-12 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 2-22-12 Delivery Date

DESTINATION

Site Name Pure Soil Technologies
County Route 547
Address Jackson, NJ 08527

Phone No. 732-657-855
CEG 020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — 2-22-12 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL [illegible] OGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/23/12 Ticket #: 169865
Time: 06:45 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: SHIRLE
SHIRLY EXP Phase: 0
Truck: AM395Z
License: SHIRLEY 09

Zone:

Product: JR66 DEFAULT ZONE NAME
JR[illegible] SOIL
JM

([illegible]) Lo[illegible] 1 Amount: 31.97 Tn 29.00 Mg
([illegible]ate) Lo[illegible]68 Amount:2190.37 Tn 1987.10 Mg

[illegible] 46.60 Tn 93200 lb 42.28 Mg
T[illegible] 14.63 Tn 29260 lb 13.27 Mg
N[illegible] 31.97 Tn 63940 lb 29.00 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 3017

SOIL SAFE, INC.

Log Number: 03144

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name: Chelsea W 26 LLC
Address: 537 W. 65th Street
New York, NY 10025
Phone No.:

Shipping Location: 260 W. 26th Street
Address: 260 W. 26th Street
New York, NY
Phone No.:

Approval Number: 1201044

Description of Material: Non-Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

GES agent to generator — 2/22/12
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name: AmV/ Dobin Trucking
Address: 190 Drake Lane
Ledgewood, NJ 07852
Driver Name (Print): Danny
Vehicle License No./State: AM395Z
Truck Number: 9

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 03-22-12
Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 03-22-12
Delivery Date

DESTINATION

Site Name: Rule Soil Technologies
Phone No.: 732-657-8551
Address: County Route 527
Jackson, NJ 08527
CBE 020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

KC — 2-23-12
Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/23/12 Ticket #: 169866
Time: 06:47 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: SHIRLE
SHIRLY EXP Phase: 0
Truck: AM110T
License: SHIRLEY 6

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 2 Amount: 63.88 Tn 57.95 Mg
(To-Date) Loads: 69 Amount:2222.28 Tn 2016.05 Mg

Gross:	46.72 Tn	93440 lb	42.39 Mg
Tare:	14.81 Tn	29620 lb	13.44 Mg
Net:	31.91 Tn	63820 lb	28.95 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

Log Number 03127

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea W26 LLC
Address 27 W. 65th Sheet
New York, NY
Phone No.

Shipping Location 260 W. 26th Shee
Address 260 W. 26th Sheet
New York, NY
Phone No.

Approval Number 1201044

Description of Material: Non-Hazardous Petroleum Contaminated Soils

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — Signature — 2/22/12
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMV / Dubin Trucking
Address 190 Drake Lane
Ledgewood, NJ 07852

Driver Name (Print) Carlos
Vehicle License No./State AM110T
Truck Number 06 - Shirley

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date

DESTINATION

Site Name Pure Soil Technologies
Address County Route 547
Jackson, NJ 08527

Phone No. 732-657-8551
CRG 020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

LC — 2-23-12

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/23/12 Ticket #: 169867
Time: 06:49 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: RLS
RLS TRANSPORTATION LLC Phase: 0
Truck: AN969F
License: RLS TRANS 38

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 3 Amount: 93.47 Tn 84.80 Mg
(To-Date) Loads: 70 Amount:2251.87 Tn 2042.90 Mg

Gross:	44.40 Tn	88800 lb	40.26 Mg
Tare:	14.81 Tn	29620 lb	13.44 Mg
Net:	29.59 Tn	59180 lb	26.84 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

Log Number 03143

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea W 26 LLC
Address 37 W. 65th Sheet
New York, NY 10025
Phone No.

Shipping Location 260 W 26th Shee
Address 260 W 26th Sheet
New York, NY
Phone No.

Approval Number 1201044

Description of Material: Non-Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

Assigant to generator — 2/22/12
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name AMV/ Dobin Trucking
Address 190 Drake Lane
Ledgewood, NJ 07852

Driver Name (Print) JAIRO
Vehicle License No./State AN969F
Truck Number AN 969F

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 2-22-12 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 2-22-12 Delivery Date

DESTINATION

Site Name Pure Soil Technologies
County Route 547
Address Jackson, NJ 08527

Phone No. 732-657-8551
CBG 020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — 2-23-12 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/23/12 Ticket #: 169935
Time: 11:43 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: KAS
KAS TRUCKING Phase: 0
Truck: AM309P
License: KAS 02

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 4 Amount: 126.36 Tn 114.63 Mg
(To-Date) Loads: 71 Amount:2284.76 Tn 2072.73 Mg

Gross:	47.47 Tn	94940 lb	43.07 Mg
Tare:	14.58 Tn	29160 lb	13.23 Mg
Net:	32.89 Tn	65780 lb	29.84 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

Log Number 03122

NON-HAZARDOUS MATERIAL MANIFEST

94900

GENERATOR

Generator Name Chelsea W. 26 LLC
Address 37 W. 65th Street
New York, NY 10025
Phone No.

Shipping Location 260 W 26th Street
Address 260 W. 26th Street
New York, NY
Phone No.

Approval Number	Description of Material	GROSS / TARE / NET / TONNAGE
2010144	Non-Hazardous Petroleum Contaminated Soil*J	

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

As agent to generator — Signature — 2/23/12
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Amv/Dobin Trucking
Address 190 Dixie Lane
Ledgewood, NJ 07852

Driver Name (Print) Tom S Portillo
Vehicle License No./State AM 309 P
Truck Number 02

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 02/23/12 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date

DESTINATION

Site Name Pure Soil Technologies
Address County Route 547
Jackson, NJ 08527

Phone No. 732-657-8551
CBC 020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — 2-23-12 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/23/12 Ticket #: 169939
Time: 11:58 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: DI
D&I Phase: 0
Truck: AM687R
License: DI TRUCK 01

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 5 Amount: 161.85 Tn 146.83 Mg
(To-Date) Loads: 72 Amount:2320.25 Tn 2104.93 Mg

Gross: 48.79 Tn 97580 lb 44.26 Mg
Tare: 13.30 Tn 26600 lb 12.07 Mg
Net: 35.49 Tn [illegible] lb 32.20 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

Log Number 03153

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

Generator Name Chelsea W 26 LLC
Address 260 West 26th St NY NY
Phone No.

Shipping Location
Address Same
Phone No.

Approval Number 120104

Description of Material: Non-Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — Signature — 2/23/12
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name Ann / Dobin Trucking
Address 190 Drake Lane Ledgewood, NJ 07852

Driver Name (Print) Danilo
Vehicle License No./State A710872
Truck Number 21

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — Delivery Date

DESTINATION

Site Name Pure Soil Technologies
Address County Rt 547 Jackson, NJ 08527
Phone No. 732-657-8551 Cell 020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

2.23.12

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/23/12 Ticket #: 169940
Time: 11:59 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: ROSET
ROSETTA STONE Phase: 0
Truck: AN375K
License: ROSETTA 88

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 6 Amount: 193.52 Tn 175.56 Mg
(To-Date) Loads: 73 Amount:2351.92 Tn 2133.66 Mg

Gross:	46.12 Tn	92240 lb	41.84 Mg
Tare:	14.45 Tn	28900 lb	13.11 Mg
Net:	31.67 Tn	63340 lb	28.73 Mg

Received By: _____
Weighed By: LARRY CORREA [illegible] 3017

SOIL SAFE, INC.

Log Number 03132

NON-HAZARDOUS MATERIAL MANIFEST

92240

GENERATOR

Generator Name Chelsea-W. 26 LLC
Address 27 W 65th Street
New York, NY 10025
Phone No.

Shipping Location 260 W 26th Street
Address 260 W 26th Street
New York, NY
Phone No.

Approval Number 120044

Description of Material: Non-Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

as agent to generator — Generator/Authorized Agent Name
Signature
2/23/12 — Shipment Date

TRANSPORTER

ANV. TRU ROSETTA STONE

Transporter Name
Address
Driver Name (Print) Oscar Solano
Vehicle License No./State AN 375K
Truck Number 88

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature
2/23/12 — Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Oscar Solano — Driver Signature
2/23/12 — Delivery Date

DESTINATION

Site Name Rule Soil Technologies
Phone No. 732-657-8551
Address County Route 547
Jackson, NJ 08527
CRG 020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent
Signature
2-23-12 — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/23/12 Ticket #: 169944
Time: 12:07 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: ROSET
ROSETTA STONE Phase: 0
Truck: AN313R
License: ROSETTA 01

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 7 Amount: 227.18 Tn 206.10 Mg
(To-Date) Loads: 74 Amount:2385.58 Tn 2164.20 Mg

Gross:	47.12 Tn	94240 lb	42.75 Mg
Tare:	13.46 Tn	26920 lb	12.21 Mg
Net:	33.66 Tn	67320 lb	30.54 Mg

Received By:_____
Weighmaster: LARRY CORREA NJWMS# 30175

SOIL SAFE, INC.

Log Number 03131

NON-HAZARDOUS MATERIAL MANIFEST

GENERATOR

94240

Generator Name Chelsea W. 26 LLC

Address 37 W. 65th Street
New York, NY 10025

Phone No.

Shipping Location 260 W 26th Street

Address 260 W. 26th Street
New York, NY

Phone No.

Approval Number 1201044

Description of Material: Non-Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS agent to generator — 2/23/12

Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

SOMERSET / ROSETA STONE

Transporter Name [illegible]

Address [illegible]
Ledgewood, NJ 07852

Driver Name (Print) CARLOS OR

Vehicle License No./State AU 313R

Truck Number #

I hereby certify that the above named material was picked up at the generator site listed above.

02-23/12 — Shipment Date

Driver Signature

I hereby certify that the above named material was delivered without incident to the destination listed below.

02/23/1

Driver Signature — Delivery Date

DESTINATION

Site Name Pure Soil Technologies — Phone No. 732-657-5551

Address County Route 547
Jackson, NJ 08527

CBG 020052

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

2-23-12

Name of Authorized Agent — Signature — Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

PURE SOIL TECHNOLOGIES
655 S. HOPE CHAPEL RD
JACKSON N.J. 08527
732-657-8551

Date: 02/23/12 Ticket #: 169994
Time: 14:32 Plant: P1
*** Recycled ***

Customer: 0006435 Job: 1201044
SOIL SAFE INC. 260 W. 26TH STREET
6900 ALEXANDER BELL DRIV 260 W. 26TH STREET
COLUMBIA, MD 21046 NEW YORK, NY 10001
(410) 872-3990

P.O.#:

Carrier: SHIRLE
SHIRLY EXP Phase: 0
Truck: AN890A
License: SHIRLEY 20

Zone:

Product: JR66 DEFAULT ZONE NAME
JR66 SOIL
JMF:
(Daily) Loads: 8 Amount: 253.84 Tn 230.28 Mg
(To-Date) Loads: 75 Amount:2412.24 Tn 2188.38 Mg

Gross: 41.21 Tn 82420 lb 37.39 Mg
Tare: 14.55 Tn 29100 lb 13.20 Mg
Net: 26.66 Tn 53320 lb 24.19 Mg

Received By:_____

SOIL SAFE, INC.

NON-HAZARDOUS MATERIAL MANIFEST

Log Number: 03240

GENERATOR

Generator Name: Chelsea W. 26 LLC
Address: 37 W. 65th Street
New York, NY 10025
Phone No.:

Shipping Location: 260 W. 26th Street
Address: 260 W. 26th Street
New York, NY
Phone No.:

Approval Number: 1201044

Description of Material: Non-Hazardous Petroleum Contaminated Soil

GROSS
TARE
NET
TONNAGE

I hereby certify that the above named material does not contain free liquid as defined by 40 CFR Part 260.10 or any applicable state law, is not a hazardous waste as defined by 40 CFR Part 261 or any applicable state law, has been properly described, classified and packaged, and is in proper condition for transportation according to applicable regulations.

AS agent to generator — Signature — 2/23/12
Generator Authorized Agent Name — Signature — Shipment Date

TRANSPORTER

Transporter Name: AmV/Dabin Trucking
Address: 140 Drake Lane
Ledgewood, NJ 07852

Driver Name (Print): Luis Diaz
Vehicle License No./State: AN 8904
Truck Number: #20

I hereby certify that the above named material was picked up at the generator site listed above.

Driver Signature — 2-23-12 Shipment Date

I hereby certify that the above named material was delivered without incident to the destination listed below.

Driver Signature — 2-23-12 Delivery Date

DESTINATION

Site Name: Pure Soil Technologies - County Route 547
Address: Jackson, NJ 08527
Phone No.: 732-657-8551
CCG 020002

I hereby certify that the above named material has been accepted and to the best of my knowledge the foregoing is true and accurate.

Name of Authorized Agent — Signature — 2-23-12 Receipt Date

White - Facility Green - Facility Yellow - Generator Pink - Broker Goldenrod - Contractor Blue - Trucking Co.

APPENDIX L

Water-Proofing Membrane Specifications

PREPRUFE® LOW TEMPERATURE MEMBRANES

Pre-applied fully-bonded waterproofing membranes for low temperature applications

Description

Preprufe® Low Temperature Membranes (300LT and 160LT) are unique composite sheets comprising a thick HDPE film, an aggressive pressure sensitive adhesive formulated for application temperatures down to 25°F (-4°C), and a weather resistant protective coating.

Unlike conventional non-adhering membranes, which are vulnerable to water ingress tracking between the unbonded membrane and structure, the unique Preprufe bond to concrete prevents ingress or migration of water around the structure.

The Preprufe LT System is designed for application temperatures between 25°F (-4°C) and 60°F (+16°C) and includes:

- **Preprufe 300LT**—heavy-duty grade for use below slabs and on rafts (i.e. mud slabs). Designed to accept the placing of heavy reinforcement using conventional concrete spacers.
- **Preprufe 160LT**—thinner grade for blindside, zero property line applications against soil retention systems.
- **Preprufe Tape LT**—for covering cut edges, roll ends, penetrations and detailing
- **Bituthene® Liquid Membrane**—for sealing around penetrations, etc.

Preprufe 300LT & 160LT membranes are applied either horizontally to smooth prepared concrete, carton forms or well rolled and compacted sand or crushed stone substrates; or vertically to permanent formwork or adjoining structures. Concrete is then cast directly against the adhesive side of the membranes. The specially developed Preprufe adhesive layers work together to form a continuous and integral seal to the structure.

Preprufe can be returned up the inside face of slab formwork but is not recommended for conventional twin-sided formwork on walls, etc. Use Bituthene Low Temperature self-adhesive membrane or Procor® fluid applied membrane to walls after removal of formwork for a fully bonded system to all structural surfaces.

Advantages

- **Forms a unique continuous adhesive bond to concrete poured against it**—prevents water migration and makes it unaffected by ground settlement beneath slabs
- **Fully-adhered watertight laps** and detailing
- **Provides a barrier to water, moisture and gas**—physically isolates the structure from the surrounding ground
- **Simple and quick to install at temperatures down to 25°F (-4°C)**—requiring no priming or fillets
- **Impermeable** to moisture
- **Solar reflective**—reduced temperature gain
- **Can be applied to permanent formwork**—allows maximum use of confined sites
- **Self protecting**—can be trafficked immediately after application and ready for immediate placing of reinforcement
- **Unaffected by wet conditions**—cannot activate prematurely
- **Inherently waterproof, non-reactive system:**
  - not reliant on confining pressures or hydration
  - unaffected by freeze/thaw, wet/dry cycling
- **Chemical resistant**—effective in most types of soils and waters, protects structure from salt or sulphate attack

Installation

The minimum application temperature of Preprufe membranes is 25°F (-4°C). When installing the Preprufe waterproofing system in cold or marginal weather conditions (below 55°F (13°C)) the use of Preprufe 300LT & 160LT membranes is recommended. Preprufe 300LT & 160LT membranes are supplied in rolls 4 ft (1.2 m) wide, with a selvedge on one side to provide self-adhered side laps for continuity between rolls. The specially formulated low temperature adhesive provides for easy formation of side laps at temperatures down to 25°F (-4°C). To ensure a continuous bond is achieved, roll all laps firmly with a heavy roller. Unlike Preprufe 300R & 160R, Preprufe 300LT & 160LT membranes do not require the addition of Preprufe Tape LT at the side

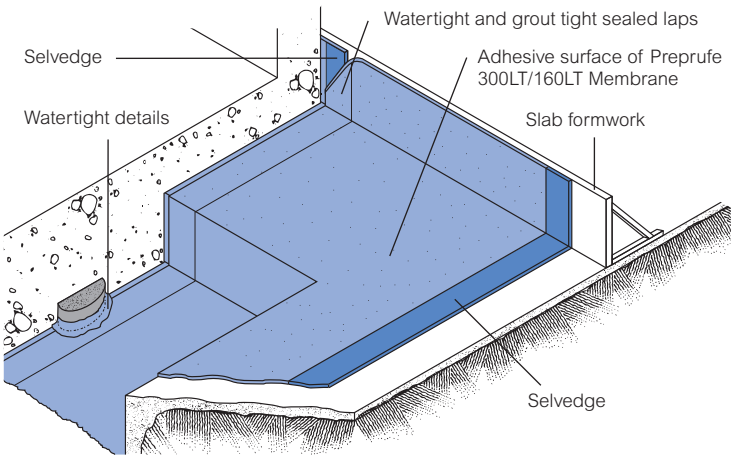

Drawings are for illustration purposes only.
Please refer to graceconstruction.com for specific application details.

Product Advantages

- Fully-bonded to concrete
- Barrier to water, moisture and gas
- Low temperature application
- Immediately trafficable
- Chemical resistant
- Solar reflective

Supply

Dimensions (Nominal)	Preprufe 300LT Membrane	Preprufe 160LT Membrane	Preprufe Tape LT
Thickness	0.046 in. (1.2 mm)	0.032 in. (0.8 mm)	
Roll size	4 ft x 98 ft (1.2 m x 30 m)	4 ft x 115 ft (1.2 m x 35 m)	4 in. x 49 ft (100 mm x 15 m)
Roll area	392 ft² (36 m²)	460 ft² (42 m²)	
Roll weight	108 lbs (50 kg)	92 lbs (42 kg)	4.3 lbs (2 kg)
Minimum side/end laps	3 in. (75 mm)	3 in. (75 mm)	
Ancillary Products			
Bituthene Liquid Membrane—1.5 US gal (5.7 liter) or 4 US gal (15.1 liter)			

Physical Properties

Property	Typical Value 300LT	Typical Value 160LT	Test Method
Color	white	white	
Thickness	0.046 in. (1.2 mm) nominal	0.032 in. (0.8 mm) nominal	ASTM D3767
Low temperature flexibility	Unaffected at -10°F (-23°C)	Unaffected at -10°F (-23°C)	ASTM D1970
Resistance to hydrostatic head, minimum	231 ft (70 m)	231 ft (70 m)	ASTM D5385, modified[1]
Elongation, minimum	300%	300%	ASTM D412, modified[2]
Tensile strength, film, minimum	4000 psi (27.6 MPa)	4000 psi (27.6 MPa)	ASTM D412
Crack cycling at -10°F (-23°C), 10 cycles	Unaffected	Unaffected	ASTM C836
Puncture resistance	221 lbs (990 N)	100 lbs (445 N)	ASTM E154
Peel adhesion to concrete, minimum	5.0 lbs/in. (880 N/m) width	5.0 lbs/in. (880 N/m) width	ASTM D903, modified[3]
Lap peel adhesion	2.5 lbs/in. (440 N/m) width	2.5 lbs/in. (440 N/m) width	ASTM D1876, modified[4]
Permeance to water vapor transmission, maximum	0.01 perms (0.6 ng/(Pa x s x m²))	0.01 perms (0.6 ng/(Pa x s x m²))	ASTM E96, method B
Water absorption, maximum	0.5%	0.5%	ASTM D570
Methane permeability	9.1 mls/m²/day	N/A	University of London, QMW College[3]
Permeability[5] (hydraulic conductivity)	K=<1.4 x 10^{-11}cm.s^{-1}	K=<1.4 x 10^{-11}cm.s^{-1}	ASTM D5084-90

Footnotes:
1. Hydrostatic head tests of Preprufe Membranes are performed by casting concrete against the membrane with a lap. Before the concrete cures, a 0.125 in. (3 mm) spacer is inserted perpendicular to the membrane to create a gap. The cured block is placed in a chamber where water is introduced to the membrane surface up to the head indicated.
2. Elongation of membrane is run at a rate of 2 in. (50 mm) per minute.
3. Concrete is cast against the protective coating surface of the membrane and allowed to properly dry (7 days minimum). Peel adhesion of membrane to concrete is measured at a rate of 2 in. (50 mm) per minute at room temperature.
4. The test is conducted 15 minutes after the lap is formed (per Grace published recommendations) and run at a rate of 2 in. (50 mm) per minute at 25°F (-4°C).
5. Result is lower limit of apparatus. Membrane therefore considered impermeable.

laps at temperatures below 55°F. However, Preprufe Tape LT should still be used for all end laps and other details requiring tape. During cold or damp conditions, the selvedge and tape adhesive can be gently warmed using a hot air gun or similar to remove moisture and improve initial adhesion. Refer to the Preprufe 300R & 160R data sheet, application guides, and technical letters for all other standard application details.

The rolls of Preprufe Membrane and Preprufe Tape are interwound with a disposable plastic release liner which must be removed before placing reinforcement and concrete. Steel reinforcement should be placed using approved rebar chairs as explained in Technical Letter #15, *Rebar Chairs on Preprufe 300R Membrane*. Follow American Concrete Institute's *Cold Weather Concreting – ACI 306R88* to ensure concrete properly cures allowing the Preprufe to form an intimate bond to the concrete.

For the most current application instructions, detail drawings and technical letters for Preprufe Membranes, go to www.graceconstruction.com or contact your local Grace representative.

Specification Clauses

Preprufe 300LT or 160LT shall be applied with its adhesive face presented to receive fresh concrete to which it will integrally bond. Only Grace Construction Products approved membranes shall be bonded to Preprufe 300LT/160LT. All Preprufe 300LT/160LT system materials shall be supplied by Grace Construction Products, and applied strictly in accordance with their instructions. Specimen performance and formatted clauses are also available.

NOTE: Use Preprufe Tape to tie-in Procor with Preprufe.

Limitations

It is recommended that concrete be poured within 56 days of application of the membrane.

Preprufe 300LT & 160LT should only be used when application temperatures are between 25°F (-4°C) and 60°F (+16°C). For application temperatures above 60°F (+16°C), use Preprufe 300R & 160R membranes.

Health and Safety

Refer to relevant Material Safety data sheet. Complete rolls should be handled by a minimum of two persons.

www.graceconstruction.com

For technical assistance call toll free at 866-333-3SBM (3726)

Preprufe and Bituthene are registered trademarks of W. R. Grace & Co.–Conn.
Procor is a U.S. registered trademark of W. R. Grace & Co.–Conn., and is used in Canada under license from PROCOR LIMITED.

We hope the information here will be helpful. It is based on data and knowledge considered to be true and accurate and is offered for the users' consideration, investigation and verification, but we do not warrant the results to be obtained. Please read all statements, recommendations or suggestions in conjunction with our conditions of sale, which apply to all goods supplied by us. No statement, recommendation or suggestion is intended for any use which would infringe any patent or copyright. W. R. Grace & Co.–Conn., 62 Whittemore Avenue, Cambridge, MA 02140. In Canada, Grace Canada, Inc., 294 Clements Road, West, Ajax, Ontario, Canada L1S 3C6.

This product may be covered by patents or patents pending. Copyright 2009. W. R. Grace & Co.–Conn.
PF-174 Printed in U.S.A. 8/09 FA/pdf

GRACE
